

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting


General Topics:

- Last truss set today!
- GN2 testing - Thurs pm
- CUB 2 exterior panels are done
- No work Fri 27 Dec
- Weekend work






UTILITY LEVEL PRESS TEST

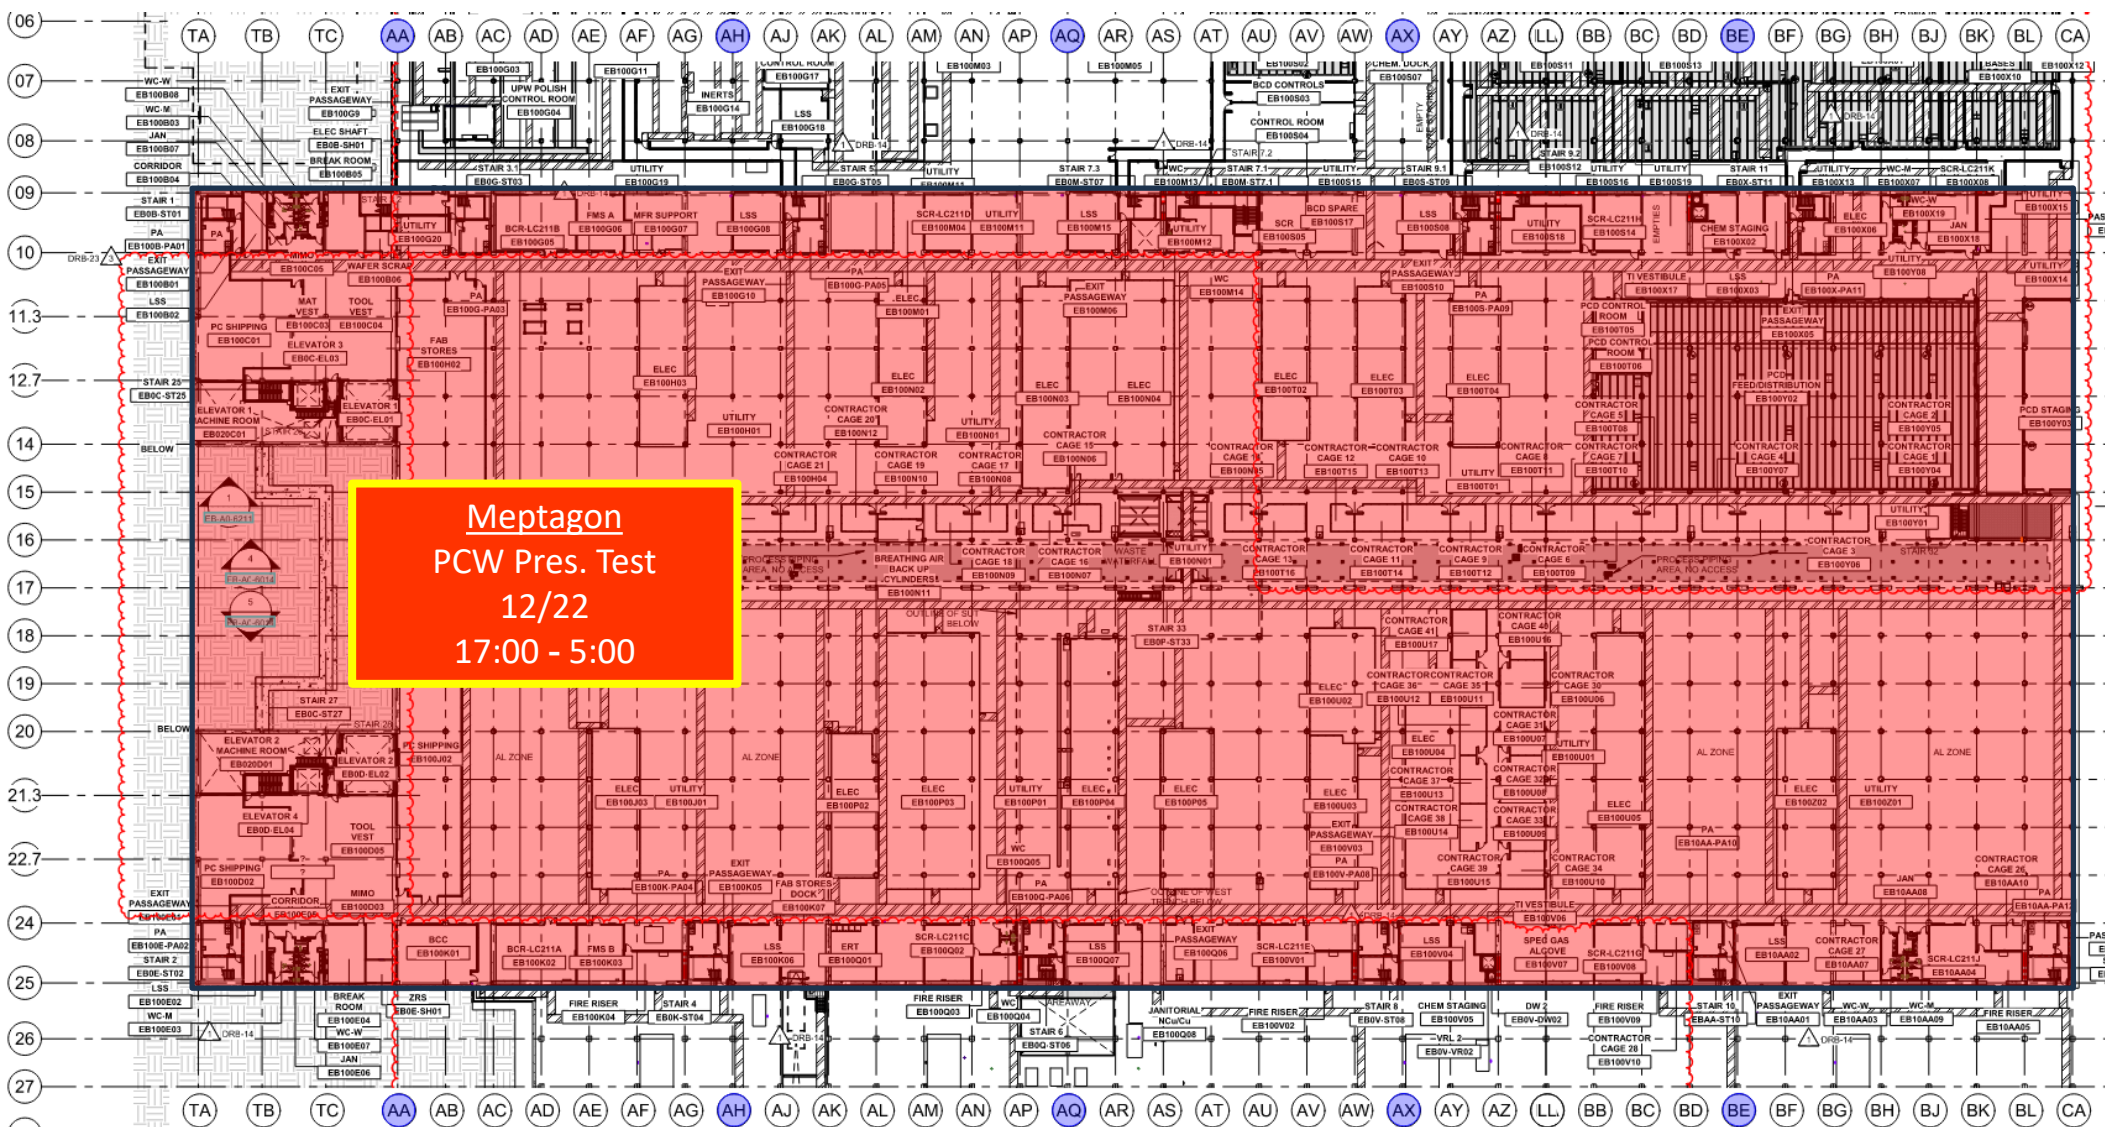




UTILITY LEVEL PRESS TEST

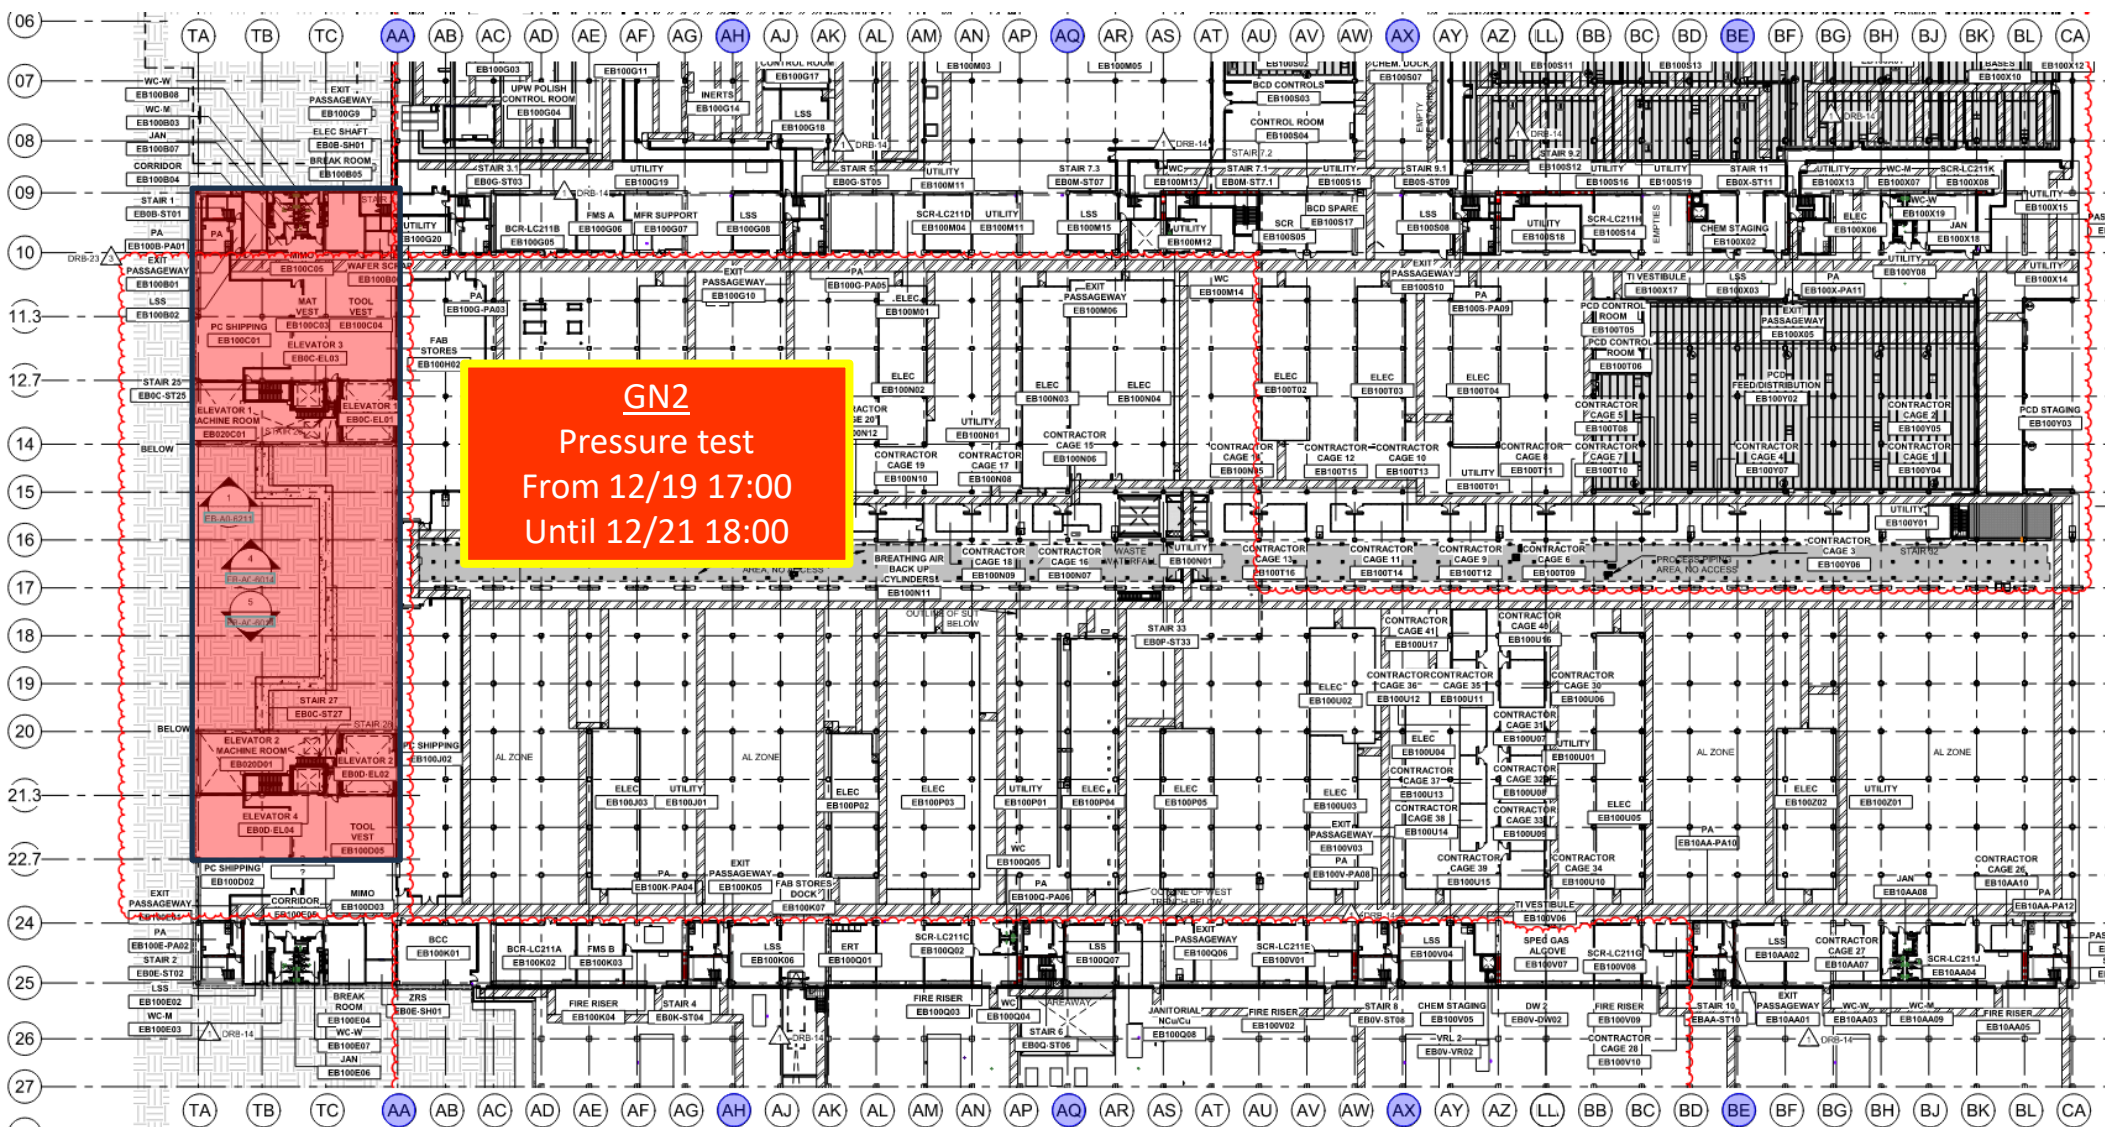



UTILITY LEVEL MOD1

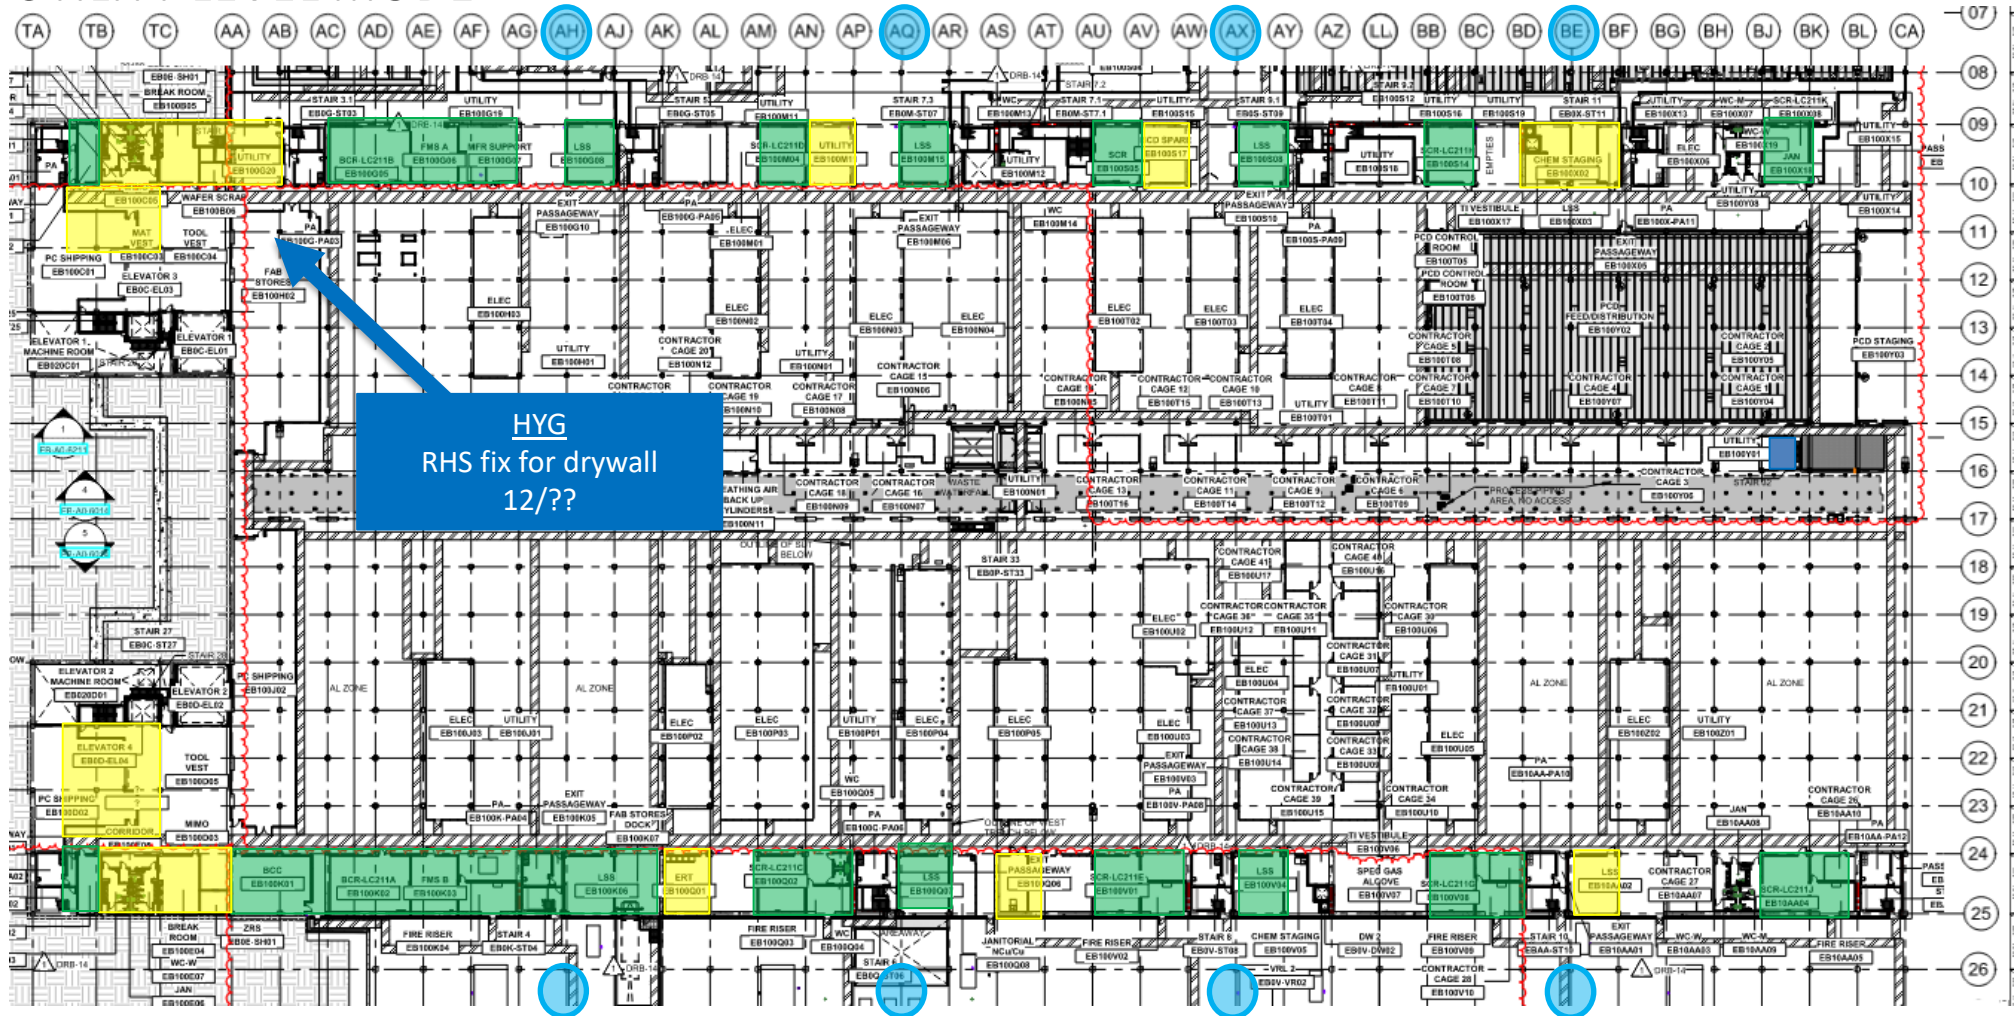


ELRAM
Drywall install

MEP+Elctrical
Ready for re-install



UTILITY LEVEL MOD2

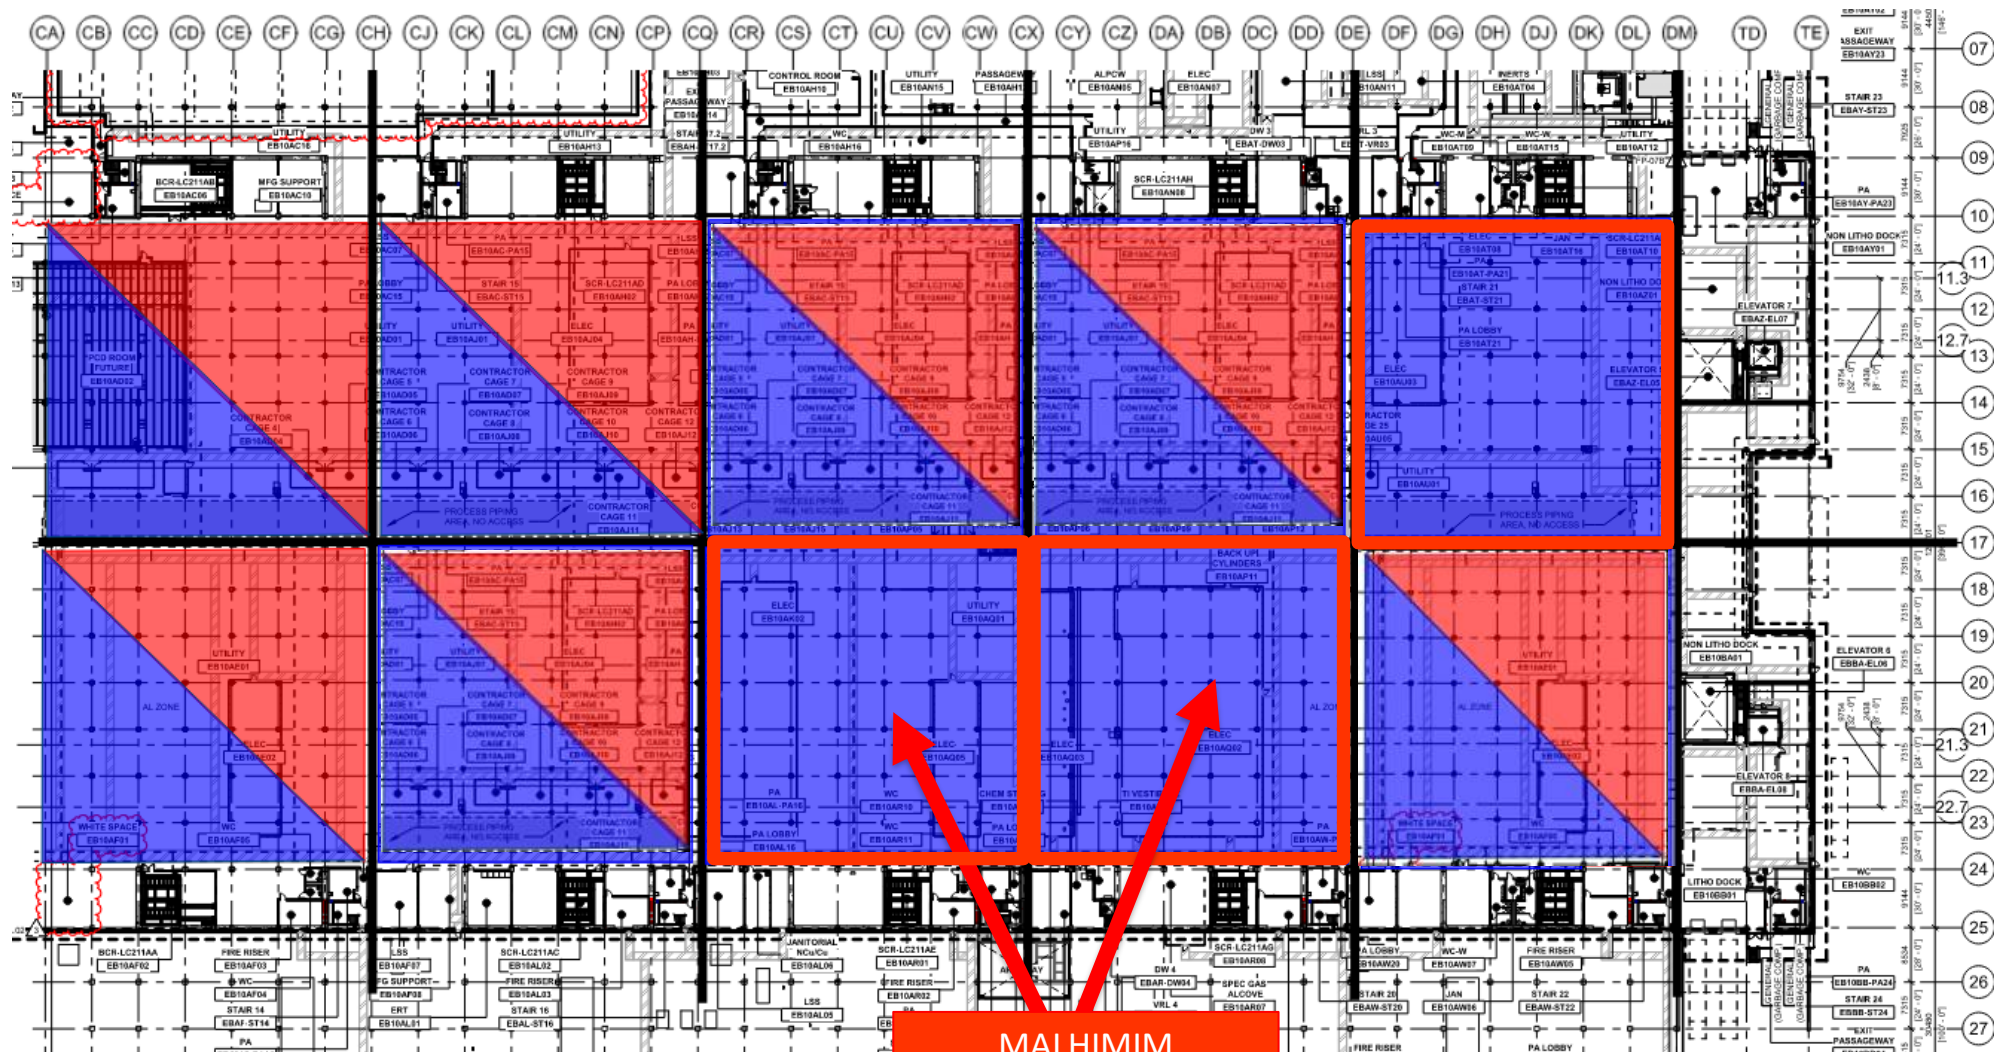


MALHIMIM
8W & 9W
Ongoing




SUT PRESS TEST

Meptagon
PCW Pres. Test
12/22
17:00 -5:00

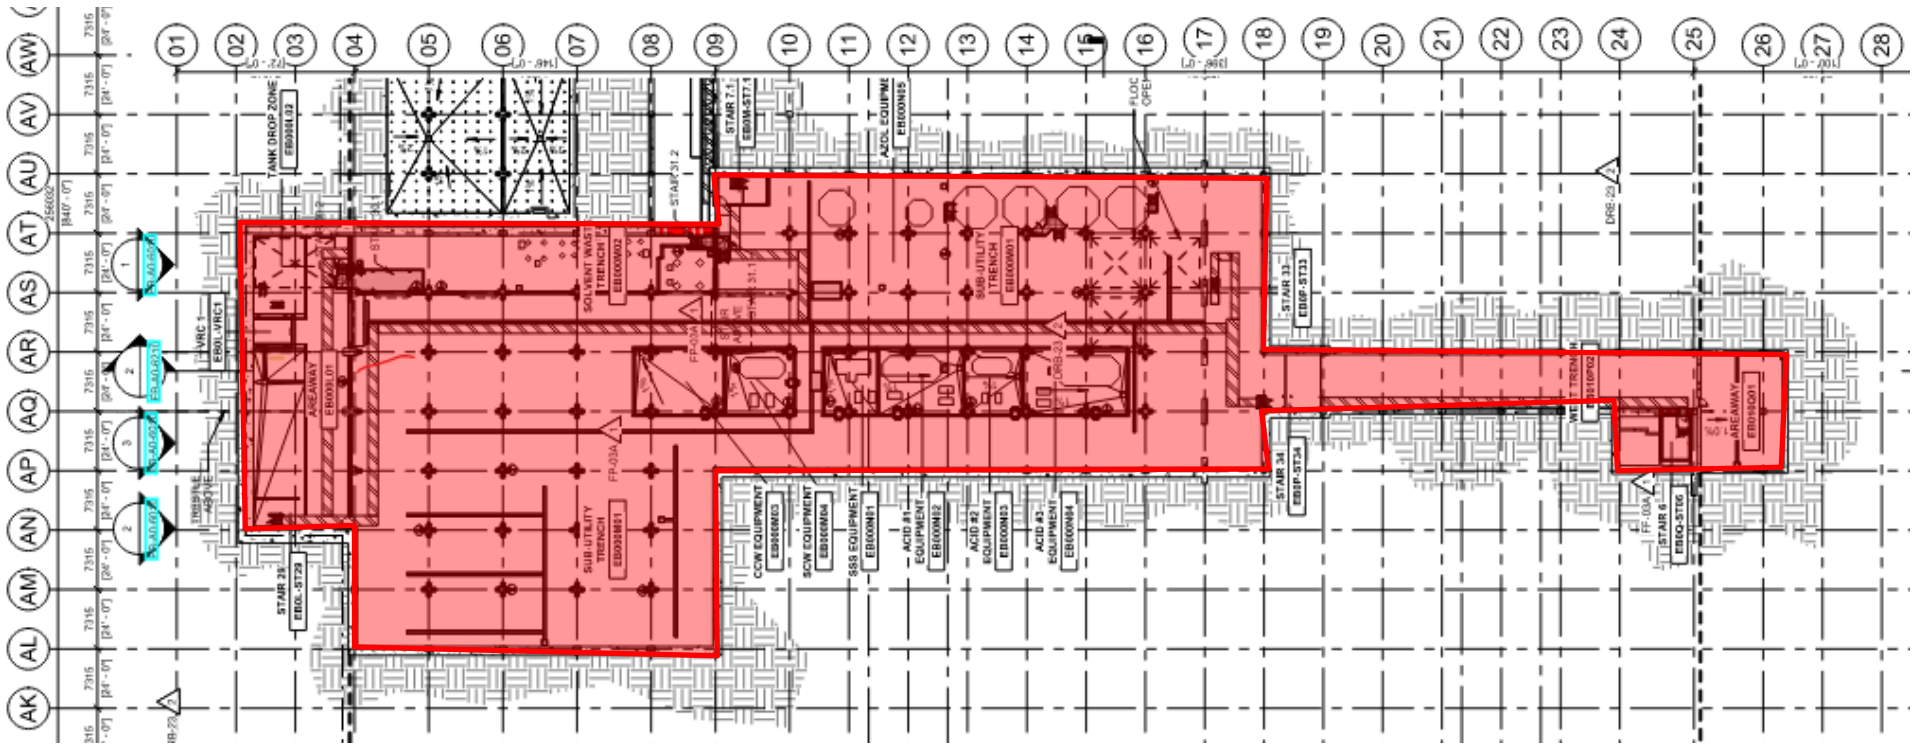




SUT 38.1 LEVEL

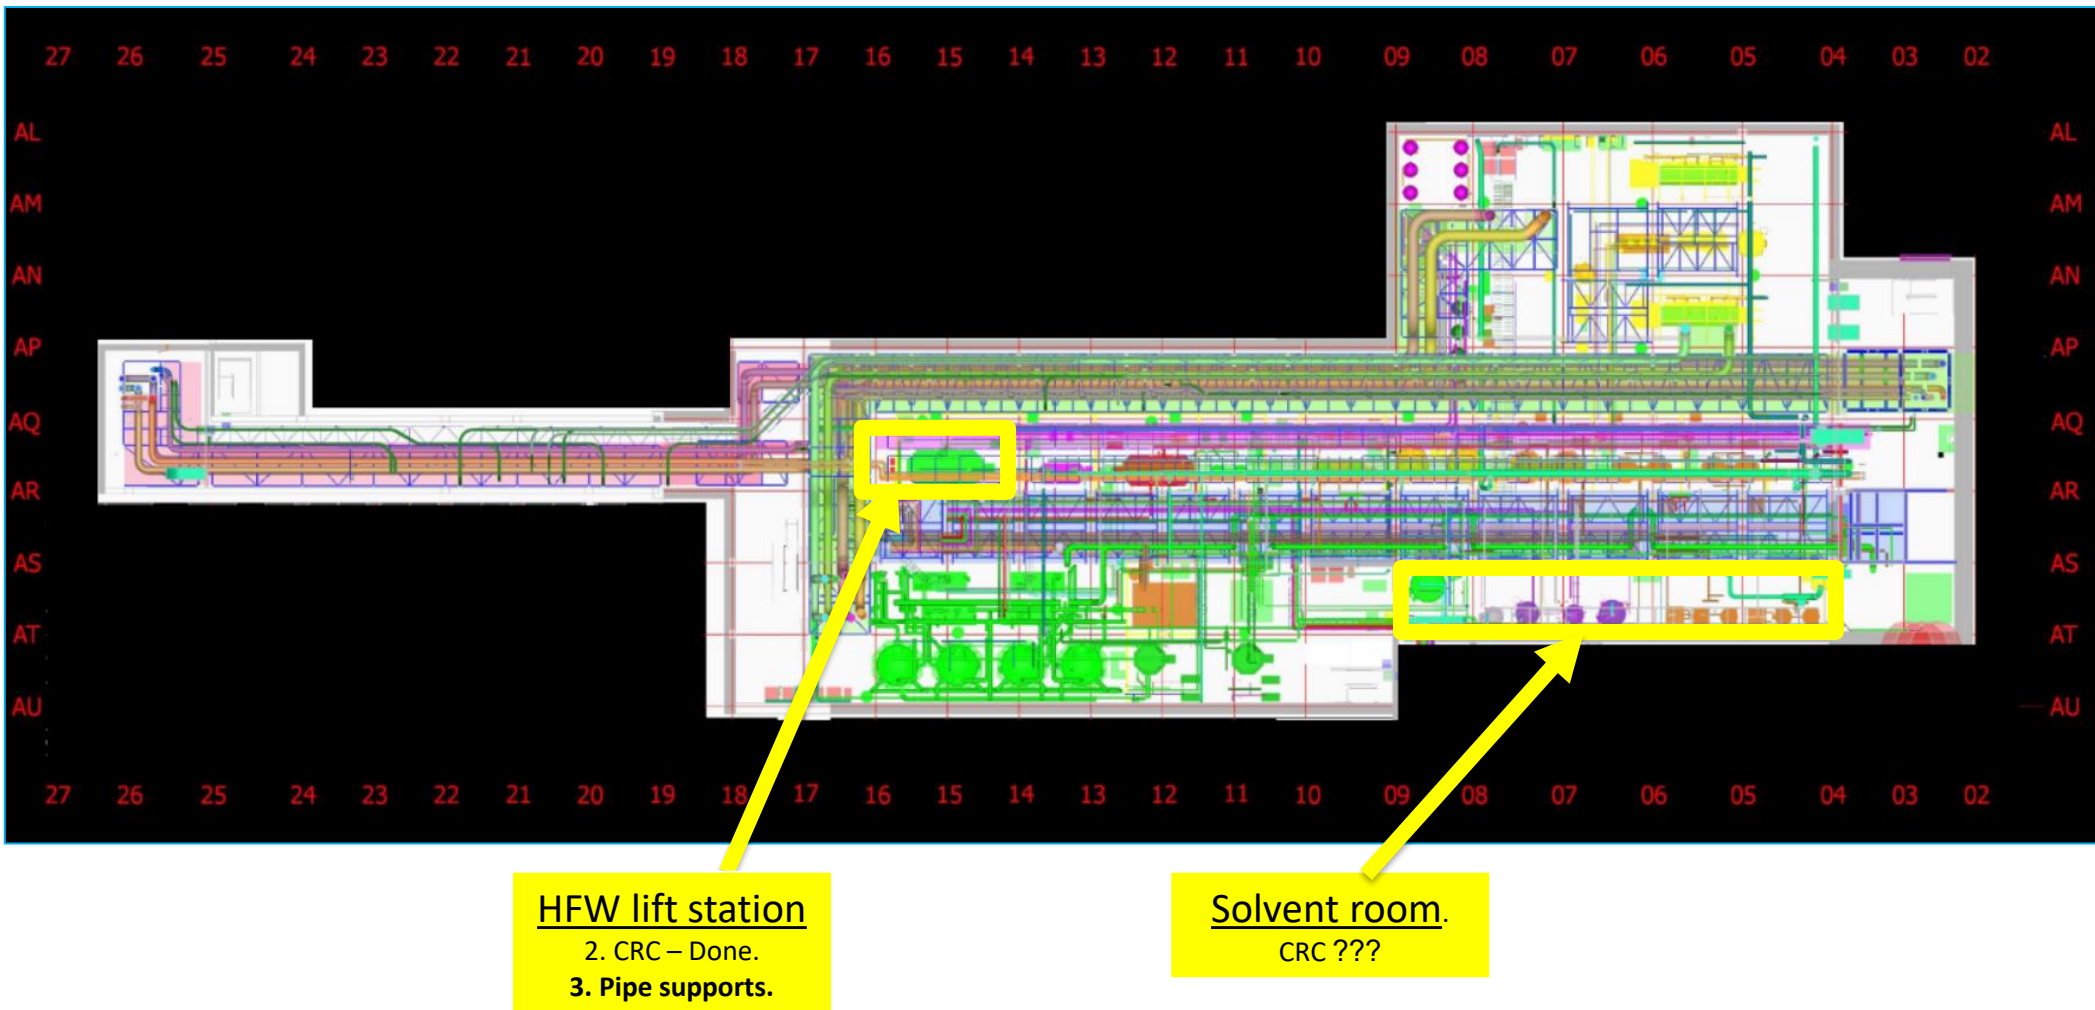

SUT 38.2 LEVEL

Rack 4b
Lifting
schedule
#3-16/12v
#4 – 22/12
#5 – 26/12

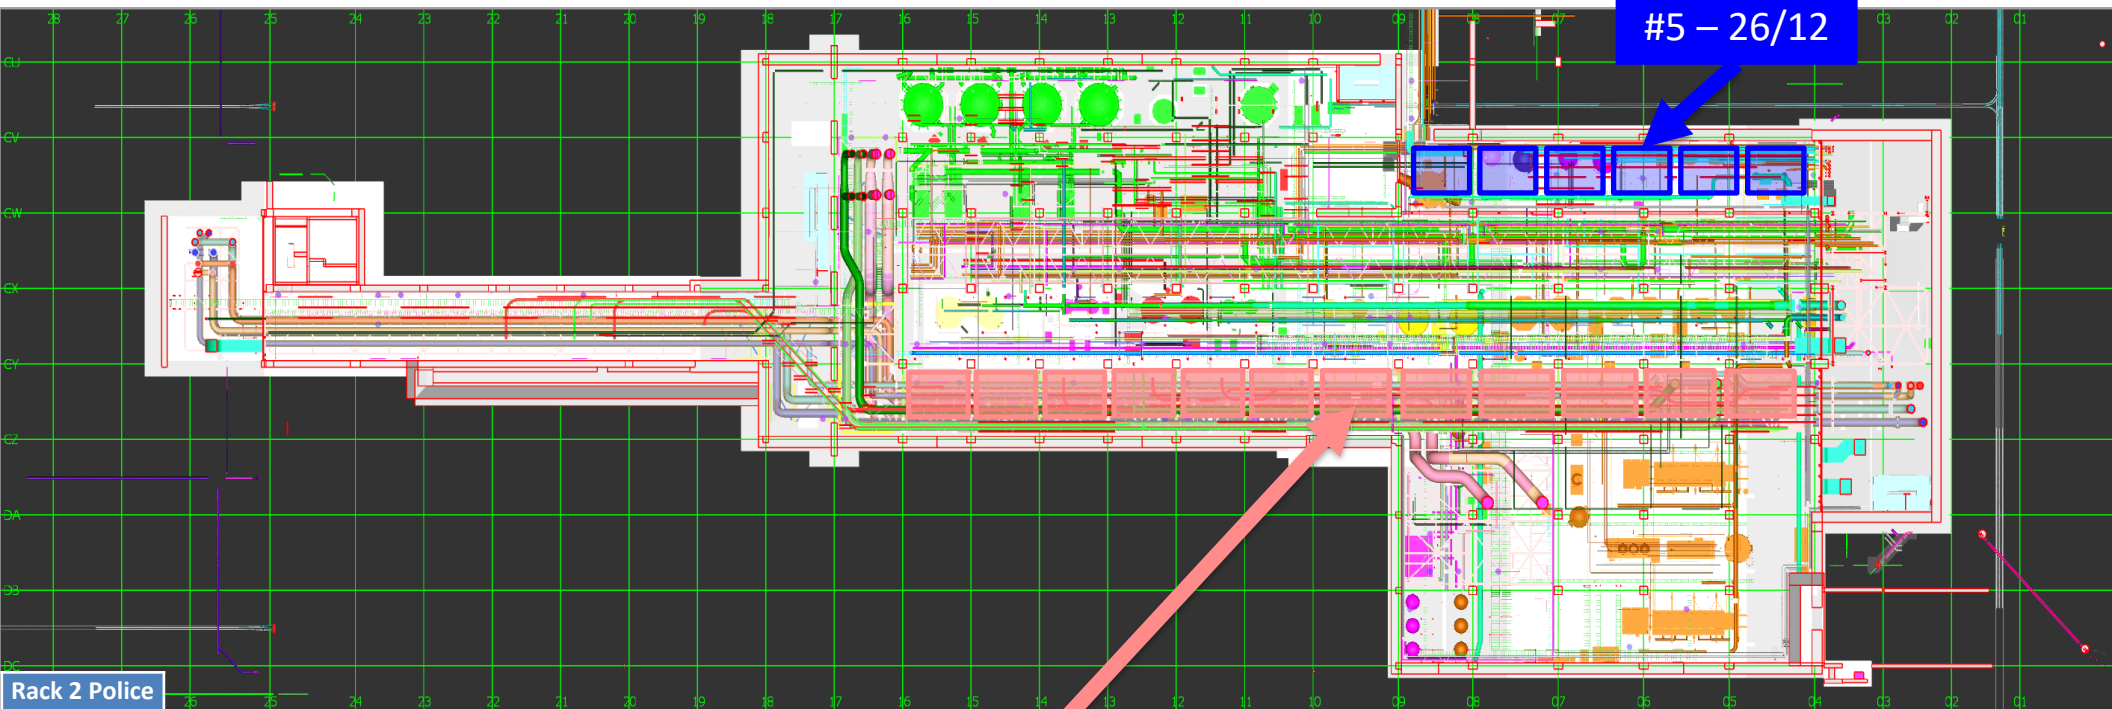


**Rack 2 Police
escort dates**


24.11.24
25.11.24
3.12.24
9.12.24
12.12.24
15.12.24
17.12.24
22.12.24
5.1.25
14.1.25
2.2.25
9.2.25

Rack 2
MIMO -
Module #7
17th of Dec


SUBFAB BUILDOUT MOD 1

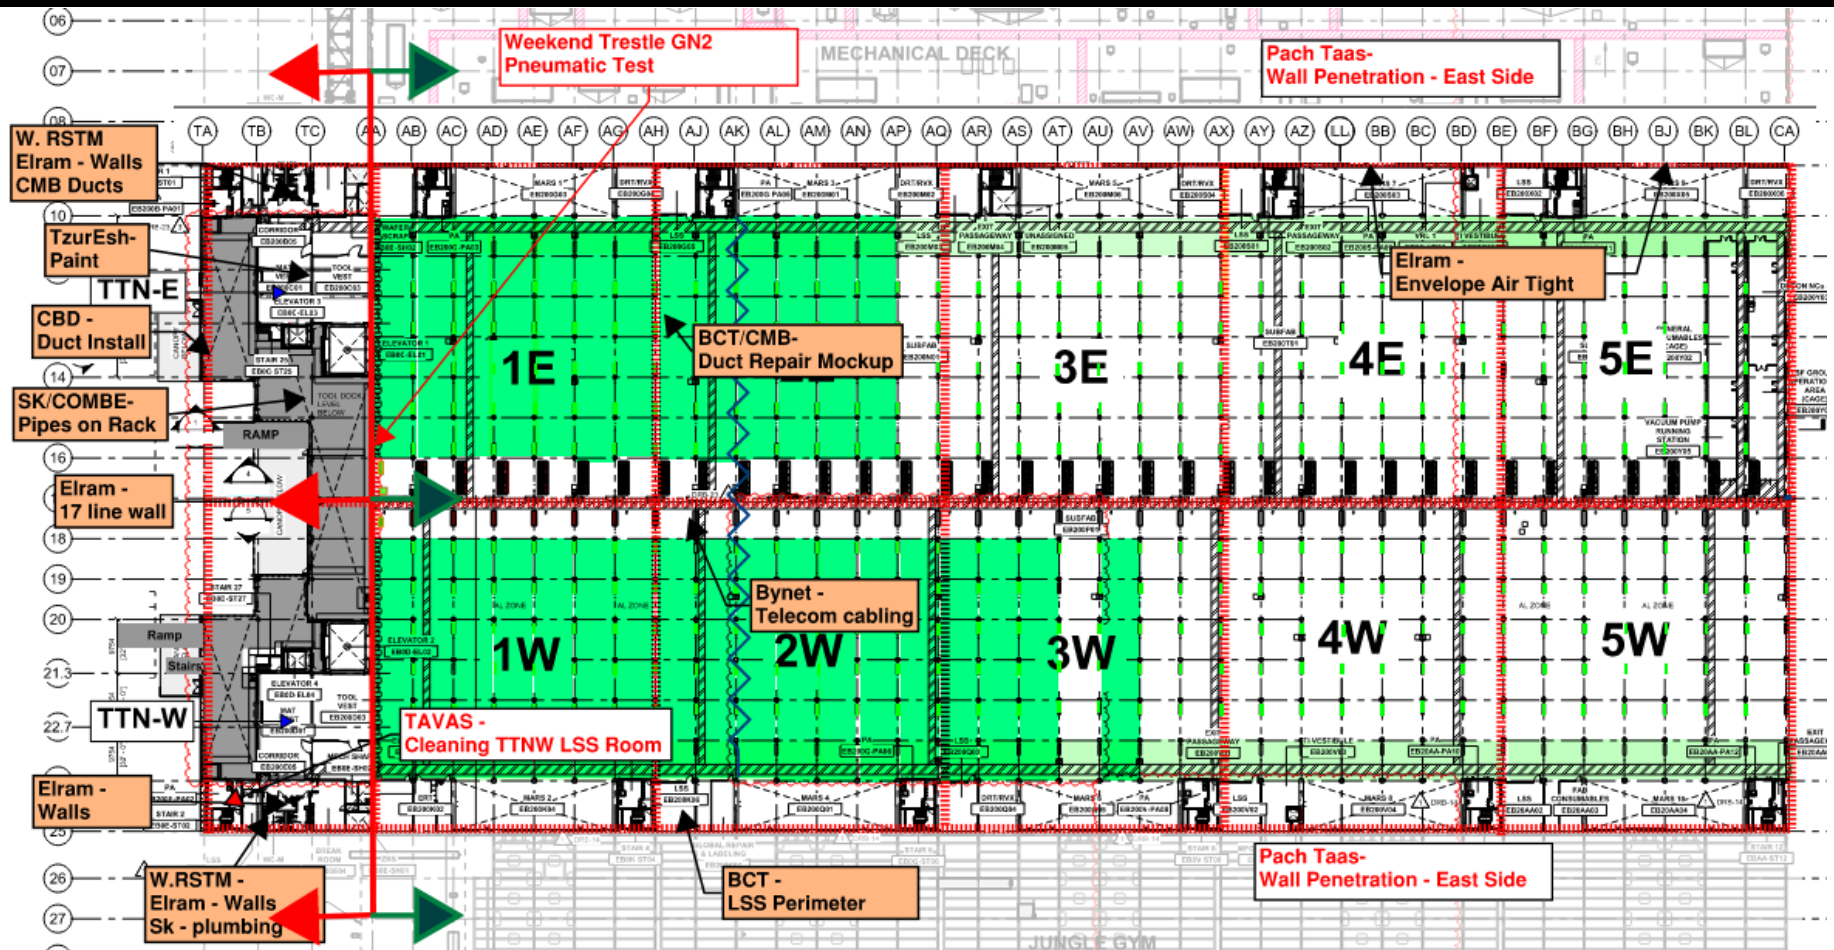


SUBFAB CRC TOPCOAT

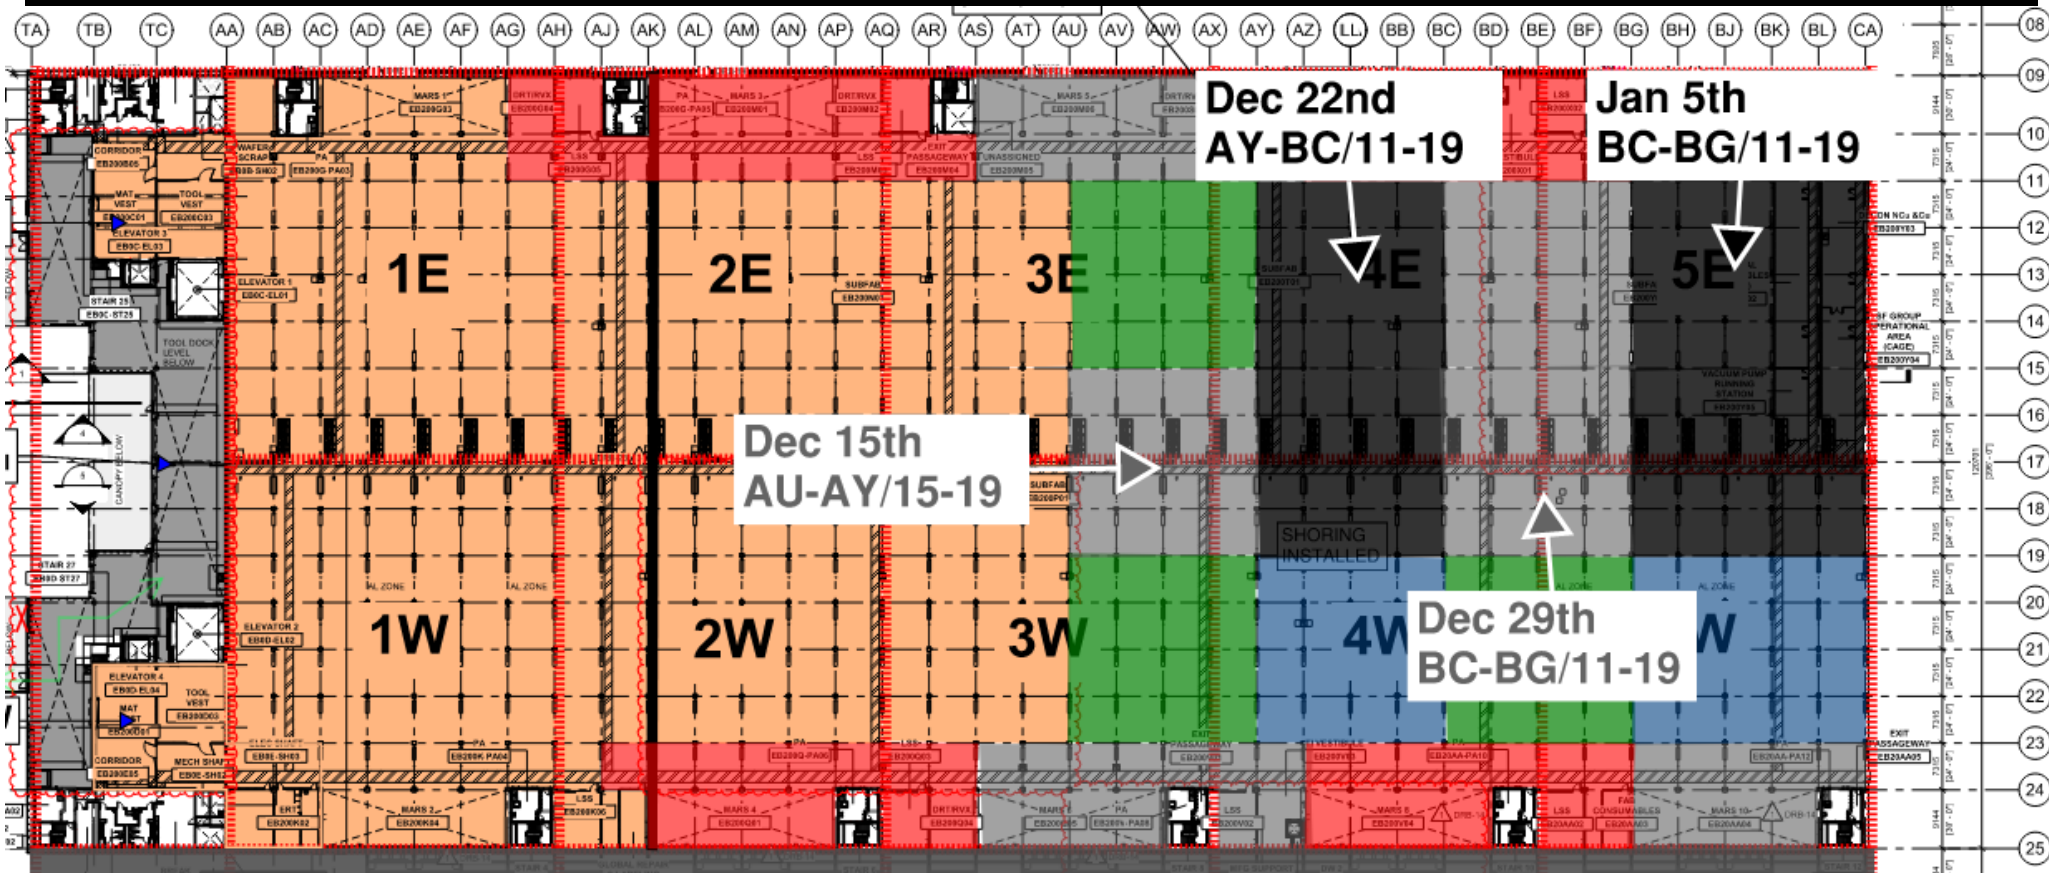


BCT Pressure Test Today

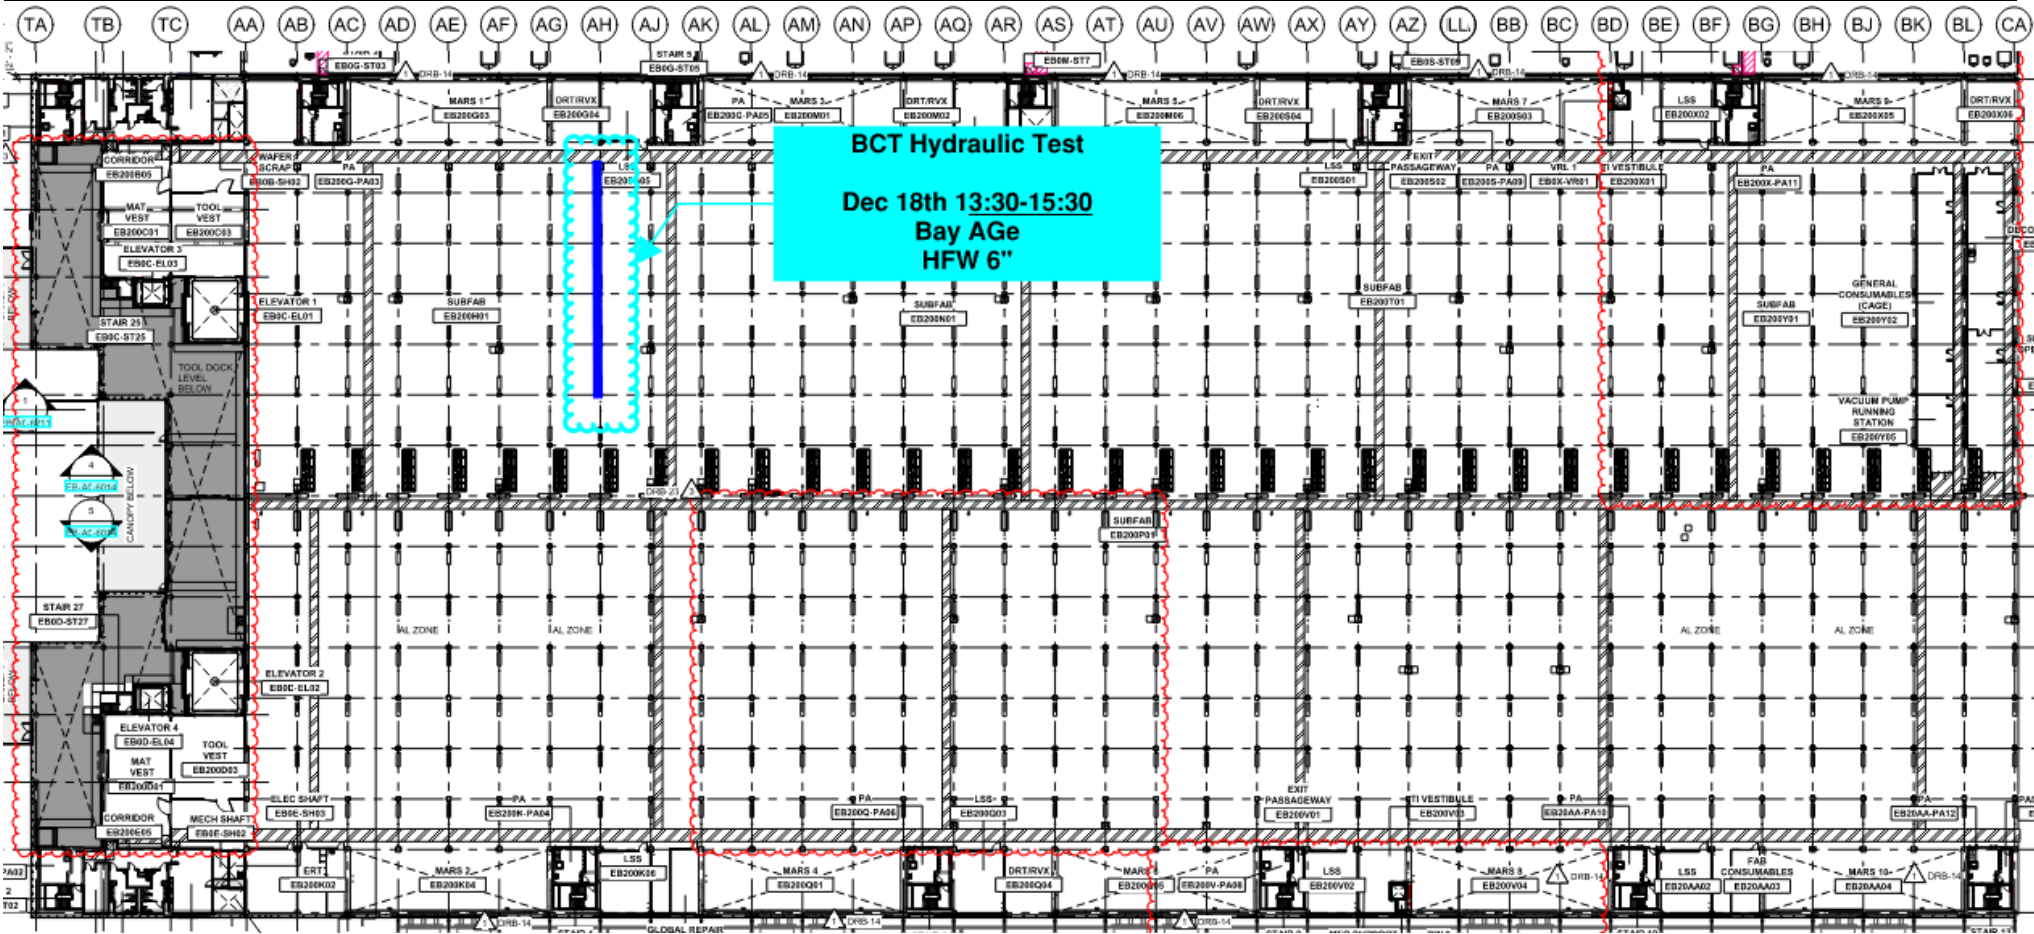


BCT Pressure Test Sunday

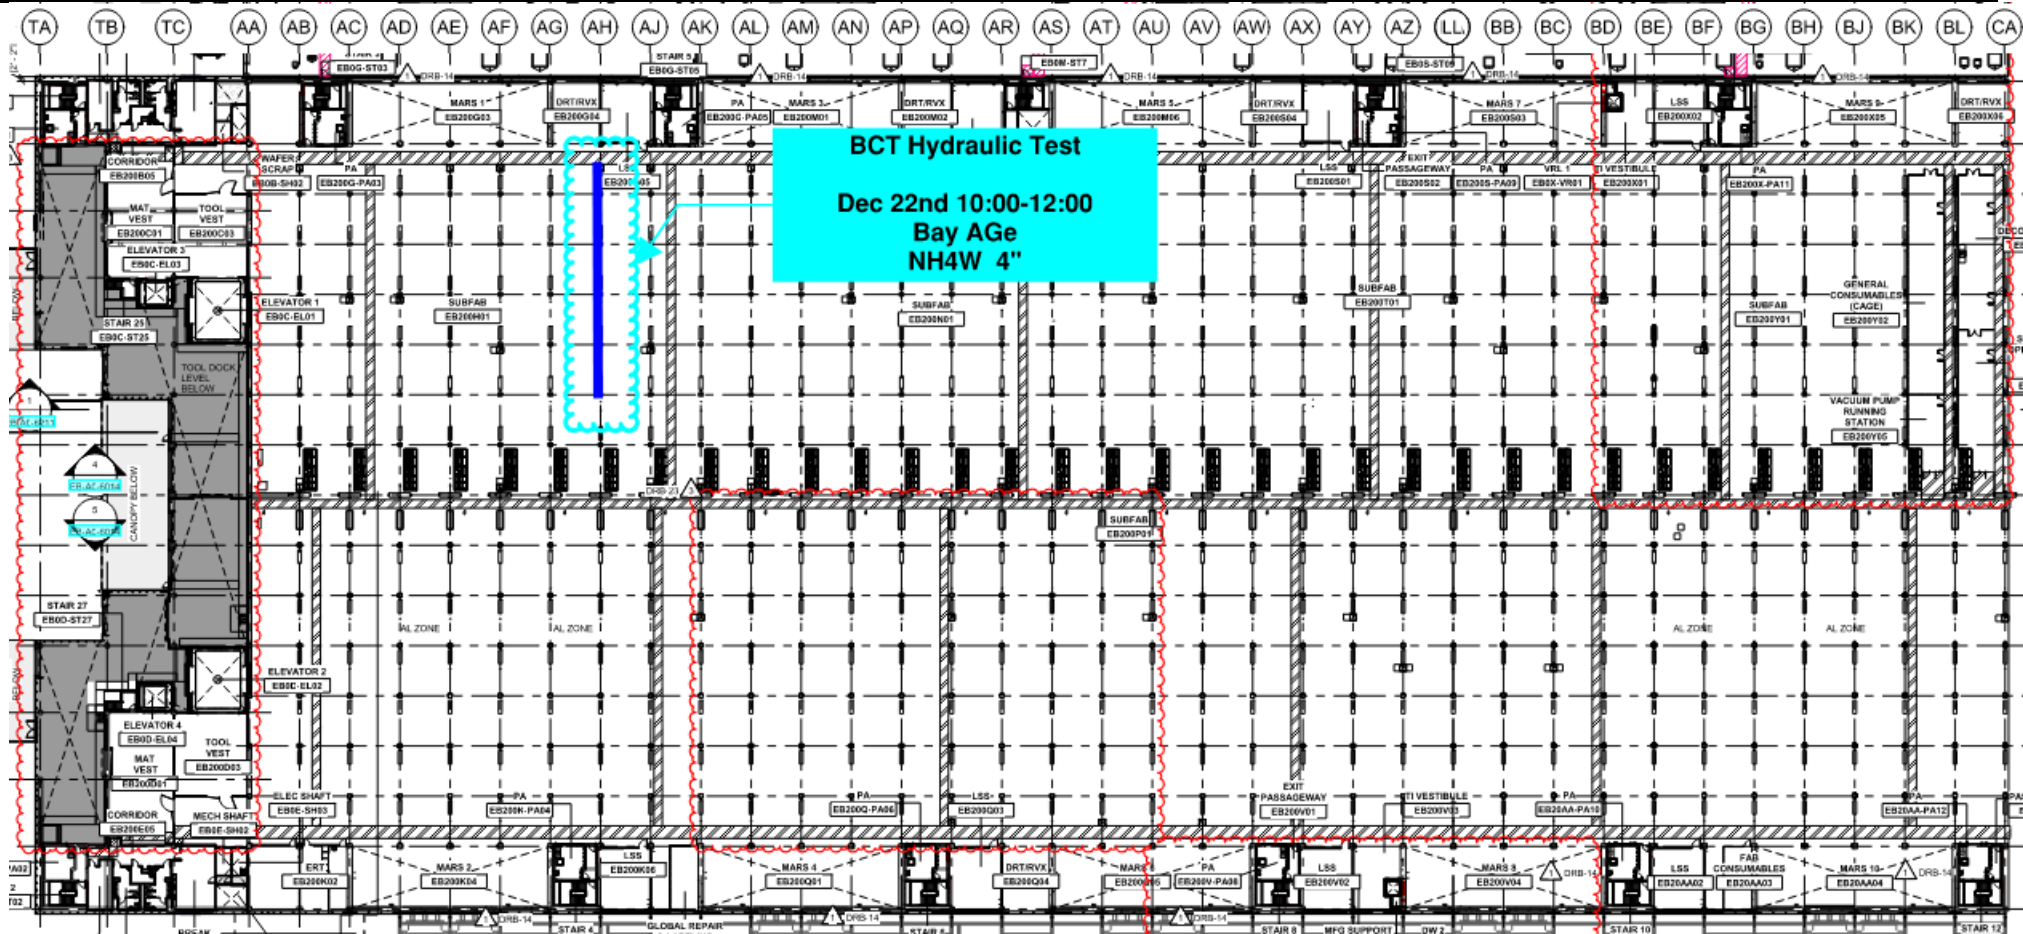

SUBFAB BUILDOUT MOD 2

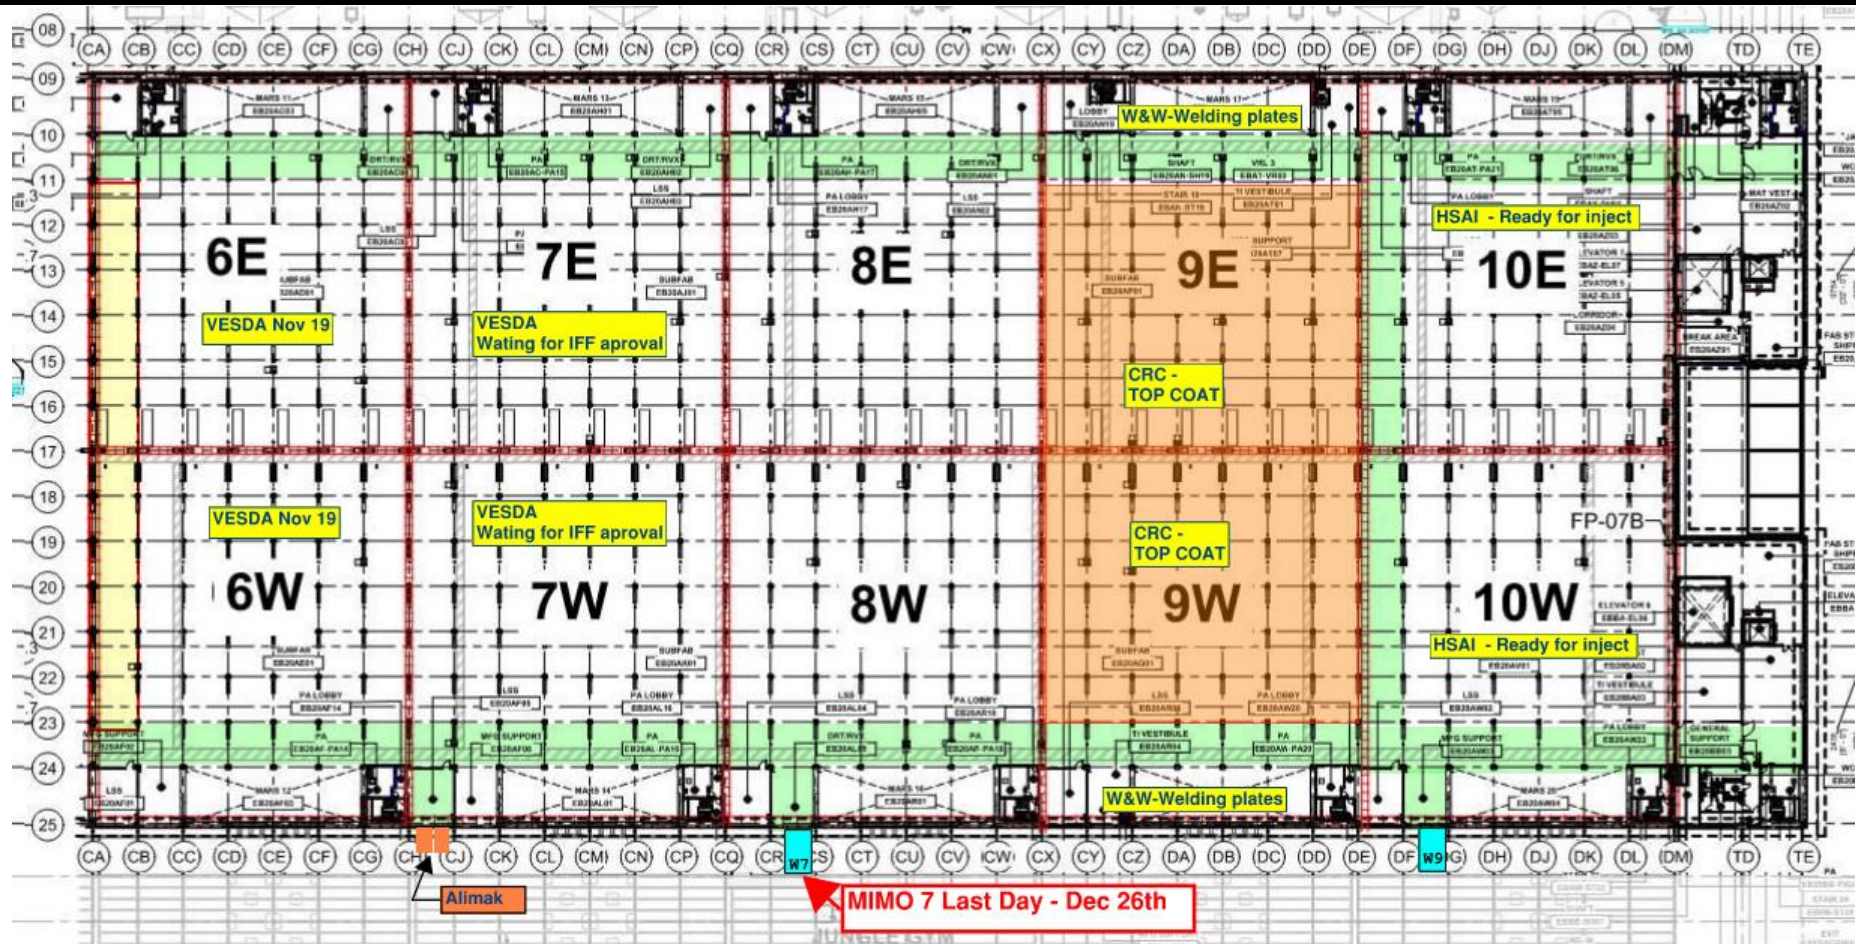

SUBFAB BUILDOUT BULLET PROOF

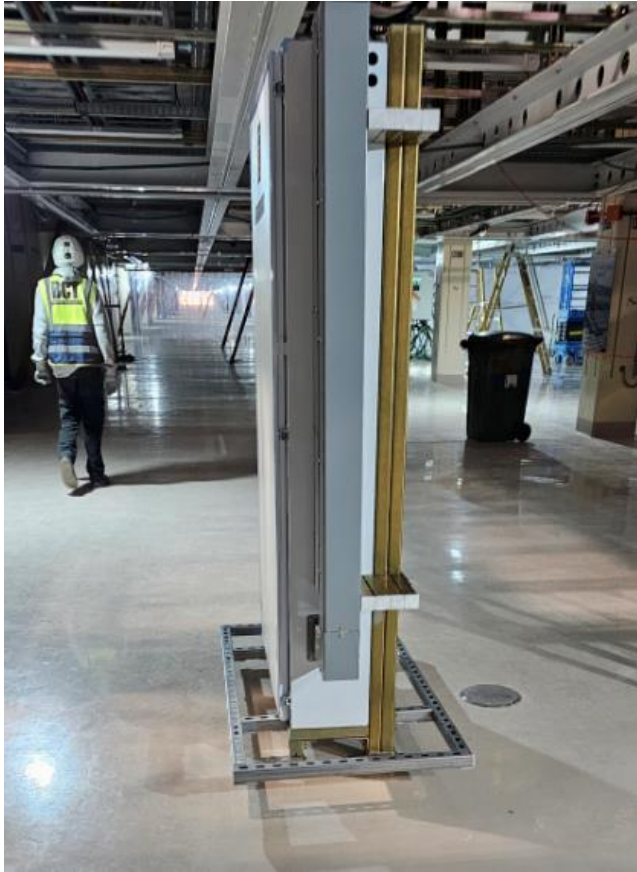

**Meptagon LSS
GDP Panels.**






60% Blow down area- AK-AZ
Start to plan where to stage material


NO activity allowed due to NG2 test TTNE/W


CR level:

- Afcon - Cable trays, modules and stickers
- MB- Pipes and drops
- Elram - 9-10,24-25 columns/shaft walls. 17 line column wraps
- Meptagon - EMT Pipes+devices. TET/NET devices all areas
- D&P - Rods install, seismic cables
- Tzur-esh - 5E blades. Paint rust on columns
- HYG - Shaft beams install
- Talad - 1W cutting around steel lids. UPN install

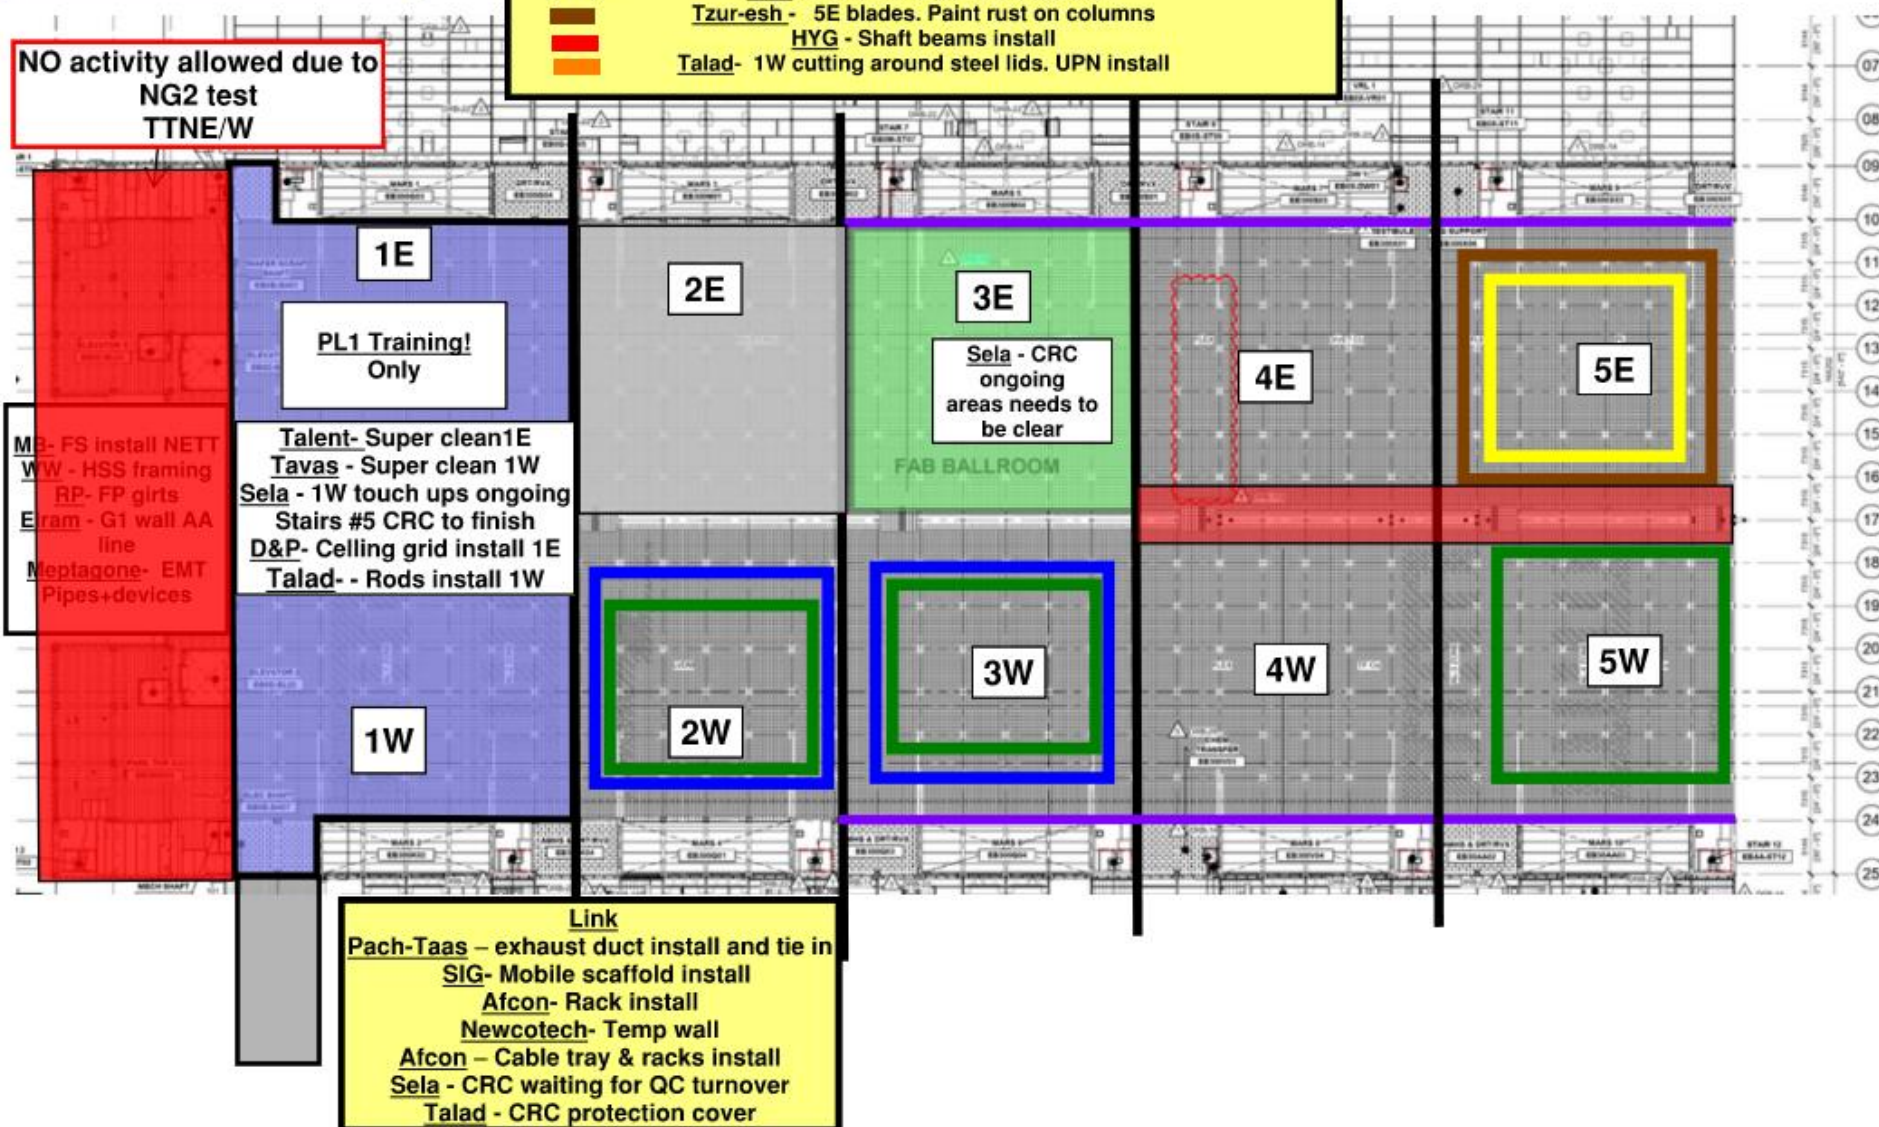

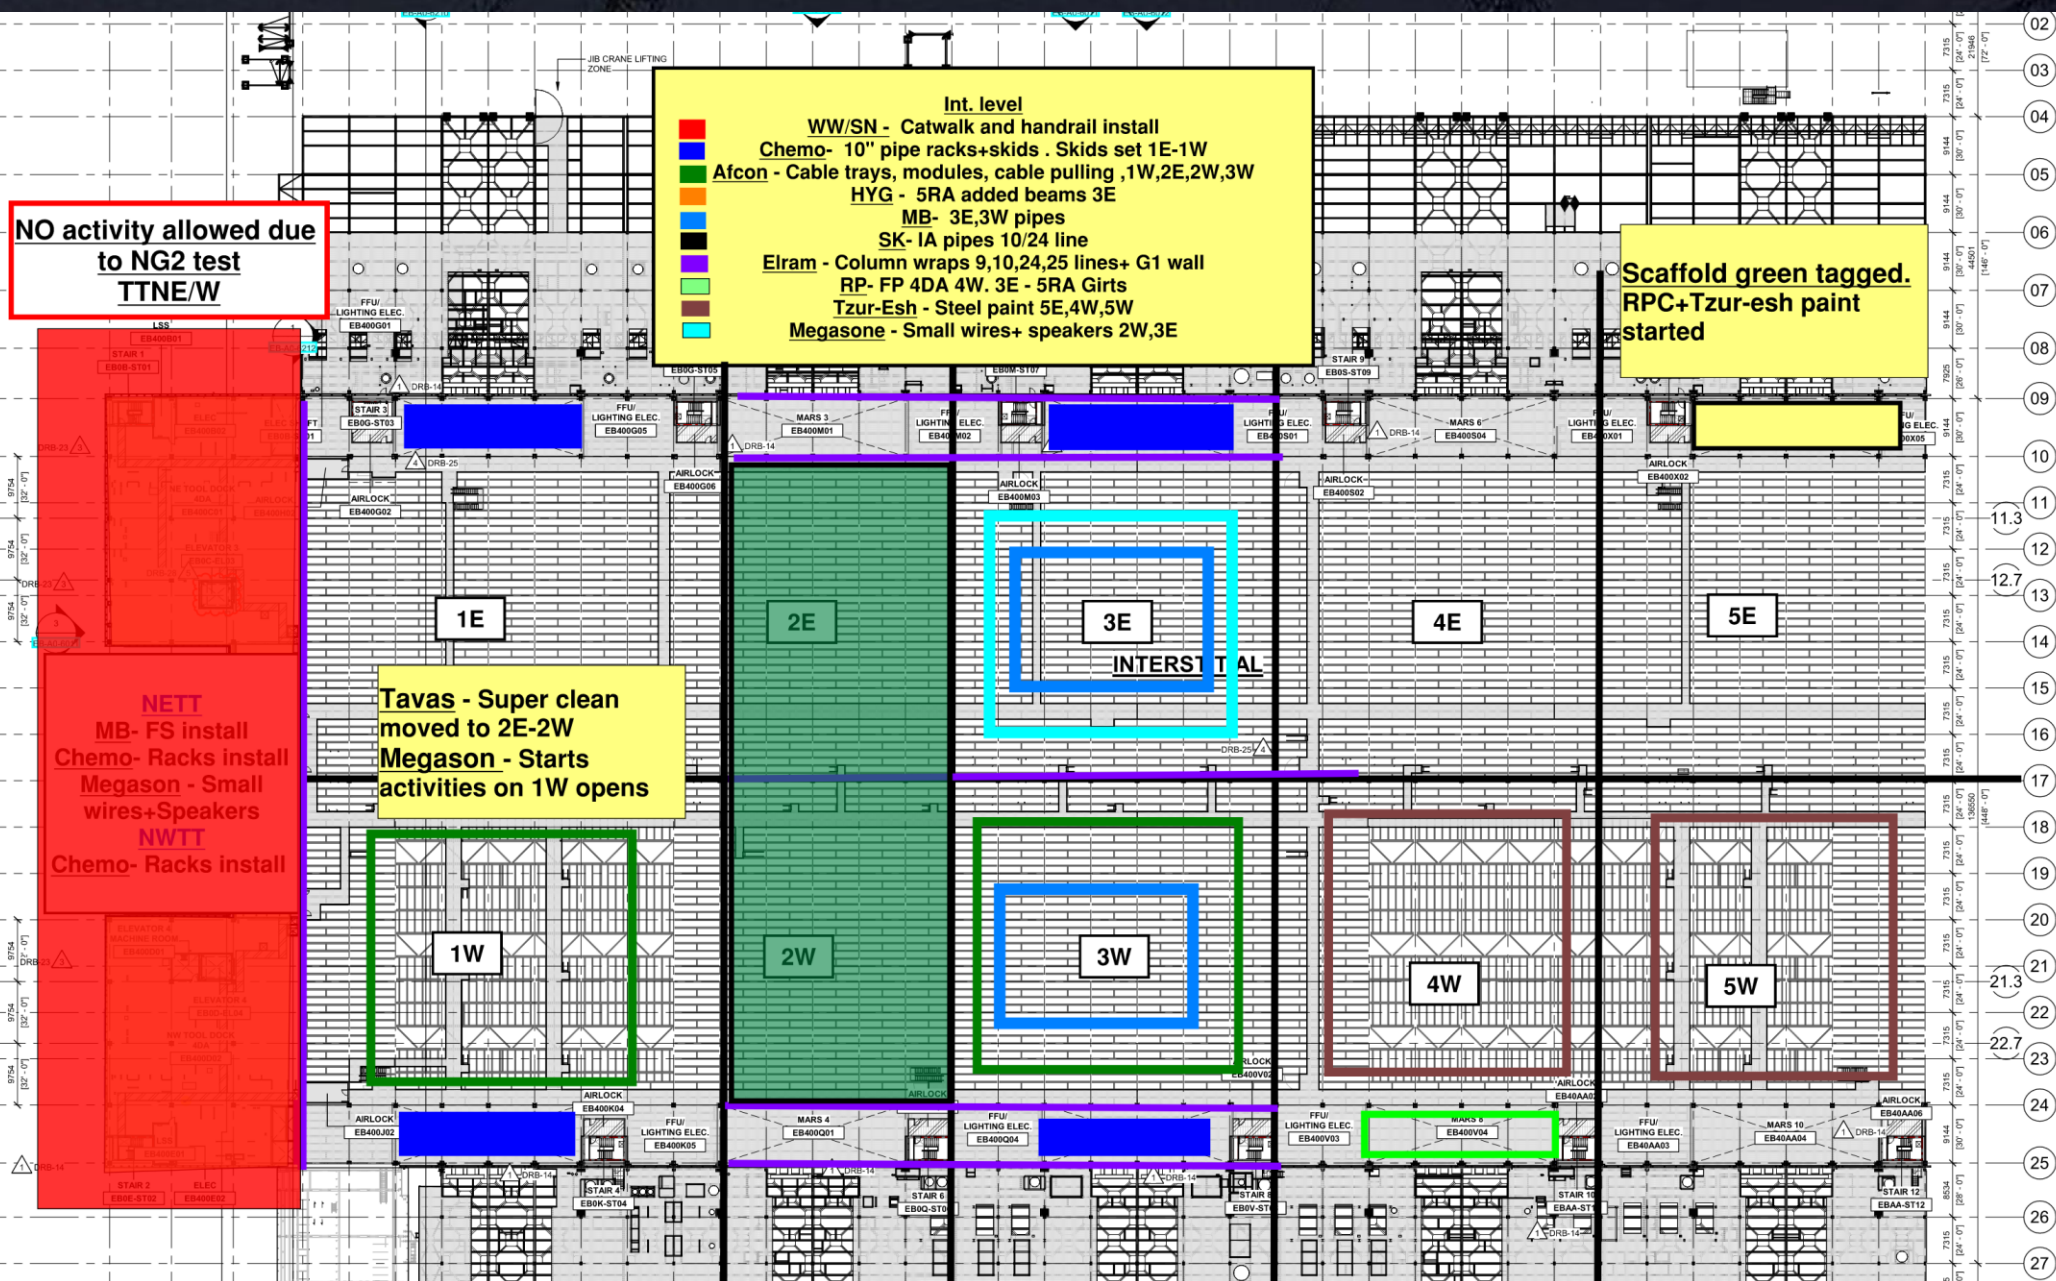

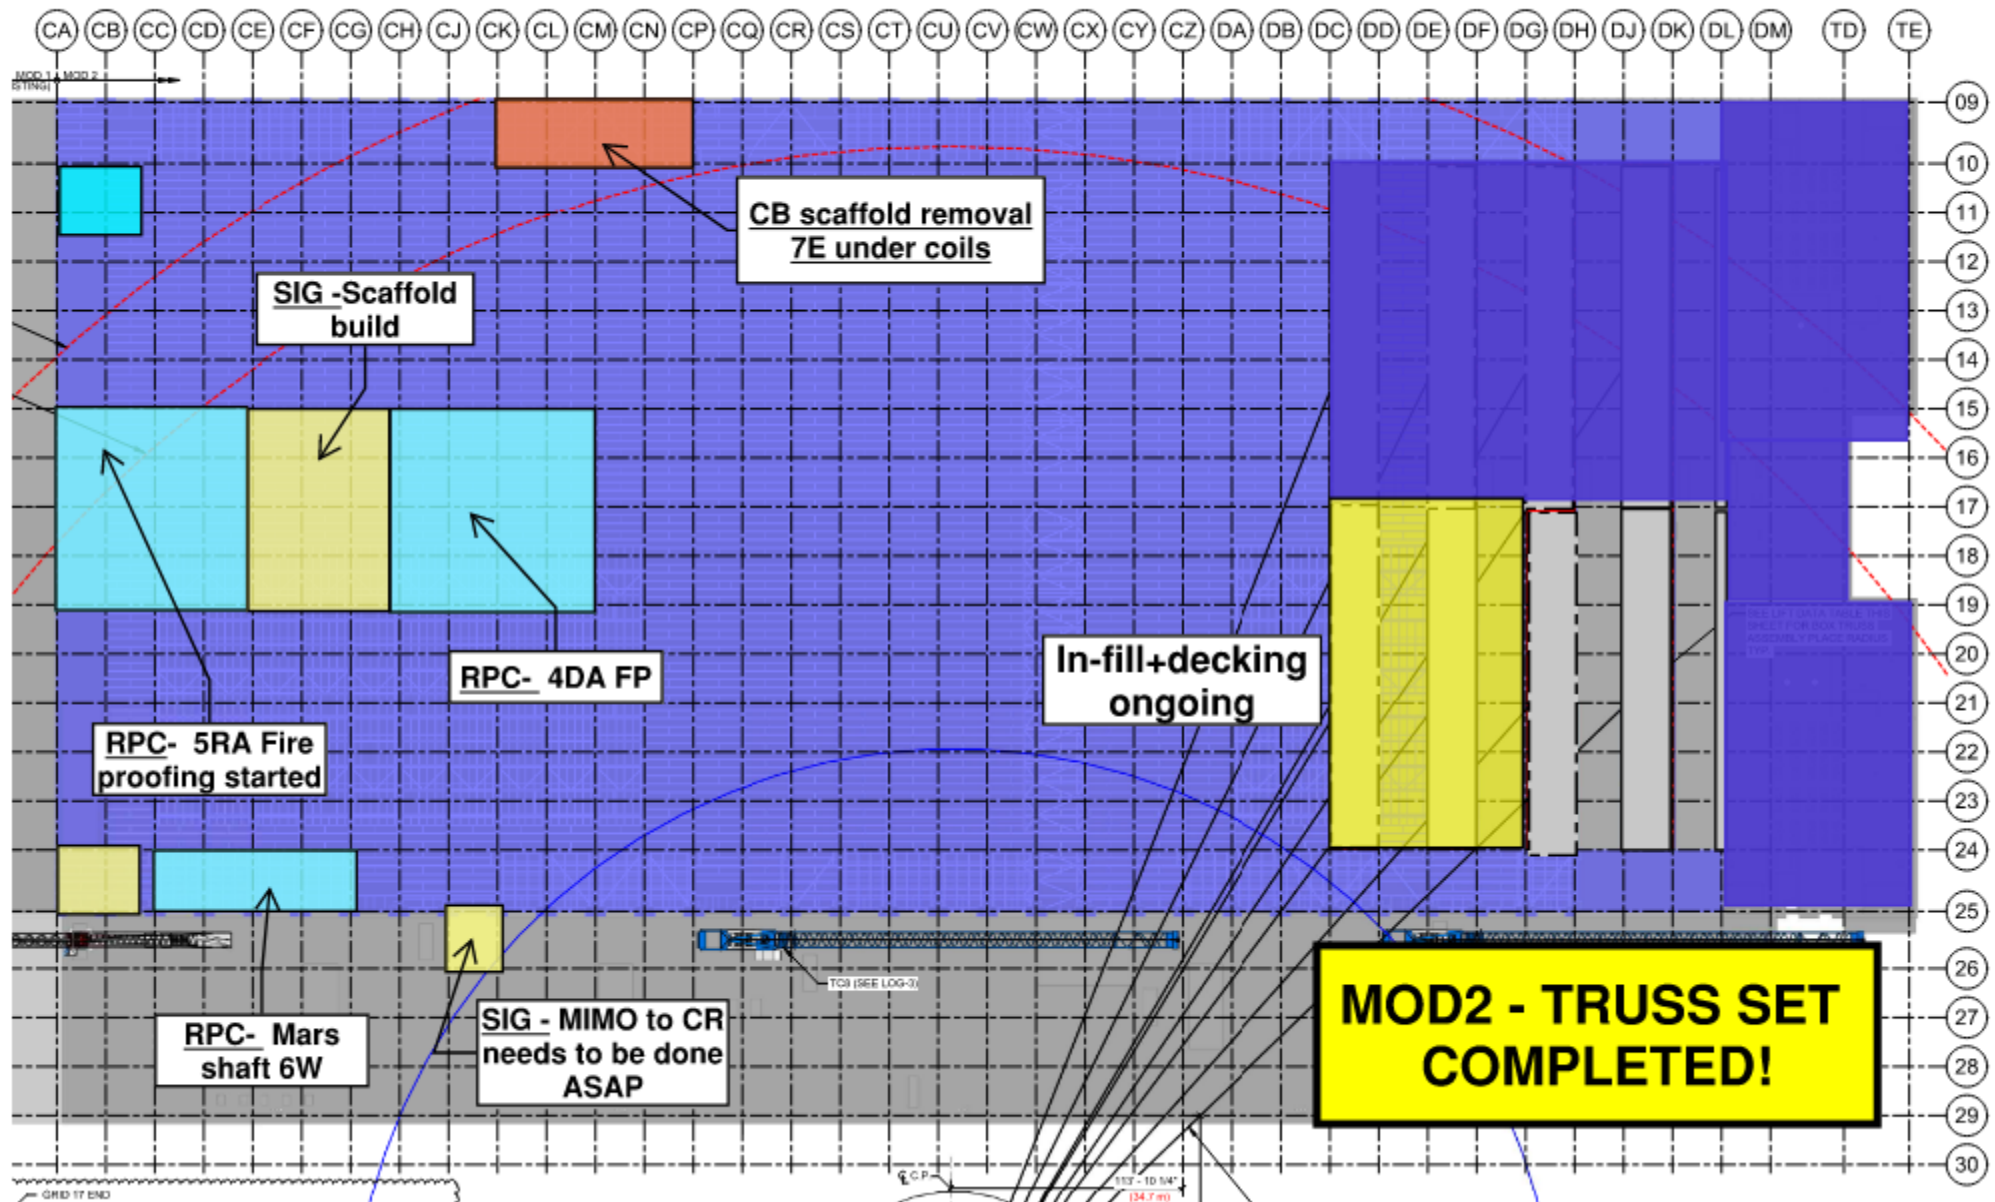

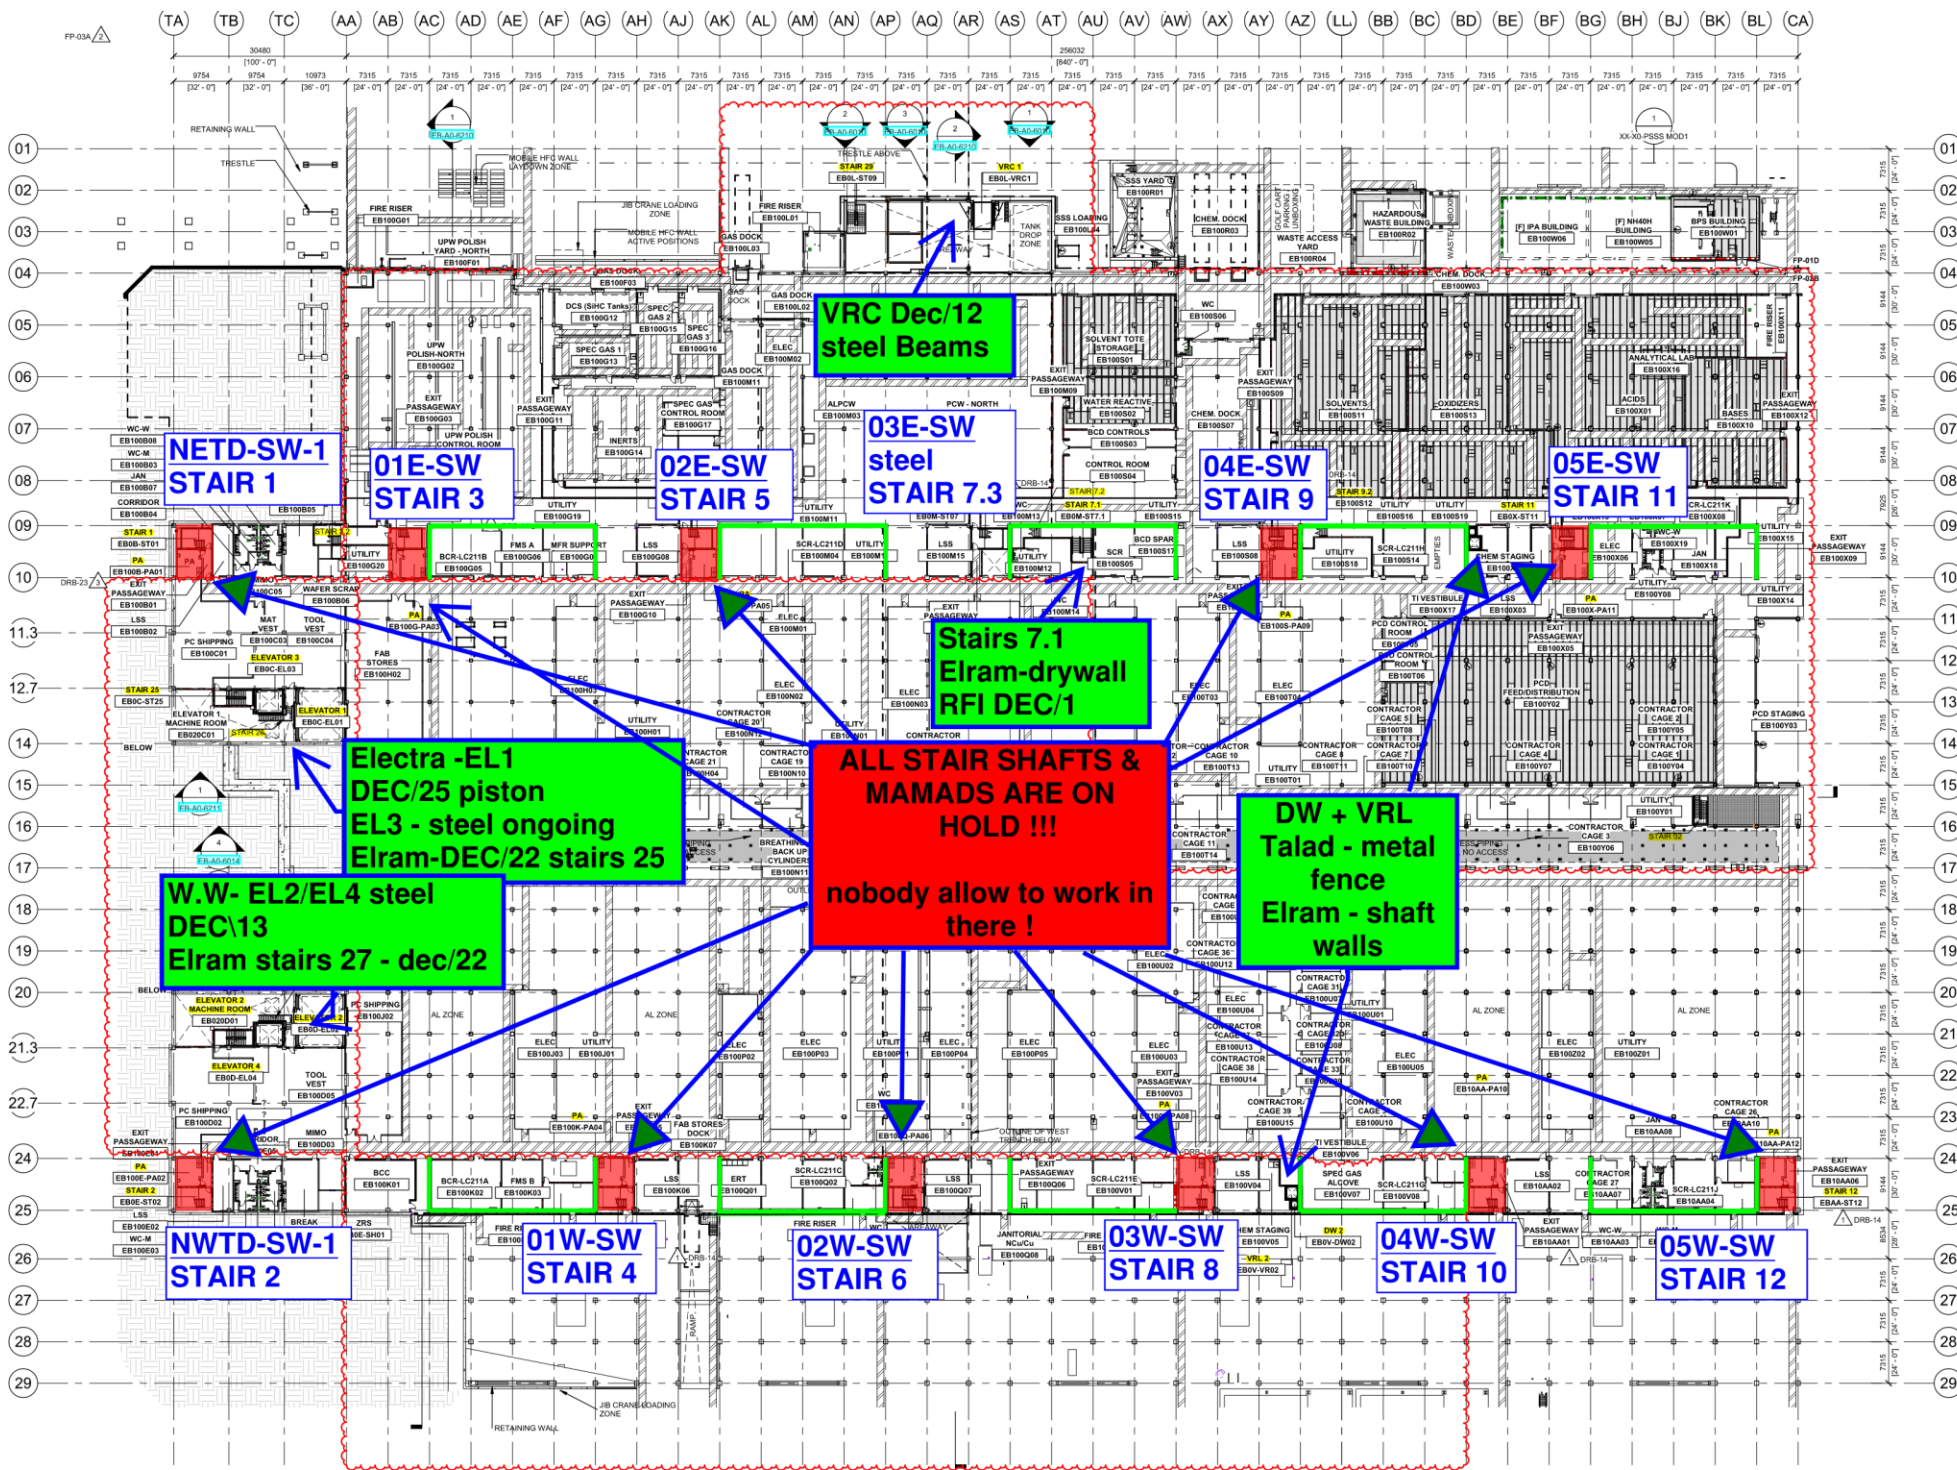

Siding - West FAB - JYG


BLOWDOWN 30%

[illegible]


Siding - East FAB - PSSS


BLOWDOWN 30%

CA	CB	CC	CD	CE	CF	CG	CH	CI	CJ	CK	CL	CM	CN	CO	CP	CQ	CR	CS	CT	CU	CV	CW	CX	CY	CZ	DA	DB	DC	DD	DE	DF	DG	DH	DI	DJ	DK	DL	DM	DN	DO	DP	DQ	DR	DS	DT	DU	DV	DW	DX	DY	DZ	EA	EB	EC	ED	EE	EF	EG	EH	EI	EJ	EK	EL	EM	EN	EO	EP	EQ	ER	ES	ET	EU	EV	EW	EX	EY	EZ	FA	FB	FC	FD	FE	FF	FG	FH	FI	FJ	FK	FL	FM	FN	FO	FP	FQ	FR	FS	FT	FU	FV	FW	FX	FY	FZ	GA	GB	GC	GD	GE	GF	GG	GH	GI	GJ	GK	GL	GM	GN	GO	GP	GQ	GR	GS	GT	GU	GV	GW	GX	GY	GZ	HA	HB	HC	HD	HE	HF	HG	HH	HI	HJ	HK	HL	HM	HN	HO	HP	HQ	HR	HS	HT	HU	HV	HW	HX	HY	HZ	IA	IB	IC	ID	IE	IF	IG	IH	II	IJ	IK	IL	IM	IN	IO	IP	IQ	IR	IS	IT	IU	IV	IW	IX	IY	IZ	JA	JB	JC	JD	JE	JF	JG	JH	JI	IJ	JK	JL	JM	JN	JO	JP	JQ	JR	JS	JT	JU	JV	JW	JX	JY	JZ	KA	KB	KC	KD	KE	KF	KG	KH	KI	KJ	KK	KL	KM	KN	KO	KP	KQ	KR	KS	KT	KU	KV	KW	KX	KY	KZ	LA	LB	LC	LD	LE	LF	LG	LH	LI	LJ	LK	LM	LN	LO	LP	LQ	LR	LS	LT	LU	LV	LW	LX	LY	LZ	MA	MB	MC	MD	ME	MF	MG	MH	MI	MJ	MK	ML	MM	MN	MO	MP	MQ	MR	MS	MT	MU	MV	MW	MX	MY	MZ	NA	NB	NC	ND	NE	NF	NG	NH	NI	NJ	NK	NL	NM	NN	NO	NP	NQ	NR	NS	NT	NU	NV	NW	NX	NY	NZ	OA	OB	OC	OD	OE	OF	OG	OH	OI	OJ	OK	OL	OM	ON	OO	OP	OQ	OR	OS	OT	OU	OV	OW	OX	OY	OZ	PA	PB	PC	PD	PE	PF	PG	PH	PI	PJ	PK	PL	PM	PN	PO	PP	PQ	PR	PS	PT	PU	PV	PW	PX	PY	PZ	QA	QB	QC	QD	QE	QF	QG	QH	QI	QJ	QK	QL	QM	QN	QO	QP	QQ	QR	QS	QT	QU	QV	QW	QX	QY	QZ	RA	RB	RC	RD	RE	RF	RG	RH	RI	RJ	RK	RL	RM	RN	RO	RP	RQ	RR	RS	RT	RU	RV	RW	RX	RY	RZ	SA	SB	SC	SD	SE	SF	SG	SH	SI	SJ	SK	SL	SM	SN	SO	SP	SQ	SR	SS	ST	SU	SV	SW	SX	SY	SZ	TA	TB	TC	TD	TE	TF	TG	TH	TI	TJ	TK	TL	TM	TN	TO	TP	TQ	TR	TS	TT	TU	TV	TW	TX	TY	TZ	UA	UB	UC	UD	UE	UF	UG	UH	UI	UJ	UK	UL	UM	UN	UO	UP	UQ	UR	US	UT	UU	UV	UW	UX	UY	UZ	VA	VB	VC	VD	VE	VF	VG	VH	VI	VJ	VK	VL	VM	VN	VO	VP	VQ	VR	VS	VT	VU	VV	VW	VX	VY	VZ	WA	WB	WC	WD	WE	WF	WG	WH	WI	WJ	WK	WL	WM	WN	WO	WP	WQ	WR	WS	WT	WU	WV	WW	WX	WY	WZ	XA	XB	XC	XD	XE	XF	YG	YH	YI	YJ	YK	YL	YM	YN	YO	YP	YQ	YR	YS	YT	YU	YV	YW	YX	YY	YZ	ZA	ZB	ZC	ZD	ZE	ZF	ZG	ZH	ZI	ZJ	ZK	ZL	ZM	ZN	ZO	ZP	ZQ	ZR	ZS	ZT	ZU	ZV	ZW	ZX	ZY	ZZ
751/752		741/742		731/732		721/722		711/712		551/552		541/542		531/532		521/522		511/512		501/502		491/492		481/482		471/472		461/462		451/452		441/442		431/432		421/422		411/412		401/402		391/392		381/382		371/372		361/362		351/352		341/342		331/332		321/322		311/312		301/302		291/292		281/282		271/272		261/262		251/252		241/242		231/232		221/222		211/212		201/202		191/192		181/182		171/172		161/162		151/152		141/142		131/132		121/122		111/112		101/102		91/92		81/82		71/72		61/62		51/52		41/42		31/32		21/22		11/12		1/2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24	24</																																													

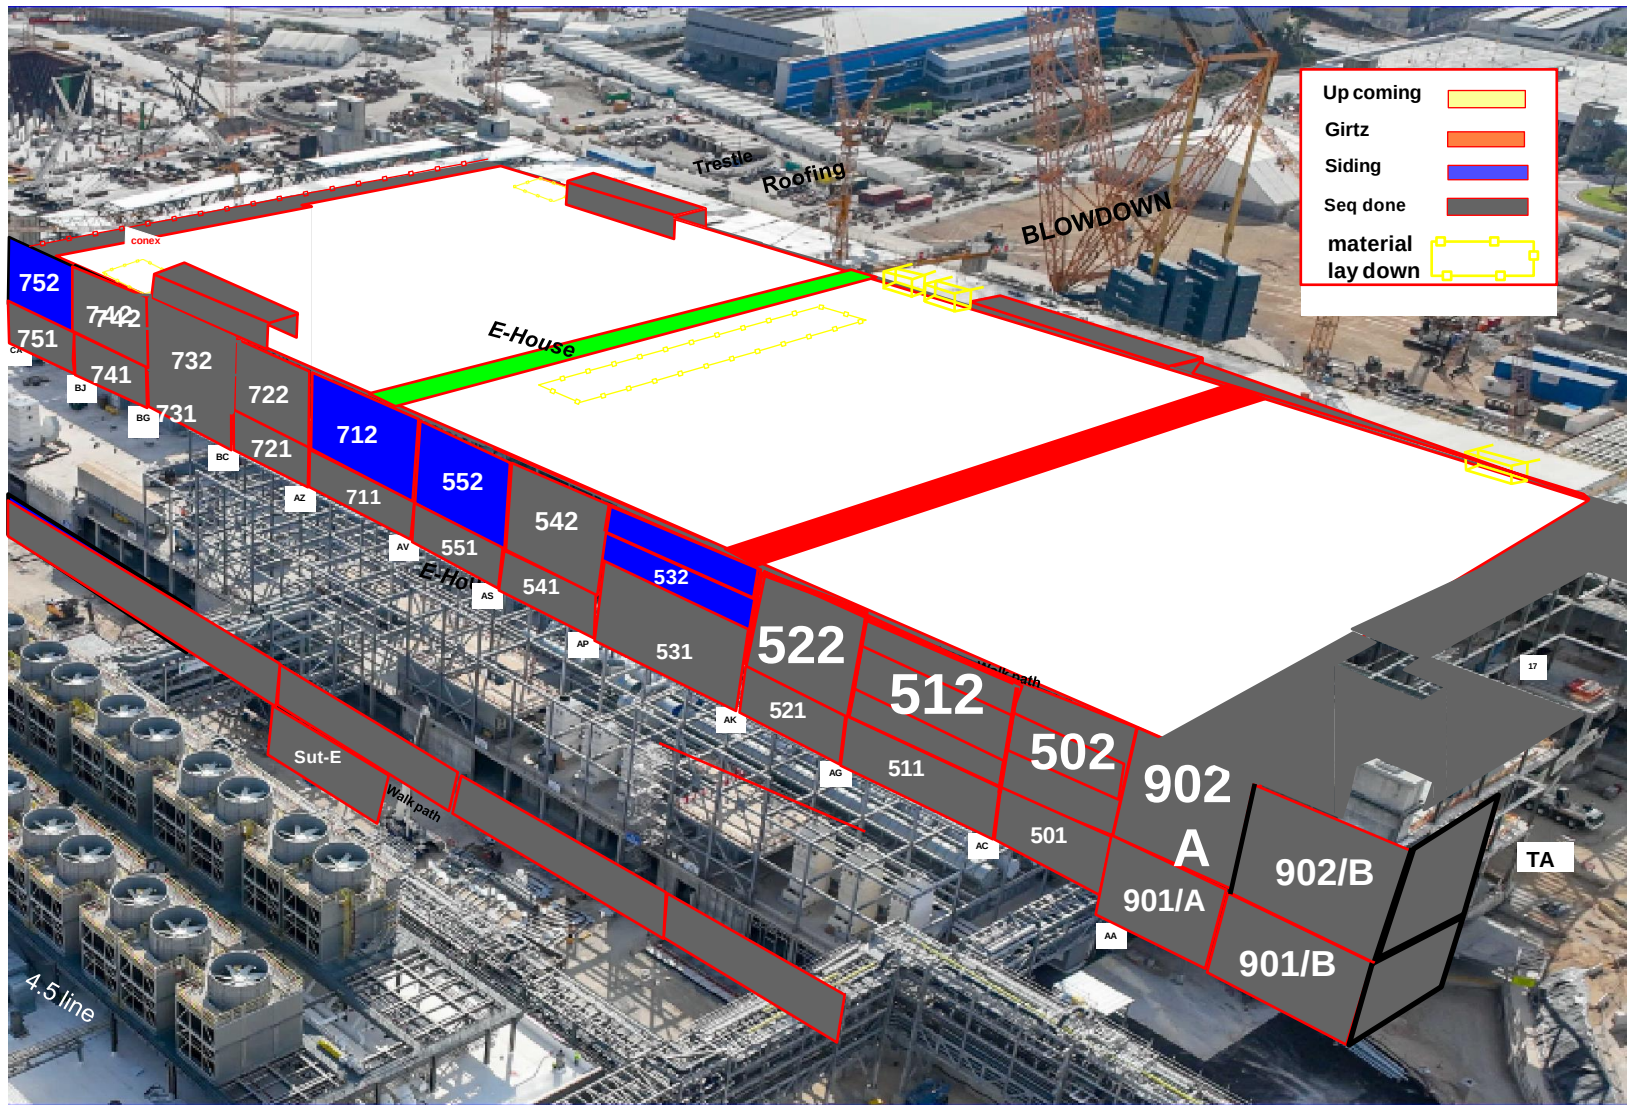

Walk path

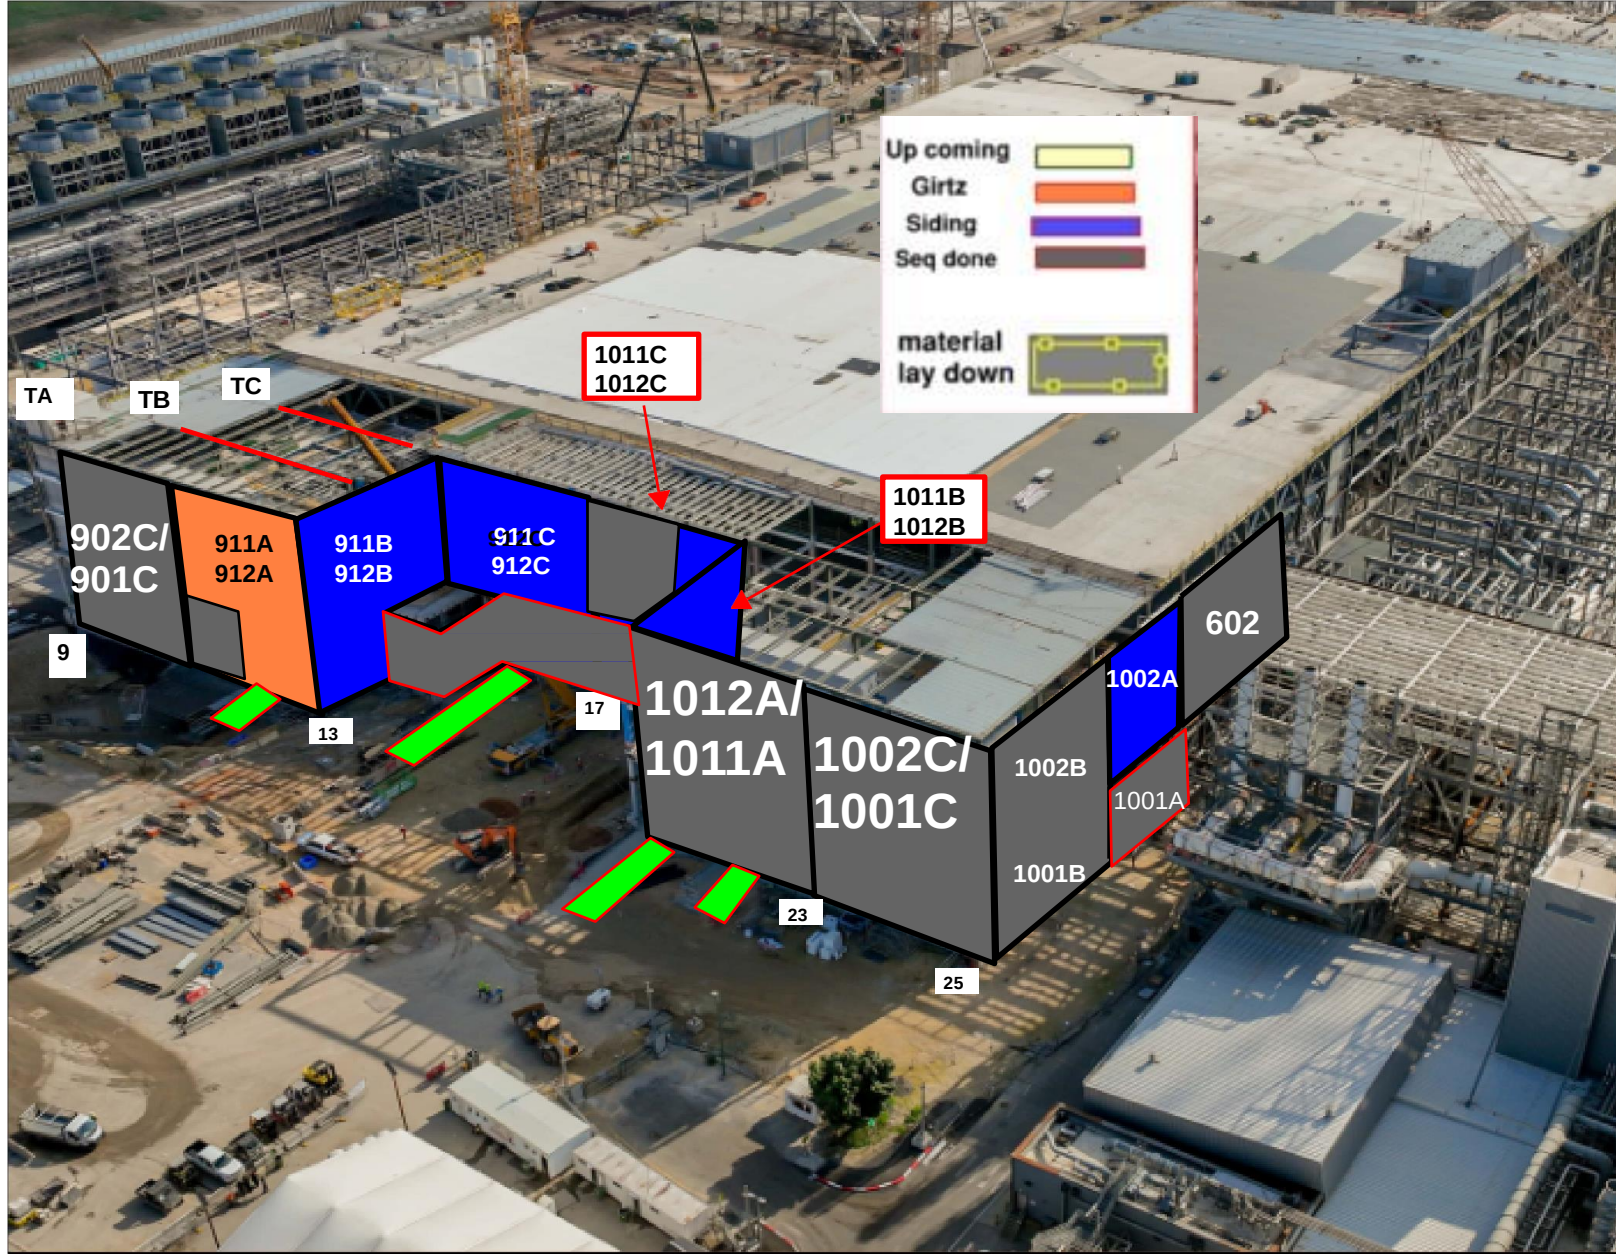


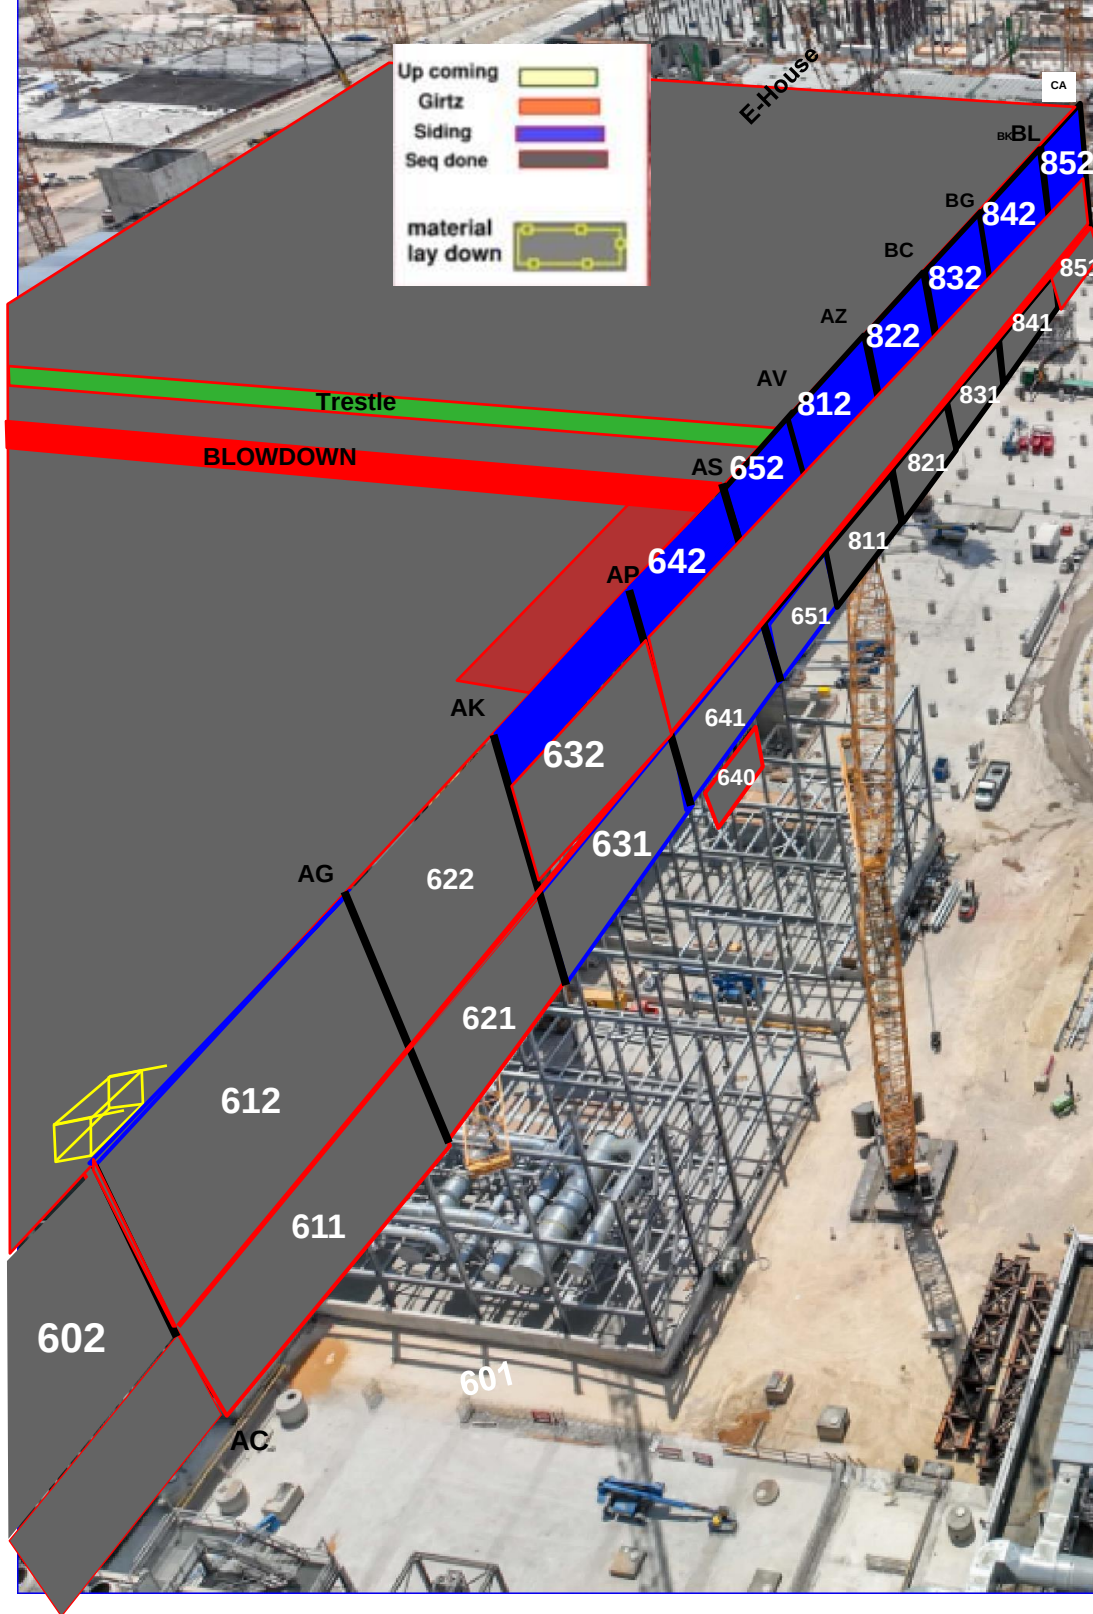

PSSS.1

Utility Level 1YA


PSSS Roof 2SA

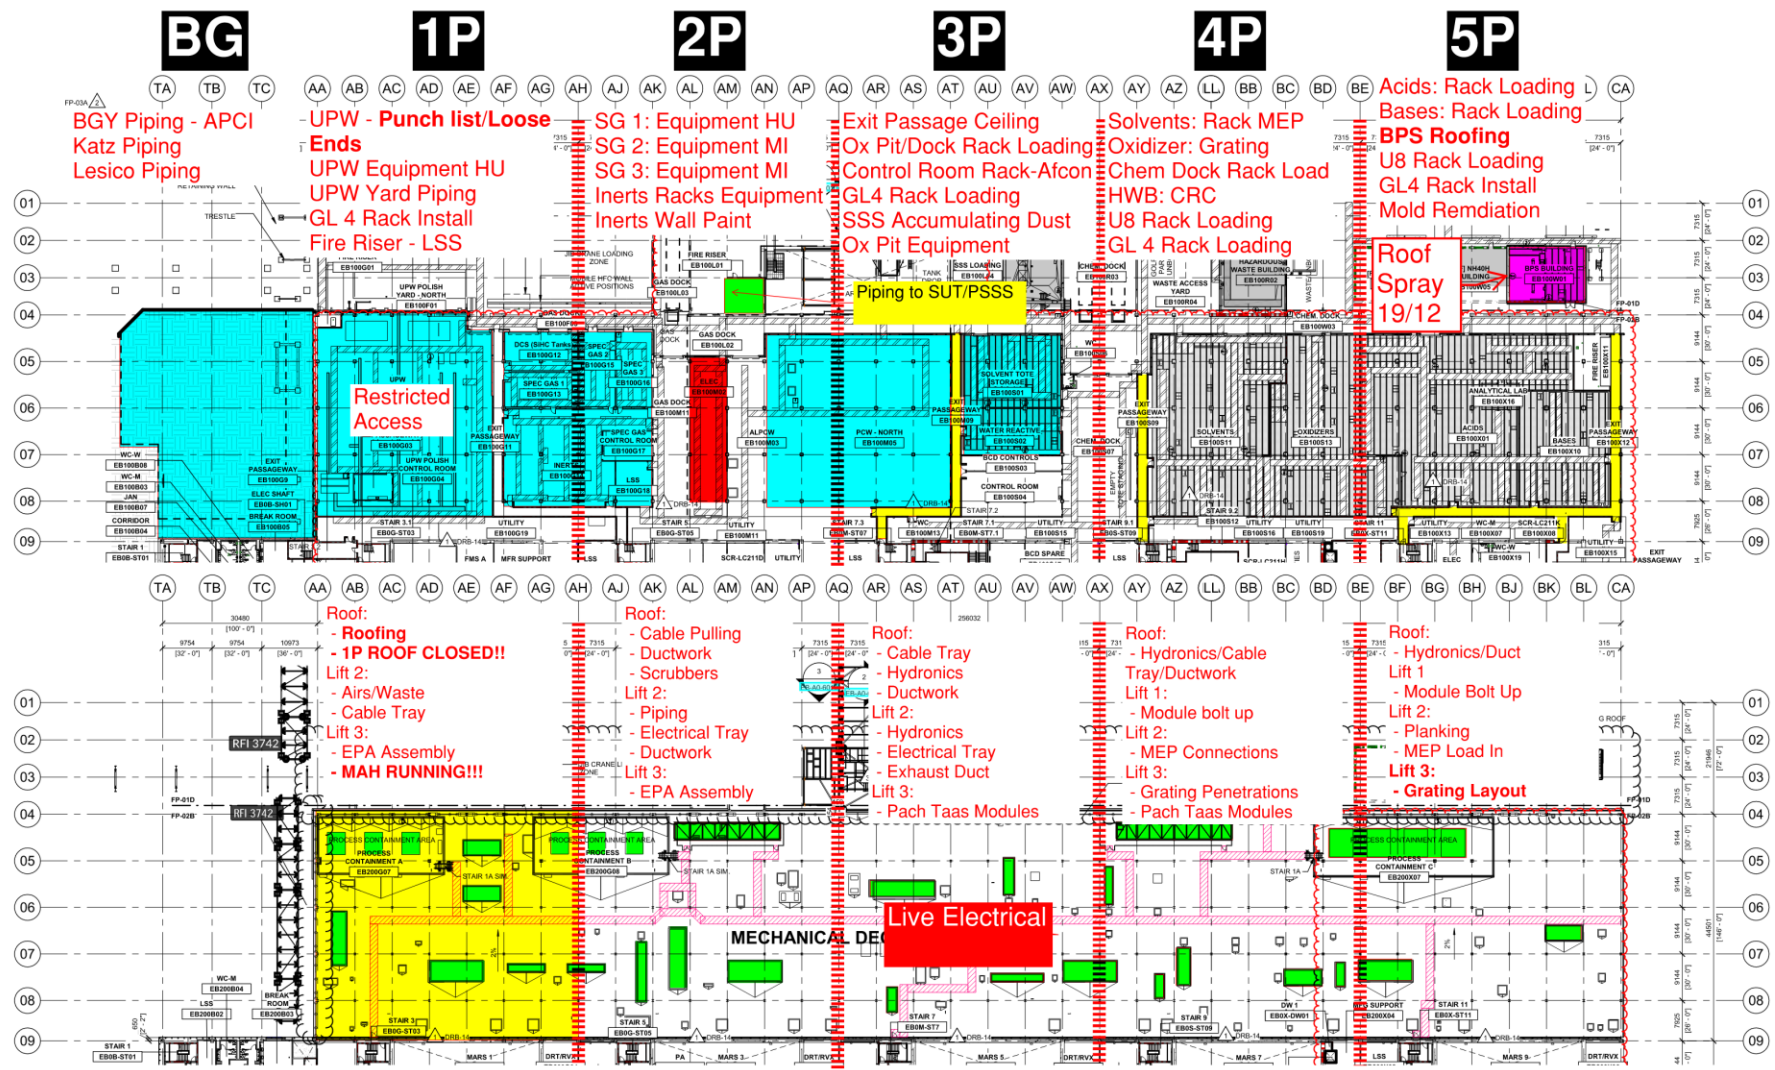


PSSS.2

Utility Level
1YA


PSSS Roof
2SA

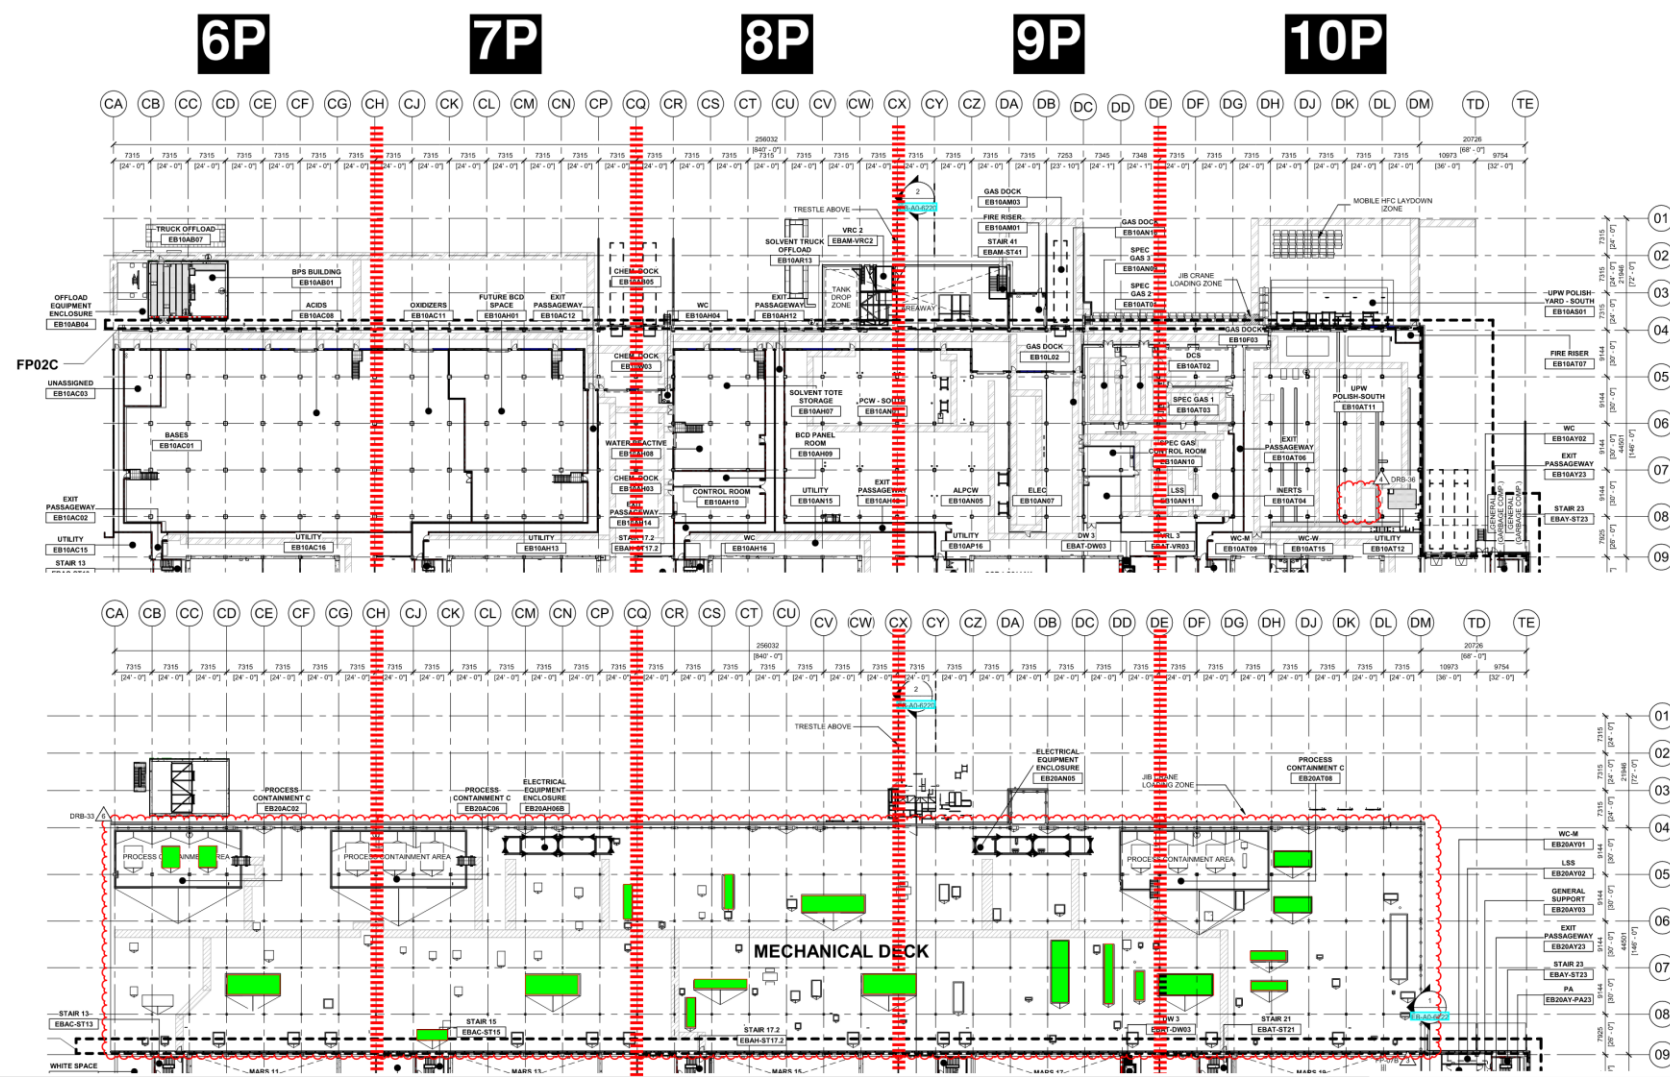

3800
Build
22nd_
26th

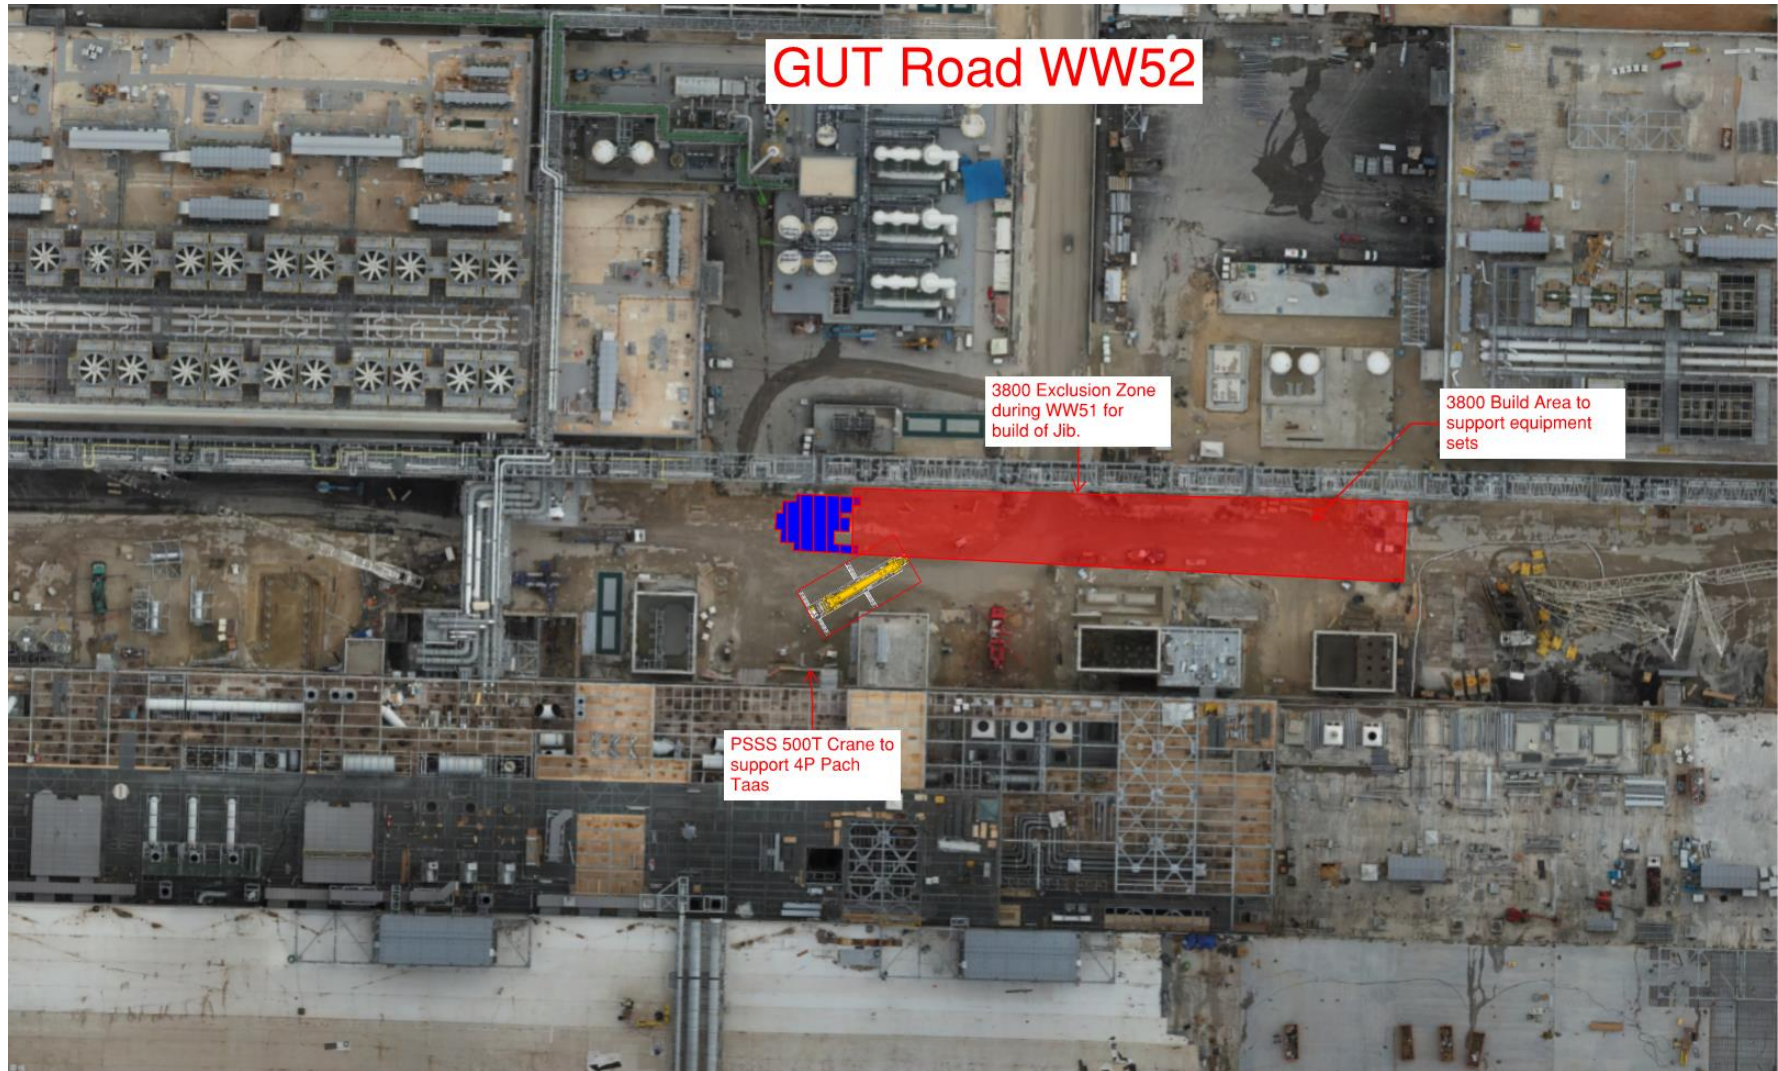

PCW/
ALPCW
Test
22/12
17:00 –
05:00

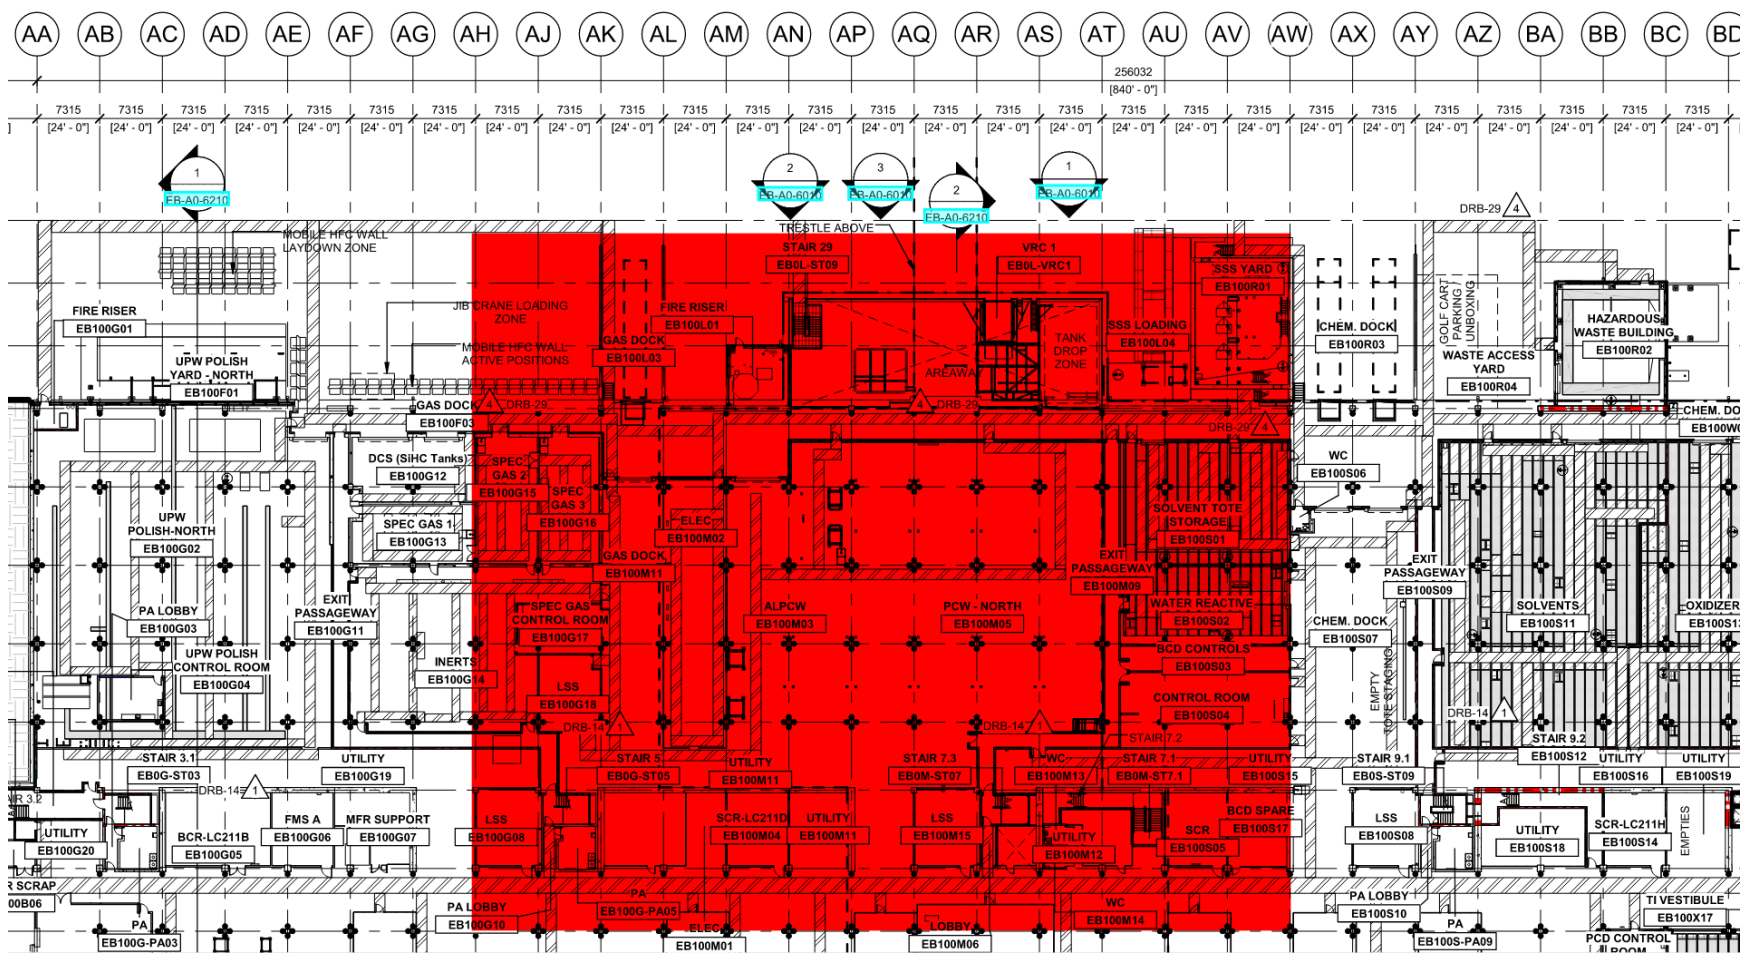

3800


Build

22nd -

26th




WJG 01J, 02J LIFT 2 & 3

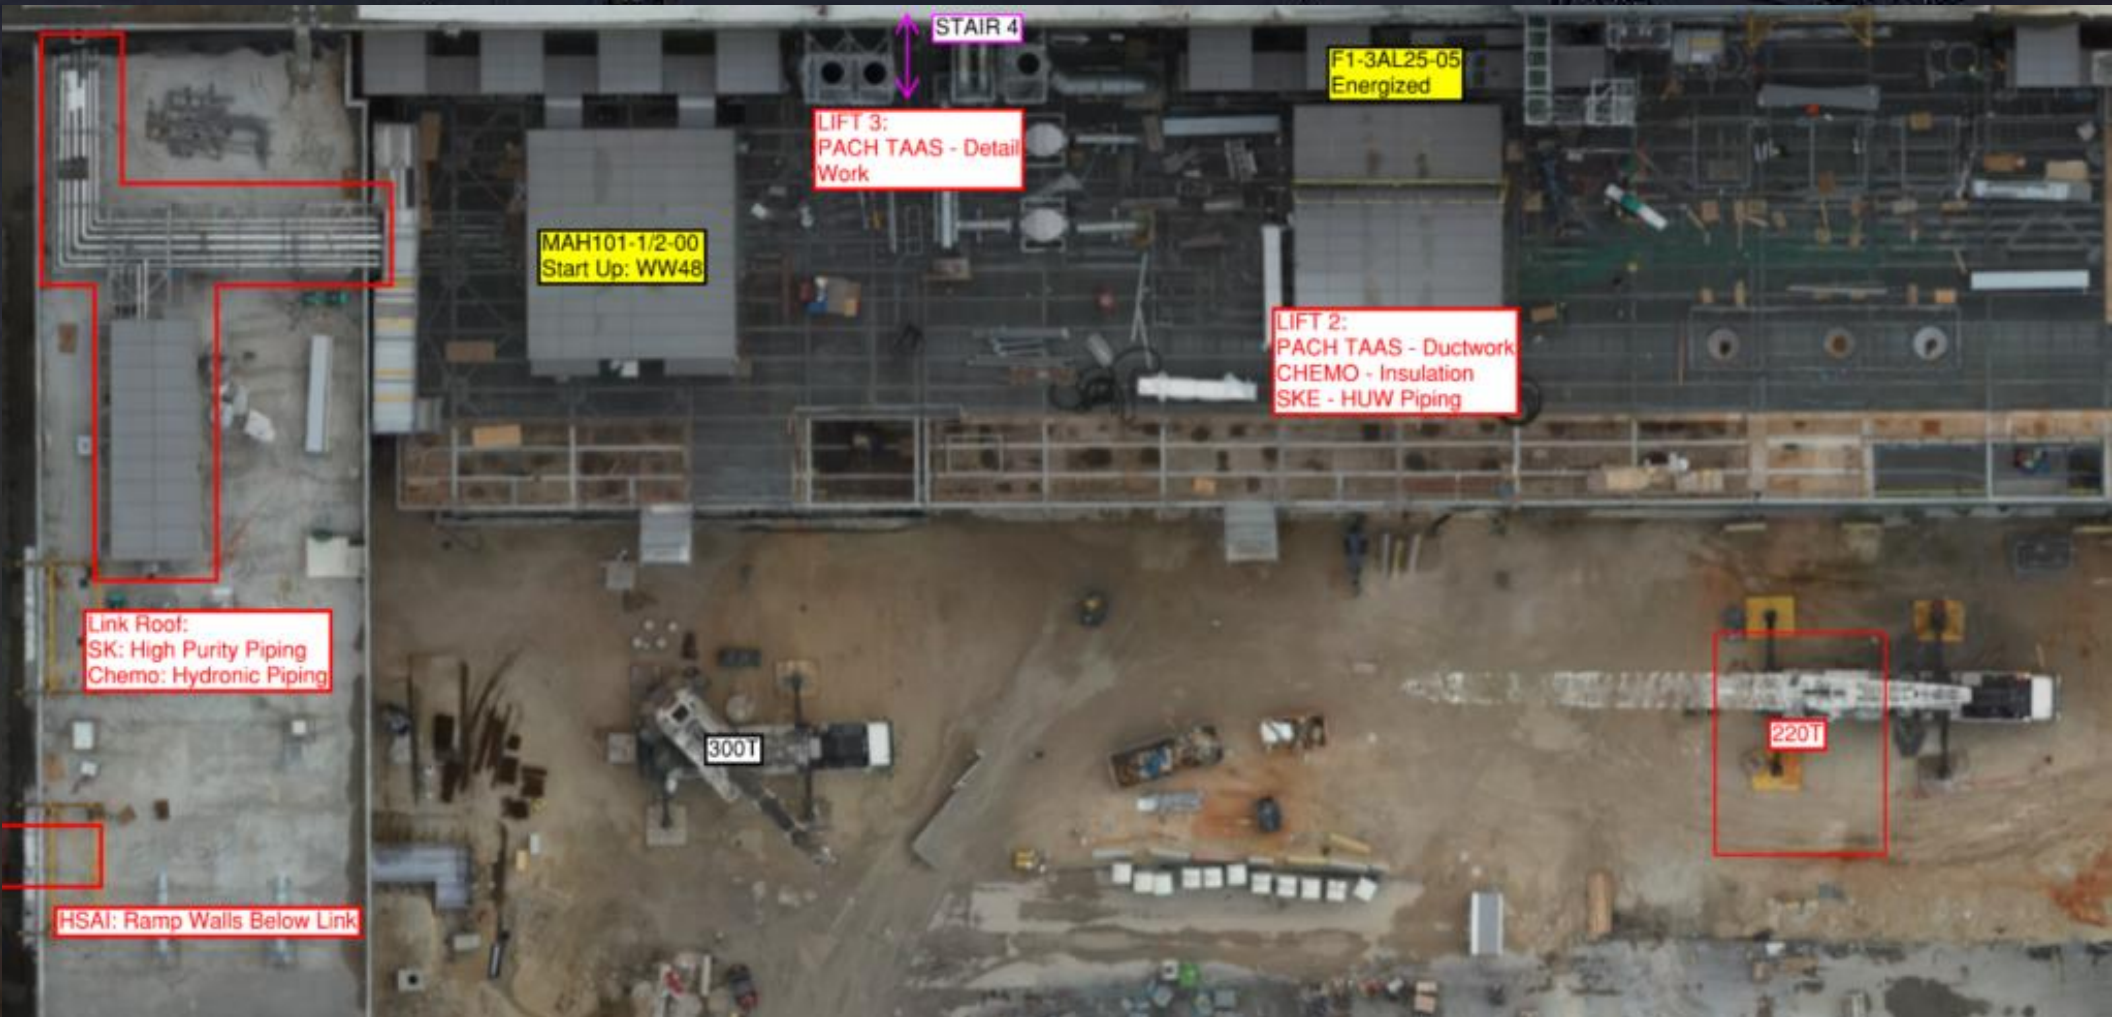



WJG 03J, 04J, 05J LIFT 2 & 3



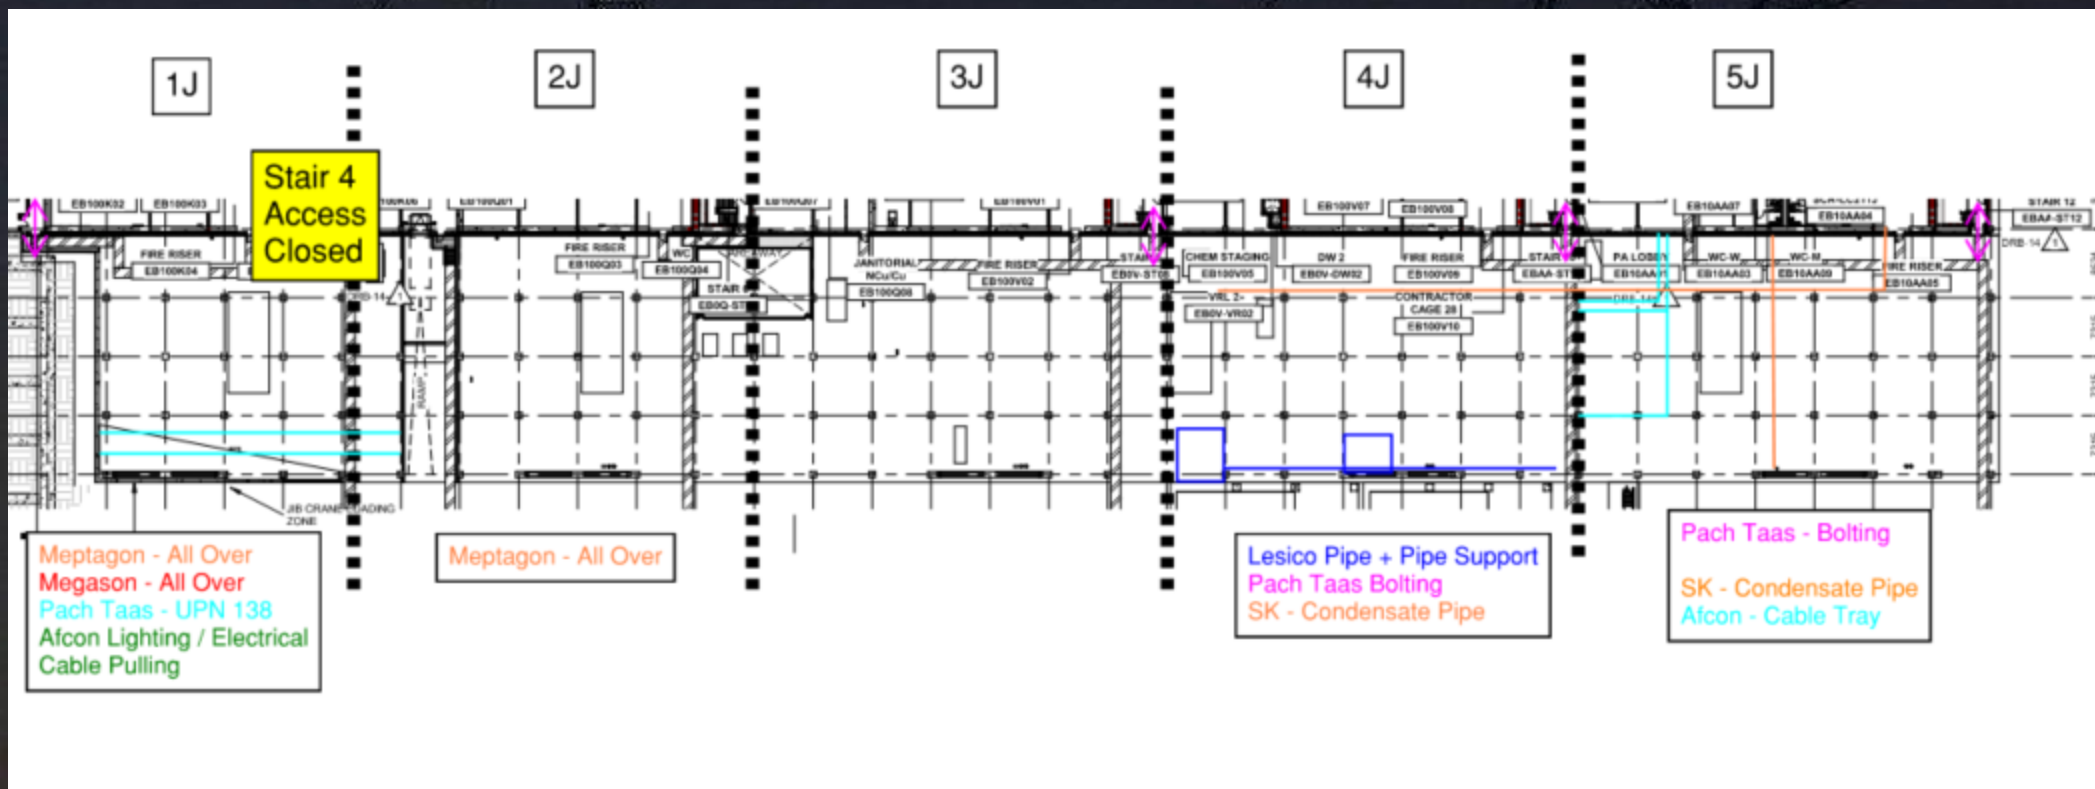



HOFFMAN CONSTRUCTION COMPANY




CC3800 DEMOB WW51







CUB 1

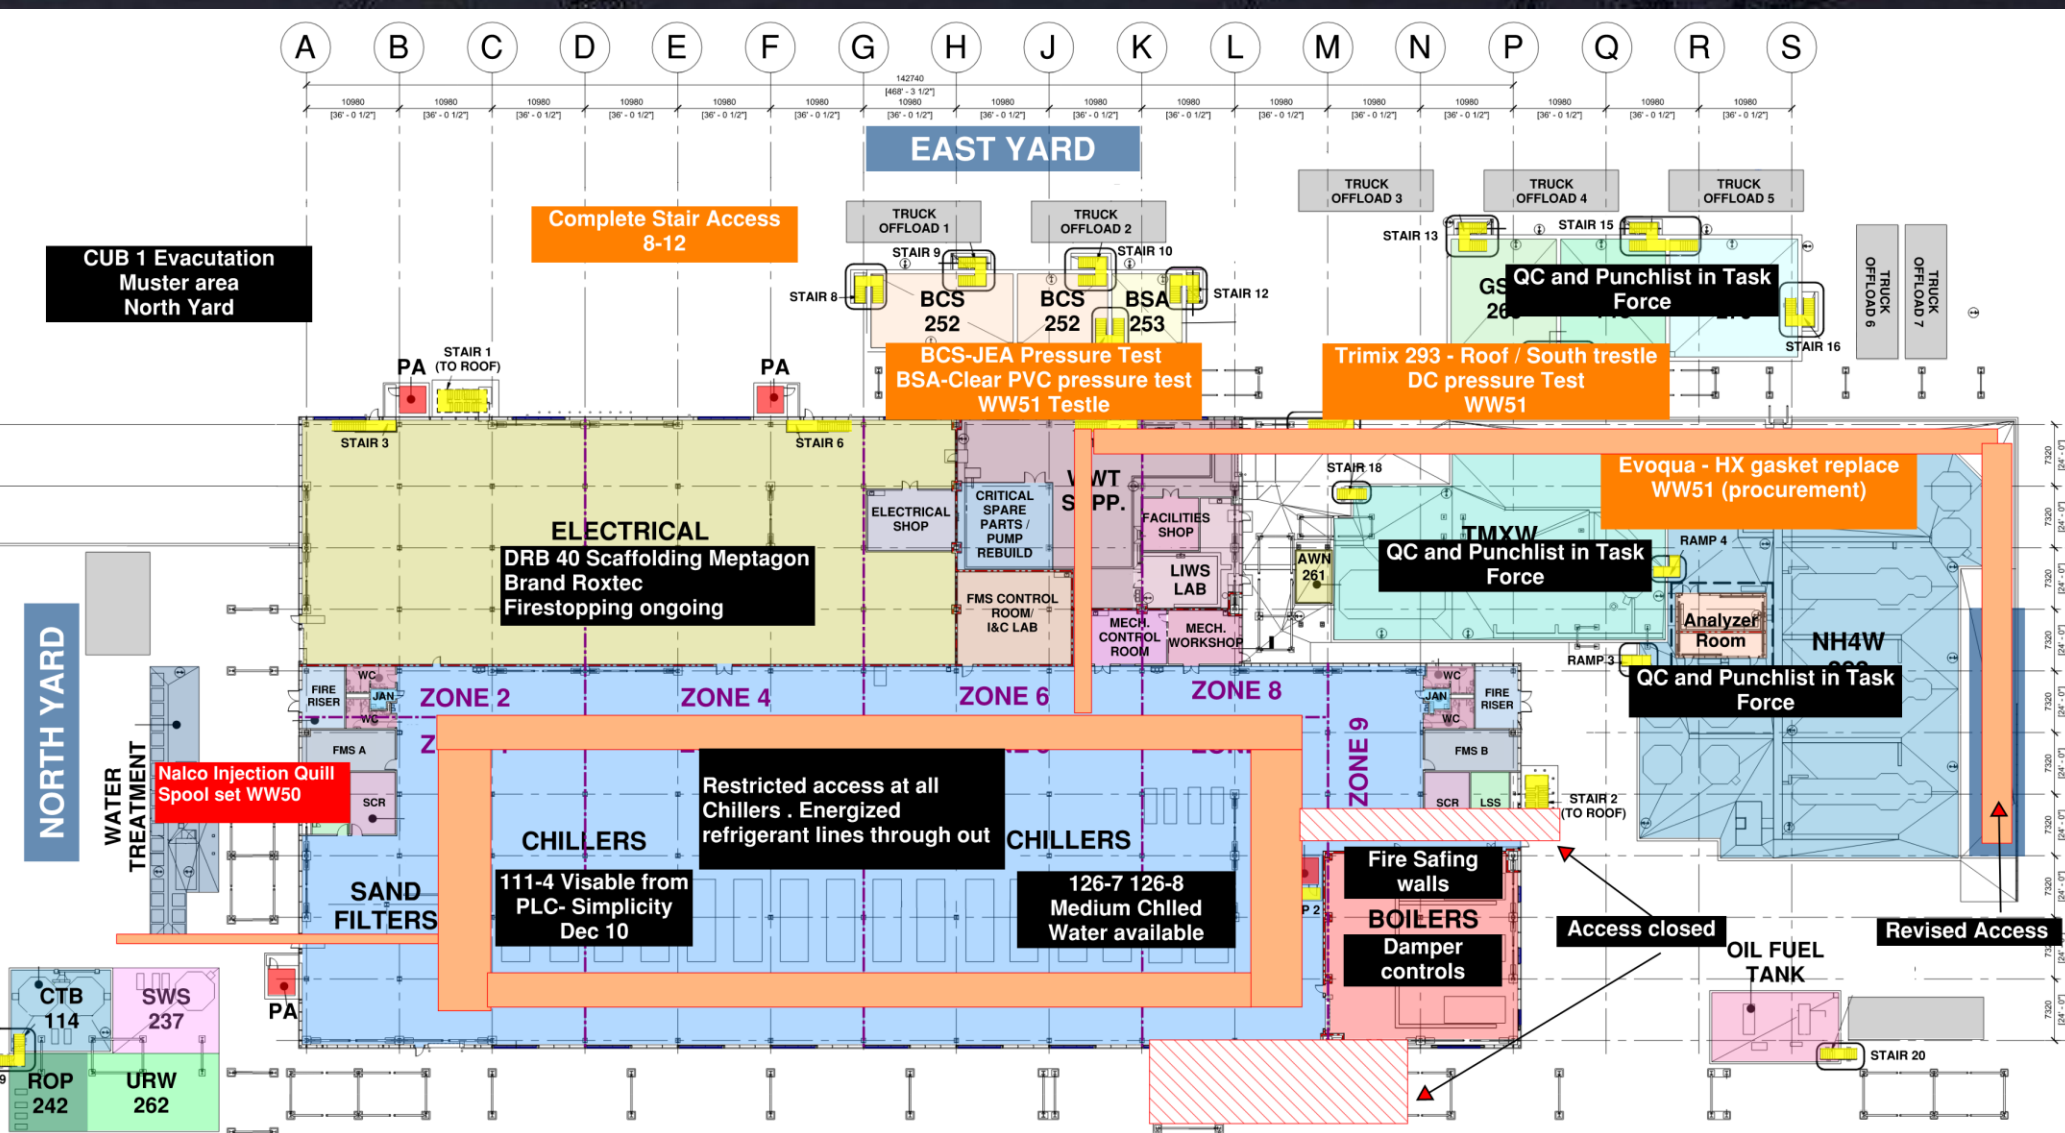


CUB 1 – EXTERIOR/ROOF

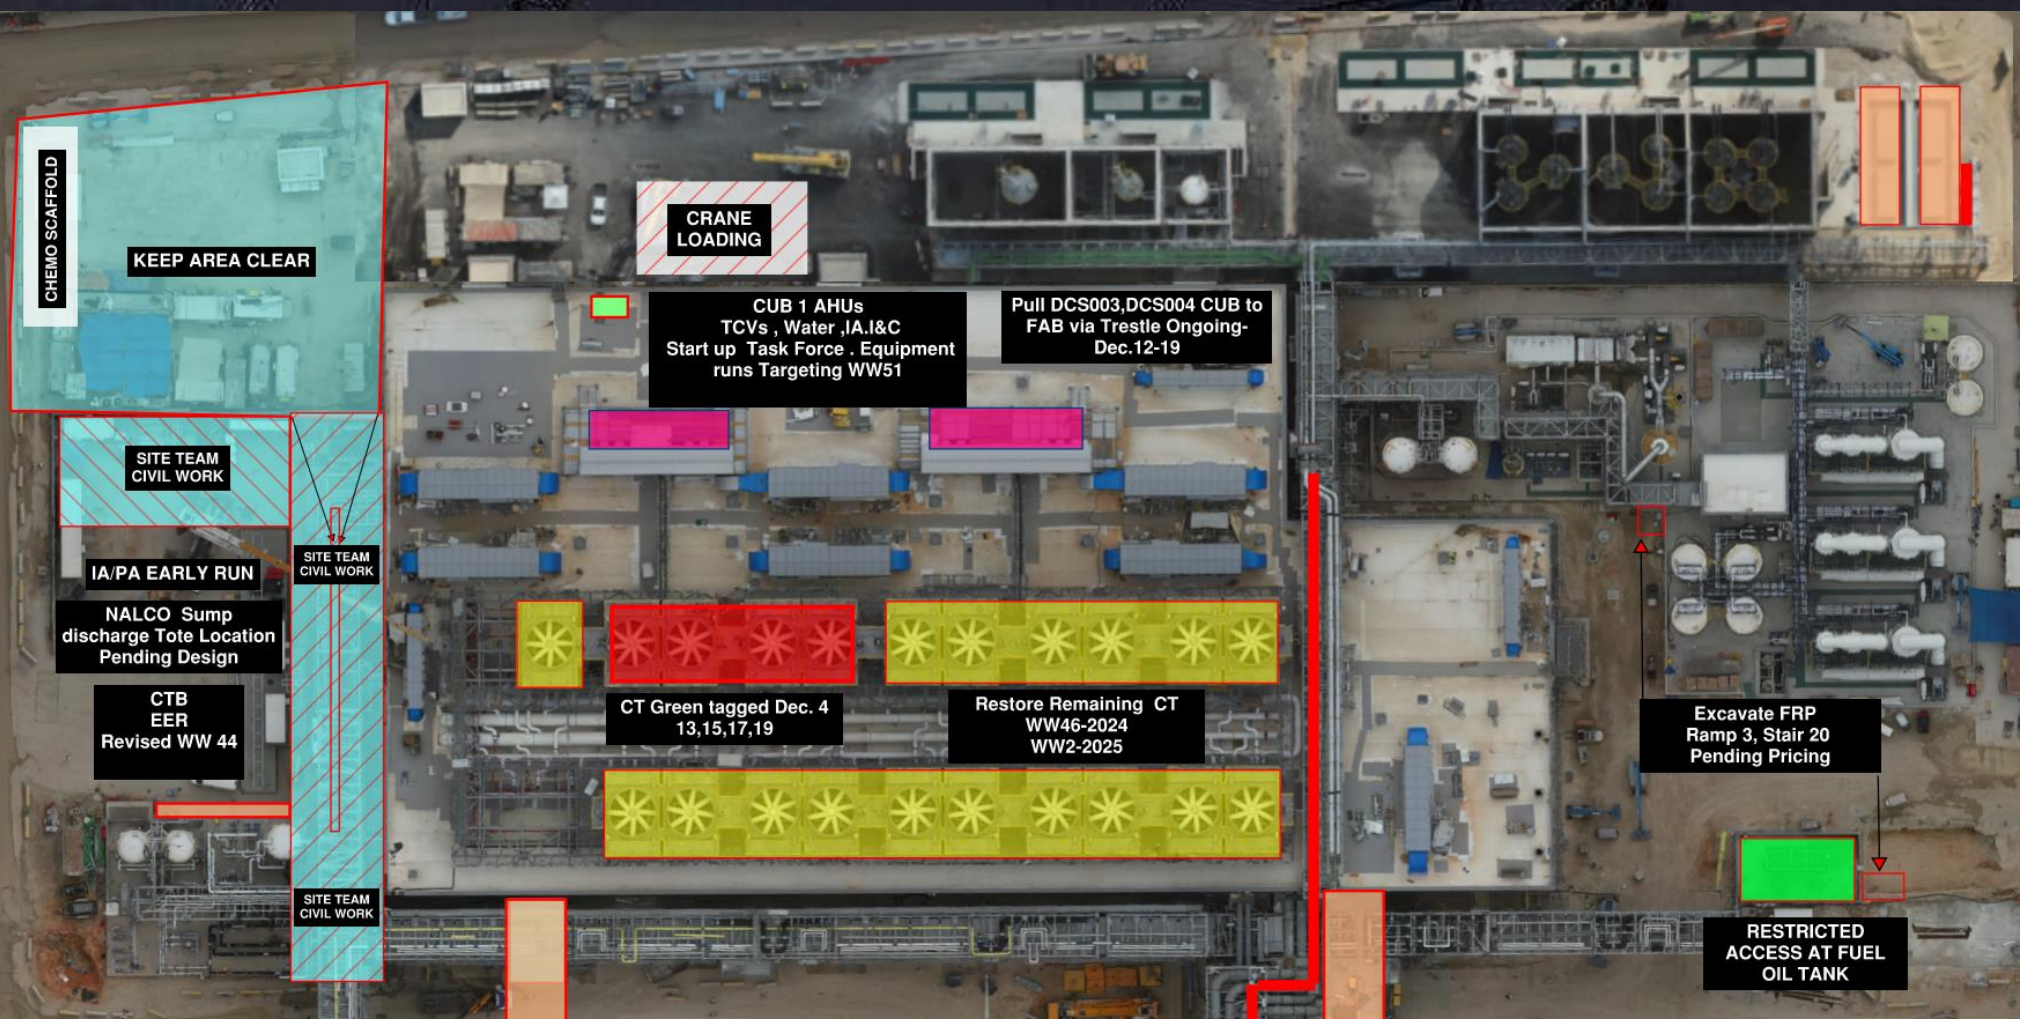

CUB 2- Load in and H&T

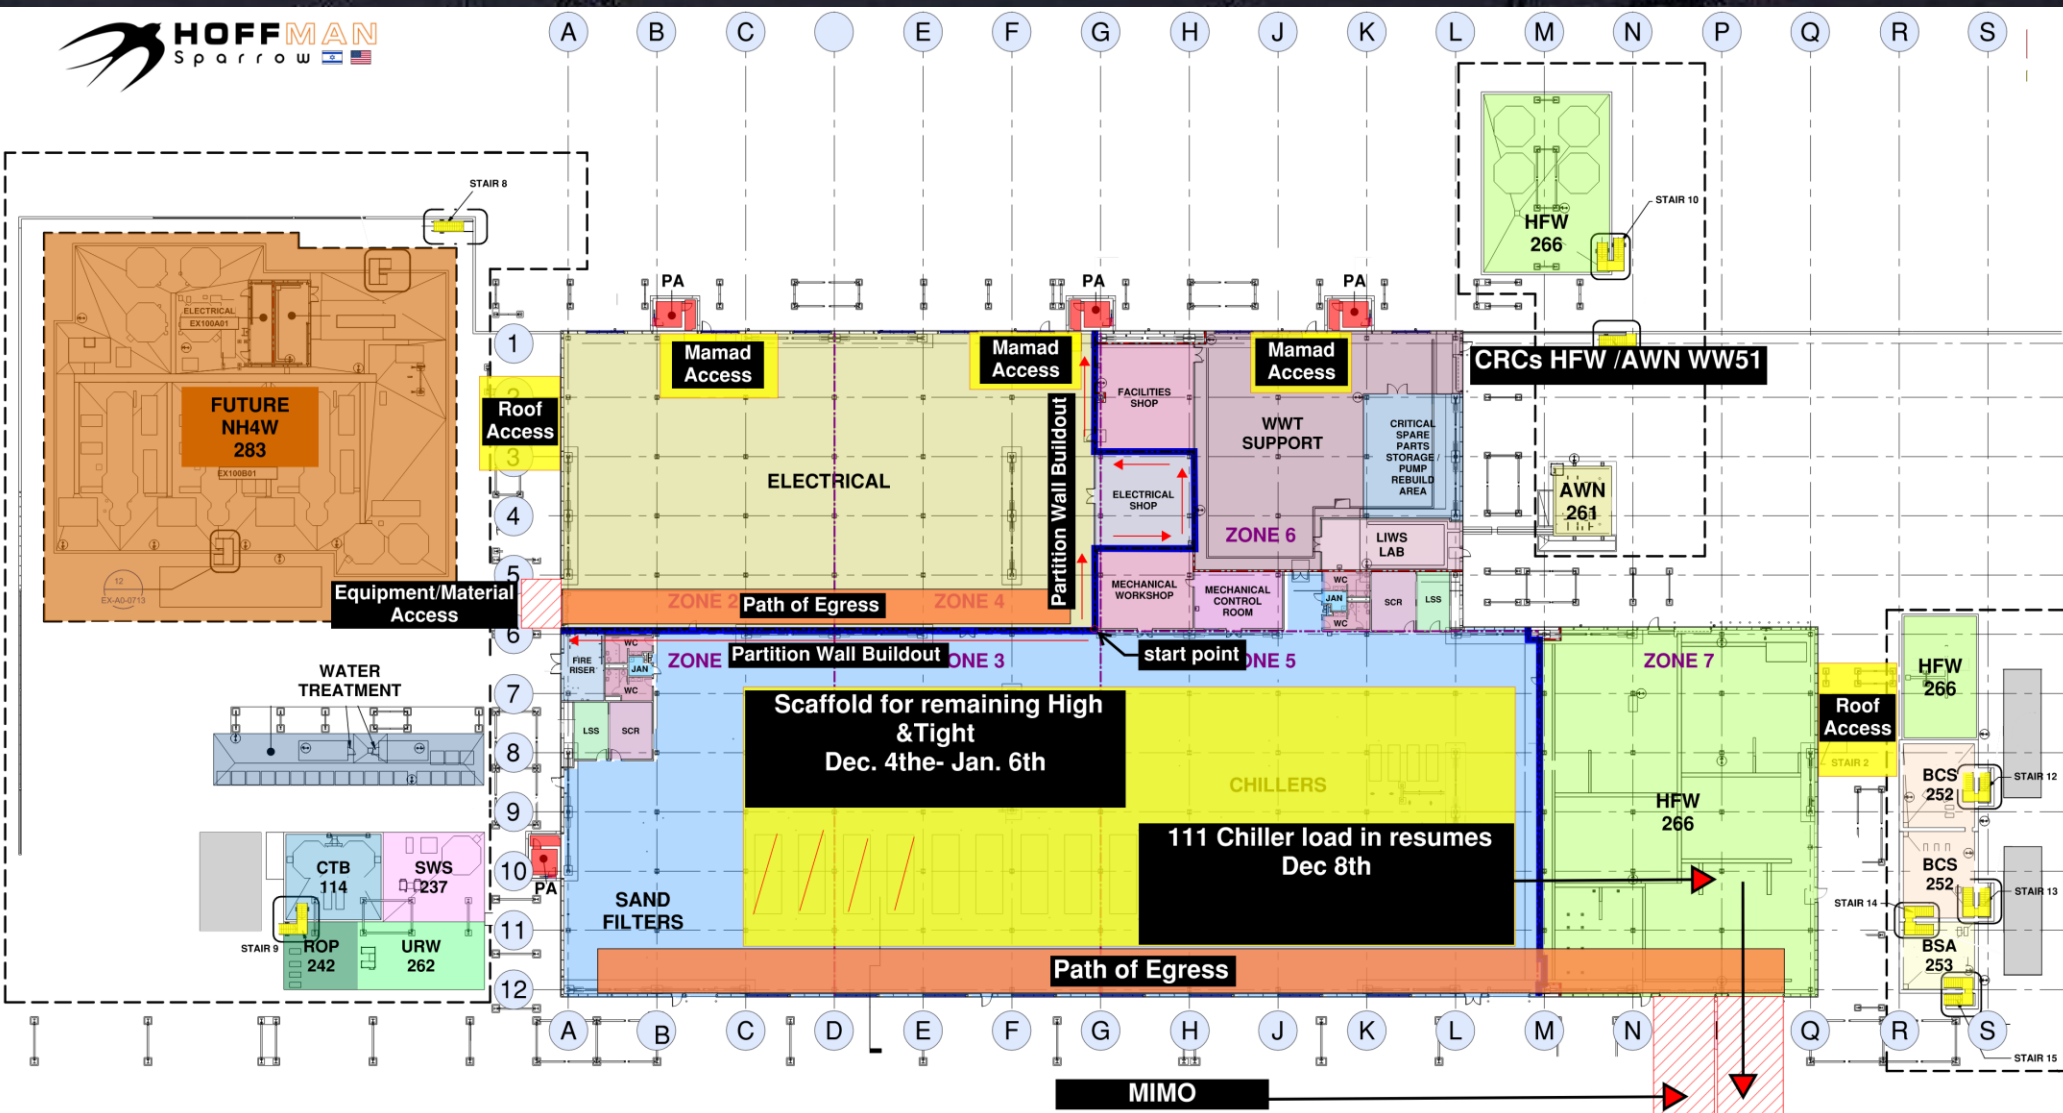



CUB 2 – EXTERIOR/ROOF

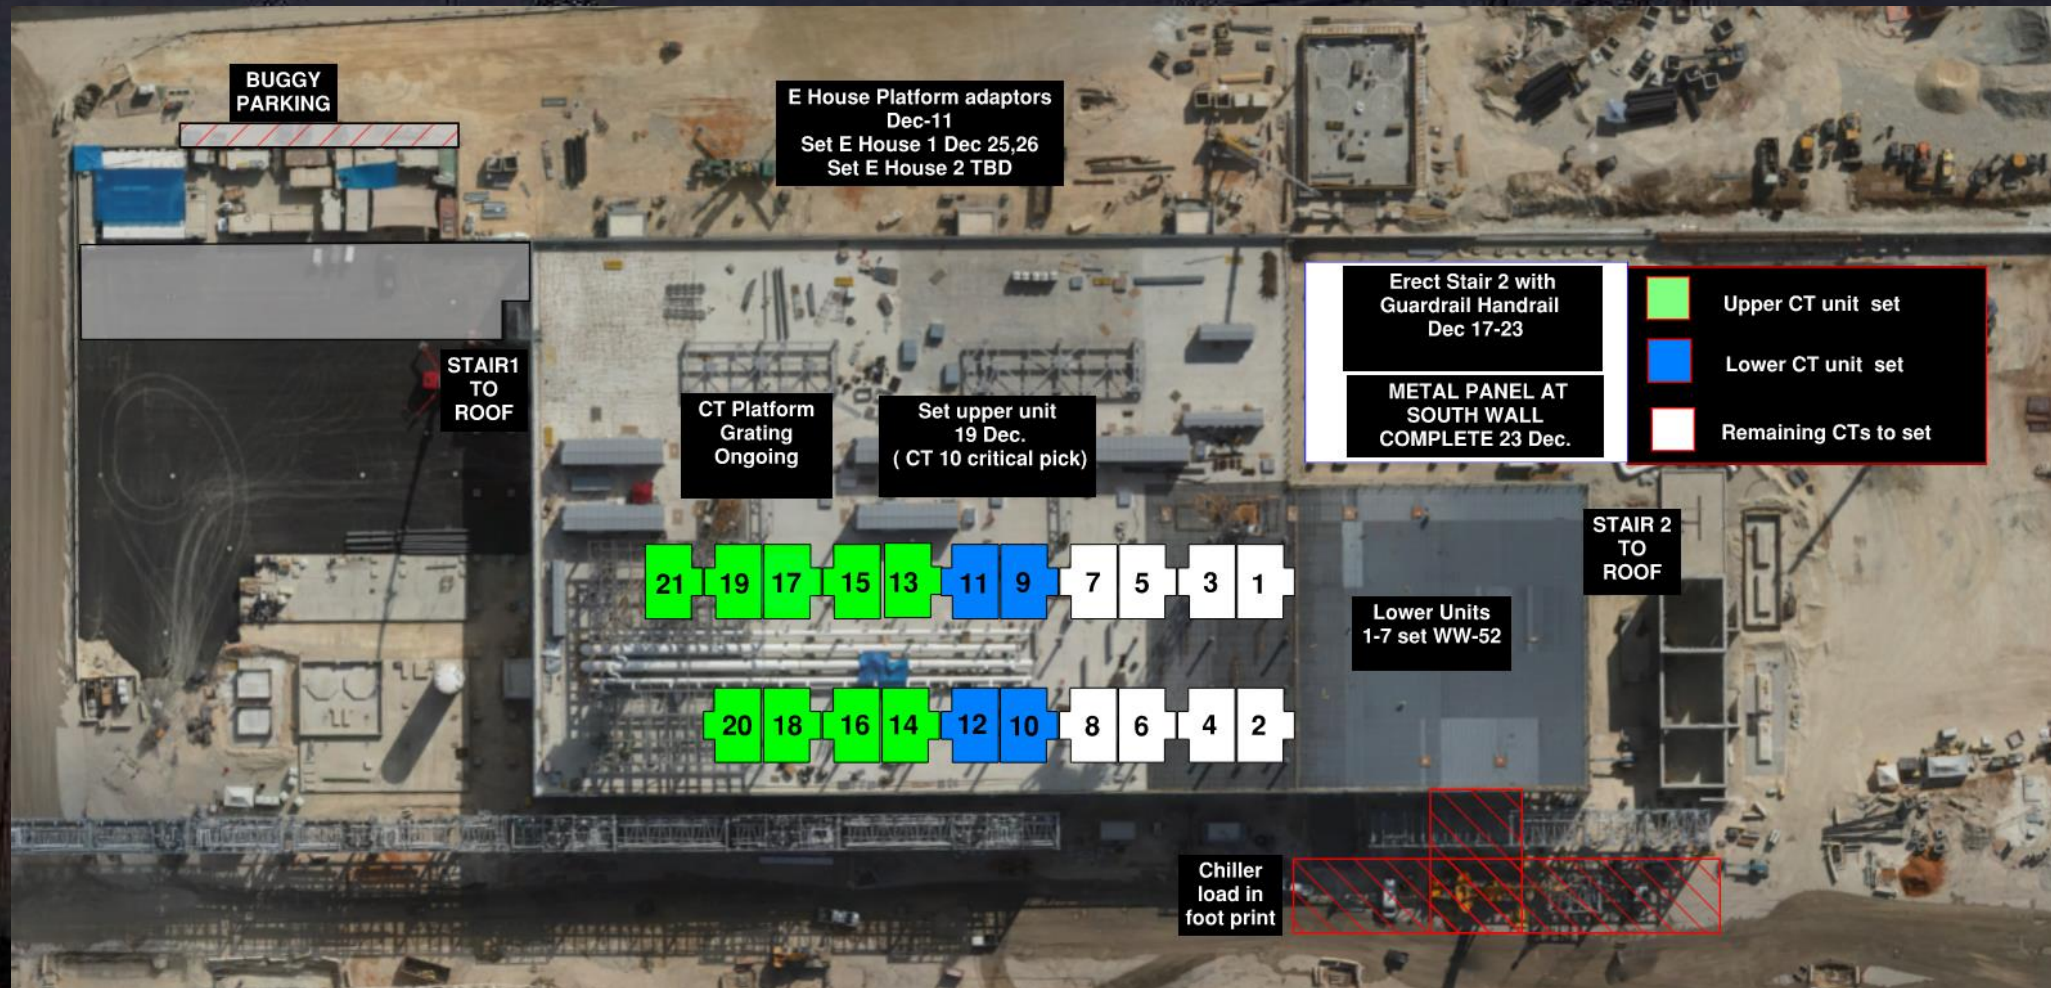



GIS GATE
closed 29/Dec /2024

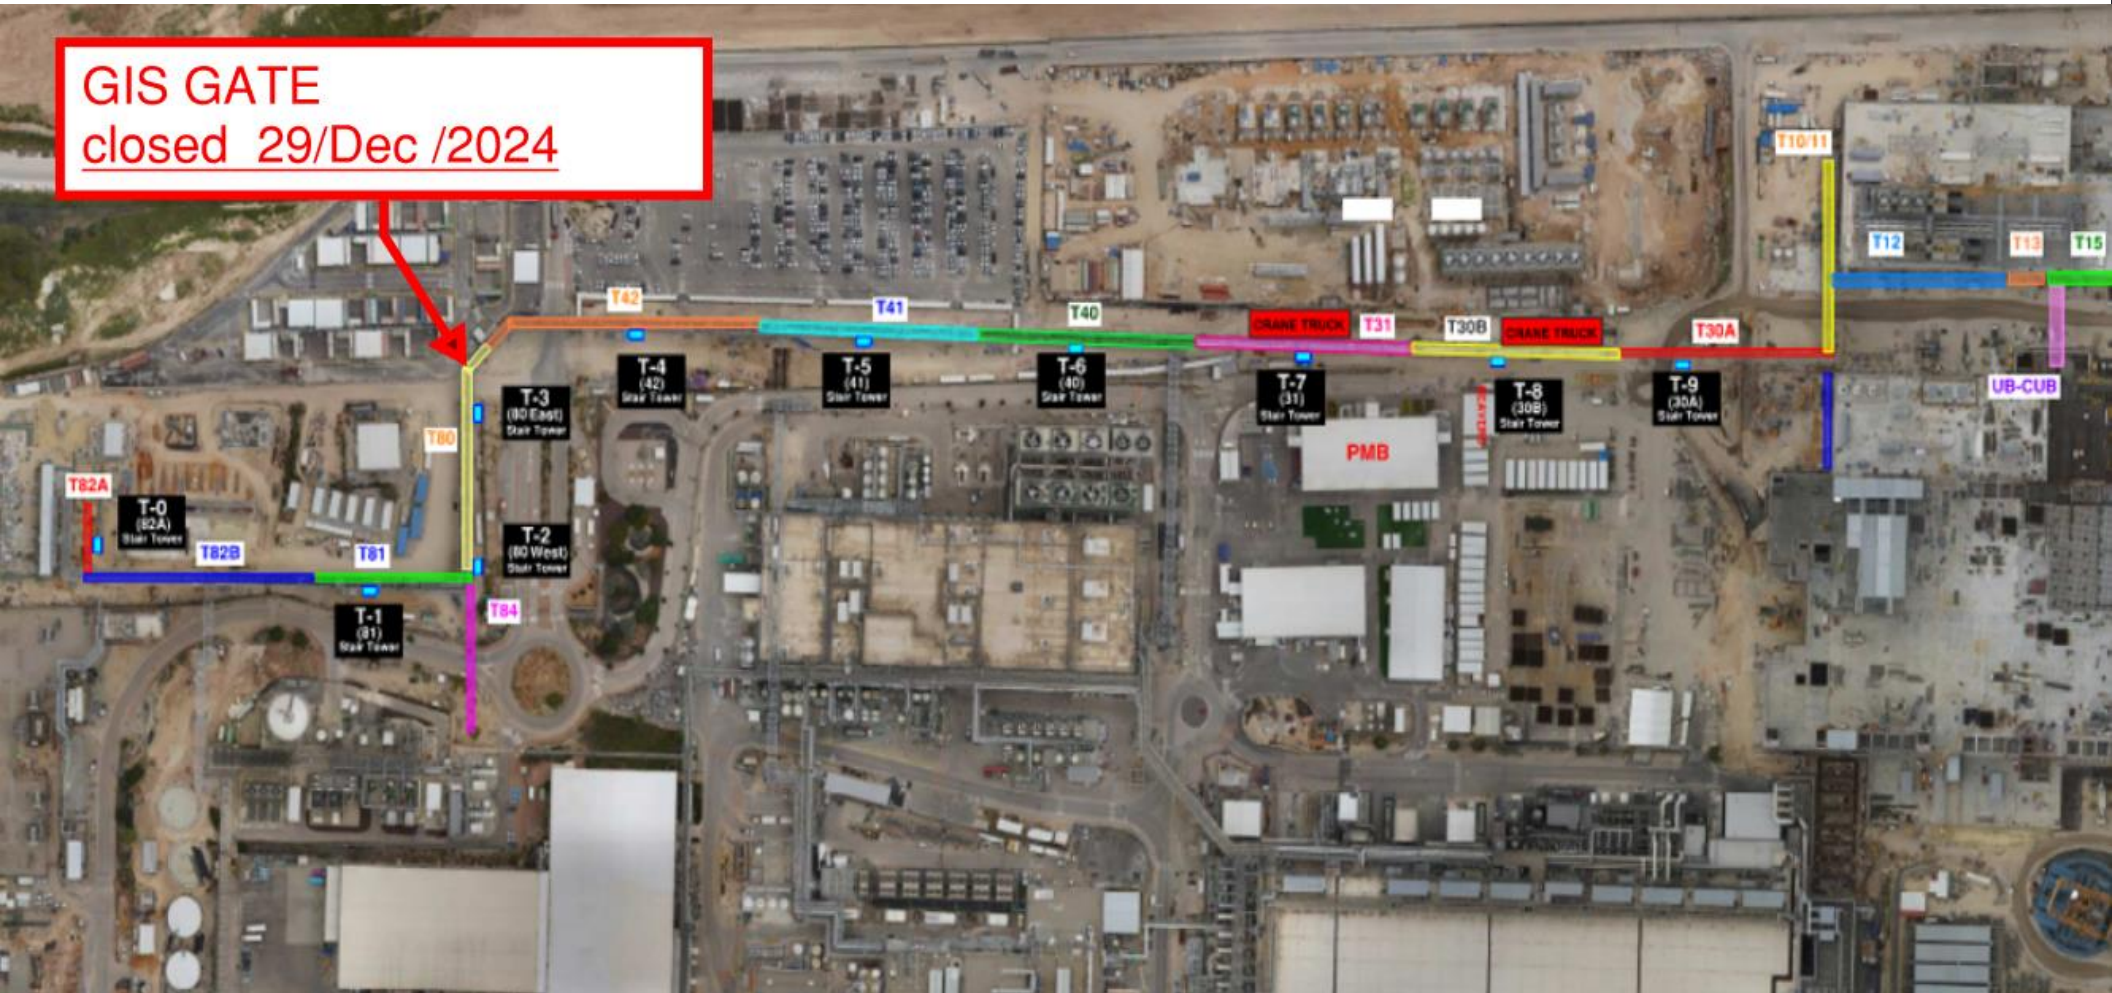



HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

SUT

UB CUB - STAIRCASE DISMANTEL

24/12/2024


CUB



TRESTLE GN2 PRESSURE TEST
12-19-24 17:00 - 12-21-24 18:00

ROAD CLOSED
HARD BARRICADE

ROAD CLOSED
HARD BARRICADE

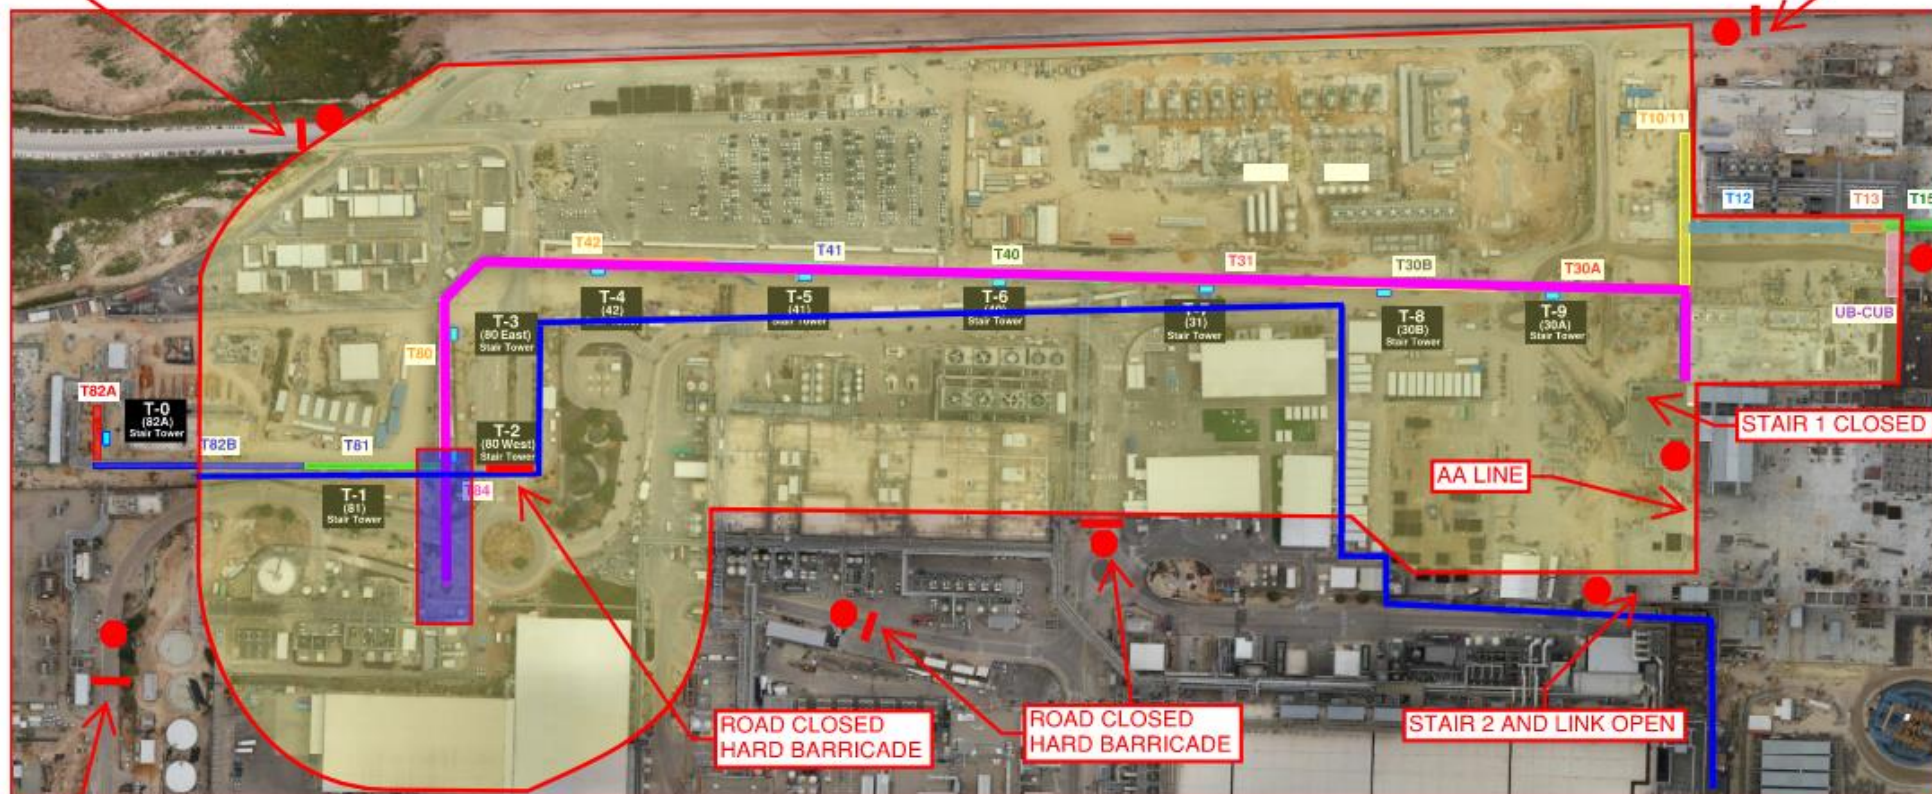

- EXCLUSION ZONE FOLLOWING ASME PCC-2 APPENDIX 501-II AND 501-III
- EXCLUSION ZONE FOLLOWING TABLE 7 INTEL ADOPTED PRESSURE TESTS OF PIPING
- GN2 LINE UNDER TEST
- INTEL FENCE
- SPOTTERS

BGC - NDT

Starting -Monday December 23rd night at 19:00
Finish Tuesday December 24th at 05:00am.

Starting -Tuesday December 24th at 19:00
Finish Wednesday December 25th at 05:00am


Starting -Wednesday December 25th at 19:00
Finish Thursday December 26th at 05:00am

No impact on PMB
entrance\Exit

Safety spotter

Safety spotter

Safety spotter

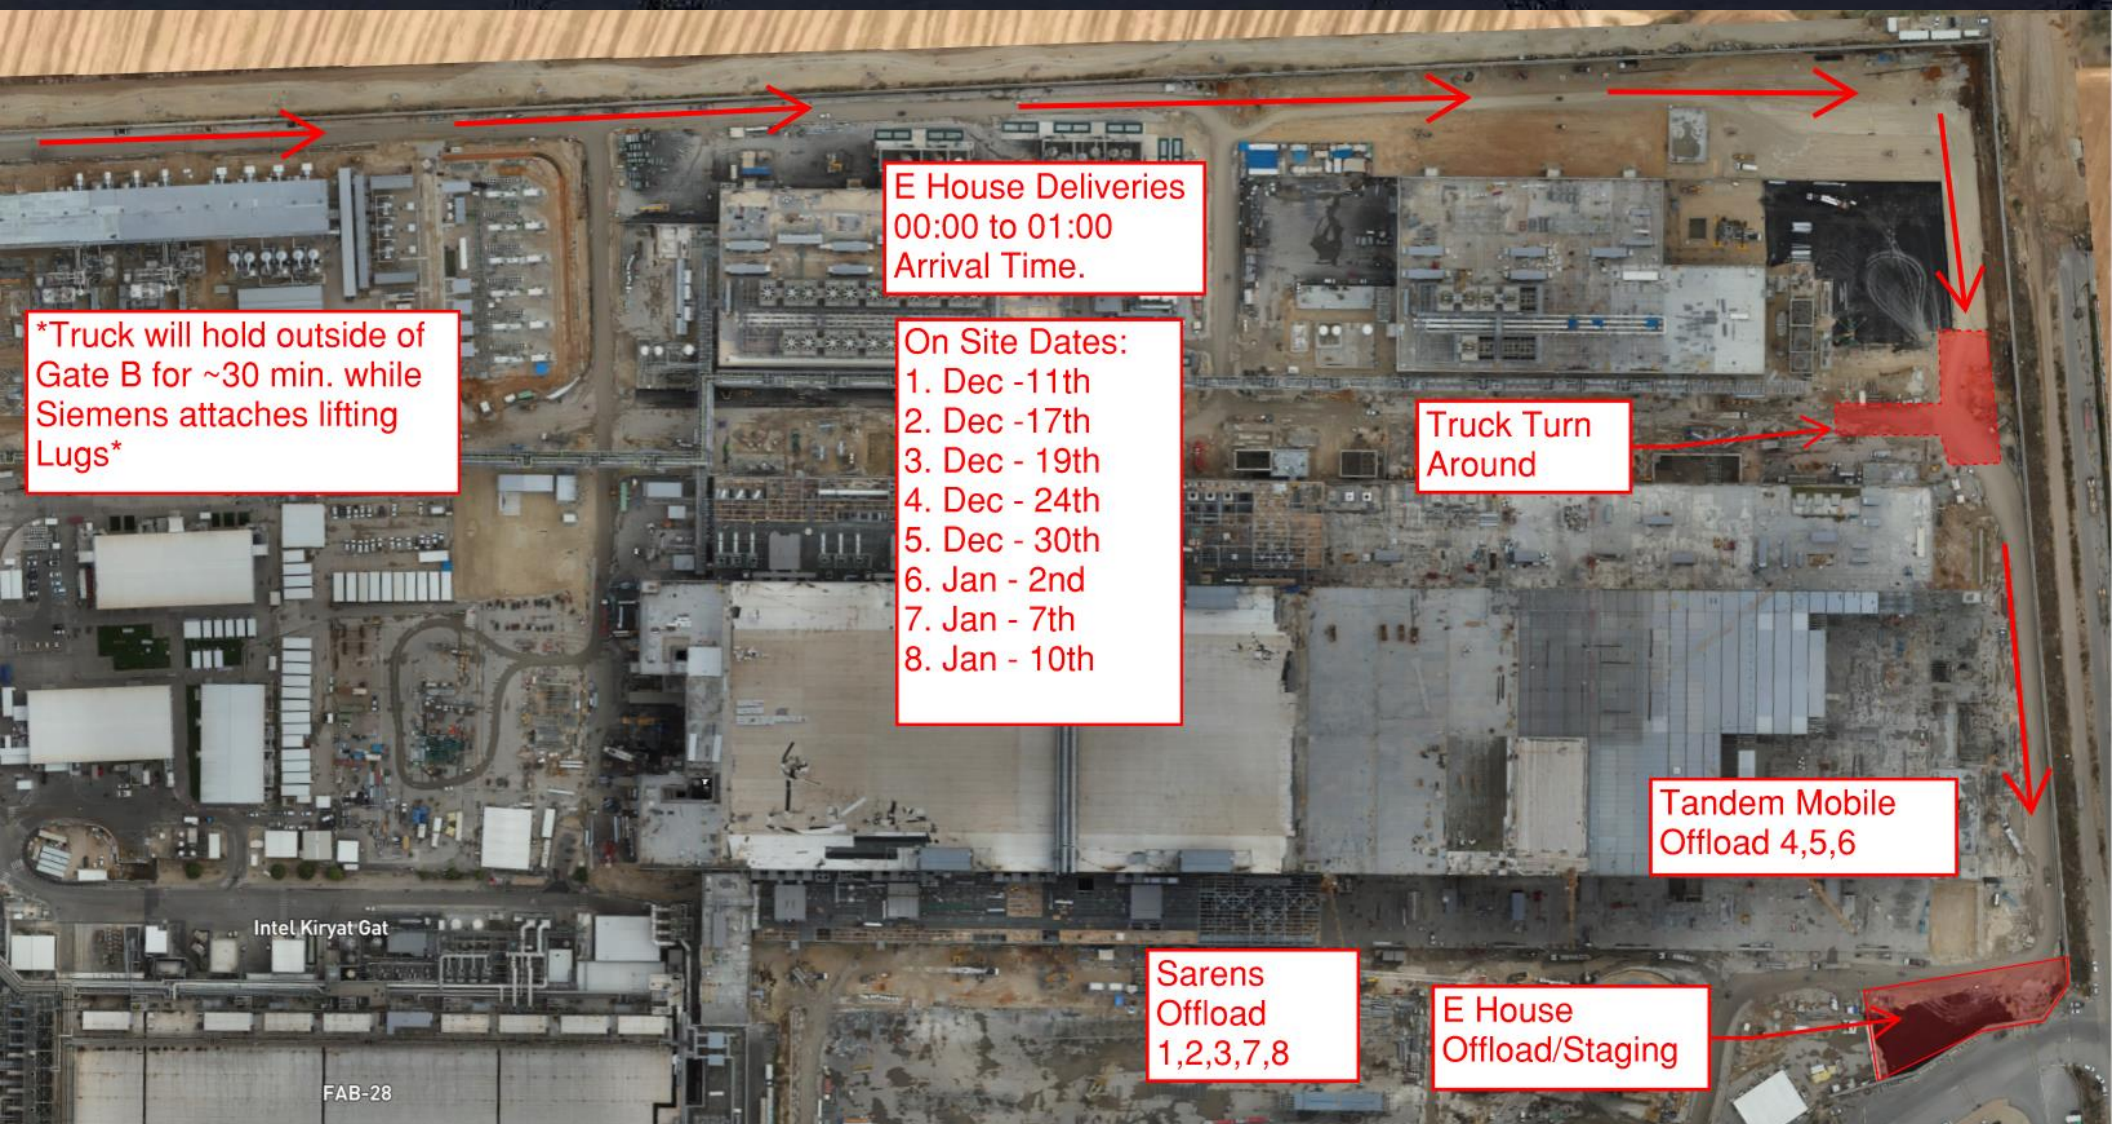

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:

1. Dec -11th
2. Dec -17th
3. Dec -19th
4. Dec -24th
5. Dec -30th
6. Jan -2nd
7. Jan -7th
8. Jan -10th

Truck Turn
Around

Tandem Mobile
Offload 4,5,6

Sarens
Offload
1,2,3,7,8

E House
Offload/Staging

*Truck will hold outside of
Gate B for ~30 min. while
Siemens attaches lifting
Lugs*


Intel Kiryat Gat

FAB-28

Daily Coordination Meeting

Site Logistics

North

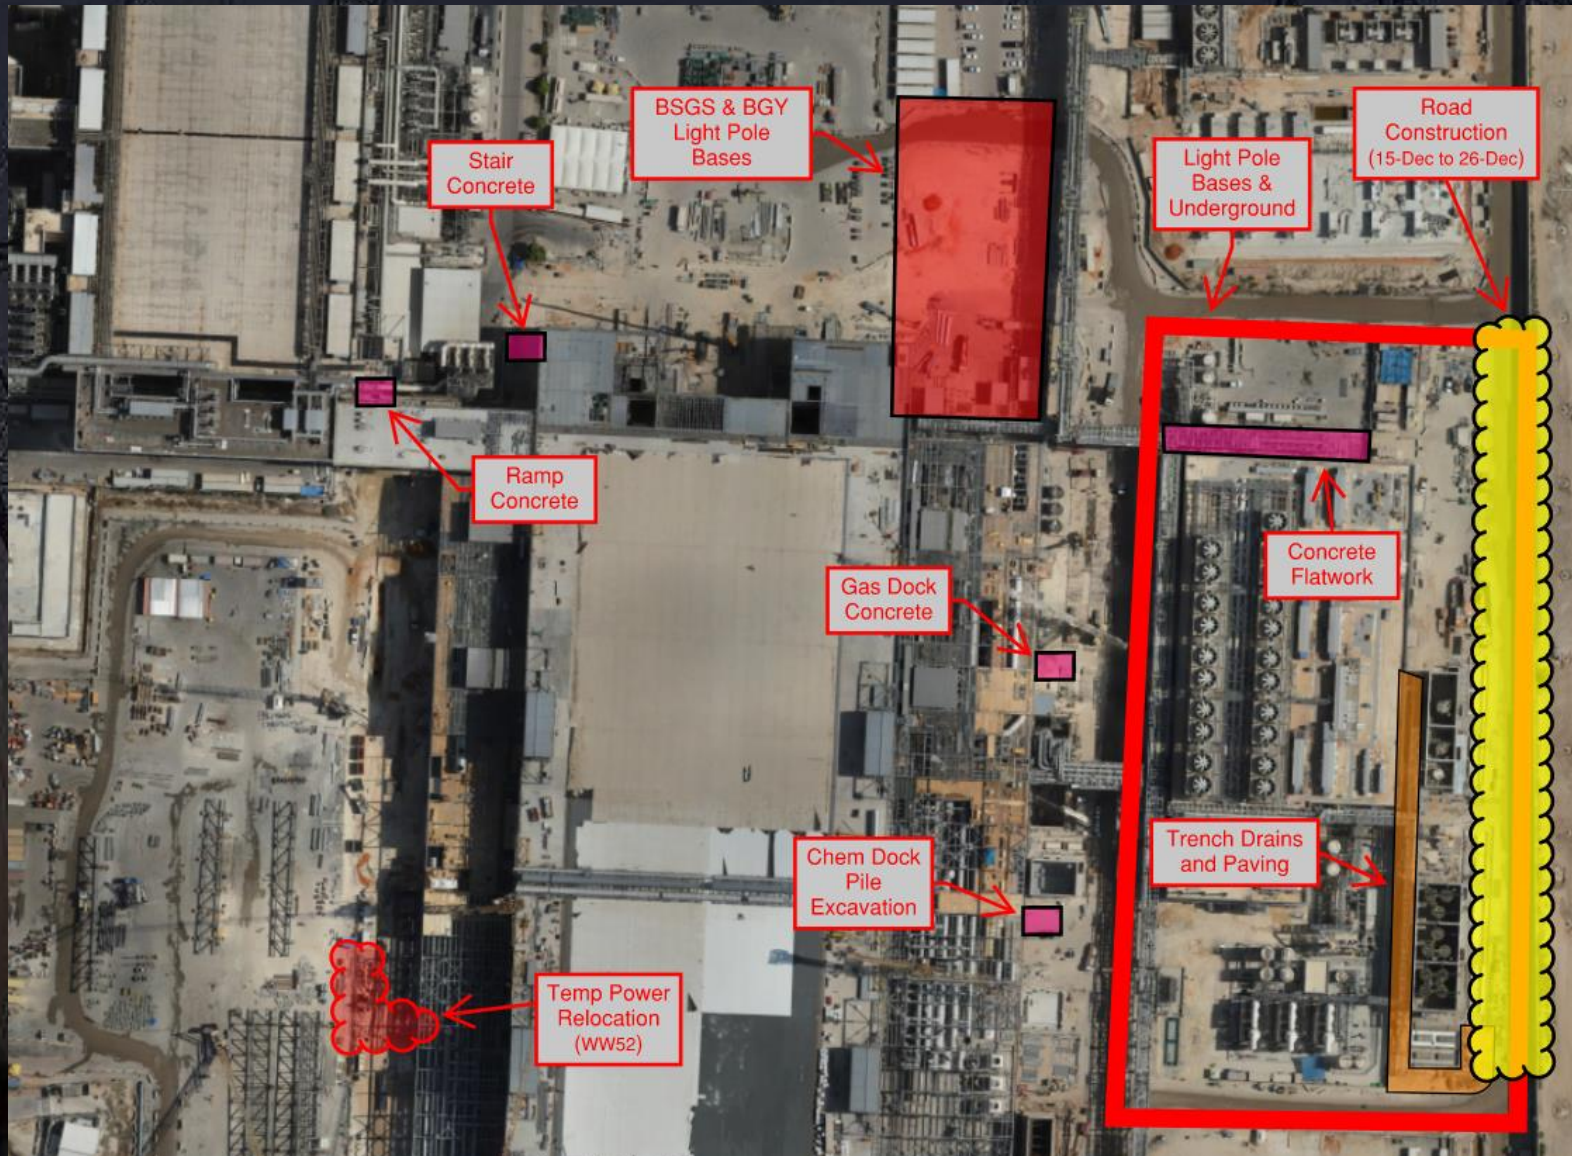




Daily Coordination Meeting

Site Logistics

East CUB1 Road Closure

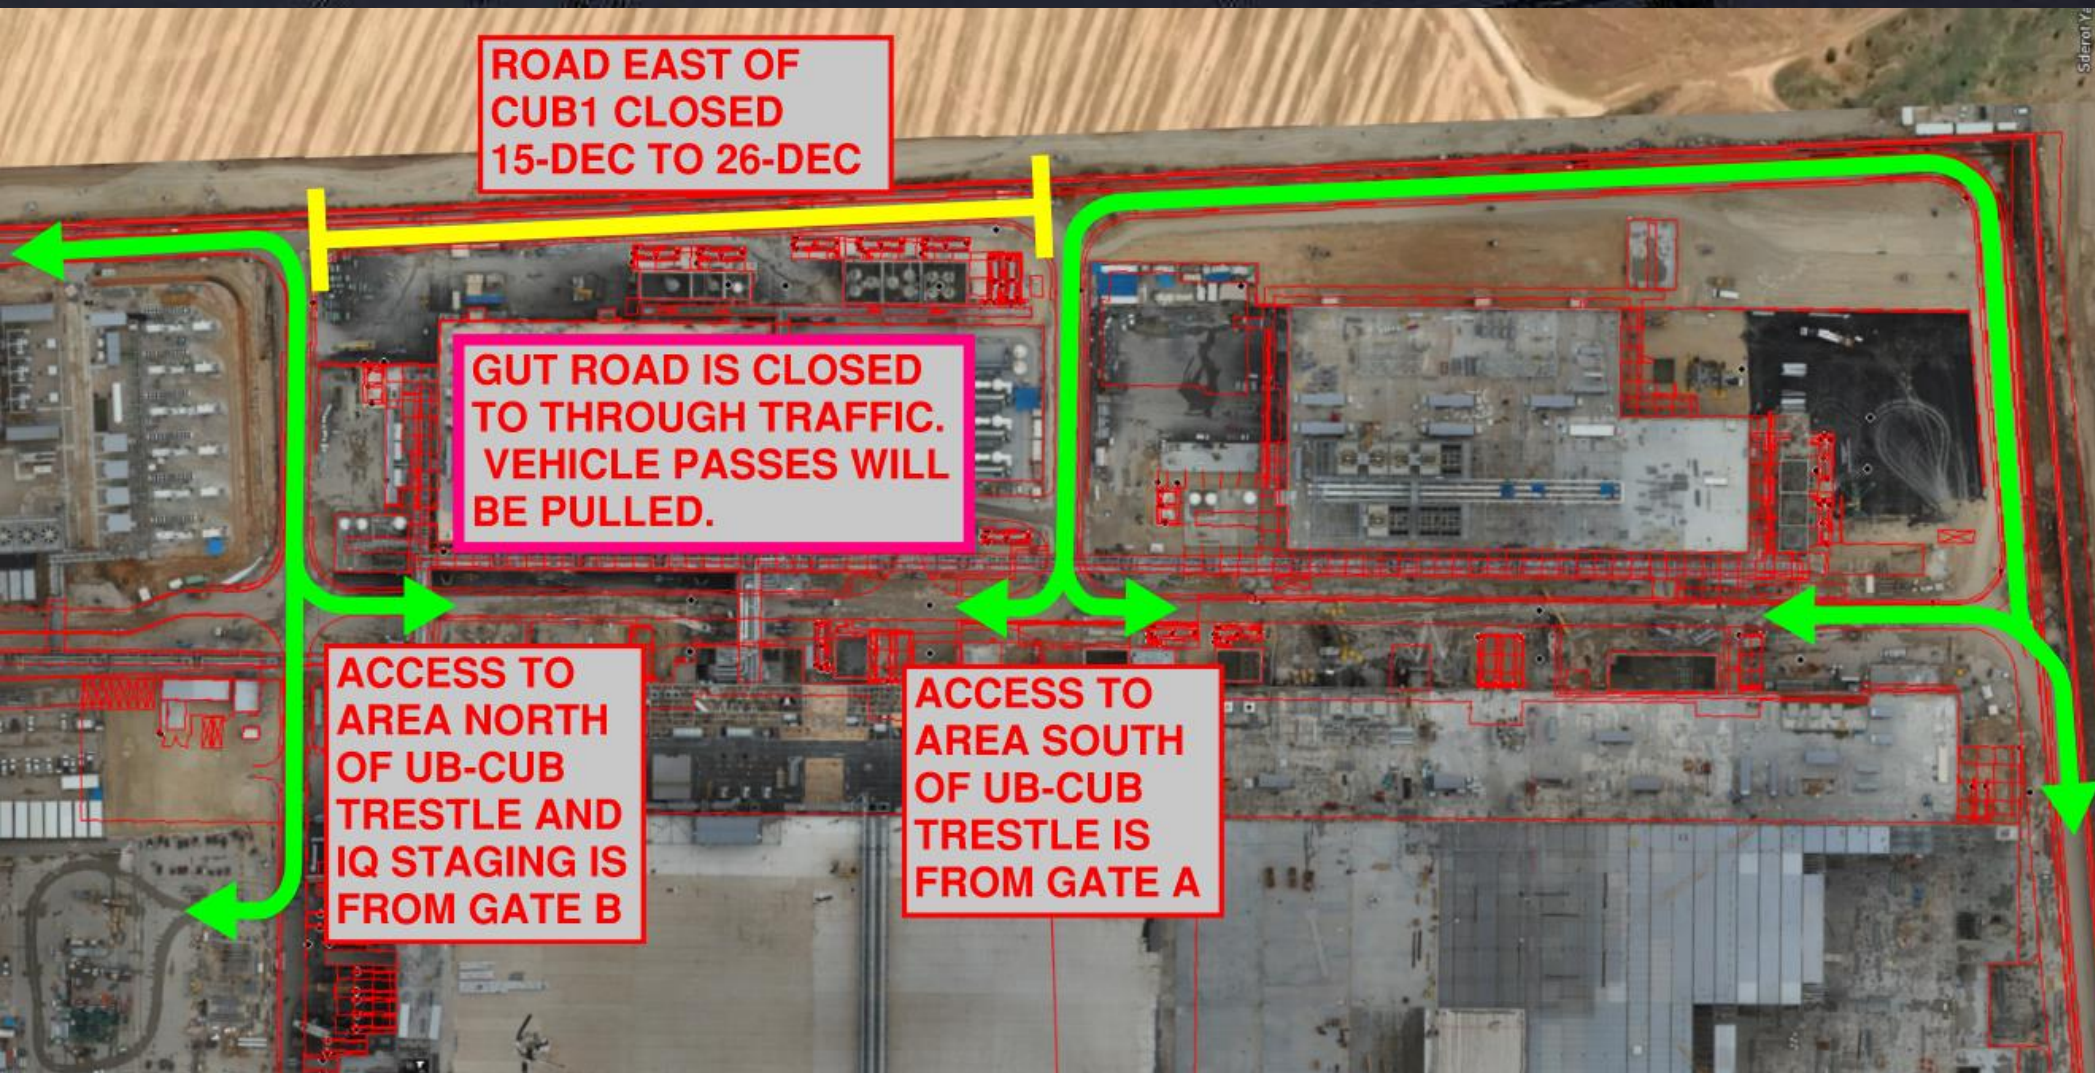




Daily Coordination Meeting

Site Logistics

South

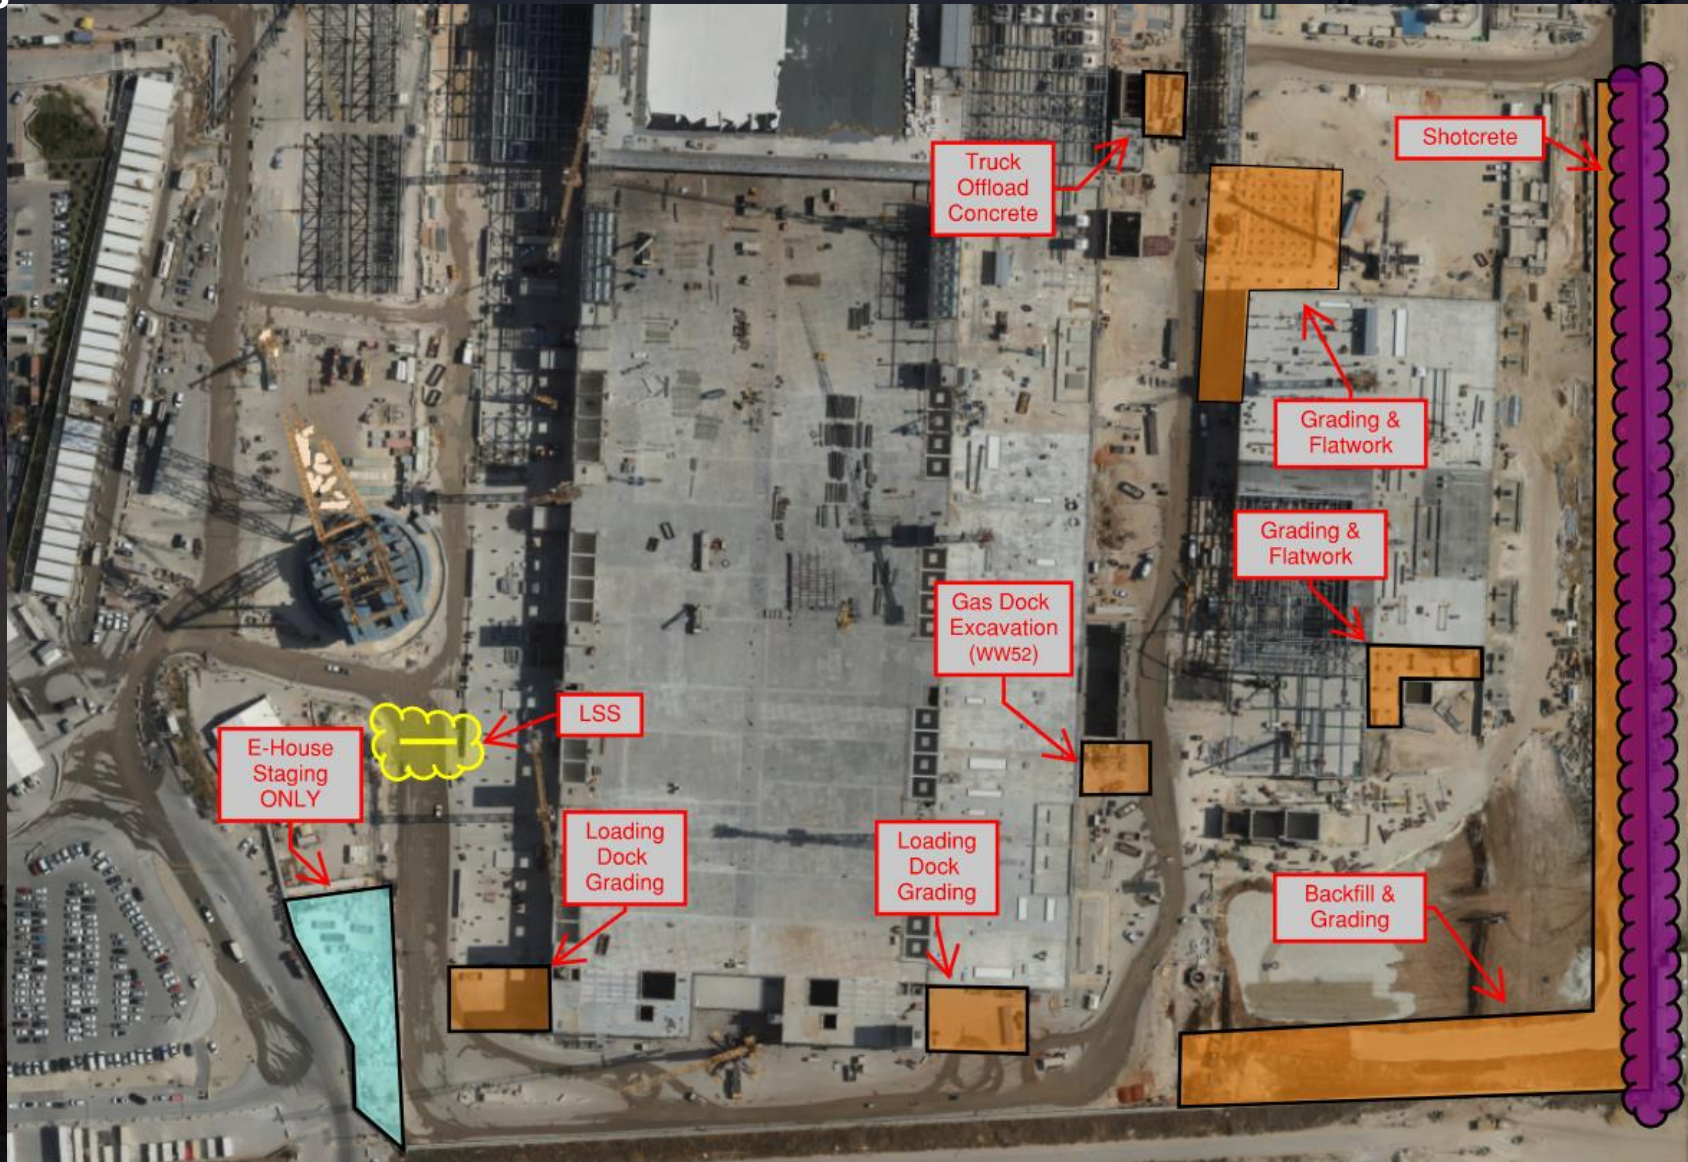

Fall protection plans

Management needs to do more than just tell employees, "Take a harness and secure yourself."

Give your employees a plan to work with!



HCC/EHS Weekend Work- 20.12.2024

White Board Meeting in Beavers at 06:30

Superintendents

Ethan Wolery 052-6041765
Idan Goffer 052-5279970
Avinadav Ben Yehuda 052-8197360

CSA CM

Ran Shwartz 052-8766701

MEP

Paschalis Papadopoulos 052-2168215
Udi (Ehud) Komi 052-6215327
Igal Amano 052-6217328

OSM

CX/QA

Calum Martin 052-4372208
John Renwick 052-3820589

Cranes

Yossi Atias 052-3060790

Safety

Safety Foreman- Adir Elmakayes- 054-7254767 Adir-Elmakayes@Hoffmancorp.com
Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com
Safety Professional - Or Pitusi- 054-812-4788 Or-Pitusi@Hoffmancorp.com

Subcontractor Weekend Work- 20.12.2024

FAB

Utility Level / Roof / Stair Shaft

Combe waste

Foreman: Denis 0525238504

Ehs: Michael 0525506596

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

Pach Taas

AVw Wall Penetration

Natanel 0543301880

Afcon E

LSS Rooms , MARSES

Avi Eli : 0526008487

MEGASON

Mod2, 4W LSS Room

Israel: 0526869393

SELA

SF Zones 4, Beauty coat.

Yoav 0548076339

Clean Room

Talad – CR 2 E – UPN Install, 4E Grating (EHS Marcelo 0523540242, Super Igor 0544509386)

Sig – 10 GUYS 5W INT 4W, 3E Handrails (EHS Beni 0506232032, Super Shmulik 0549205966)

Afcon – CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Rolling Plains – 20 guys INT NWTT 5RA, Marshaft 4W, 5RA, MOD2 CA CH 17,24,10 (Super oleg +353873794553 , 0542689370 , EHS MARCOV 0546596857)

Chemo –30 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)

Megason - 16 GUYS INT LEVEL + 7 GUYS ON UTILITY LEVEL FOREMAN ISRAEL BITON 0526869393 EHS GUY ISHBIT

Sela – 2E CRC (Supervisor yoav 0548076339)

Subcontractor Weekend Work- 20.12.2024

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2 1-3P

Foreman – Vadim – 053-5552472

Safety – Offek – 050-2161429

Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2

Foreman – Charles – 055-2740190

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-5P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

W&W – 138 Grating (lift 3 5P)

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Elram – 3P and 4P Exit Passage Ceiling

Foreman – ???

Safety – ???

HSAI – 1P Scrubber Containment/TC3 @ Roof

Foreman – Dave – 052-4121028

Safety – Hiam

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcela – 054-5210133

Safety – Marzuke – 054-447-7112

WJG

W&W – grating all over

Foreman: Chris

Safety: Tony

Afcon – Lift 2 and Utility Level Cable Tray

Foreman: Montu 055 911 6973

Safety: Pradeep 055 274 2935

Chemo: 4J/5J Lift 2 Piping & Link Roof

Foreman: Maor 050 988 9071

Safety: Erez 054 971 6840

SK: Lift 2 Piping

Foreman: Taufik: 054 94333592

Pach Taas: All over

Foreman: Tomer 050 767 0585

Safety: Jad 050 5405016

Subcontractor Weekend Work- 20.12.2024

CUB

Chemo Aharon CUB 1:

Eli – 054-9966318

Leonid – 054-8883878

Sami Najami CUB 2:

Husein – 052-6917461

Alon – 050-9895008

HSAI: CUB 2

Sergey – 055-2728807

SELA: CUB 1

YOAB: 054-8076339

Sergey: 052-6650046

D&P: CUB 2

Trestle

SNJ:

PIPES –T-20

STEEL –Galvanized paint + steel adjustment - T20

FORMAN

ATEF- 0542287499

SAFETY TRESTLE

Alon Matan tel. +972 50-989-5008

Siding

Site

D.A.- shotcrete

ELMOR

Olizki – T.O.L, east road

Daily Coordination Meeting



14:00 Sign In
