

# Daily Coordination Meeting



14:00 Sign In


# Daily Coordination Meeting

## General Topics:


- Hot Work Permits
- Tie-in Requests
- Weekend Work



# UTILITY LEVEL MOD1

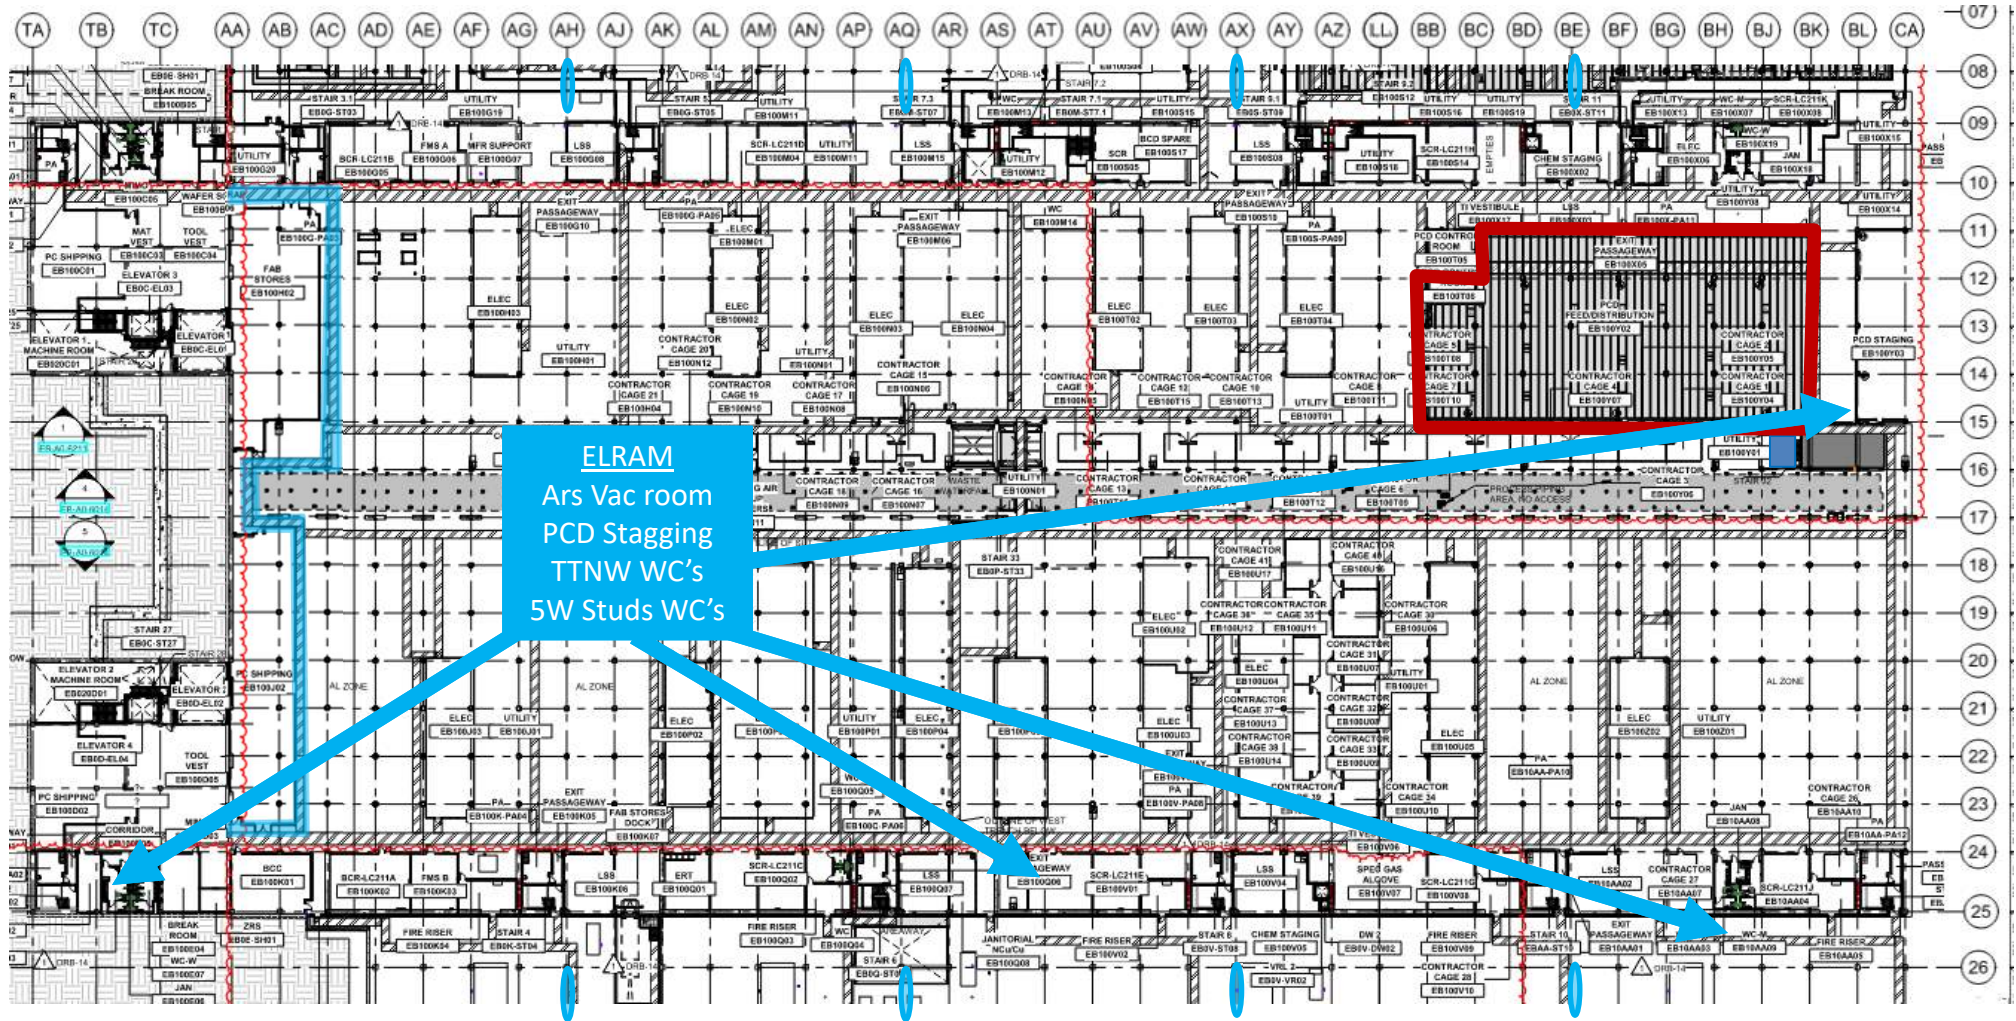

## SUT 38.1 LEVEL

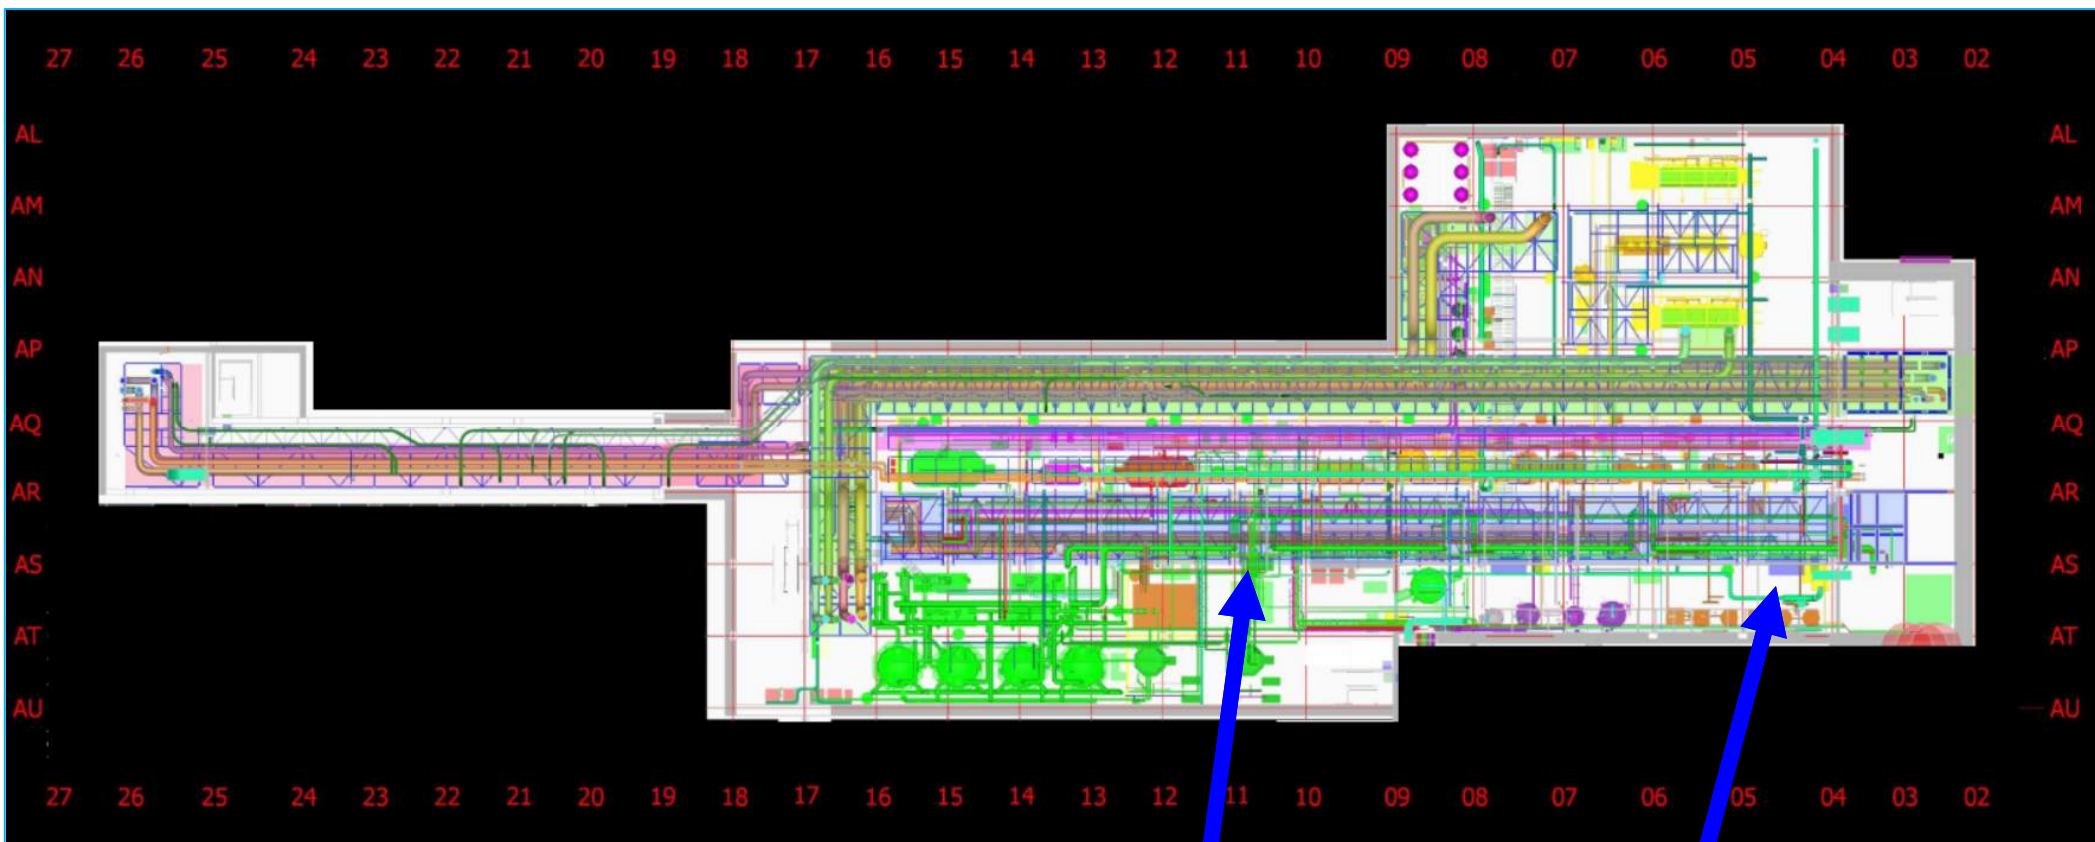

Biocide  
Totes Set  
18/2

SOG  
Ready for  
Totes set.




HOFFMAN CONSTRUCTION COMPANY



SUT 38.2 LEVEL


Rack 4b  
Inter  
Connection's

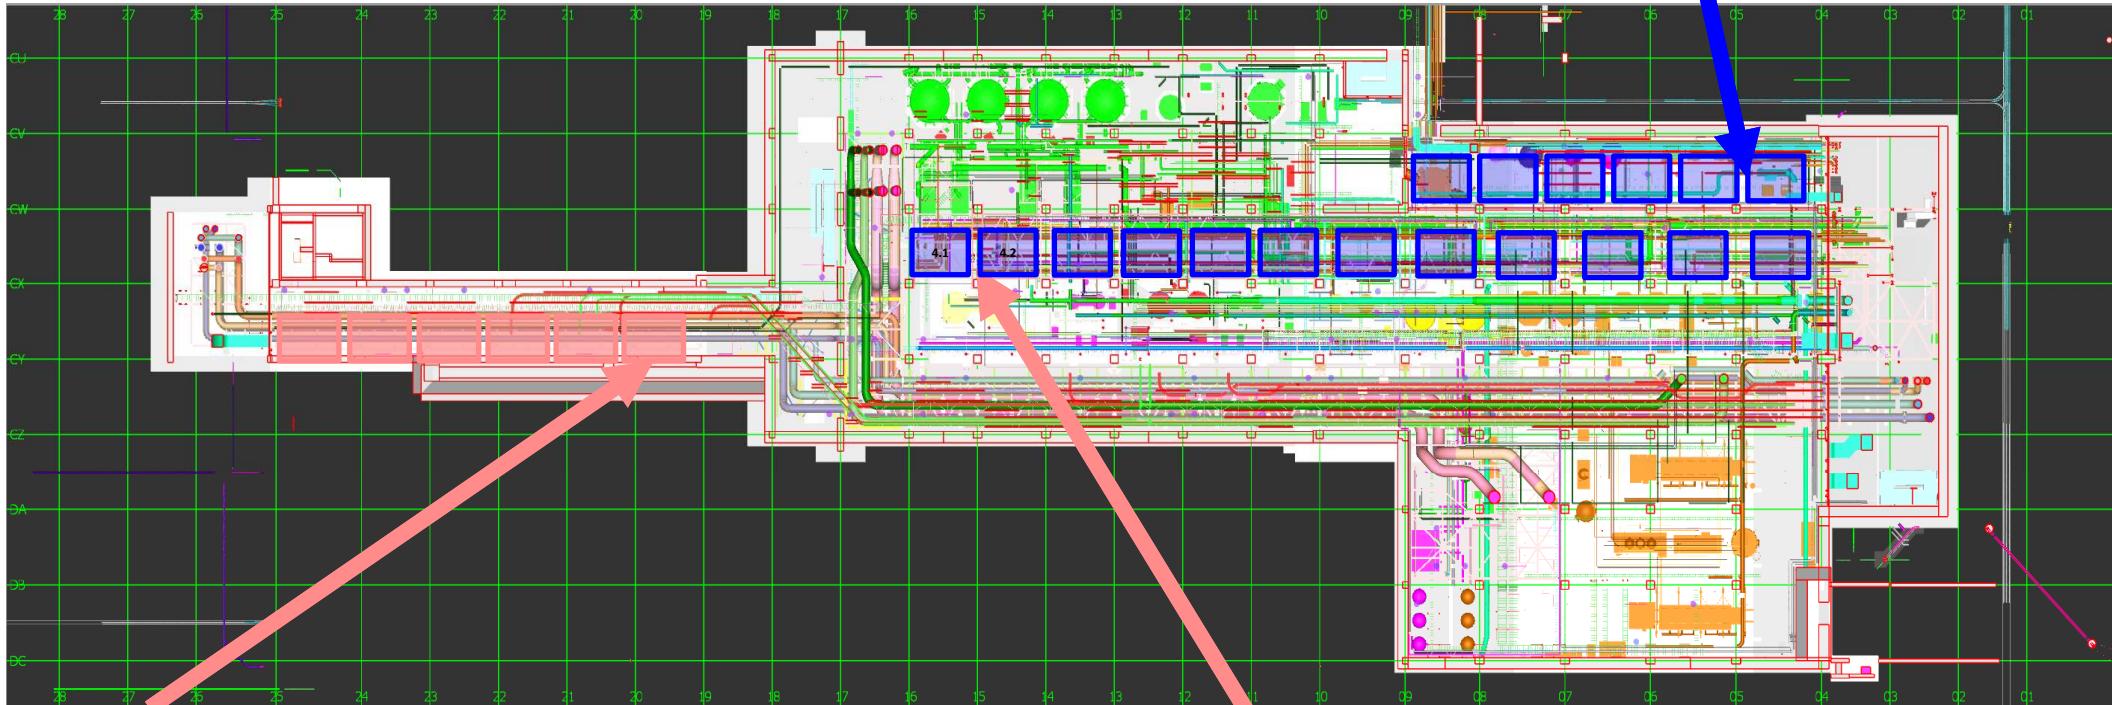

Temp stairs  
relocation

|            |          |
|------------|----------|
| 16/02/2025 | Module 1 |
| 20/02/2025 | Module 2 |
| 23/02/2025 | Module 3 |
| 26/02/2025 | Module 4 |
| 02/03/2025 | Module 5 |
| 04/03/2025 | Module 6 |

# SUBFAB BUILDOUT MOD 1

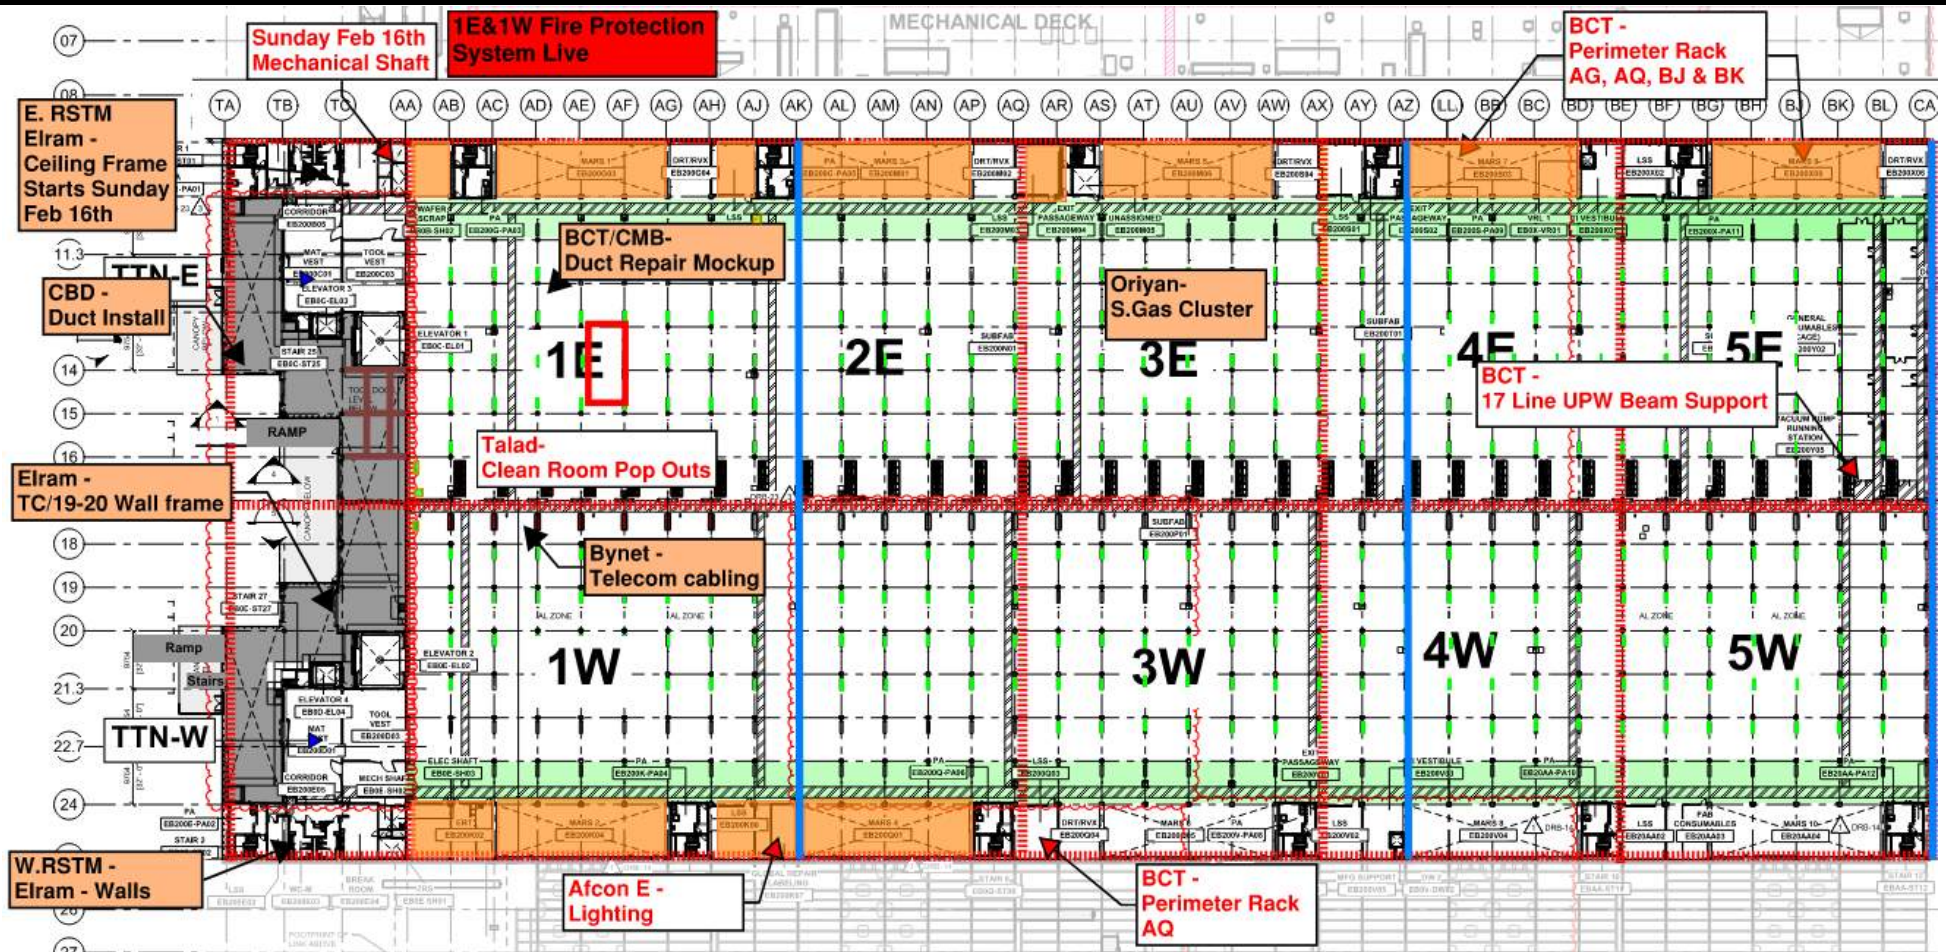

Feb 10  
AG-AP/9-11

Feb 23  
MARS 3E

Stair #5 blocked  
all Week SF Only  
2E LSS Room blocked

1E 2E 3E 4E 5E

1W 2W 3W 4W 5W

MAR 9  
BC-BG/11-15

MAR 16  
BG-CA/11-15

Feb 16  
BC-BG/19-23

MAR 23  
BG-CA/19-23

MAR 2  
MARS 3W

TTN-E


TTN-Dock Level

TTN-W


SHORING  
INSTALLED

Various room labels: EB08-ST01, EB2002-PA01, EB2002-PA02, EB2002-PA03, EB2002-PA04, EB2002-PA05, EB2002-PA06, EB2002-PA07, EB2002-PA08, EB2002-PA09, EB2002-PA10, EB2002-PA11, EB2002-PA12, EB2002-PA13, EB2002-PA14, EB2002-PA15, EB2002-PA16, EB2002-PA17, EB2002-PA18, EB2002-PA19, EB2002-PA20, EB2002-PA21, EB2002-PA22, EB2002-PA23, EB2002-PA24, EB2002-PA25, EB2002-PA26, EB2002-PA27, EB2002-PA28, EB2002-PA29, EB2002-PA30, EB2002-PA31, EB2002-PA32, EB2002-PA33, EB2002-PA34, EB2002-PA35, EB2002-PA36, EB2002-PA37, EB2002-PA38, EB2002-PA39, EB2002-PA40, EB2002-PA41, EB2002-PA42, EB2002-PA43, EB2002-PA44, EB2002-PA45, EB2002-PA46, EB2002-PA47, EB2002-PA48, EB2002-PA49, EB2002-PA50, EB2002-PA51, EB2002-PA52, EB2002-PA53, EB2002-PA54, EB2002-PA55, EB2002-PA56, EB2002-PA57, EB2002-PA58, EB2002-PA59, EB2002-PA60, EB2002-PA61, EB2002-PA62, EB2002-PA63, EB2002-PA64, EB2002-PA65, EB2002-PA66, EB2002-PA67, EB2002-PA68, EB2002-PA69, EB2002-PA70, EB2002-PA71, EB2002-PA72, EB2002-PA73, EB2002-PA74, EB2002-PA75, EB2002-PA76, EB2002-PA77, EB2002-PA78, EB2002-PA79, EB2002-PA80, EB2002-PA81, EB2002-PA82, EB2002-PA83, EB2002-PA84, EB2002-PA85, EB2002-PA86, EB2002-PA87, EB2002-PA88, EB2002-PA89, EB2002-PA90, EB2002-PA91, EB2002-PA92, EB2002-PA93, EB2002-PA94, EB2002-PA95, EB2002-PA96, EB2002-PA97, EB2002-PA98, EB2002-PA99, EB2002-PA100.


# BCT Pressure Tests Today

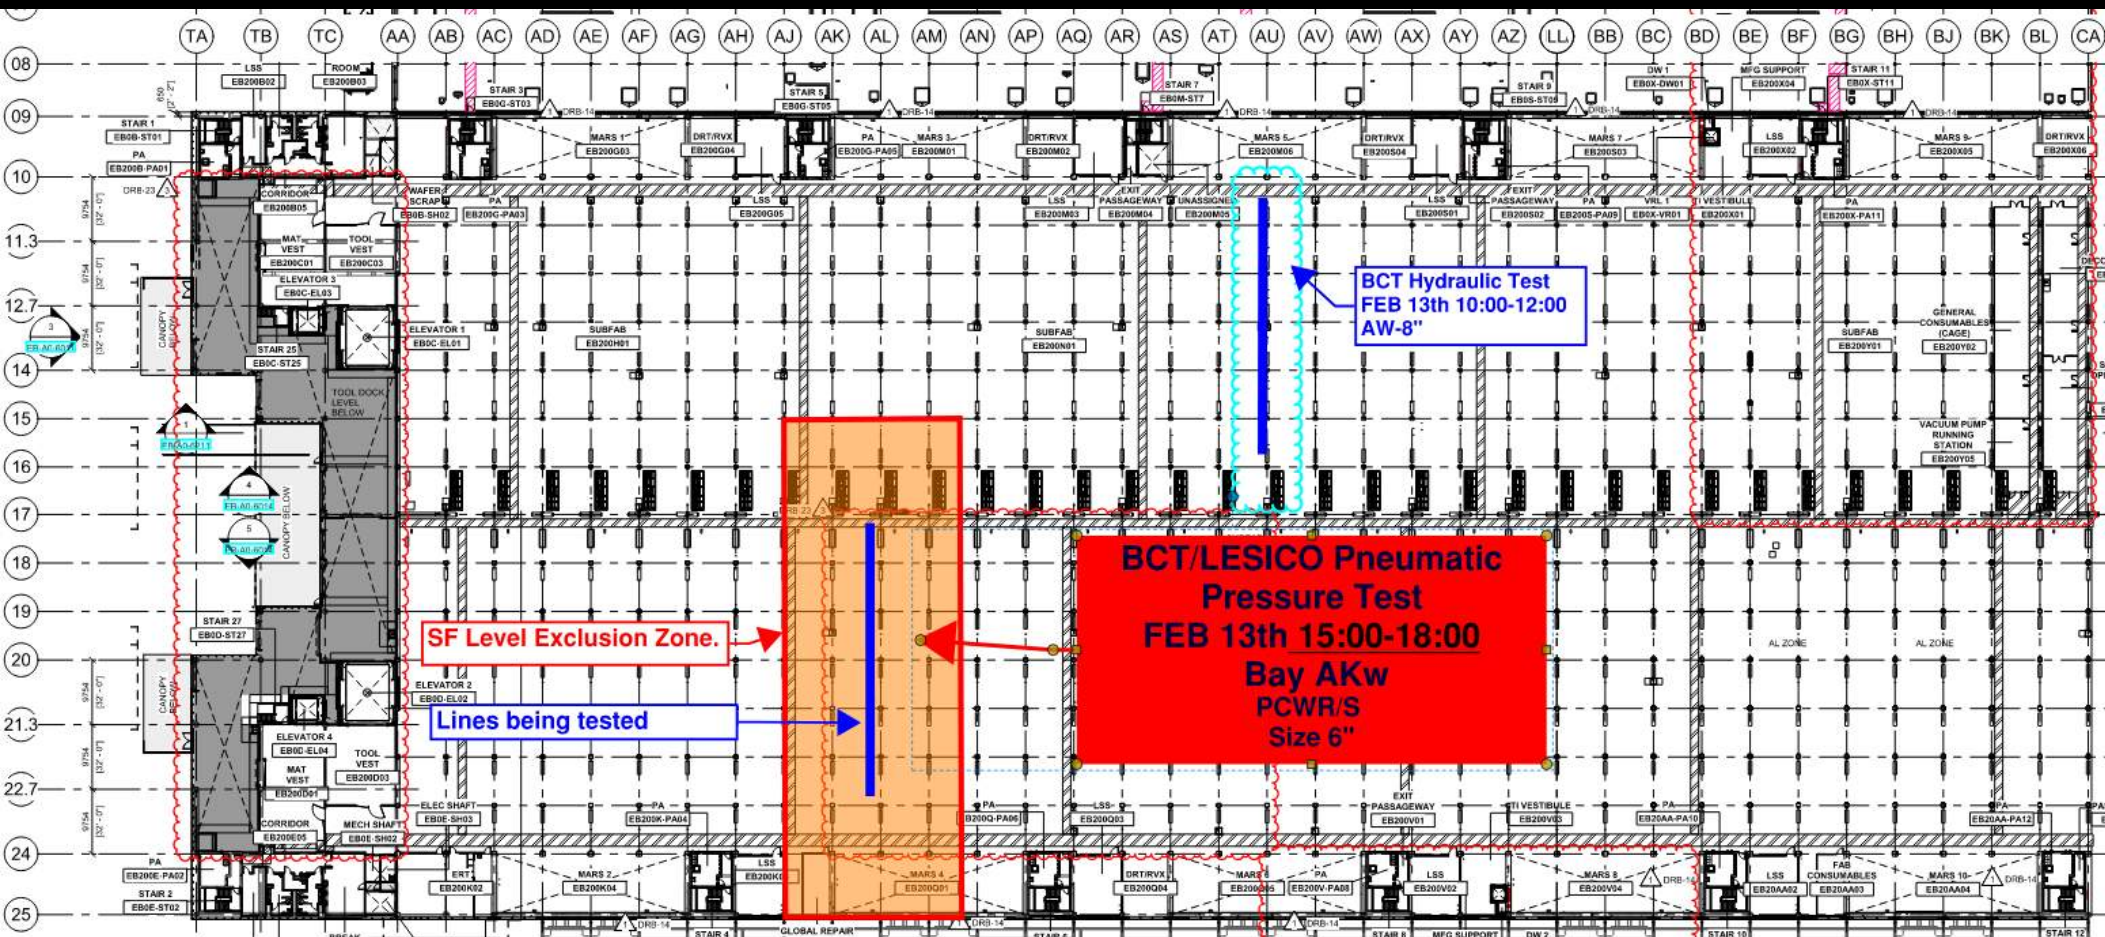


# Lesico NDT Tests Today

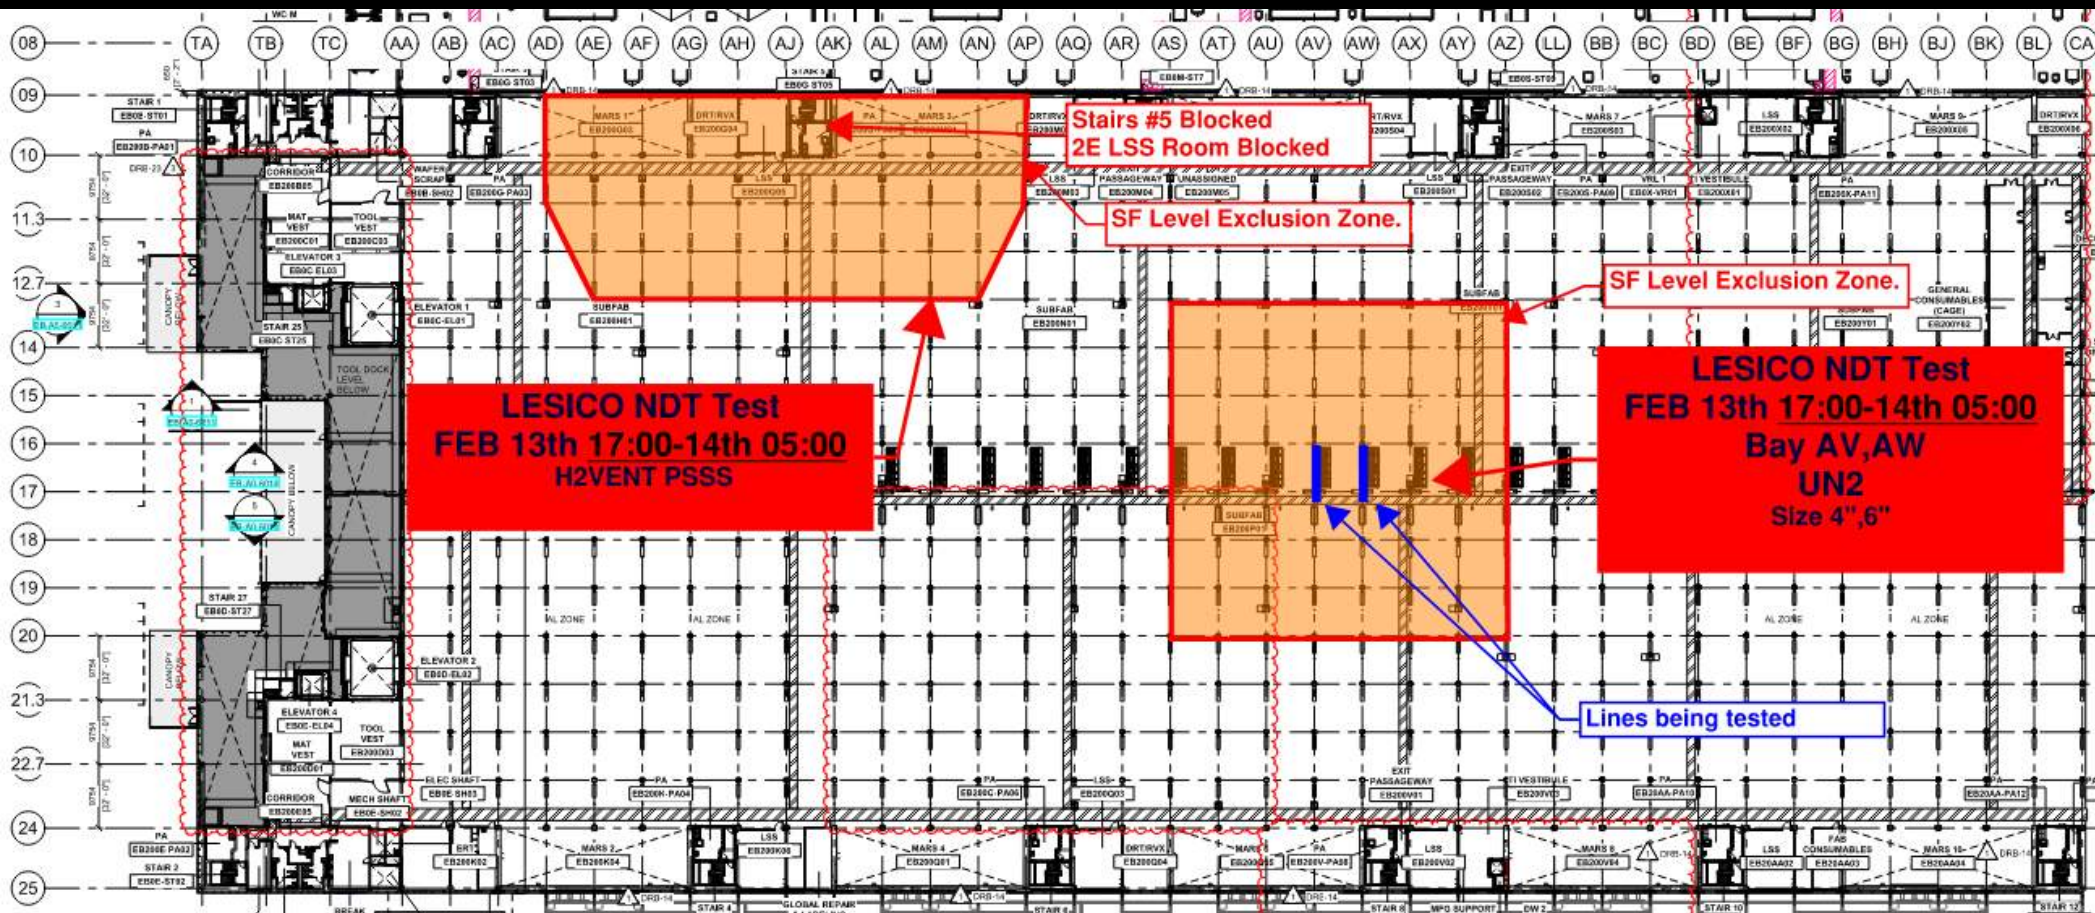



# BCT Pressure Tests Sunday

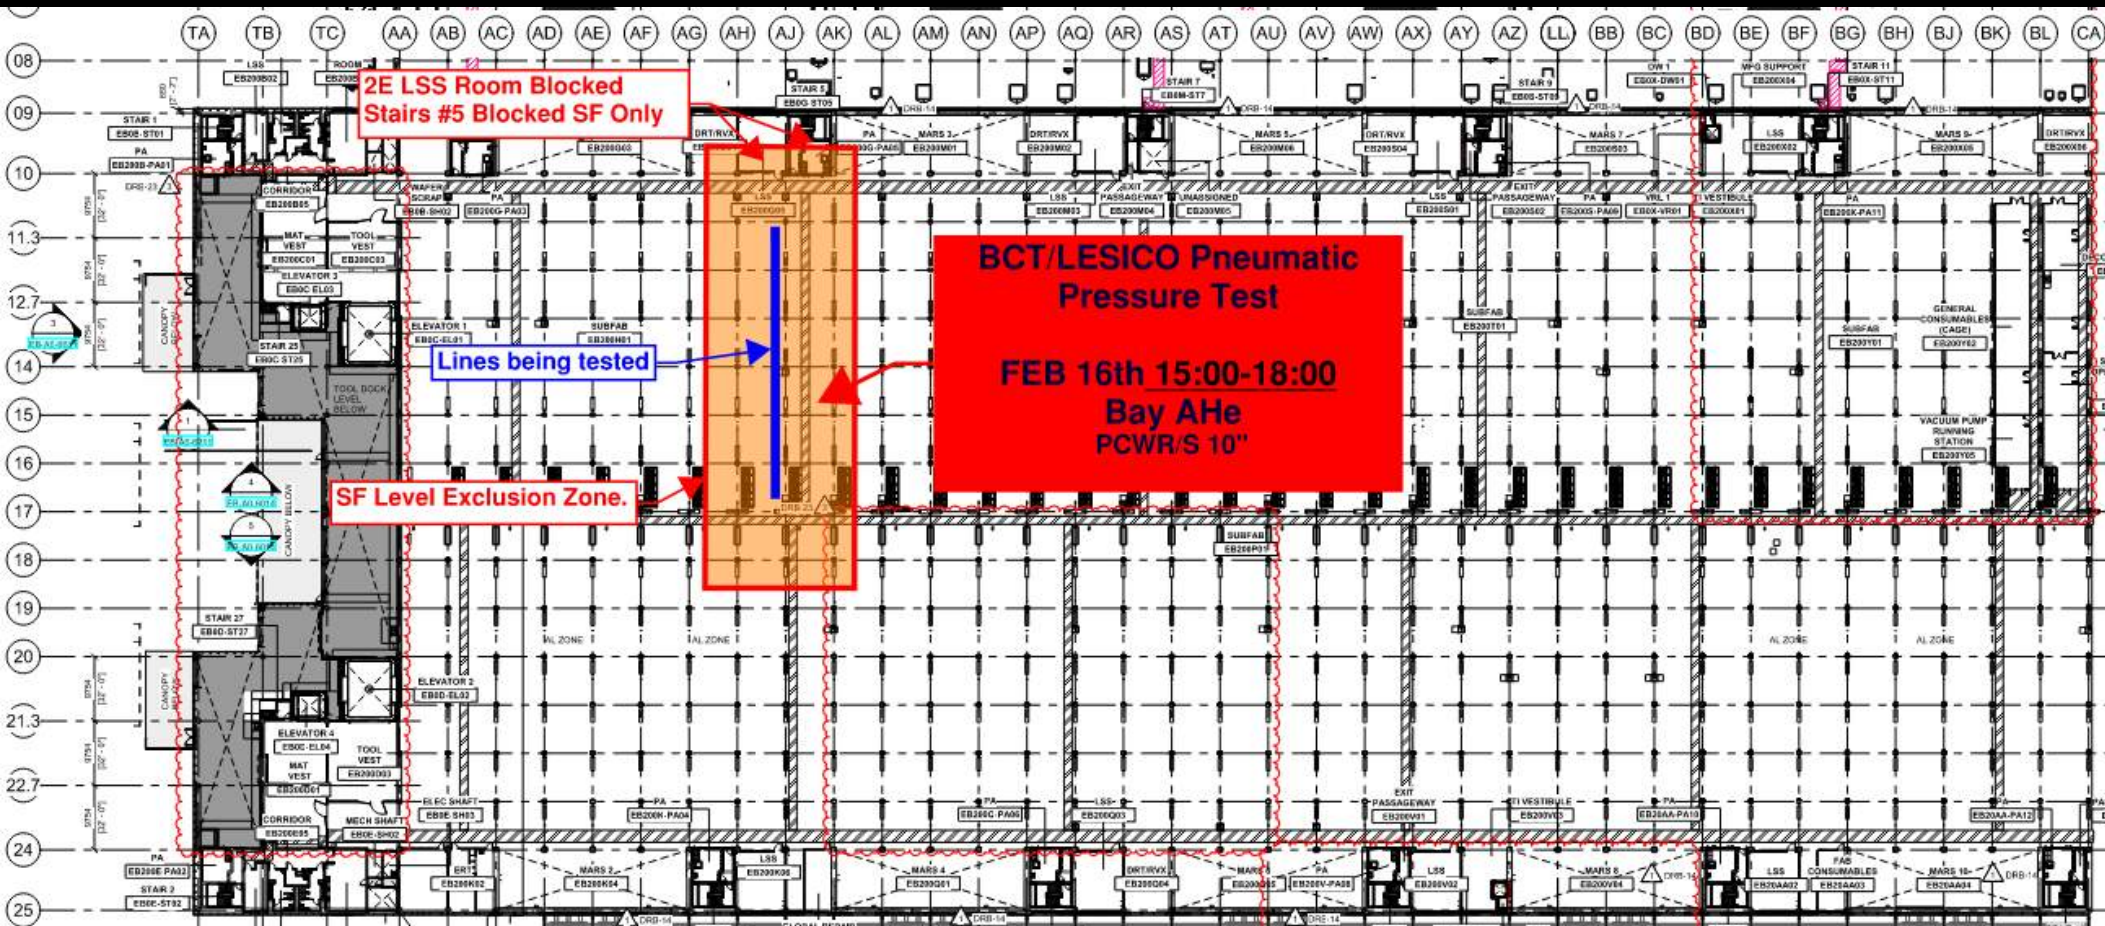


# SUBFAB BUILDOUT MOD 2

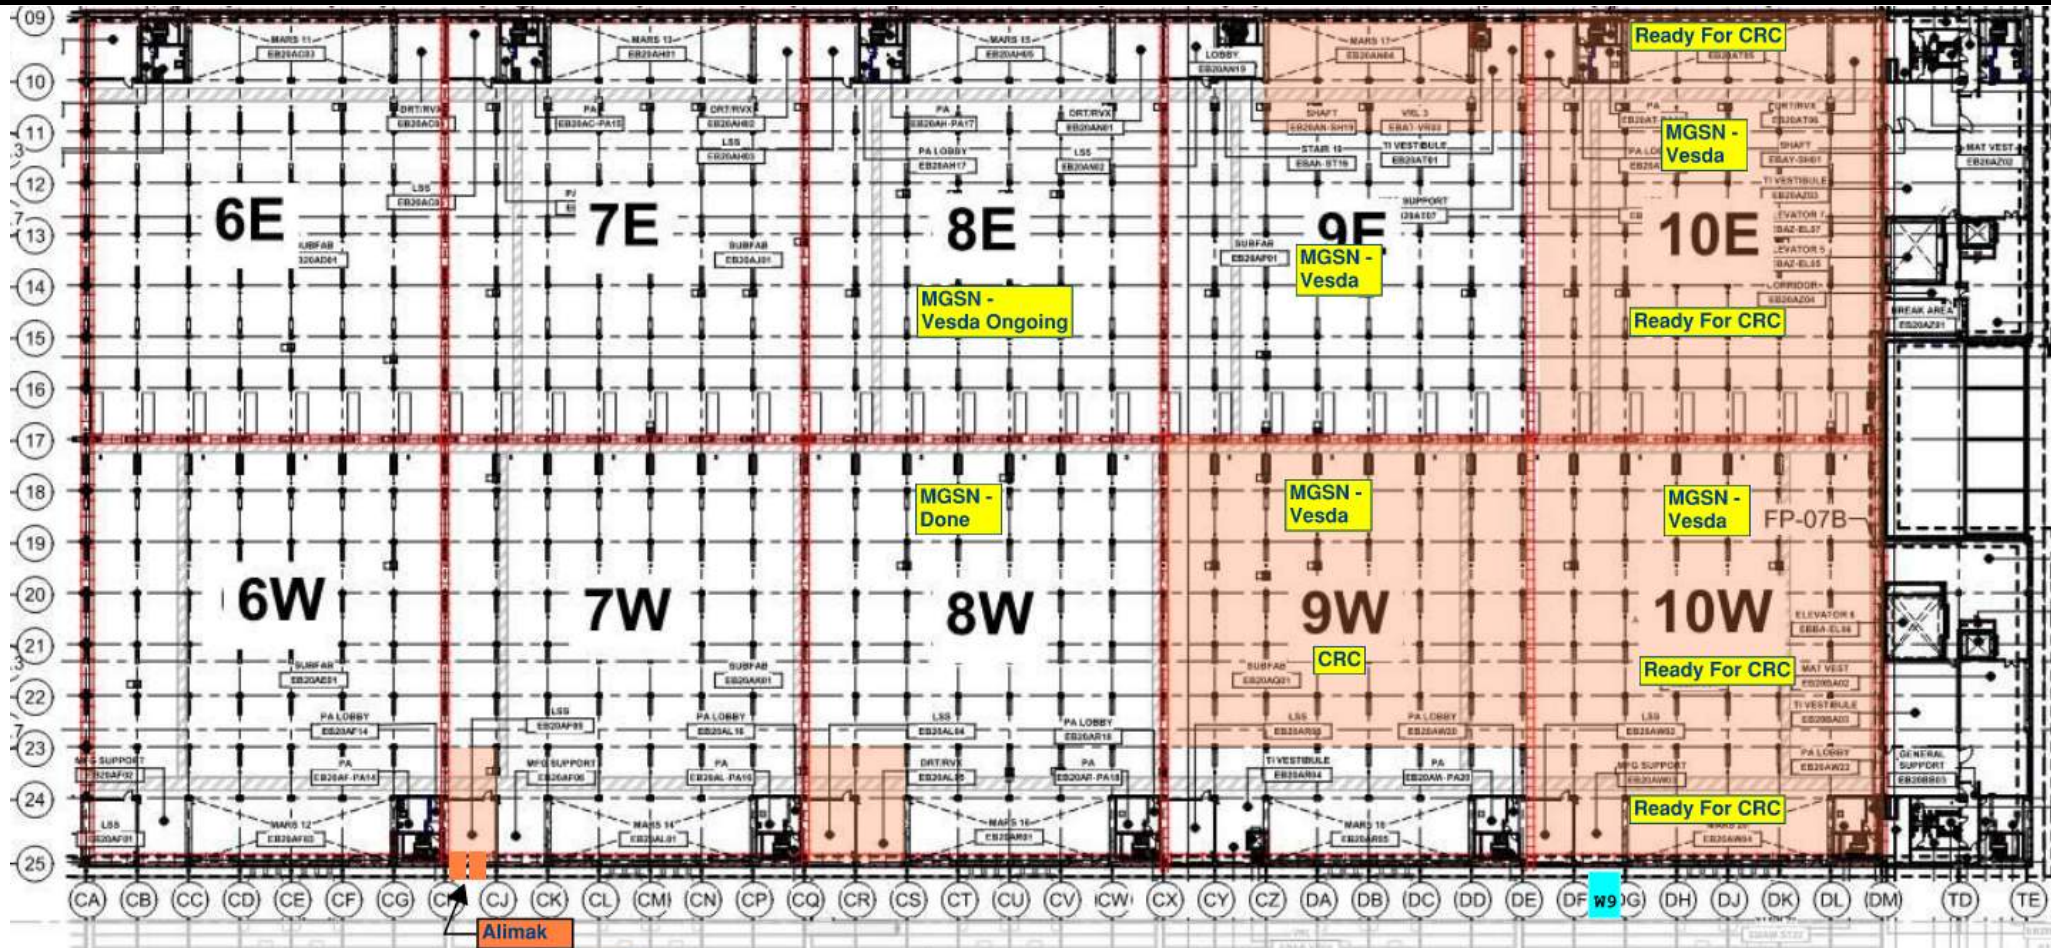

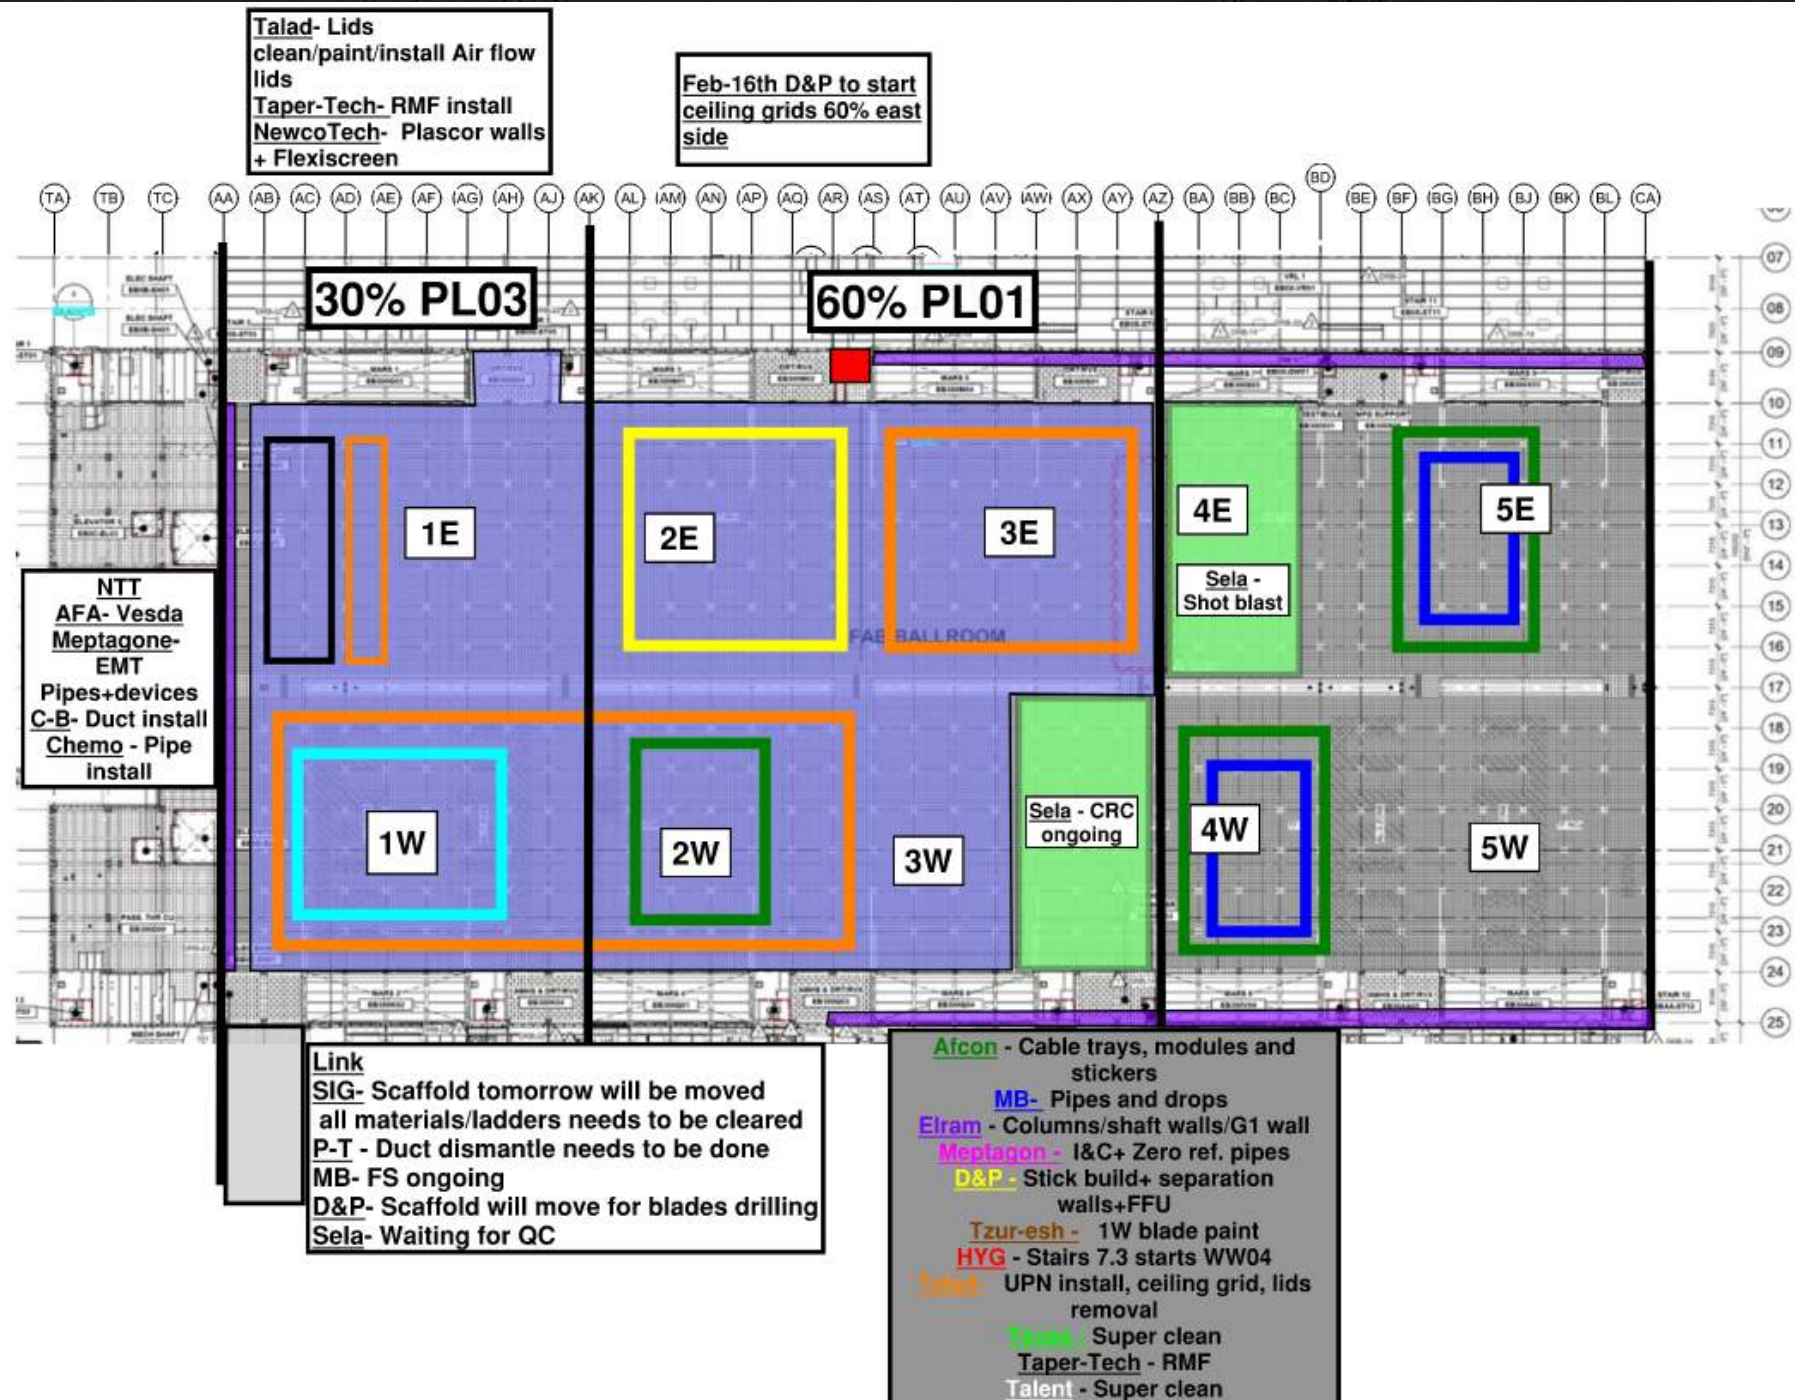

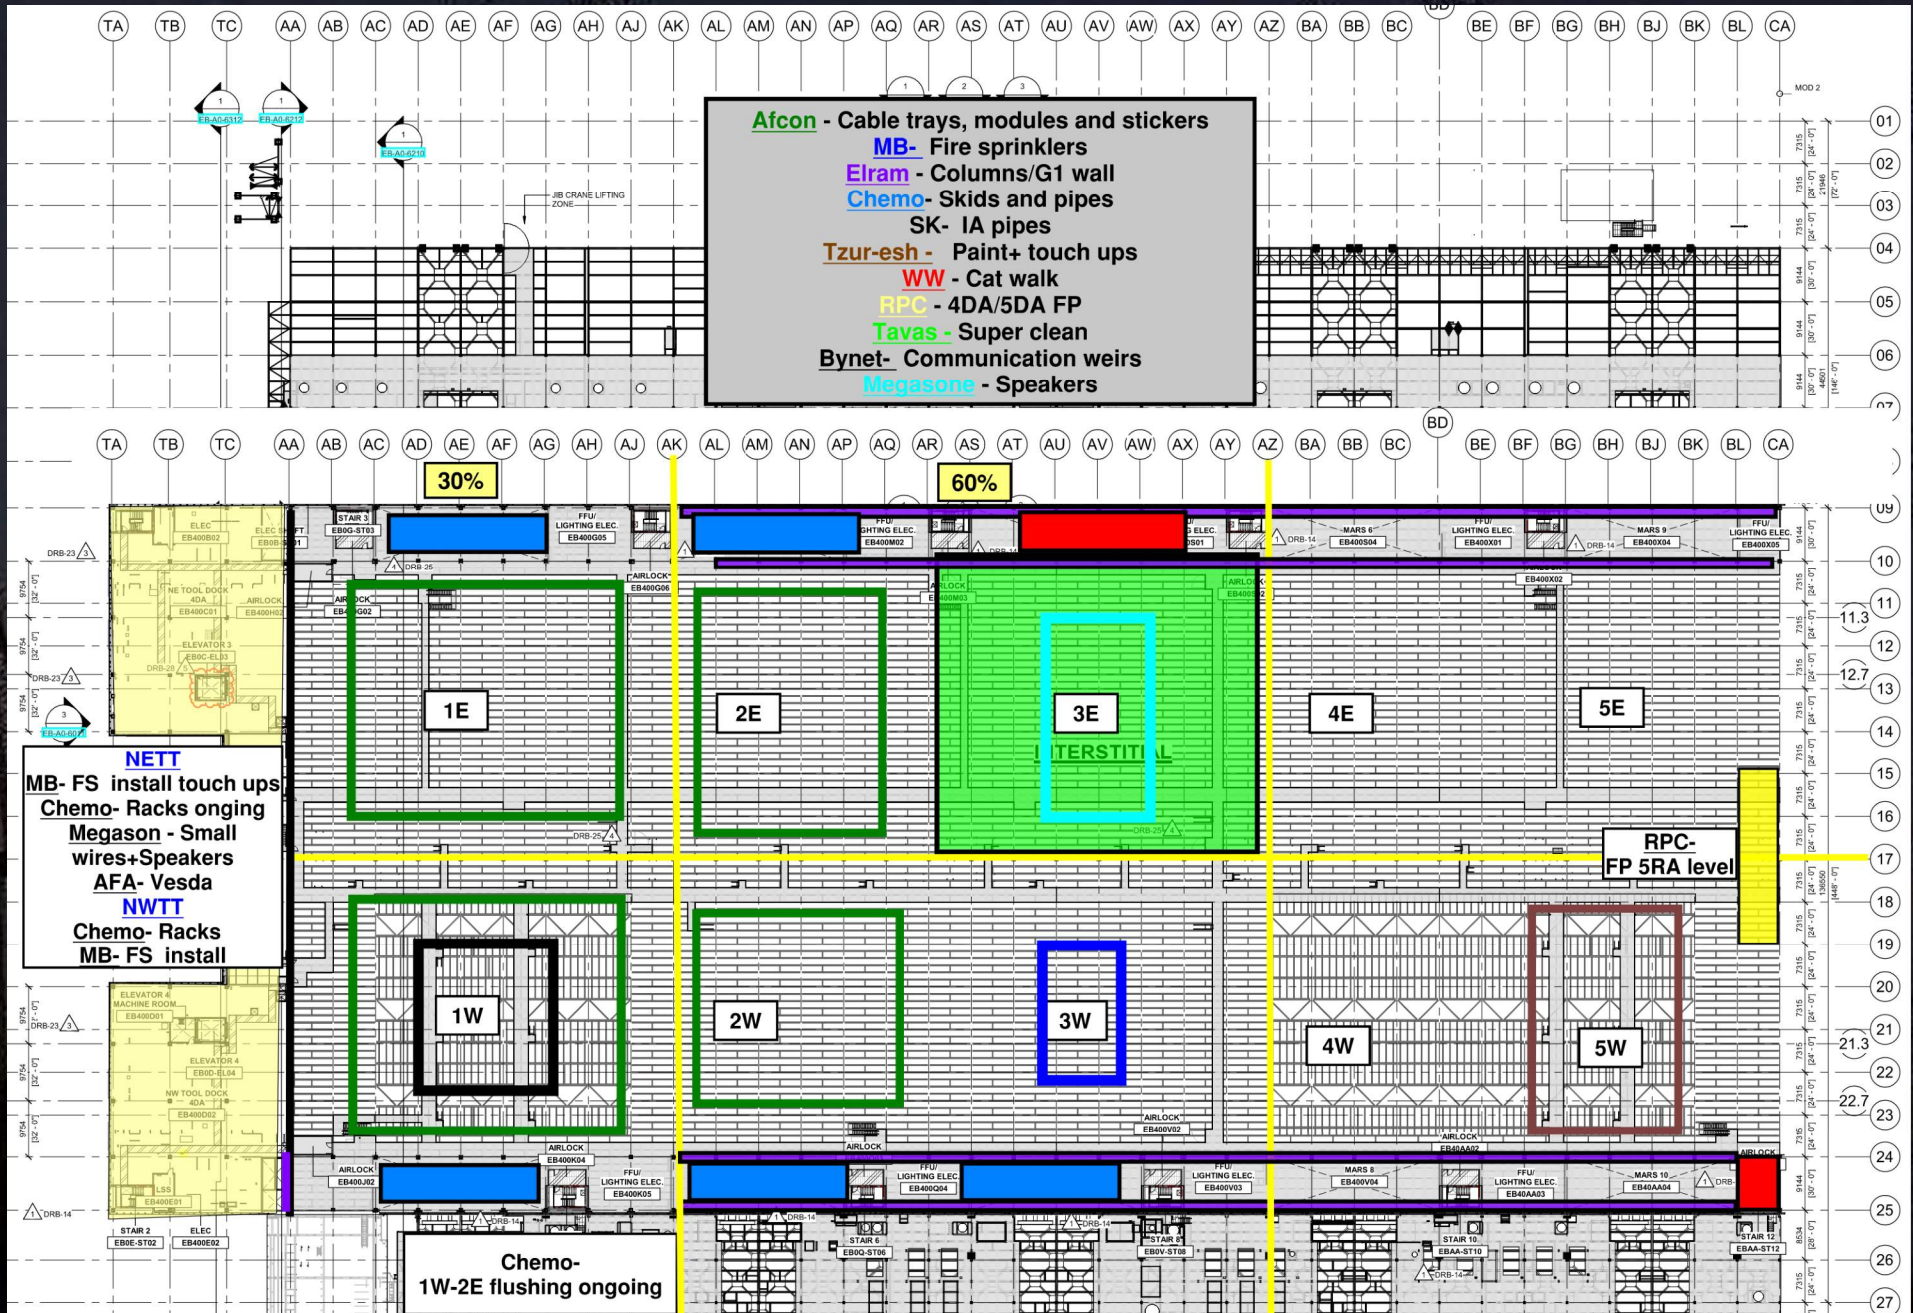

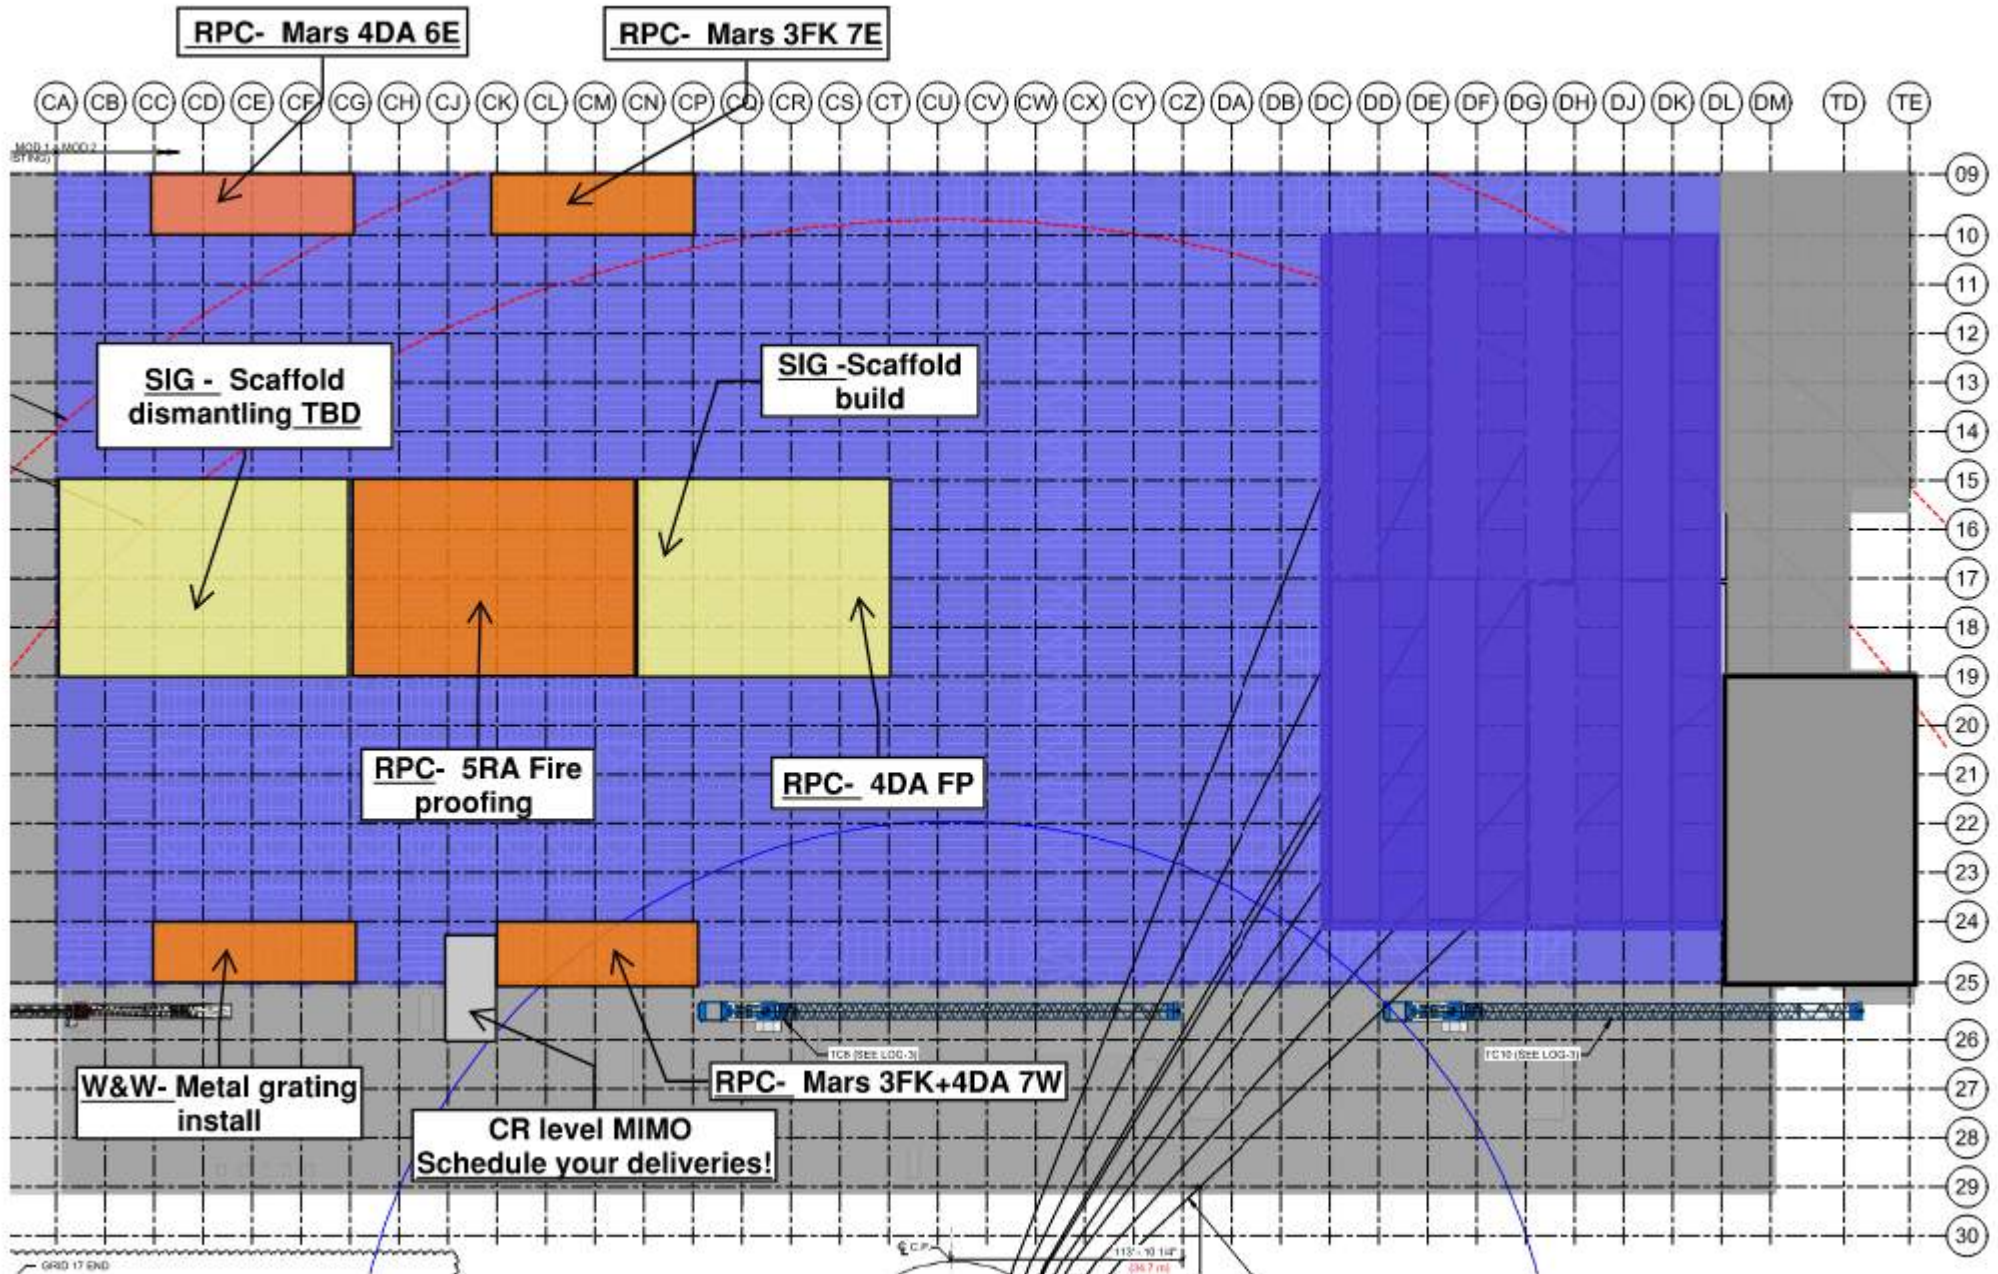








**Alimak Shut Down**  
night Shift  
Sunday + Monday  
FEB/11~12  
from 16:00 p.m till 05:00 a.m

# Siding Penetration Request Form

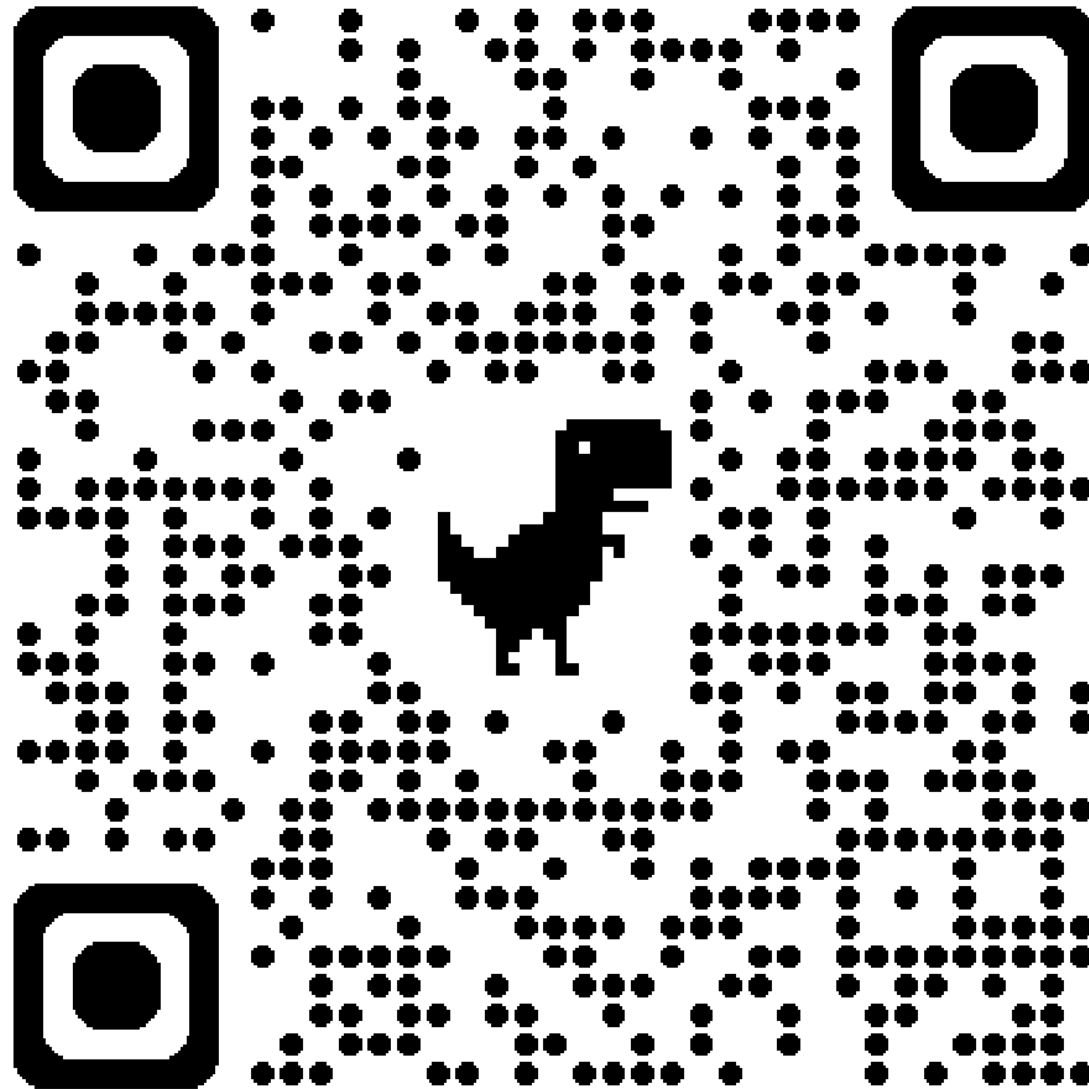

Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

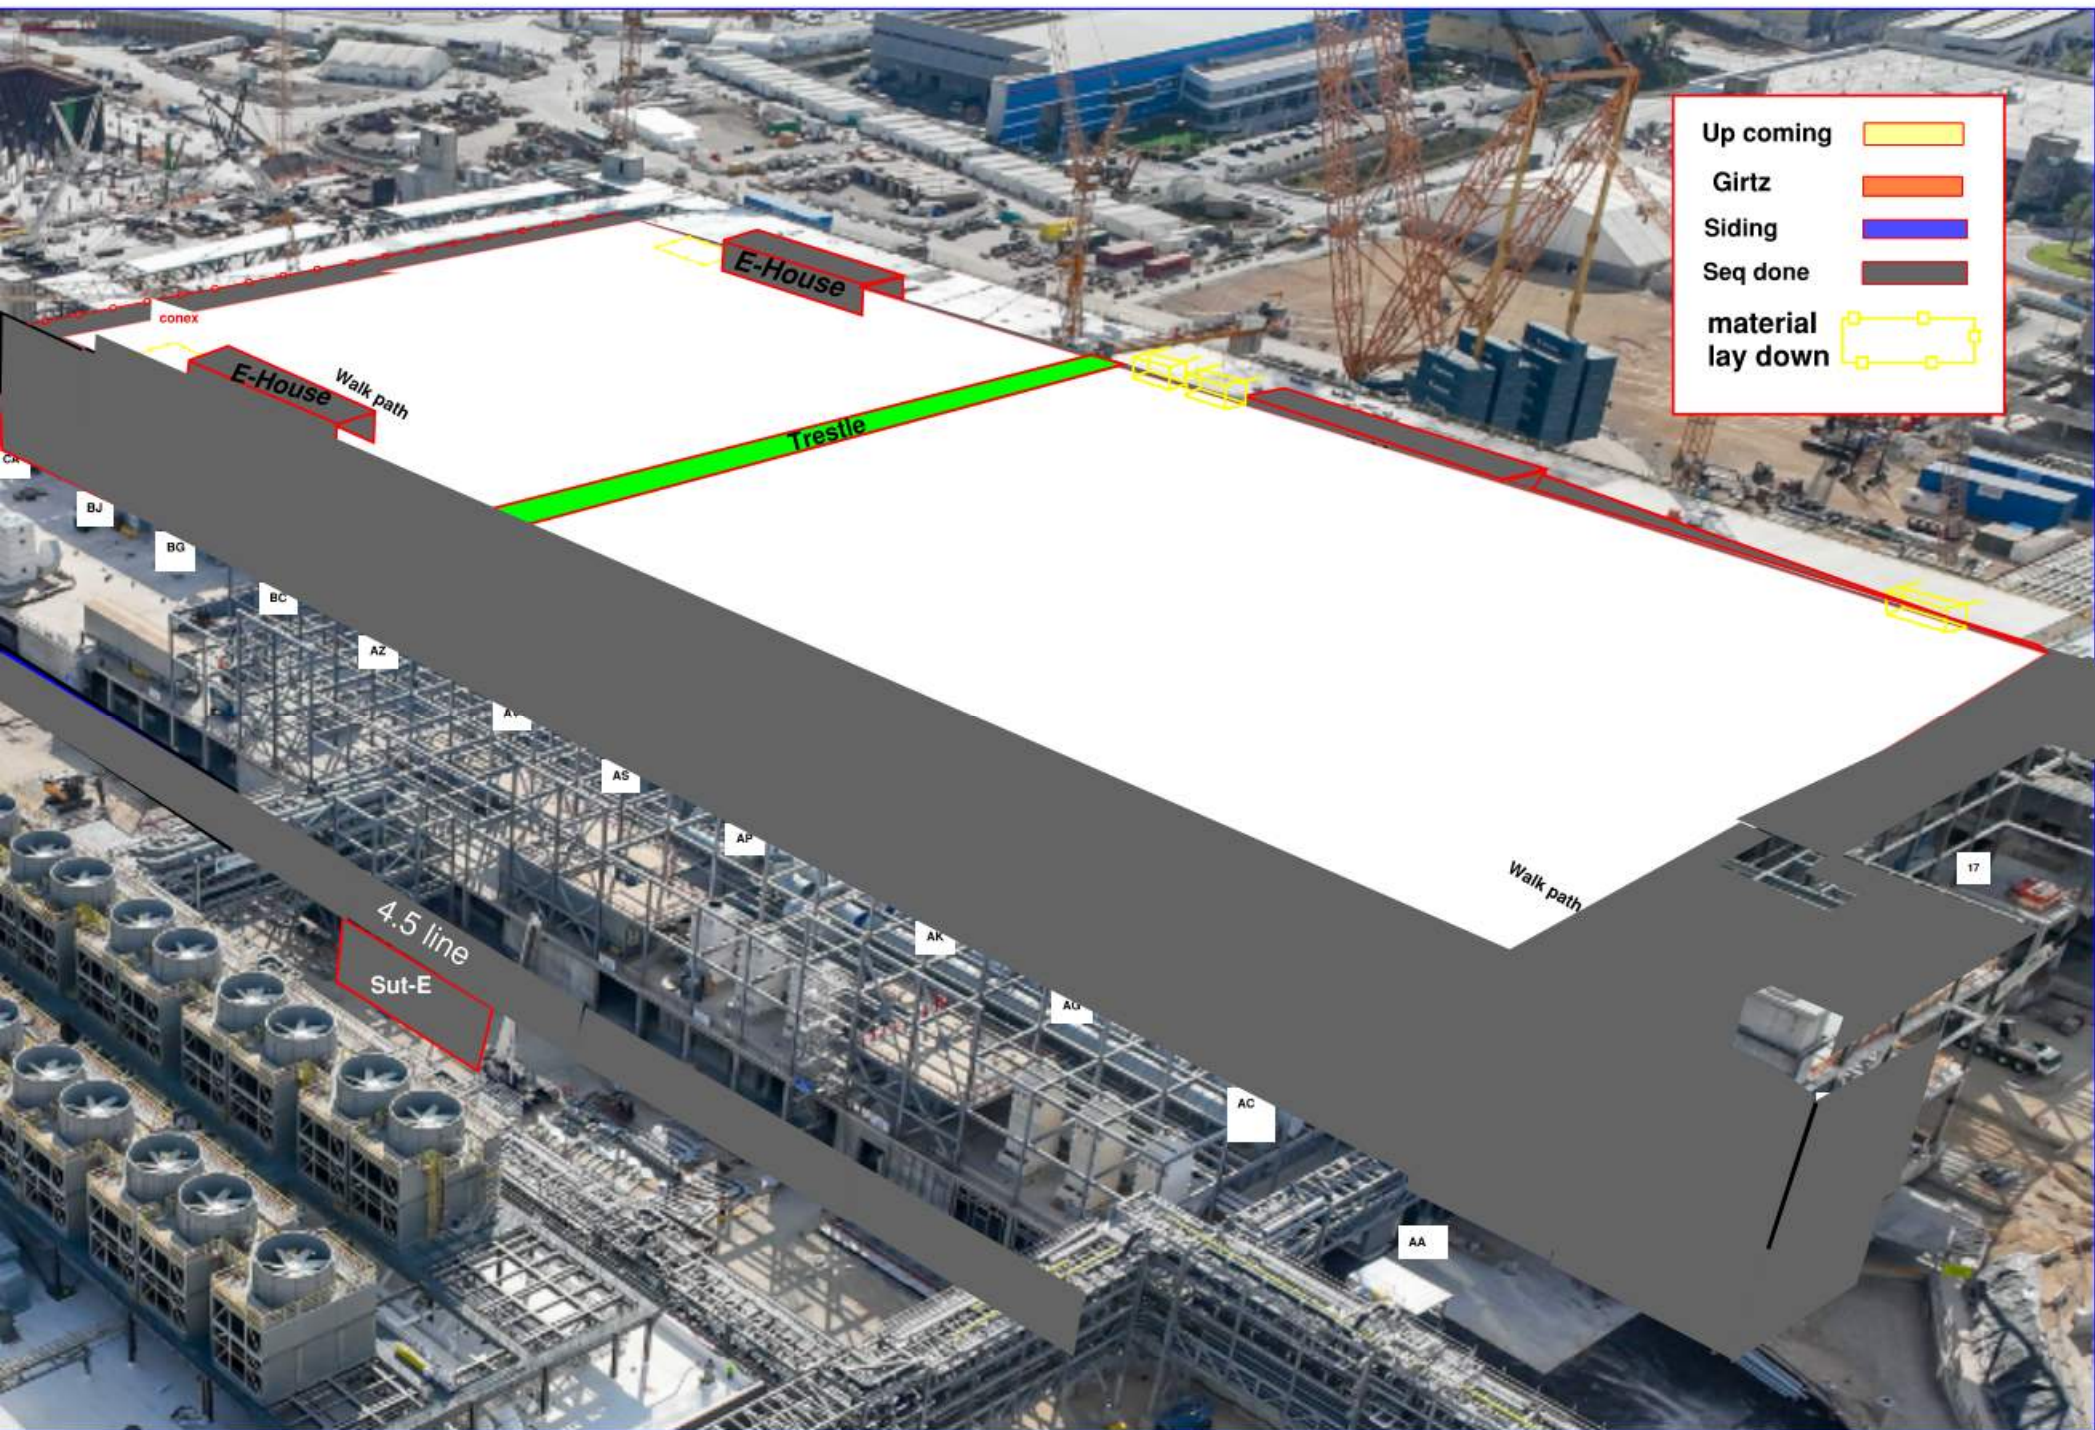

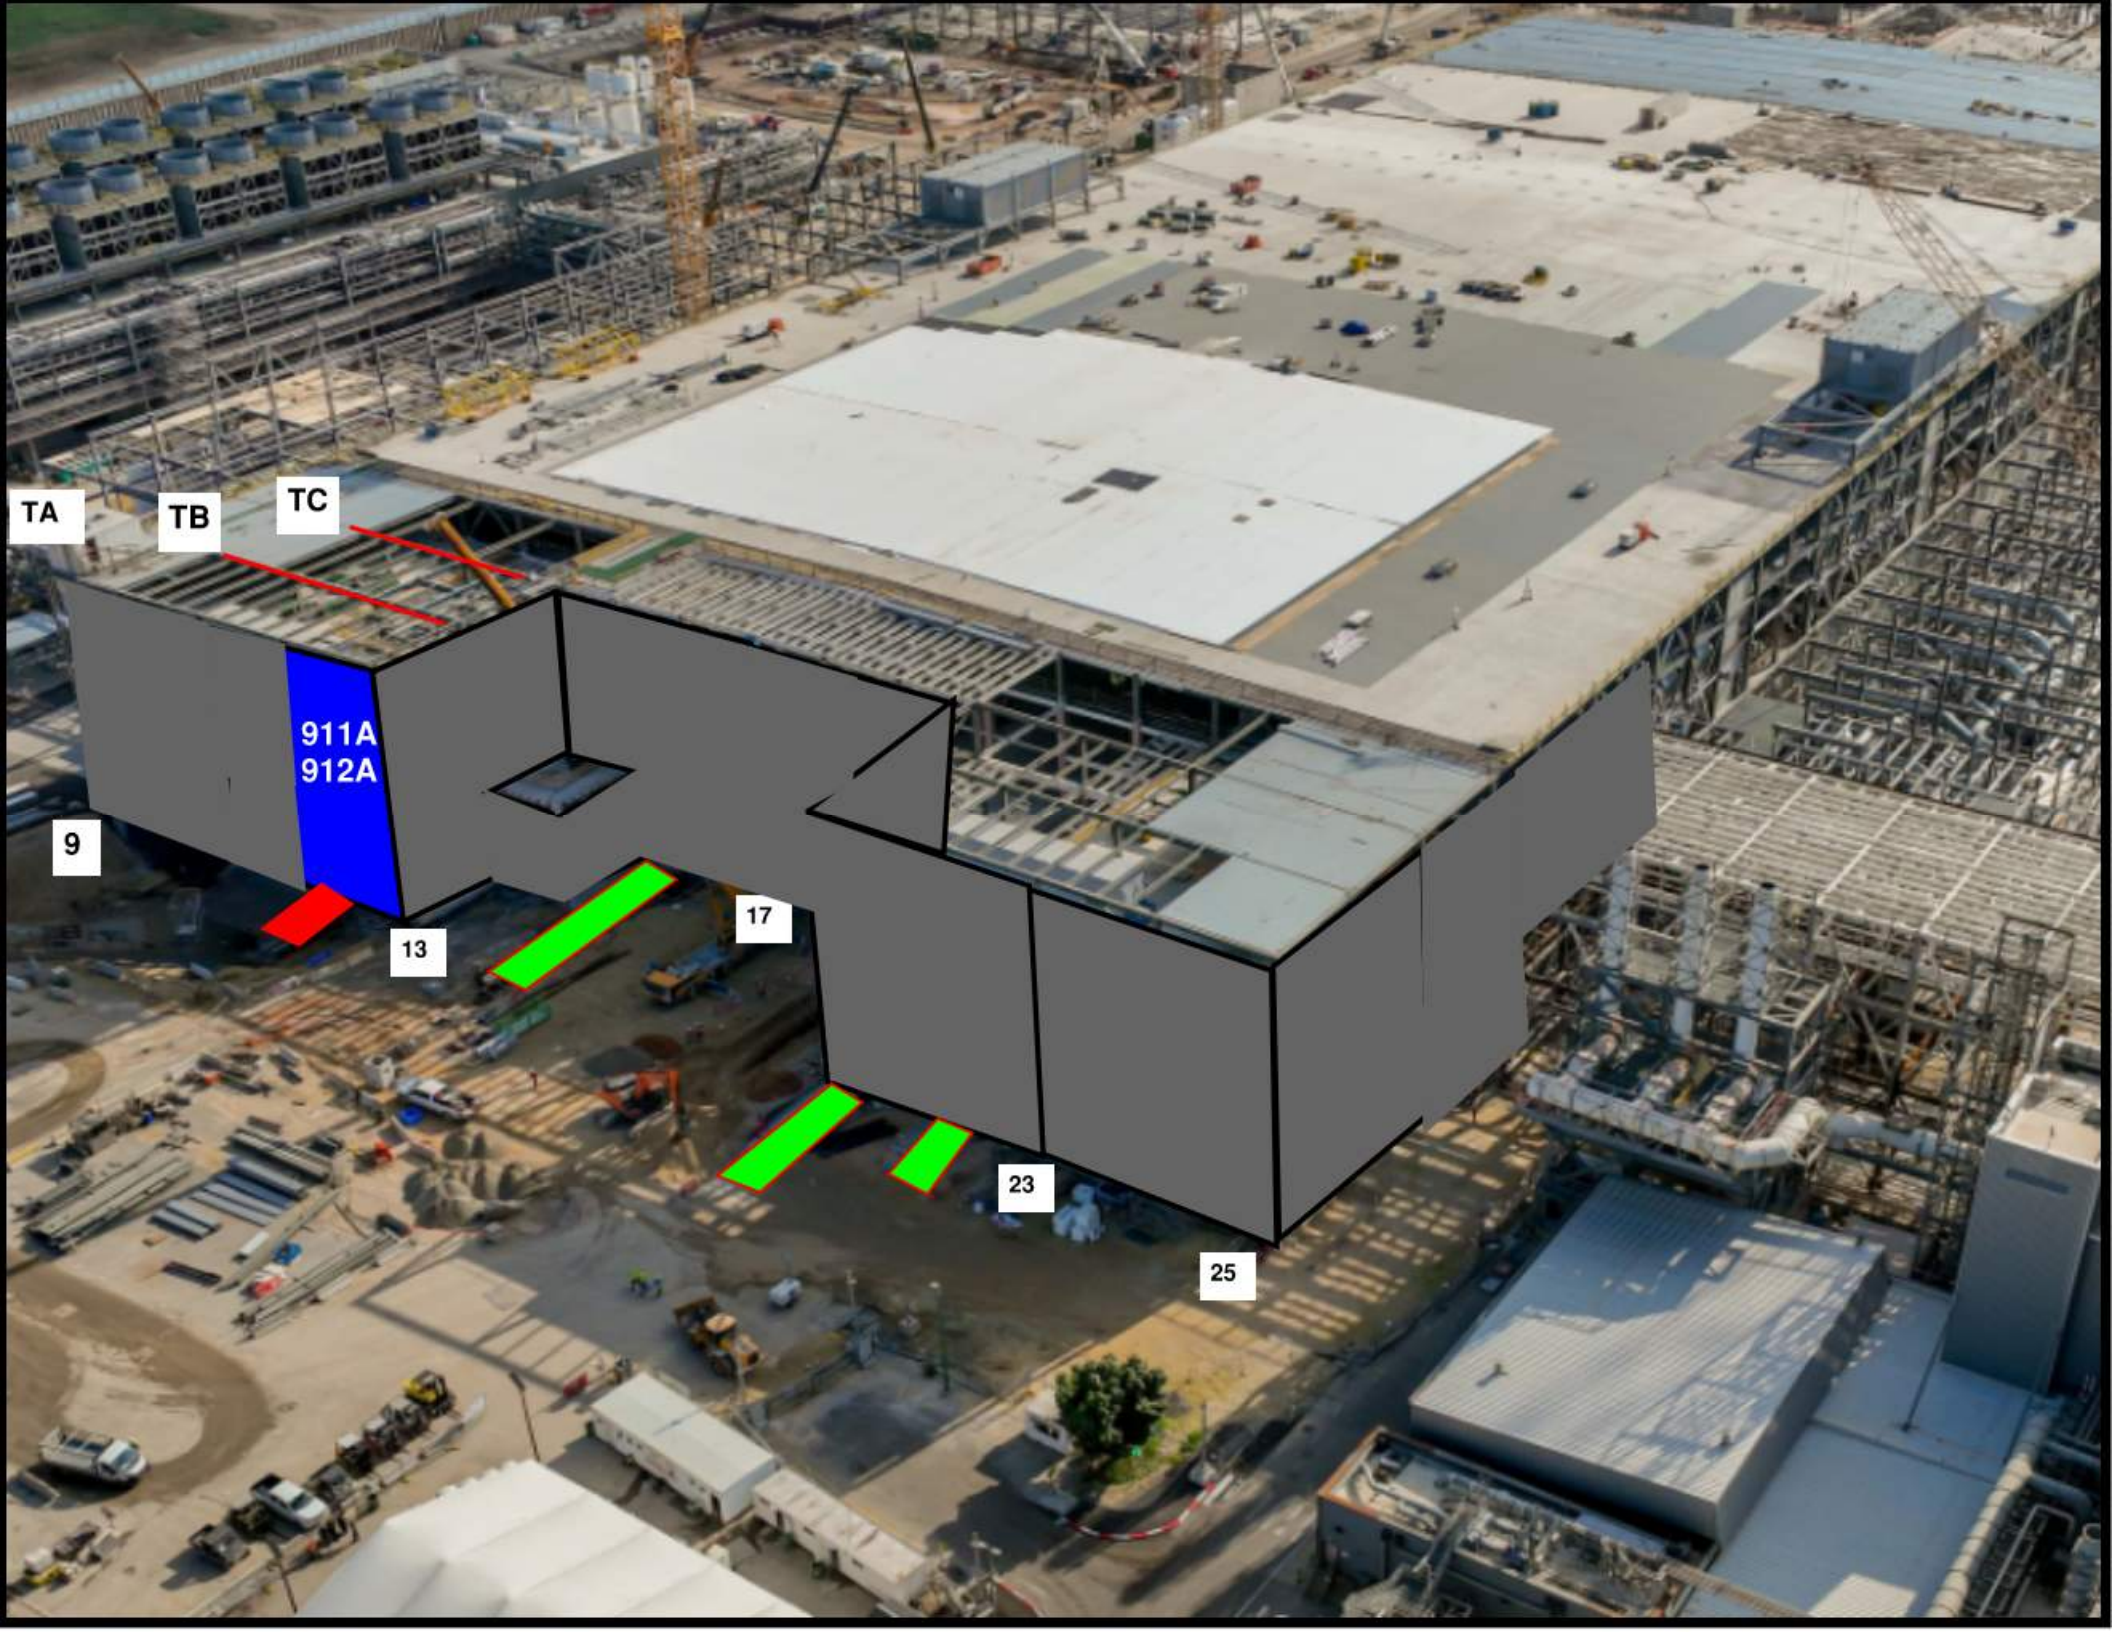

TA

TB

TC

911A  
912A

9

13

17

23


25



# PSSS.1


Utility Level  
1YA

PSSS Roof  
2SA

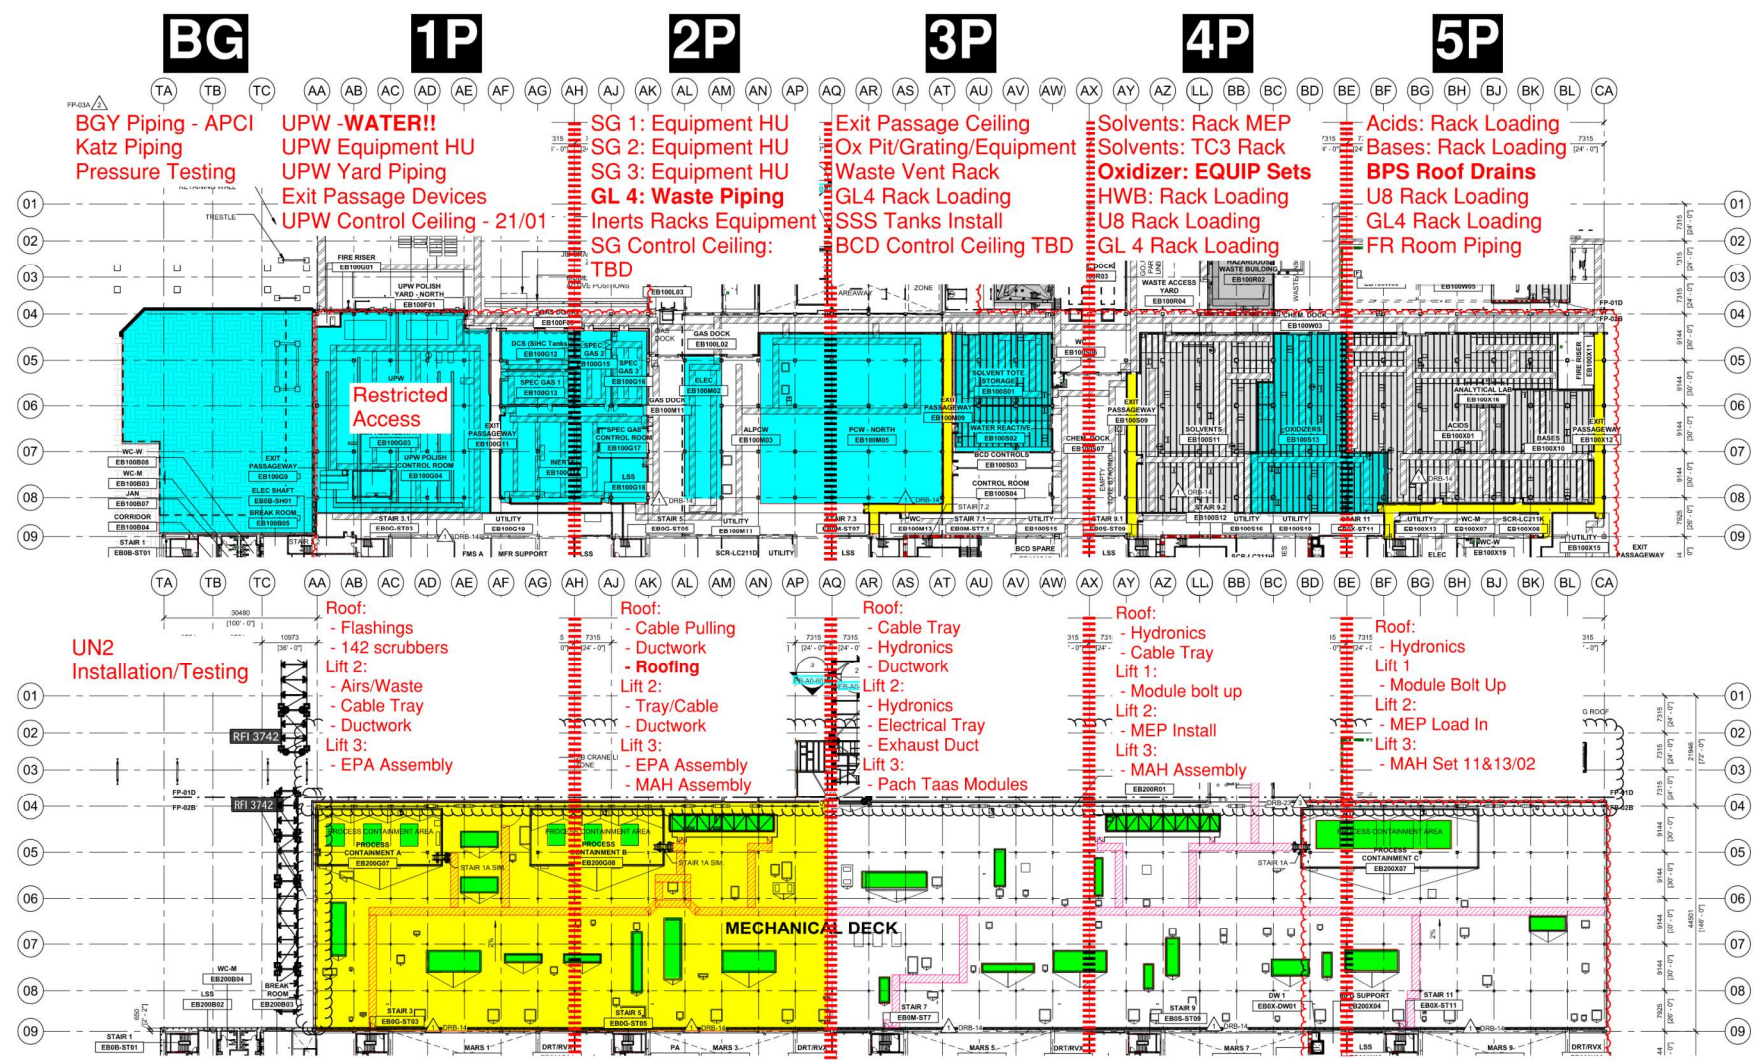


# PSSS.2


Utility Level  
1YA

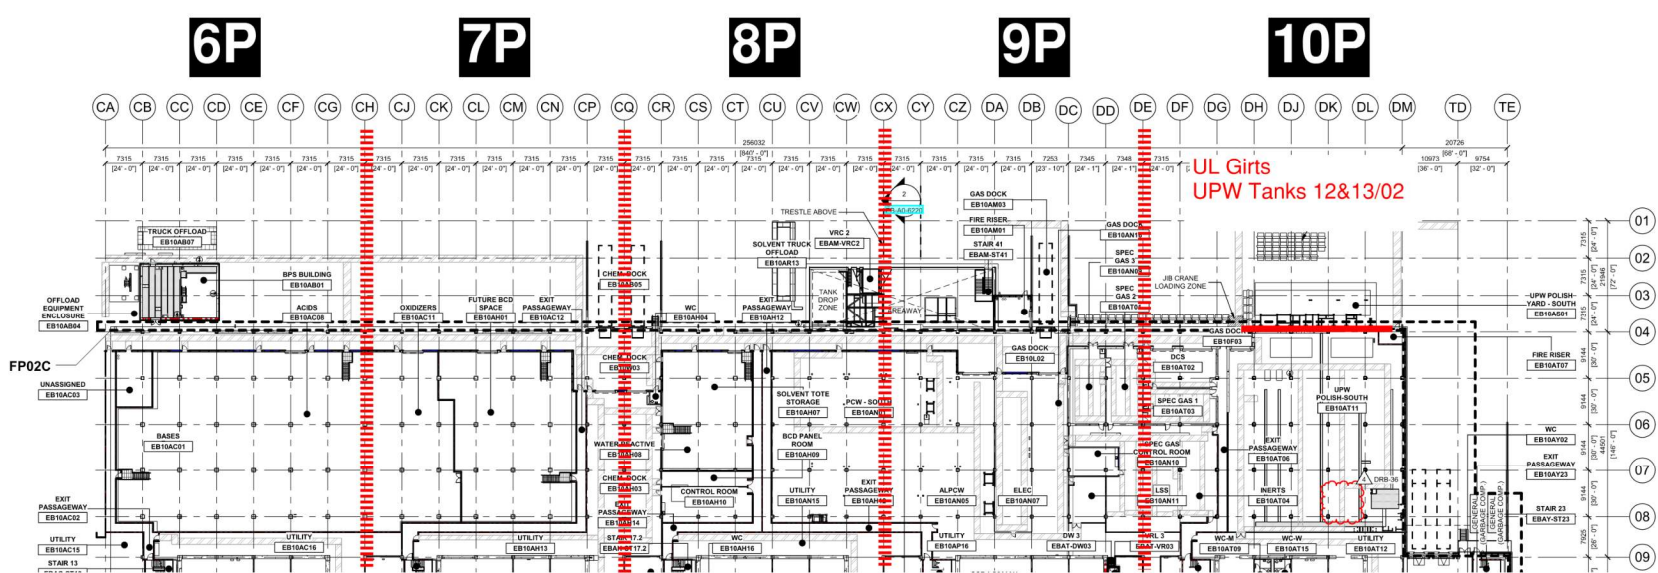


PSSS Roof  
2SA

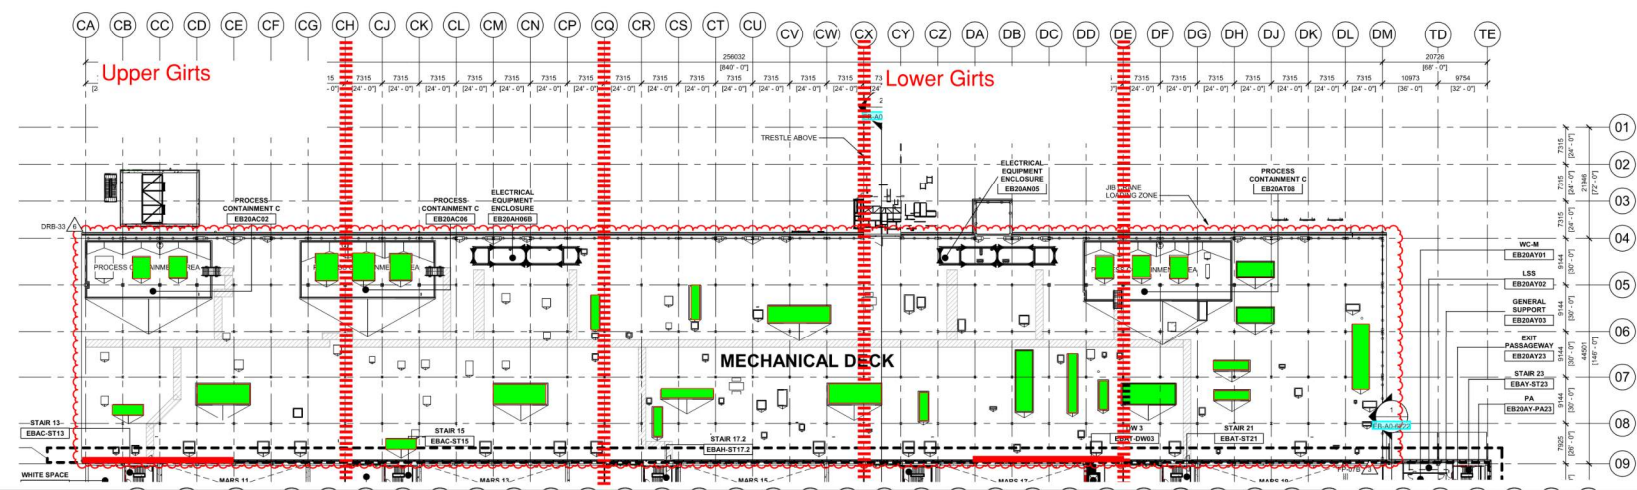

# PSSS Pressure Tests

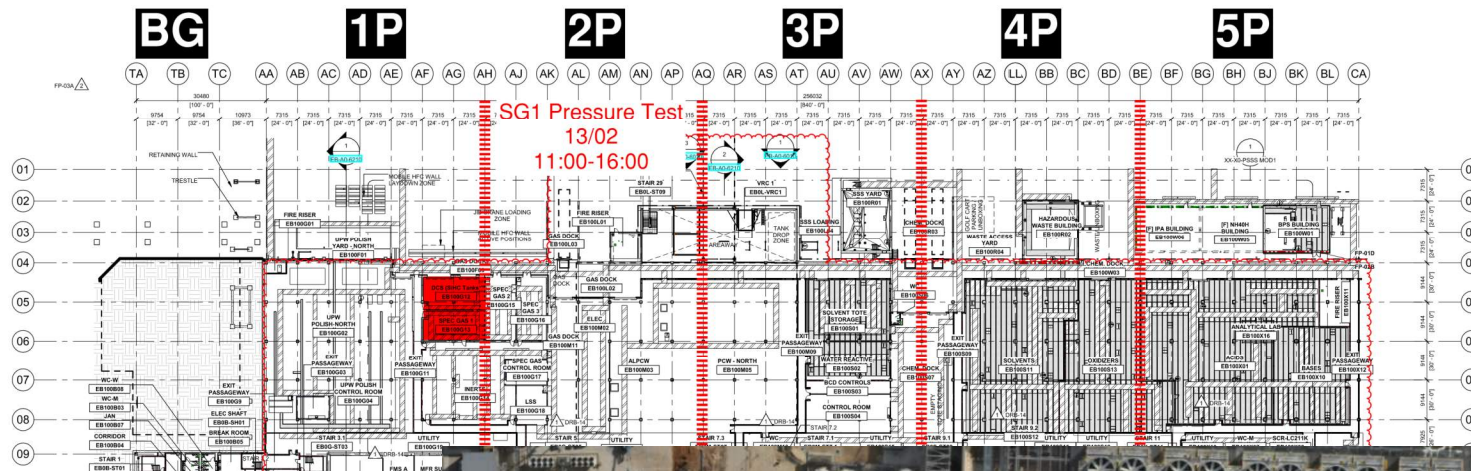

## Utility Level 1YA

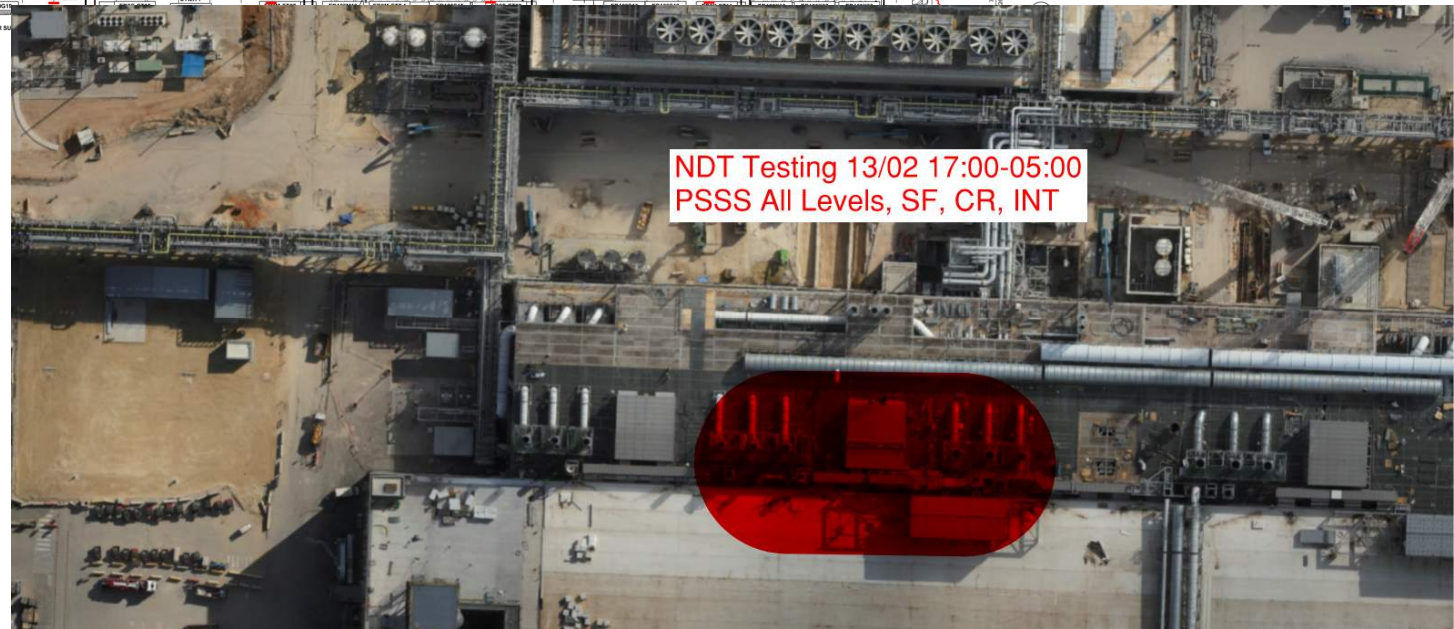

# 5P MAH Delivery 12/02





## WJG – UL


\* SIG - finished dismantling scaffold south of the link.  
\* ASD - erecting scaffold for siding team  
\* Carmel Bidud - installation of air ducts to small AH.  
\* Meptagon - connection to skids

\* Afcon - installation of permanent lighting and cable pulling from E-house to UL.  
\* Pach Taas - installation of modules in UL of west SUT.

\* Pach Taas - installation of spools and lindapters on UPN 135 and 138.  
\* Afcon - installation of permanent lighting and cable pulling to the fixtures.  
\* Meptagon - support installation next to small AH

\* Lesico - installation of NG pipes and supports.  
\* Megason - working on fire alarm piping.

\* SK - installation of plastic and cooper pipes.  
\* Megason - working on fire detection piping.  
\* Meptagon - working on I&C.

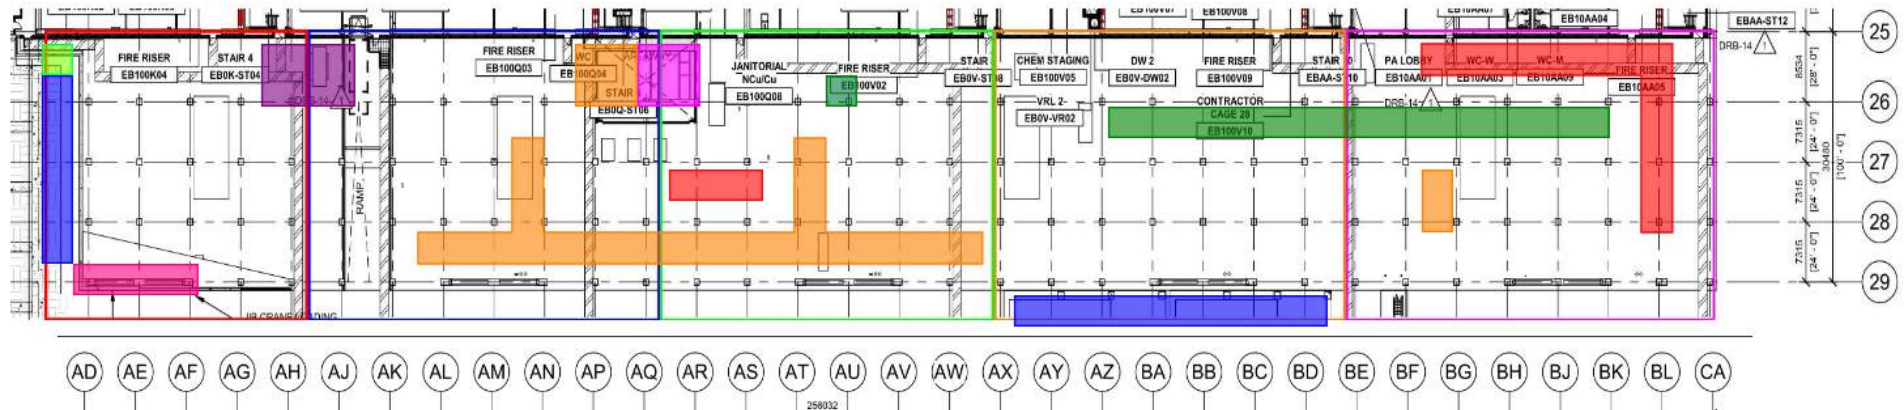

## WJG – Lift 2


Afcon - installation of electrical trays.  
 \*Carmel Bidud Scaffold - dismantle of Meptagon's scaffold.  
 \* W&W - working on Jib crane supports

\* W&W - welding stiffeners.

\* Pach Taas - installation of 1900 mm module.

\* SK - installation of CRW pipes to MAH.  
 \*Afcon - installation of cable trays and connections to MAH.

\* Pach Taas - installation of exhaust fans.  
 \* Chemo Aharon - Insulation of UPN 117.

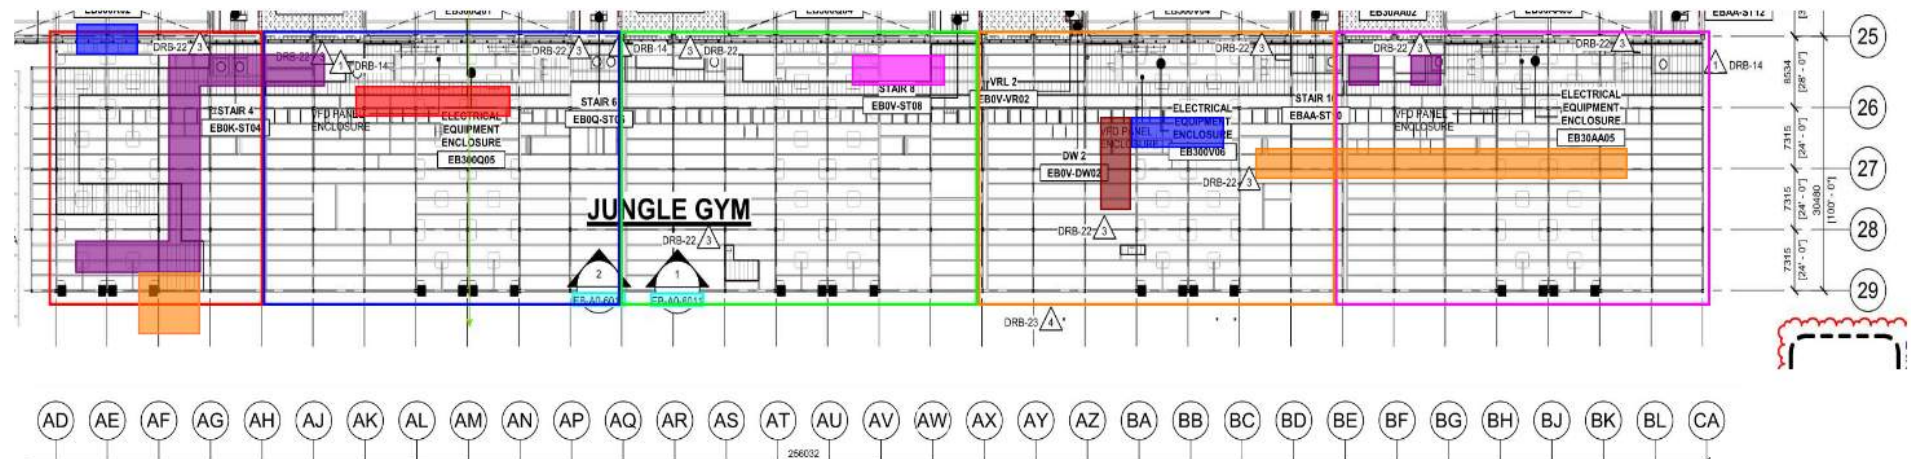

## WJG – Lift 3

|                                                                                                      |                                                                     |                                                                    |                                                                                                                                                 |                                                    |
|------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------|--------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------|
| <p>Afcon - installation of electrical trays.</p> <p>*SK - installatyon of supports for MAH pipes</p> | <p>* Chemo Aharon - installation and welding of piping to MARS.</p> | <p>* Pach Taas - lifting and installing EPA platform (on hold)</p> | <p>* SK - connection of piping to MAH.</p> <p>Sami Najami - cutting grating penetrations.</p> <p>* W&amp;W -welding supports for Jib crane.</p> | <p>Sami Najami - cutting grating penetrations.</p> |
|------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------|--------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------|



# WJG UTILITY LEVEL BUILD OUT

## Crane logistics


Crane: 220 ton  
location: AF on west  
road

Crane: 500 ton  
location: AQ on west  
road







## CUB 1

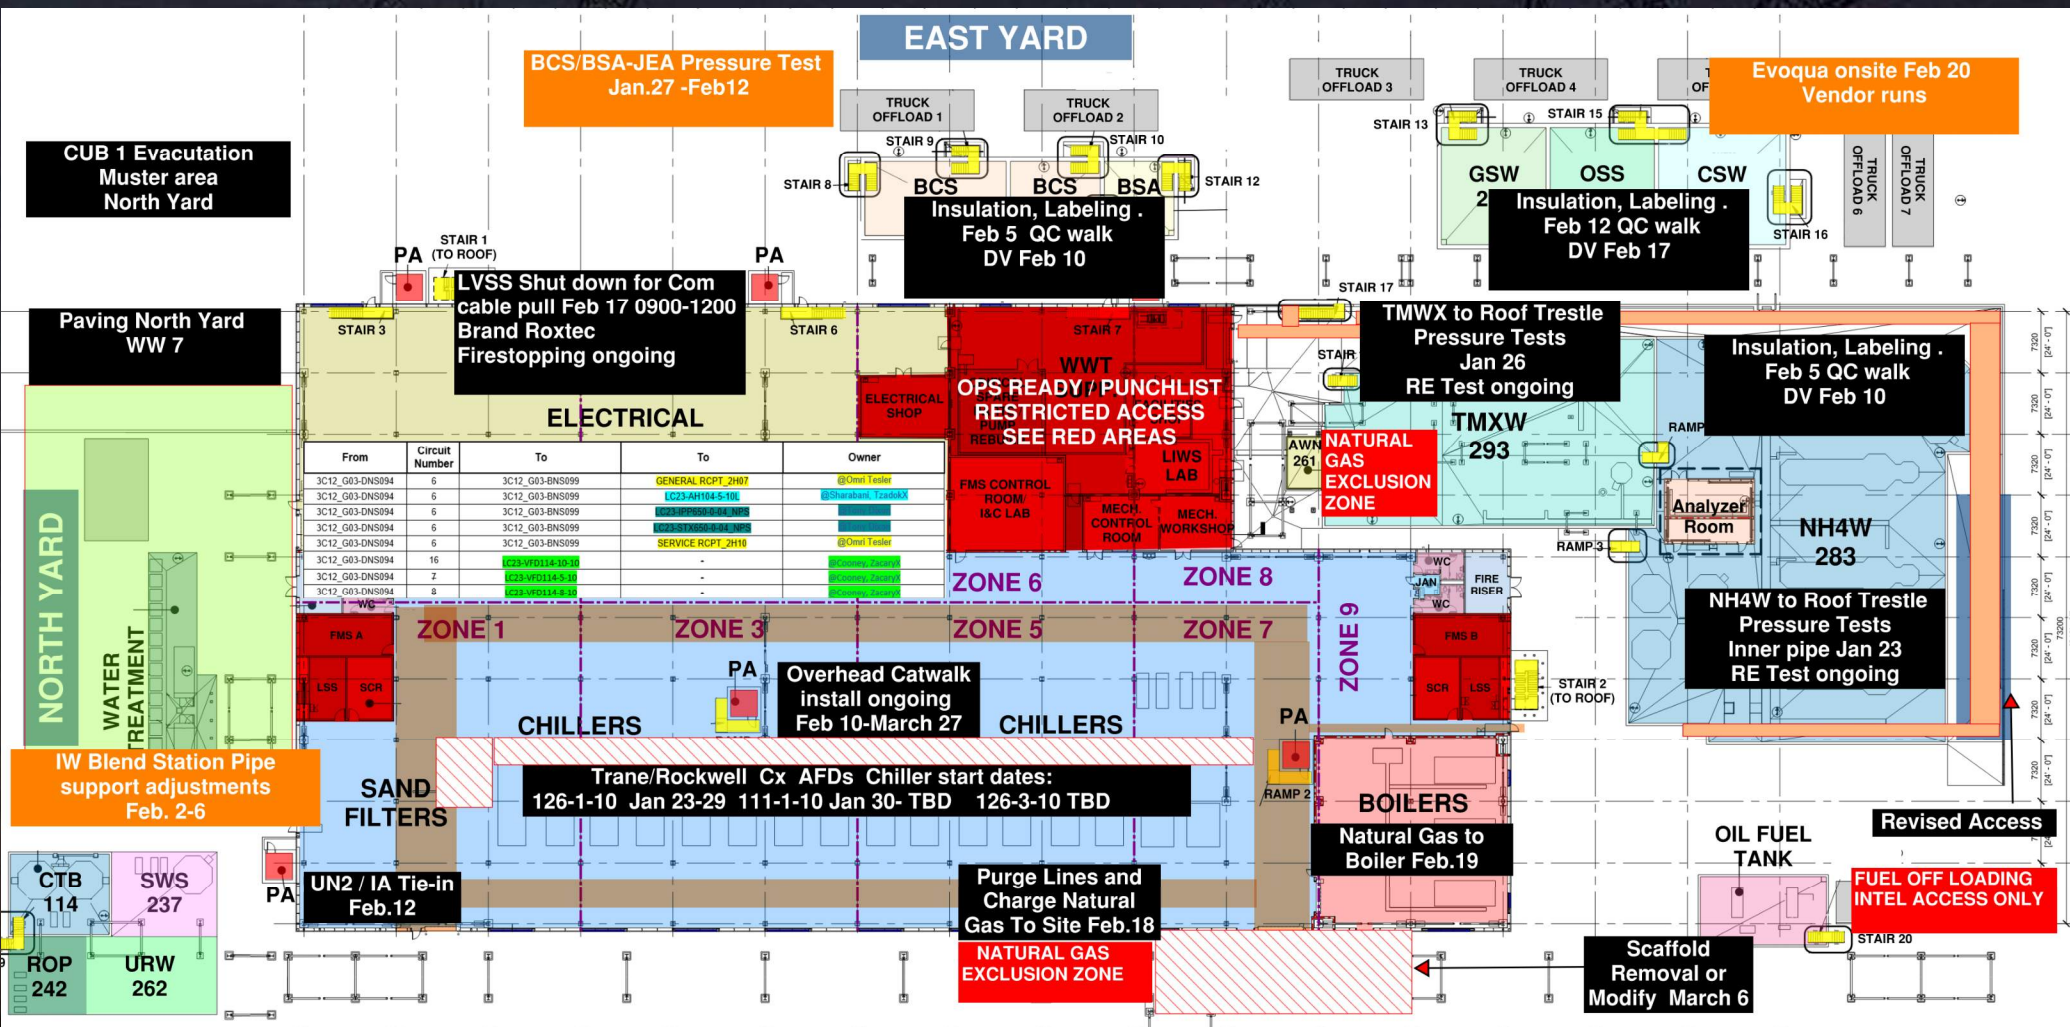


# CUB 1 Exterior Pre-Punch Status

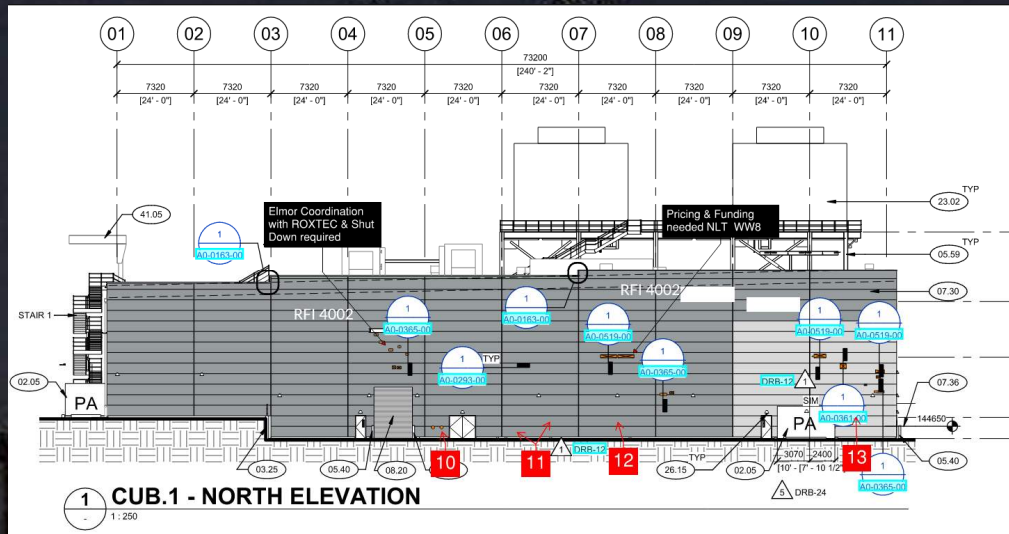

1. North Elevation ROXTEC Electrical in Coordination with Elmor WW 8
2. West Elevation pending UN2 tie in, Blank out Conditioned water to CUB 2
3. Set Final Man door complete Access Controls March 6- 20

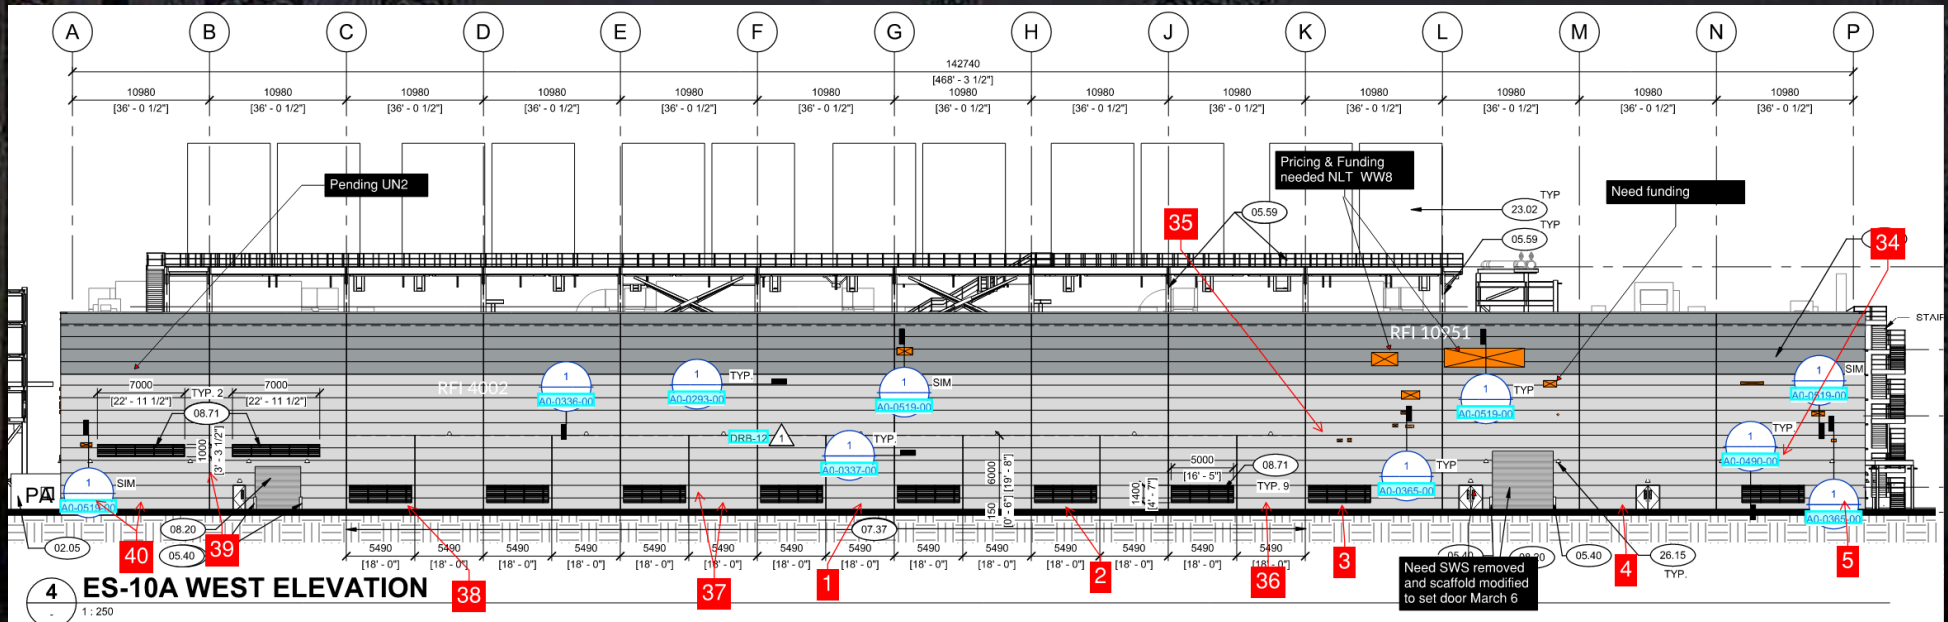


# CUB 1 – EXTERIOR/ROOF

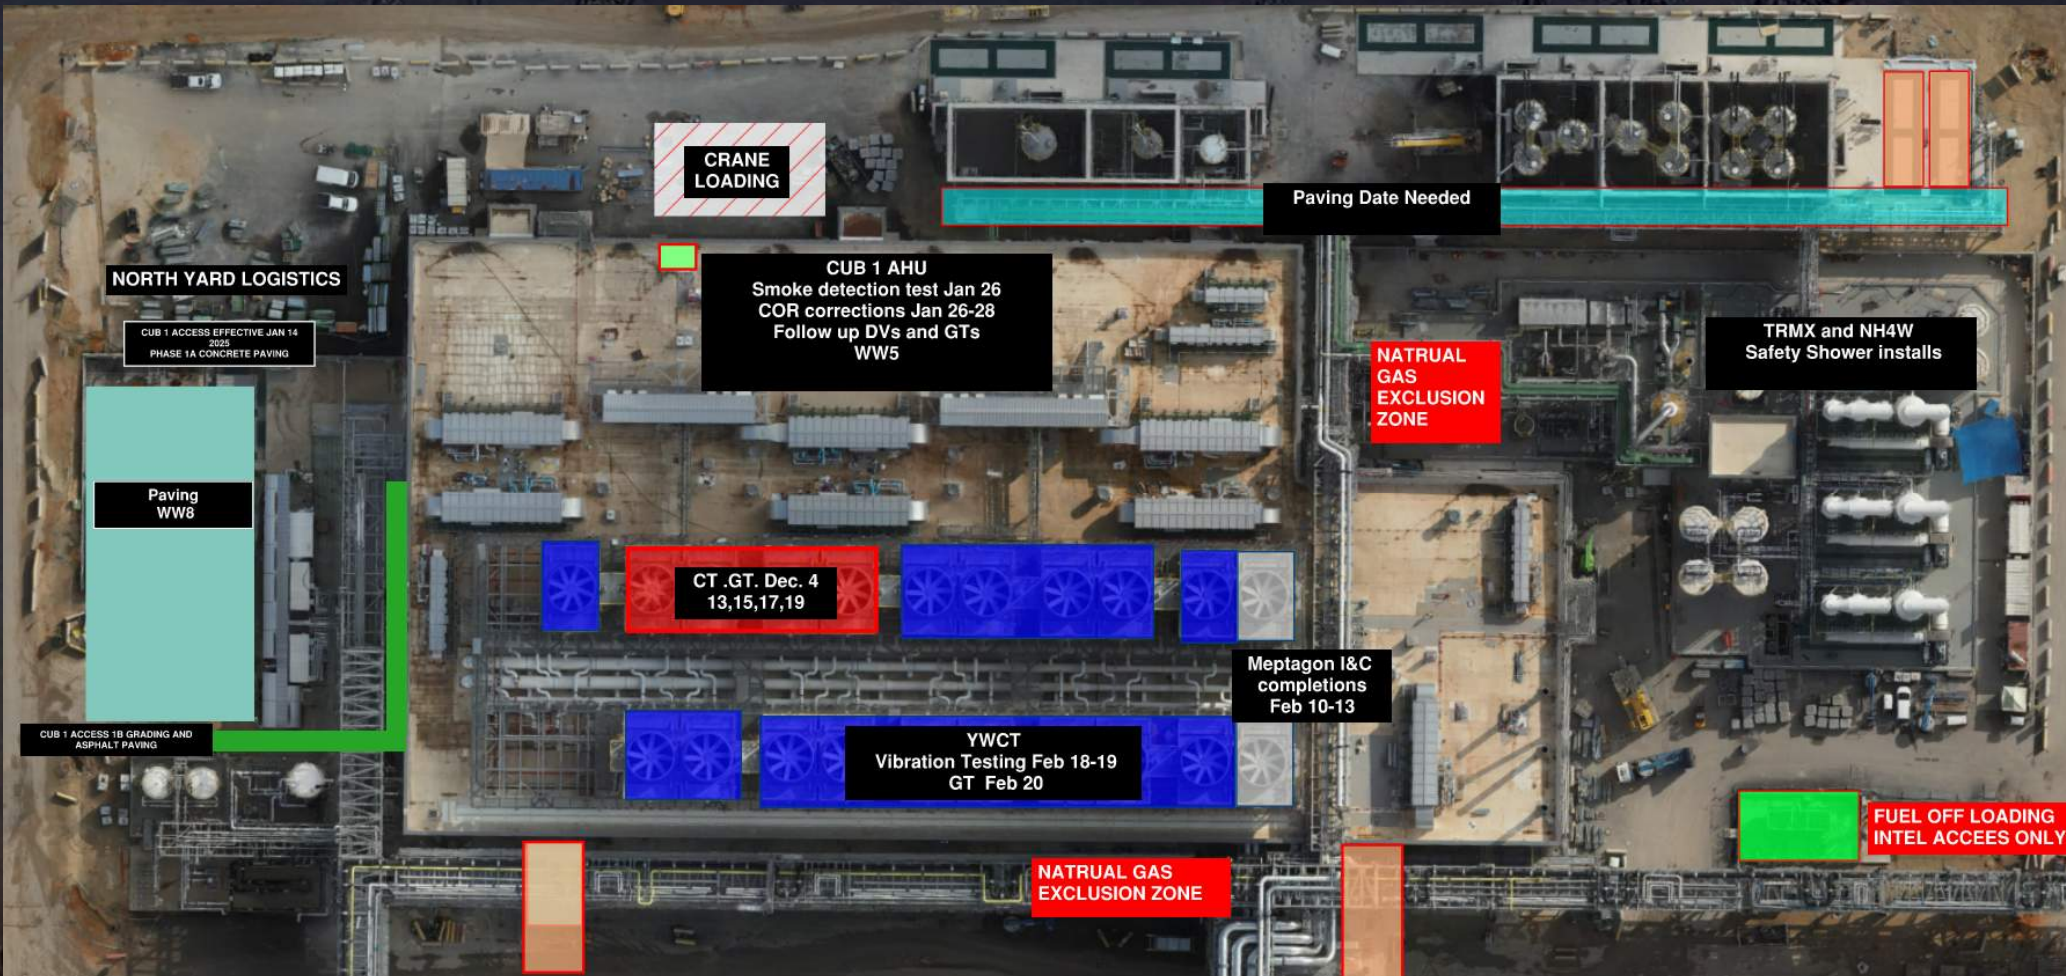


# CUB 2- Load in ,H&T, Framing and Sheetrock


## CUB 2 COORDINATION MAP

N

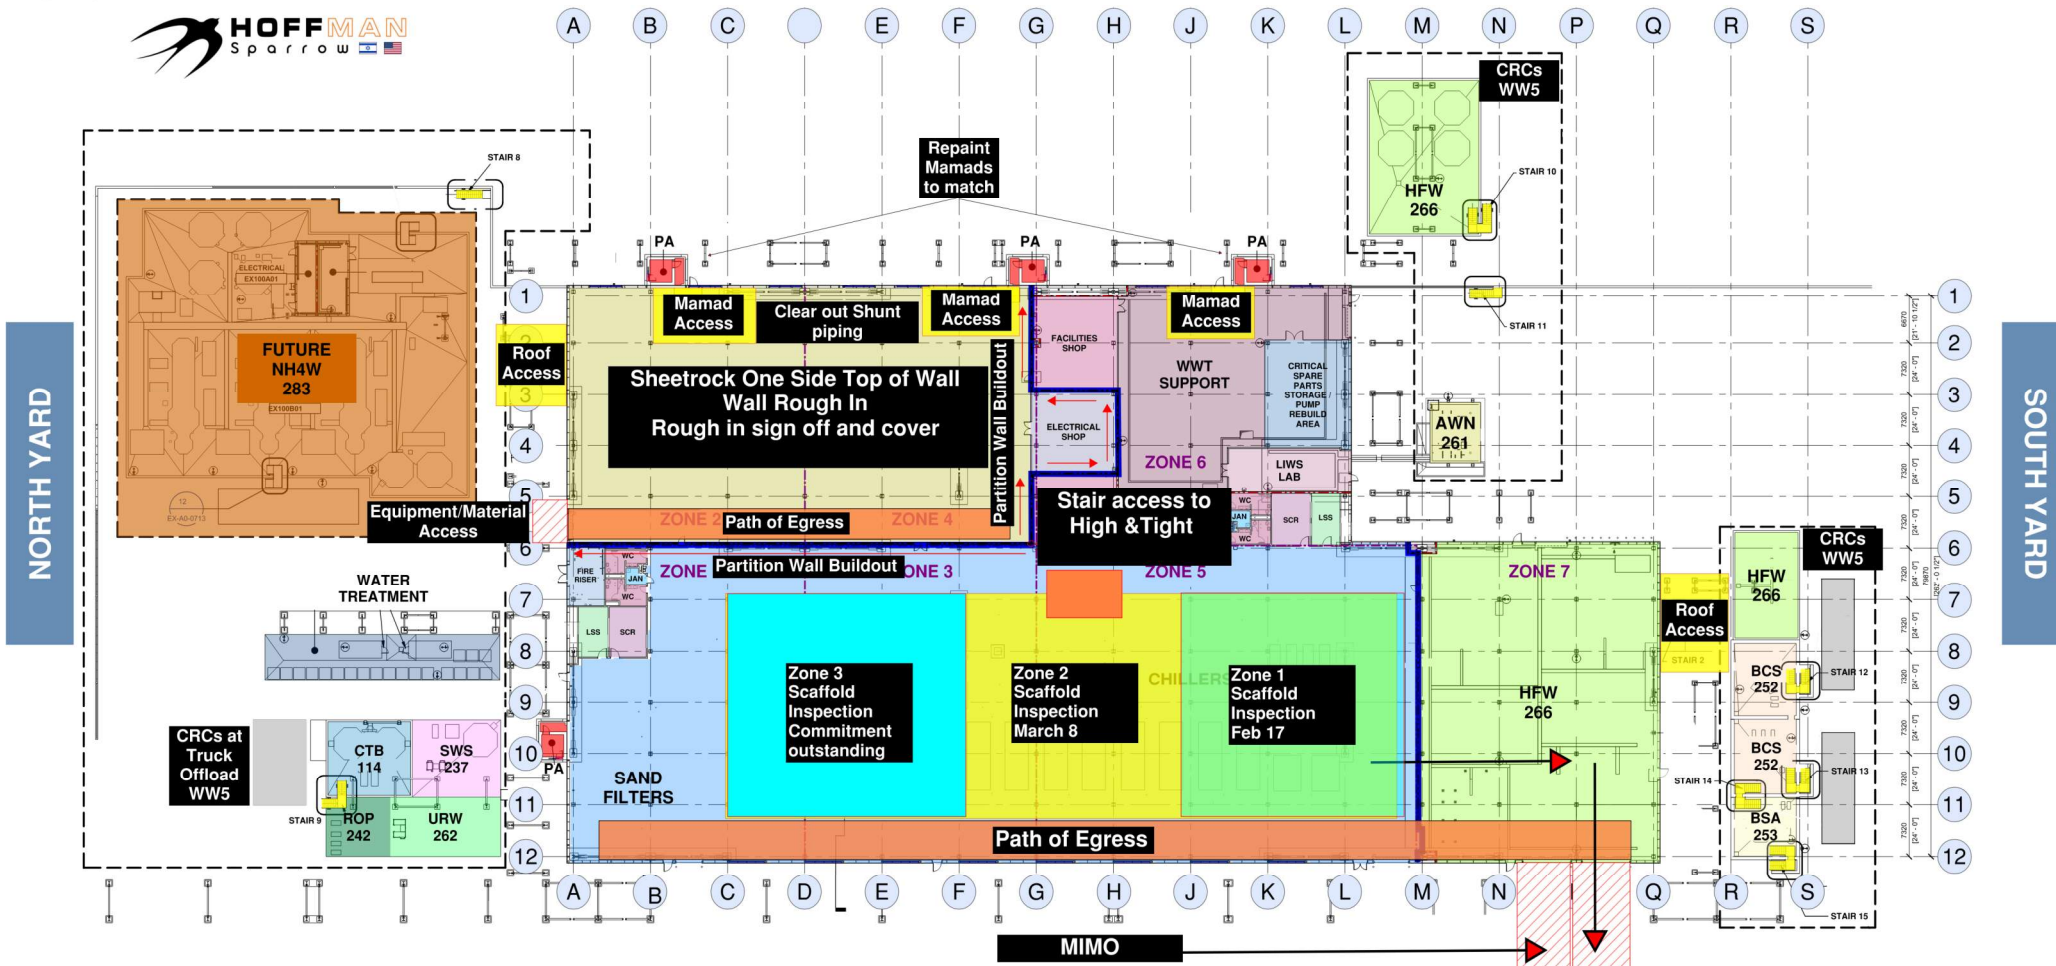


# CUB 2 – EXTERIOR/ROOF

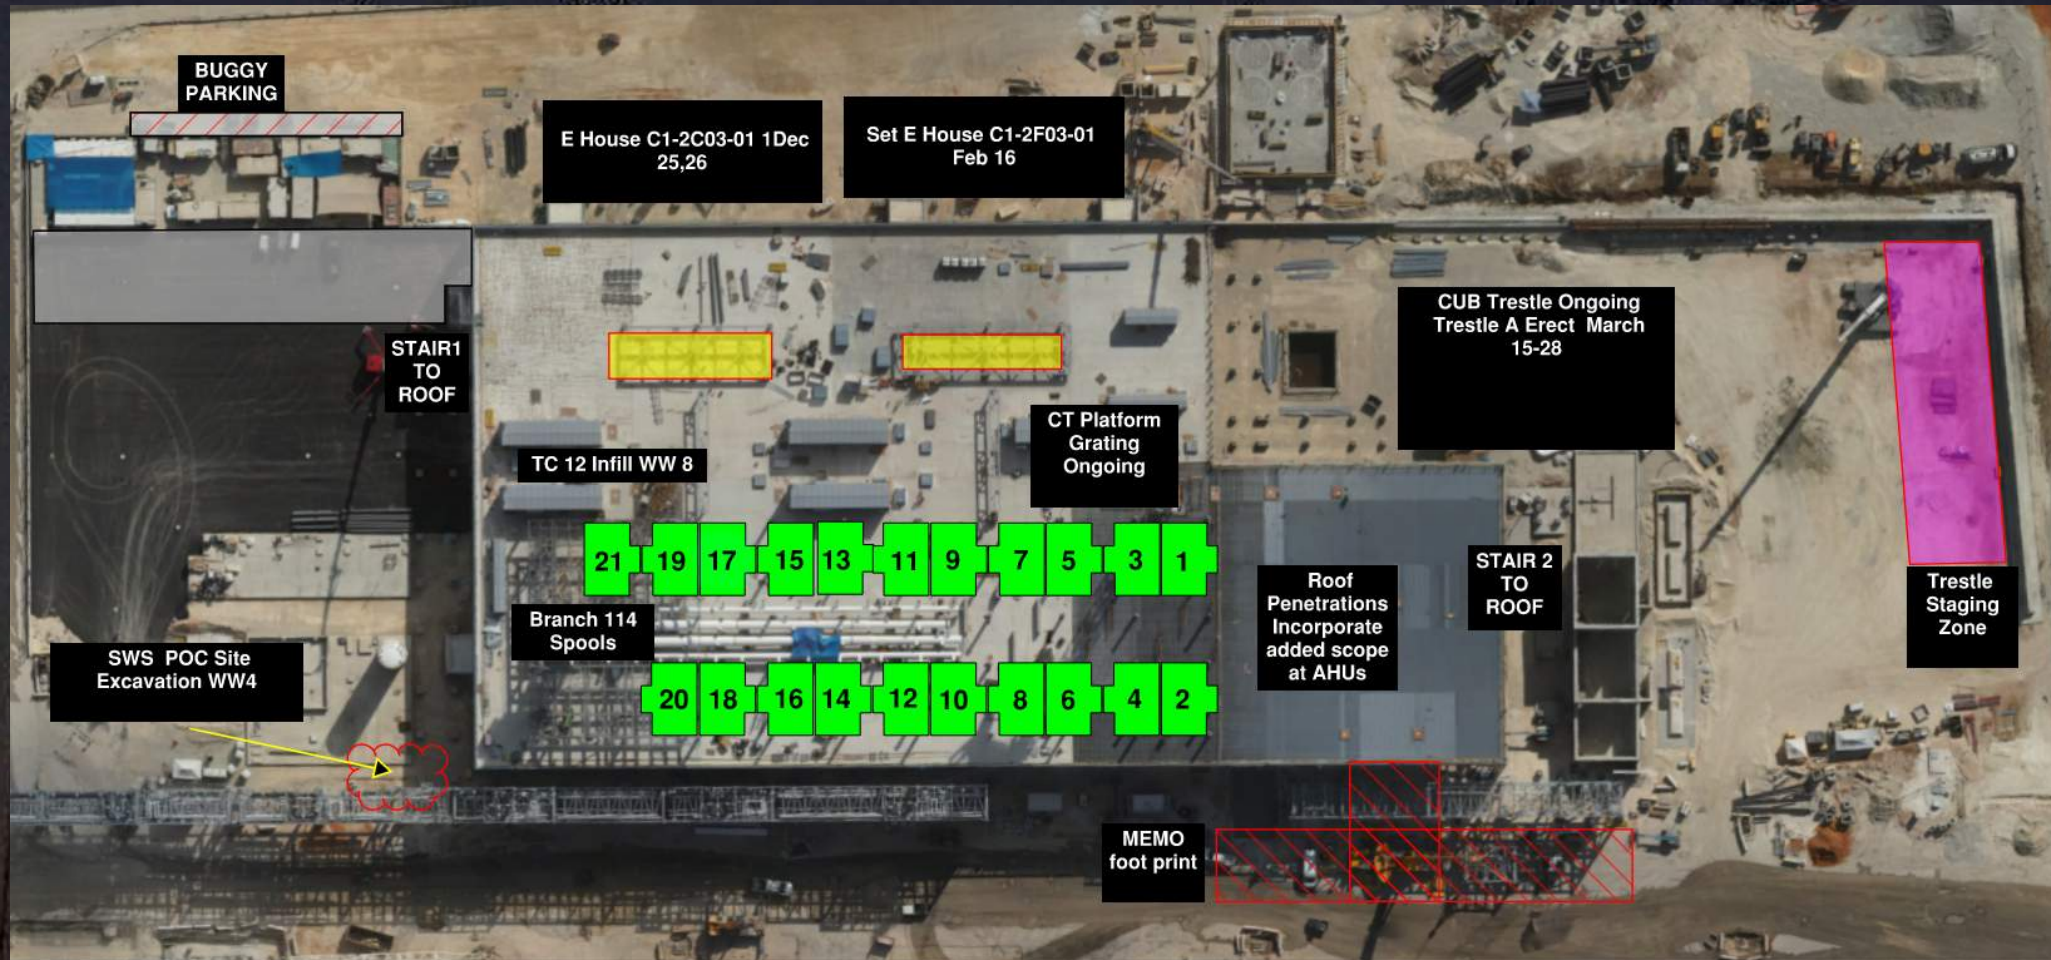



**HOFFMAN CONSTRUCTION COMPANY**

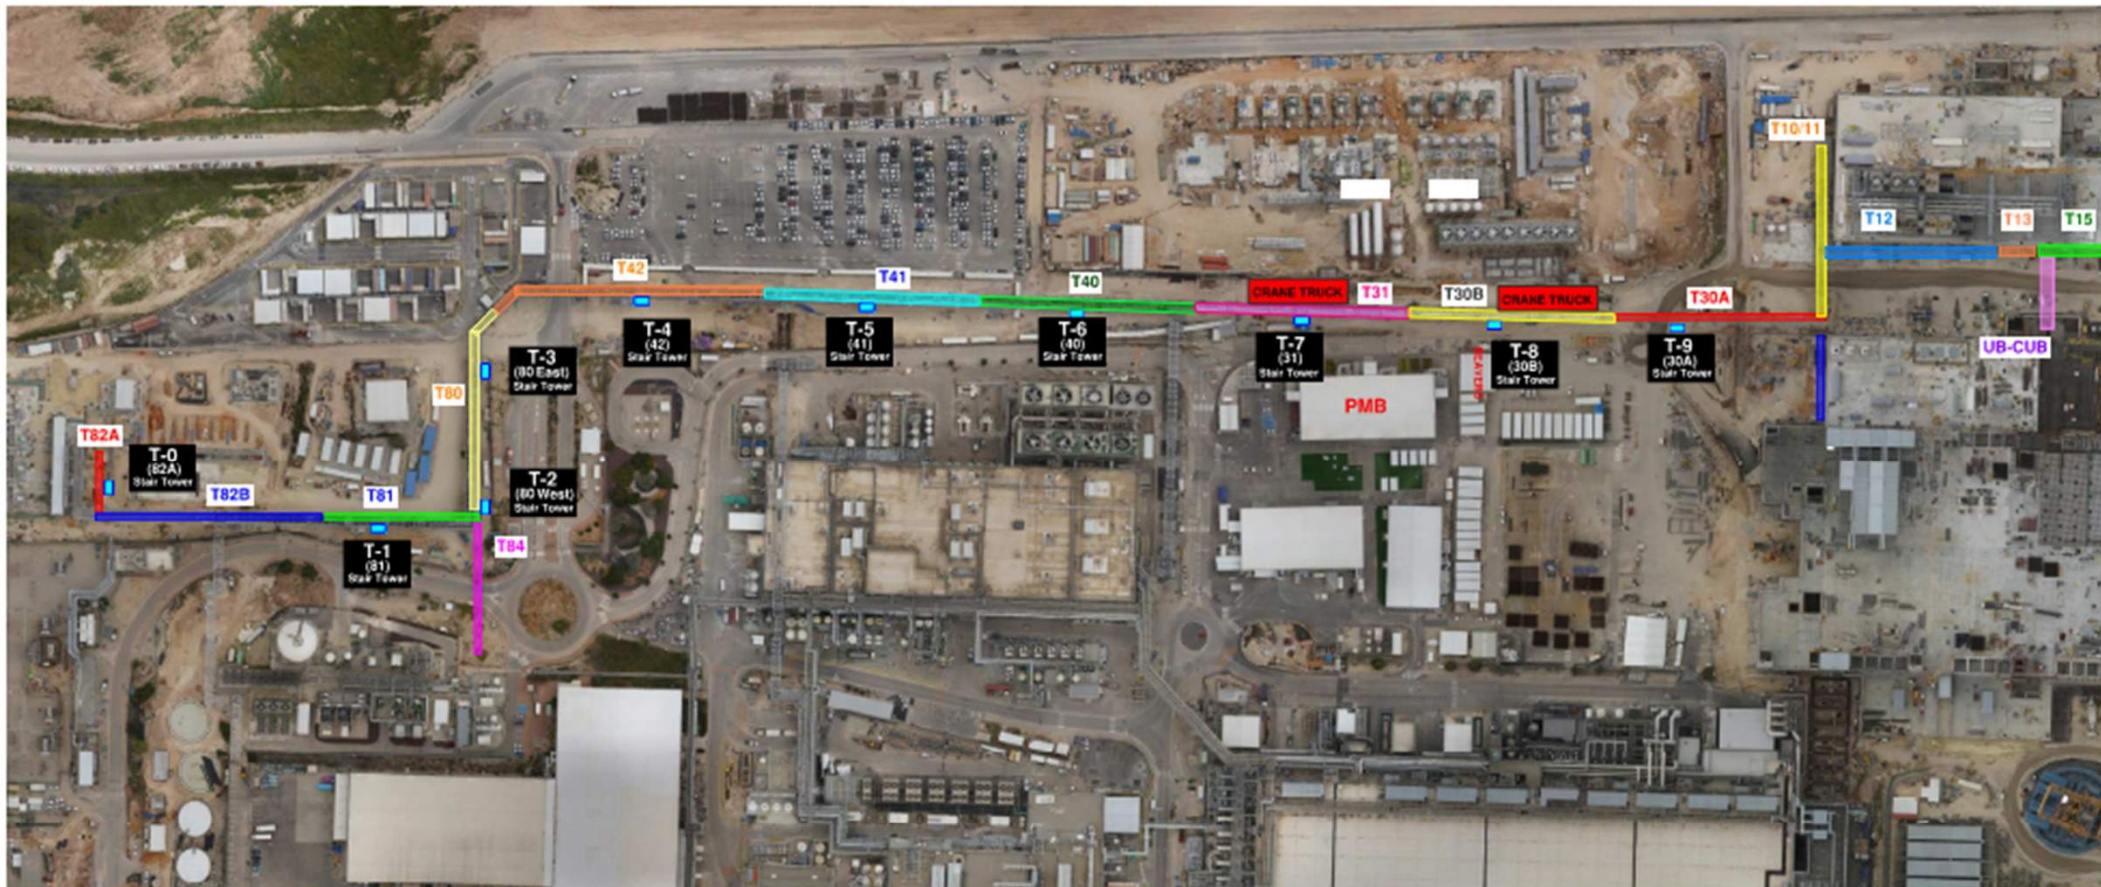

From main kiosk

Site temporary power

Legend :

— 22KV Line

— 400V Line

109 - Kiosk

● - Lift Station

Temp power shutdown  
Start: 16-Feb- 18:00 PM  
End: 16-Feb- 20:00 PM  
From AW to CC Grid line  
All the floors + JG  
SB, lights, elevator  
+TC-6

Fab 38.2

Fab 38.1

North

Cub 2

TC-12  
Done

Cub 1

TC-10

TC-8

630A  
SW

630A  
NW

630A  
NW

630A  
SE

630A  
NE

630A  
SE

630A  
NE


TC-9

TC-7

TC-5

To 115

From main

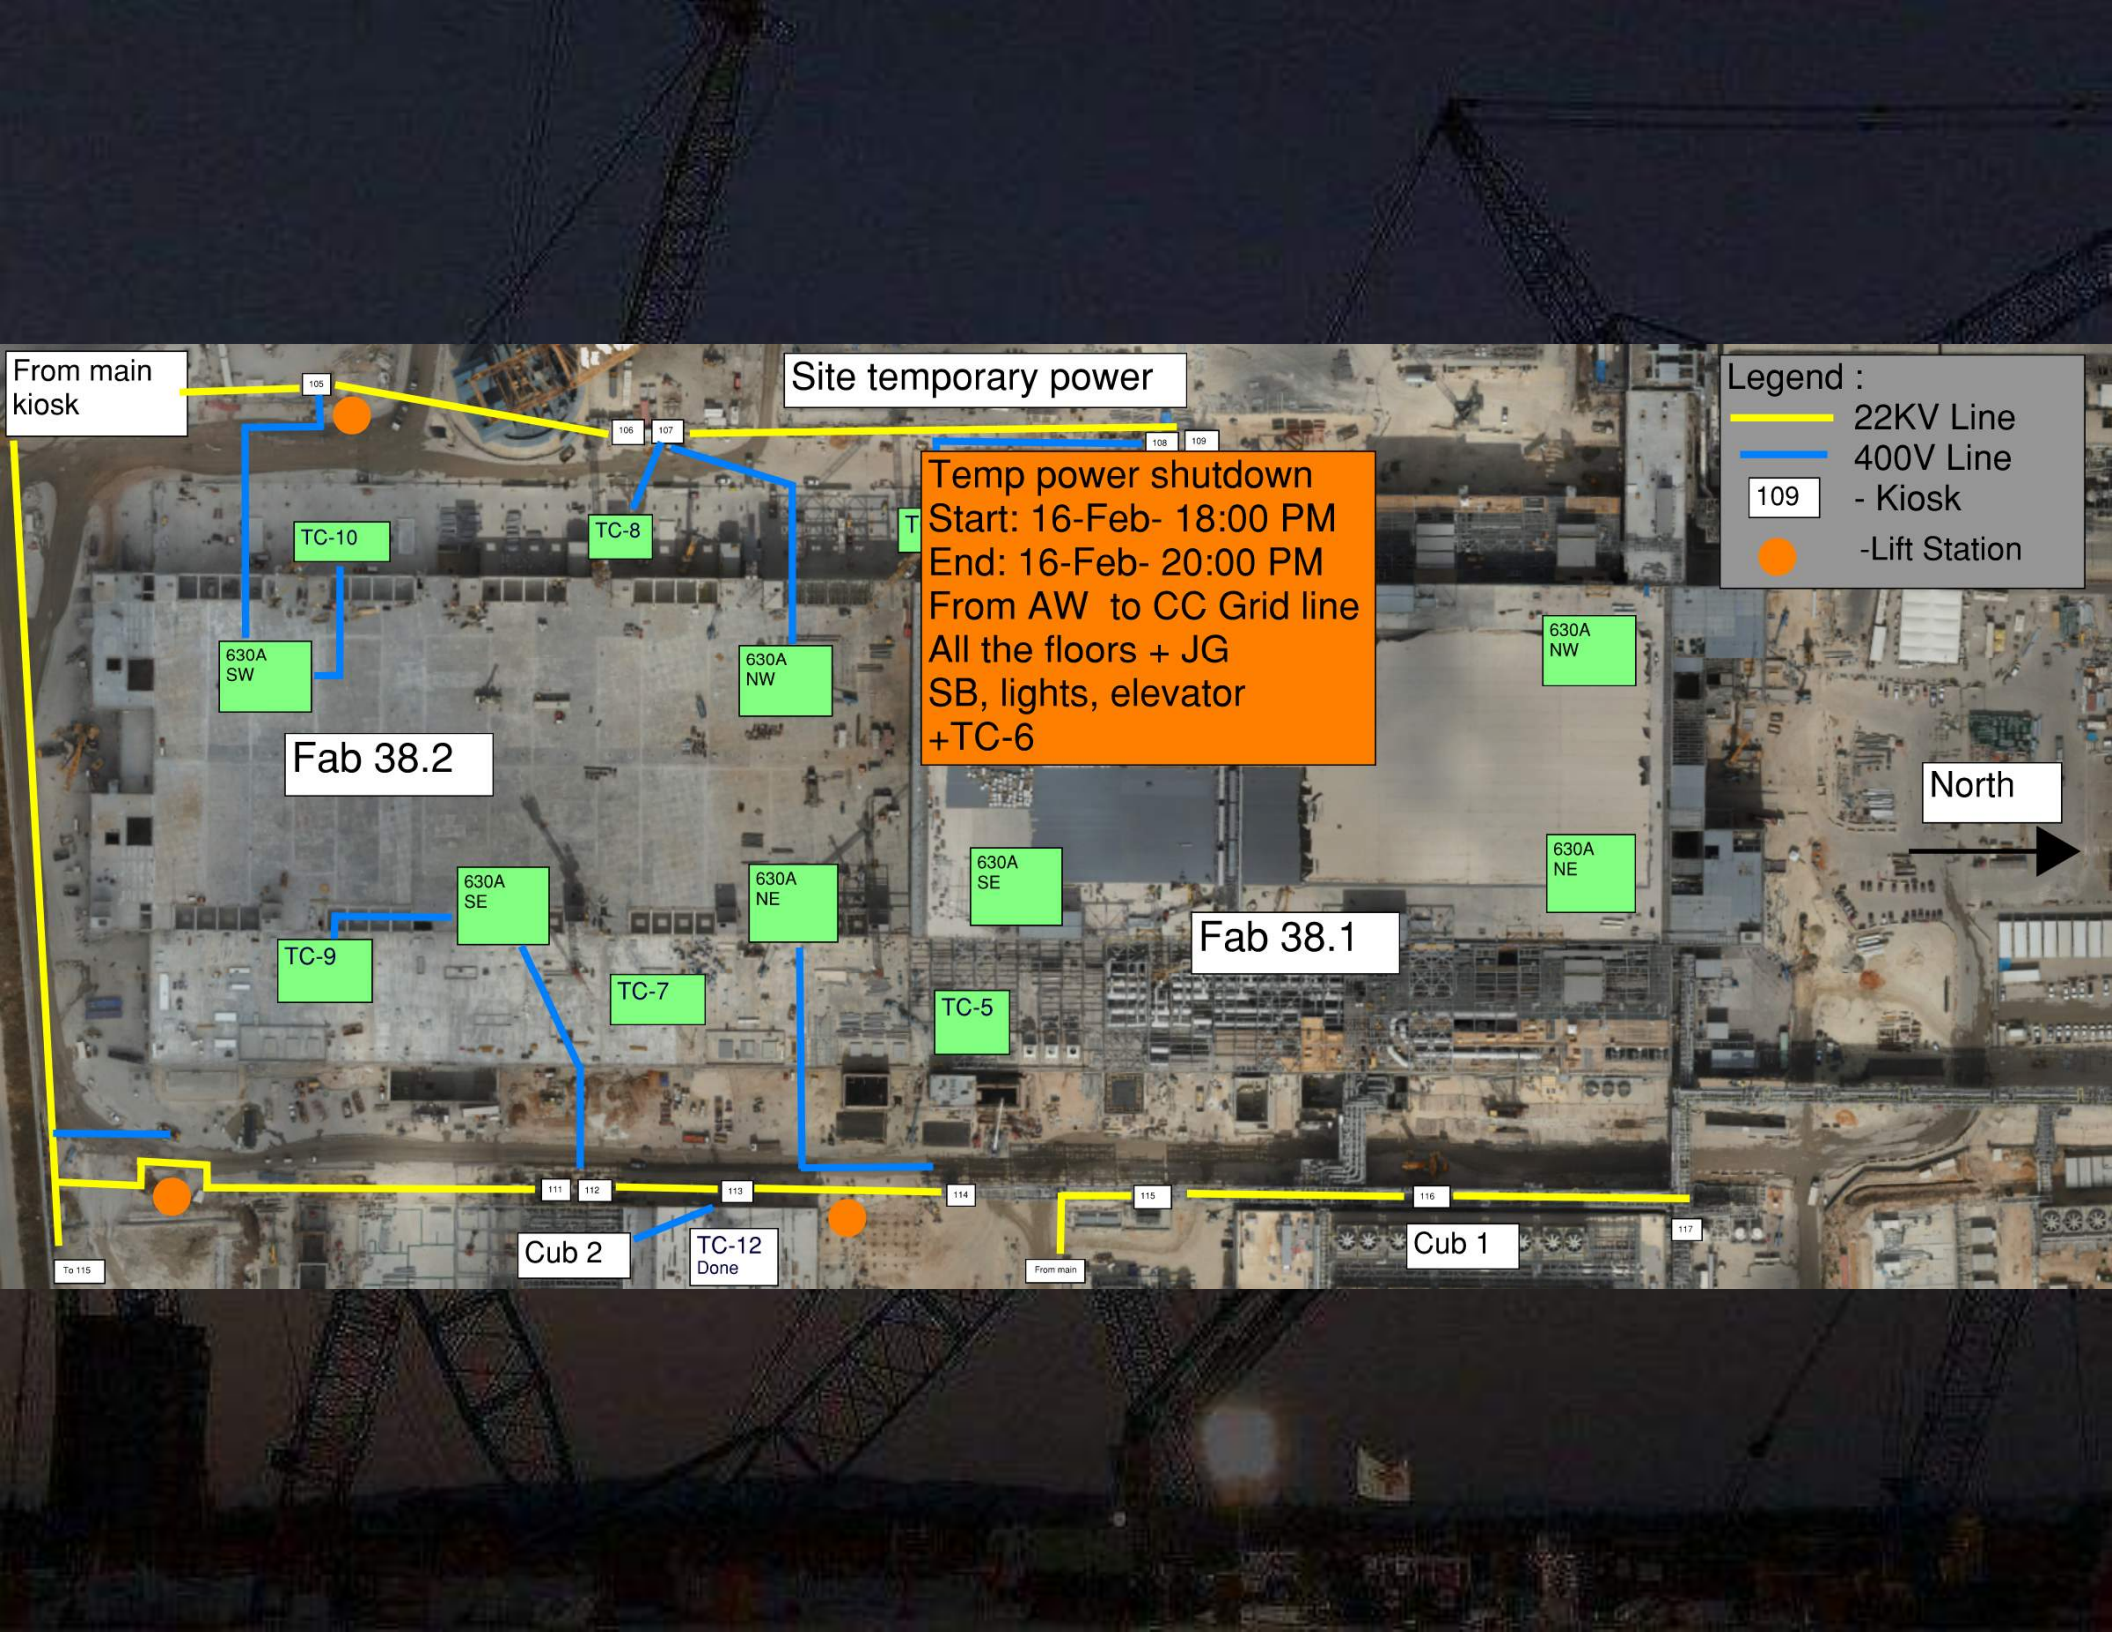




# Daily Coordination Meeting

Site Logistics

North

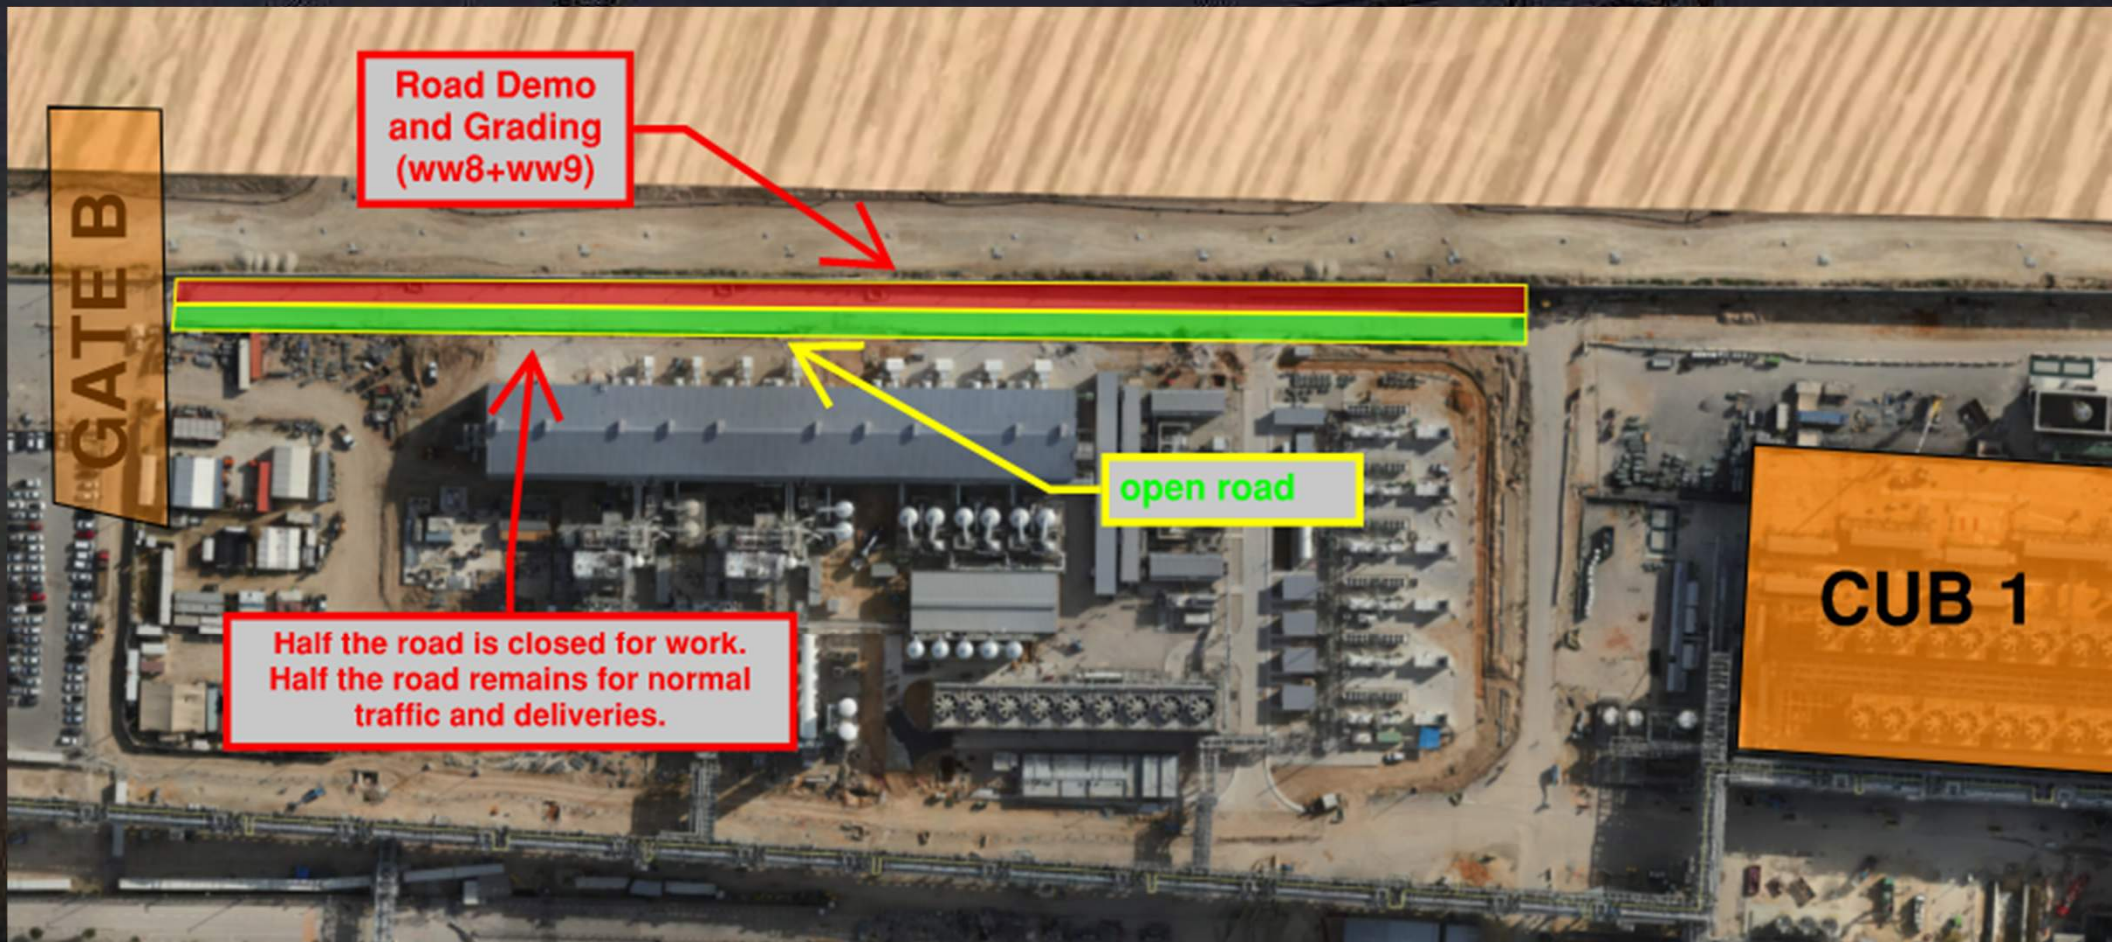



HOFFMAN CONSTRUCTION COMPANY



# Daily Coordination Meeting


Site Logistics  
North





# Daily Coordination Meeting

Site Logistics  
South

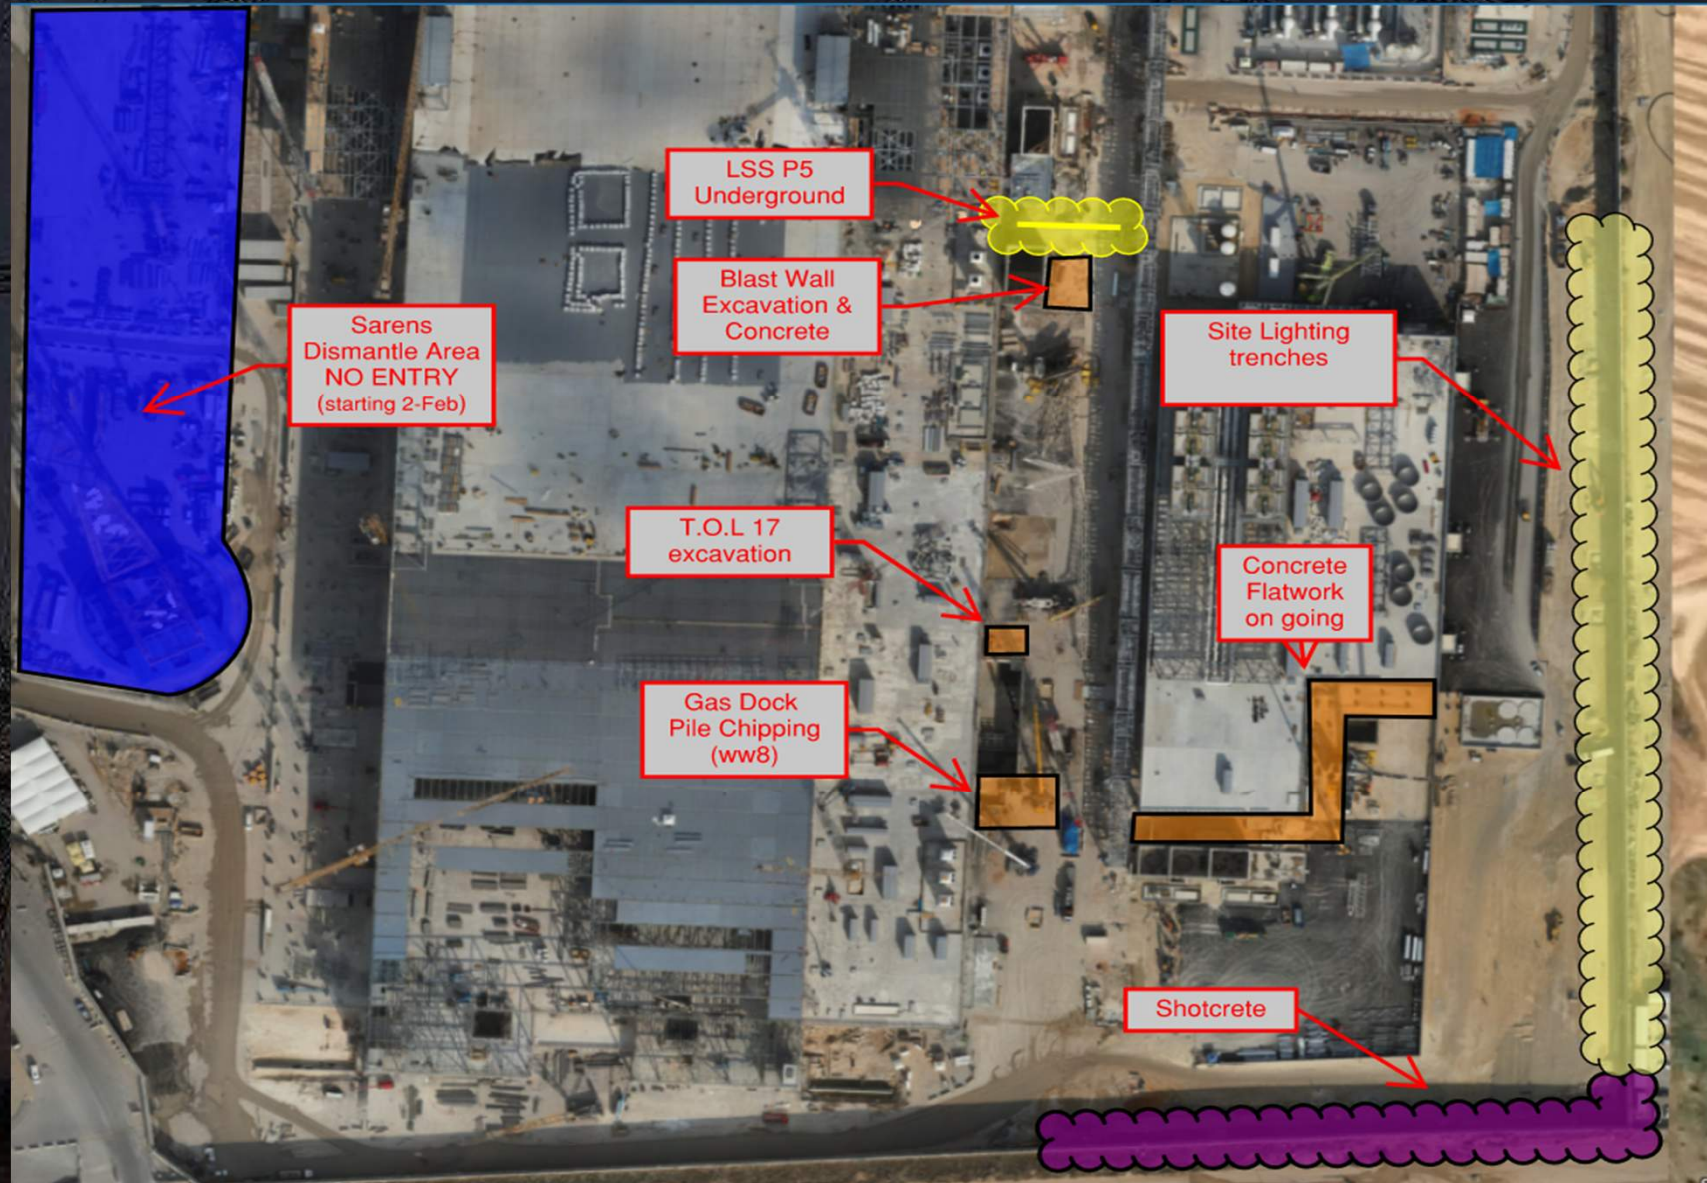

# Deviation from the Plan

- Do your crews know the process that you expect them to follow if they discover that either a plan isn't working or that changes need to be made to the plan?
- What are your expectations from your team leaders when they make changes to plans that you have approved?
- Is there a process for that plan to be rechecked before they continue?
- Do your crews understand the hold points for their work? Have you identified hold points?
- If you tell your crews to follow the plan, but don't give them direction on what they need to do when that plan isn't working, they will simply deviate and you won't know about it until there is a problem.
- Simply telling them to update the PTP may not be appropriate for all changes or all operations. Do you think they understand when that is appropriate and when it isn't?

# HCC/EHS Weekend Work- 14.02.2025

## White Board Meeting in Beavers at 06:30

### Superintendents

Jeff Bowen – 052-3787746  
Gad Yaacov - 052-3784838  
Pini Kahlon - 052-7343004  
Brian Smith - 052-2181361  
Asher Amar - 052-8801316  
David Jollands - 052-3961675

### CSA CM

Nikol – Loboda - 052-3124965  
Ben Tauar - 052-3173040  
David McBride - 052-5379828  
Shir A  
Hadar S

### MEP

### Cx

### Cranes

### Safety

- Safety Foreman -Waseem Alhozil- 052-358-4978 Waseem-Alhozil@Hoffmancorp.com
- Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

# Subcontractor Weekend Work- 14.02.2025

## FAB

### Utility level/ SUT

## Subfab

- Pach Taas
  - Wall Penetration
  - Tomer: 0507670585
  - Ofik: 0507838486
- Afcon E
  - All over SF
  - Raz: 0546838626
- MEGASON
  - MOD 2,LSS Rooms
  - Israel: 0526869393
- SELA
  - 2E MARS
  - Yuvel: 0502649246
- Afcon-Telecom
  - 5E,5W
  - Anish: 0559537332
- Elram
  - TTNE
  - Eliezer: 0544236899
- Lesico
  - 17 Line
  - Gabriel 0549892929

## Clean Room

- Talad – 25 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Marcelo 0523540242, Super Elad 0546654473)
- Chemo – 35 GUYS INT -TNTNE/W Supports, 5RA Racks, 3W Skids (EHS lotem 0544477112, Supervisor Winai – 0528090588 )
- Protocol 2 guys (Roni 0542496363, Elisha 0587963704)
- Talent solution 8 guys CR 2E 1E/W maintenance cleaning (EHS Yosiel 0508777611, Super Super Yosi 0526557130)
- W&W 20 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- Sig – 17 GUYS MOD2- 17 Line, MOD1 2E-2W scaffold (EHS Beni 0506232032, Super Shmulik 0549205966)
- Rolling Plains – 23 guys 7W, CA to CG17 MOD2- Grid 17 4DA (Super Codrin 0546594273, EHS Ovidiu 0546993648)

# Subcontractor Weekend Work- 14.02.2025

## PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P
  - Foreman – Vadim – 053-5552472
  - Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
  - Foreman – Charles – 055-2740190
  - Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
  - Foreman – Maor – 050-955-9071
  - Safety – Rotem – 054-447-7112
- Combe Waste – 2P Waste Piping at GL4/SSS Building
  - Foreman – Chaim – 054-5210133
  - Safety – Marzuke – 054-447-7112
- Lesico – H2 Vent/SUT East Area Way Rack
  - Foreman – Suju Pally – 052-7755967
  - Safety – Tal Madar – 052-8229109
- Combe UPW – BCD/UPW Rooms
  - Foreman – Boris – 054-8346412
  - Safety – Shimon – 054-5348843
- HSAI – Chem Dock Retaining Wall
  - Foreman – Dave – 052-4121028
  - Safety – Hiam
- SK Engineering – 3P roof/Lift 2 Piping
  - Foreman – Marcela – 054-5210133
  - Safety – Marzuke – 054-447-7112

## WJG

### Pach Taas

Foreman: Tomer Sasi – 0507670585

Safety: Eran Tzadok - 0547706233

### Afcon

Foreman: Montu - 0559116973

Safety: Stiven – 0552742935

### Chemo Aharon

Foreman: Shai Adi – 0524801180

Safety: Erez Megidish - 0549716840

# Subcontractor Weekend Work- 14.02.2025

## CUB

Chemo Aharon CUB 2:

Dudu - 0509808846

Alberto - 0508573970

SKE CUB 2:

Mario - 0548991051

Marzuk - 0548830263

Sami Najami CUB 2:

Husein - 052-6917461

Aviram - 050-9059920

HSAI CUB 1&2:

Sergey - 0552728807

Haim - 054-8038554

Meptagon I&C CUB 1:

Sergey - 0537981592

Itzik - 0587441140

Pach Taas CUB 1 Roof:

Tomer - 050-767-0585

Eran - 054-7706233

## Trestle

### SNJ:

### **Piping:**

17 People

### **Steal:**

15 People

### **Superintendent**

Mahmoud Ayub 054-4915889

### **Safety:**

Aviram Shriki / 050-9059920

## Site

- D.A. - shotcrete south wall
- Olizki - Cub 1 east, north,
- Afkon - BGY

# Daily Coordination Meeting



14:00 Sign In
