

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- Weekend work



NWTD Int. SOMD
2:00 am


אינטל קרית גת

FAB-28

NWTD interstitial
SOMD
2:00 am



UTILITY LEVEL MOD1

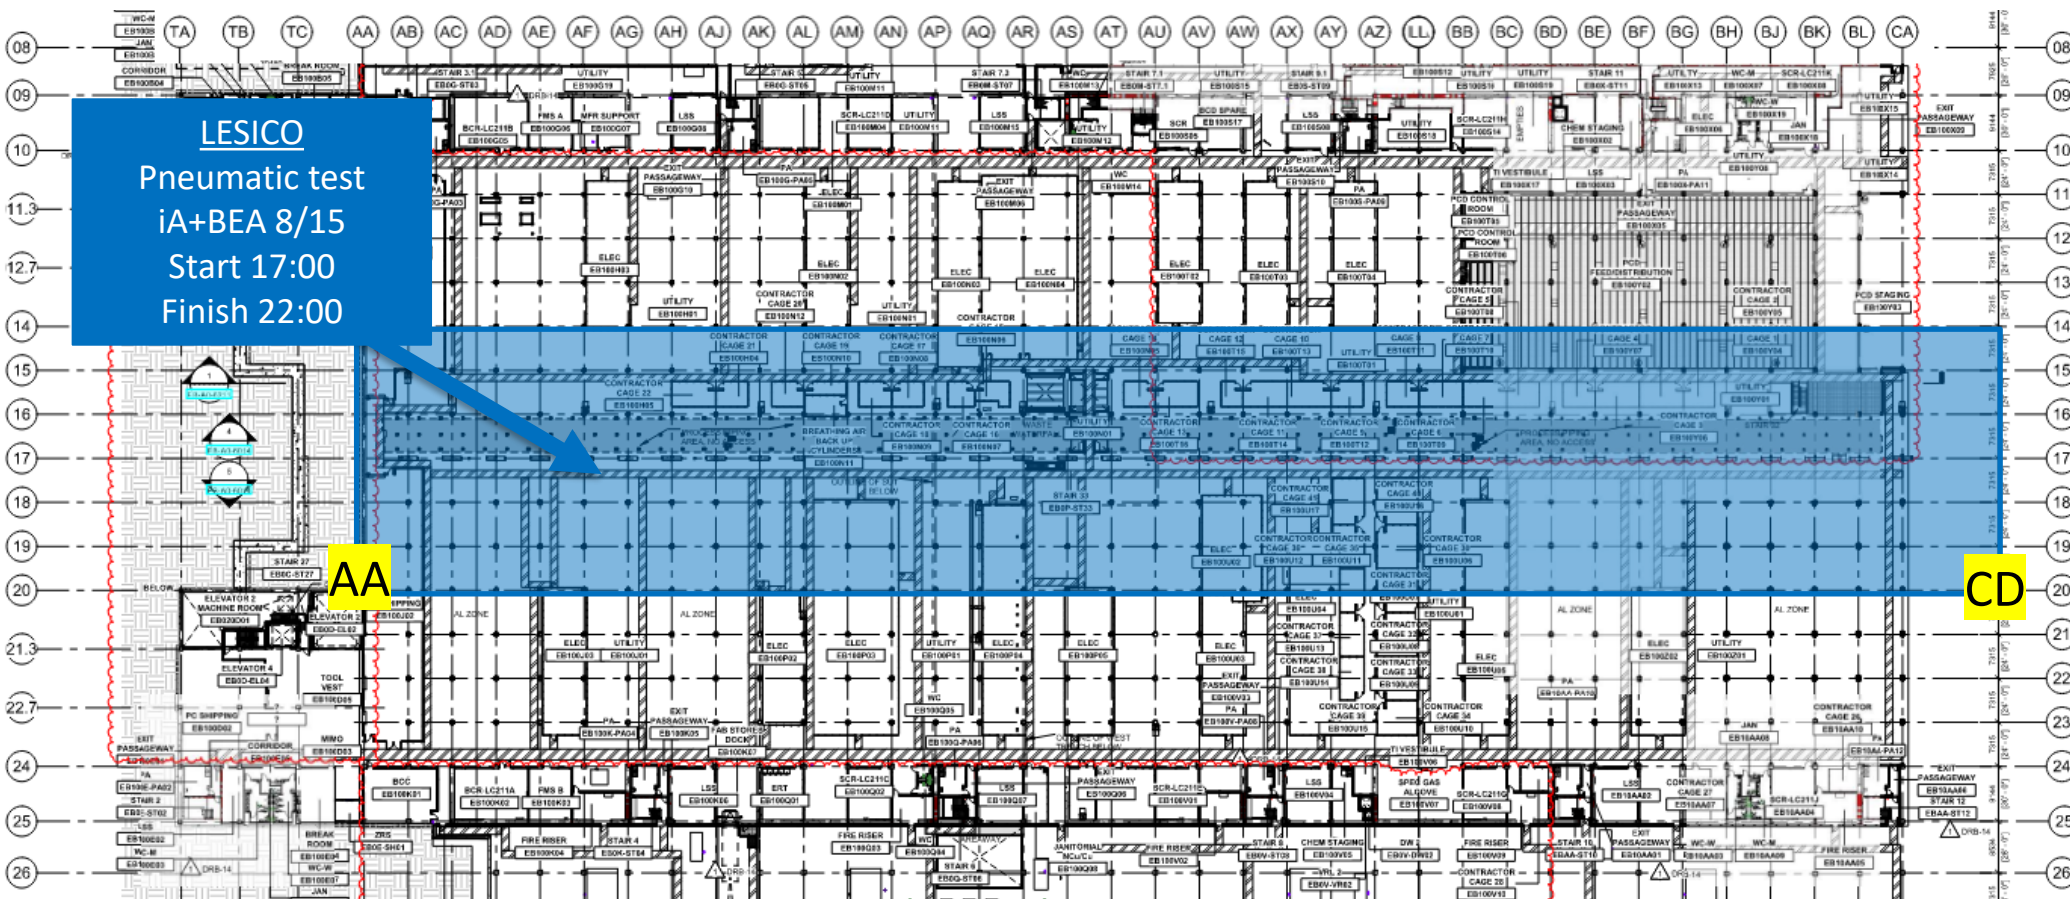




HOFFMAN CONSTRUCTION COMPANY




SUT LEVEL

LESICO
Pneumatic test
iA+BEA 8/15
Start 17:00
Finish 22:00

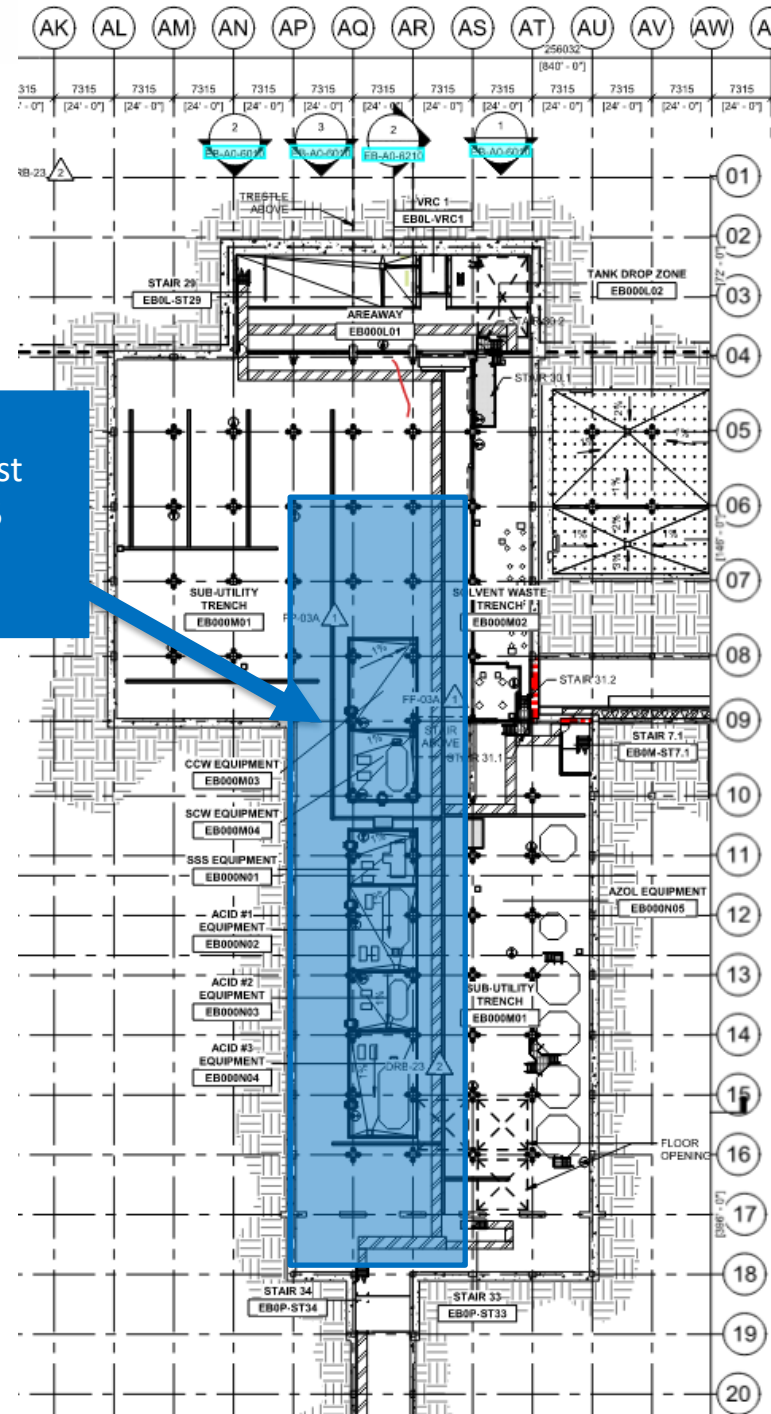




UTILITY LEVEL MOD1

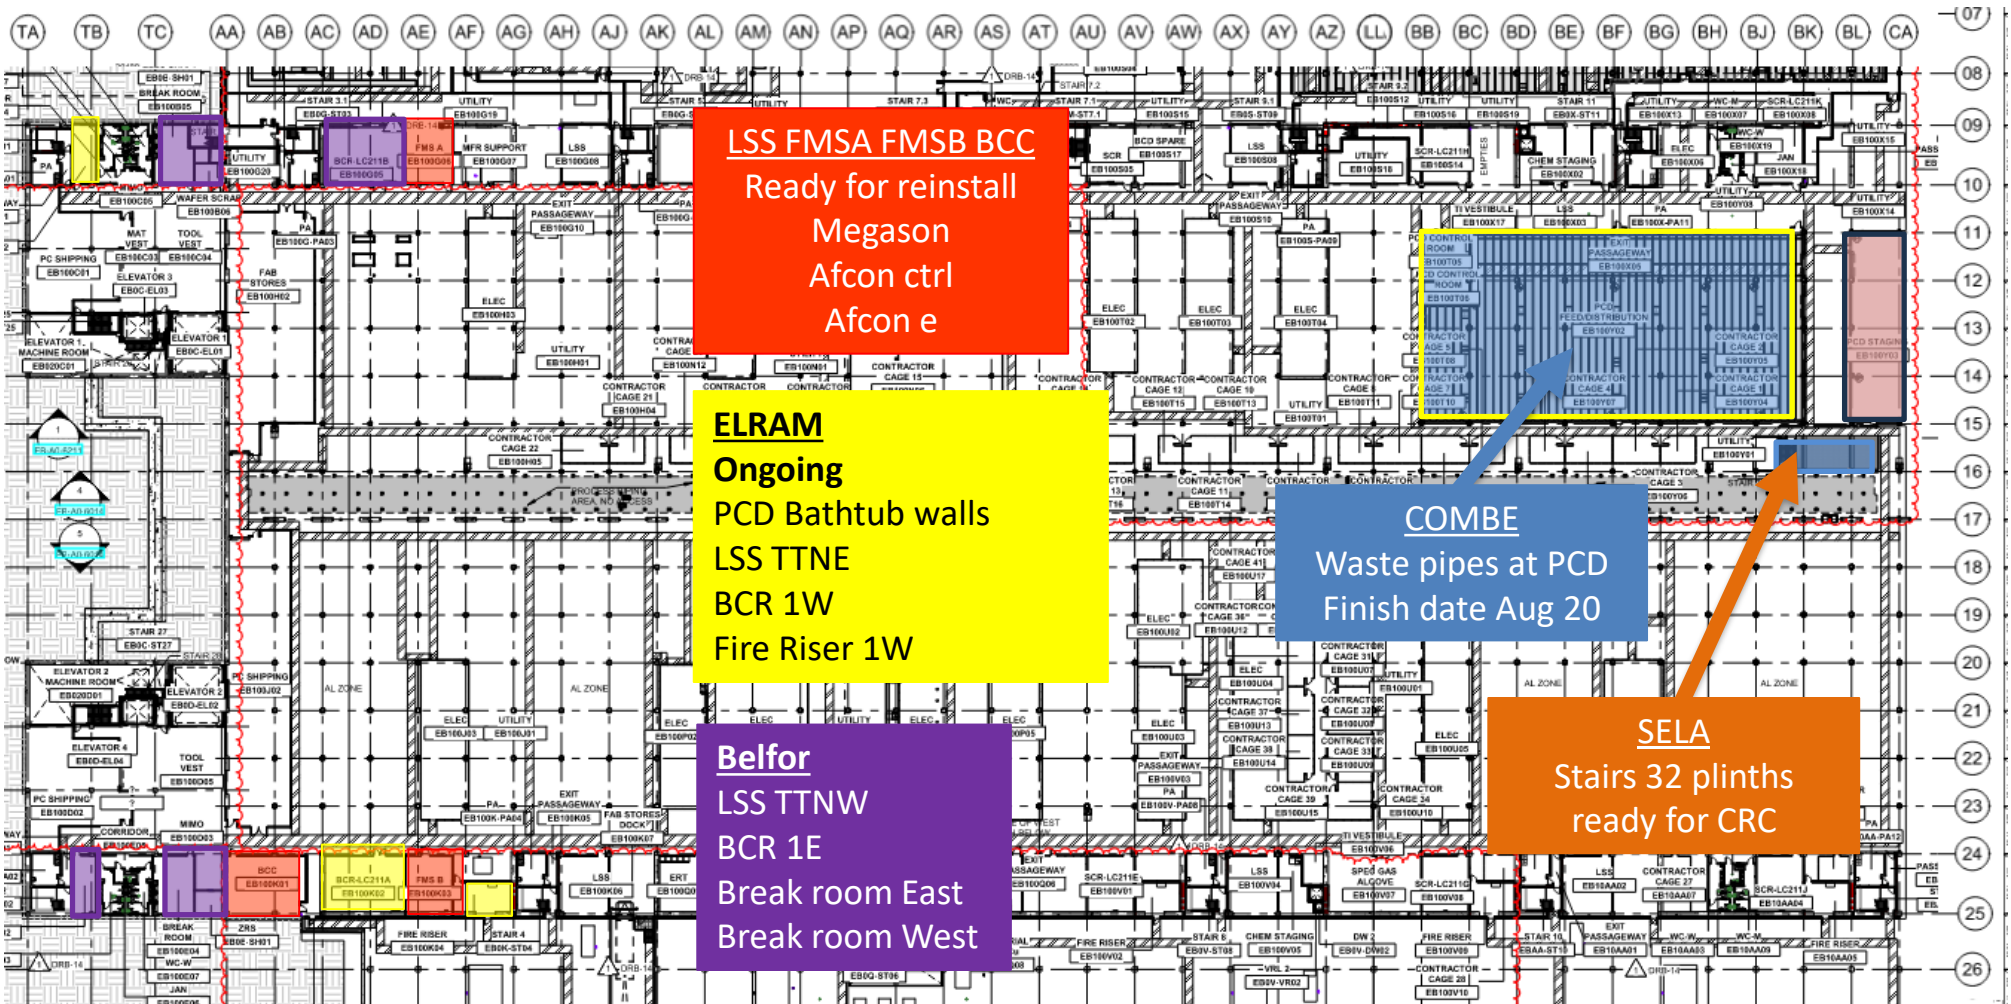


UTILITY LEVEL MOD2

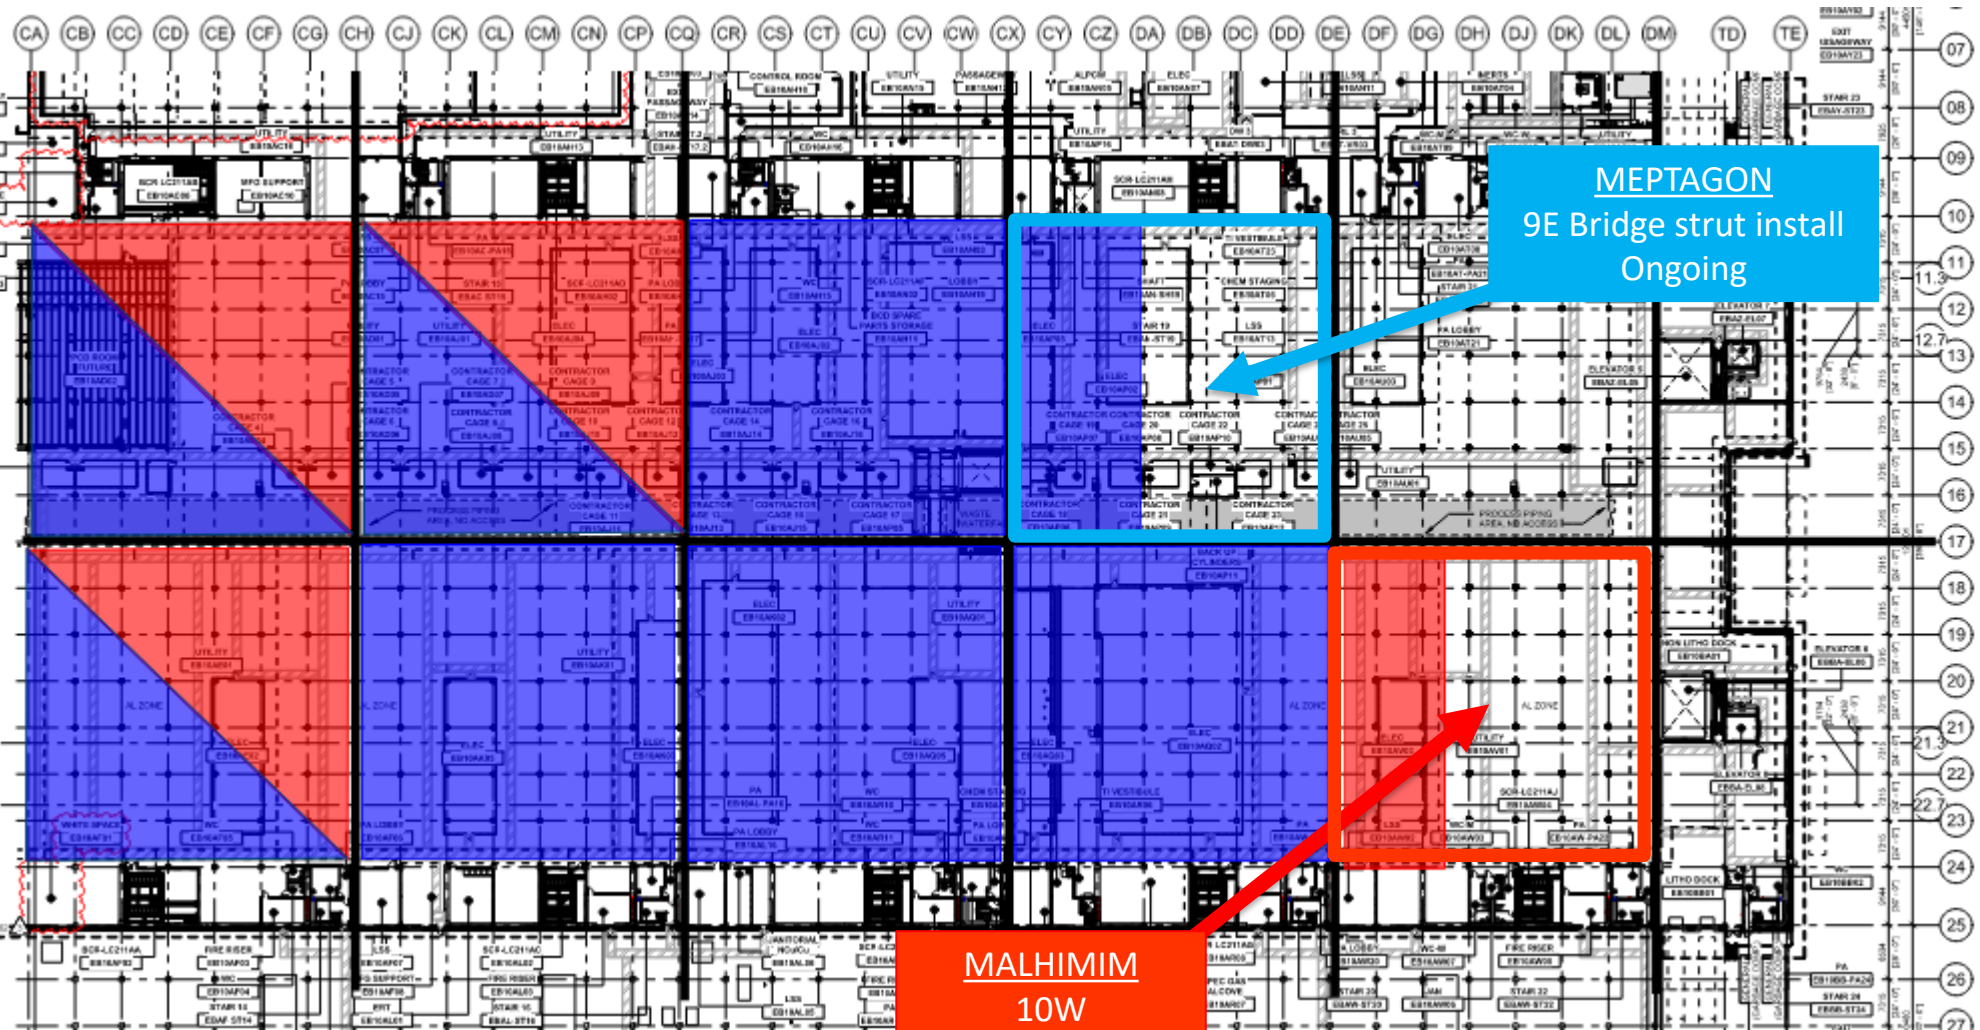




SUT 38.1 LEVEL

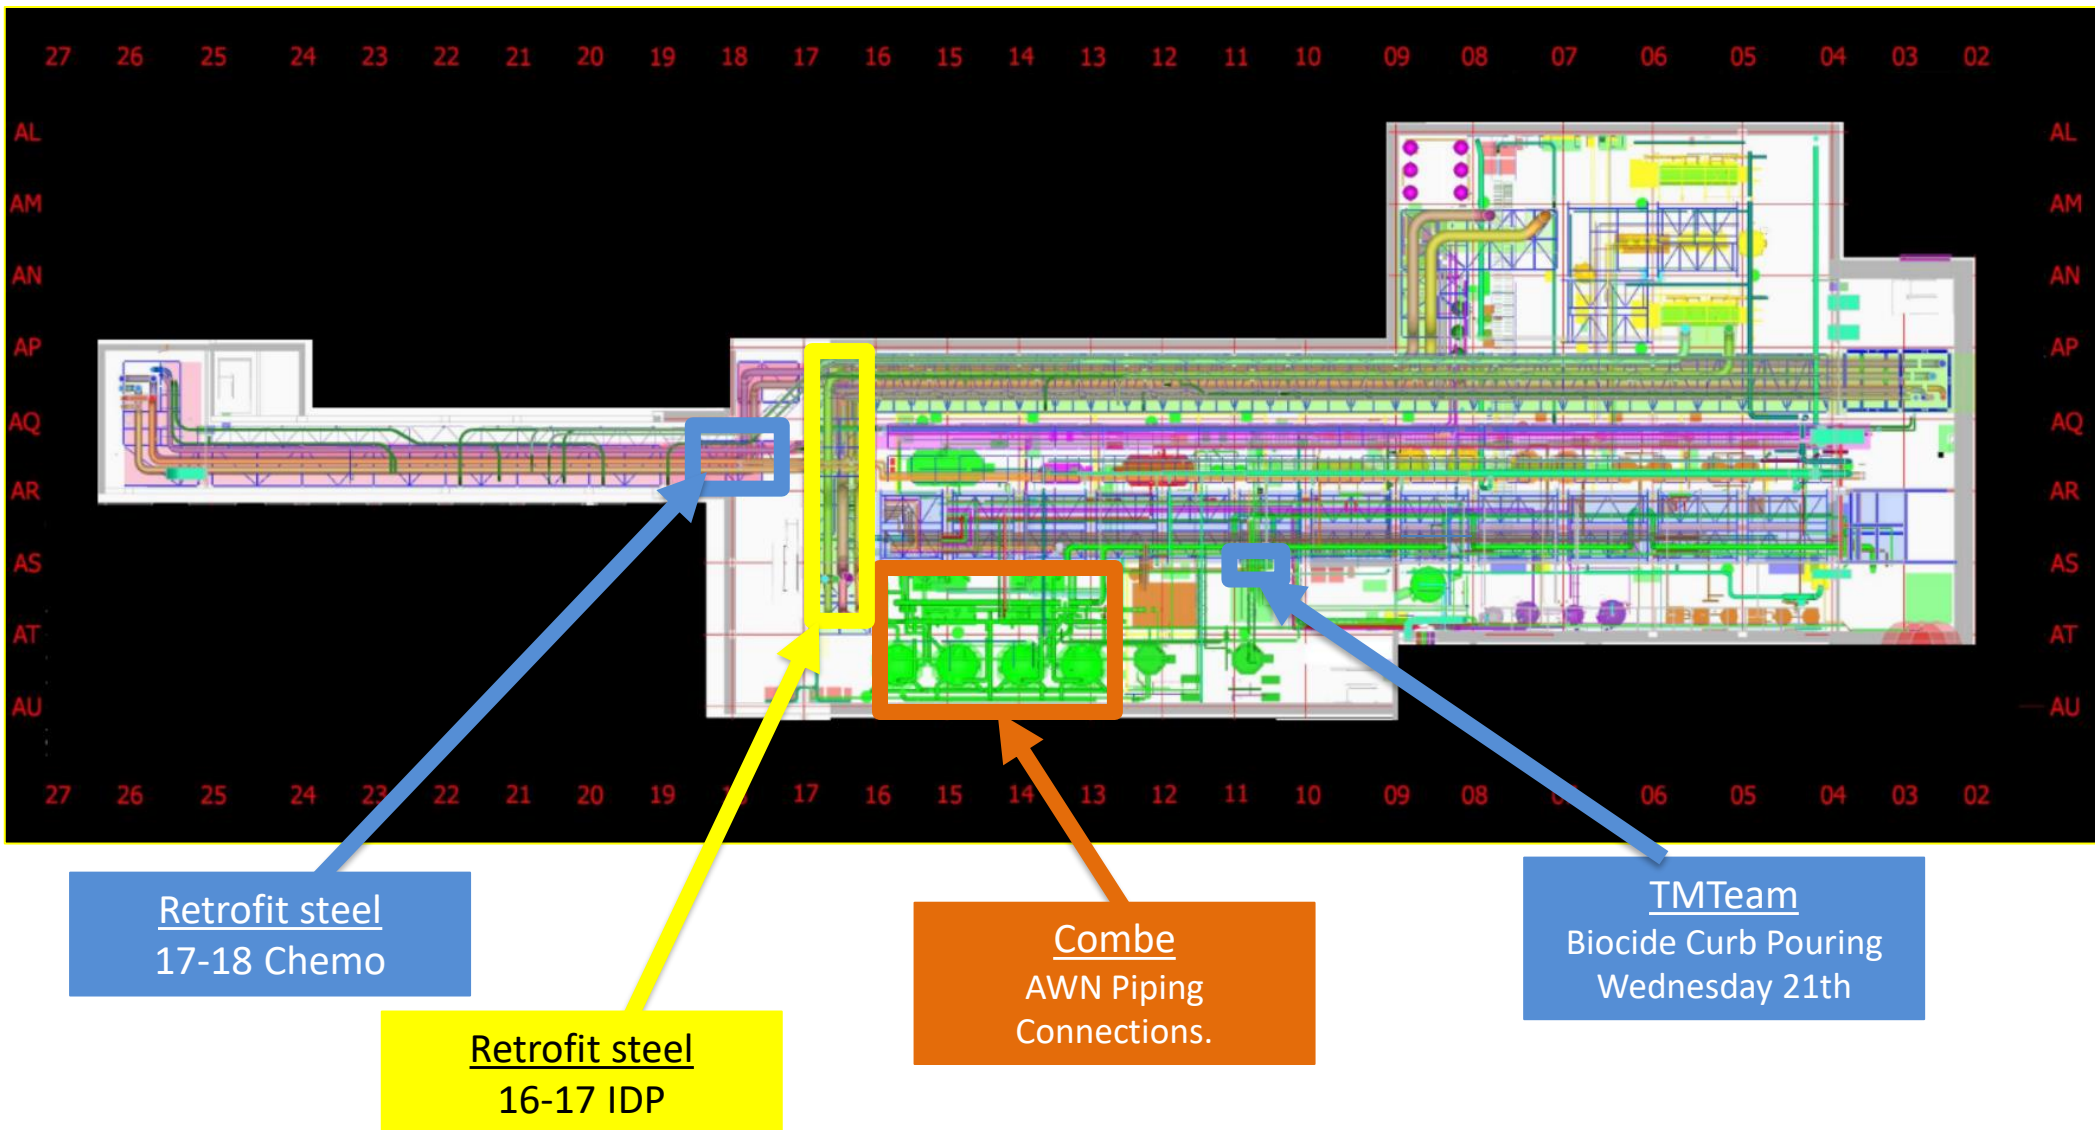



SUT 38.2 LEVEL

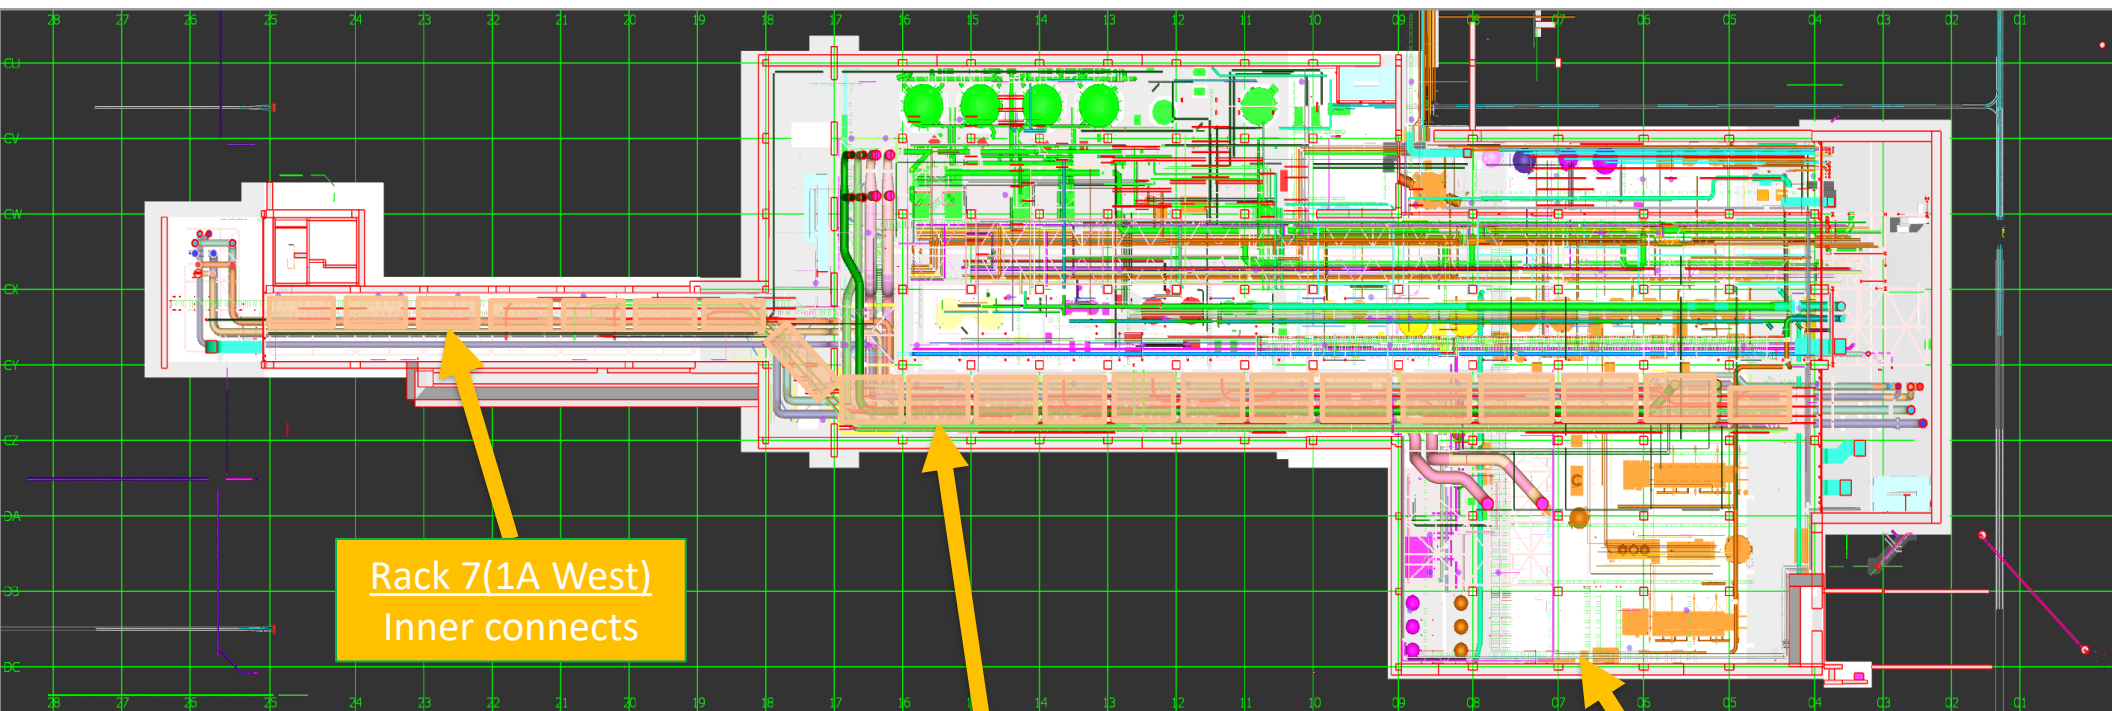

Rack 7(1A West)
Inner connects


CRW
H&T
Need to be installed

1A Rack
Inner connects


8 Rack
Lifting

Vesda
H&T
Not actively installing


SUBFAB BUILDOUT MOD 1

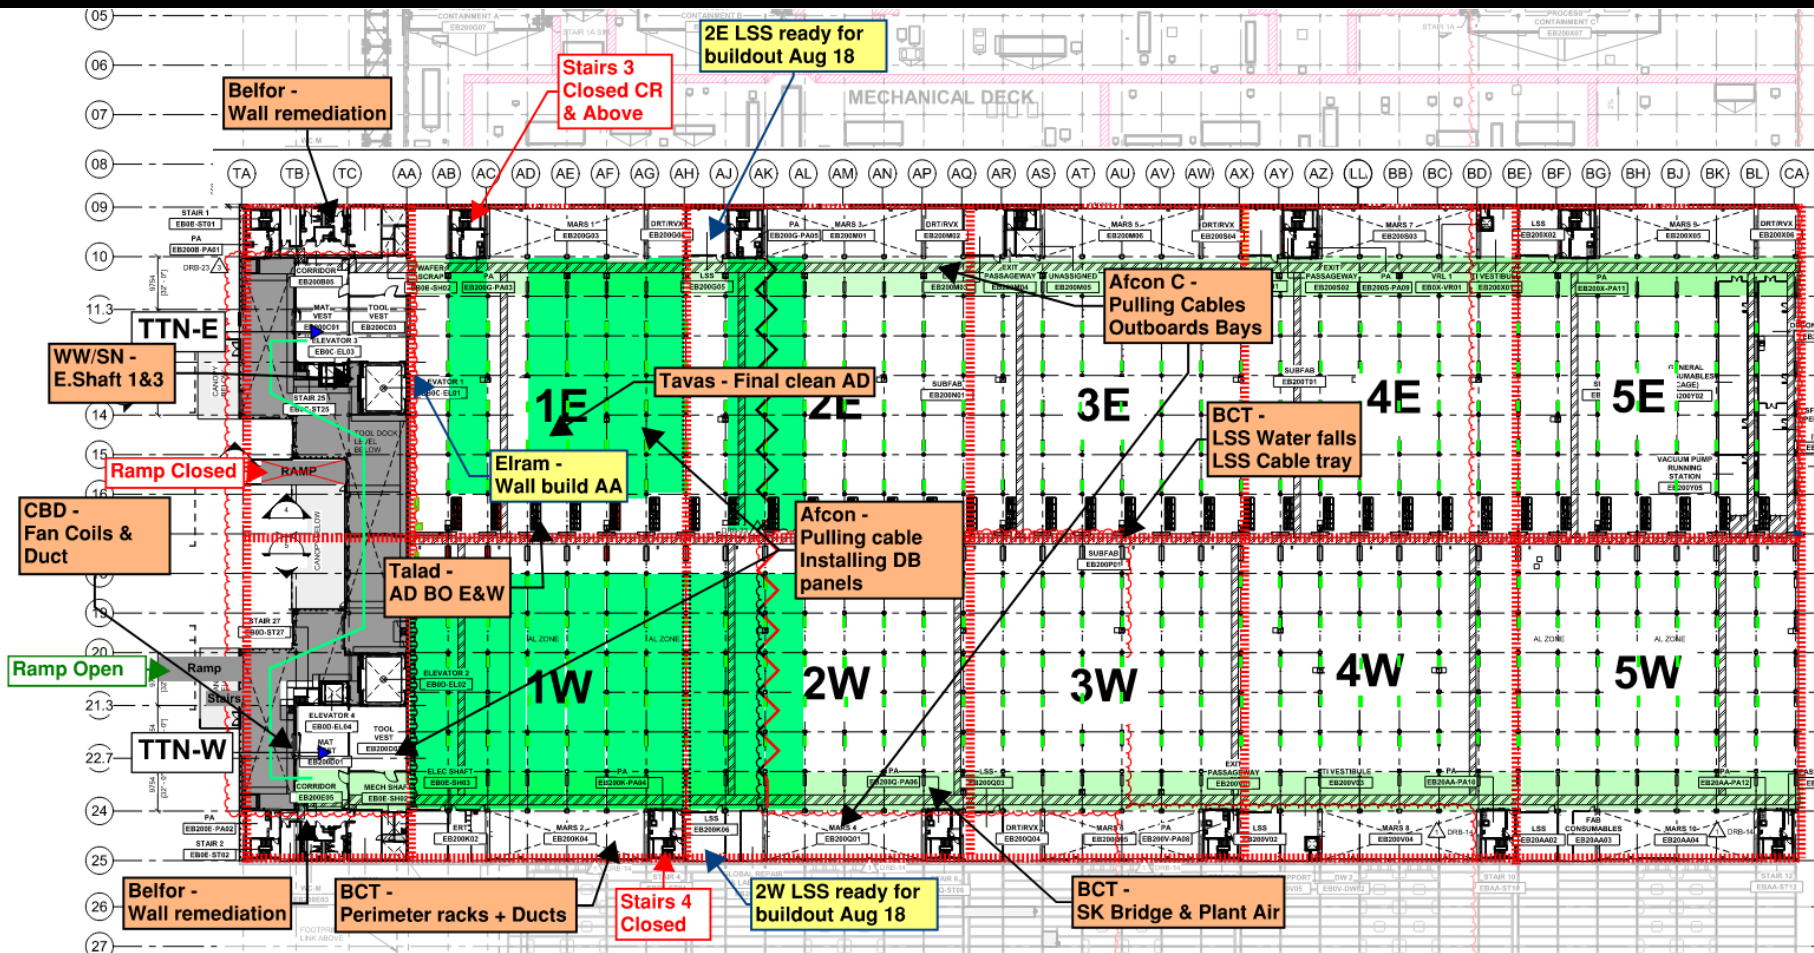

SUBFAB BUILDOUT MOD 2

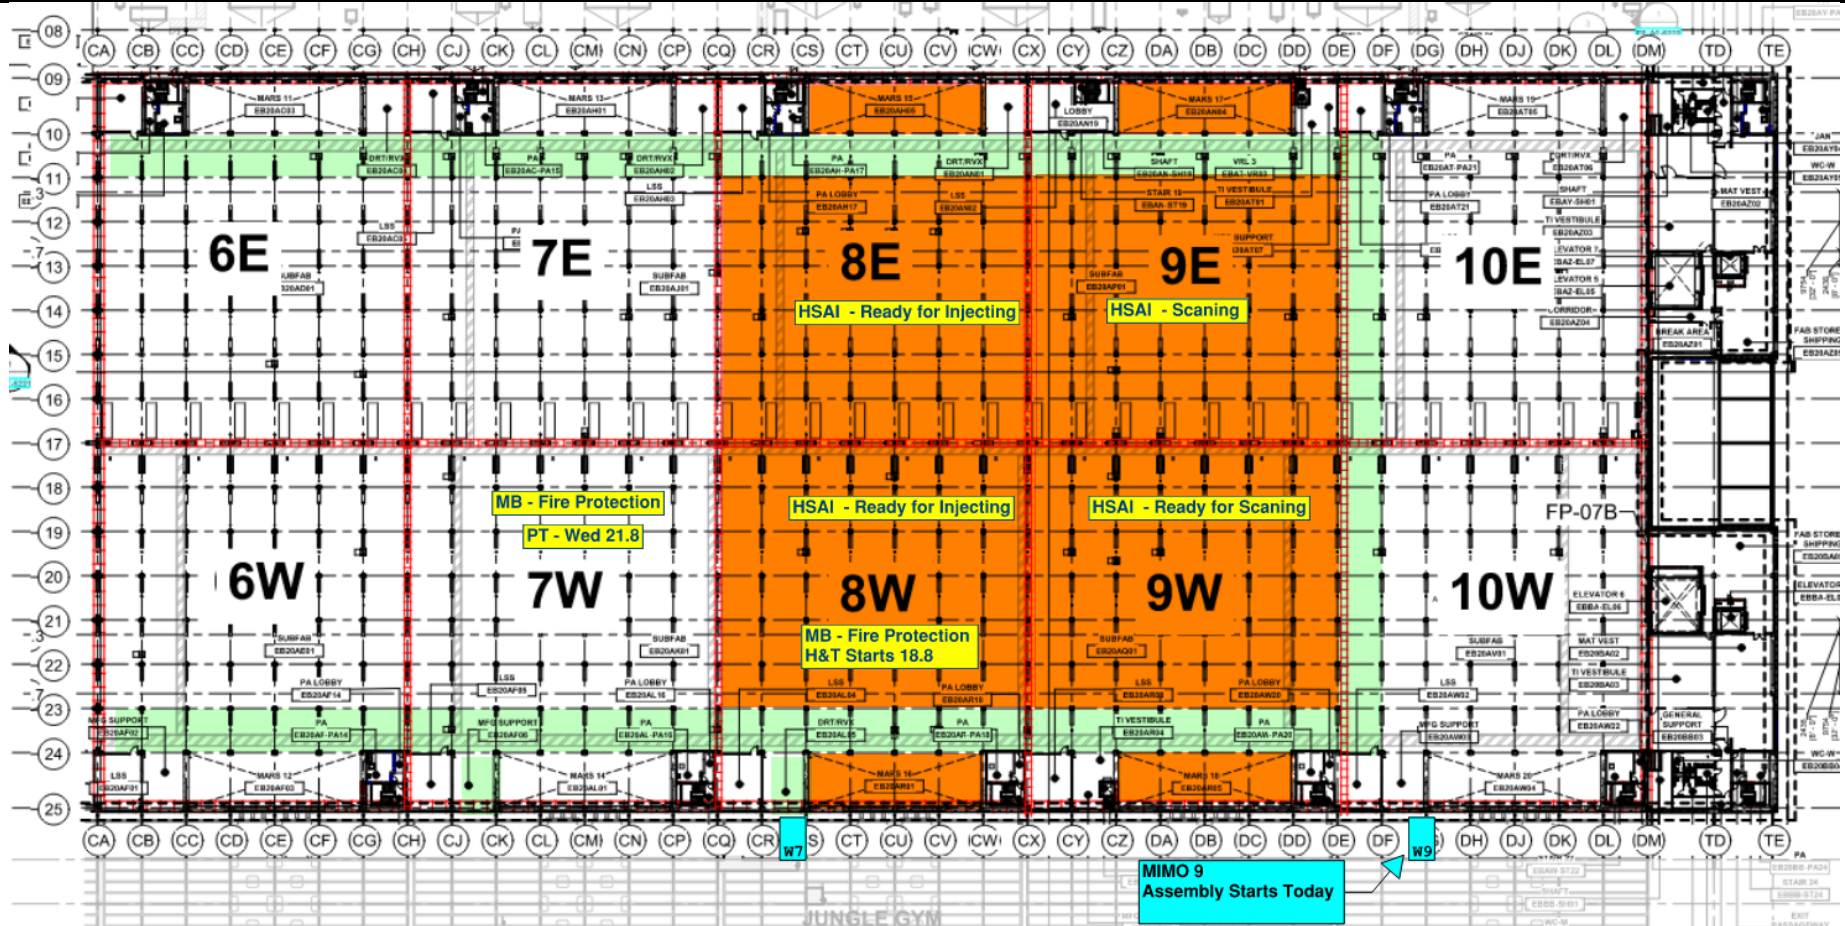

SUBFAB CRC TOP COTE

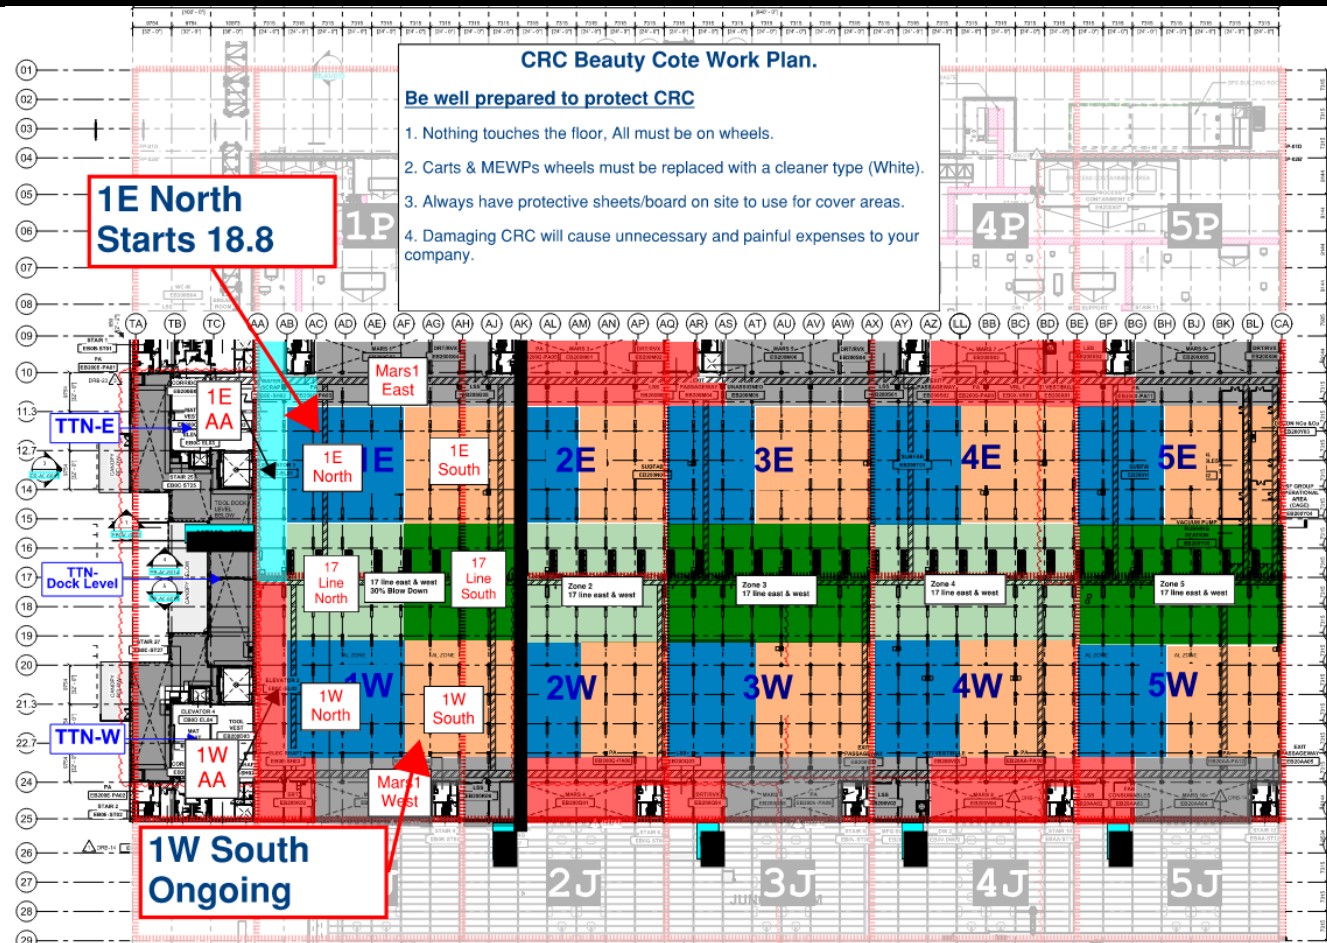








Carmel bidud pressure test need
all documentation done

Int. level


- WW/SN - 2W penetrations
- Chemo- 10" pipe racks 2E-2W started
- Afcon - Cable trays, modules, cable pulling 1E,2E,1W,2w
- HYG - 5RA added beams 2E
- MB- 2E-2W preparations for test WW33
- C-B duct - 1W-2W to schedule test WW33
- Elram - Column wraps 9,10,24 lines
- RP- FP 4DA 3E-3W
- Tzur-Esh - Steel paint 4E-4W
- Megasone - Small wires+ speakers 3E+2E

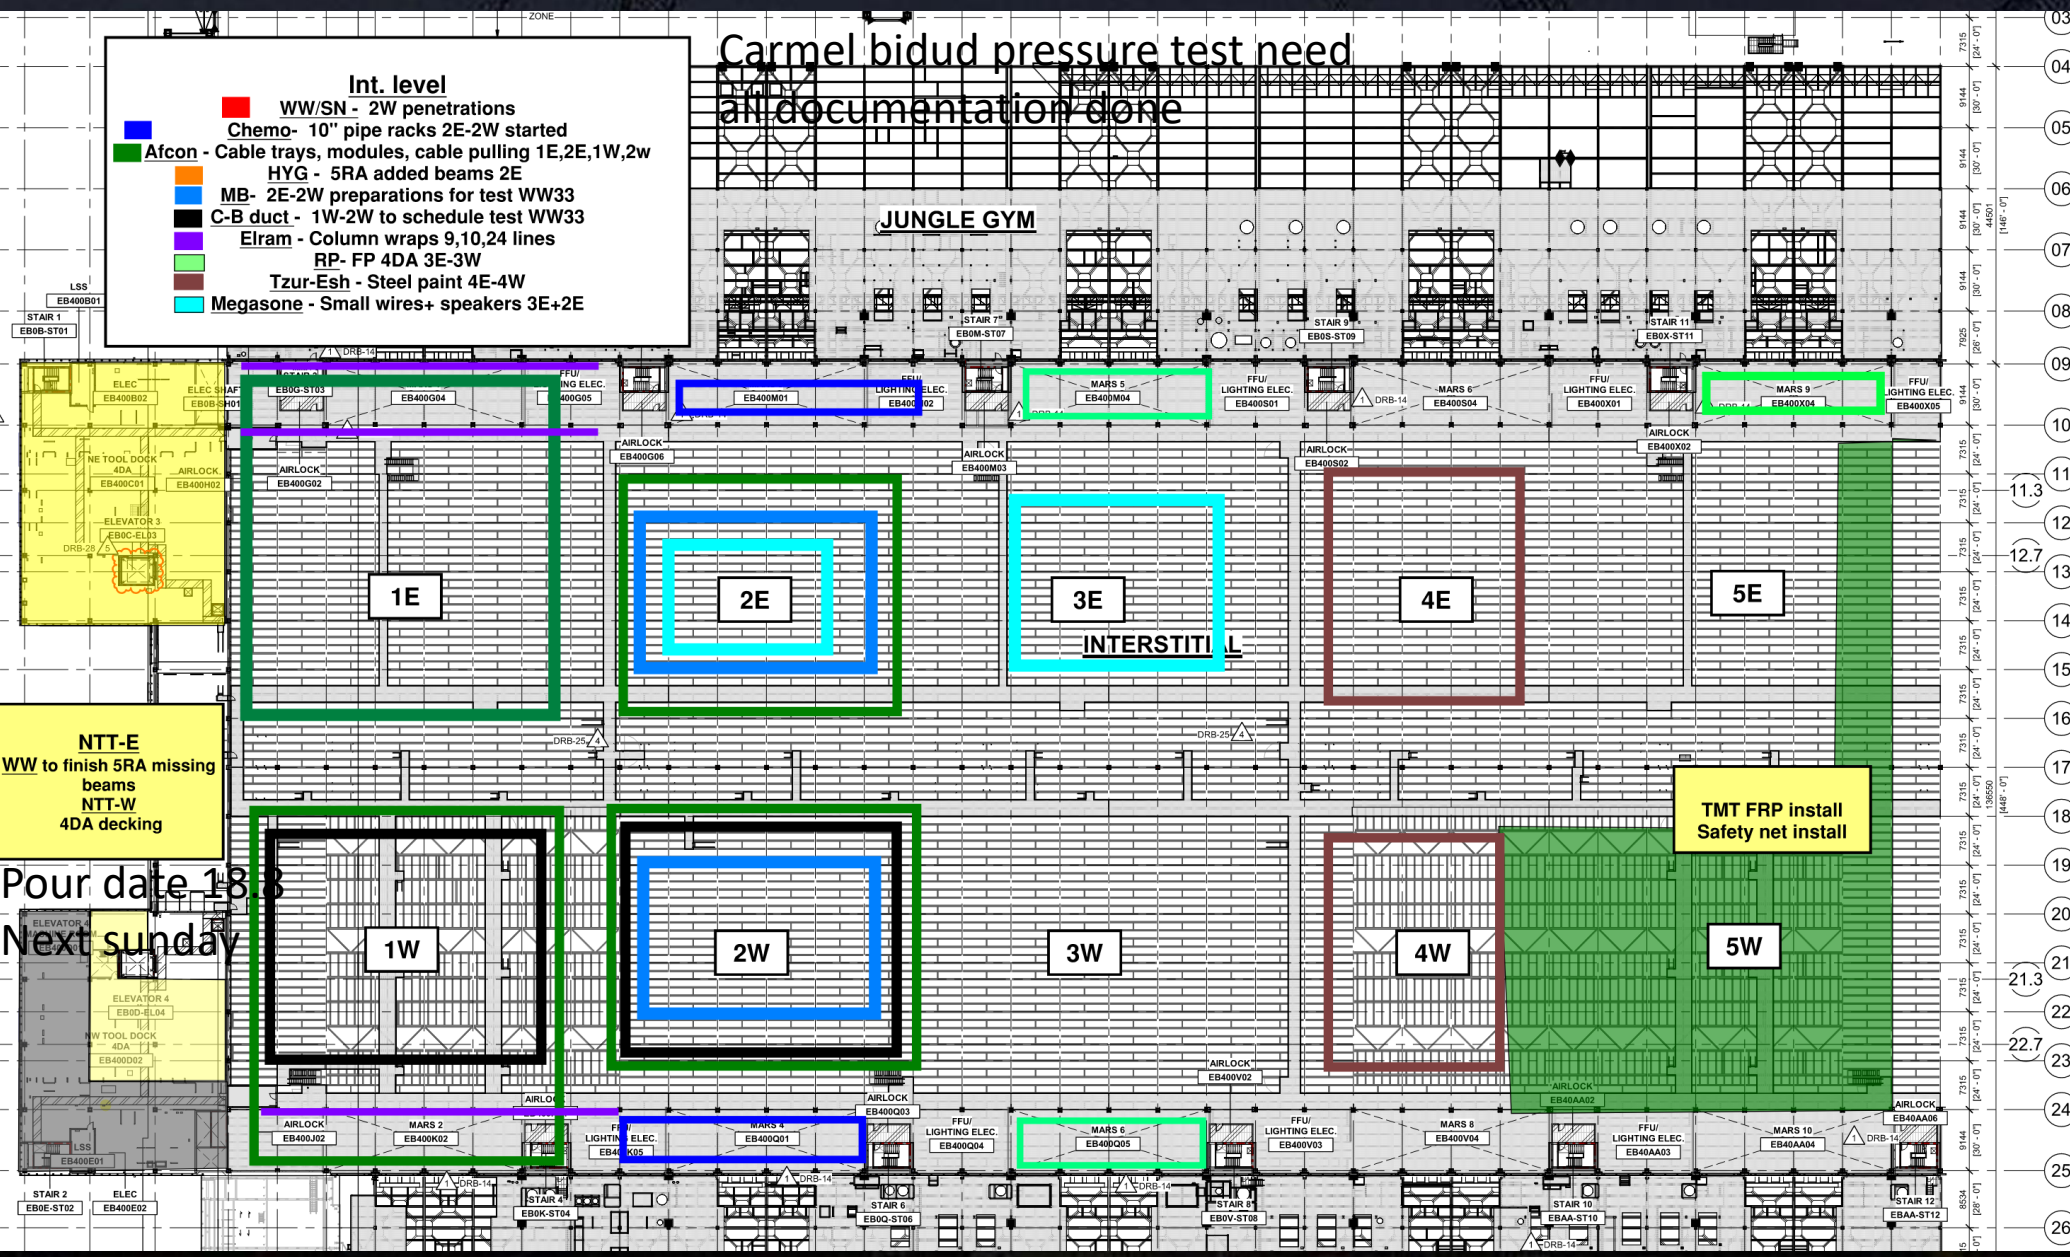



NTT-E
WW to finish 5RA missing
beams
NTT-W
4DA decking

Pour date 13.8
Next sunday


TMT FRP install
Safety net install

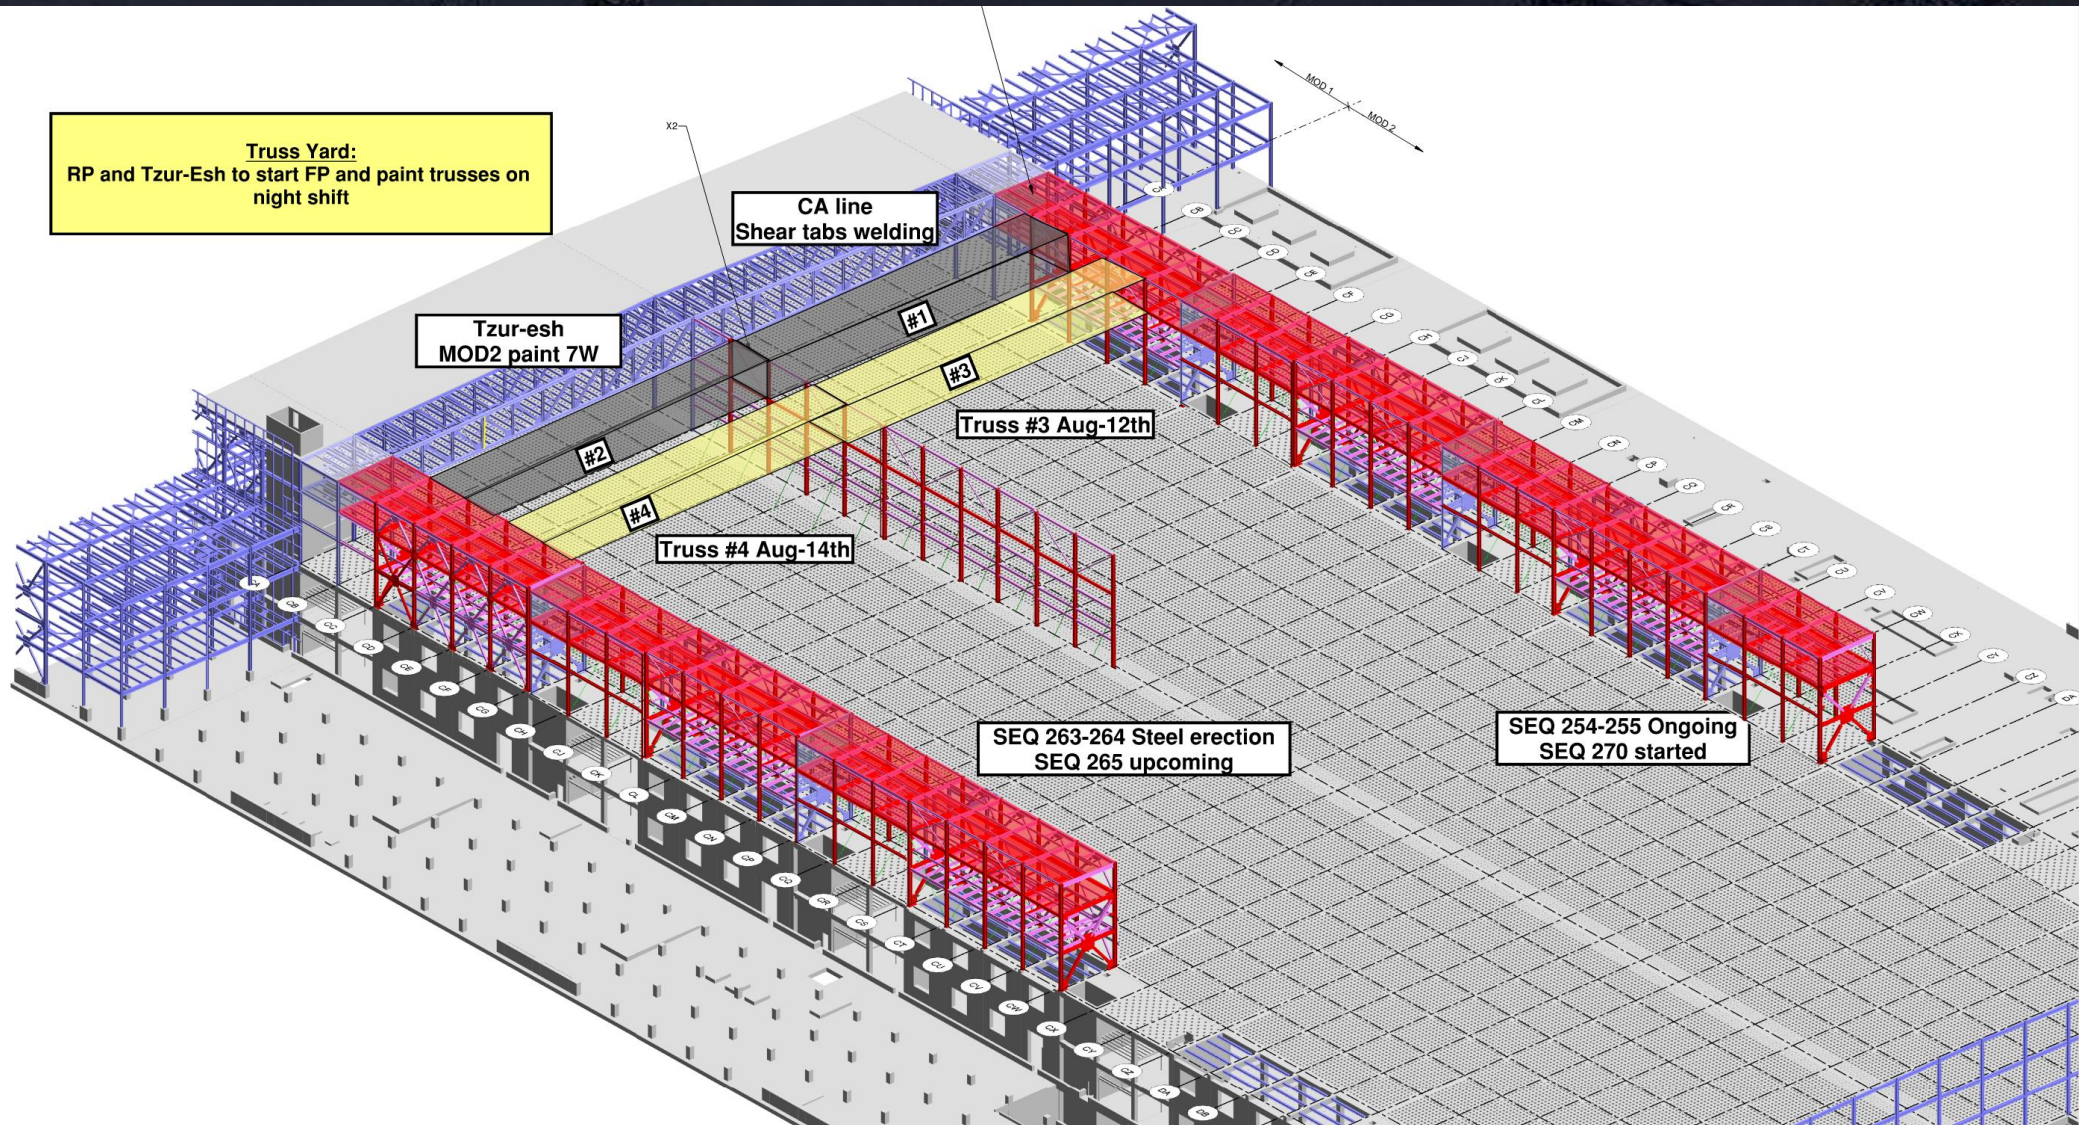


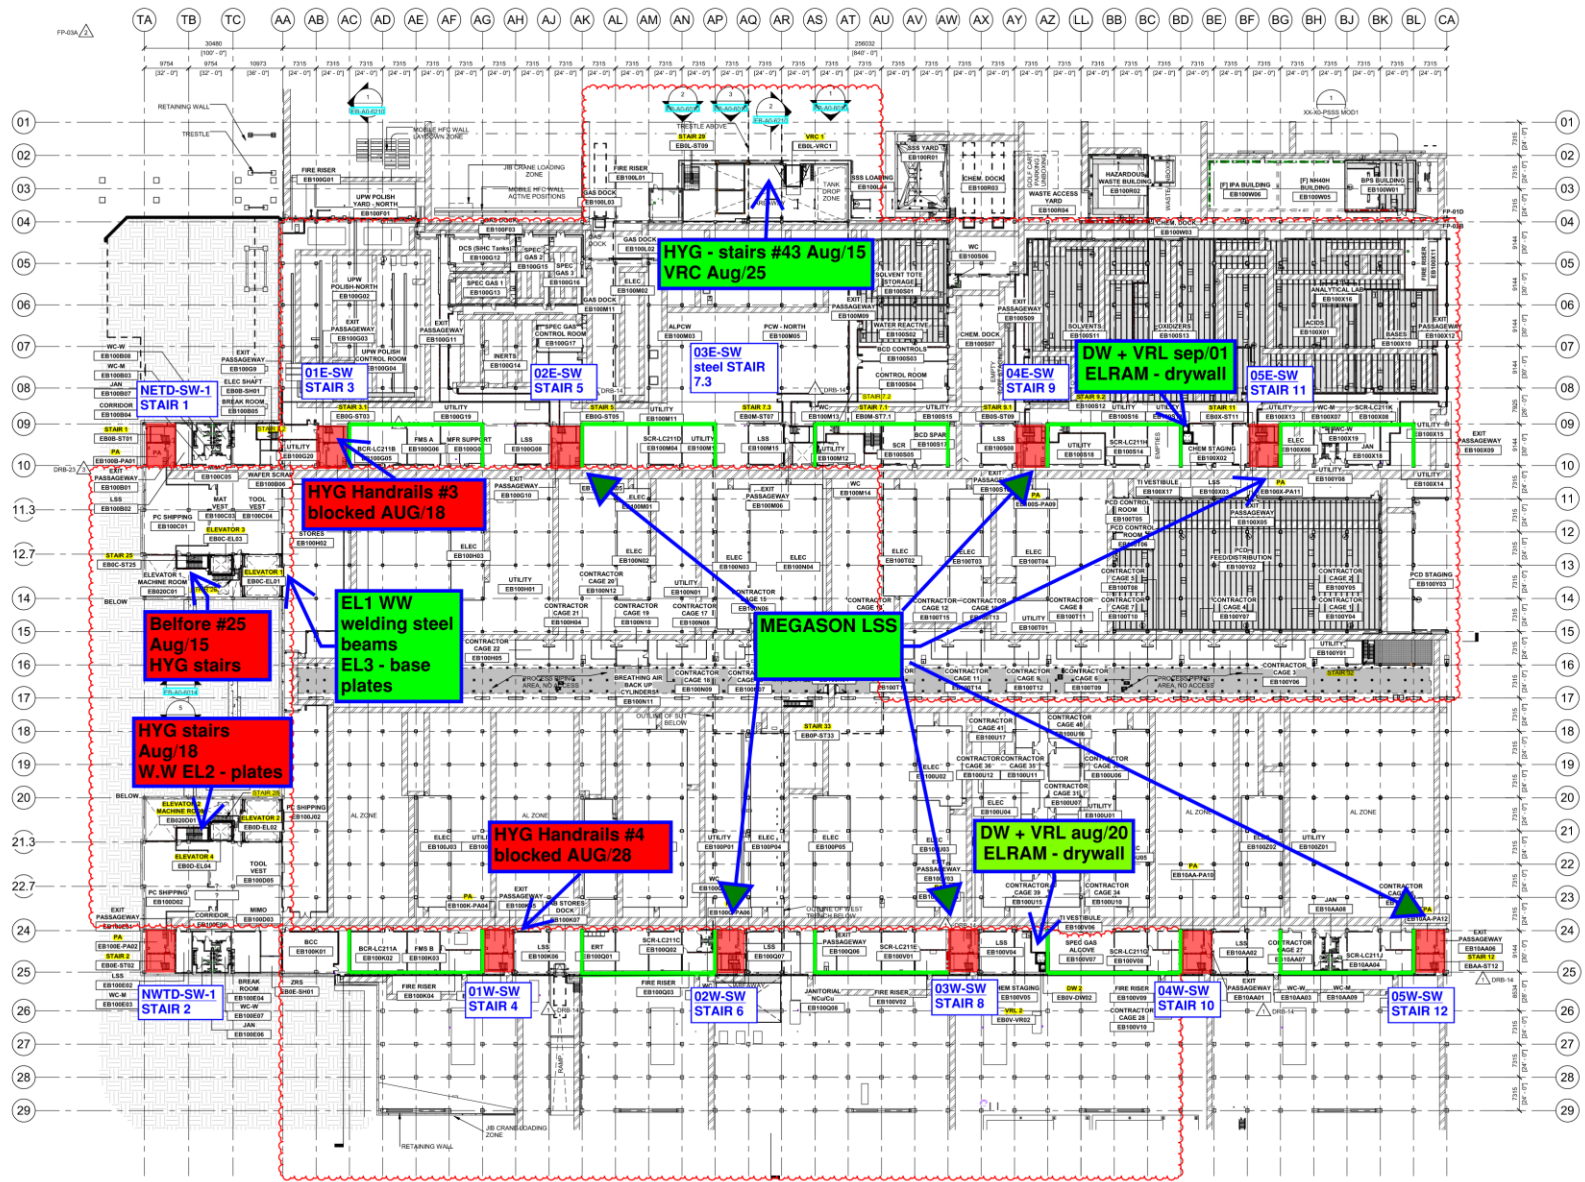

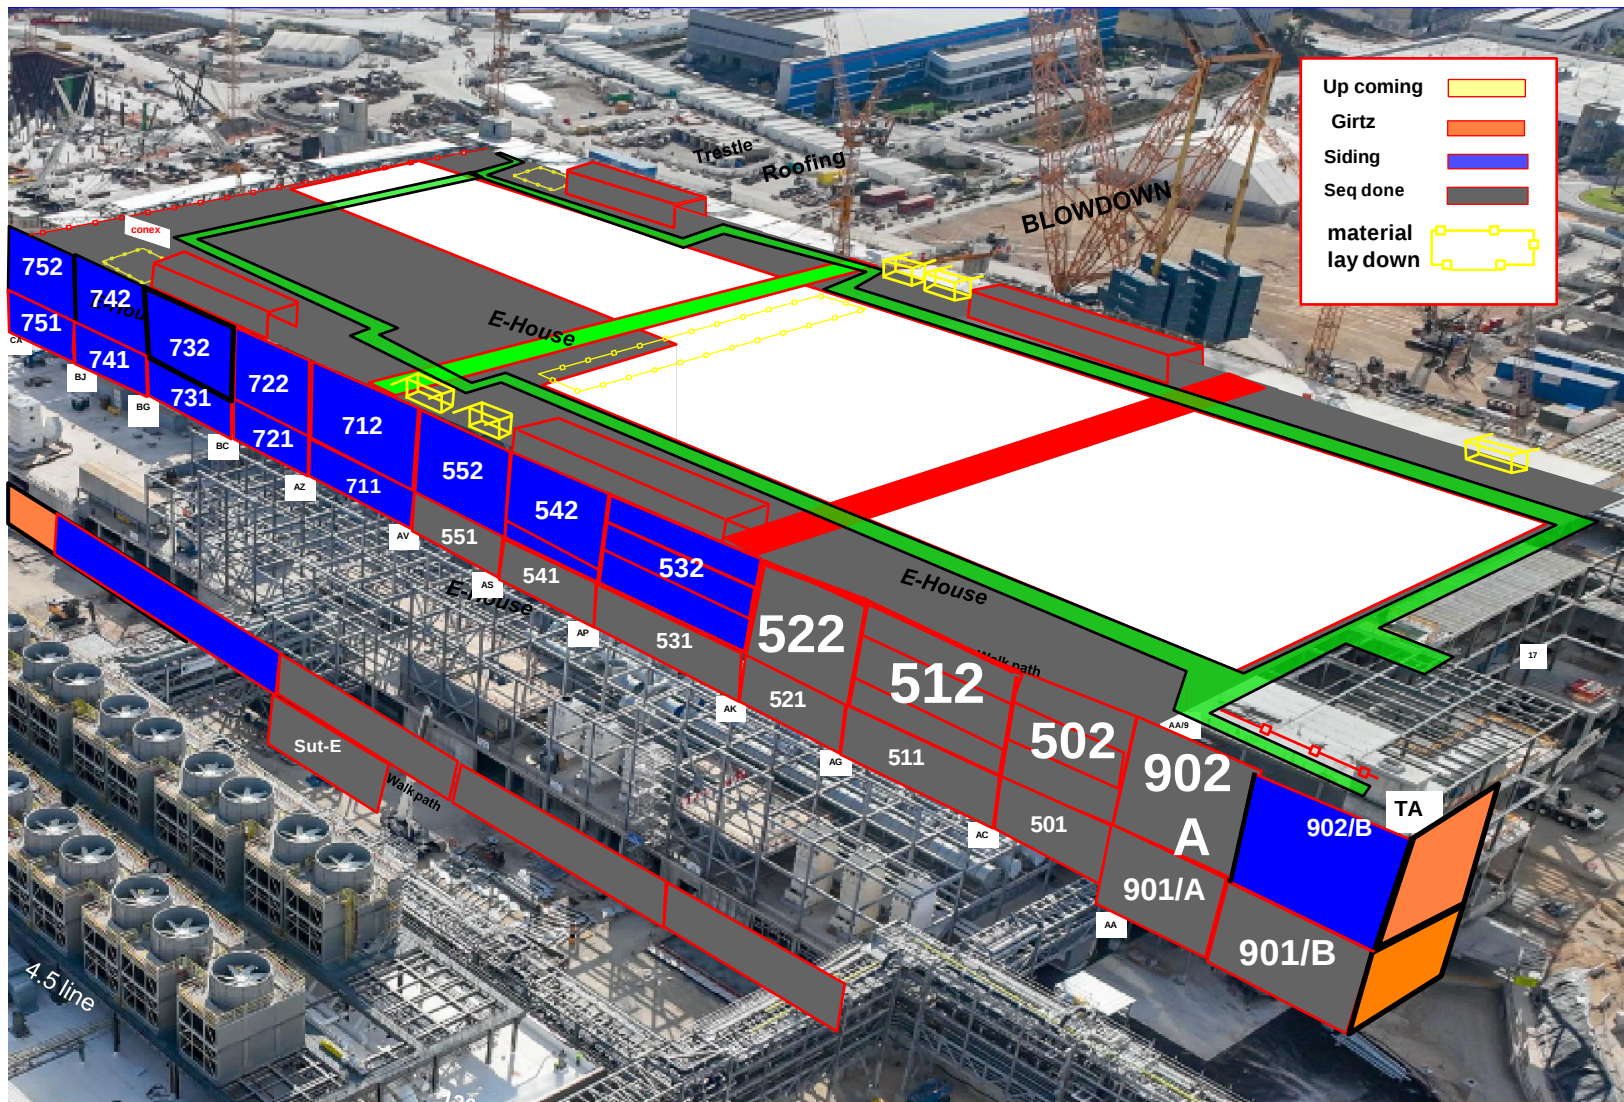

Walk path

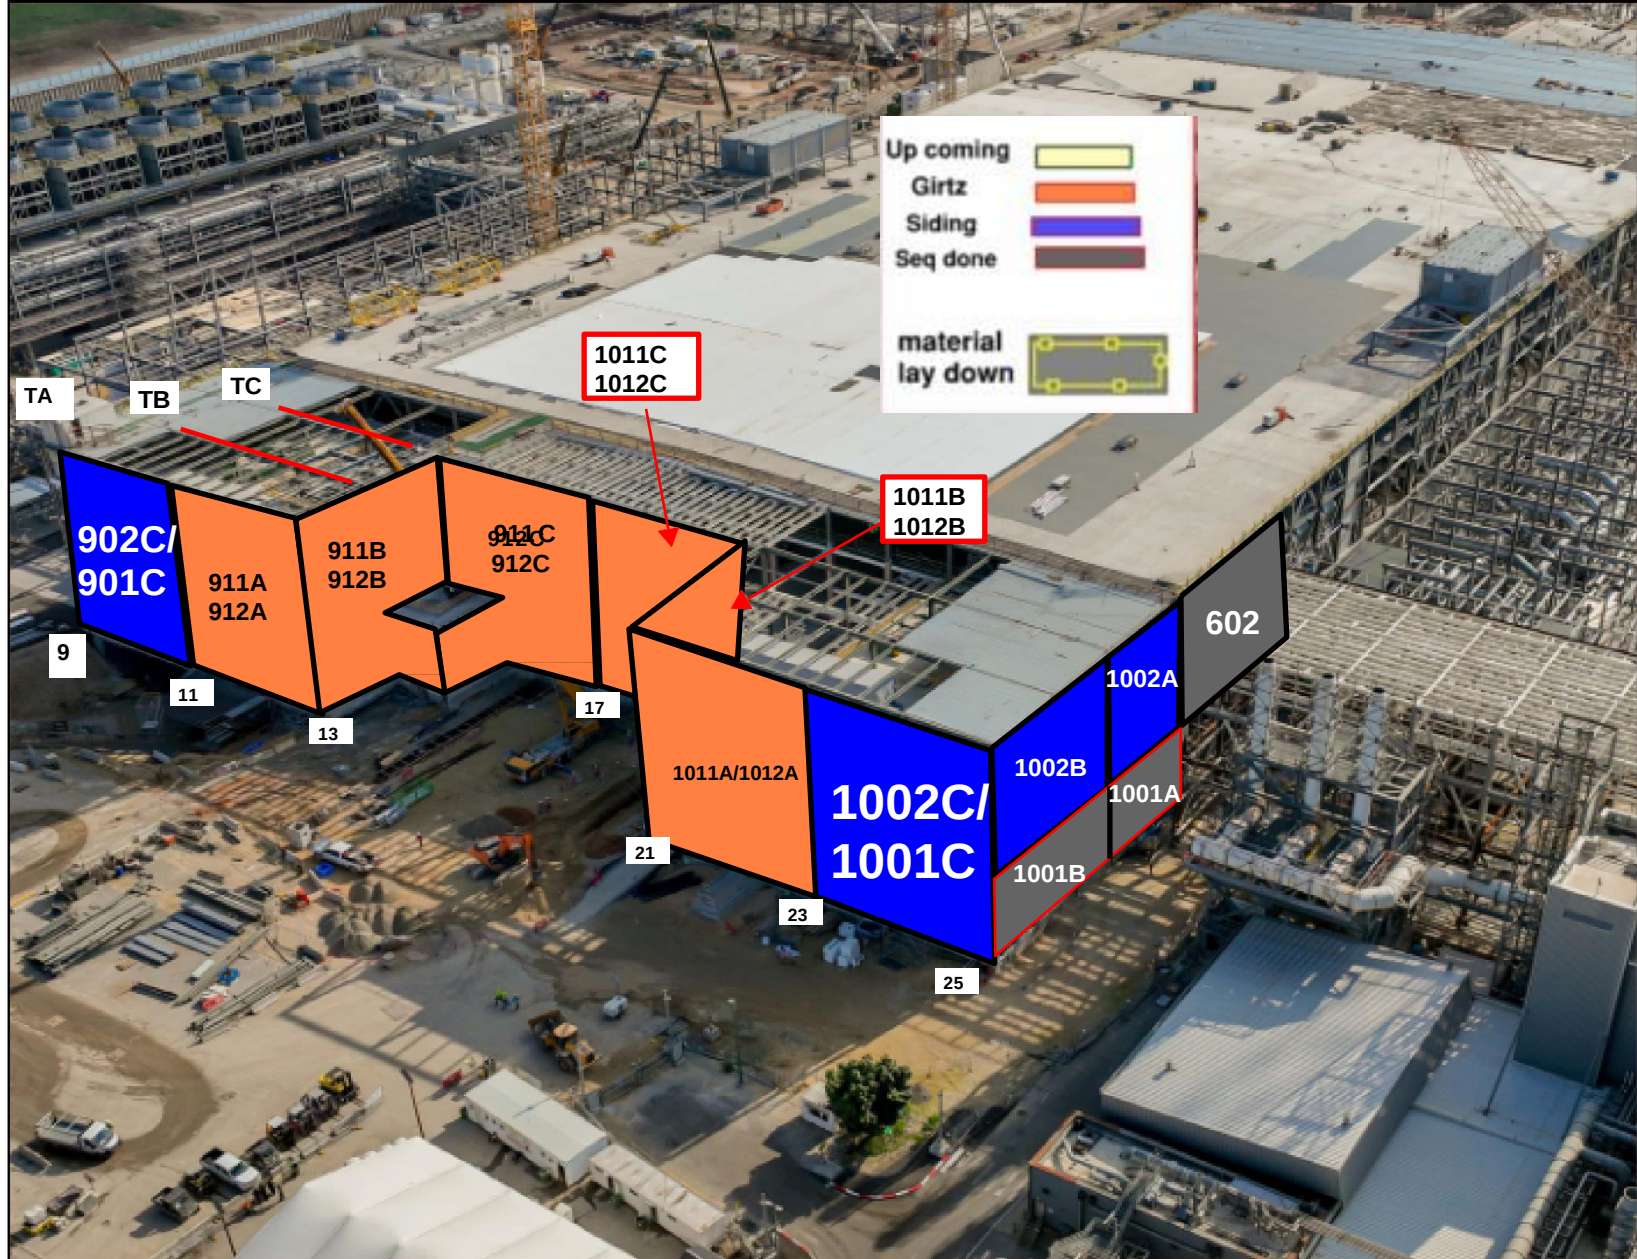


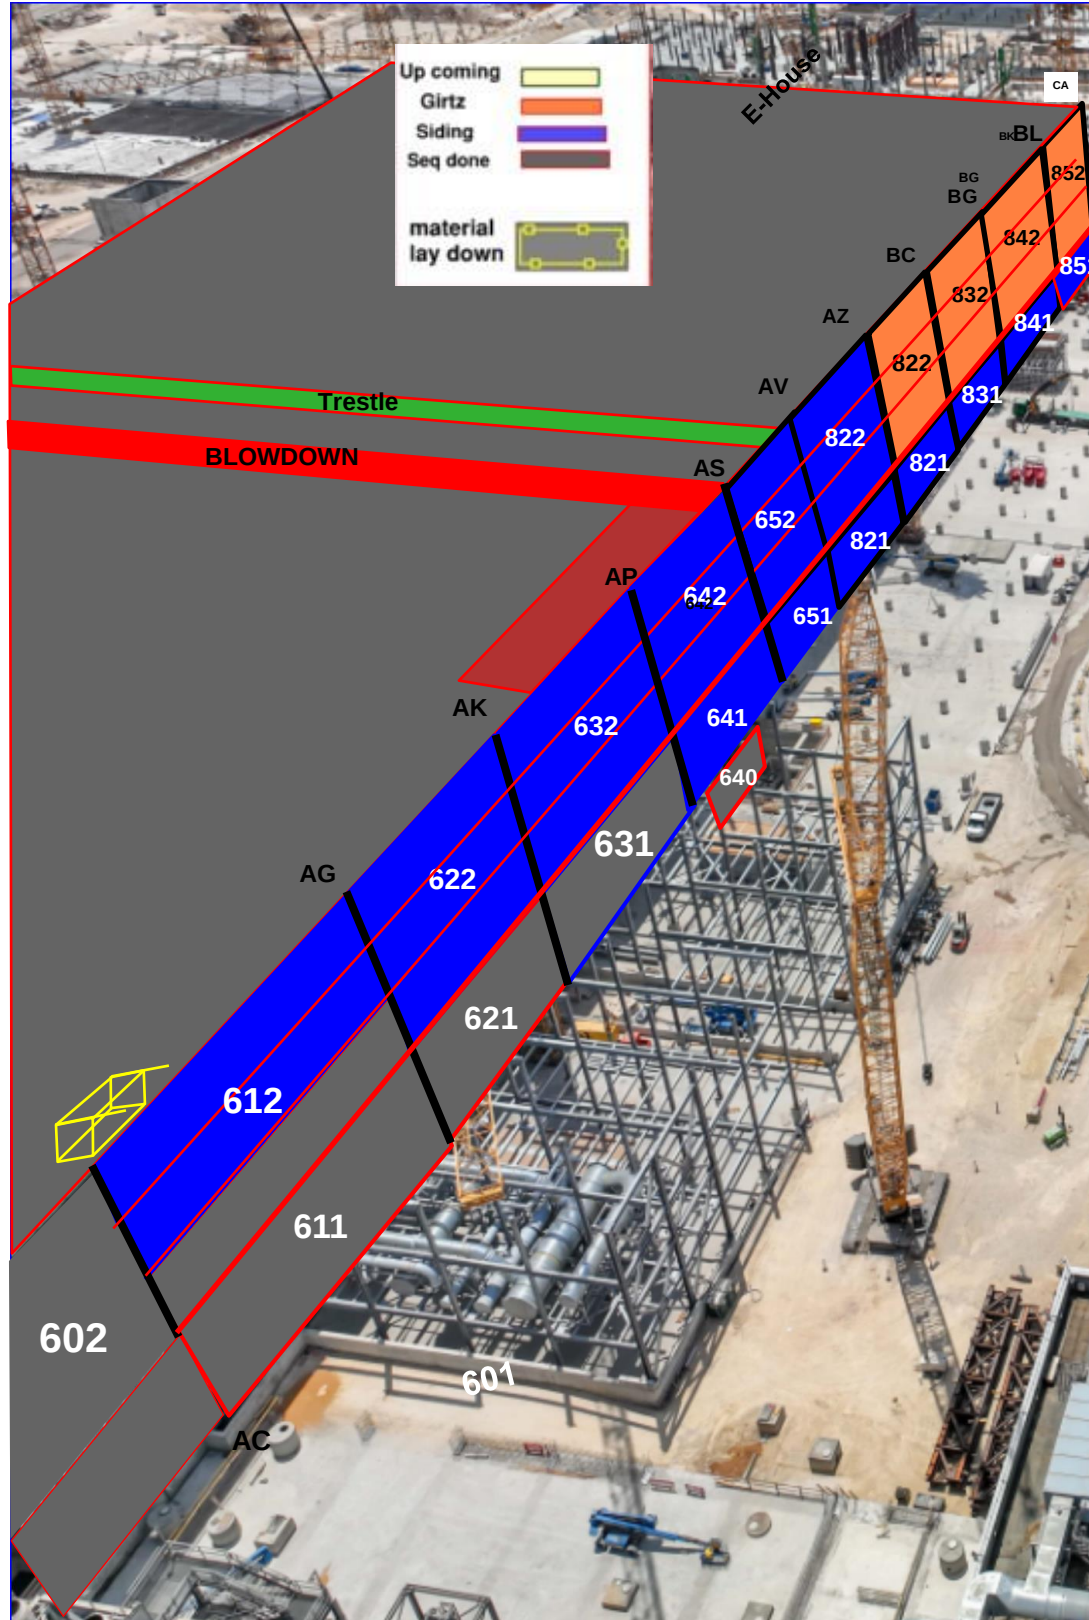

PSSS.1

Utility Level
1YA

PSSS Roof
2SA

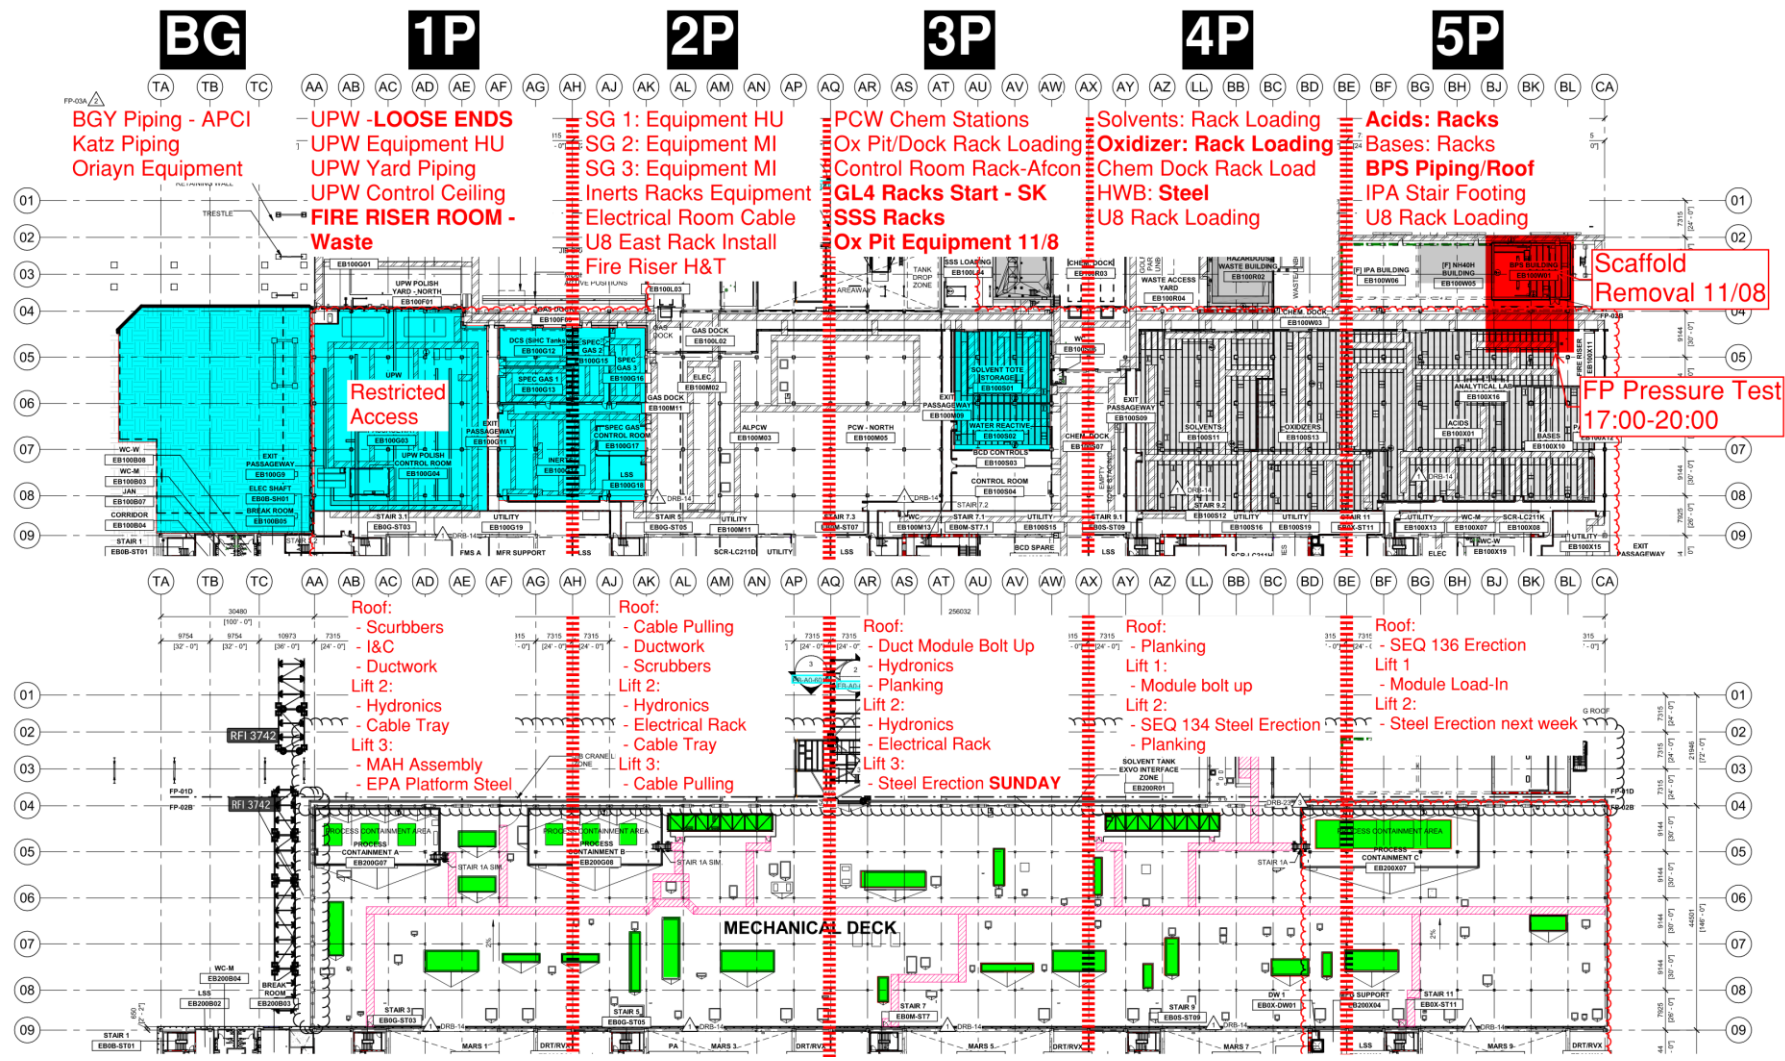



PSSS P1
PachTaas Operation
Plates: 15-08-2024
Air Blower: 20-08-2024
EPA Platform: 26-08-2024

Single
EPA Platform


Fan



WJG 01J, 02J LIFT 2 & 3



WJG 03J, 04J, 05J LIFT 2 & 3

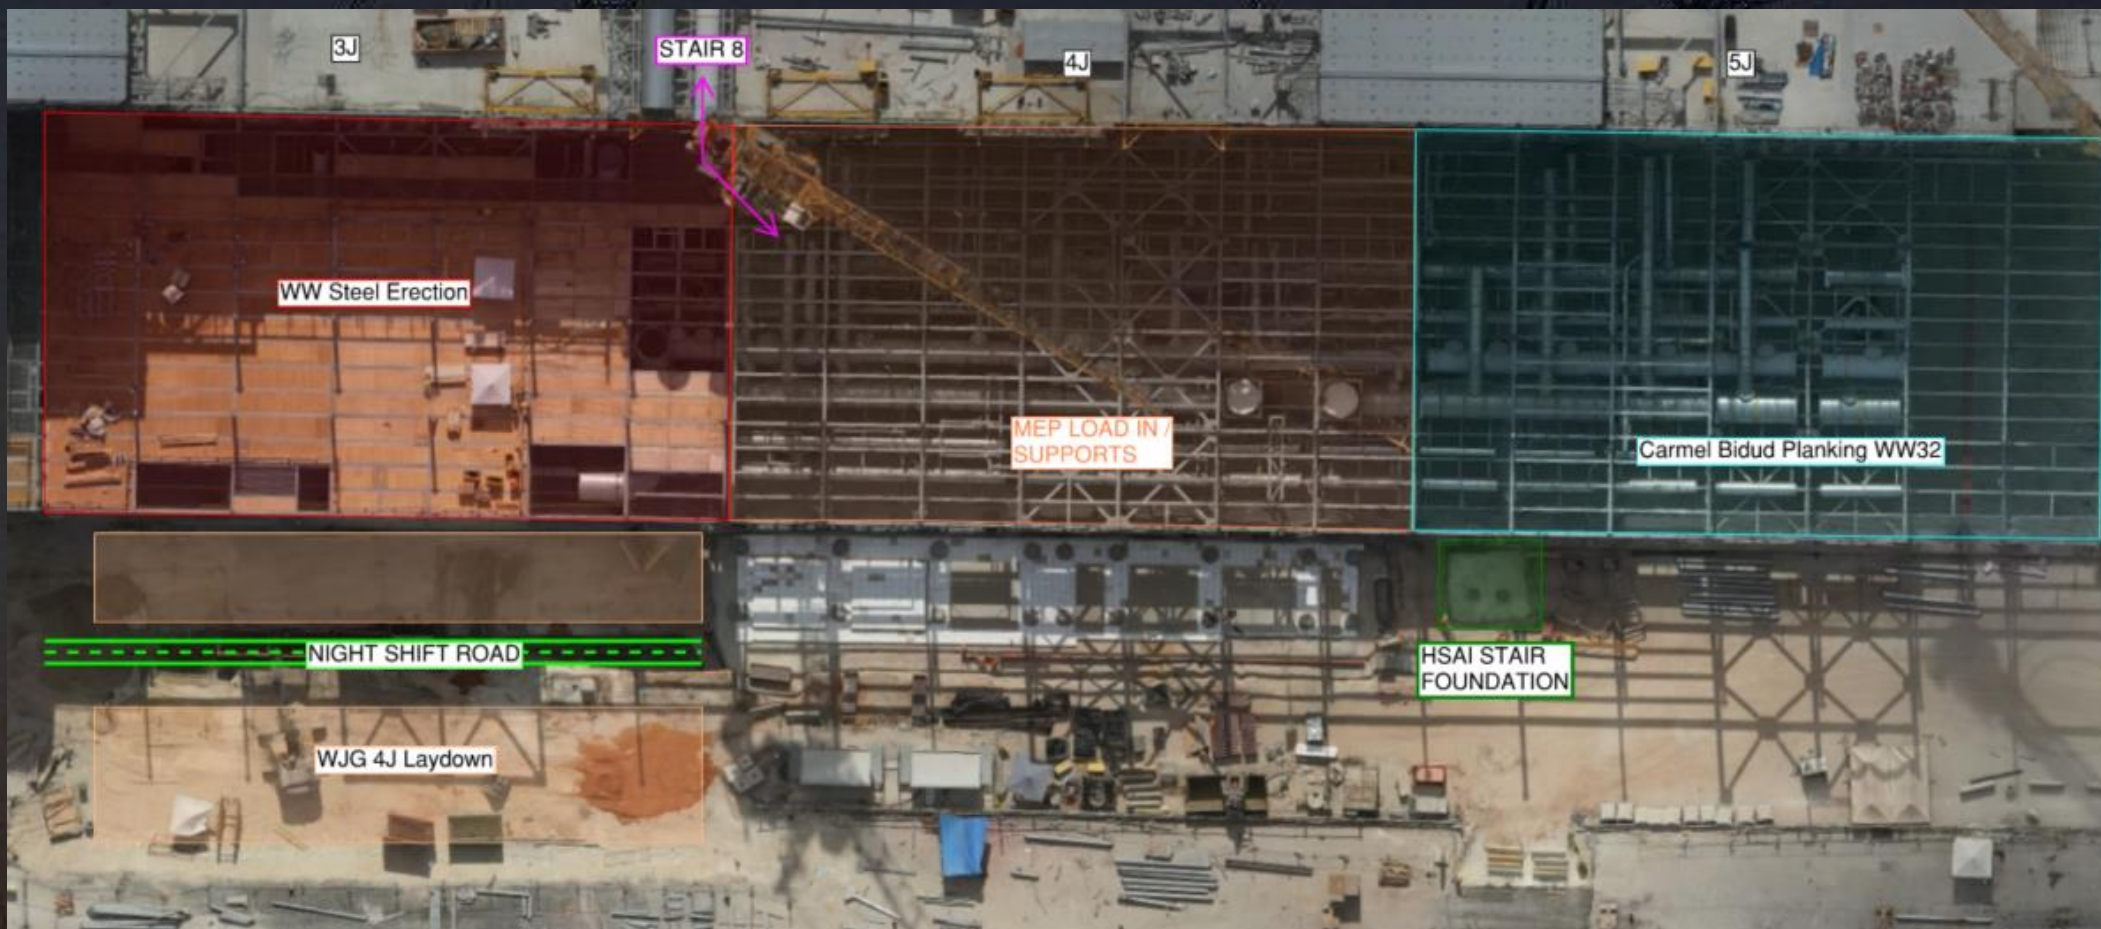

1J 2J 3J 4J 5J

EB100K02 EB100K03 EB100K04 EB100K05 EB100K06 EB100K07 EB100K08 EB100K09 EB100K10 EB100K11 EB100K12 EB100K13 EB100K14 EB100K15 EB100K16 EB100K17 EB100K18 EB100K19 EB100K20 EB100K21 EB100K22 EB100K23 EB100K24 EB100K25 EB100K26 EB100K27 EB100K28 EB100K29 EB100K30 EB100K31 EB100K32 EB100K33 EB100K34 EB100K35 EB100K36 EB100K37 EB100K38 EB100K39 EB100K40 EB100K41 EB100K42 EB100K43 EB100K44 EB100K45 EB100K46 EB100K47 EB100K48 EB100K49 EB100K50 EB100K51 EB100K52 EB100K53 EB100K54 EB100K55 EB100K56 EB100K57 EB100K58 EB100K59 EB100K60 EB100K61 EB100K62 EB100K63 EB100K64 EB100K65 EB100K66 EB100K67 EB100K68 EB100K69 EB100K70 EB100K71 EB100K72 EB100K73 EB100K74 EB100K75 EB100K76 EB100K77 EB100K78 EB100K79 EB100K80 EB100K81 EB100K82 EB100K83 EB100K84 EB100K85 EB100K86 EB100K87 EB100K88 EB100K89 EB100K90 EB100K91 EB100K92 EB100K93 EB100K94 EB100K95 EB100K96 EB100K97 EB100K98 EB100K99 EB100K100

FIRE RISER STAIR 4 WC JANITORIAL CHEM STAGING DW 2 PA LOBBY CONTRACTOR CAGE 28

EB100K03 EB100K04 EB100K05 EB100K06 EB100K07 EB100K08 EB100K09 EB100K10 EB100K11 EB100K12 EB100K13 EB100K14 EB100K15 EB100K16 EB100K17 EB100K18 EB100K19 EB100K20 EB100K21 EB100K22 EB100K23 EB100K24 EB100K25 EB100K26 EB100K27 EB100K28 EB100K29 EB100K30 EB100K31 EB100K32 EB100K33 EB100K34 EB100K35 EB100K36 EB100K37 EB100K38 EB100K39 EB100K40 EB100K41 EB100K42 EB100K43 EB100K44 EB100K45 EB100K46 EB100K47 EB100K48 EB100K49 EB100K50 EB100K51 EB100K52 EB100K53 EB100K54 EB100K55 EB100K56 EB100K57 EB100K58 EB100K59 EB100K60 EB100K61 EB100K62 EB100K63 EB100K64 EB100K65 EB100K66 EB100K67 EB100K68 EB100K69 EB100K70 EB100K71 EB100K72 EB100K73 EB100K74 EB100K75 EB100K76 EB100K77 EB100K78 EB100K79 EB100K80 EB100K81 EB100K82 EB100K83 EB100K84 EB100K85 EB100K86 EB100K87 EB100K88 EB100K89 EB100K90 EB100K91 EB100K92 EB100K93 EB100K94 EB100K95 EB100K96 EB100K97 EB100K98 EB100K99 EB100K100

Area Closed for Topping Slab 04/08 - 15/08

Carmel Bidud - Ductwork
Meptagon - High & Tight
SKE - DW/ CD Install


Afcon - MV Cable Pulling
SKE - DW/ CD Install

Carmel Bidud - Ductwork
Lesico NG Pipe Install (Fit Up +Welding)
Afcon Cable Tray Install


Chemo - Pipe Install


Chemo - Pipe Install



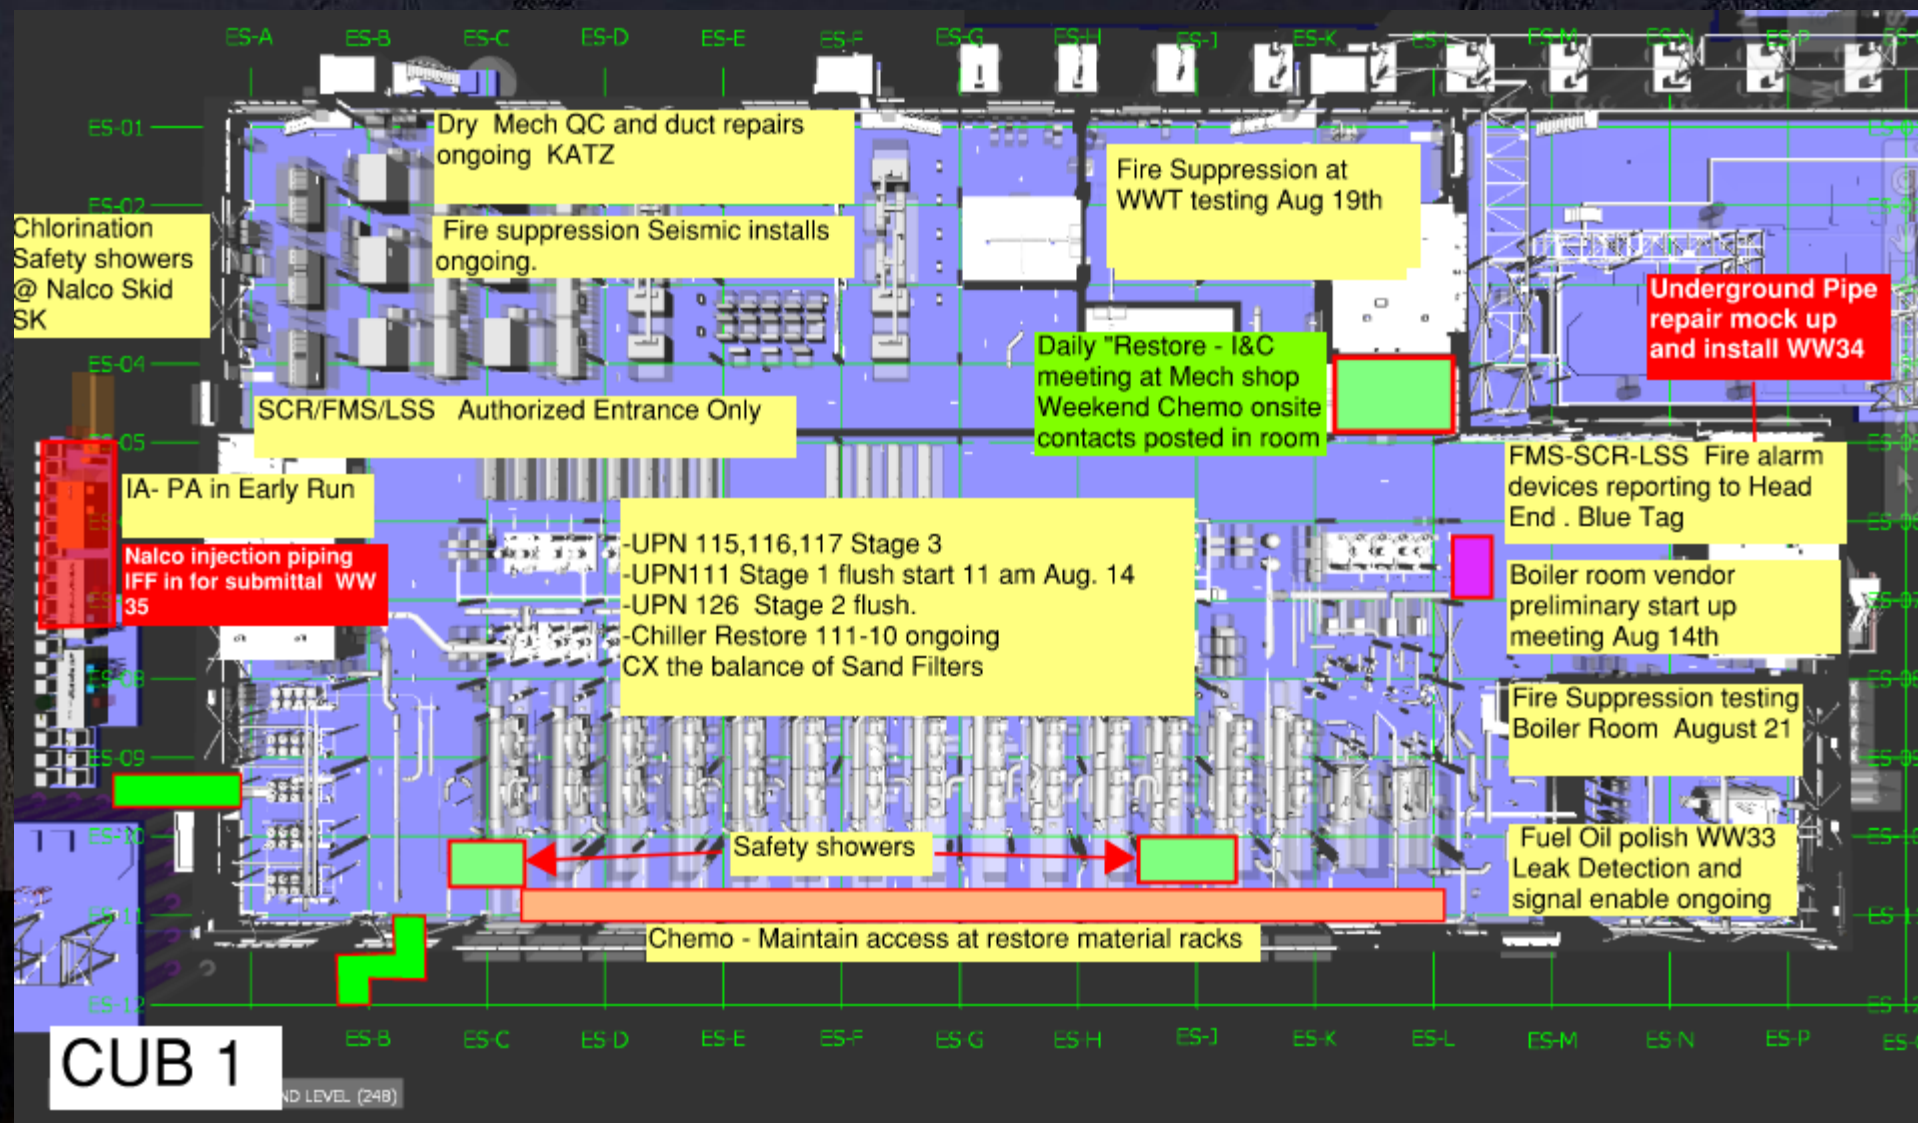



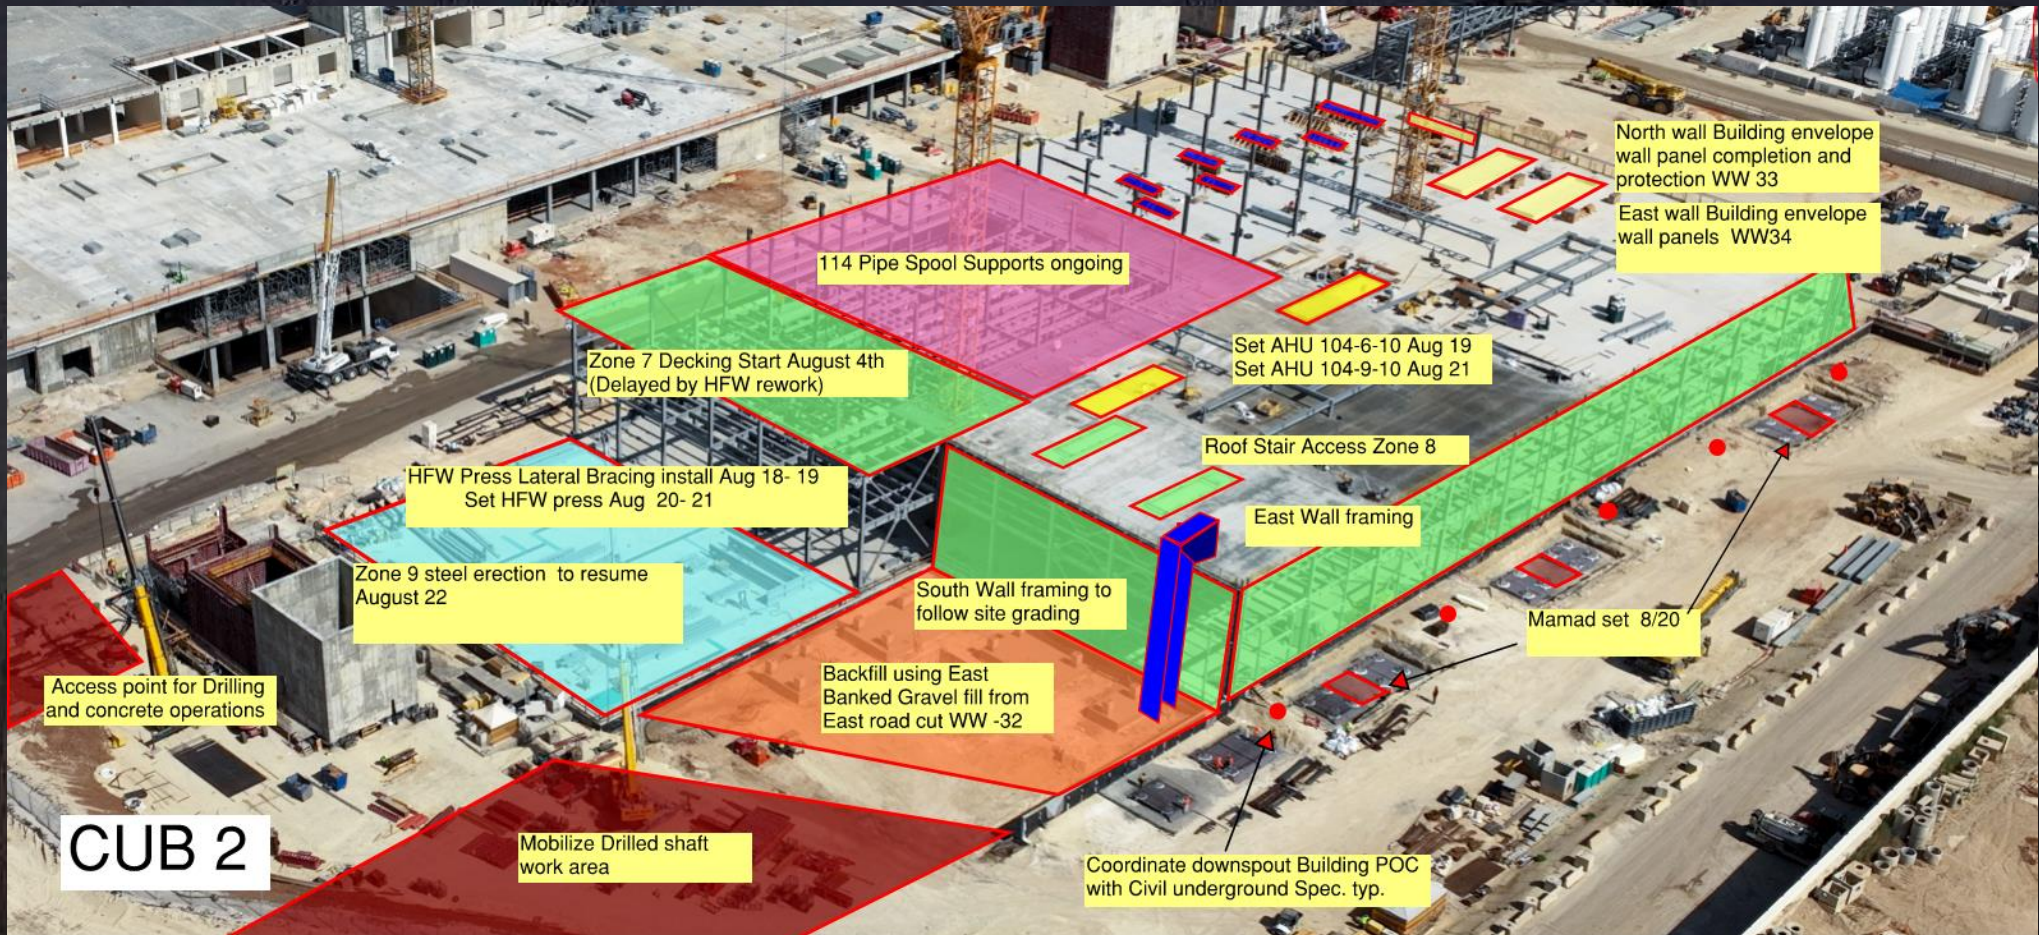

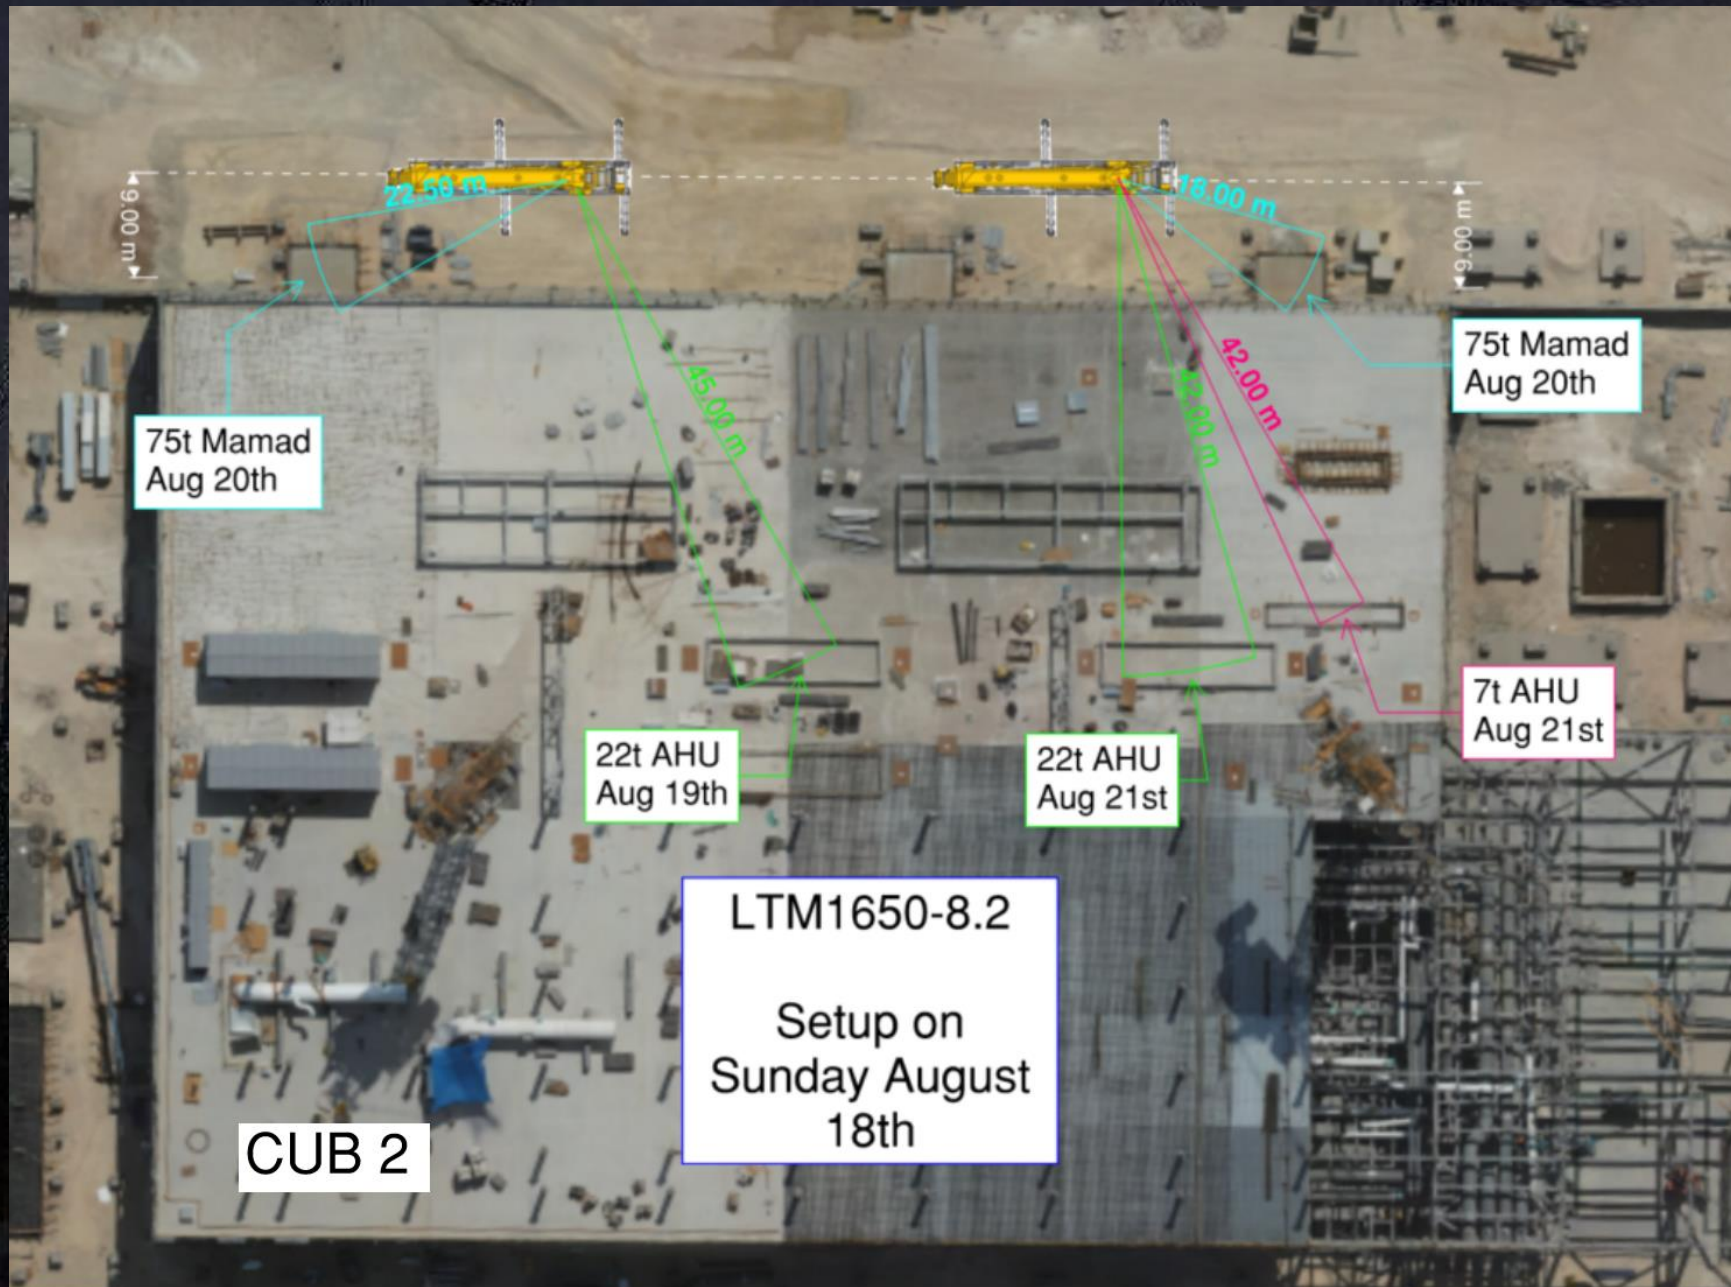

Elmor-
AIS Term control cables
SES- Megger test for MV cables
SES & AIS pulling & term control cables &
Trustle- instal EMT & pull cables for PTZ cam


BYNET- SES & AIS
Laibling & prep for GT

NO ENTRY
HV ENERGIZED AREA

TMT
Z 8 vac truck soil replacement
sealing - sewage manholes

approved sipps
Start Blue fence relocate on sunday
IDP, TMT & MEP SEC


Siemens / Pach Taas
SES & Lvss- E.F instal

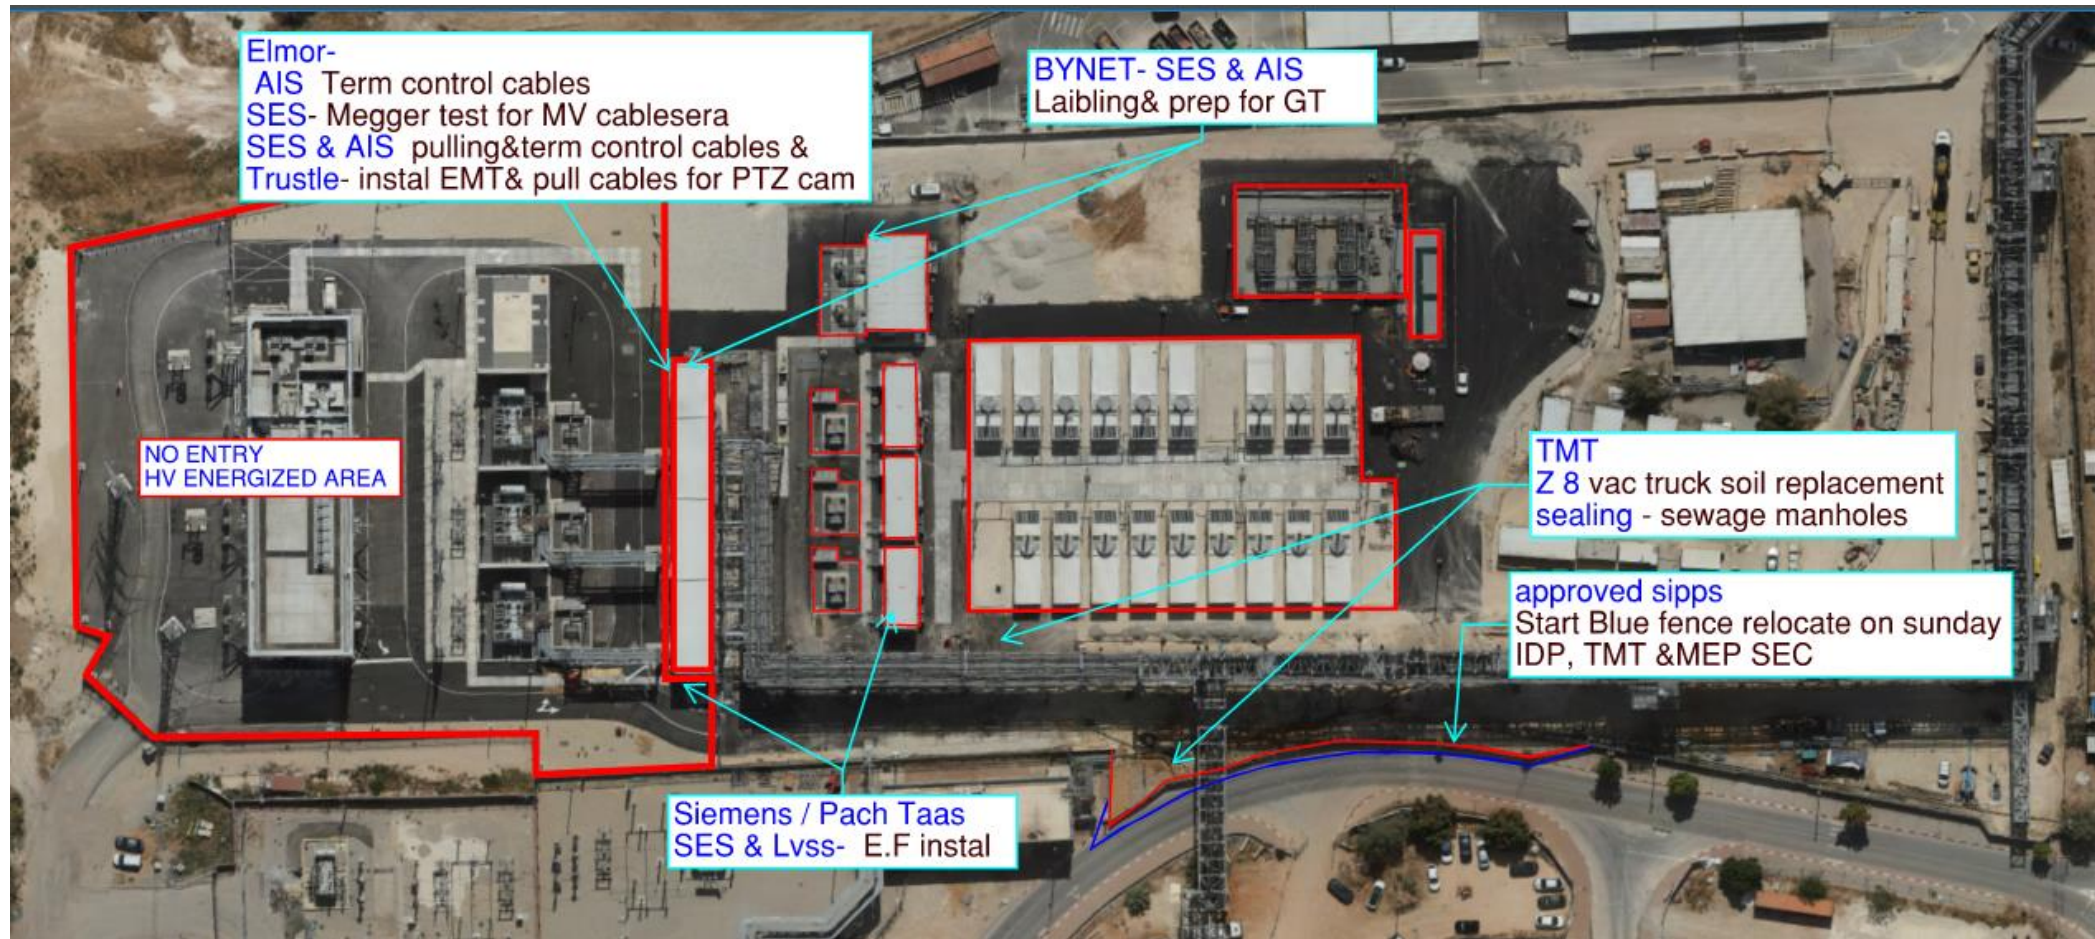



Trestle - MOD 2 Steel erection

T-17 Lvl 1

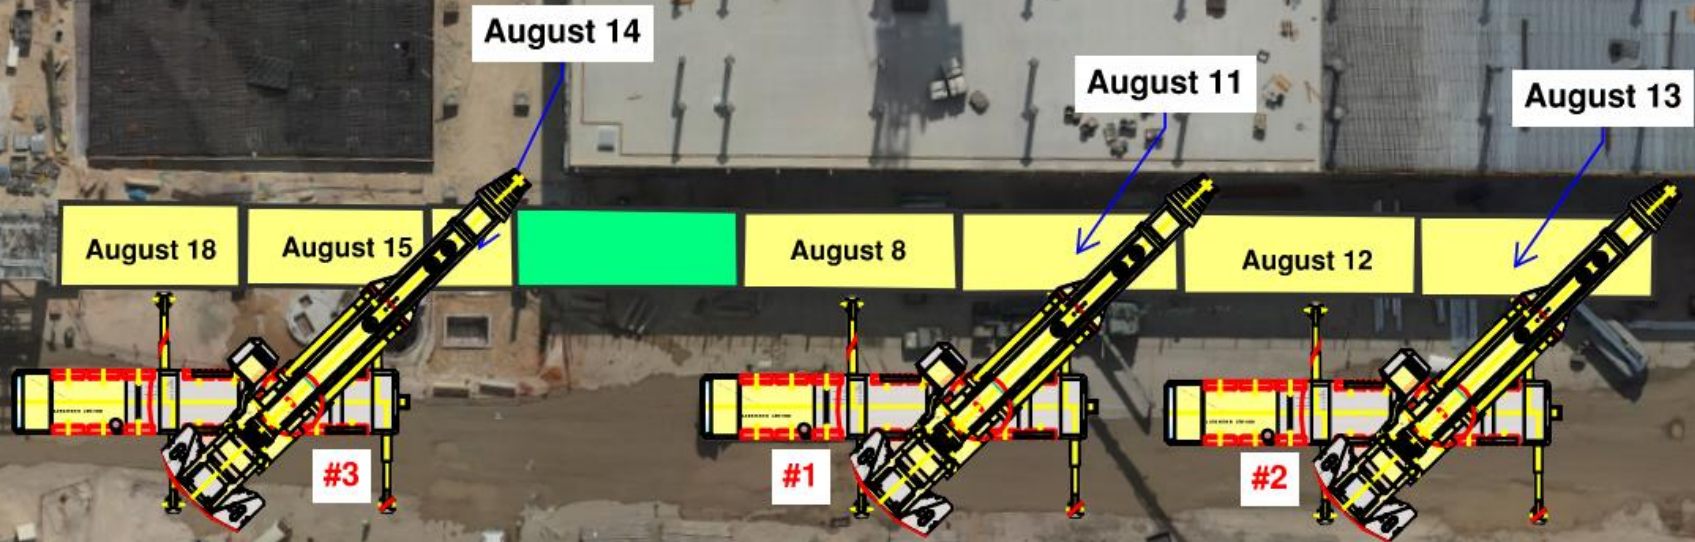

Trestle - MOD 2 Steel erection

T-17 Lvl 2

August 19

August 25

August 27

August 21

August 20


August 22

August 26

#1

#2

#3

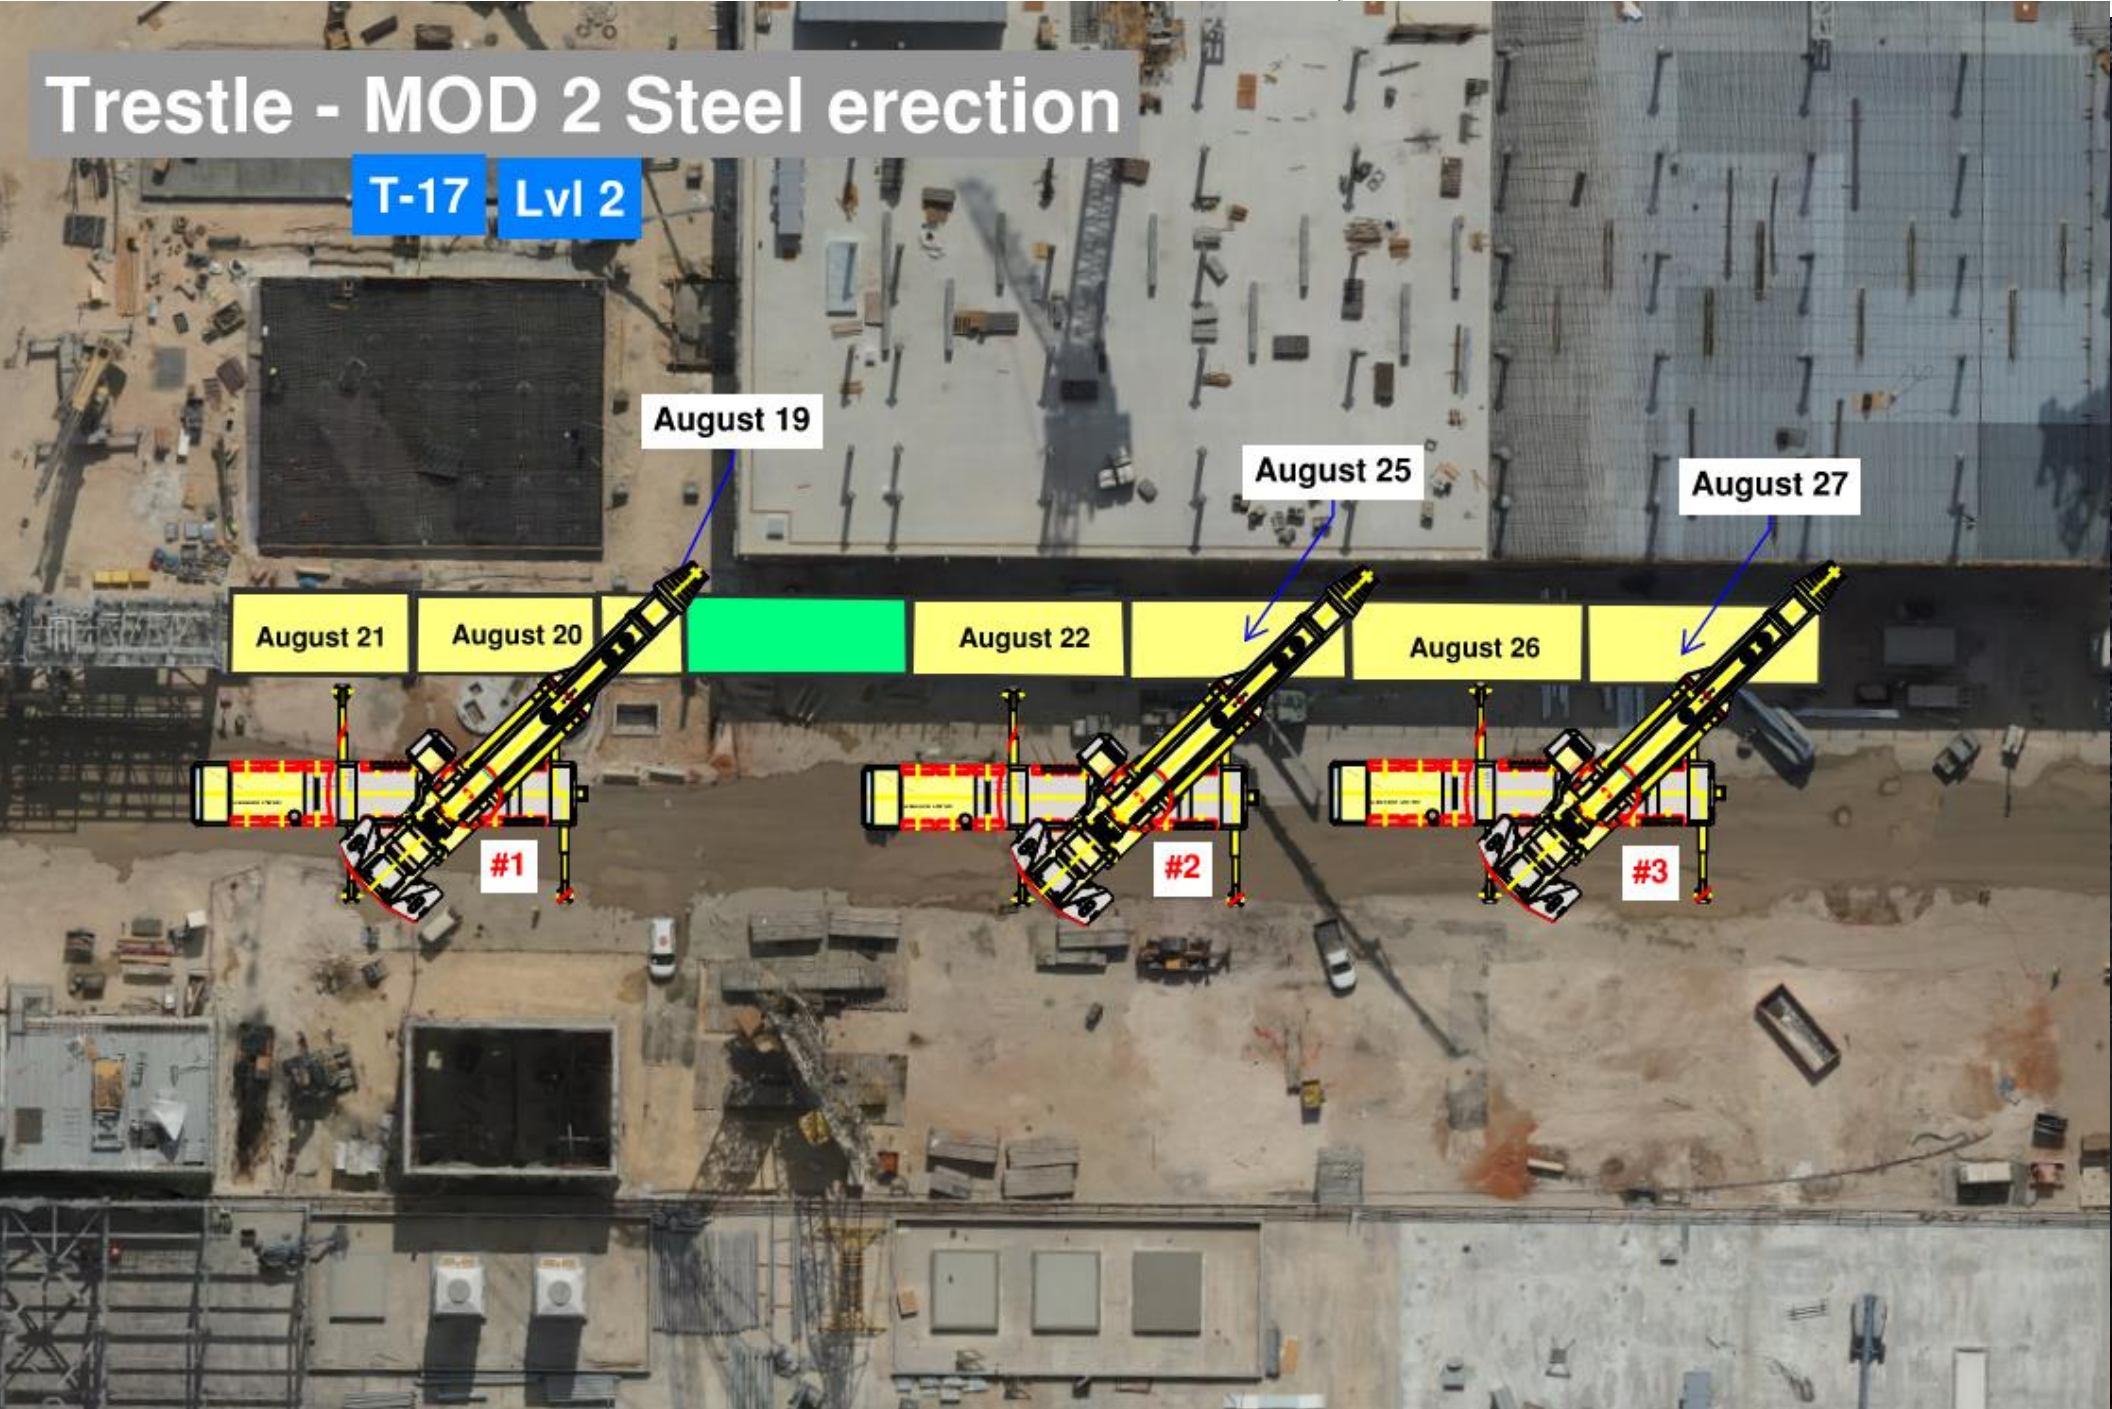

BSGS




TRESTLE

Lesico 12" natural gas pipe pressure test exclusion zone


Wednesday, August 21st 1800 -Thursday, Aug 22nd 0100



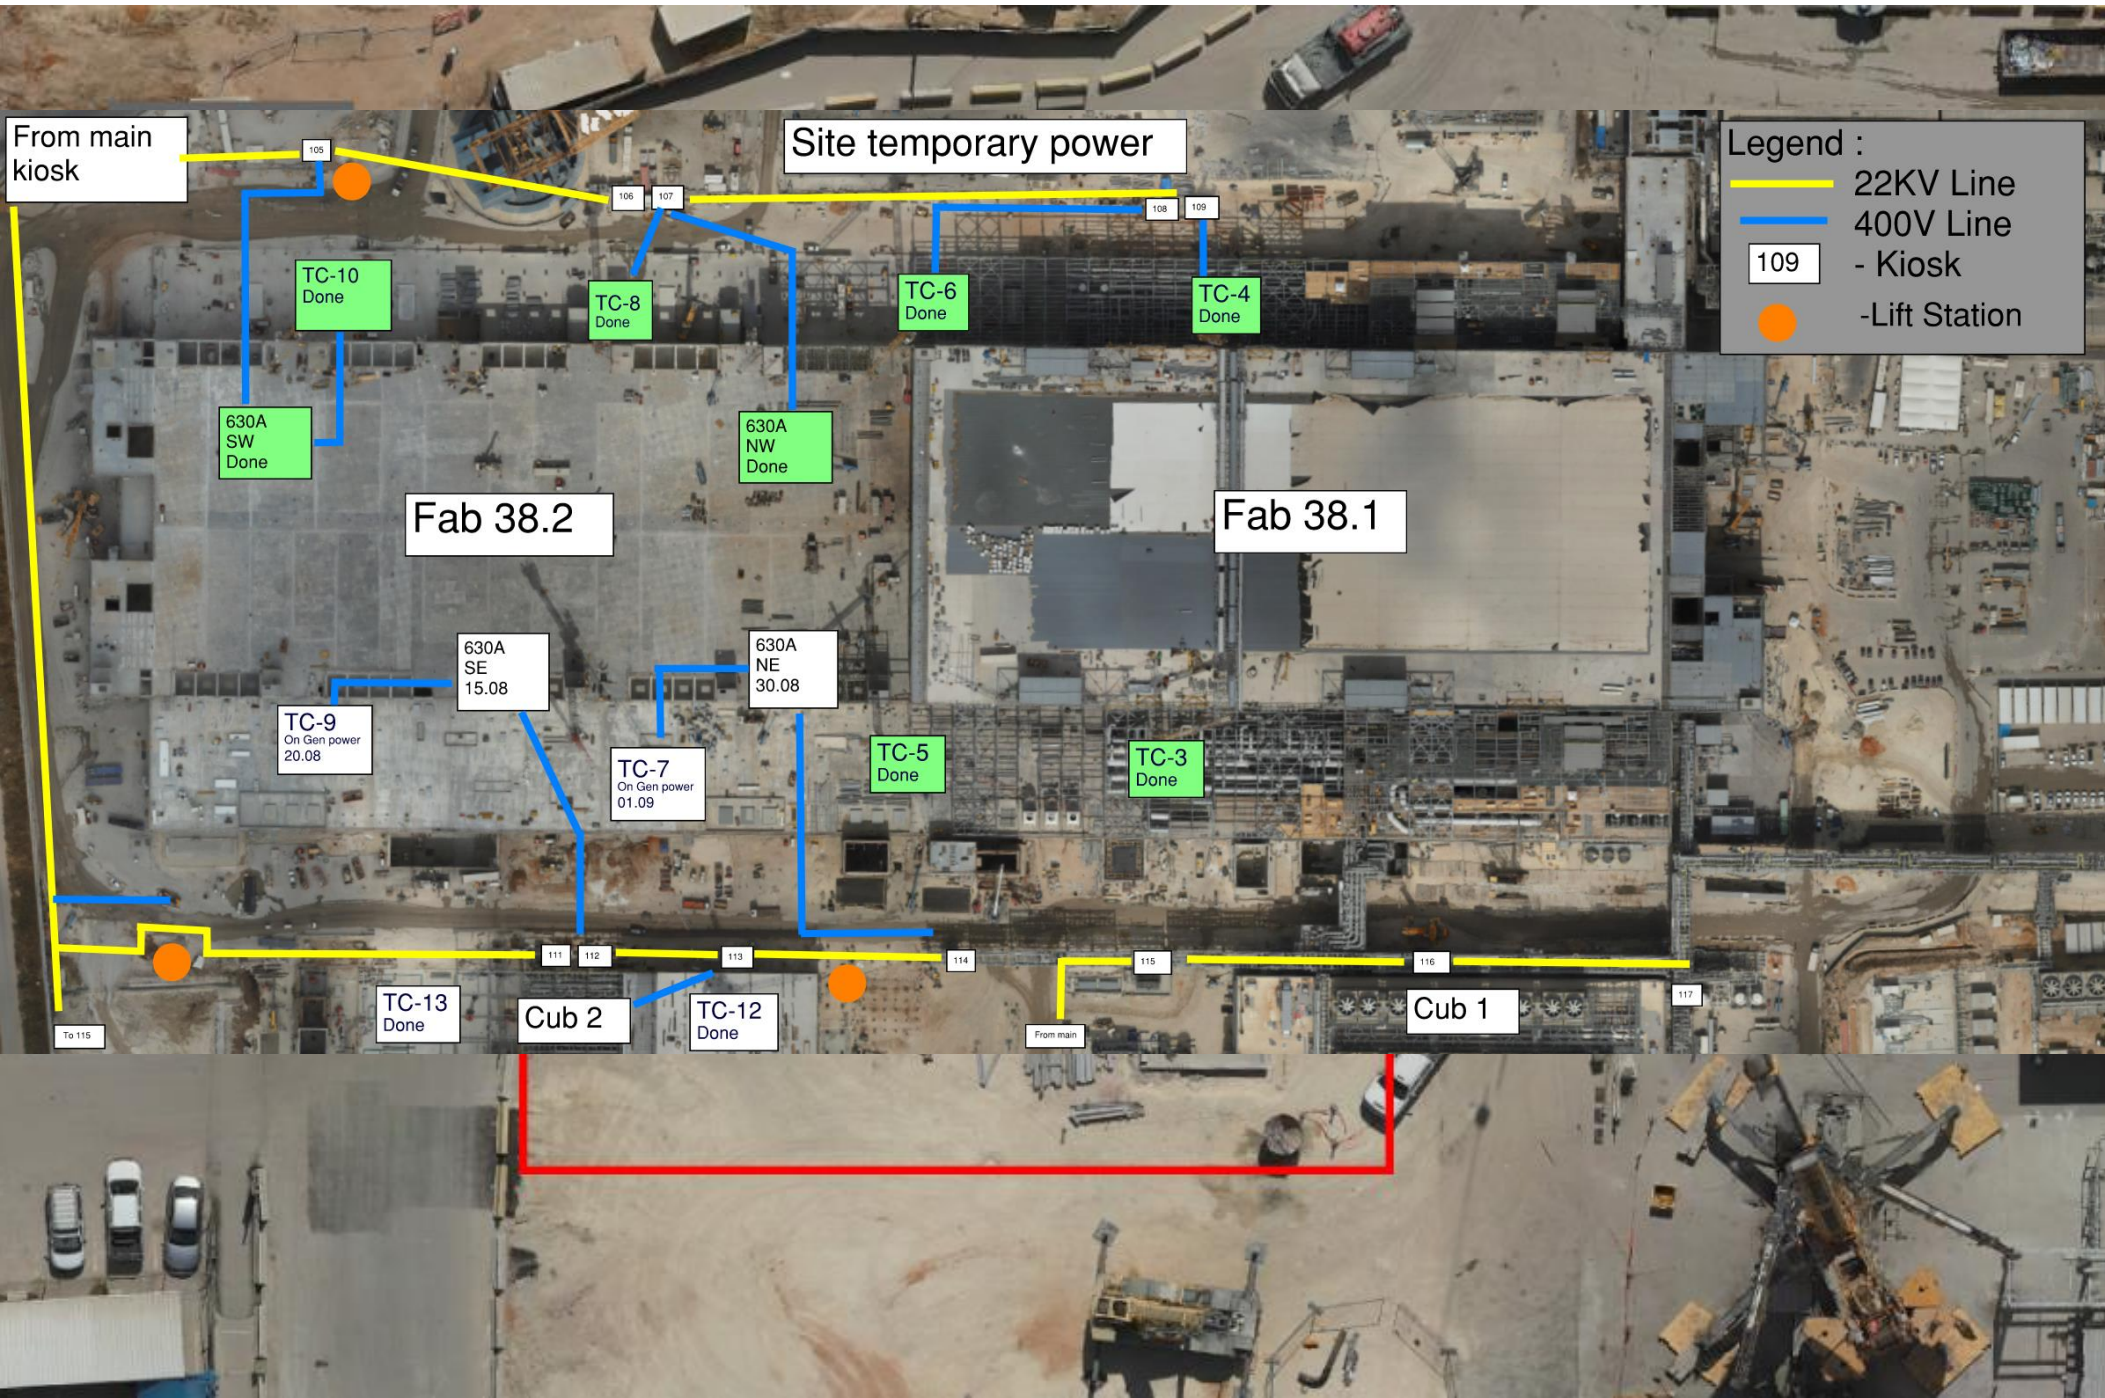

Daily Coordination Meeting


Site Logistics
North Gate B

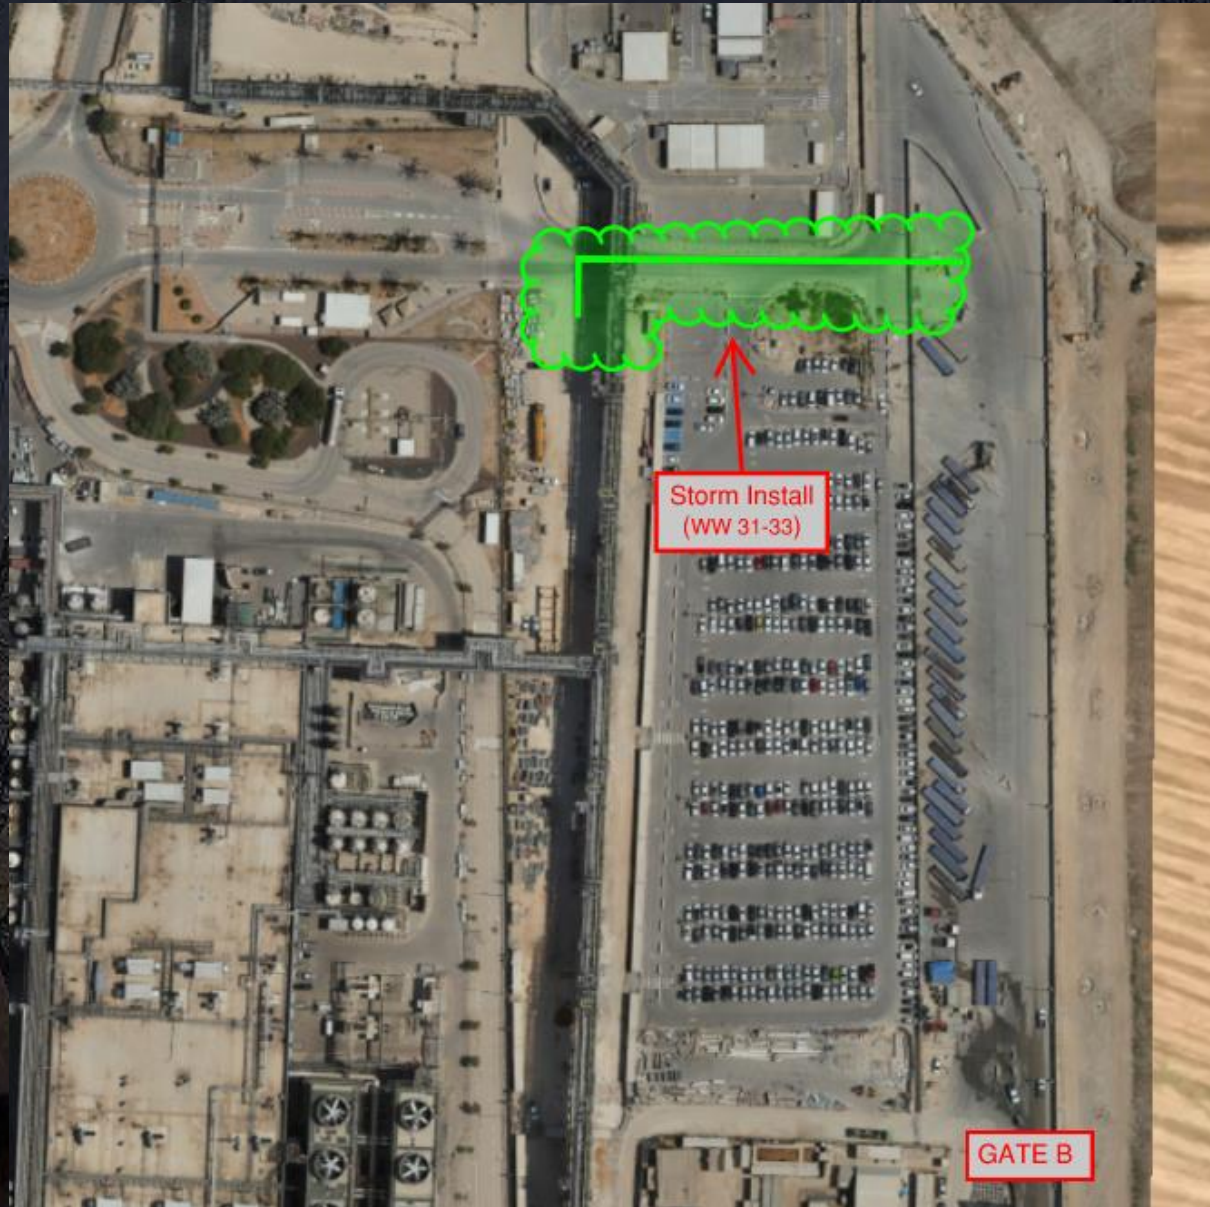

Daily Coordination Meeting

Site Logistics


Traffic Plan

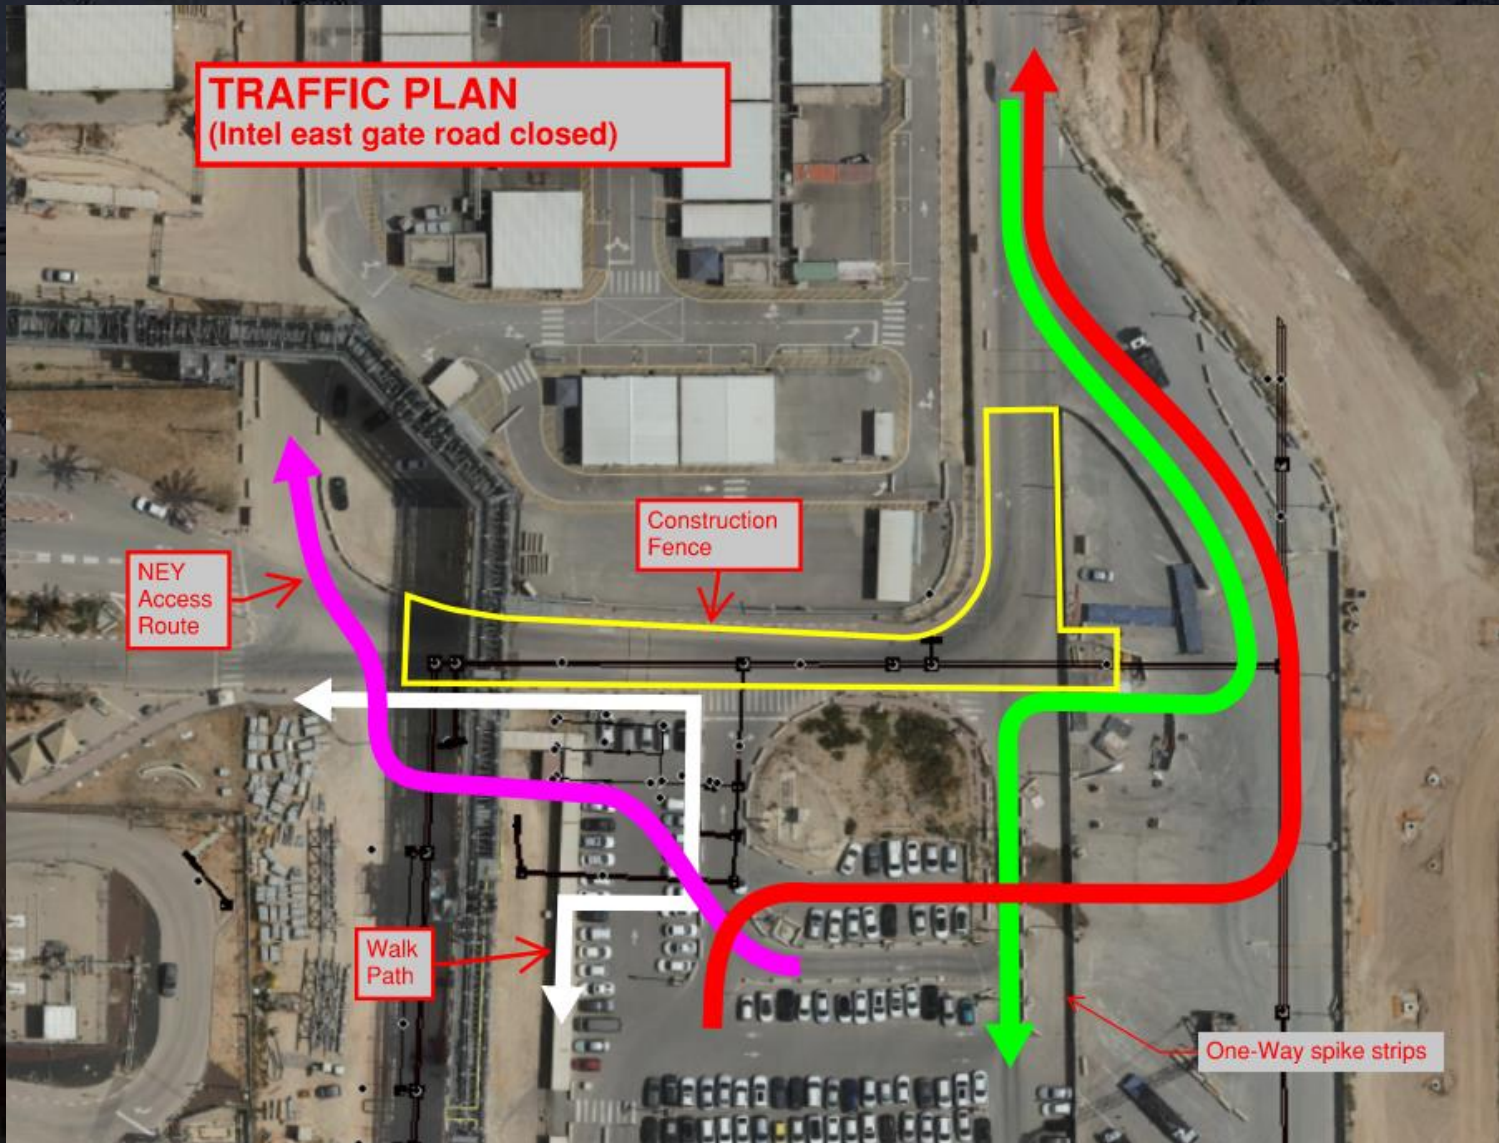

Daily Coordination Meeting

Site Logistics

North

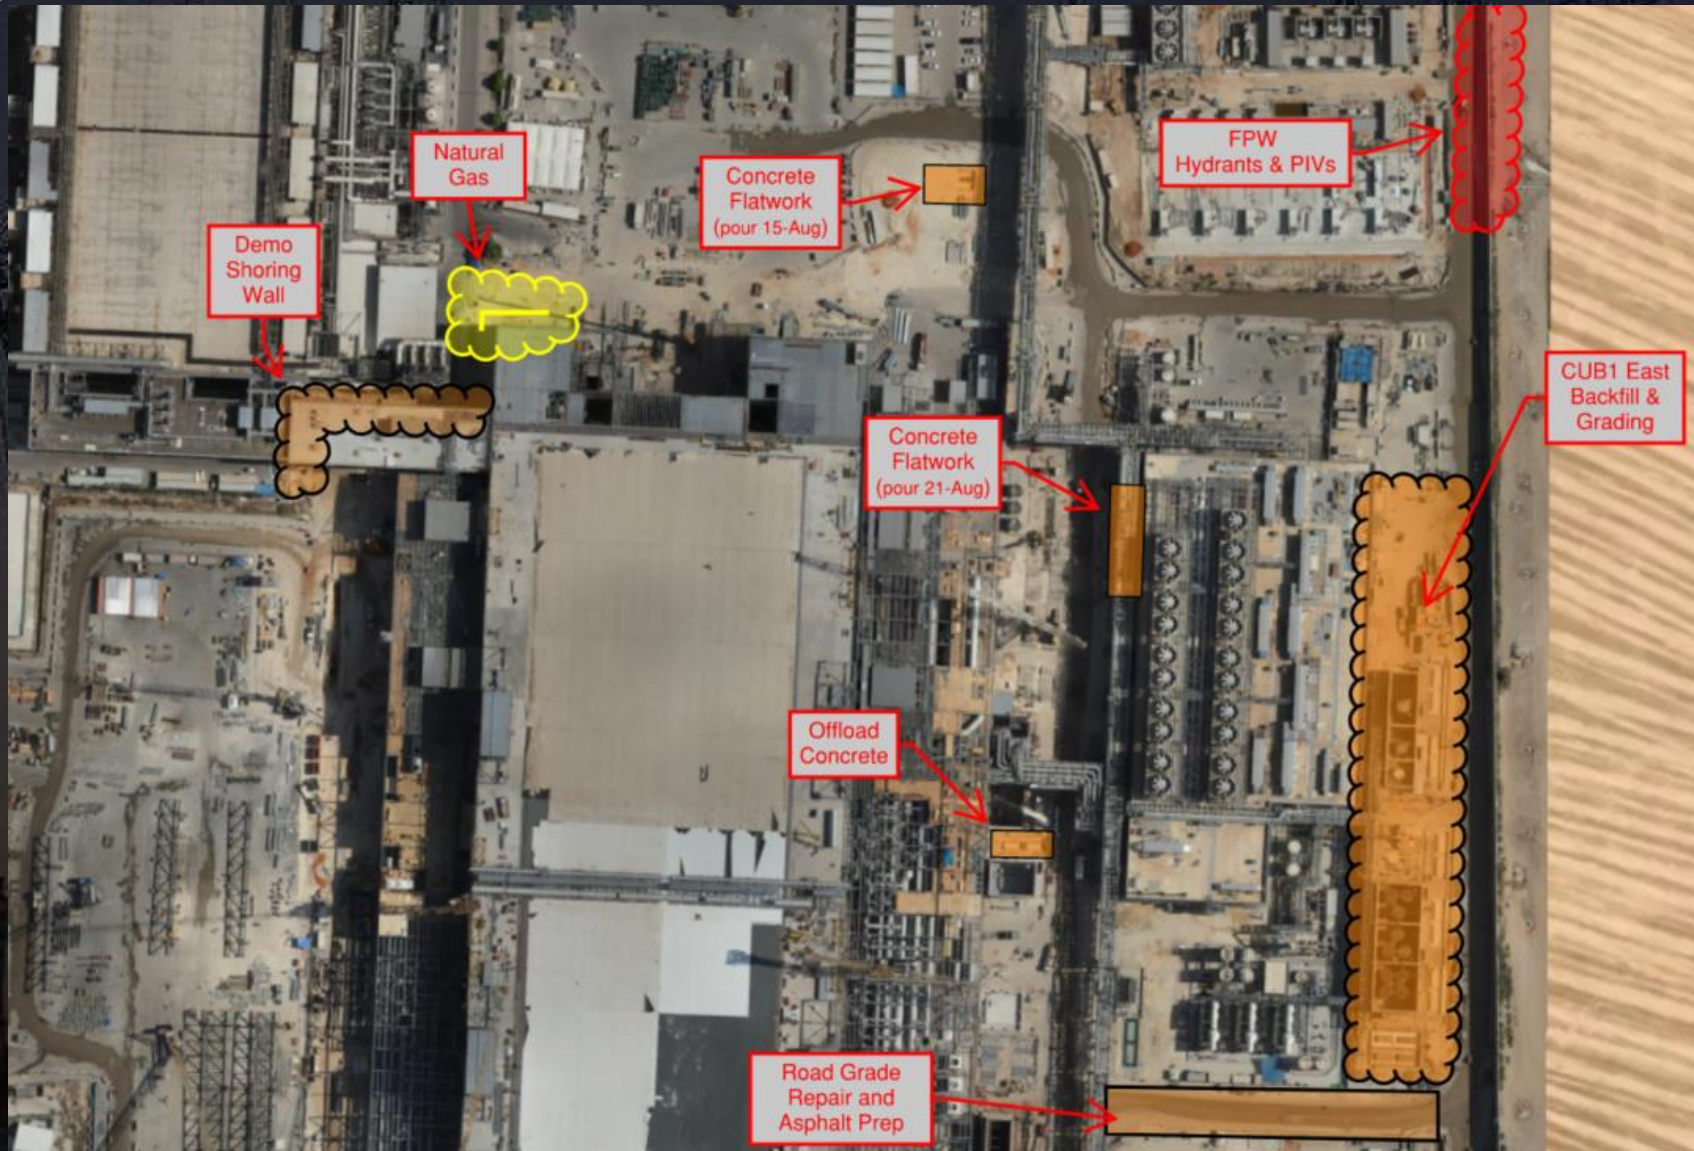

Daily Coordination Meeting

Site Logistics


South




Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

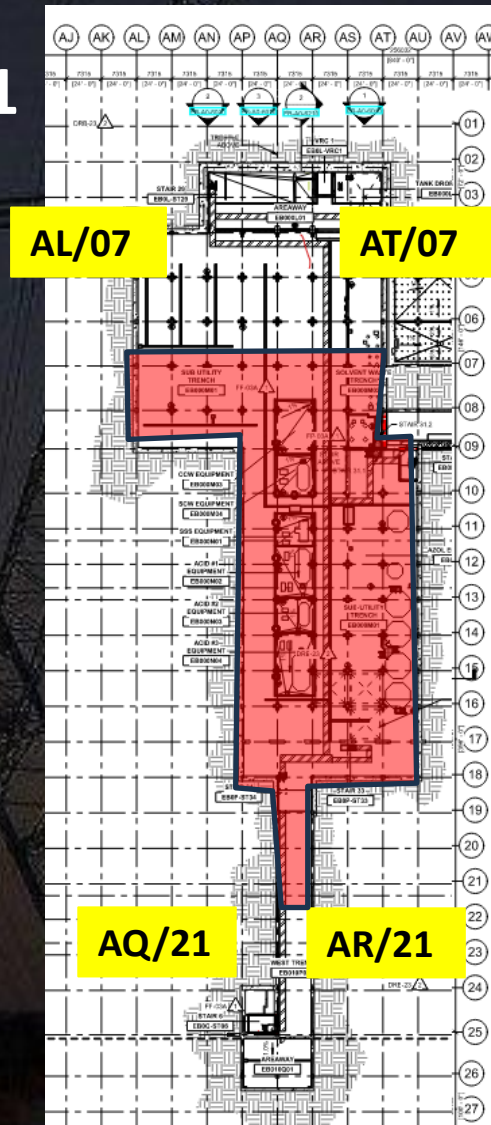


SUT2

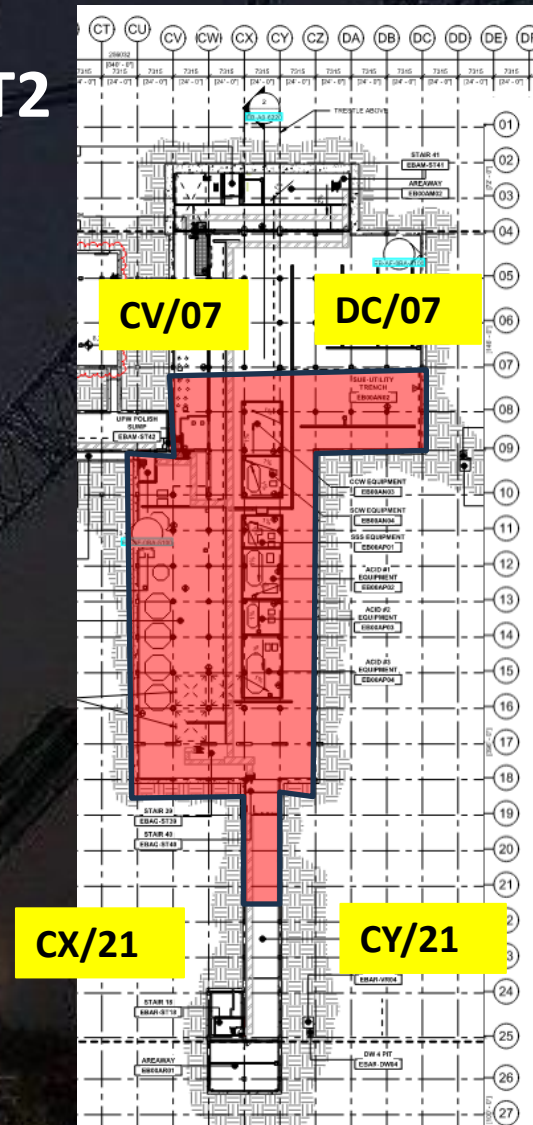

Daily Coordination Meeting


Site Logistics - Protected Areas (Utility Level)

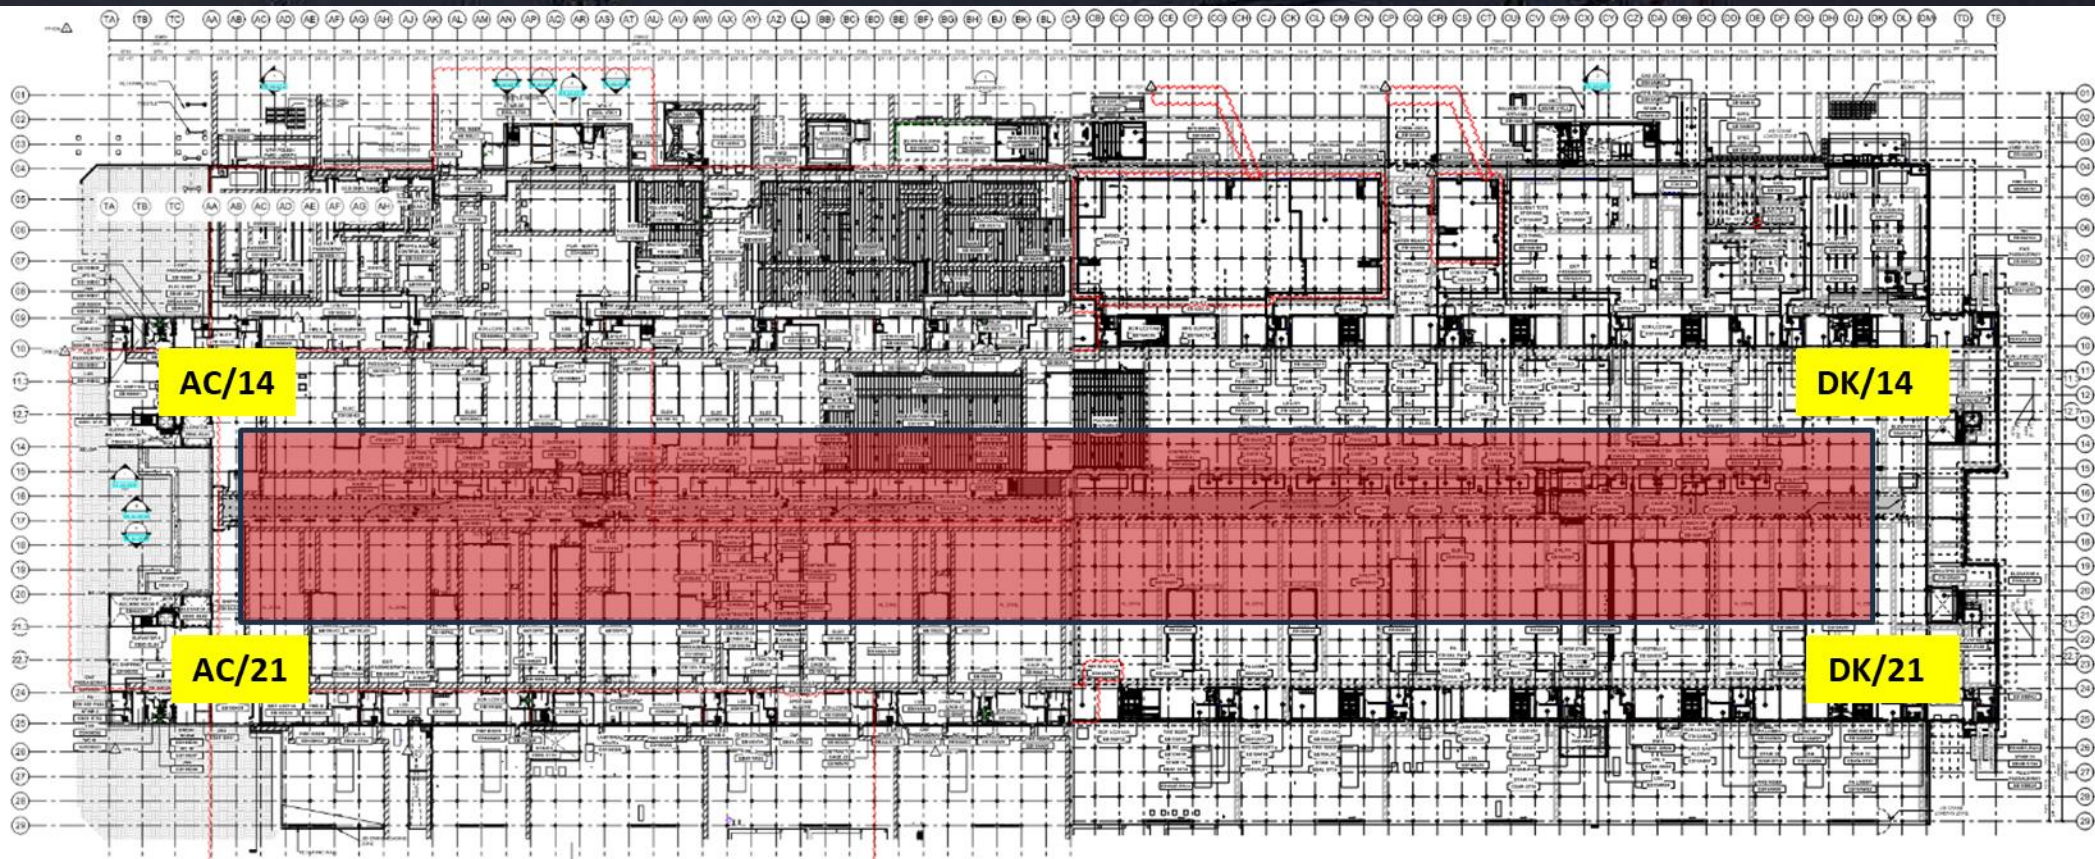



Daily Coordination Meeting


Site Logistics - Protected Areas (Subfab Level)

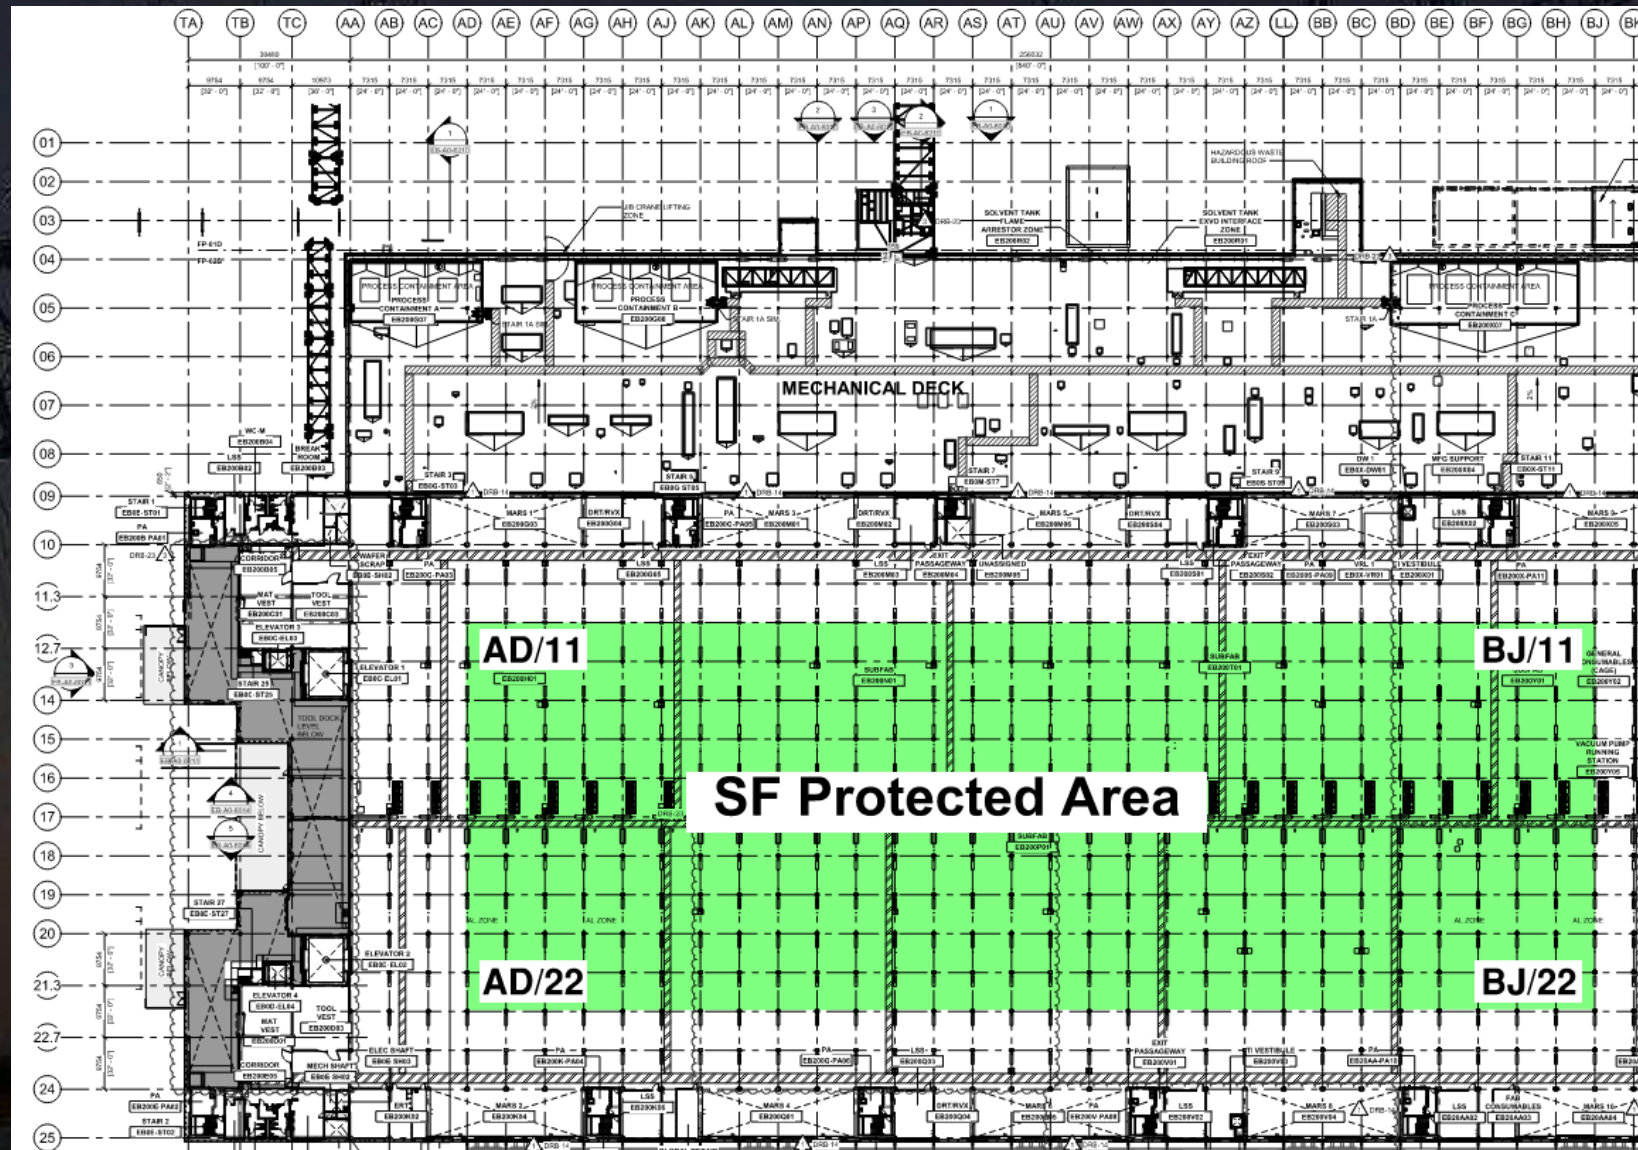

Daily Coordination Meeting

Site Logistics


Protected Areas

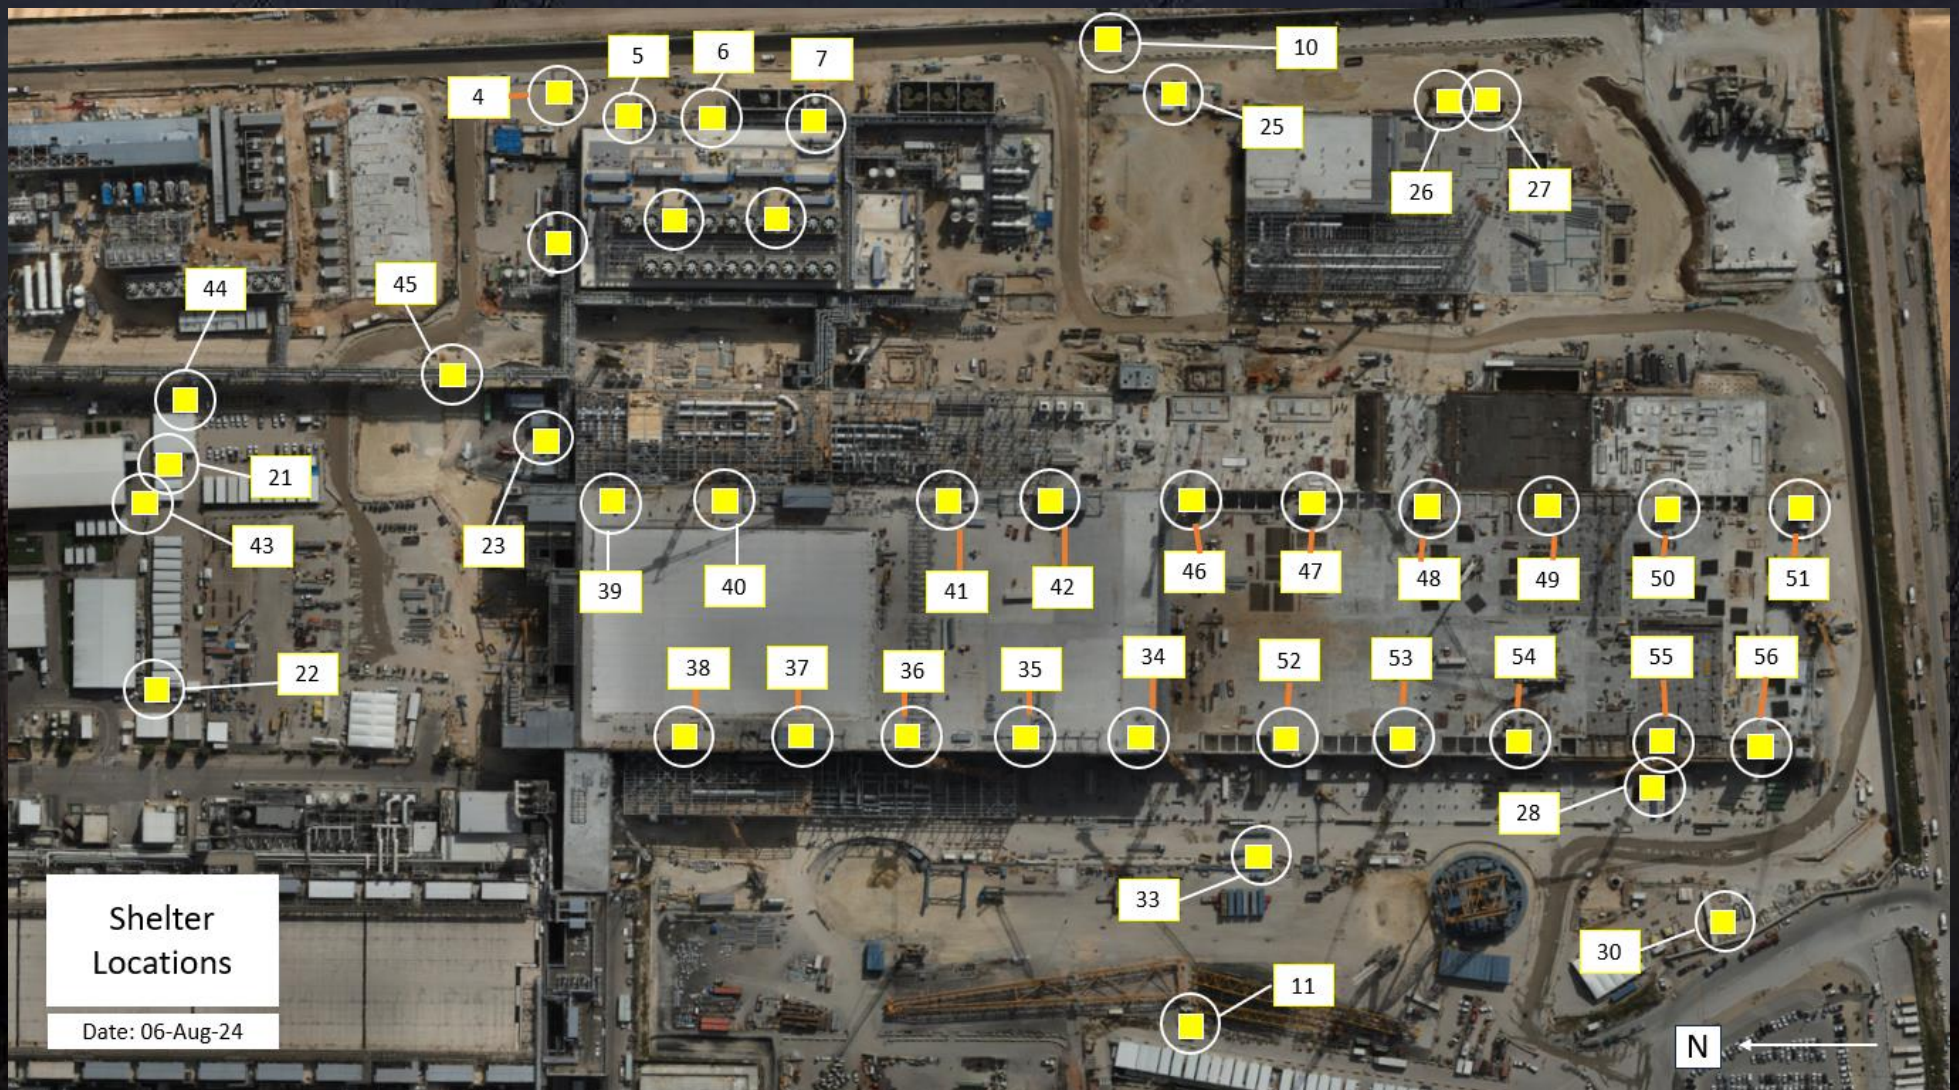

Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

BF (1) AT GIS

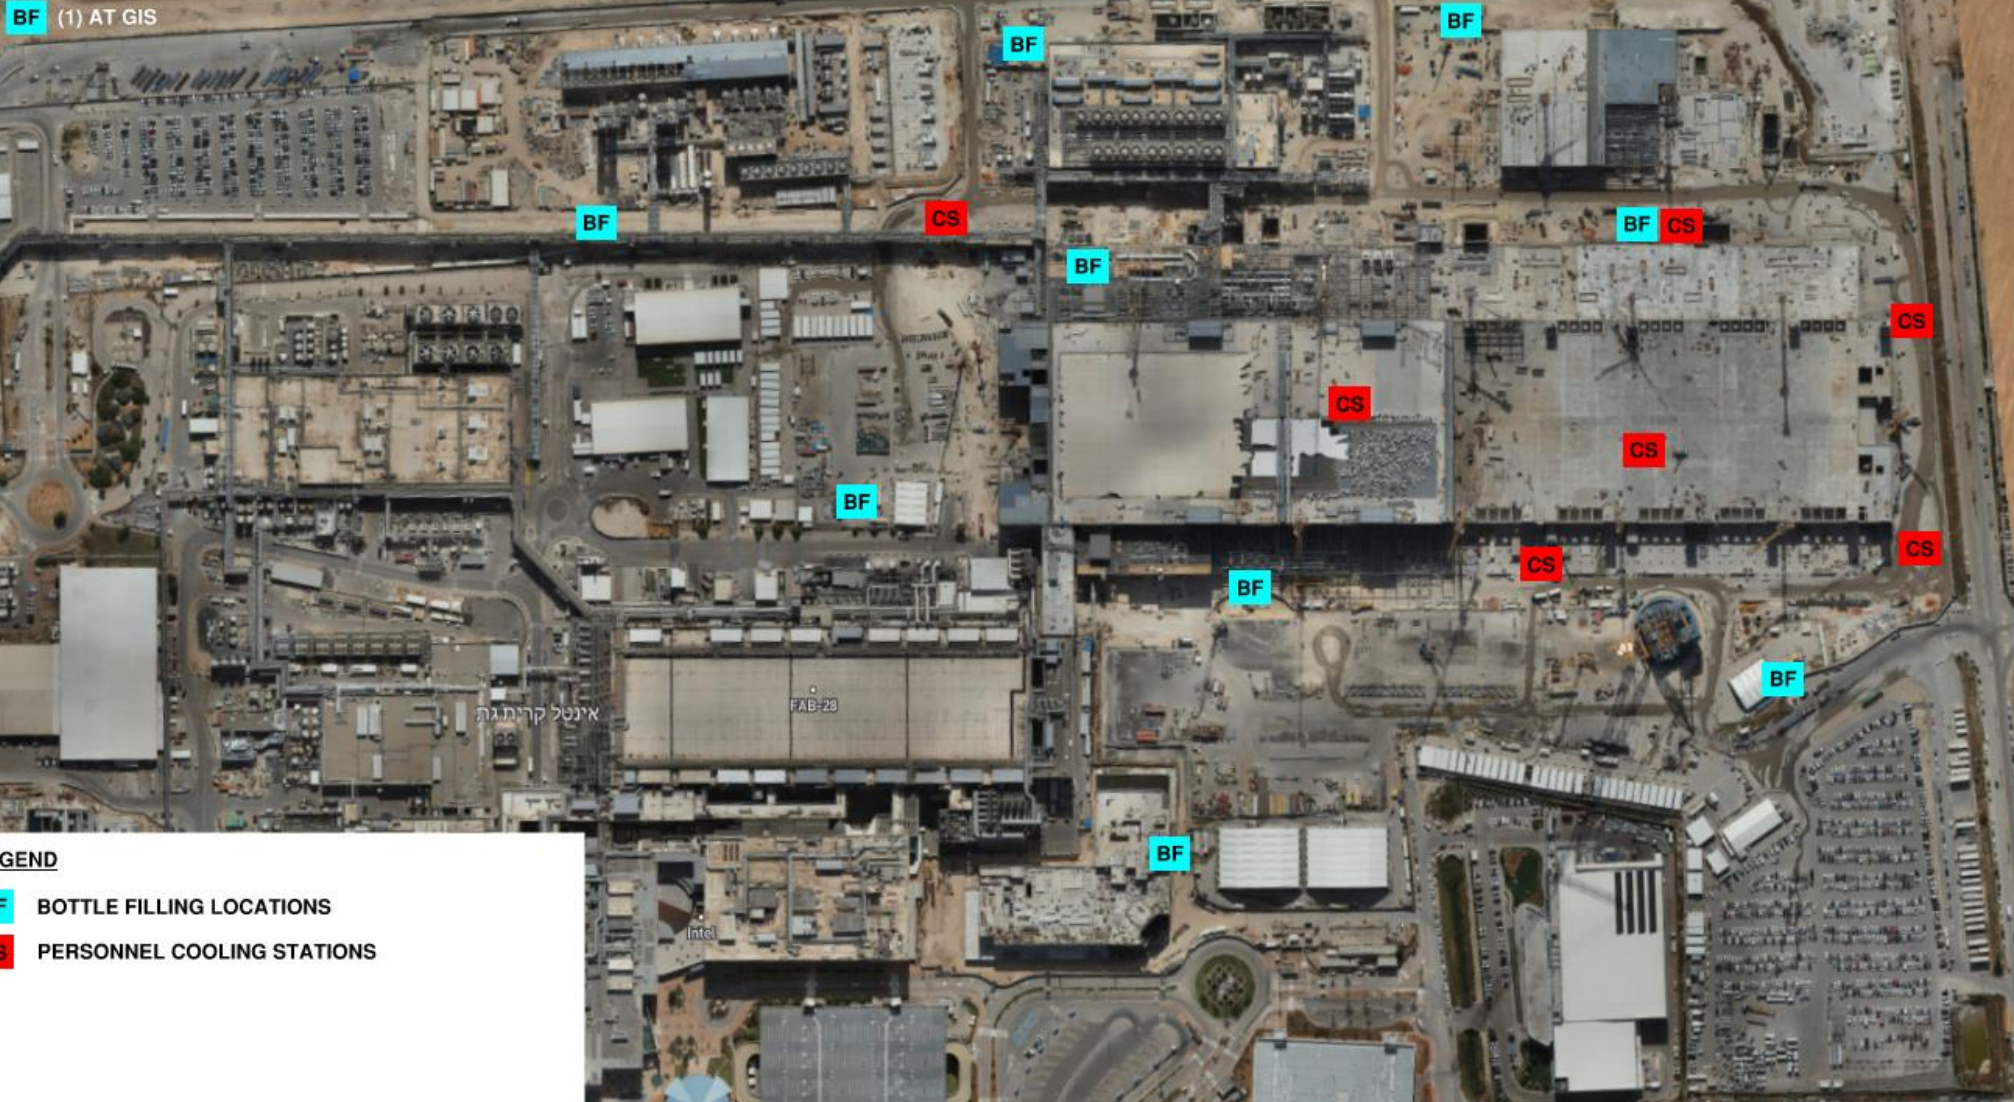

Deep Cleaning of Break Tent B on Friday 16th Aug



LOF Injuries

- Today we had another line of fire injury. An employee was holding something with one hand and hammering on it with the other when they hit their thumb. Now, this is common and many of us have done the same at work or at home.
- However, there are better ways. This employee easily could have held the object with pliers, secured it with clamps, etc. to ensure that they could perform their work without risk to their fingers.
- Common practices aren't always the best practices. We need to ensure we are actually taking steps to set our workers up to do their work as safely as possible and coaching them when we see them doing something that could be performed safer.

Stop and Think– We've Got the Power

Subs that **HAVE NOT** completed a
Stop and Think



Afcon Control and Automation
Atkor
Avi Cranes
Belfor
Binyan Haretz
EL Fire Proof
Electra
Elram
ETC system
Siemens Industrial
Skyline Cranes & Technologies



Complete 1 per day



Stop and Think- We've Got the Power

Company	Number Expected	Number Completed	Percent
Oriyan	4	15	375%
Tzur Esh Projects	4	10	250%
Rehatot Be'er Sheva	4	8	200%
Pach Taas	16	28	175%
Stage Design	4	7	175%
D&P Clean Room	4	6	150%
Other	4	6	150%
ByNet System Application	4	5	125%
ElectroSafe	4	5	125%
Malchimim Badarom	8	9	113%
Brand Industrial	4	4	100%
Derech Afar	4	4	100%
SIG Industrial	4	4	100%
Talad T.S	4	4	100%
DVIR.IE	4	3	75%
ES Entry Systems	4	3	75%
HYG Steel	4	3	75%
IDP/Sela	4	3	75%
Meptagon I&C	4	3	75%
Newco-Tech	4	3	75%
Rolling Plains Construction Inc	4	3	75%

Company	Number Expected	Number Completed	Percent
SK Engineering and Project	8	5	63%
HSAL	12	7	58%
Air Products	4	2	50%
El-Mor Electric	4	2	50%
HLM	4	2	50%
Meptagon	4	2	50%
Olitzki	4	2	50%
Ranpro	4	2	50%
TM TEAM	4	2	50%
TM TEAM - Job service	8	4	50%
Sami Najami Engineering & Project	32	12	38%
Chemo Aharon	40	14	35%
Belfor	4	1	26%
A.S. Barzel	8	2	25%
Afcon Control and Automation	4	1	25%
Atkor	4	1	25%
Avi Cranes	4	1	25%
BCT Pipeline Processes	12	3	25%
Binyan Haertz	4	1	25%
EL Fire Proof	4	1	25%
Electra	4	1	25%
Elram	4	1	25%
ETC System	4	1	25%
Lesico	12	3	25%
Megason Electric	4	1	25%
Siemens Industrial	4	1	25%
Skyline	4	1	25%
W&W - AFCO Steel LLC	4	1	25%
Carmel Bidud	24	4	17%
Katz Arie Stainless Steel	16	2	13%
Shuv Eli Electric Engineering	8	1	13%
Afcon Contracting Services	42	5	12%
Combe	24	2	8%

Stop and Think- We've Got the Power

Stand Out Individuals from Subcontractors

Shimshon Yosef	9	Tzur Esh
David Tordjman	8	Reshatot Be'er Sheva
Adib Farag	7	Pach Taas
Michael Ben Mocha	7	Oriayan
Vadim Kirichenko	6	Pach Taas



Thank you!!

Heat Index- August 18th

	temperature (°F)																
	80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110	
Relative Humidity (%)	40	80	81	83	85	88	91	94	97	101	105	109	114	119	124	130	136
	45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137	
	50	81	83	85	88	91	95	99	103	108	113	118	124	131	137		
	55	81	84	86	89	93	97	101	106	112	117	124	130	137			
	60	82	84	88	91	95	100	105	110	116	123	129	137				
	65	82	85	89	93	98	103	108	114	121	128	136					
	70	83	86	90	95	100	105	112	119	126	134						
	75	84	88	92	97	103	109	116	124	132							
	80	84	89	94	100	106	113	121	129								
	85	85	90	96	102	110	117	126	135								
	90	86	91	98	105	113	122	131									
	95	86	93	100	108	117	127										
	100	87	95	103	112	121	132										

Caution

Extreme Caution

Danger

Extreme Danger

Extreme Caution Bordering on Danger

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress
- Additional water breaks mandated. (Can be in work area)
- Increased rotation and monitoring of workers and area conditions.

With this jump in temperature after a weekend we need to hit the hydration early and start the hourly checks of workers and increased breaks earlier than normal.

HCC/EHS Weekend Work- 16.08.2024

White Board Meeting in Beavers at 06:30

Superintendents

- Shelby Standefer 052-3440752
- Husein Abu Hammad 052-4106872
- Shimon Simo Ben Shetrit 052-5952059

CSA CM

- Konstantyn (Kosta) Povetkin 052-2124018
- Leonid Khomich 053-2722138

MEP

- Udi (Ehud) Komi 052-6215327
- Paschalis Papadopoulos 052-2168215
- David Chavez 052-2756390
- Sean Neil 052-2506892
- Paruic O'Reilly 052-3571665
- Michael Ohehir 052-4168879

CX/QA

Cranes

- Brady Prouty 052-6047531

Safety

- Safety Foreman- Adir Elmakayes- 054-7254767 Adir-Elmakayes@Hoffmancorp.com
- Safety Assistant- Gaber Aloka-050-2238719 Gaber-Aloka@Hoffmancorp.com
- Safety Professional - Adam Benisty- 054-3327444 Adam-Benisty@Hoffmancorp.com

Subcontractor Weekend Work- 16.08.2024

FAB

- Dvir 3 survey crews at FAB at CUB

Manager on site is Daniel Bitton 052-312-8268

EHS Manager is Guy Ishbit 054-491-5407

Utility Level

- Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

- Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

- HYG

Ehs Salah 0507773119

Foreman Avishai 0503303939

- Combe waste

Foreman: Denis 0525238504

Ehs: Michael 0525506596

- Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

- Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Clean Room

- Rolling Planes:

Lead – Codrin : 054.6594273

Safety – Ovidiu Lacob: 054.6993648

- Elram:

Lead – Eliezer Bonillo

Safety – Shlomo Amar:

- Chemo:

Lead – Mr. Winai Sirimat: 052.8090588

Safety – Lotem: 054.4477112

- Talad:

Lead – Hen Asulin 054-6654471

Lead Elad Amoyal 052-7457957

Safety – Guy Ishbit 0544-915407

- Sig:

Lead – Nodar

Safety - Benny

Subfab

- Elram -LSS 2E/W – Finish walls.

Team Lead : Elad 0586793504

- Afcon E

Mars 1E/W Ducts

Team Lead : Aviel 0526008487

- HYG -Stair 4 Railing

Team Lead : Salah 0507773119

- Pach Taas- Mars 1E/W Lighting fixtures

Team Lead : Gai Cohen 0535552472

PSSS

- ChemoA.

Maor d 0509889071

- PachTaas's

Guy c 0535552472

Meir d 0502161429

- HSAI

Dave s 0524121028

Haim. 0548038554

- AFCoN

Mor 0542250099

Siding

- SNJ- FAB

Liran T. 052-6533558

Barak B. 053-3003902

Subcontractor Weekend Work- 16.08.2024

WJG

- Pach Taas: 1J UL, 2J Lift 2 Module Bolting
- Team leader - Victor 053-9633138
Safety - Meir - 0502161429
Foreman - Guy - 0535552472

Site

- Derech Afar – Fire protection water underground
- Supervision = Raed: 054-2442030
EHS = Alex: 054-5403849- Olizki – Sweepers and water trucks & concrete forming

Supervision = Or: 052-4917313
EHS = Ben: 052-4033565- TM Team – Telecom CLSM backfill

Supervision = Rafi: 050-8723363
EHS = Alon: 054-7711469

Trestle

- SNJ – FOUATION
- FORMAN abed 0528168353
- SNJ- PIPING
- FORMAN HAMADA SALEM tel. 05435169722safety trestle Alon Matan tel.
+972 50-989-5008

GIS/NEY

No work

CUB

CUB 1

- Chemo Aharon:
- Dudu - 0509808846
Leonid - 0548883878- SKE:

Marzuk - 0548830263
Reynato - 0548991623- HSAI

CUB HYDRO WATCH:

- CHEMO AHARON:
- 24 HOURS FRIDAY-SATURDAY
ONSITE DAY SHIFT 0700-1900
Friday Day shift Yothoanasak 052-3911674
Friday Night shift Chatchai 052-9386530
Saturday Day shift Kawee 052 8980429
Saturday Night shift Yosawat 052 8404983- EK

052 3623553 SUPERVISOR ON CALL
Sharon Aronovich HCC WET MECH CM +972 50 668 0986

Daily Coordination Meeting



14:00 Sign In
