

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- Keep your cool




UTILITY LEVEL MOD1

LESICO
Pneumatic test
iA+BEA 8/22
Start 17:00
Finish 22:00


AA

CD

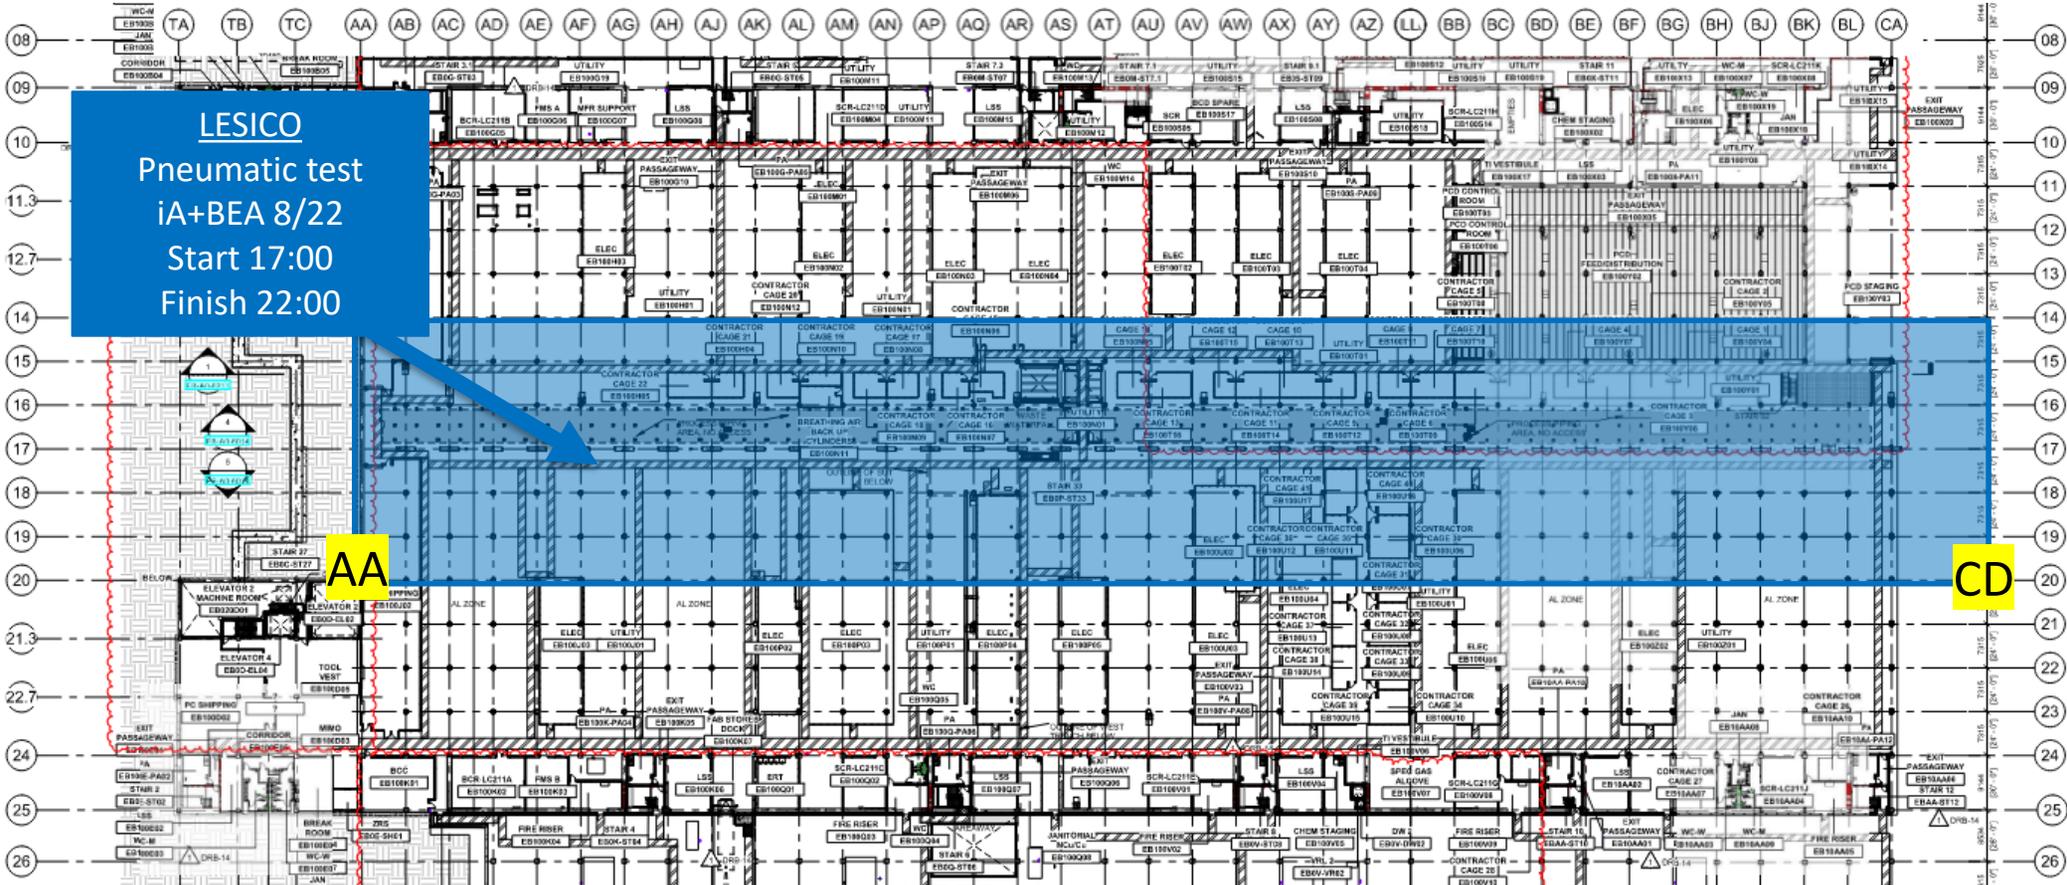




SUT LEVEL

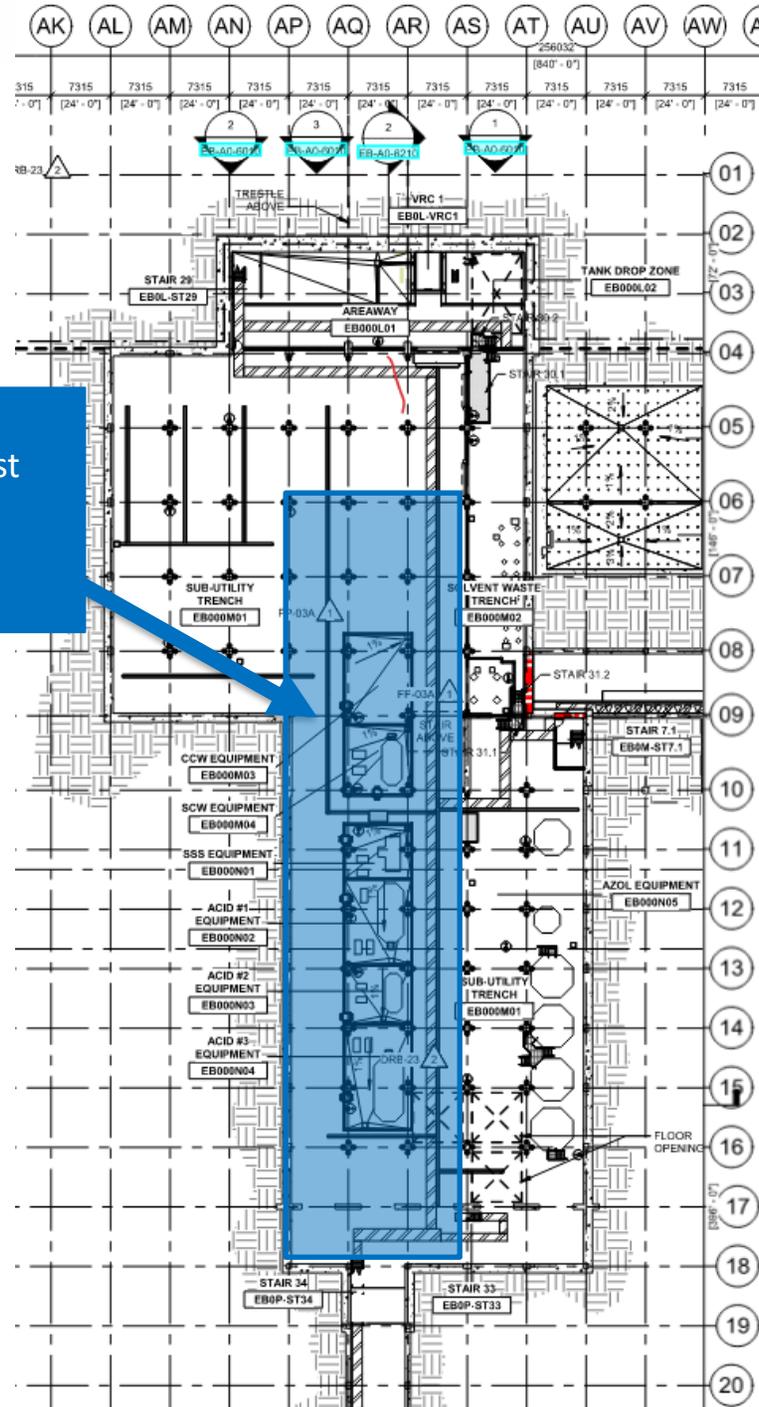

LESICO
 Pneumatic test
 iA+BEA 8/22
 Start 17:00
 Finish 22:00

UTILITY LEVEL MOD1

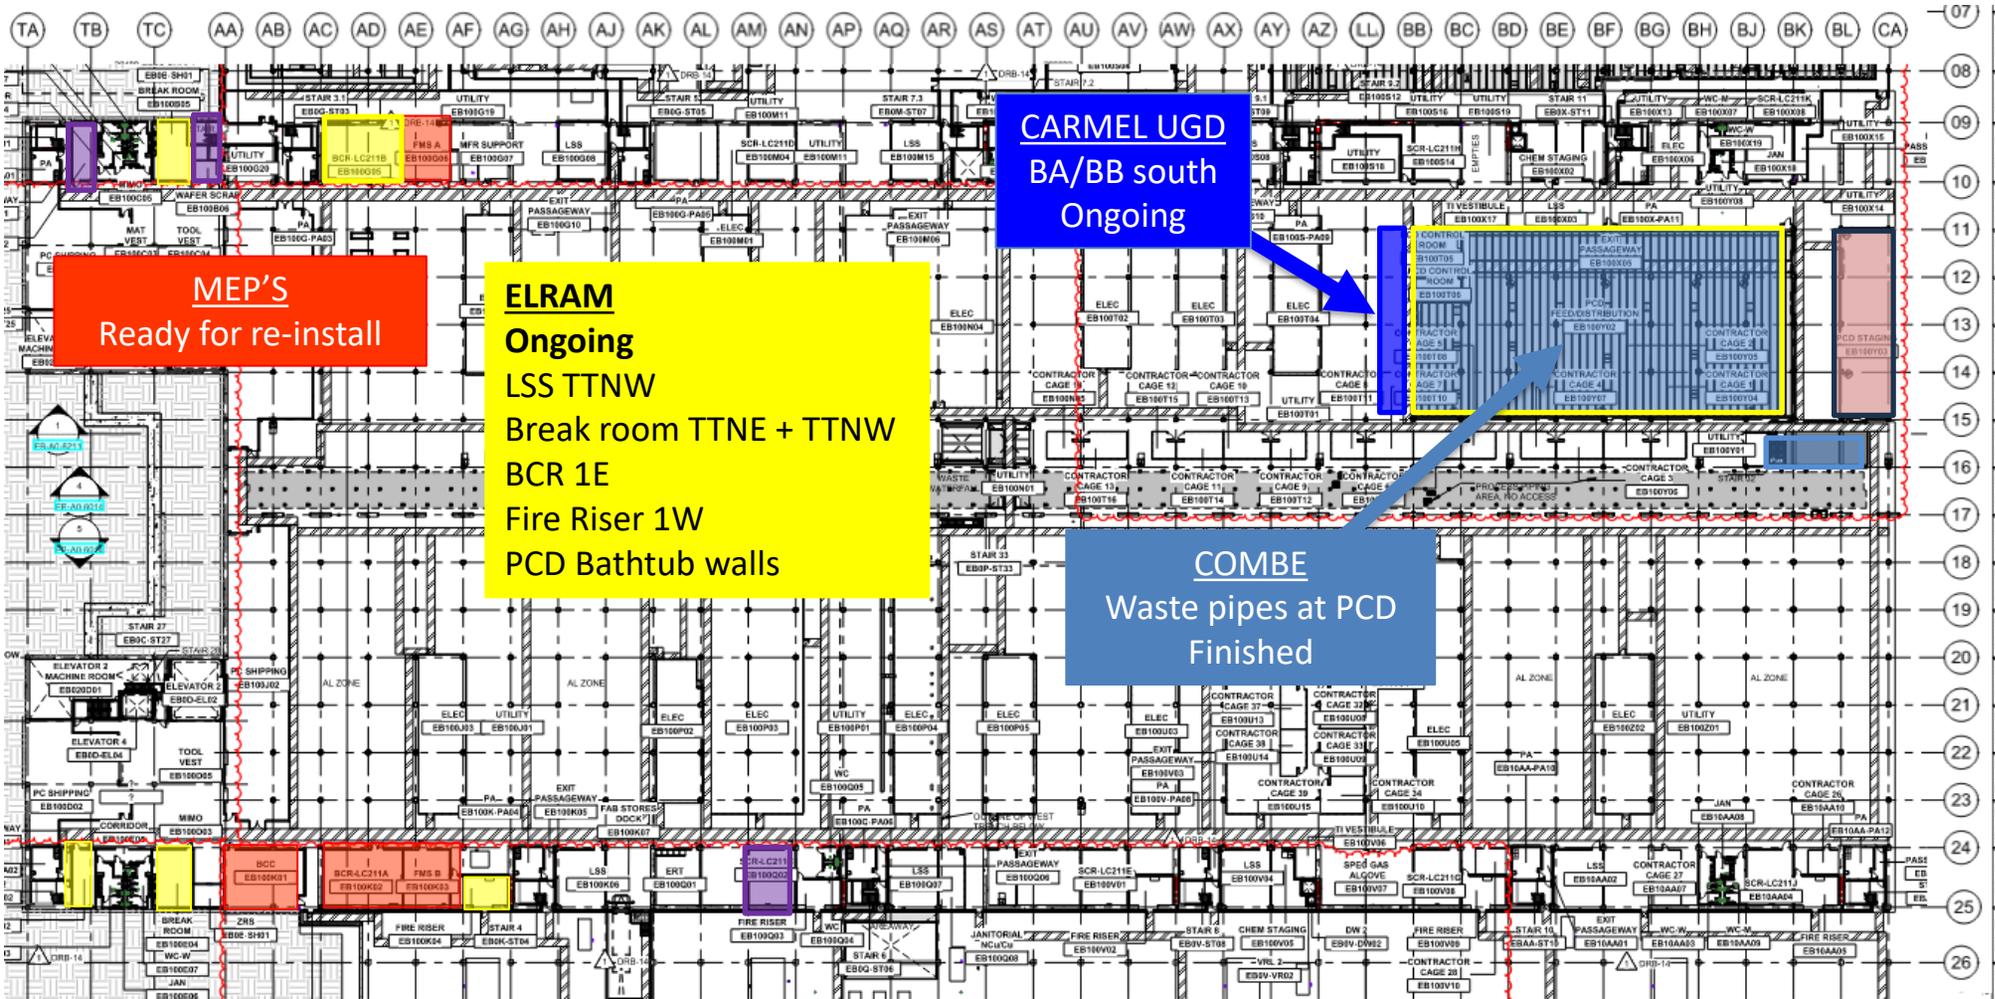

MEP'S
Ready for re-install


ELRAM
Ongoing
LSS TTNW
Break room TTNE + TTNW
BCR 1E
Fire Riser 1W
PCD Bathtub walls

CARMEL UGD
BA/BB south
Ongoing

COMBE
Waste pipes at PCD
Finished

07
08
09
10
11
12
13
14
15
16
17
18
19
20
21
22
23
24
25
26


UTILITY LEVEL MOD2

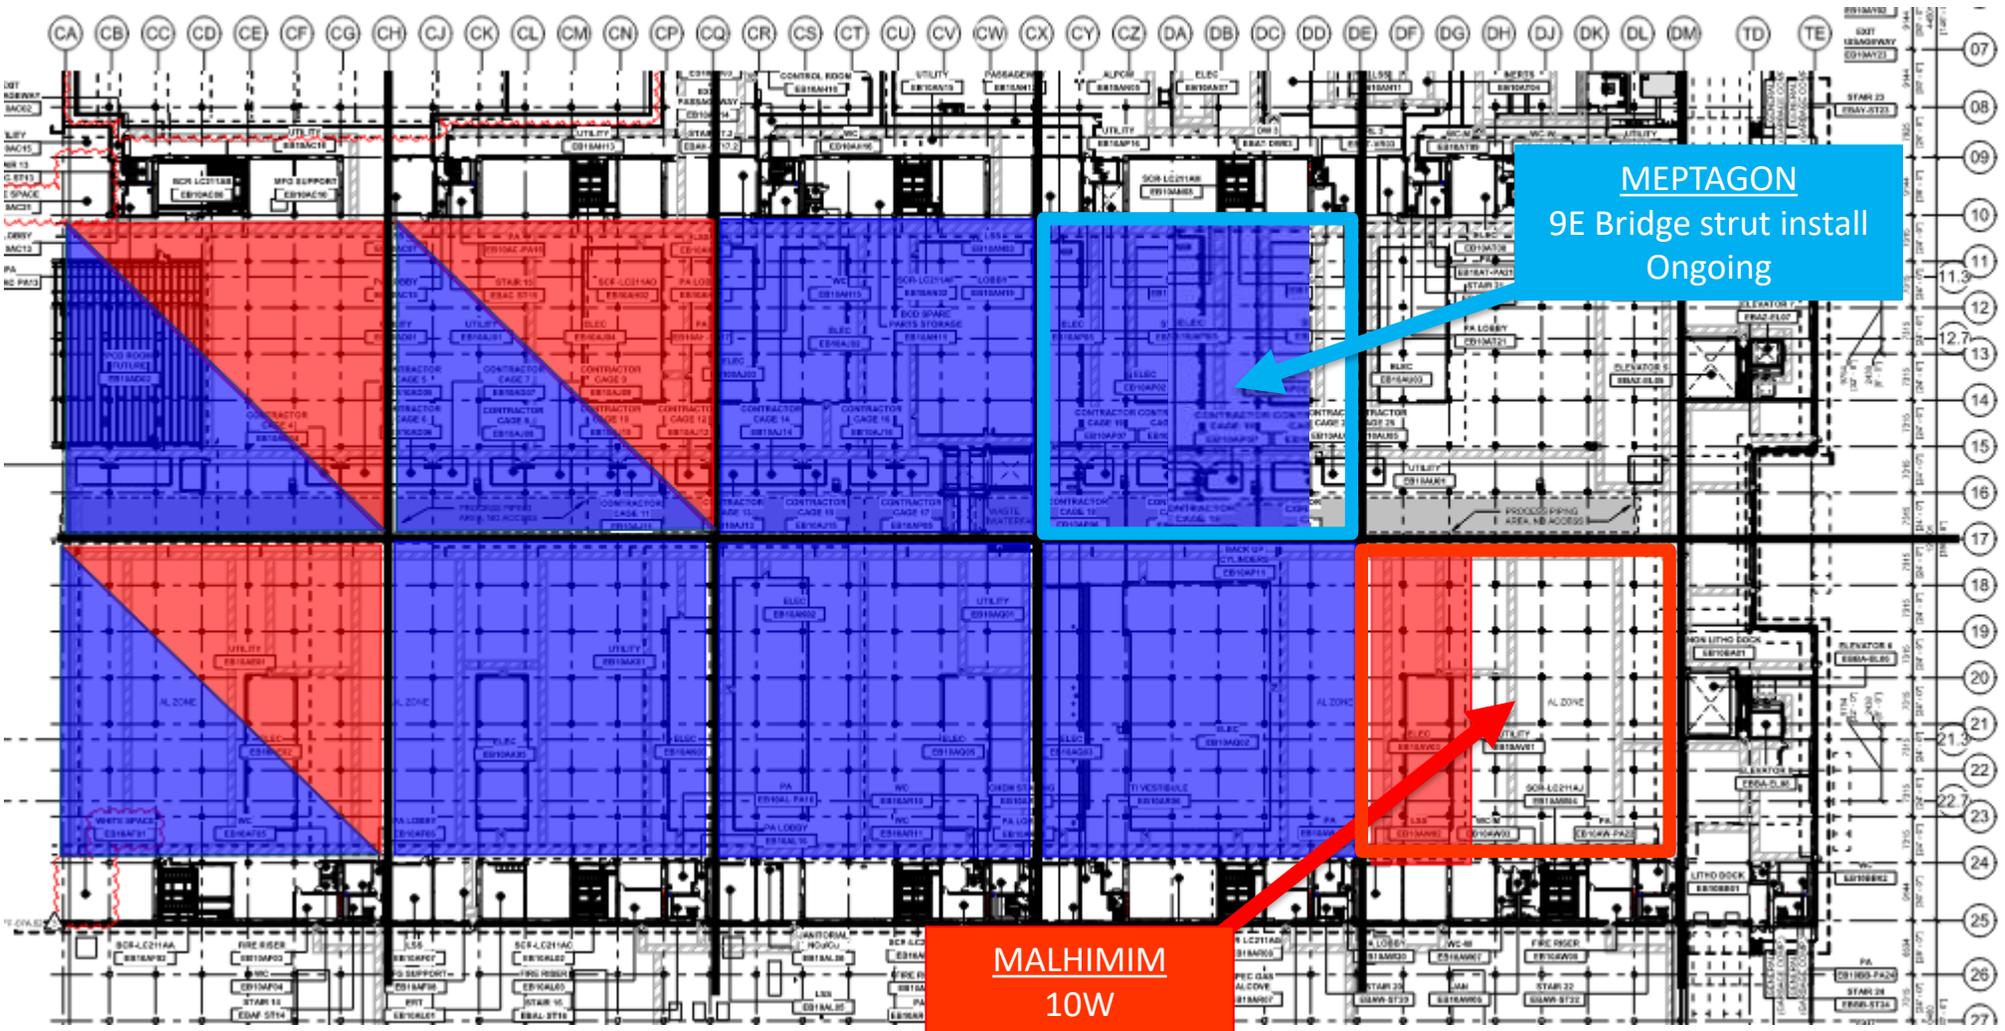

MEPTAGON
9E Bridge strut install
Ongoing

MALHIMIM
10W
Sprinklers install

SUT 38.1 LEVEL

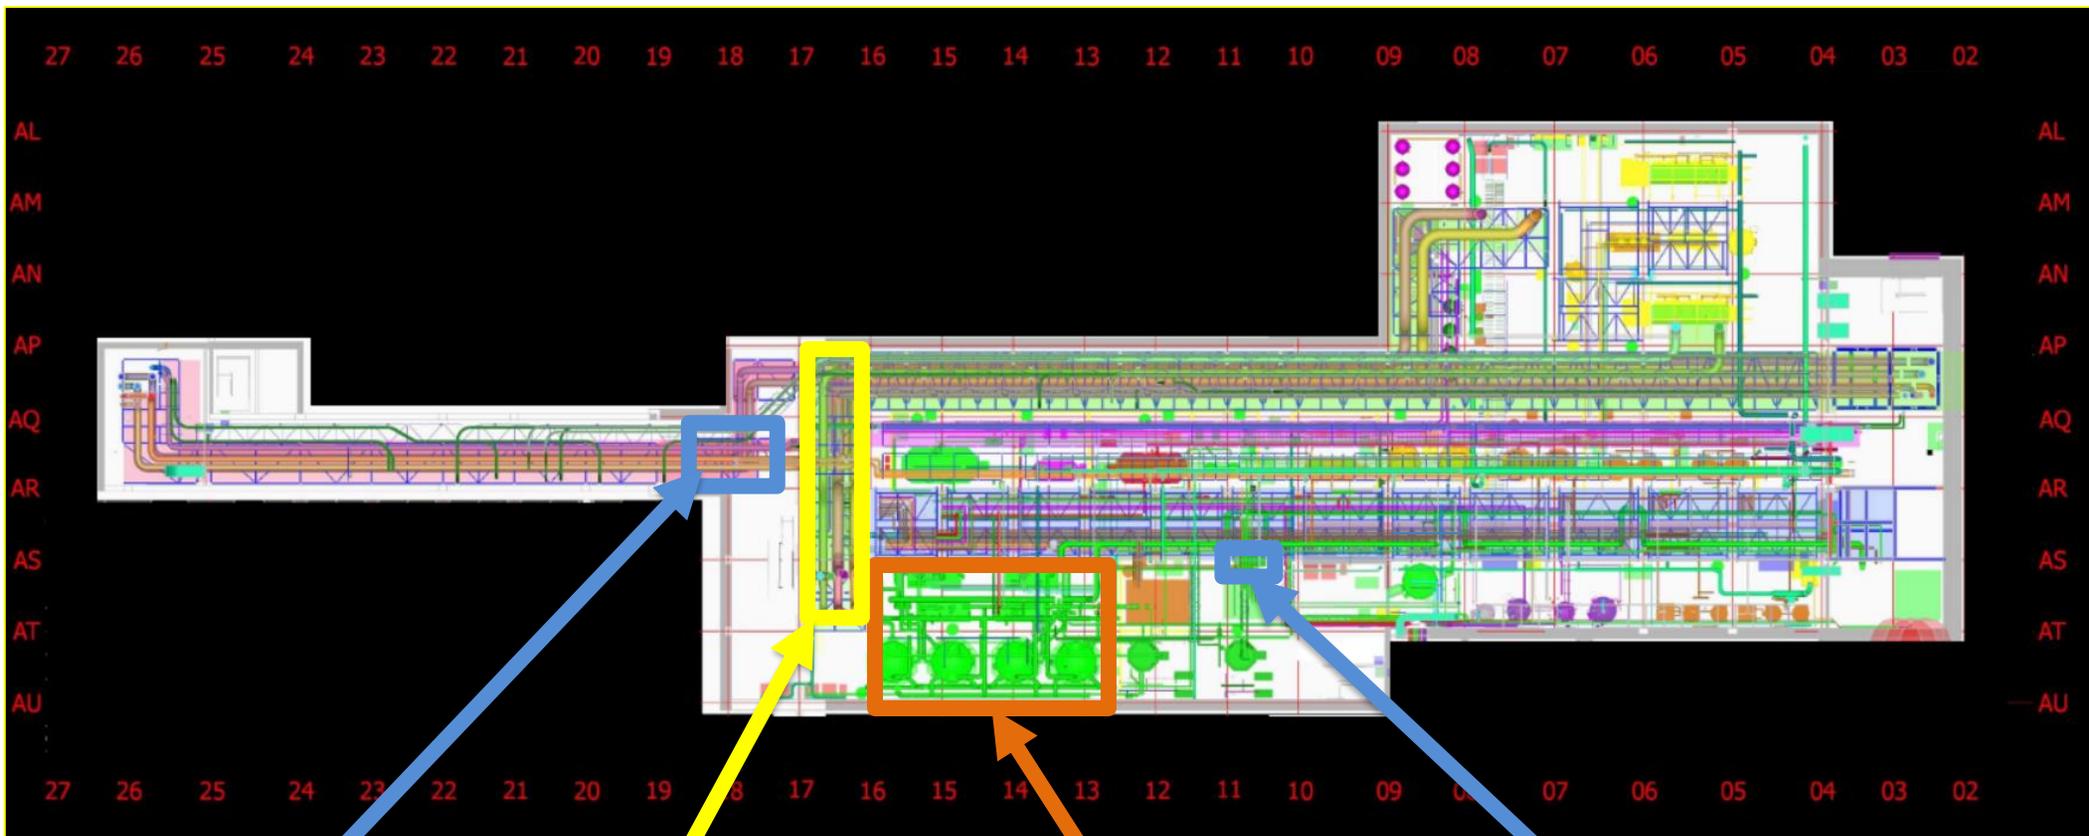


Chemo
17-18 Retrofit steel

IDP
16-17 Retrofit steel


Combe
AWN Piping
Connections.

TMTeam
Biocide Curb Pouring
Aug 21st


SUBFAB BUILDOUT MOD 1

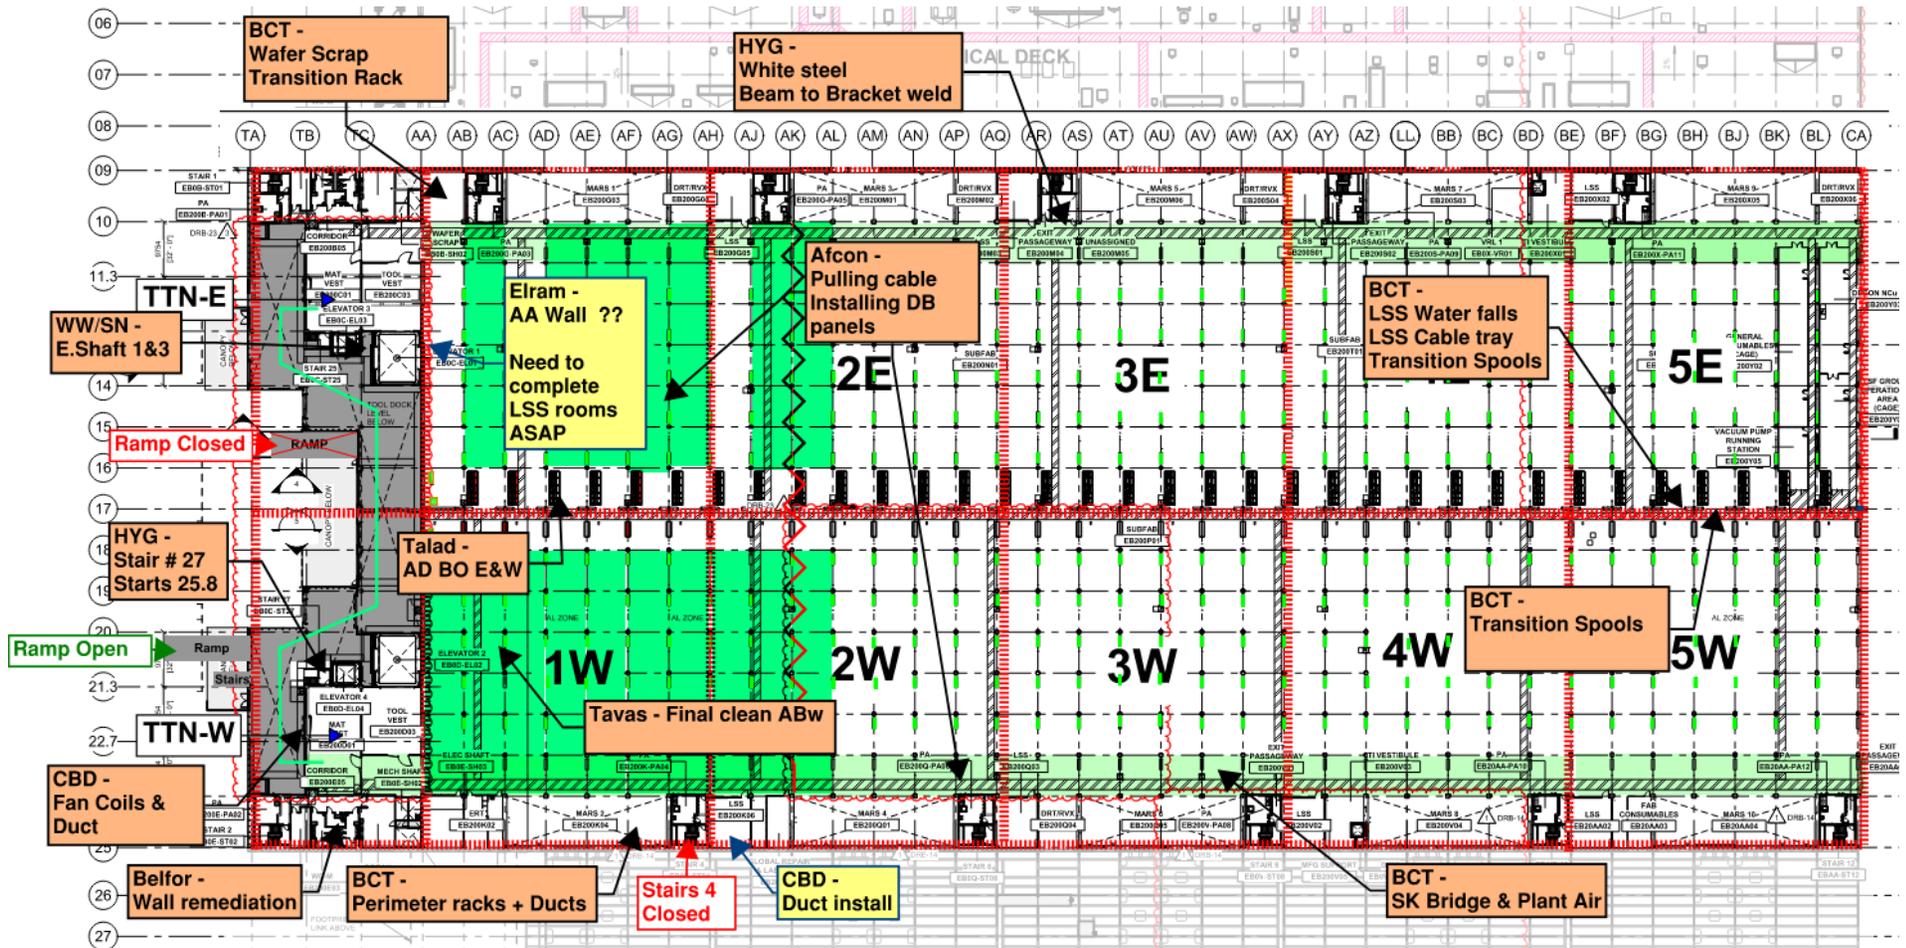

SUBFAB BUILDOUT MOD 2

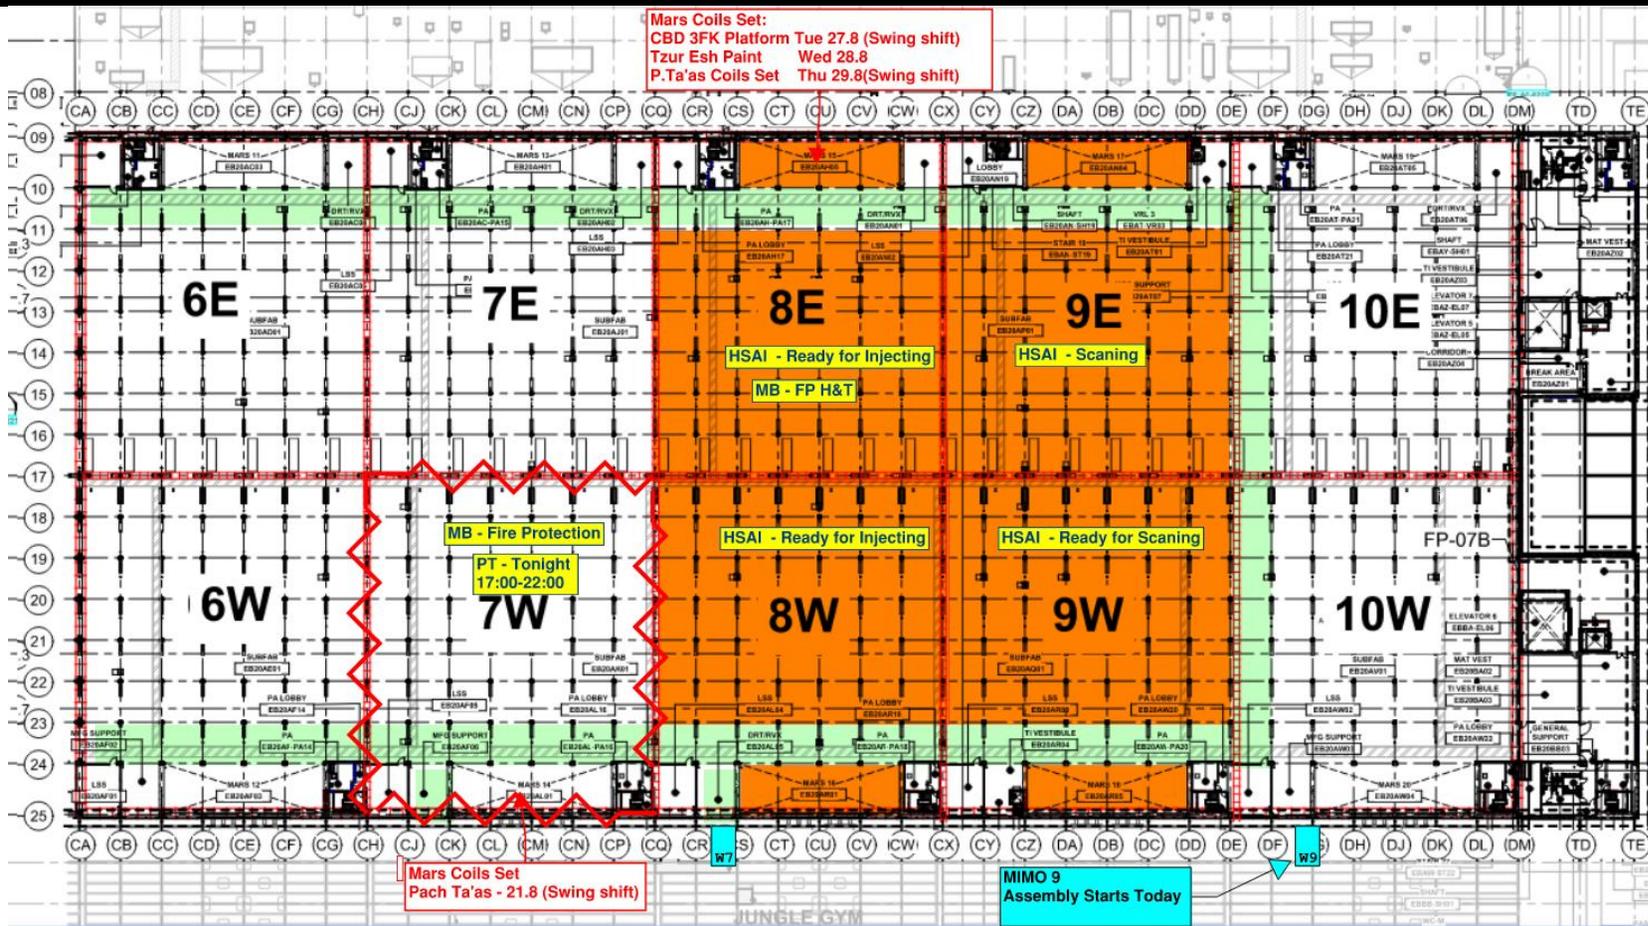

SUBFAB CRC TOPCOAT

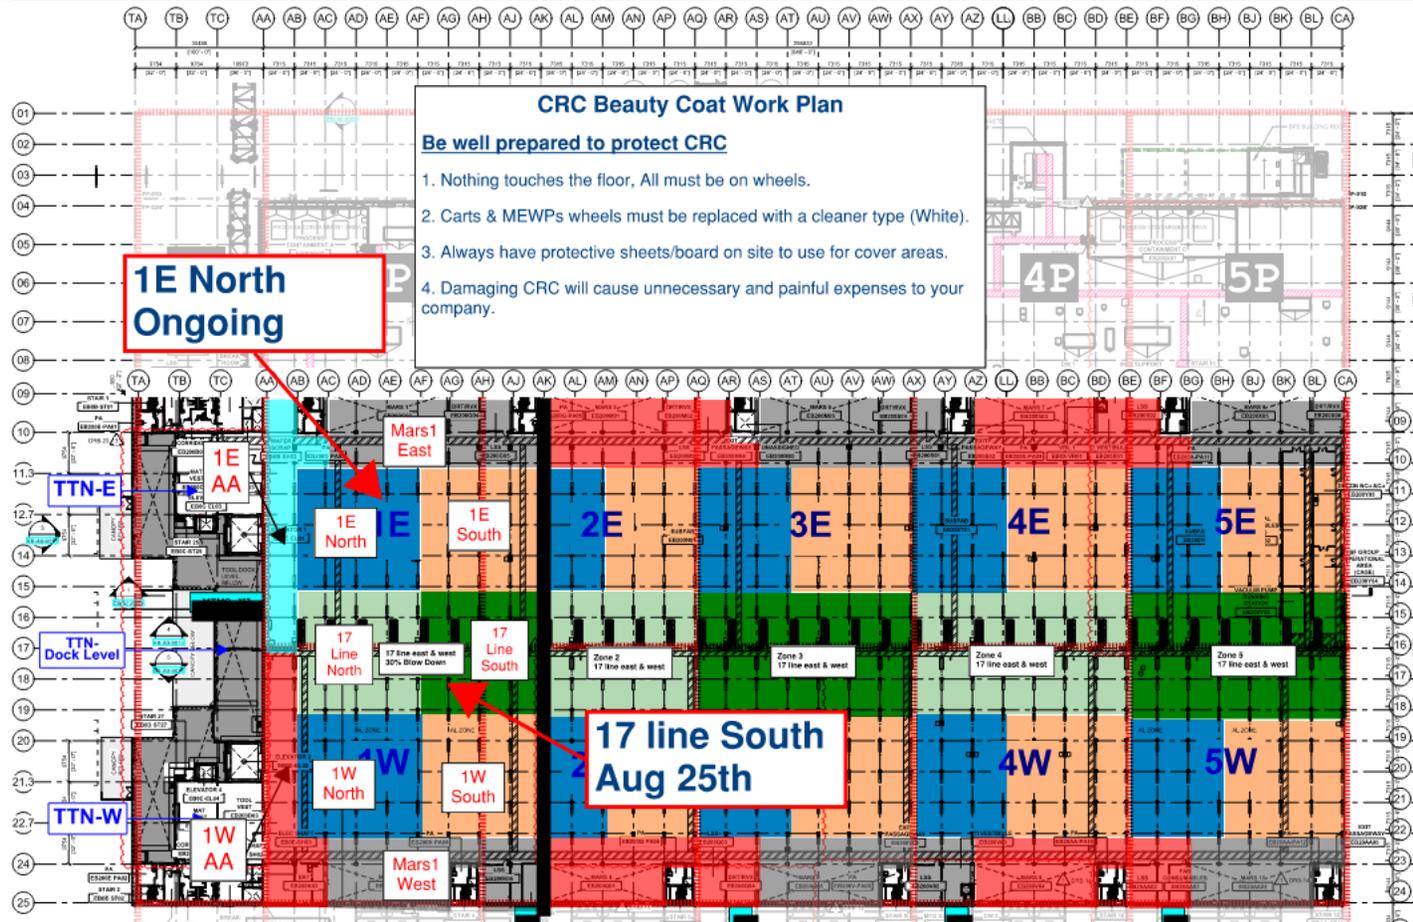

NTTEW
 WW/SN - west side welding tabs and replacing beams
 Elram - East/West floor done QA/QC
 SK - east side pipes needs to be completed
 HYG - East to finish steel. West receiving material

Belfor TC line

CR level:
 Afcon - Cable trays, modules and stickers 1W,2E, 2W,3E,3W
 MB- 1E drops, 1W drops. 2E- drops
 Elram - 10, 24 columns/shaft walls. AA line column wraps
 WW/JS - 17-18 line added beams+ AS south stocker beams
 Meragon - I&C 1E
 D&P - Ceiling rods 1E, 5E blades install.
 Tzur-esh - 24-25 lines. 4E-4W blades
 HYG- 1W Litho crane QA, 5W Litho crane steel
 PT - Duct prep for test AA-AH east
 Talad- Blades install 24-25 lines




Sig-mobile scaffold 5/9

Link
 RP - FP 5RA level
 MB - Supports install

Paint will be done by tomorrow 07:00

Mb-upper level fire protection piping

Pach taas – exhaust duct install and tie in

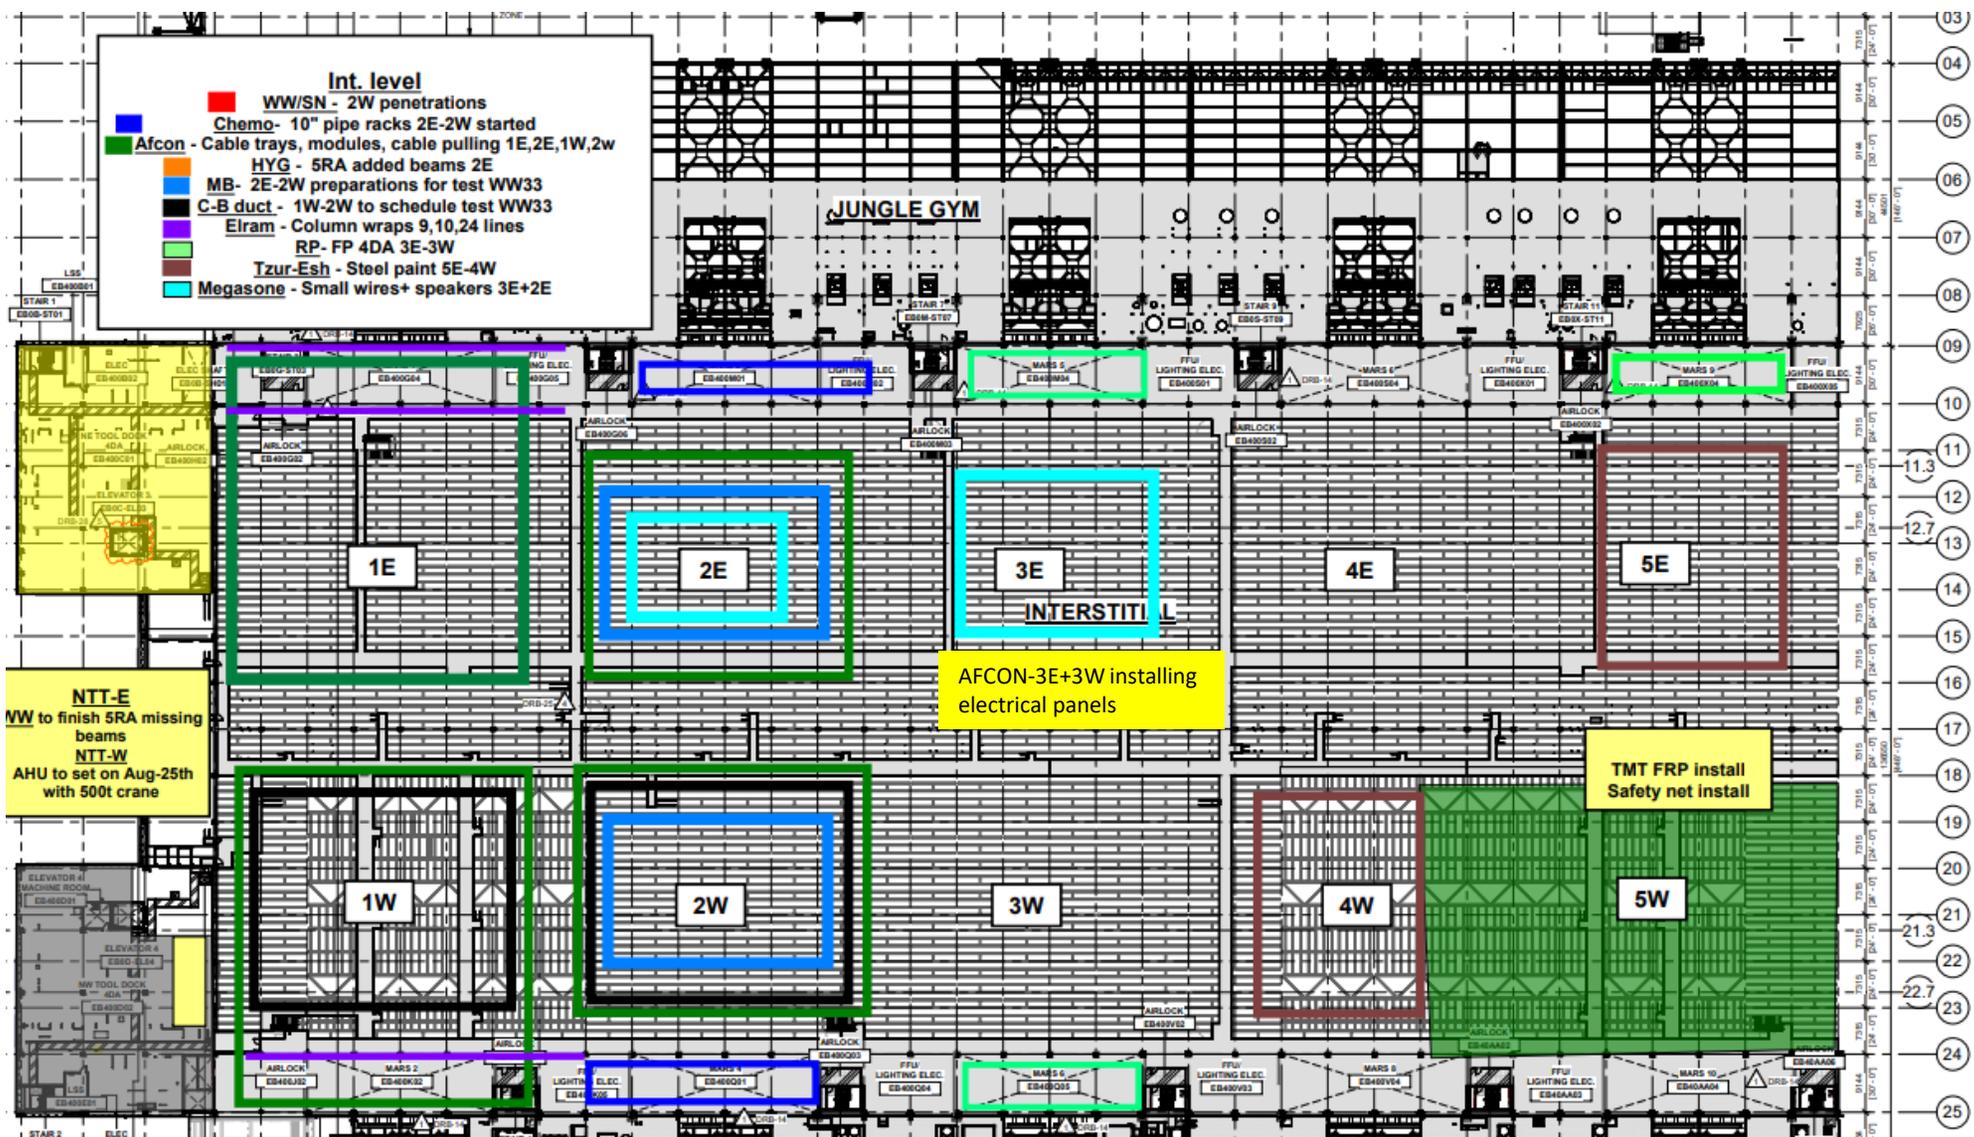

- Int. level**
- WW/SN - 2W penetrations
 - Chemo - 10" pipe racks 2E-2W started
 - Afcon - Cable trays, modules, cable pulling 1E,2E,1W,2w
 - HYG - 5RA added beams 2E
 - MB - 2E-2W preparations for test WW33
 - C-B duct - 1W-2W to schedule test WW33
 - Eiram - Column wraps 9,10,24 lines
 - RP- FP 4DA 3E-3W
 - Tzur-Esh - Steel paint 5E-4W
 - Megasone - Small wires+ speakers 3E+2E

NTT-E
 WW to finish 5RA missing beams
NTT-W
 AHU to set on Aug-25th with 500t crane


AFCON-3E+3W installing electrical panels

TMT FRP install Safety net install


03
04
05
06
07
08
09
10
11.3
12
12.7
13
14
15
16
17
18
19
20
21
21.3
22
22.7
23
24
25


HOFFMAN


17 SUPPORT STEEL PER ERECTION PROCEDURE SHOWN ON SHEETS XAF-038.1 AND XAF-038.5.

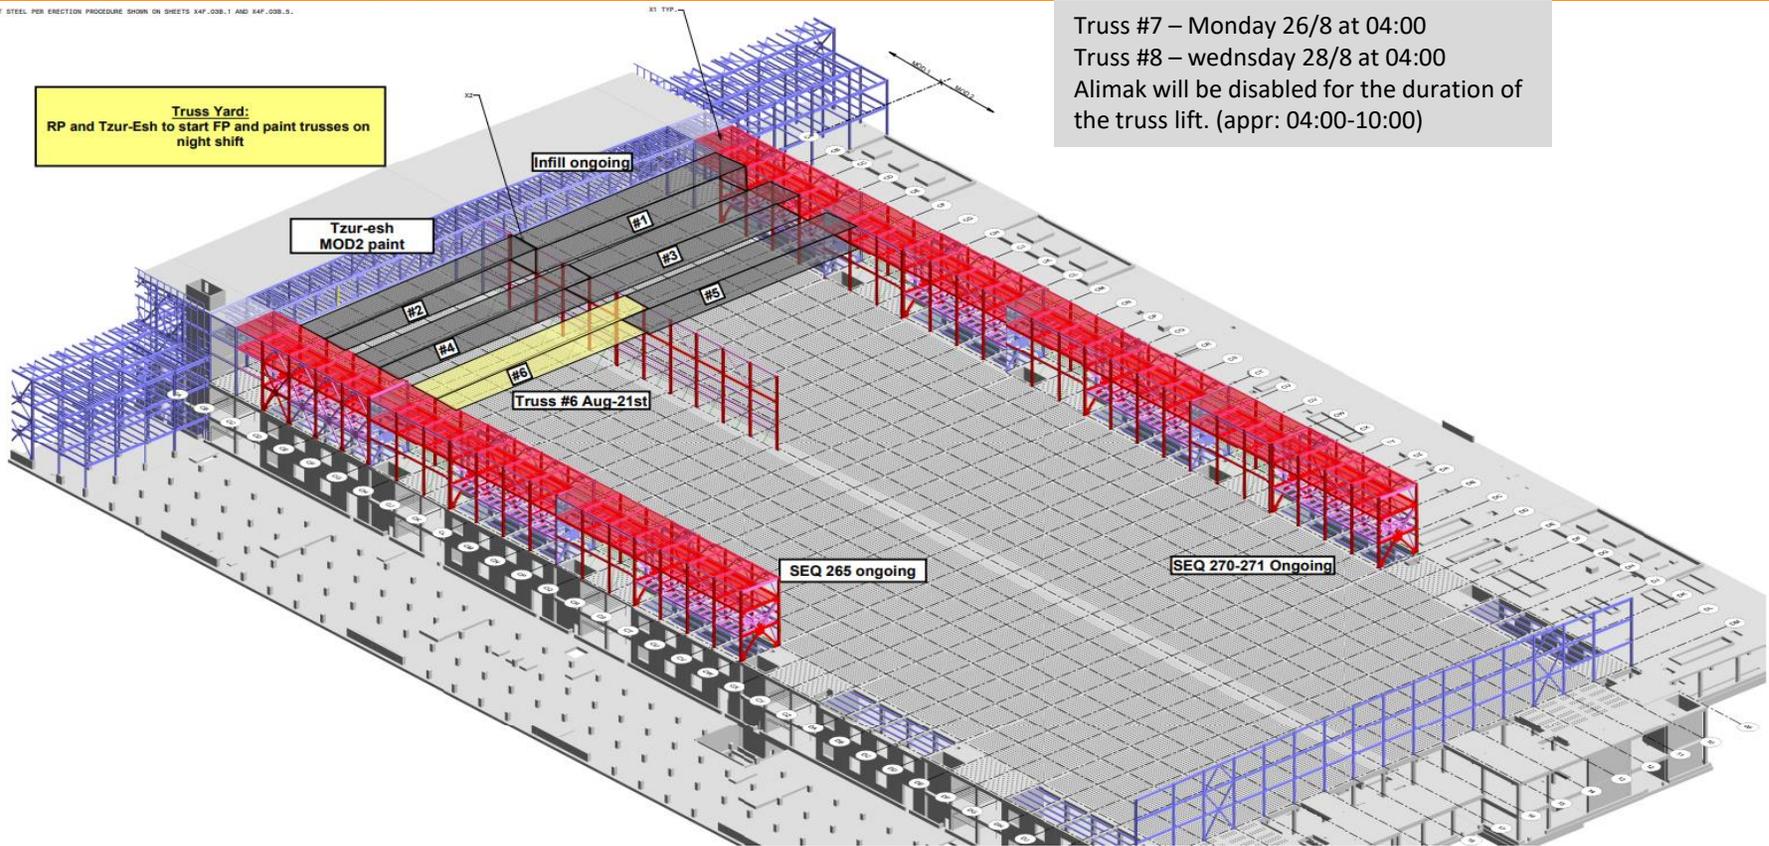

Truss #7 – Monday 26/8 at 04:00
Truss #8 – wednesday 28/8 at 04:00
Alimak will be disabled for the duration of the truss lift. (appr: 04:00-10:00)

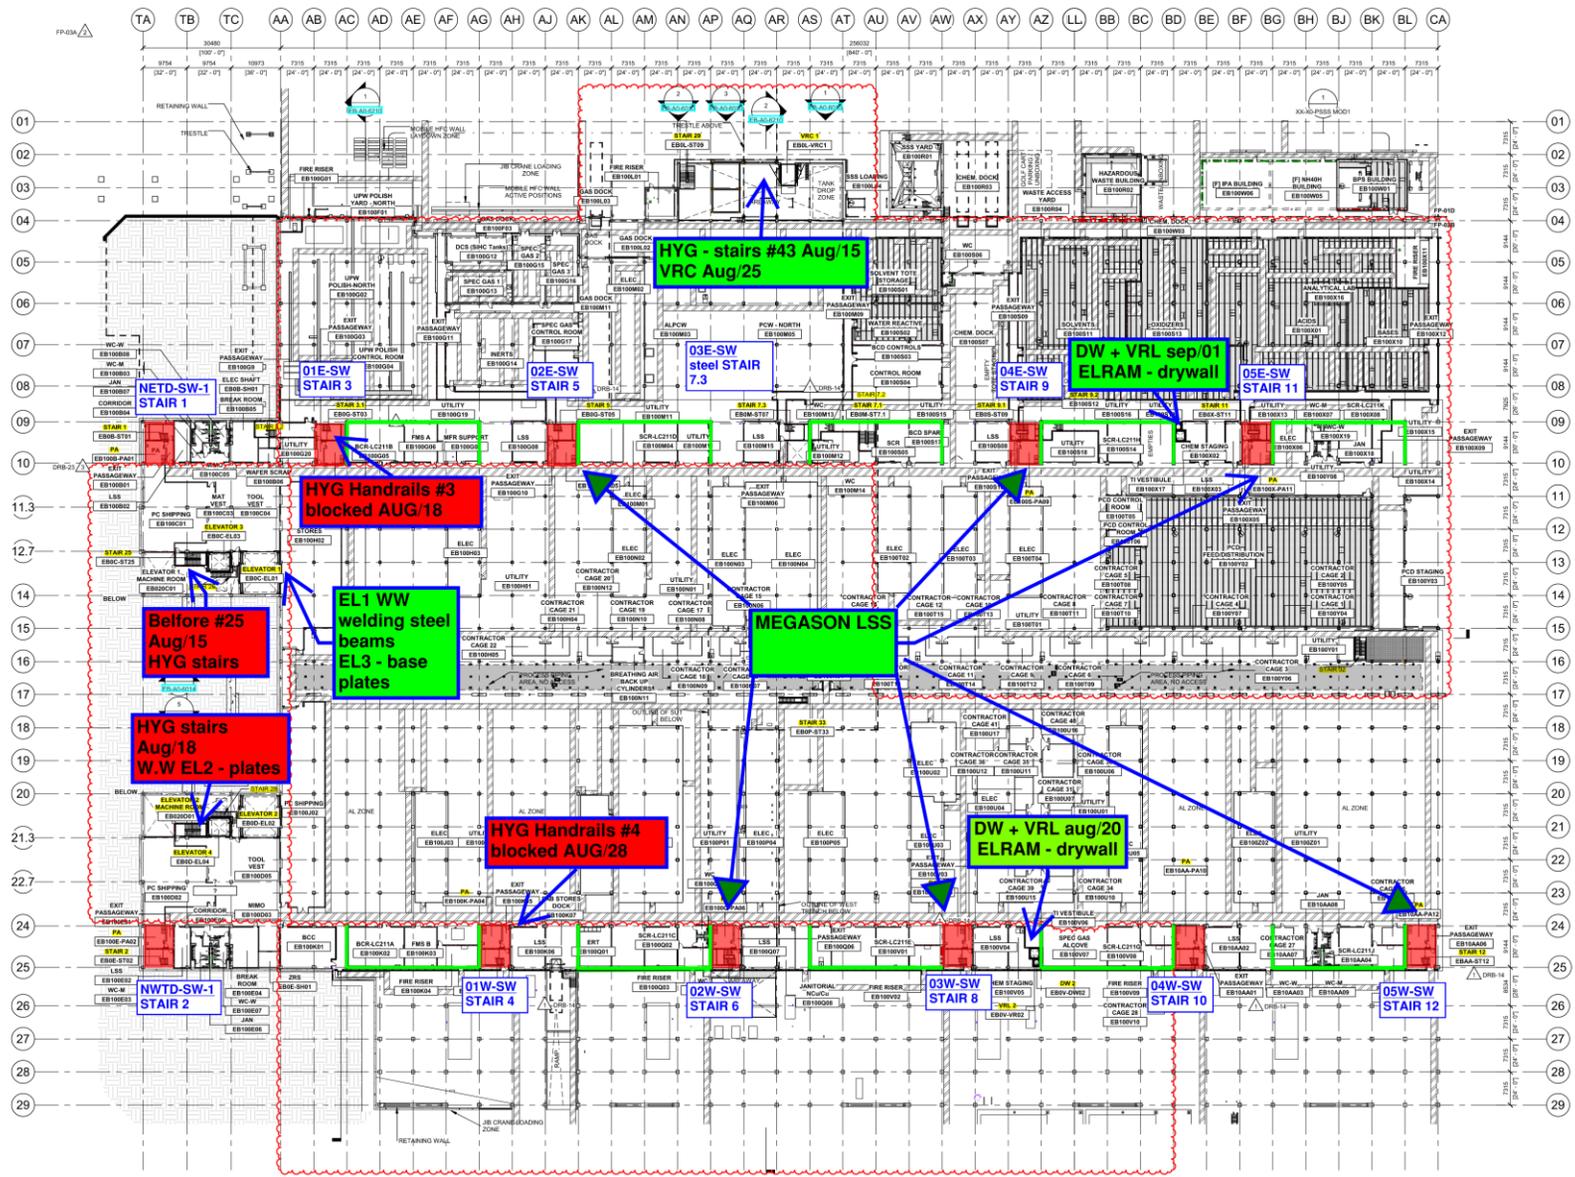

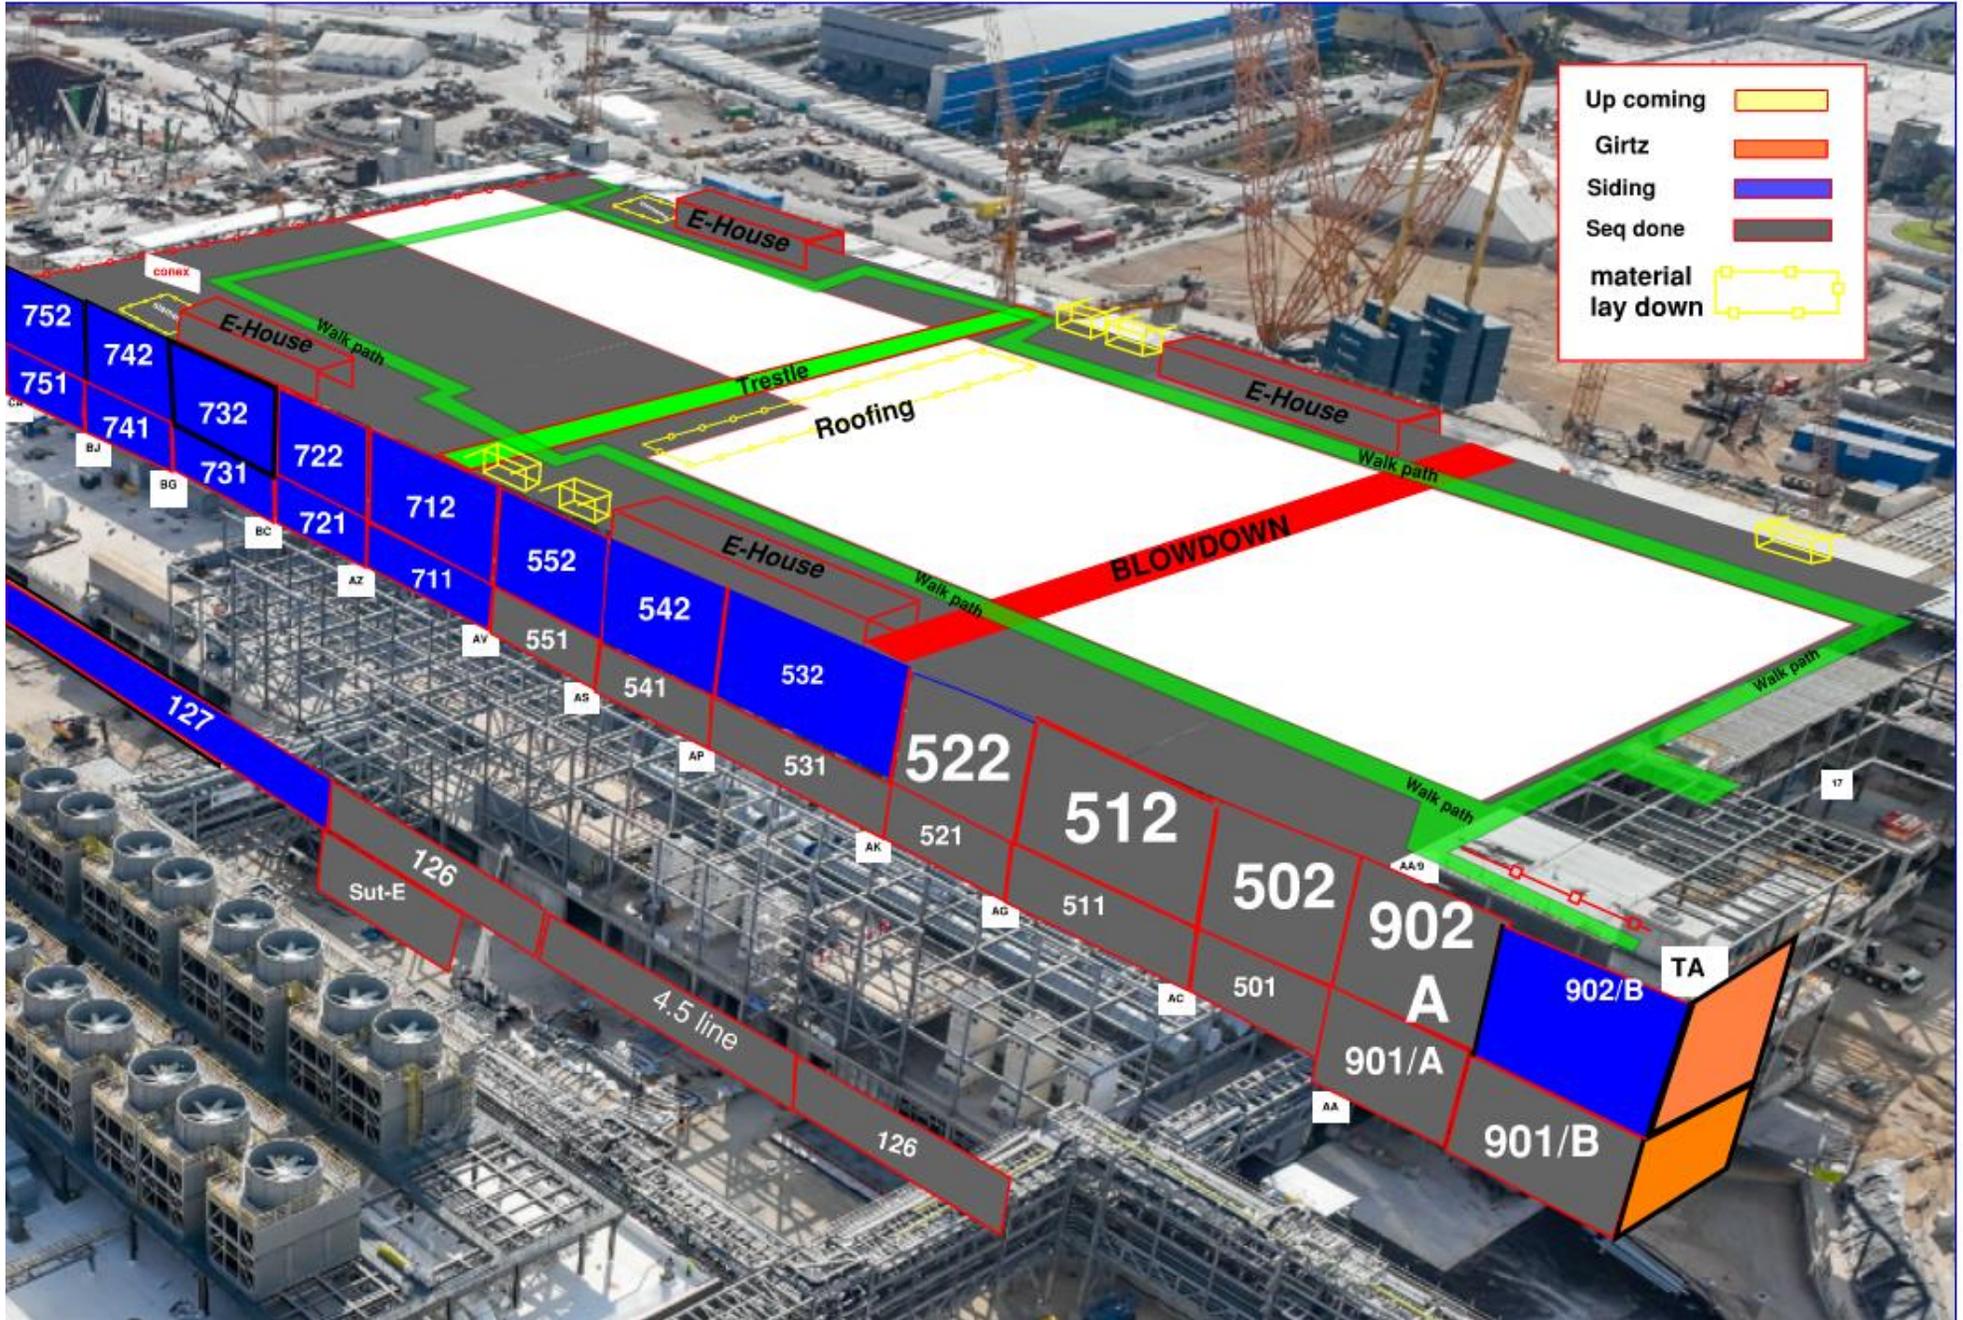

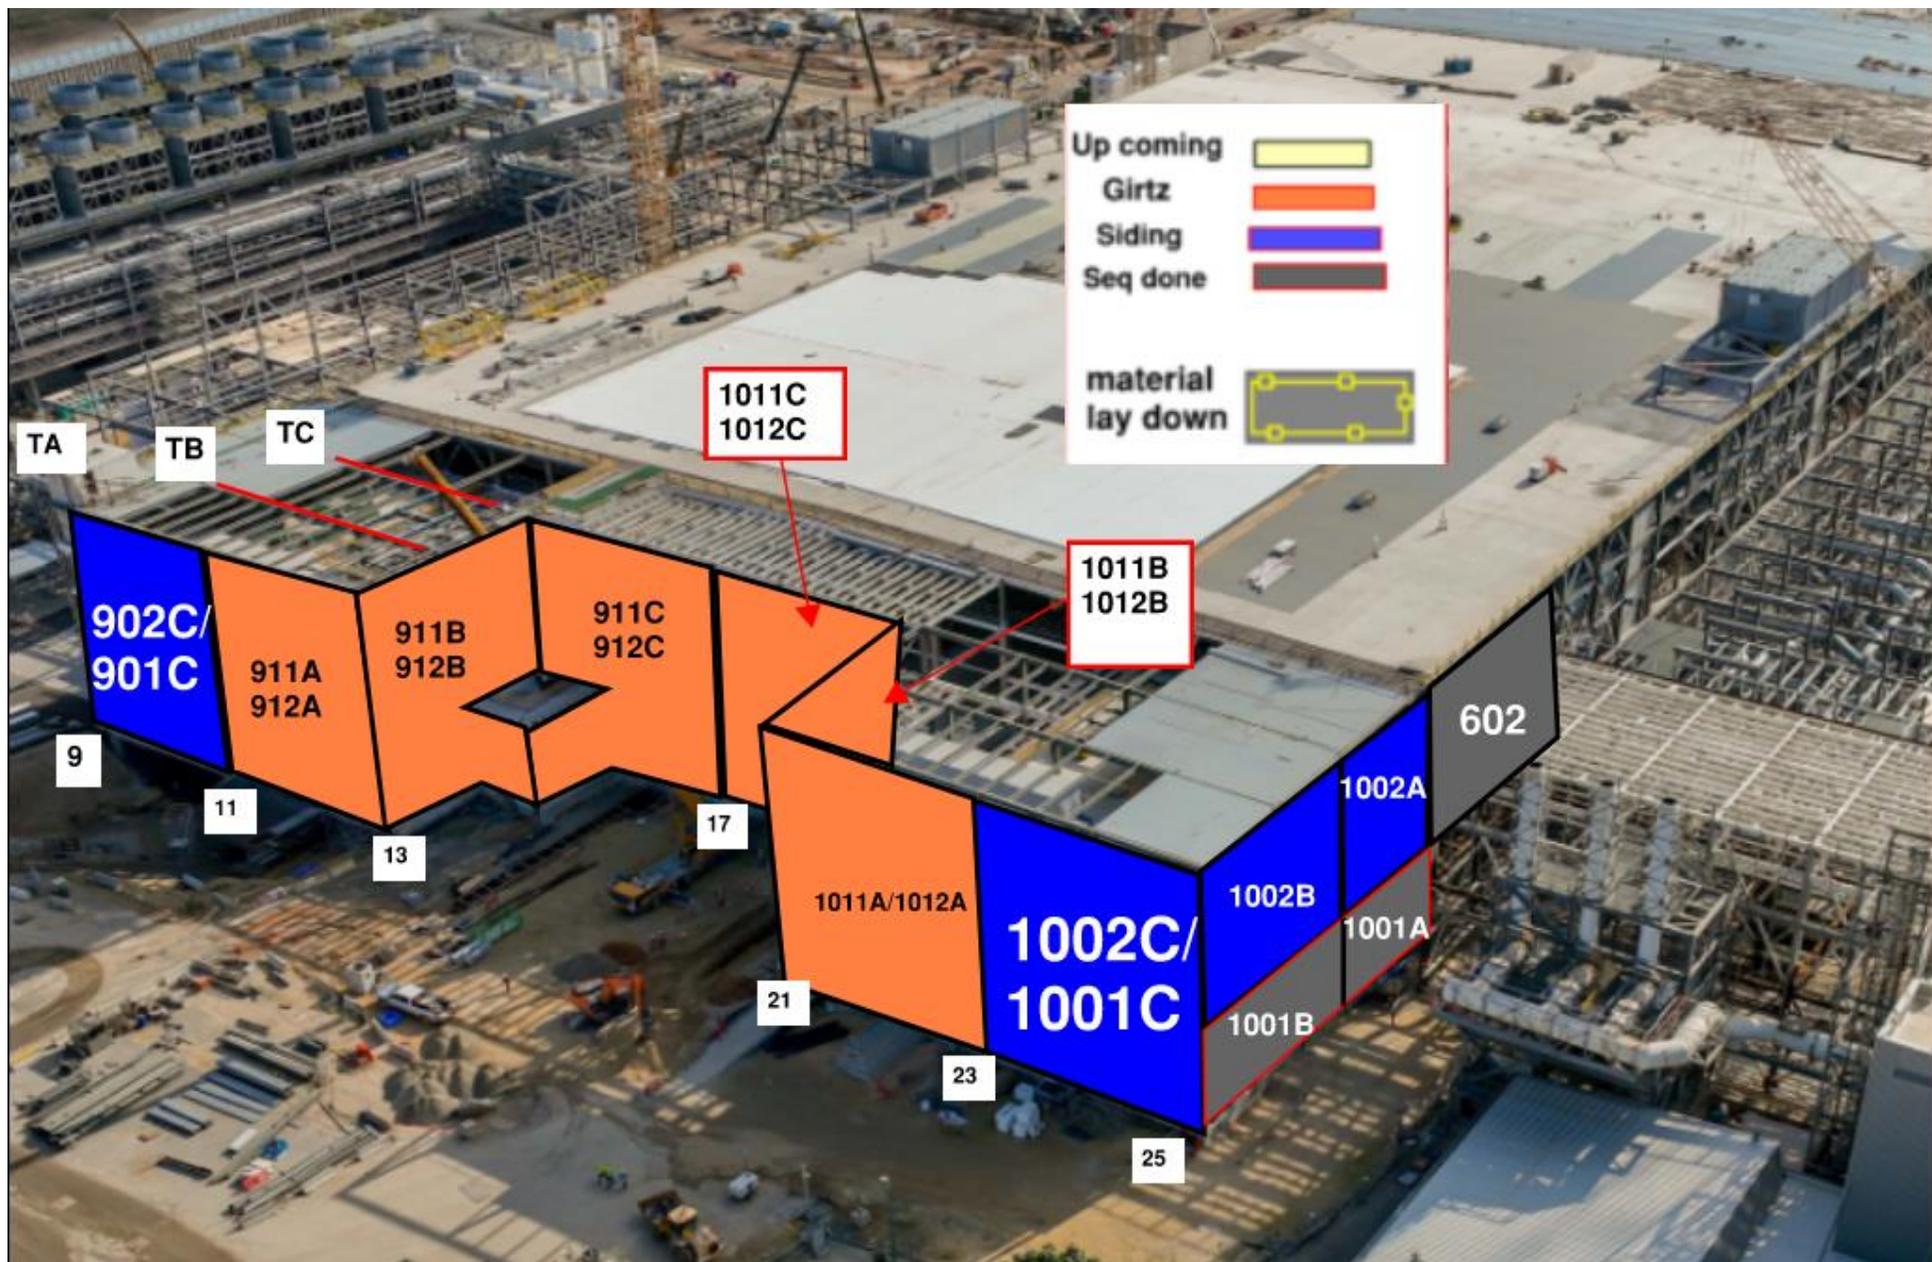

Up coming

Girtz

Siding

Seq done

material lay down

TA

TB

TC

1011C
1012C

1011B
1012B

902C/
901C

911A
912A

911B
912B

911C
912C

602

9

11

13

17

1011A/1012A

1002C/
1001C

1002A

1002B


1001A

1001B

21

23


25

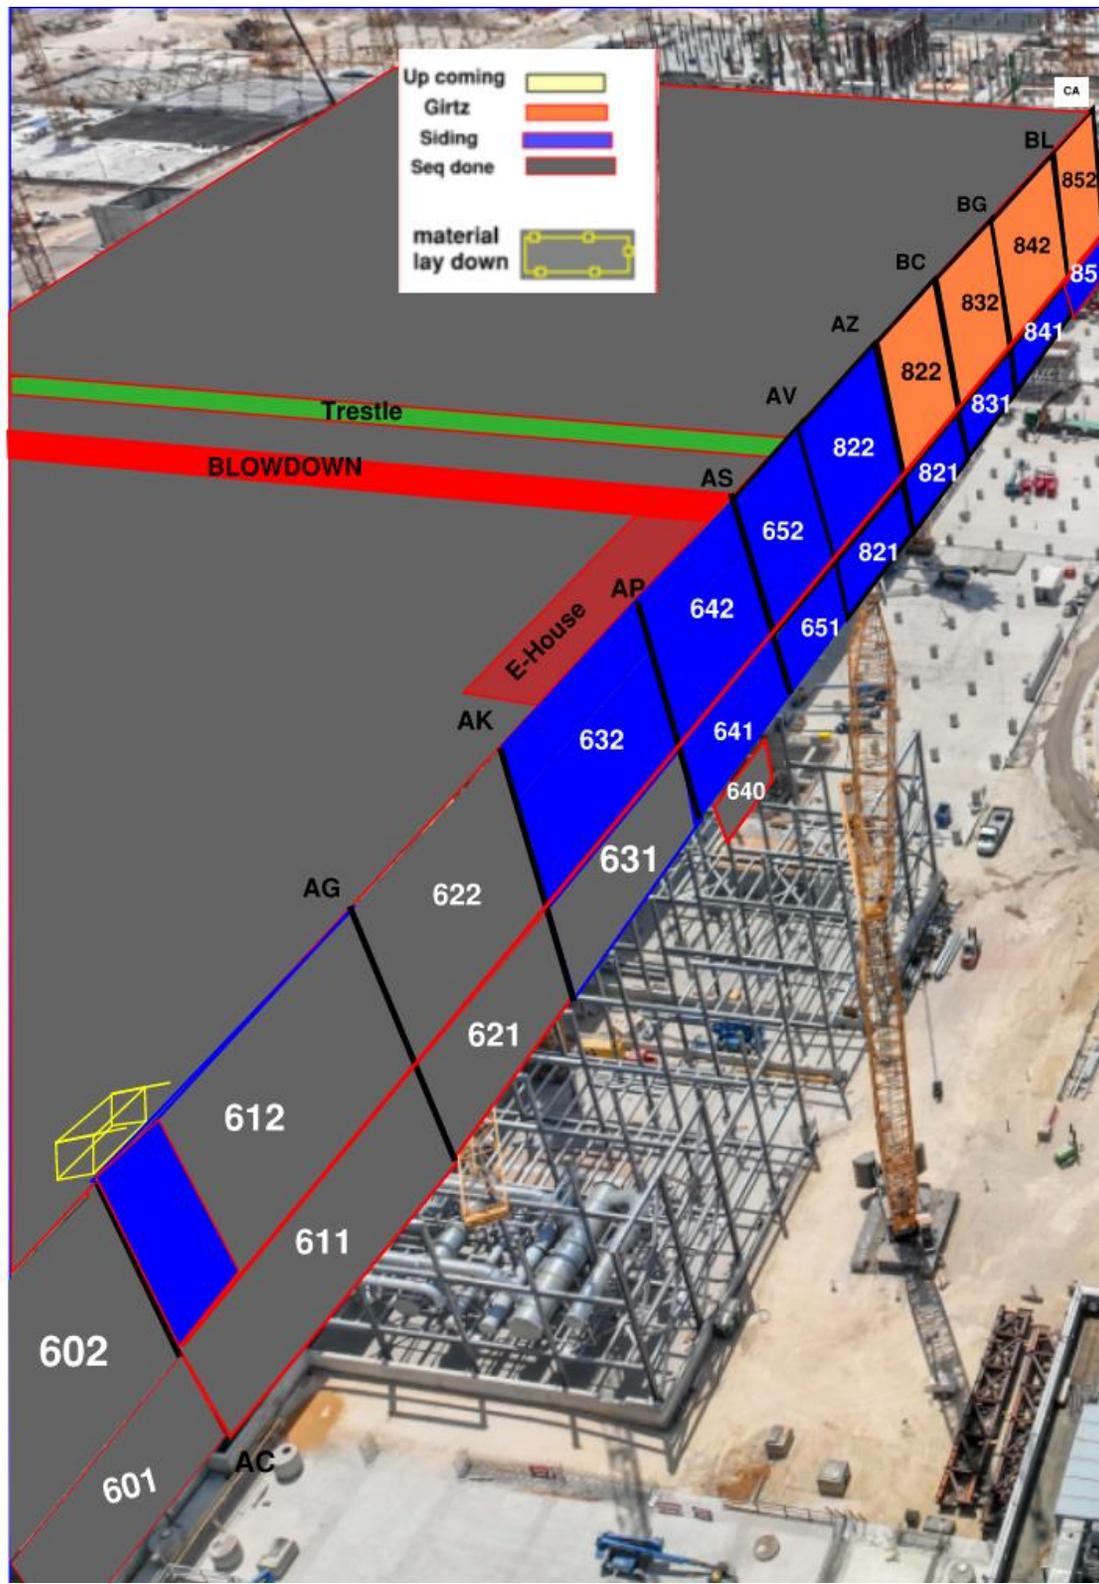

PSSS.1

Utility Level
1YA


PSSS Roof
2SA

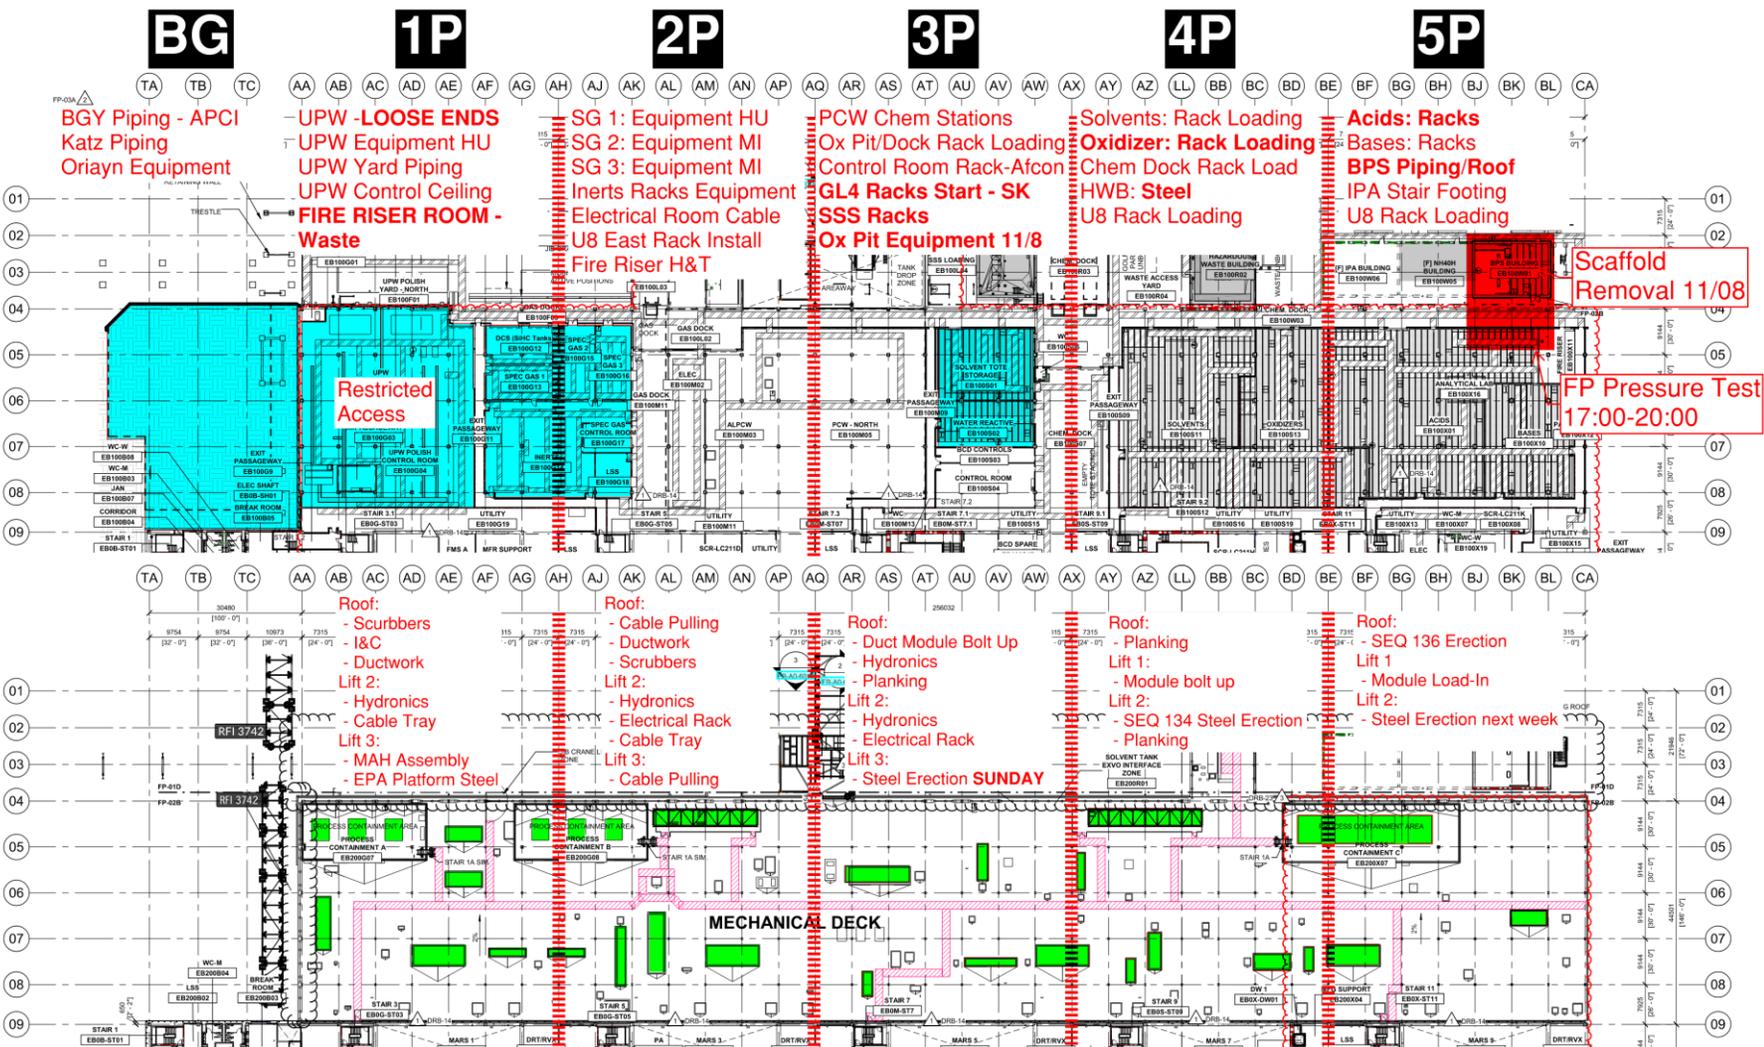


PSSS.2


6P **7P** **8P** **9P** **10P**

Utility Level
1YA

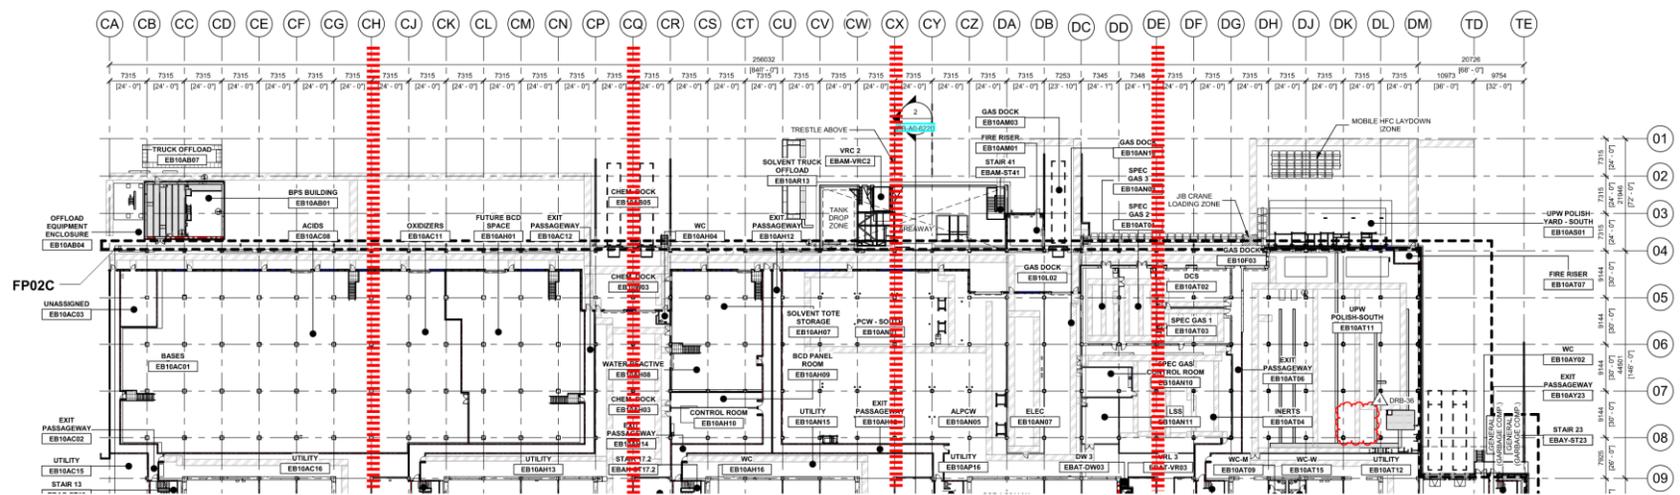

PSSS Roof
2SA

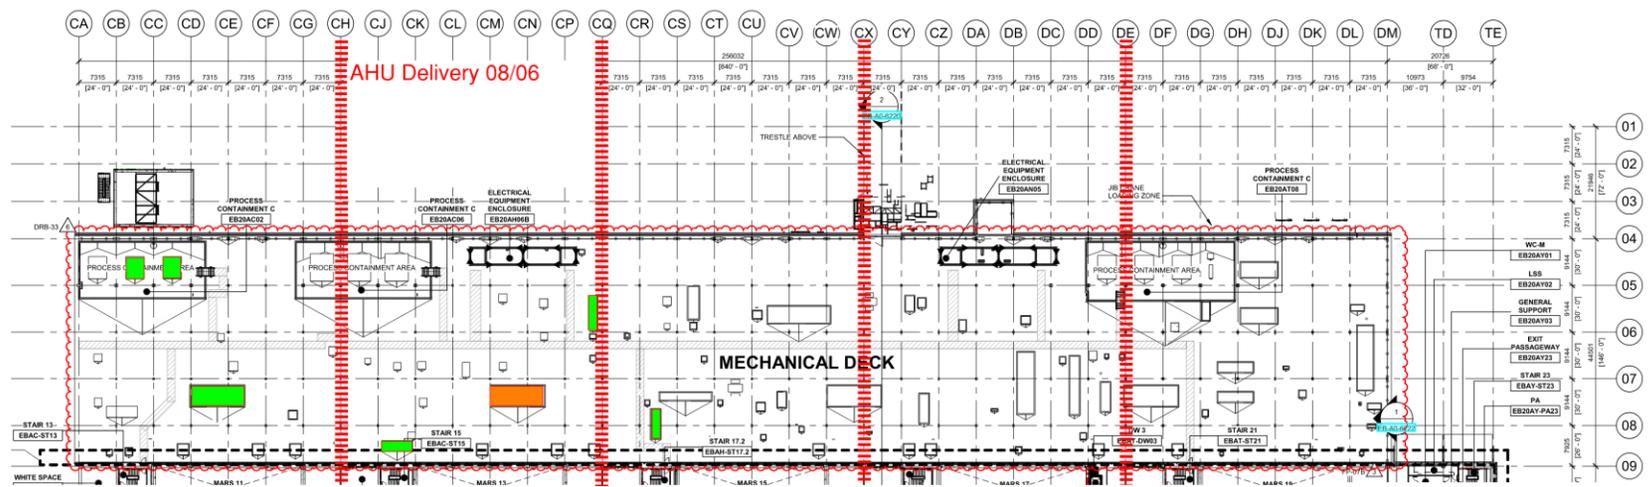

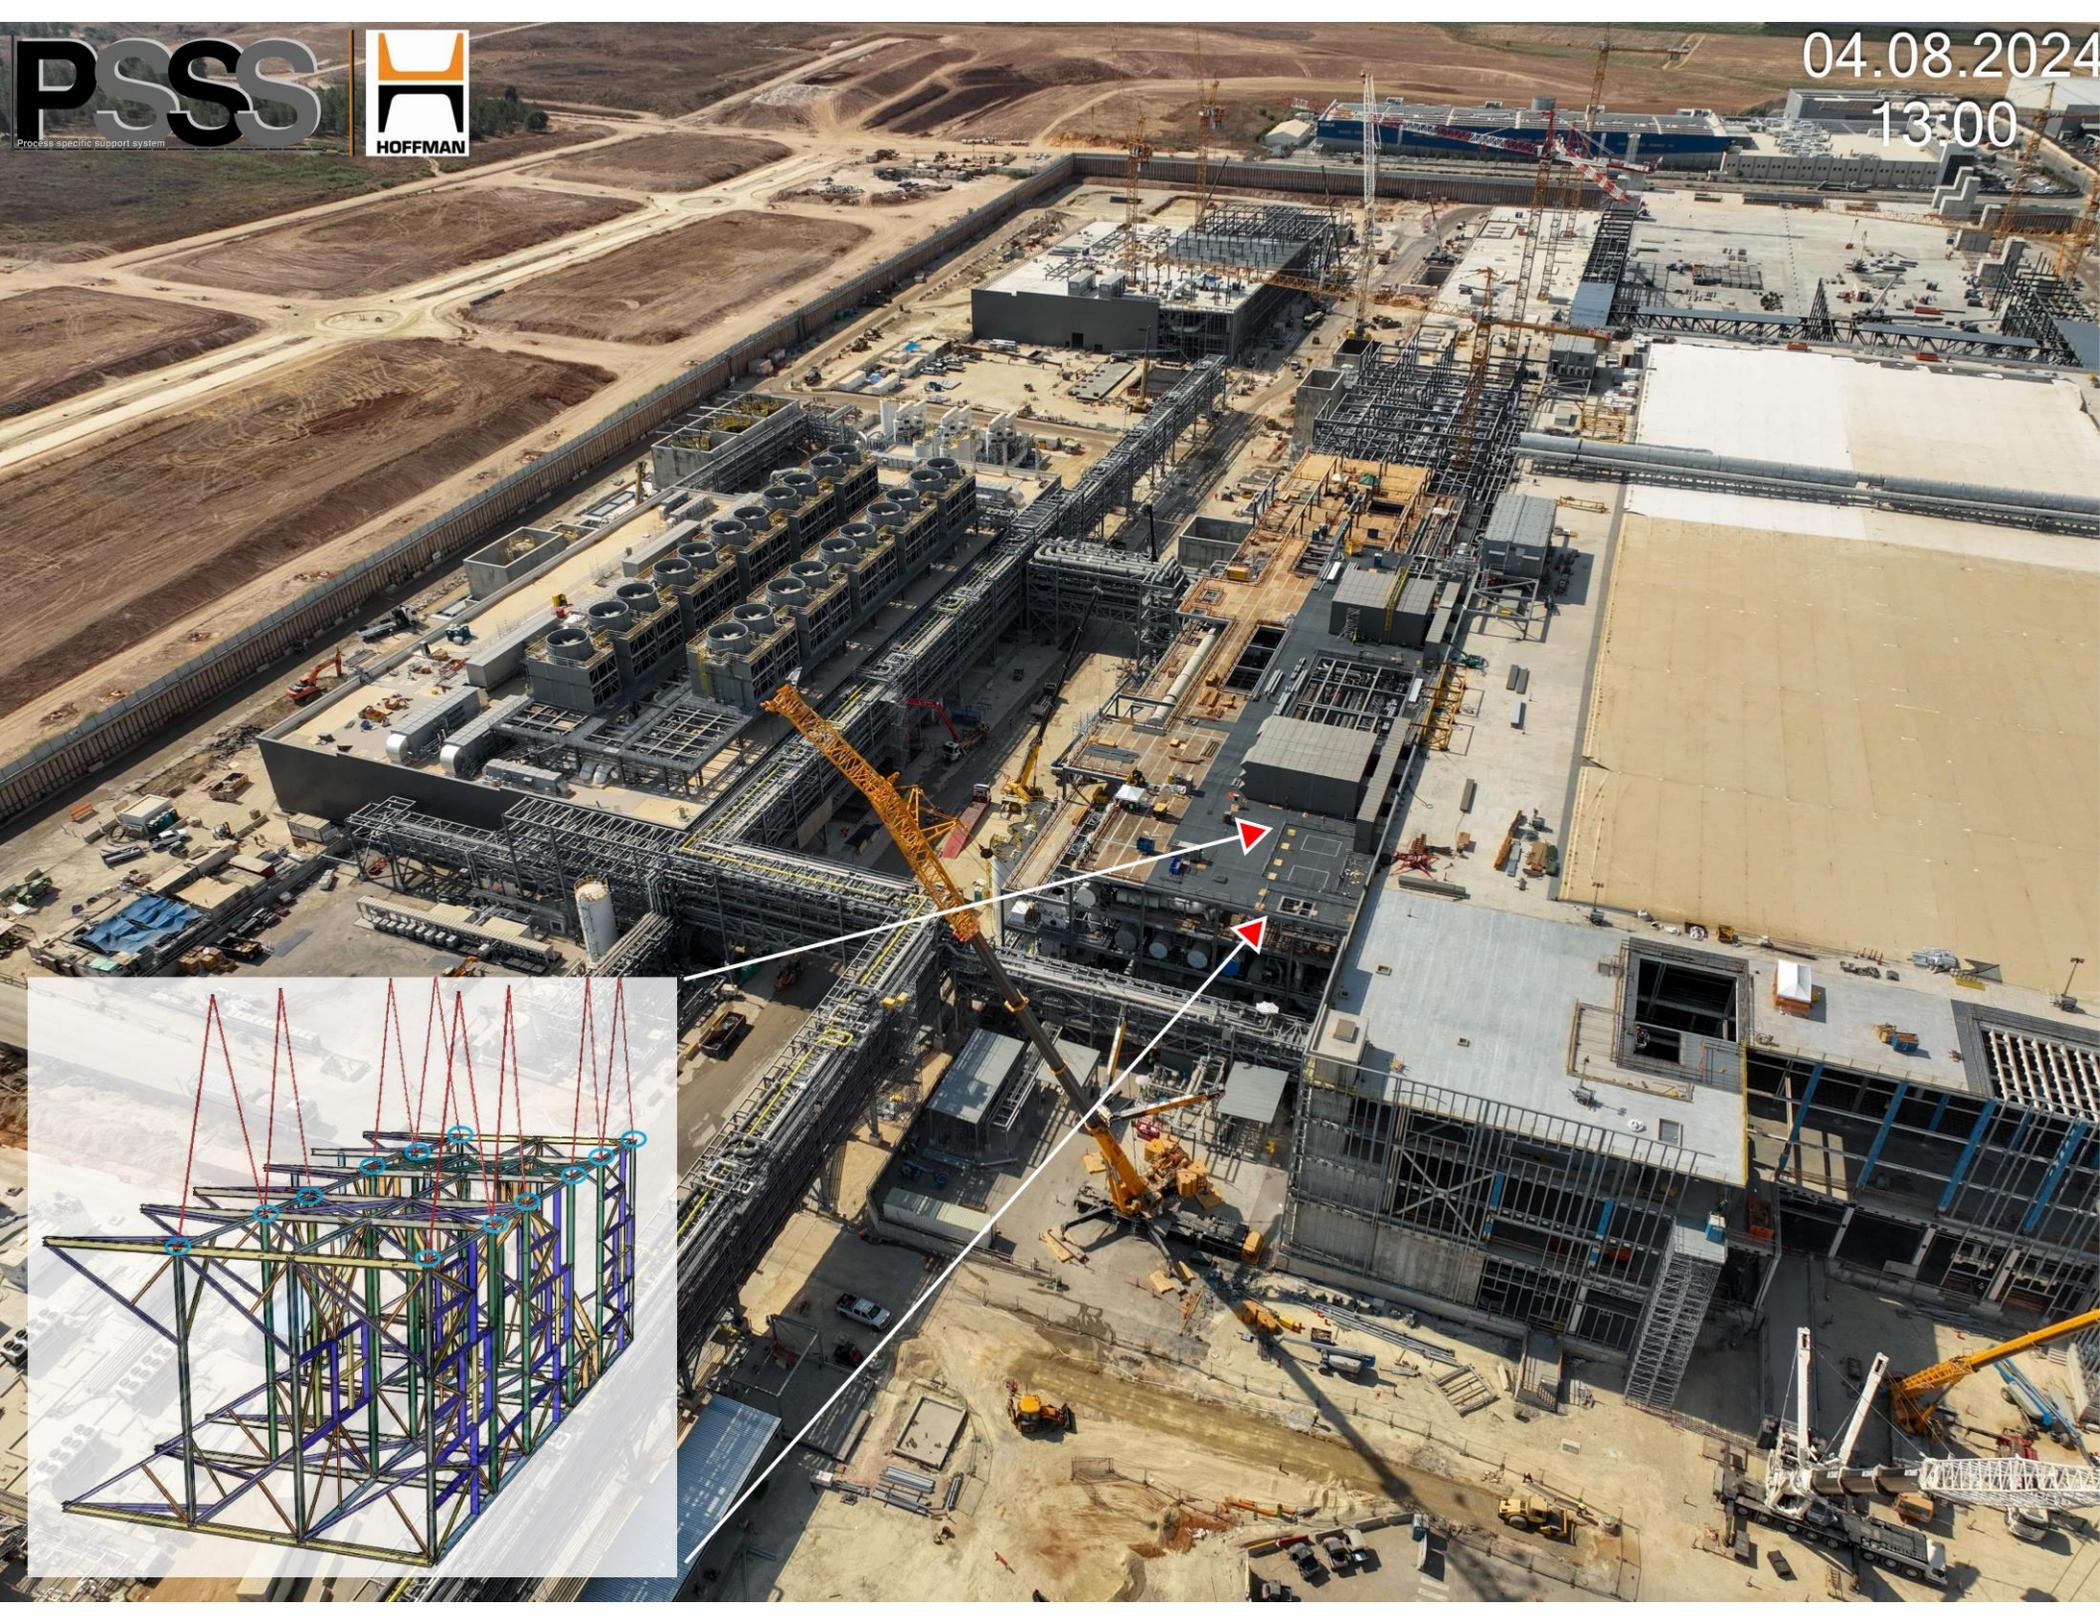



Single
EPA Platform


Fan

PSSS P1
PachTaas Operation
Plates: 15-08-2024
Air Blower: 20-08-2024
EPA Platform: 26-08-2024


WJG 01J, 02J LIFT 2 & 3



WJG 03J, 04J, 05J LIFT 2 & 3

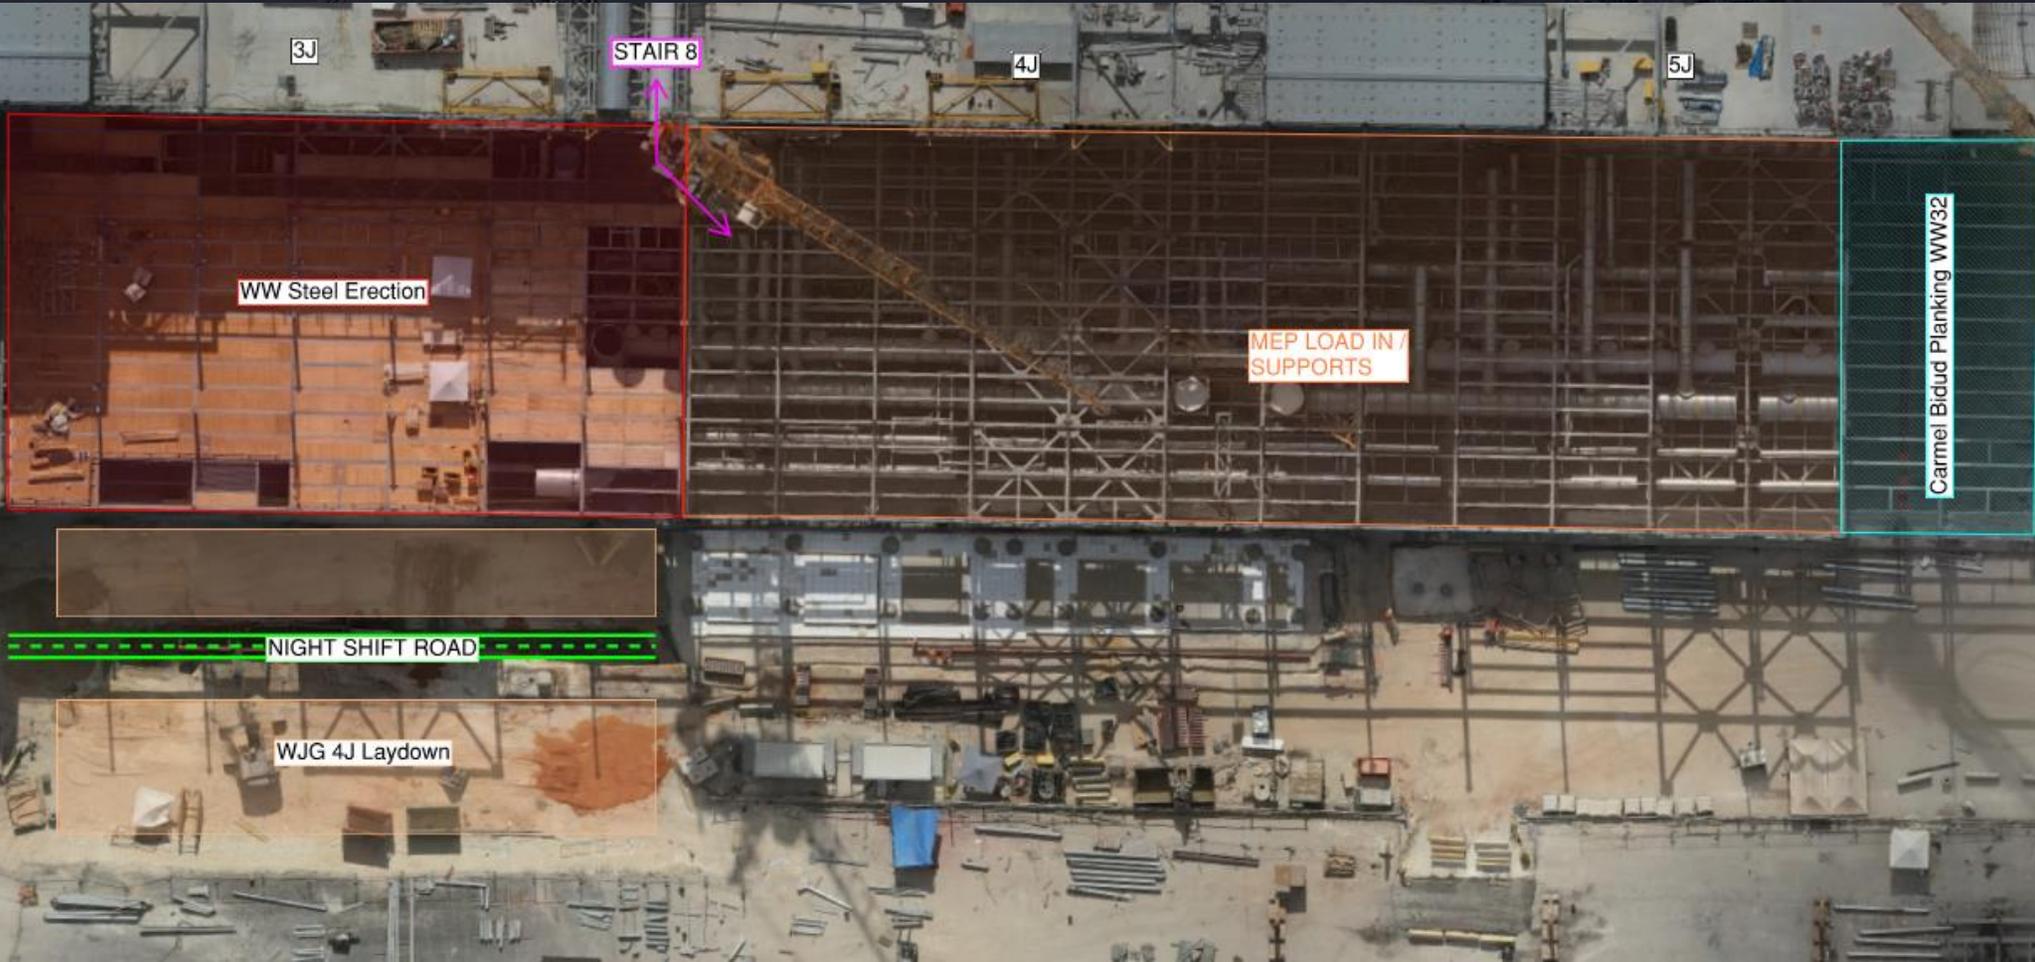


WJG UTILITY LEVEL BUILD OUT

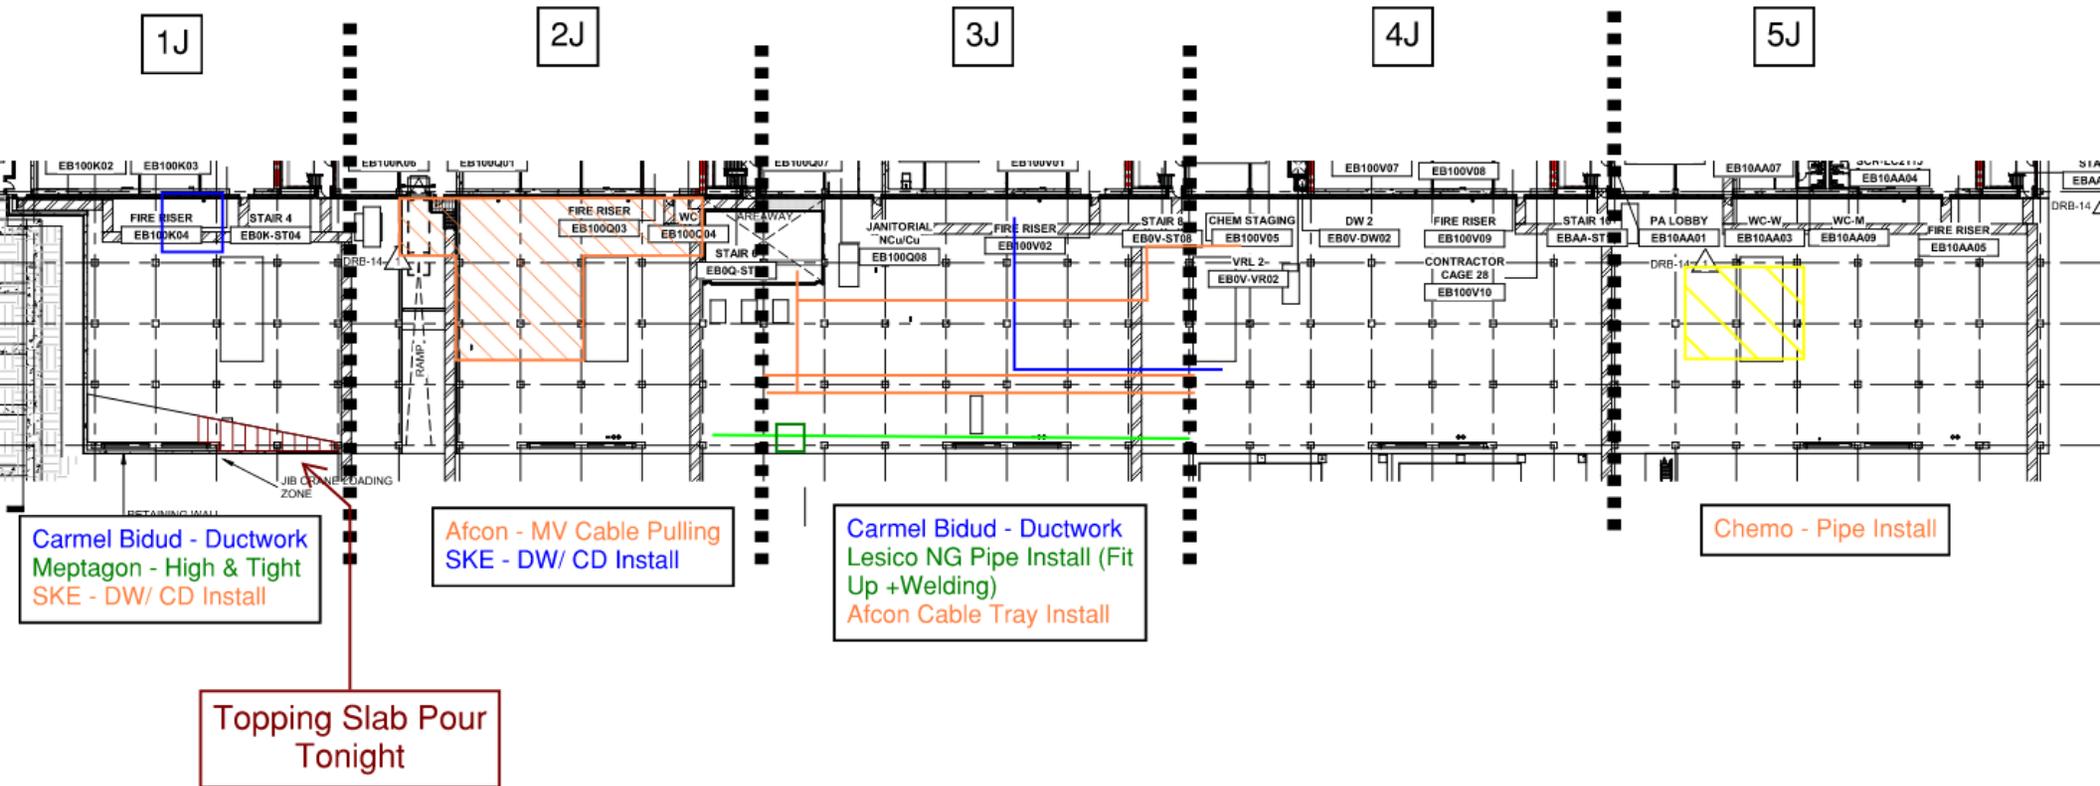

CUB 1

EAST YARD

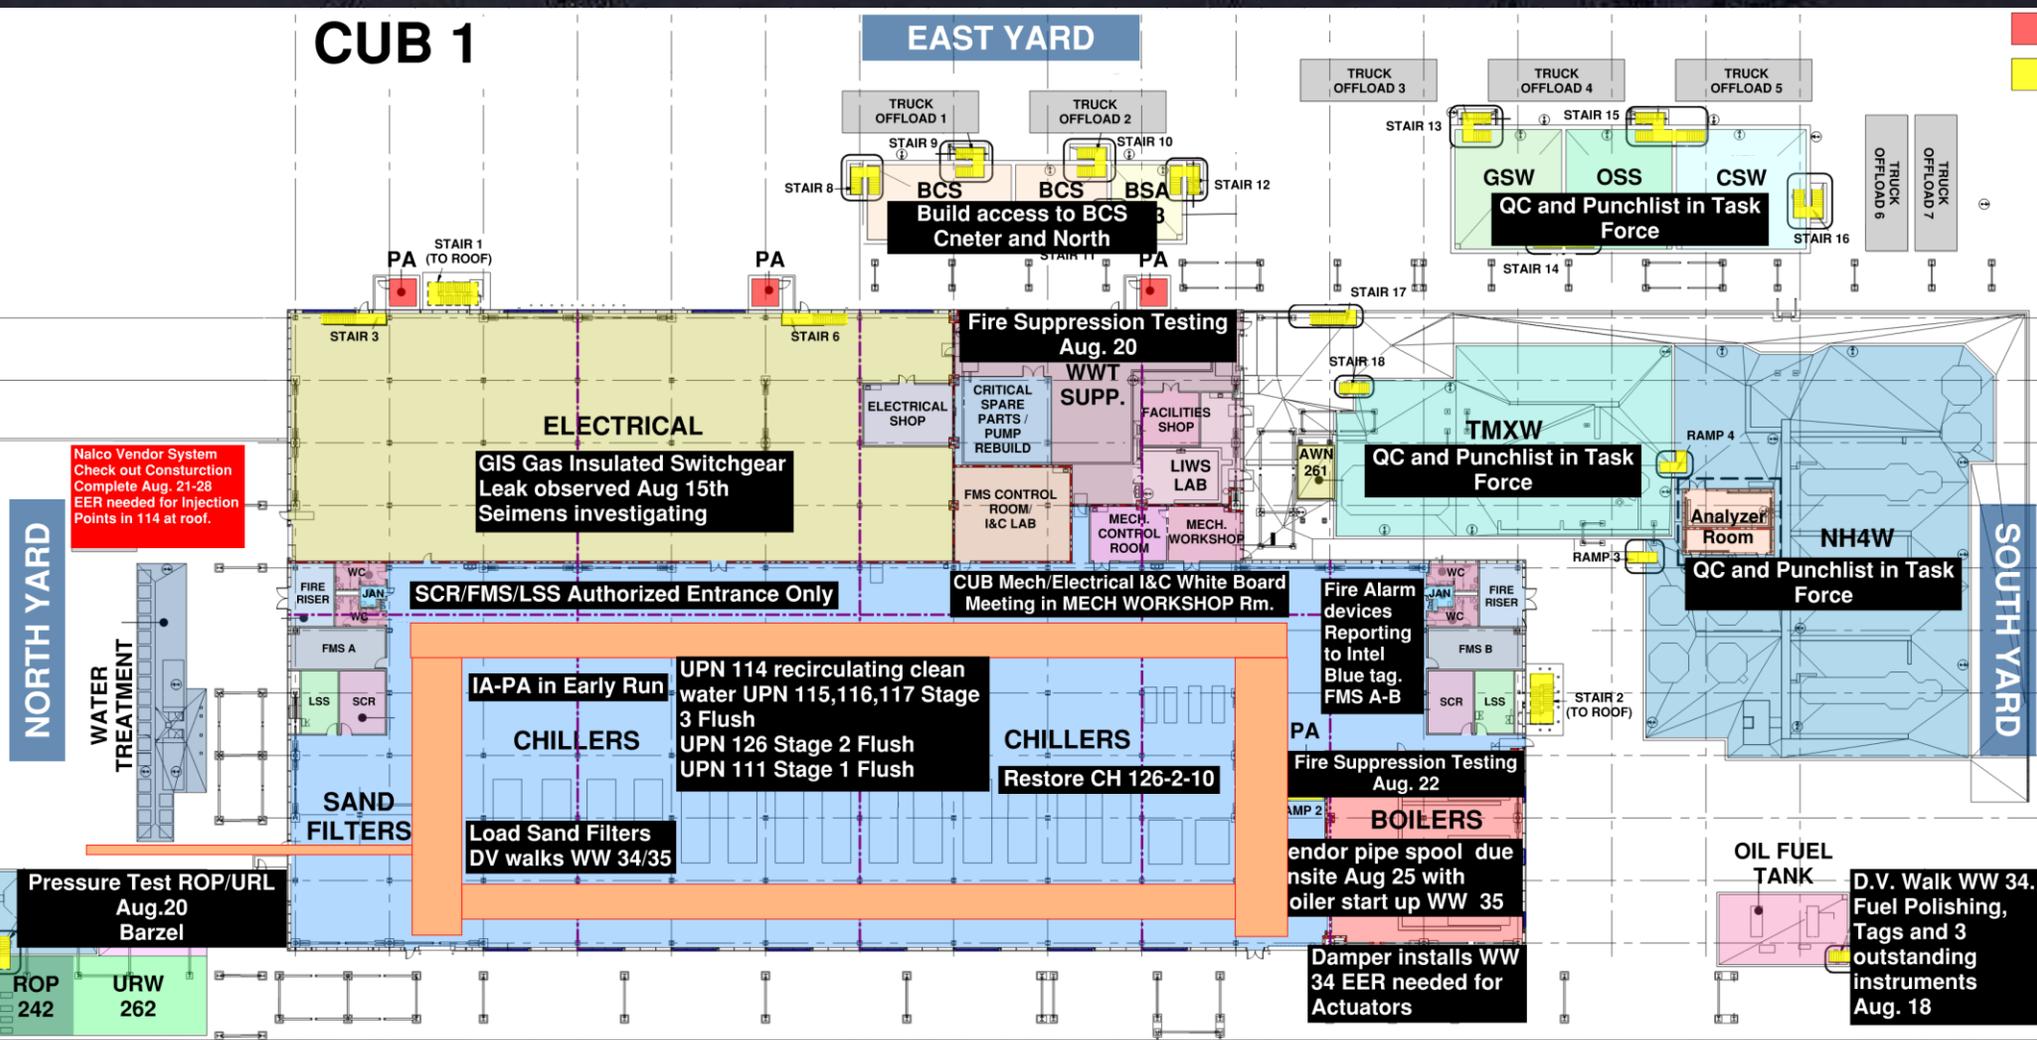

Nalco Vendor System
Check out Consturction
Complete Aug. 21-28
EER needed for Injection
Points in 114 at roof.

GIS Gas Insulated Switchgear
Leak observed Aug 15th
Seimens investigating

Fire Suppression Testing
Aug. 20
WWT SUPP.

QC and Punchlist in Task
Force

QC and Punchlist in Task
Force

IA-PA in Early Run
UPN 114 recirculating clean
water UPN 115,116,117 Stage
3 Flush
UPN 126 Stage 2 Flush
UPN 111 Stage 1 Flush

Load Sand Filters
DV walks WW 34/35

Restore CH 126-2-10


Fire Suppression Testing
Aug. 22


BOILERS
vendor pipe spool due
onsite Aug 25 with
oiler start up WW 35

Damper installs WW
34 EER needed for
Actuators


OIL FUEL
TANK
D.V. Walk WW 34.
Fuel Polishing,
Tags and 3
outstanding
instruments
Aug. 18




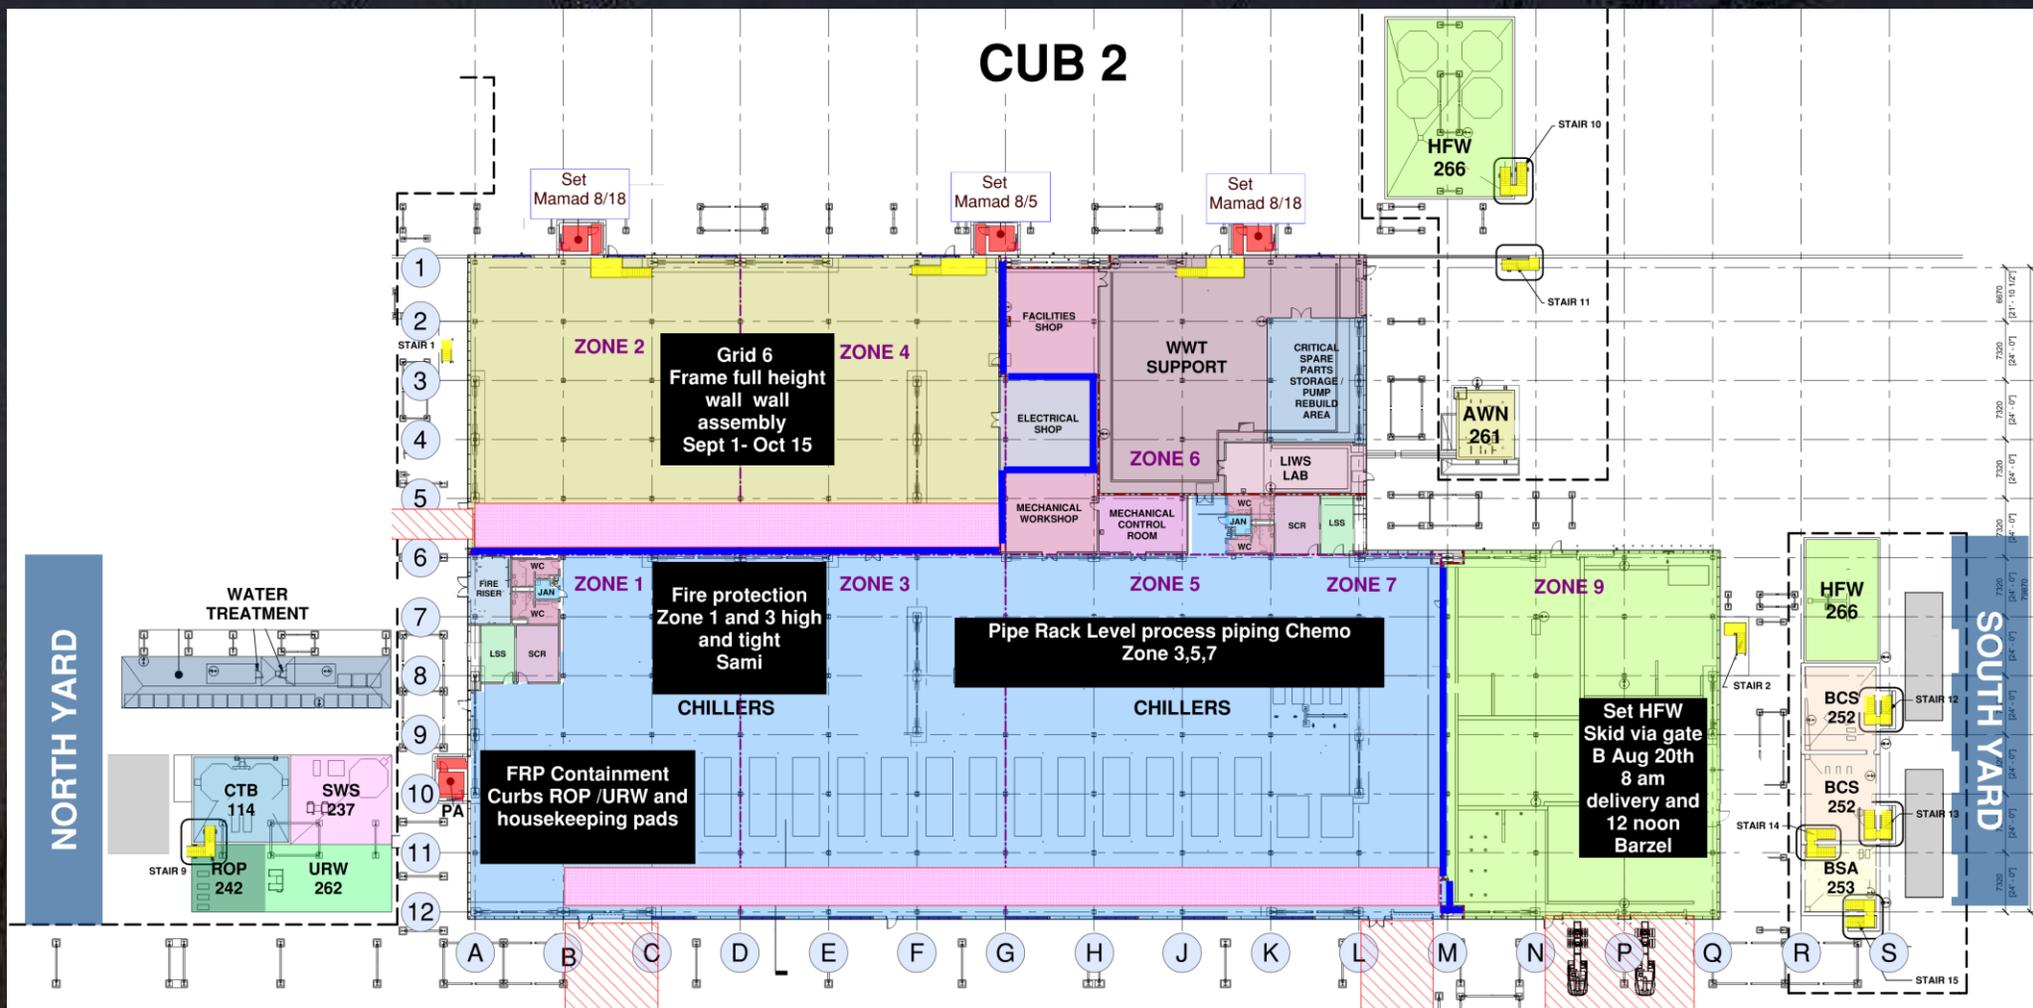

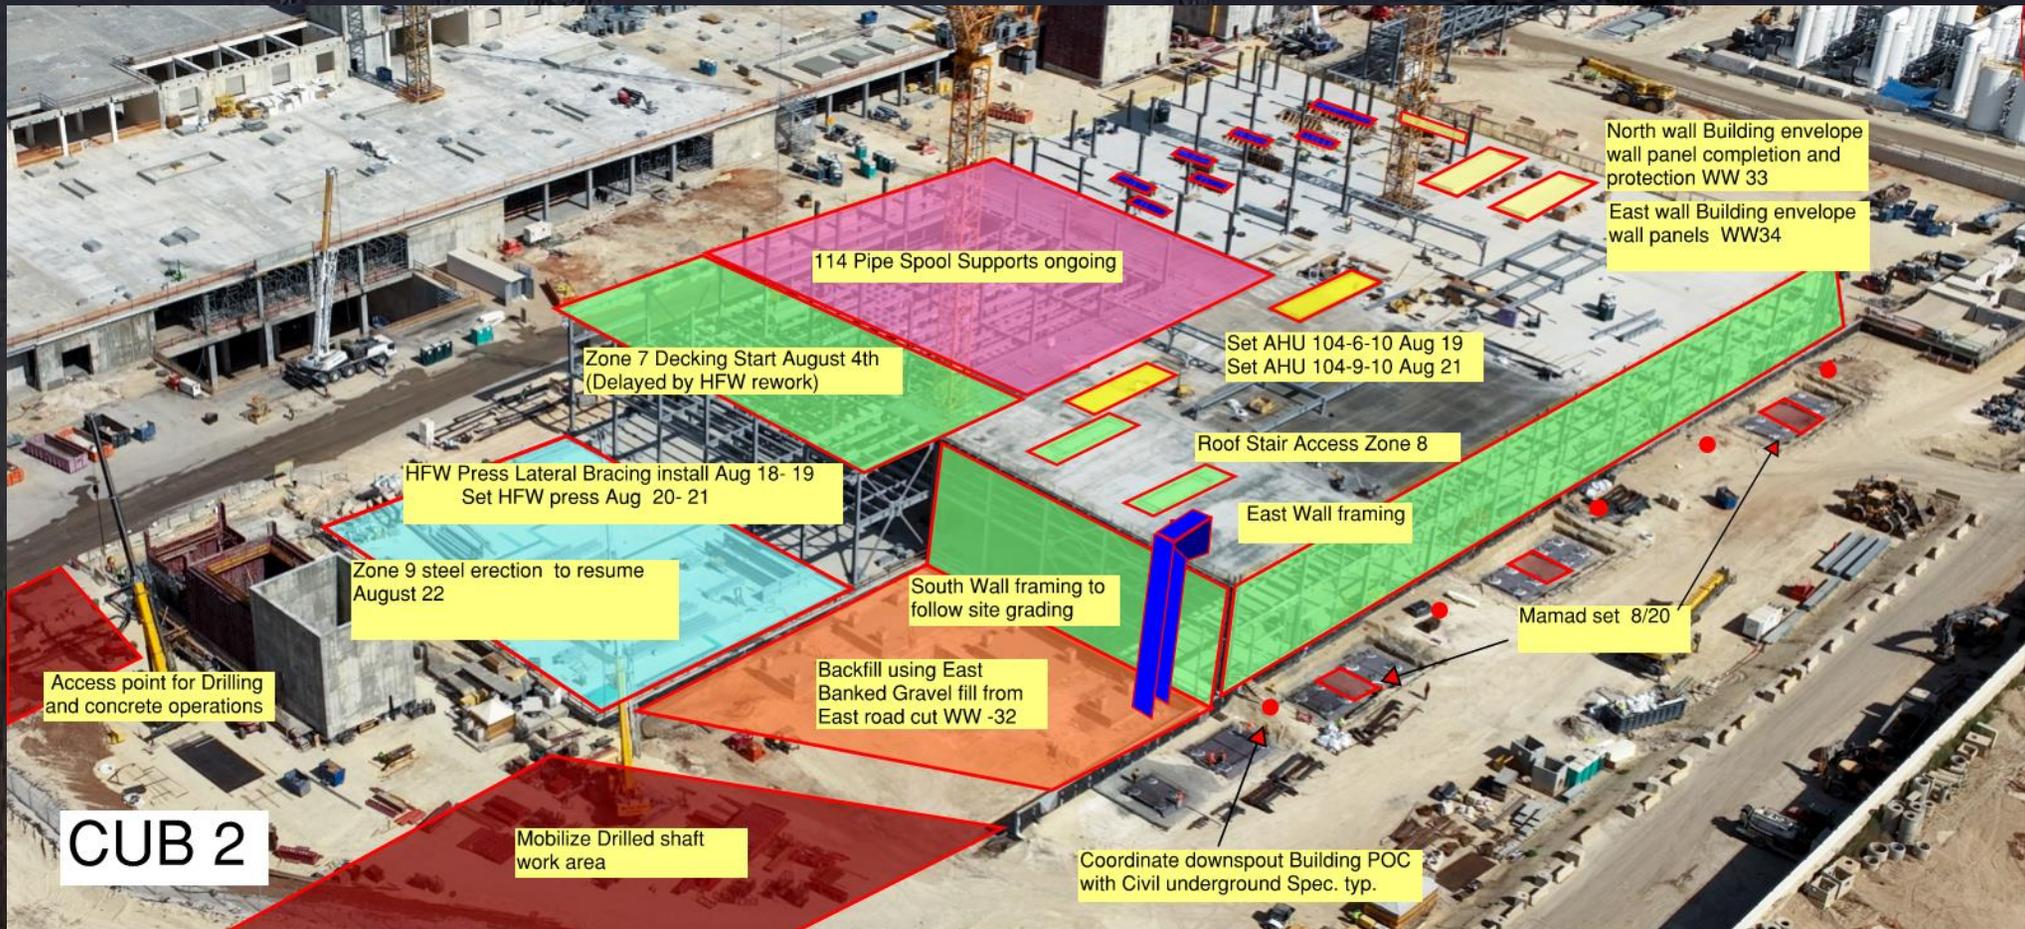

Mentorship and Leadership acknowledgement of the CUB 2 team (HASI, Rampro, Pachtaas, Avi Crane)

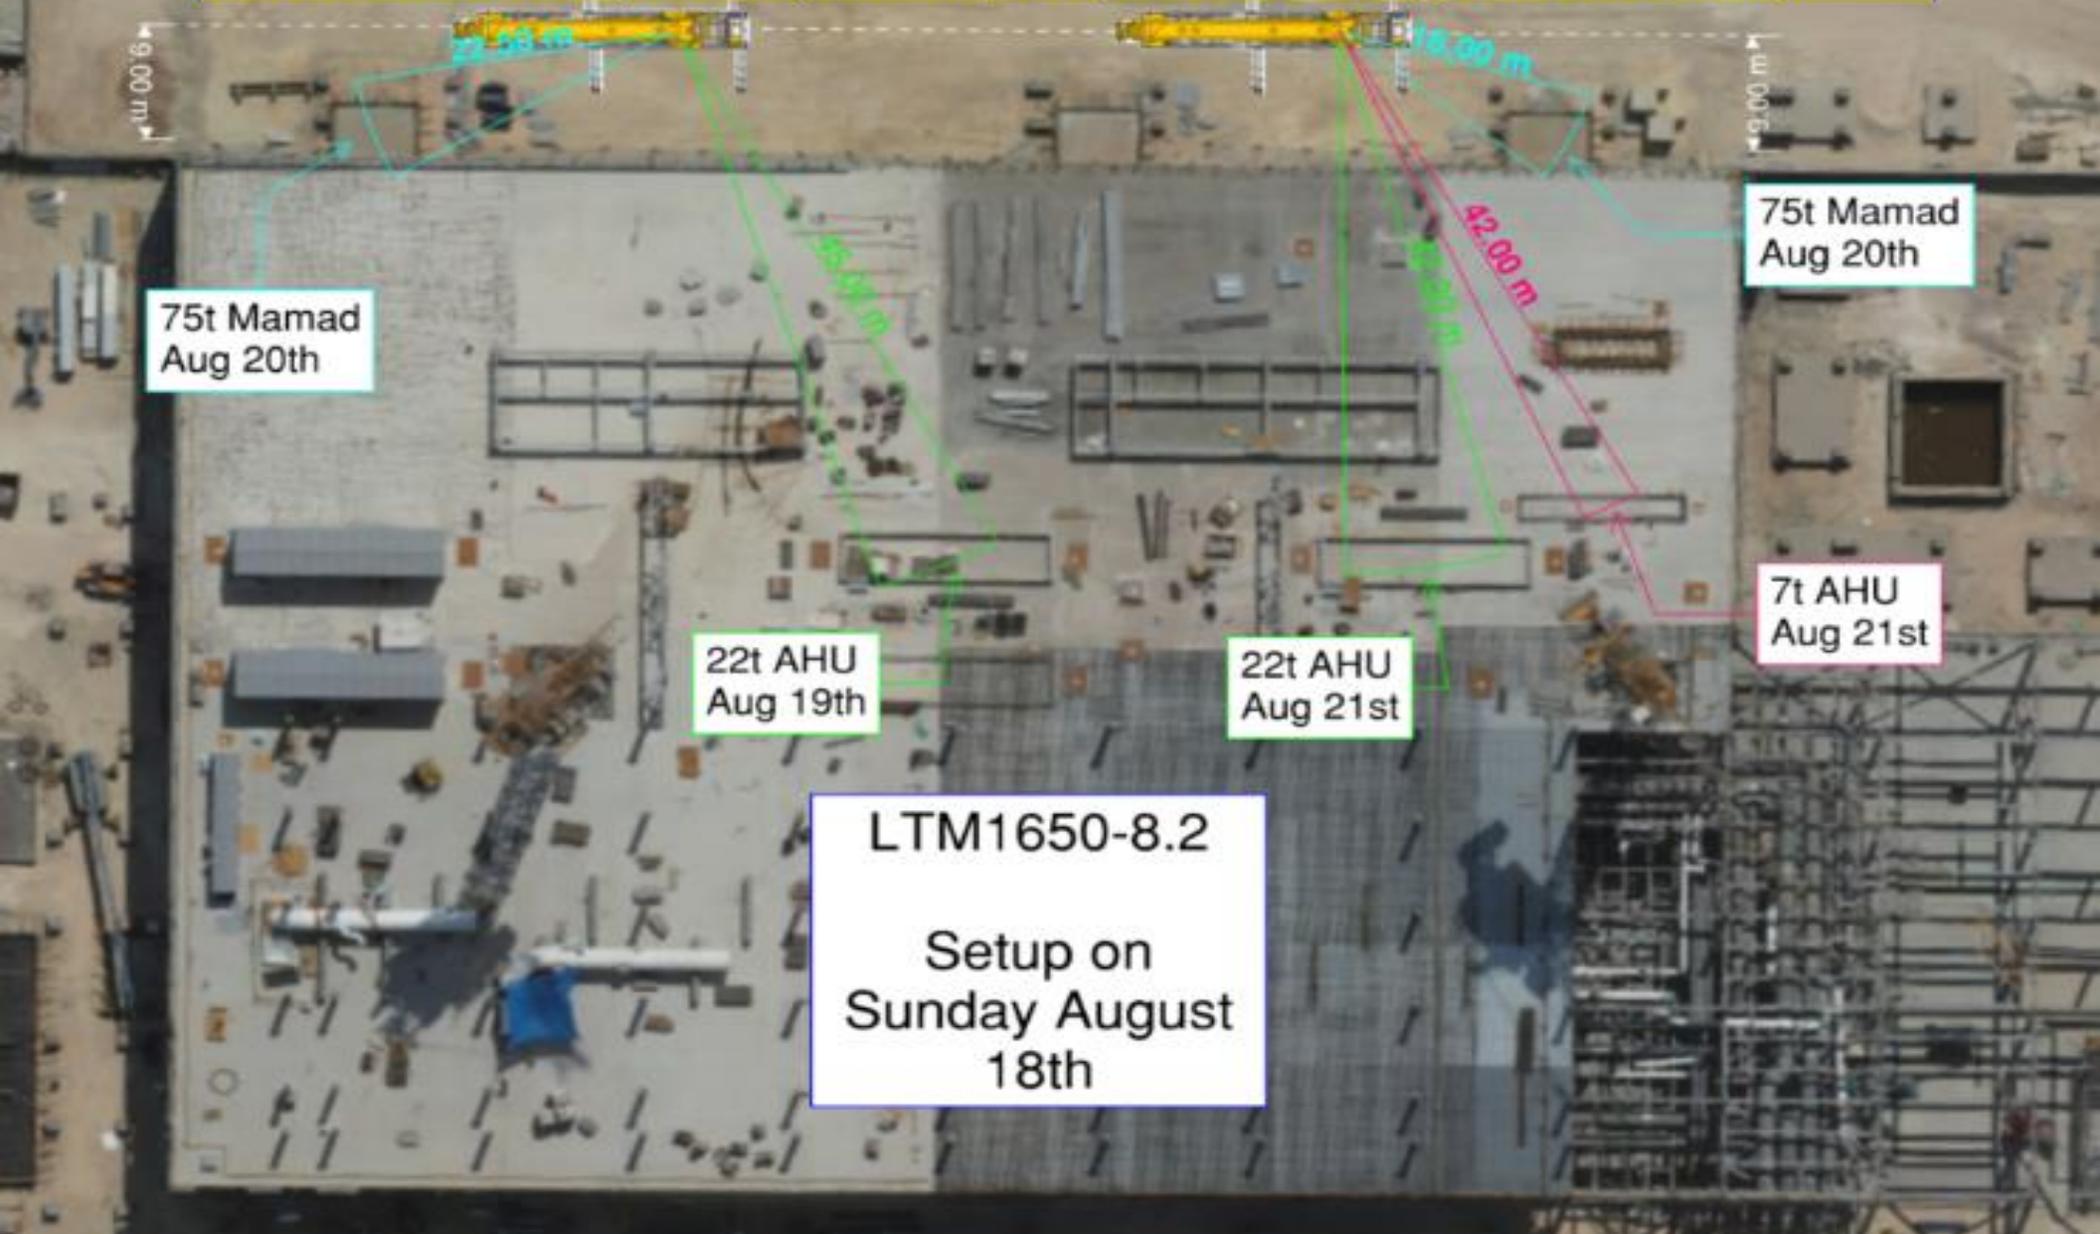

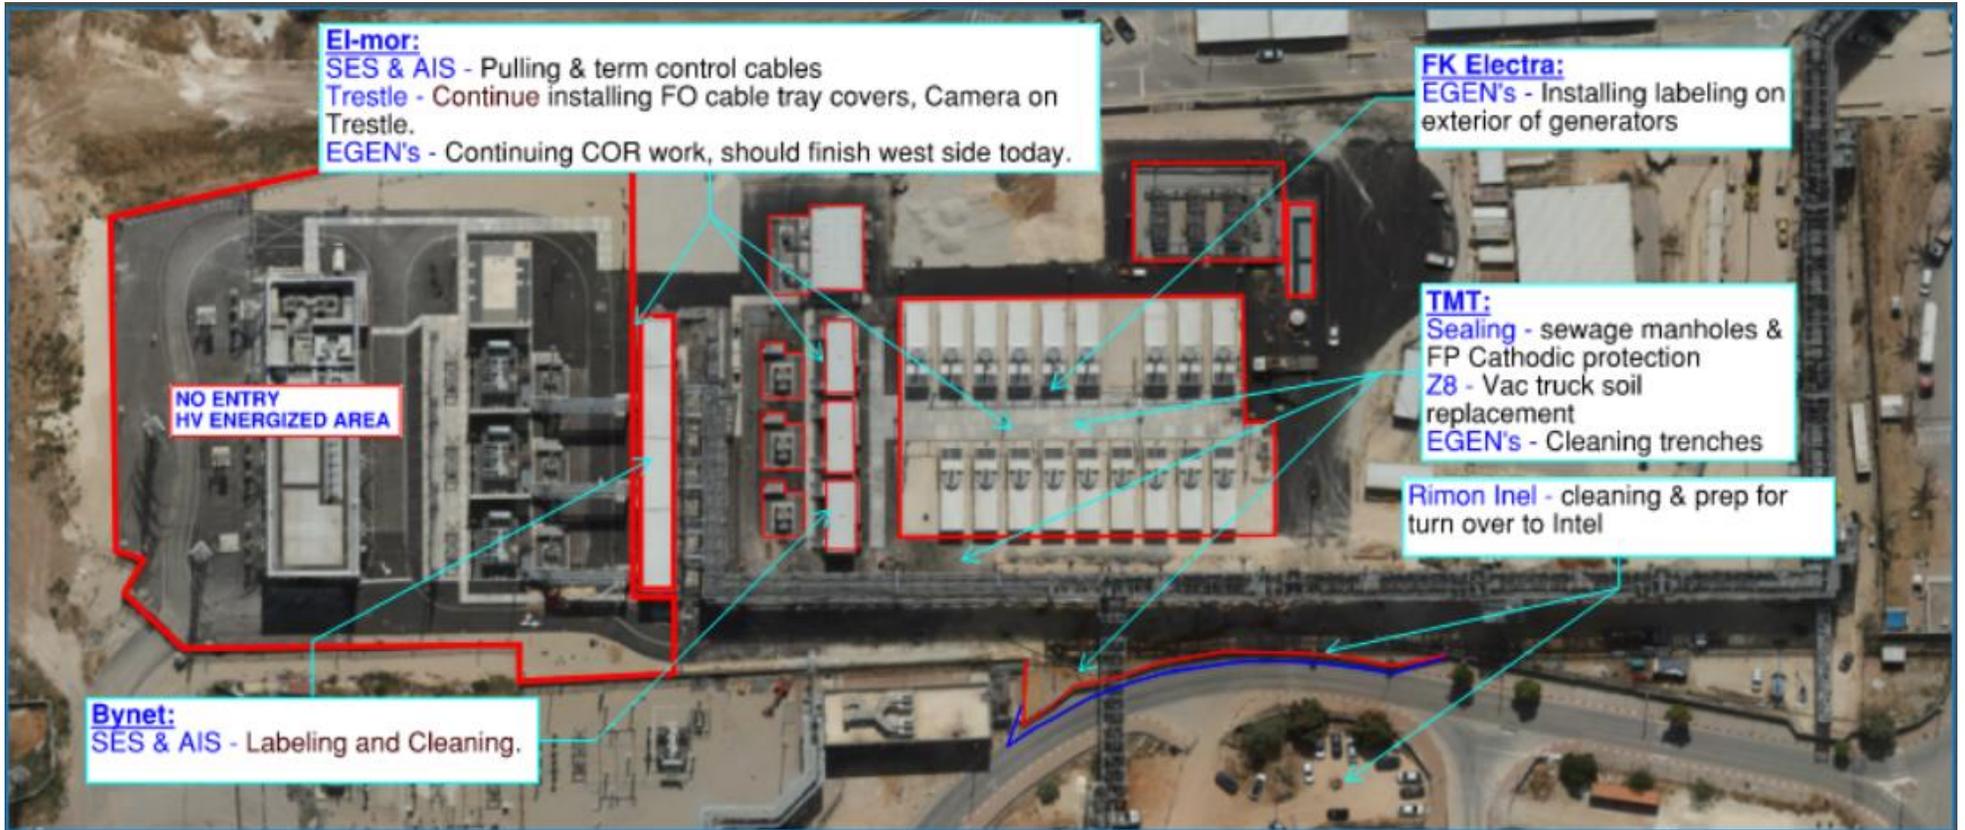



LTM 1650-8.1
60 meter radius
Chart Capacity 14t
Expected use 9t

Crane setup Aug 22
Hook Ready Aug 25


Replace 29 lids marked with yellow and remove 10 lids marked with red.

5.50 m

17.00 m

60.00 m


FAB GIS 33&34 Train A PERMENENT POWER AUGUST 27TH 17:00 to 18:00.

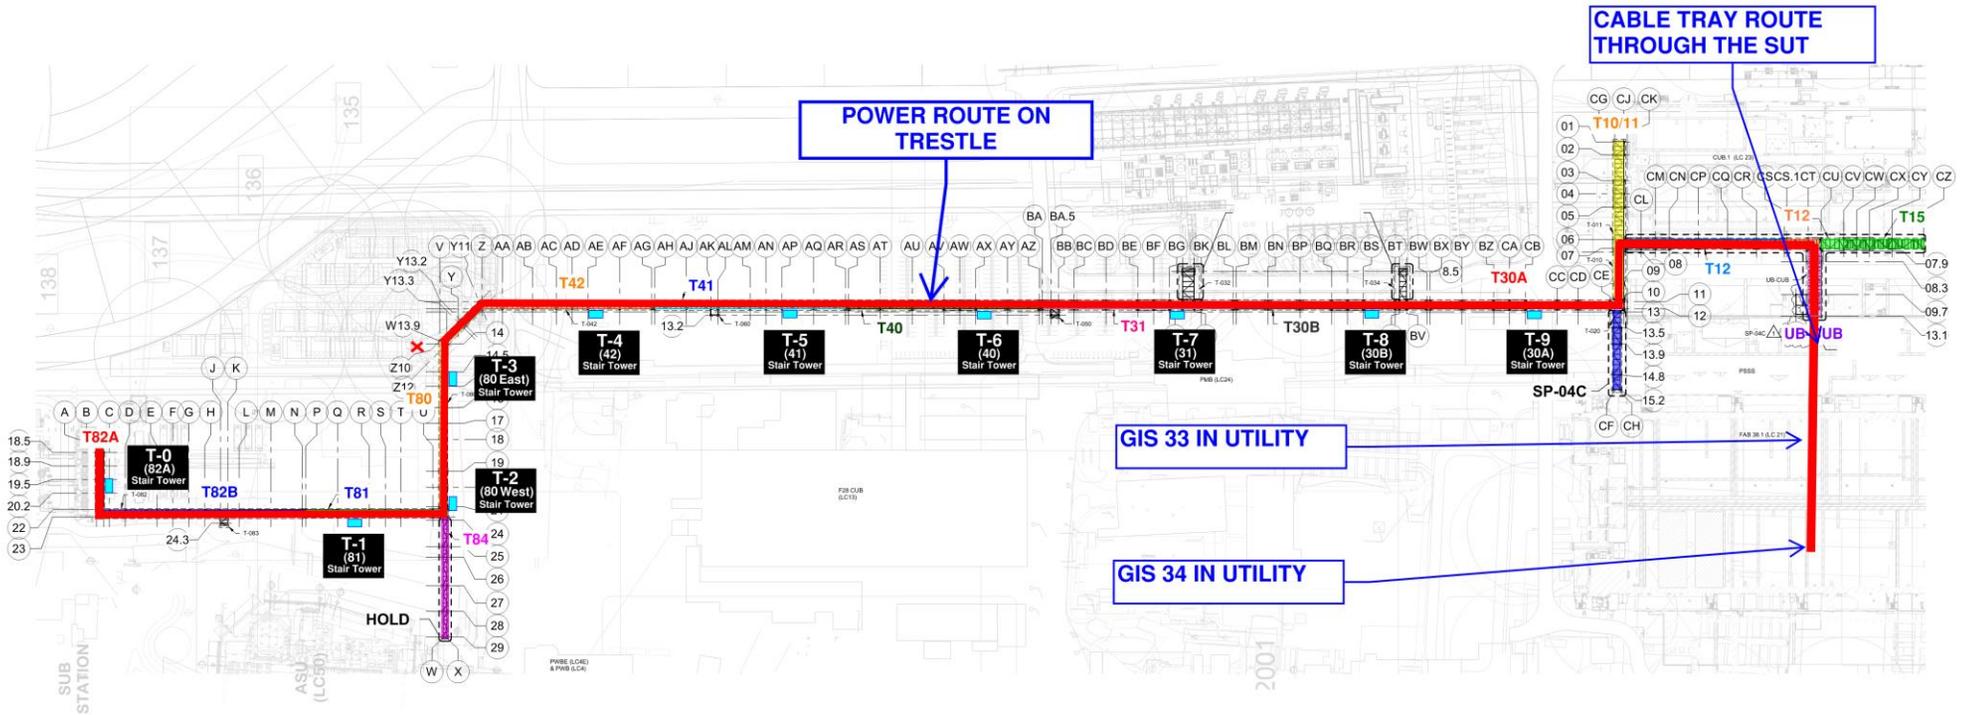




Trestle - MOD 2 Steel erection


T-17 Lvl 1

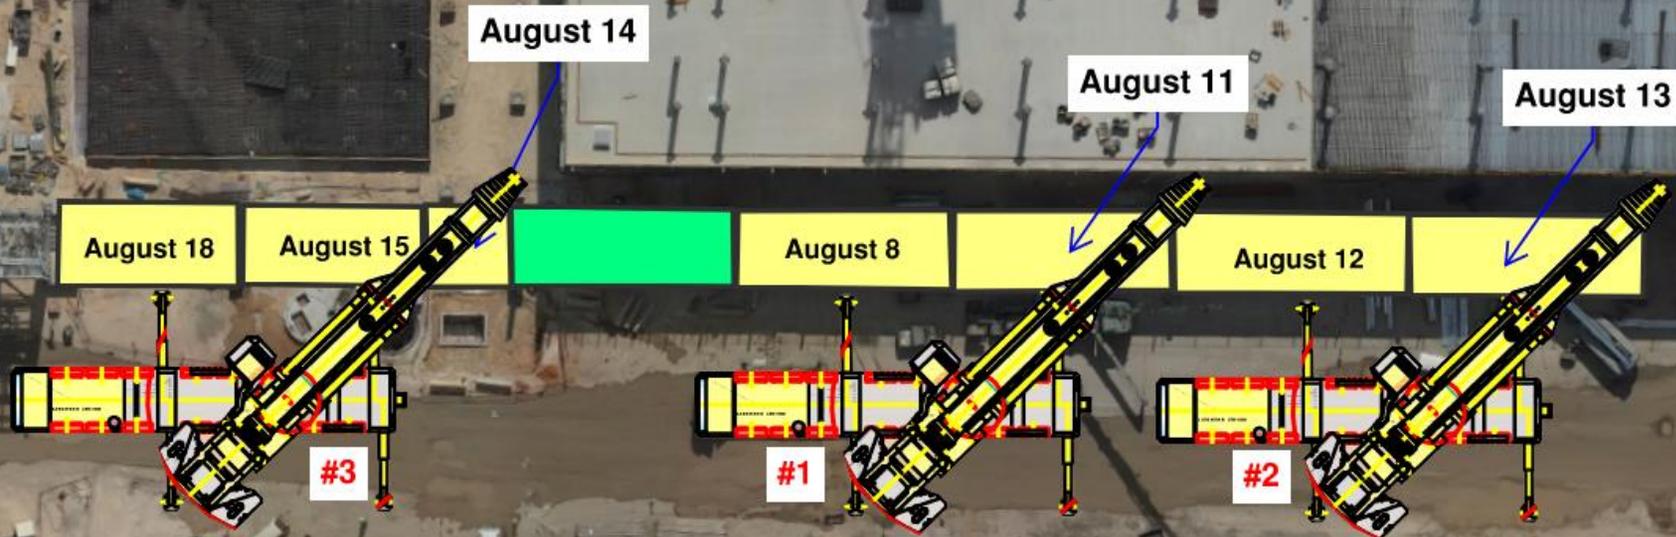

Trestle - MOD 2 Steel erection

T-17 Lvl 2

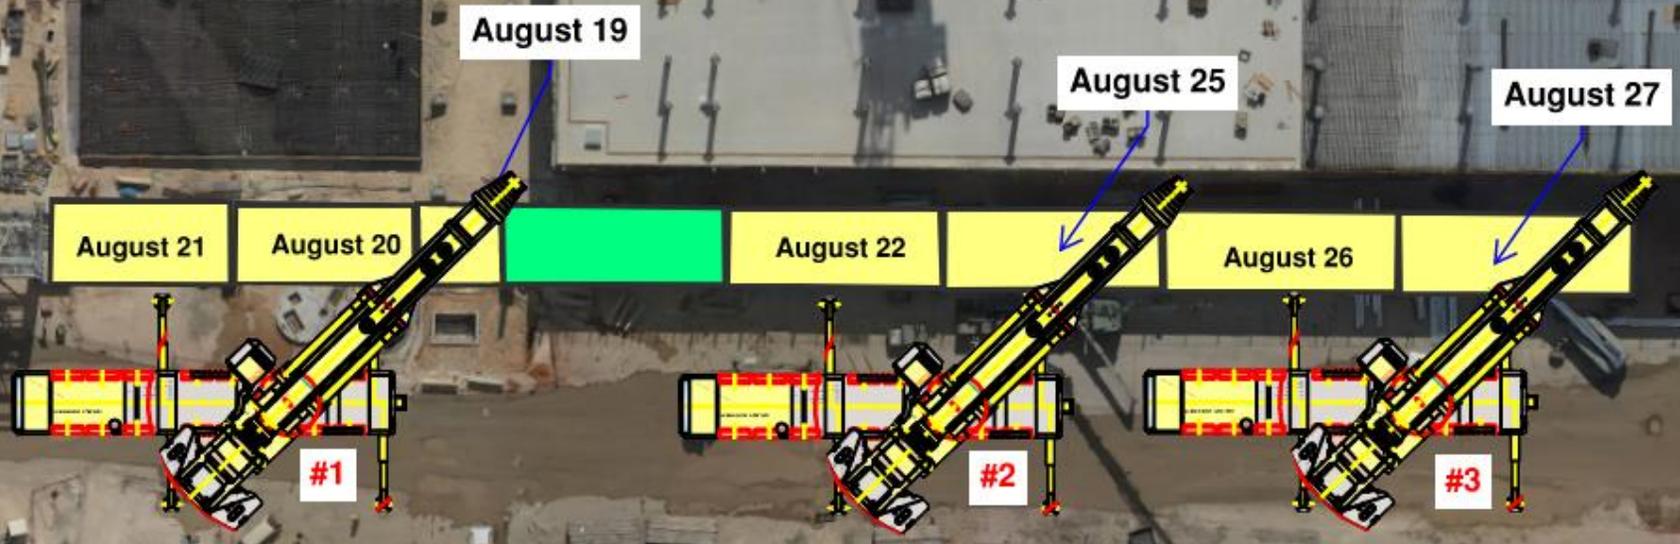




HOFFMAN CONSTRUCTION COMPANY





HOFFMAN
Sparrow  

BSGS

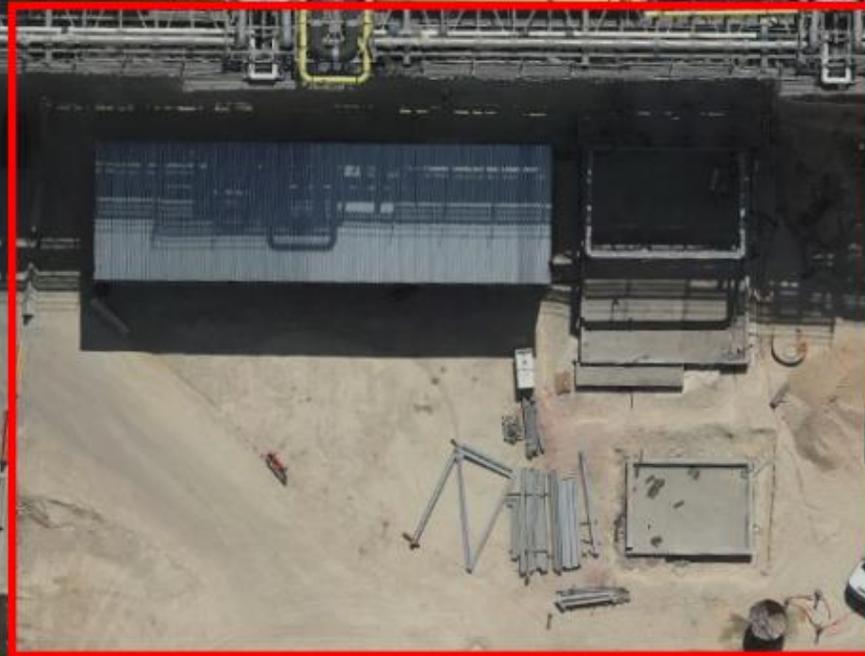


CENTER CATWALKS LEVEL 2 FIBER OPTIC TRAYS

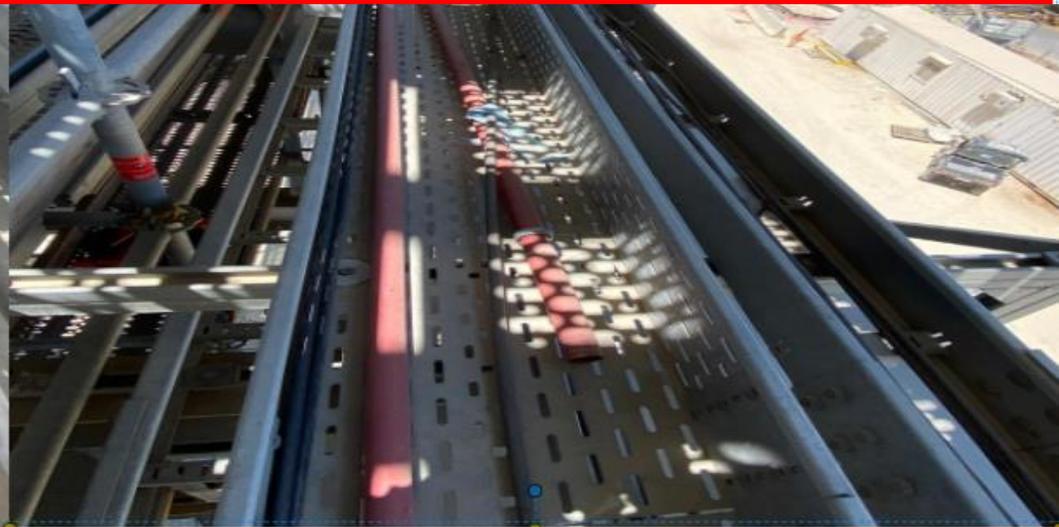

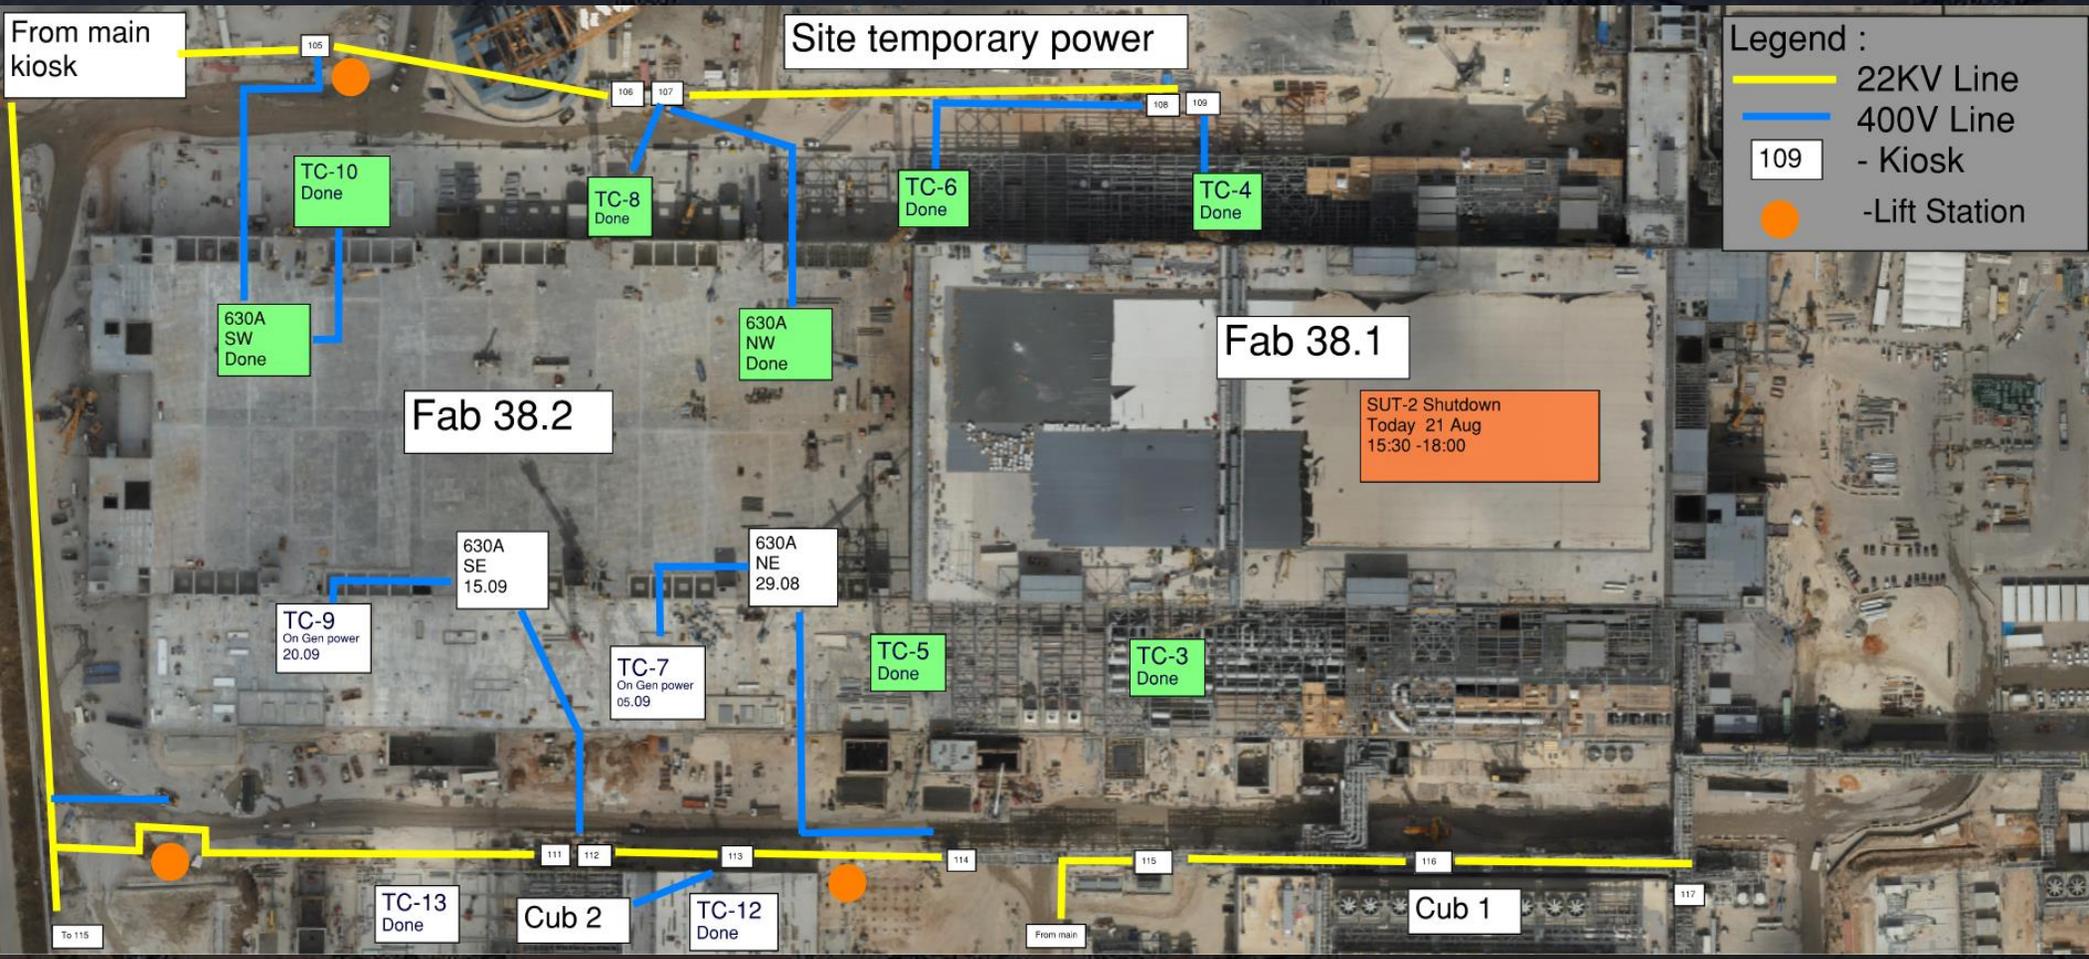

Daily Coordination Meeting


Site Logistics
North Gate B

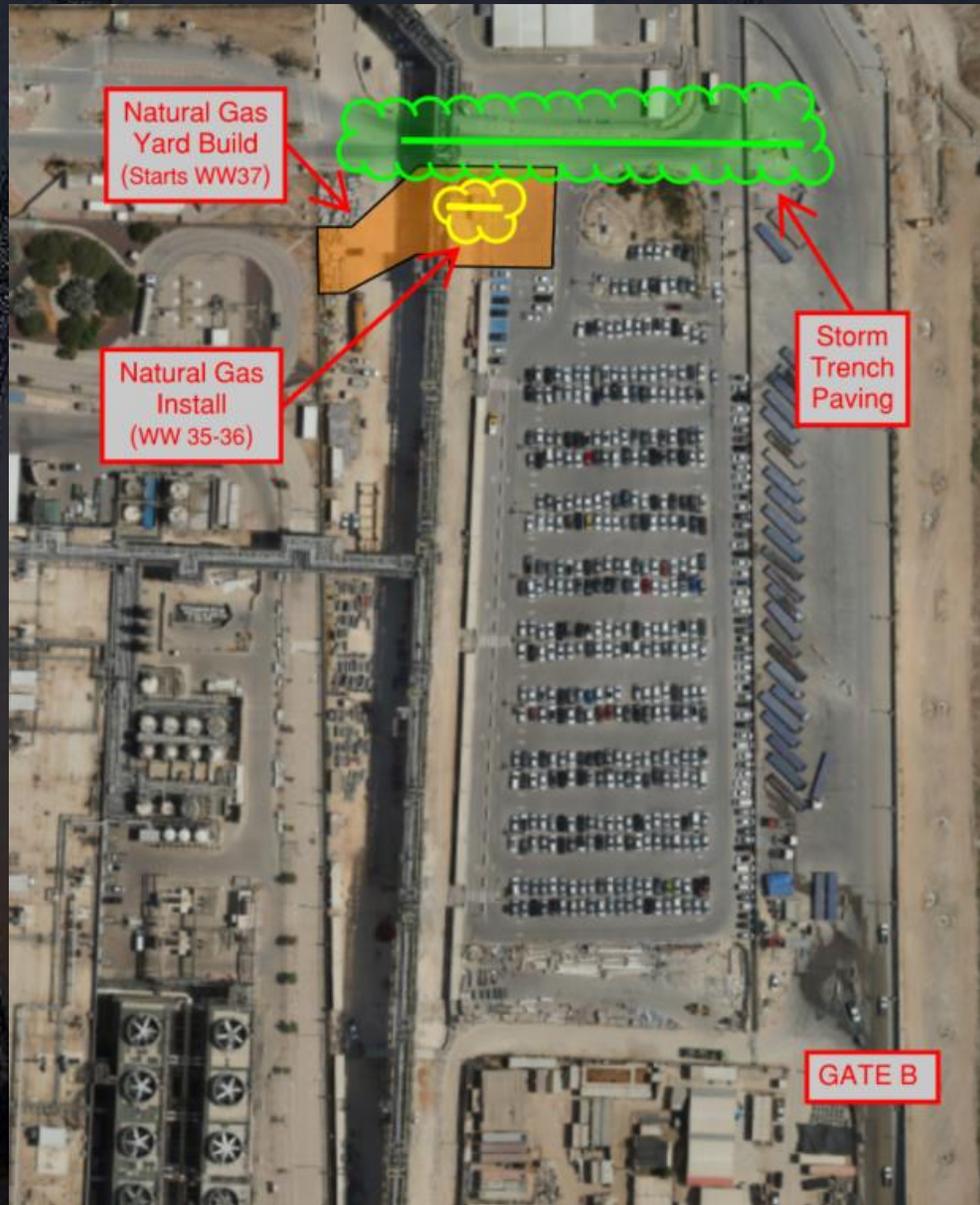

Daily Coordination Meeting

Site Logistics

North

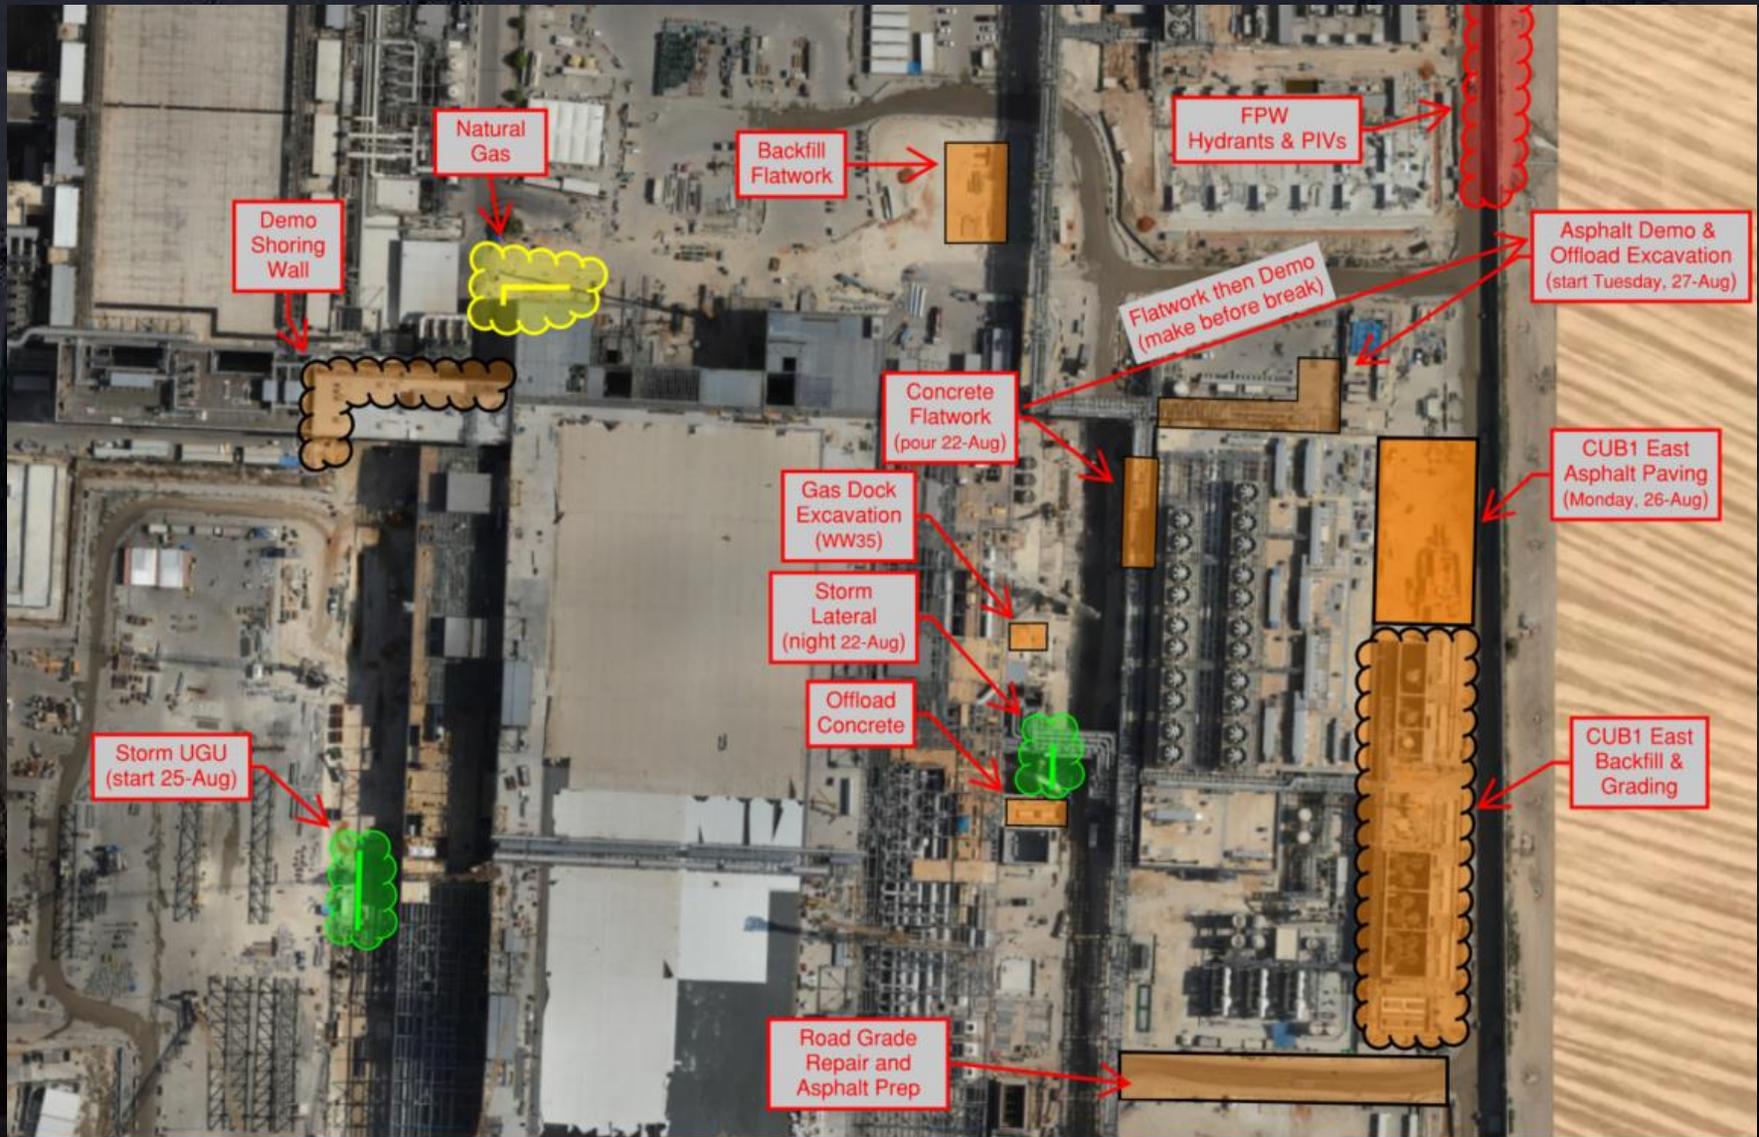

Daily Coordination Meeting

Site Logistics

South







Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

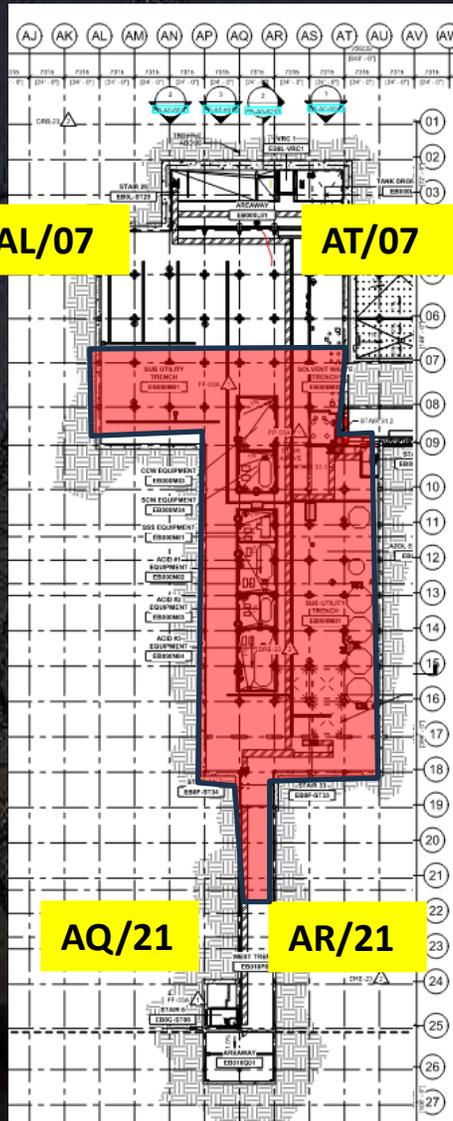


SUT2

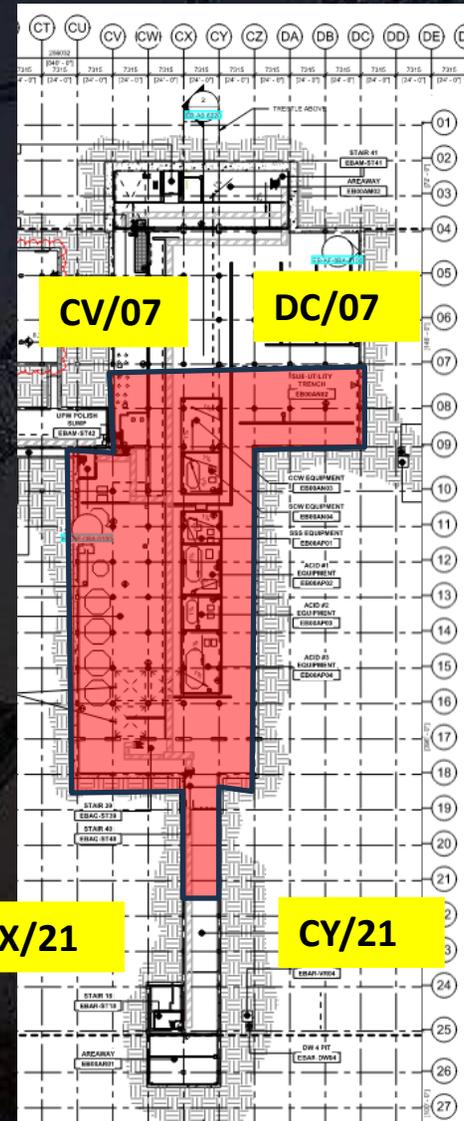

Daily Coordination Meeting


Site Logistics - Protected Areas (Utility Level)

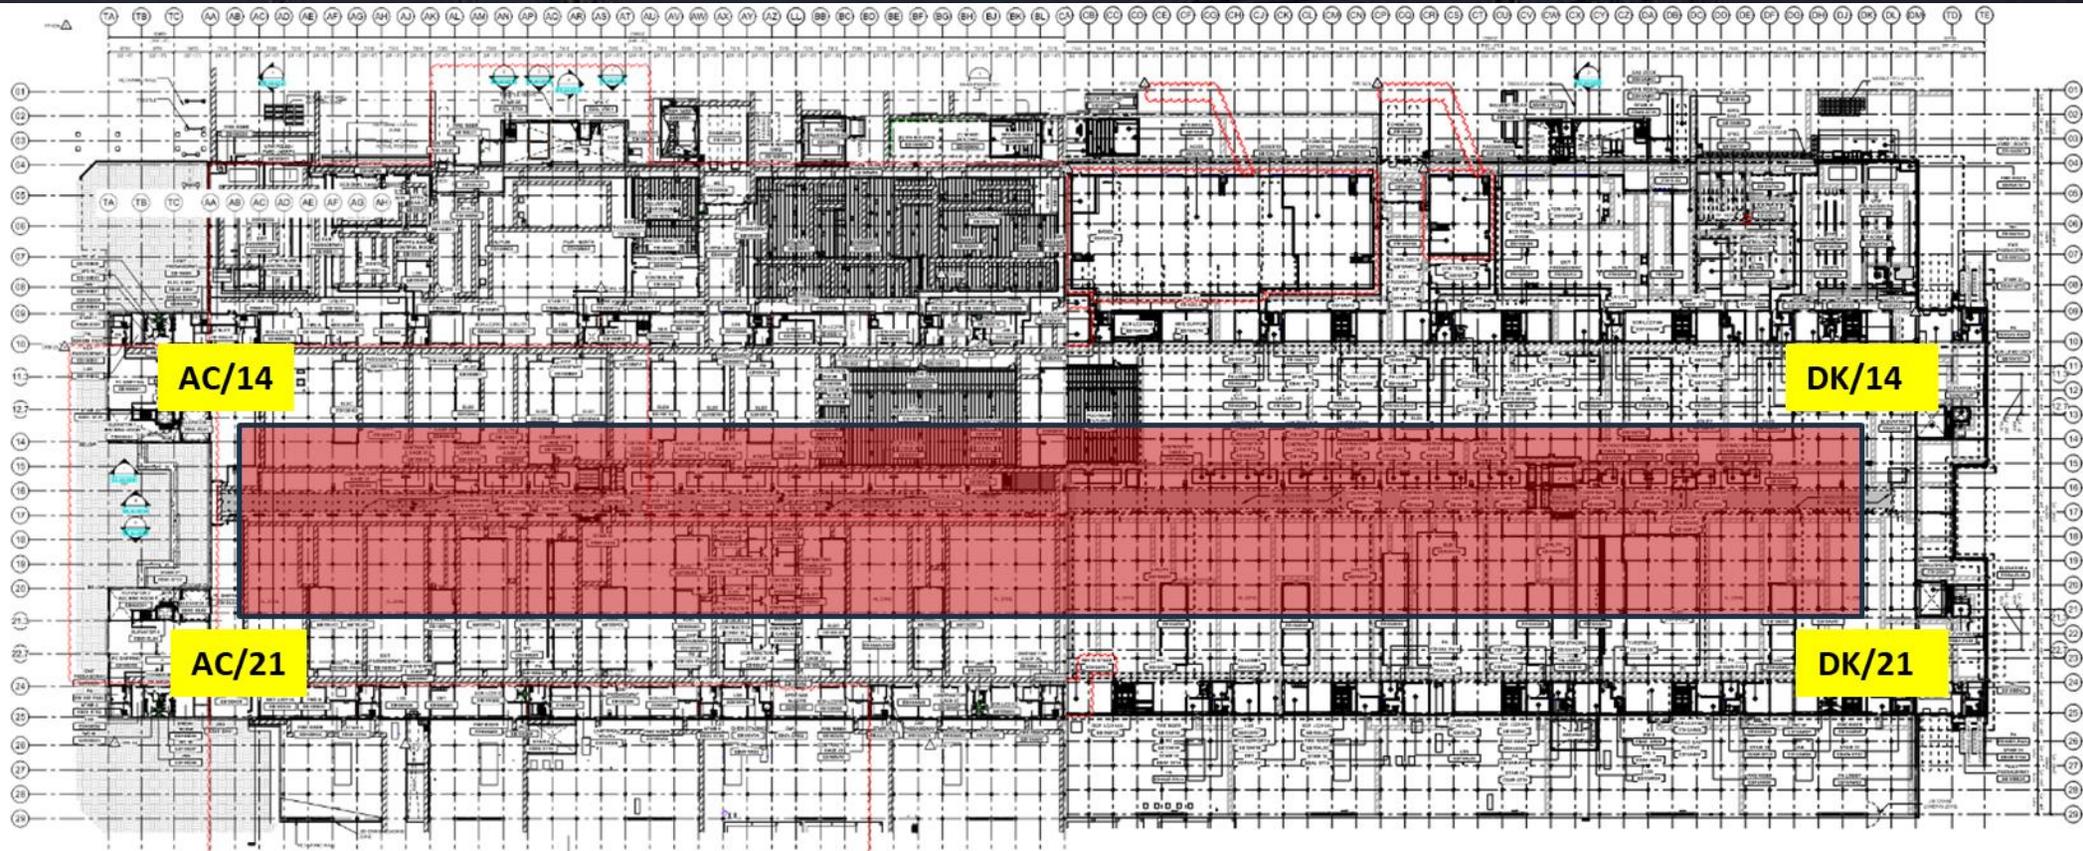



Daily Coordination Meeting


Site Logistics - Protected Areas (Subfab Level)

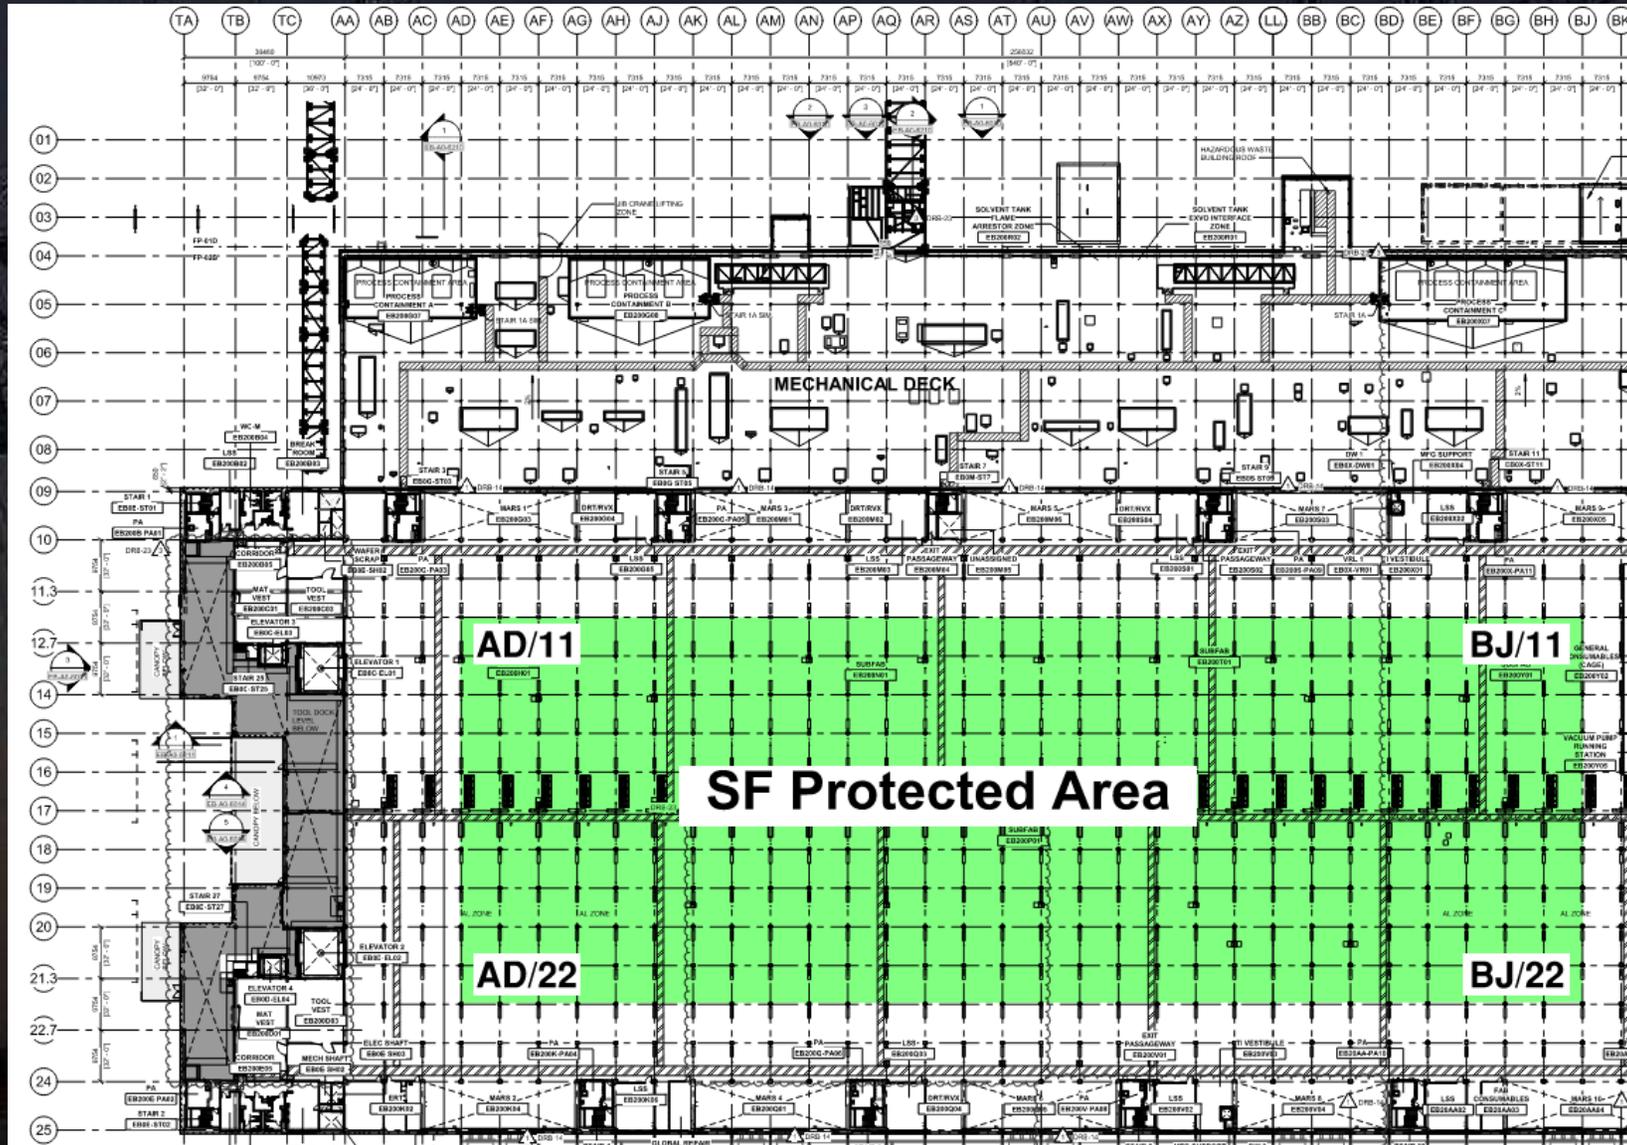

Daily Coordination Meeting


Site Logistics

Protected Areas

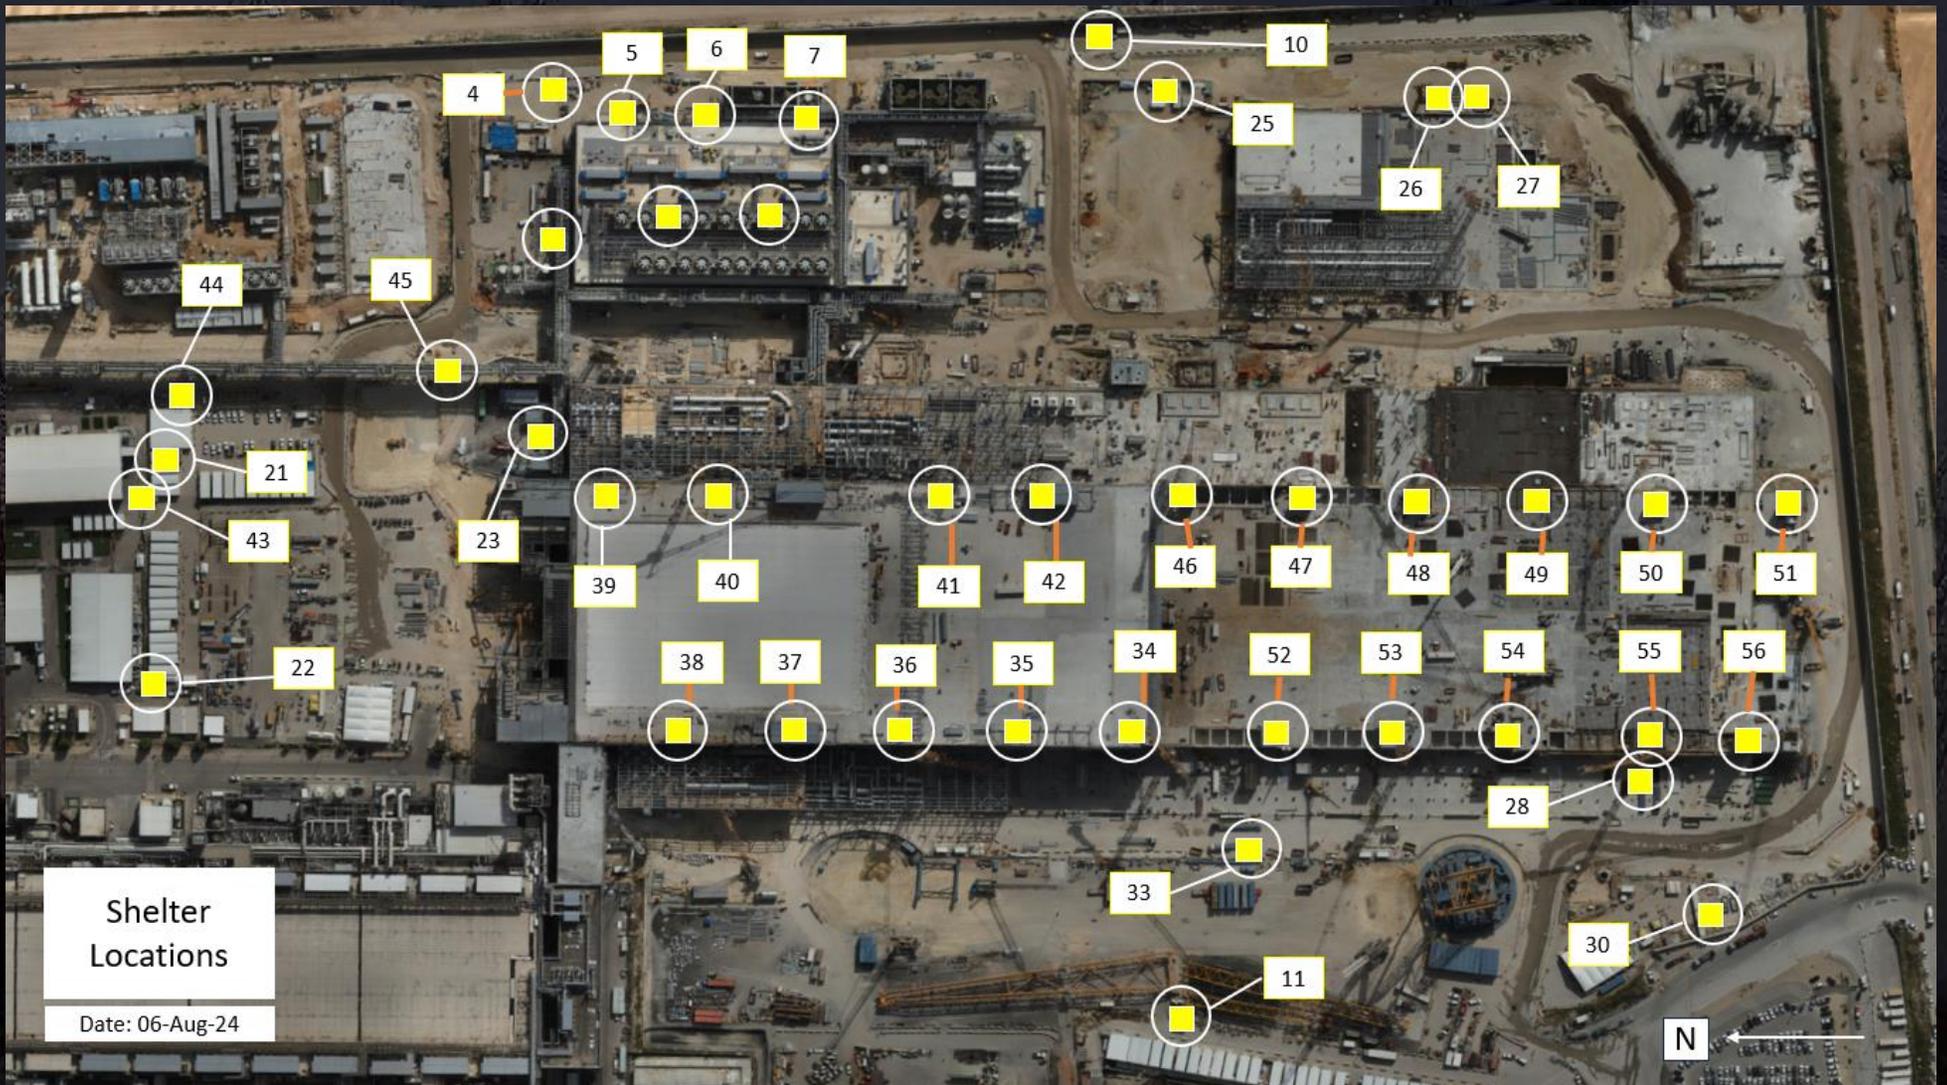

Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

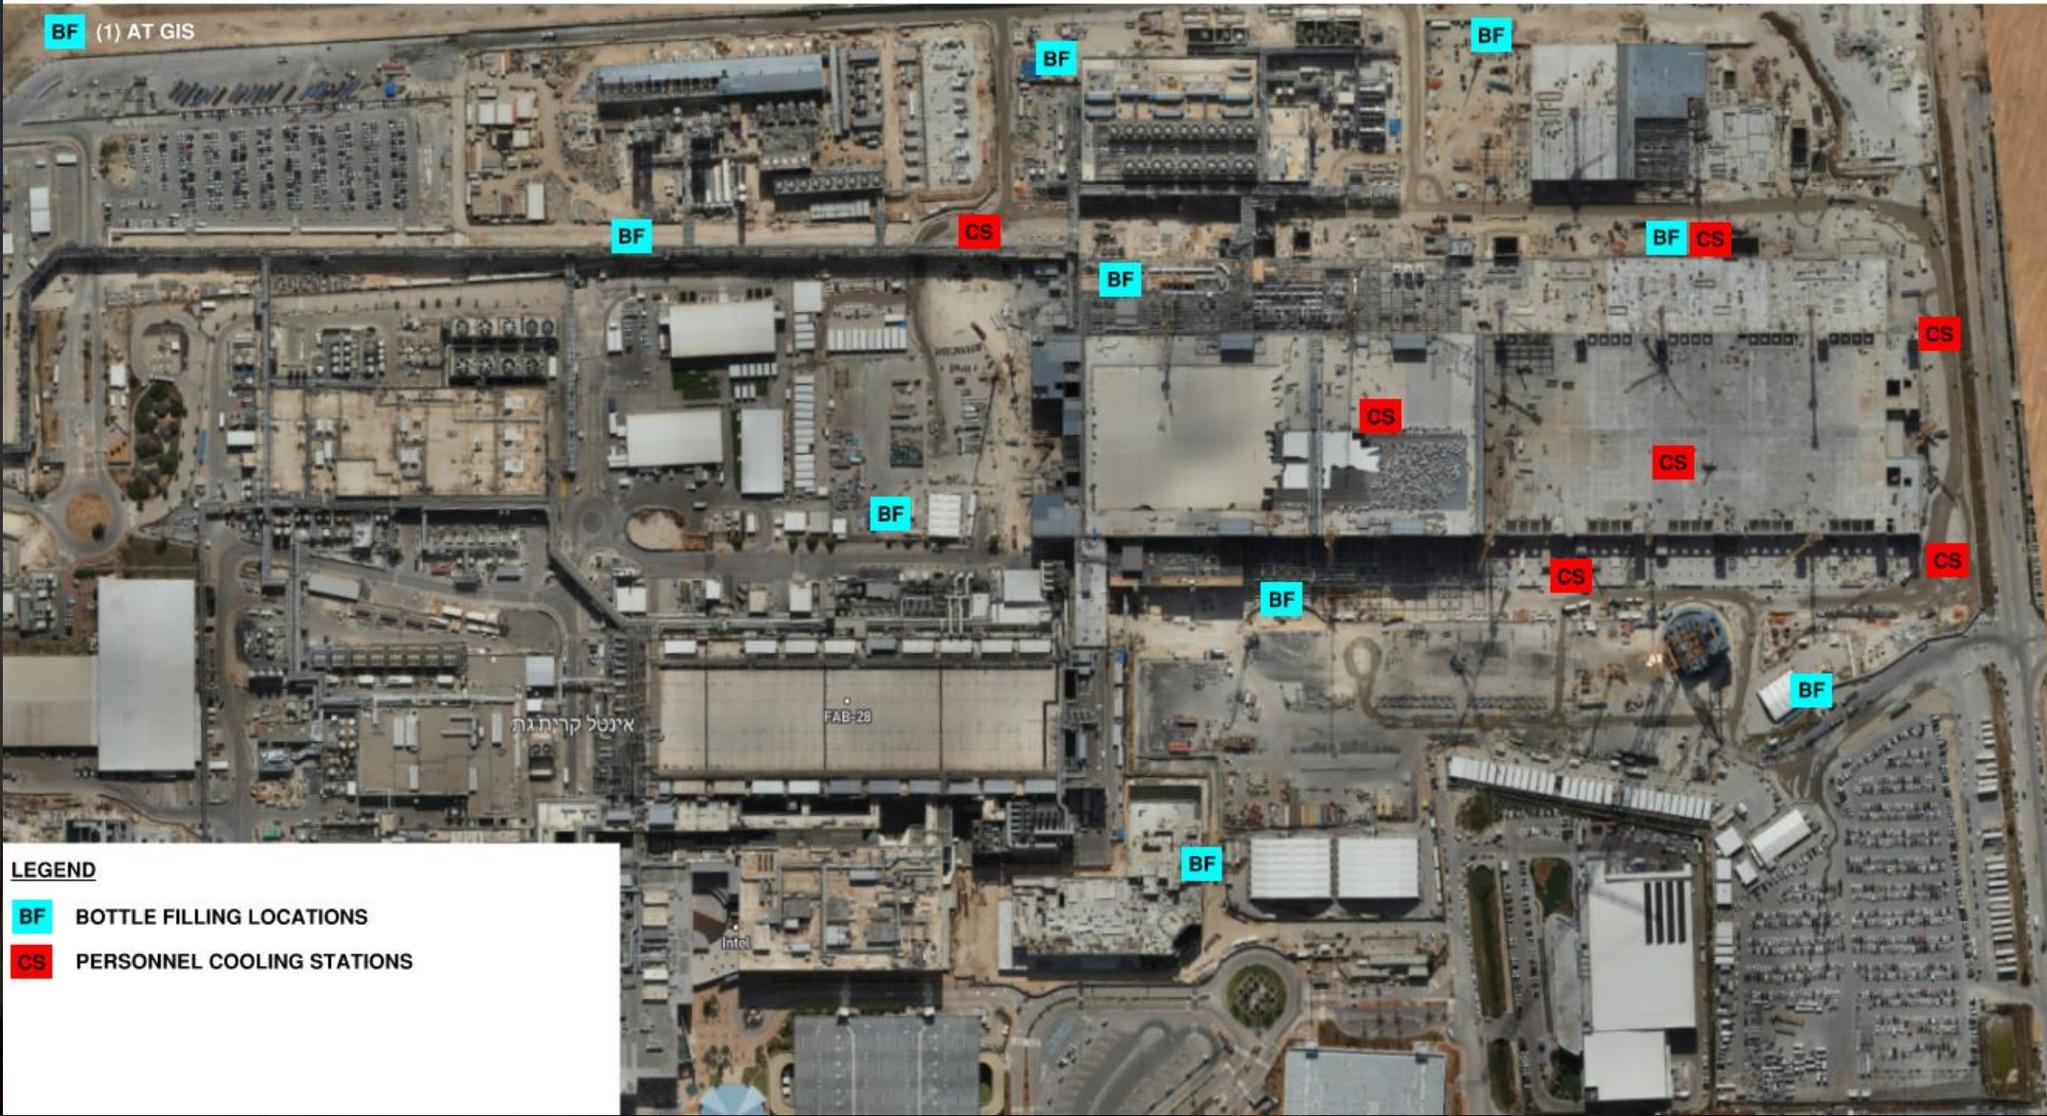

Job Services

Work Week 34

- ▶ Bottle water stations



Deep Cleaning of Break Tent B on Friday 23th Aug



Lead by Example

- As leaders on this project we must ensure we are following every rule and setting a good example for the workers.
- Sometimes, it is easy to think that as a leader you should be given special leeway to not have to follow a rule, wear your PPE, have a PTP when you perform work, etc.
- The expectation is the exact opposite. As leaders you are held to a higher standard.
- We cannot expect the workers to do the right thing if we as leaders do not.
- So, always ensure you are going the speed limit, wearing your PPE, using the walk path, etc.

Heat Index- August 22nd

		temperature (°F)															
		80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110
Relative Humidity (%)	40	80	81	83	85	88	91	94	97	101	105	109	114	119	124	130	136
	45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137	
	50	81	83	85	88	91	95	101	103	108	113	118	124	131	137		
	55	81	84	86	89	93	97	101	106	112	117	124	130	137			
	60	82	84	88	91	95	100	105	110	116	123	129	137				
	65	82	85	89	93	98	103	108	114	121	128	136					
	70	83	86	90	95	100	105	112	119	126	134						
	75	84	88	92	97	103	109	116	124	132							
	80	84	89	94	100	106	113	121	129								
	85	85	90	96	102	110	117	126	135								
	90	86	91	98	105	113	122	131									
95	86	93	100	108	117	127											
100	87	95	103	112	121	132											

Caution

Extreme Caution

Danger

Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

Daily Coordination Meeting



14:00 Sign In
