

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting

General Topics:



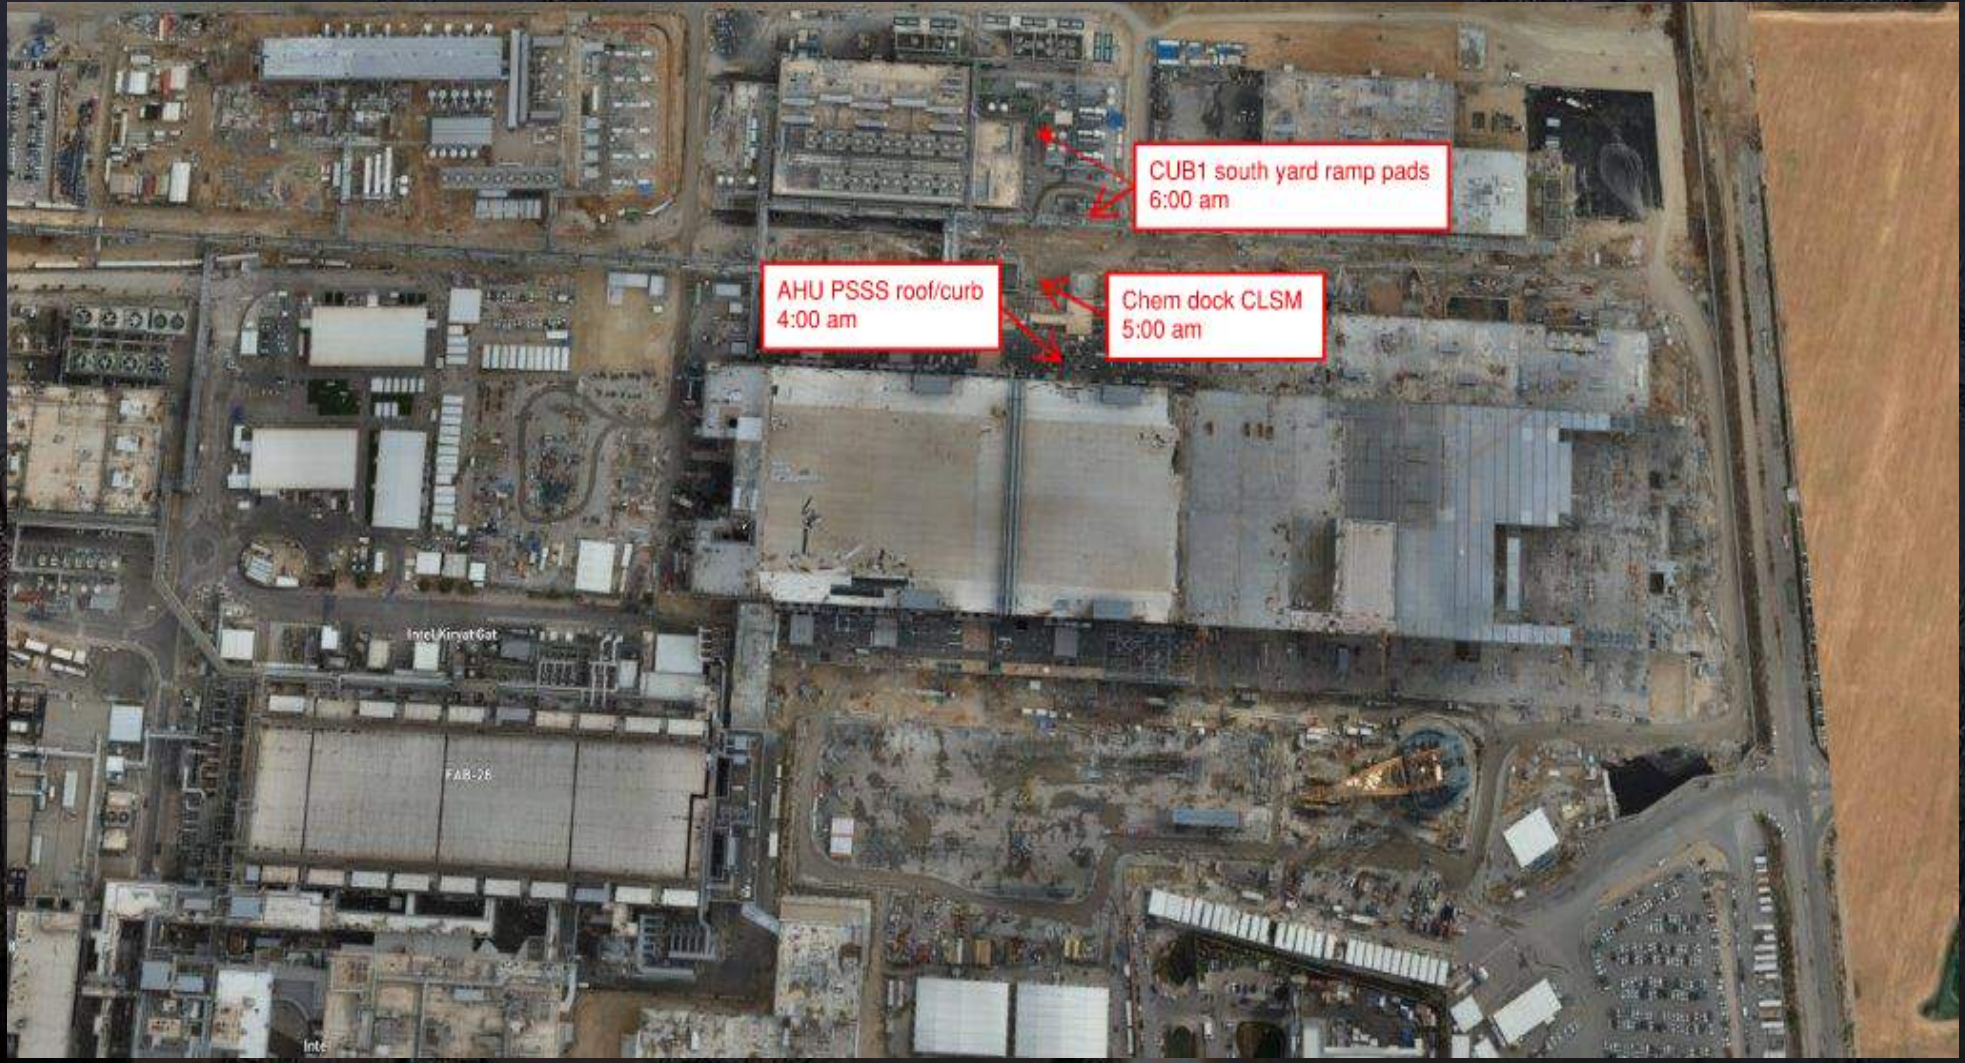

CUB1 south yard ramp pads
6:00 am

AHU PSSS roof/curb
4:00 am

Chem dock CLSM
5:00 am


Intel Kinyot Gat

FAR-26

Inte




UTILITY LEVEL PRESS TEST

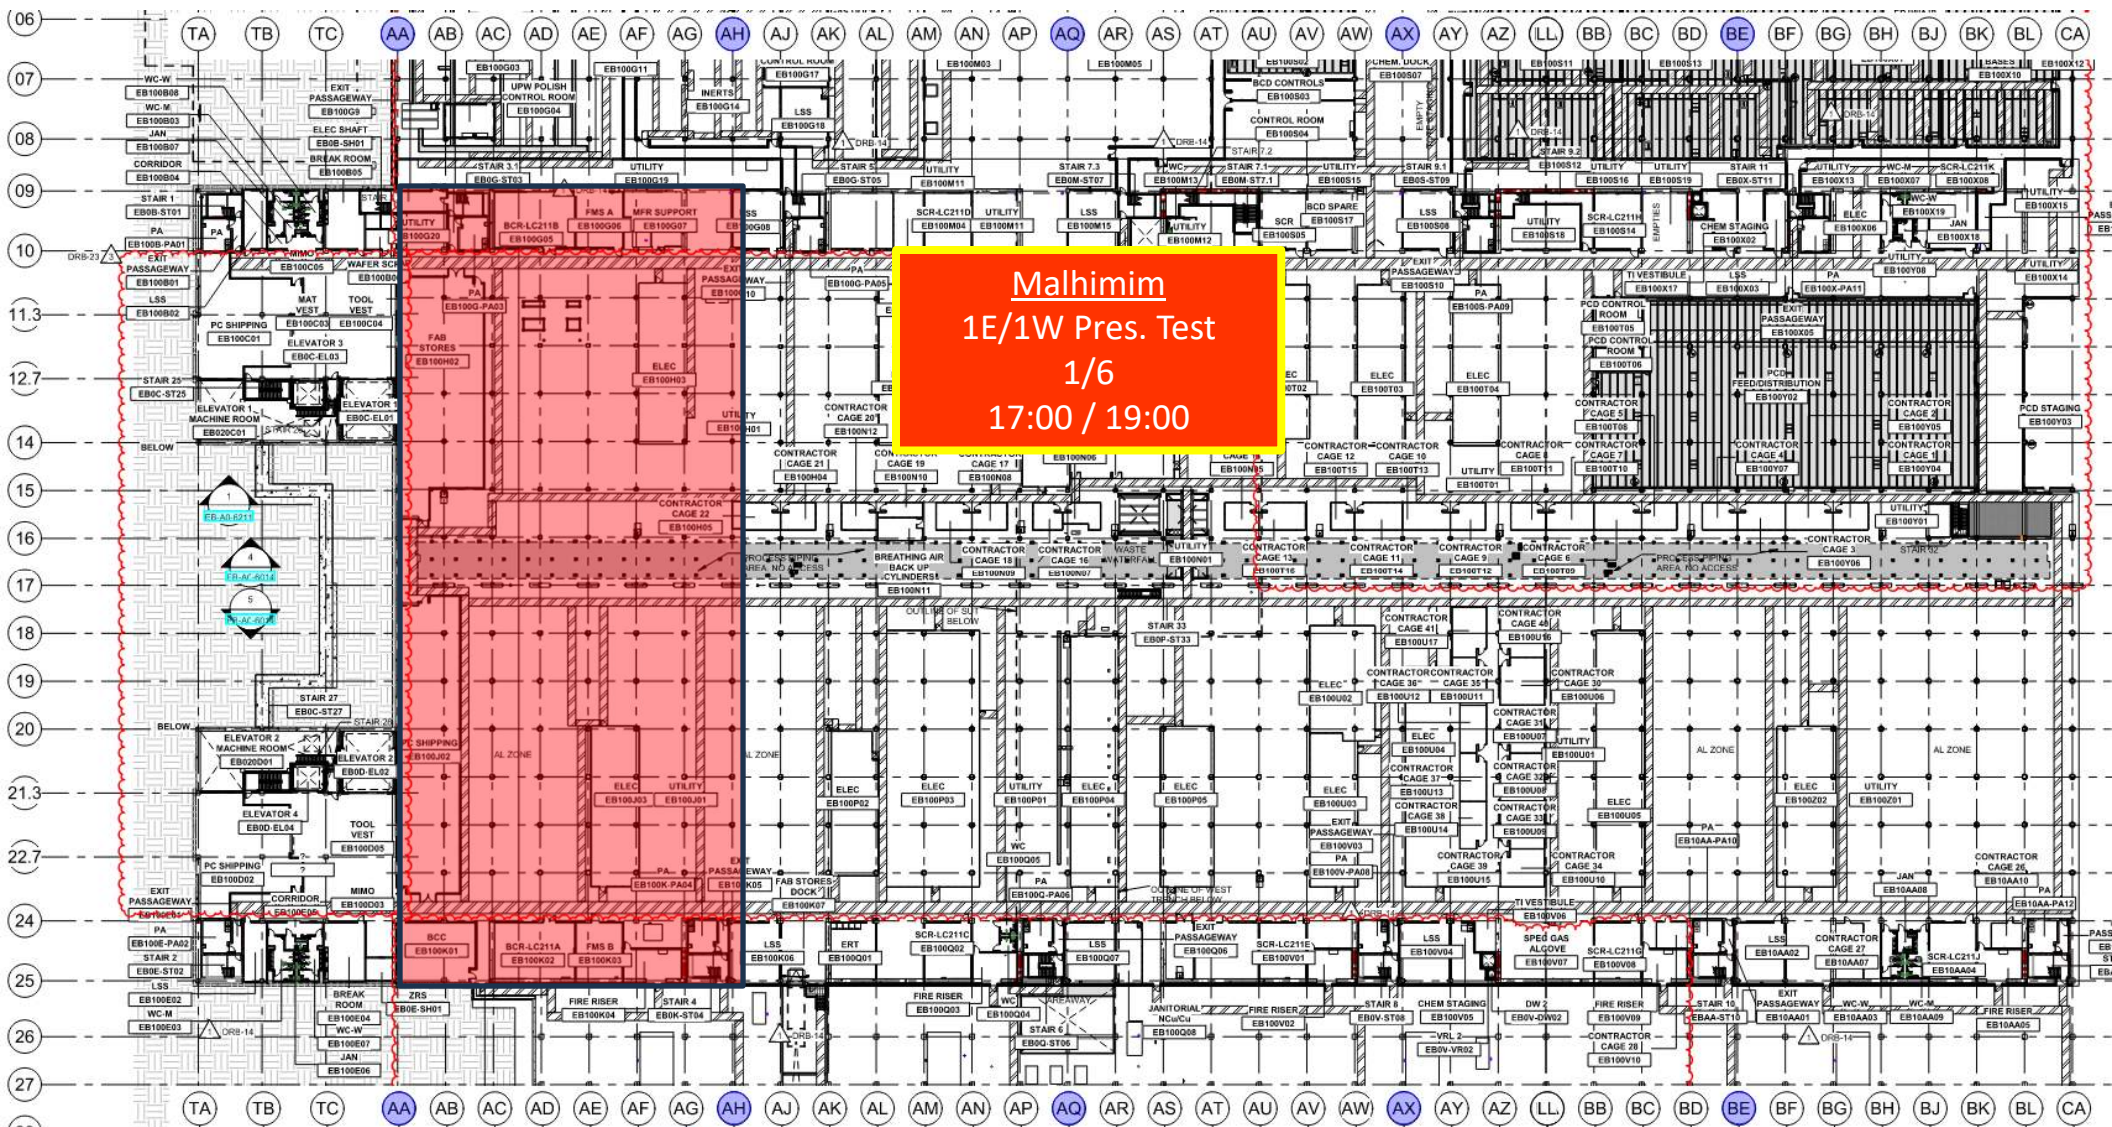

Malhimim
1E/1W Pres. Test
1/6
17:00 / 19:00

UTILITY LEVEL MOD1

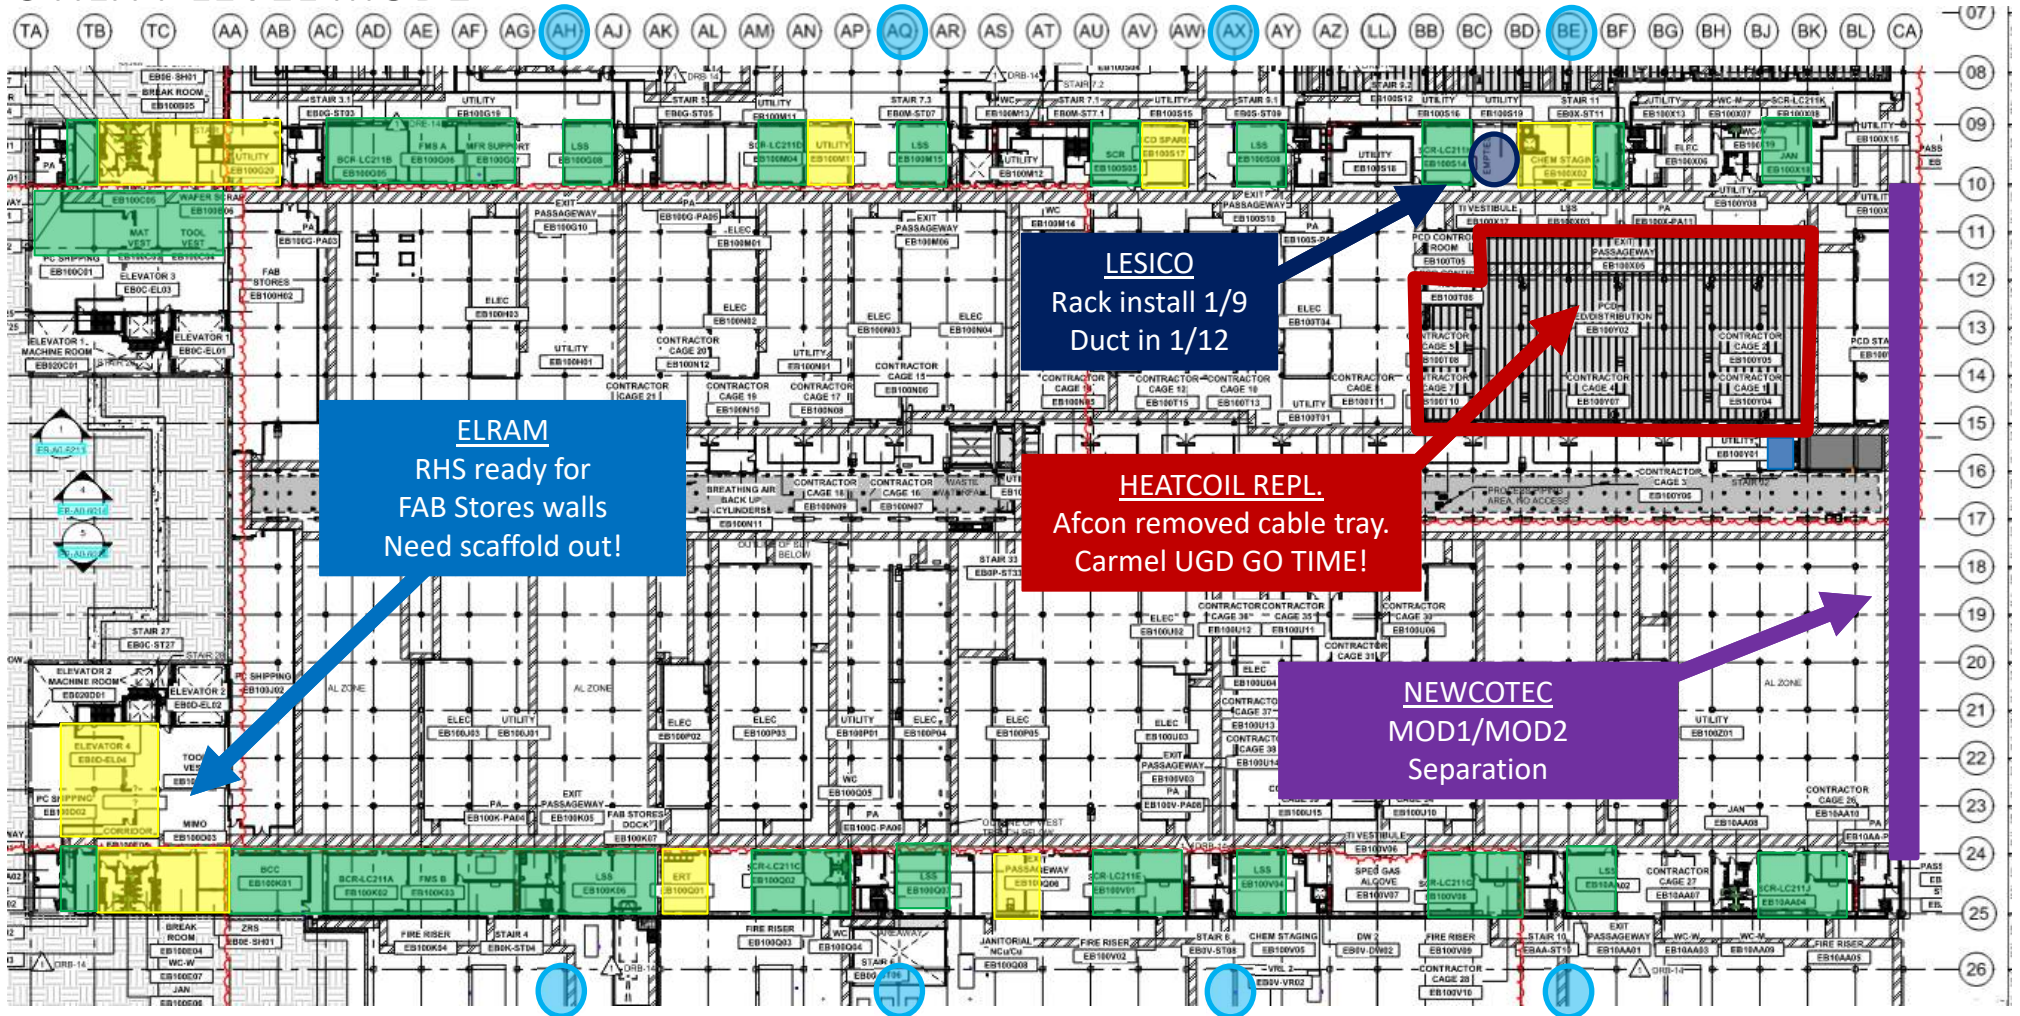

ELRAM
RHS ready for
FAB Stores walls
Need scaffold out!

LESICO
Rack install 1/9
Duct in 1/12


HEATCOIL REPL.
Afcon removed cable tray.
Carmel UGD GO TIME!

NEWCOTEC
MOD1/MOD2
Separation

ELRAM
Drywall install

MEP+Electrical
Ready for re-install

UTILITY LEVEL MOD2

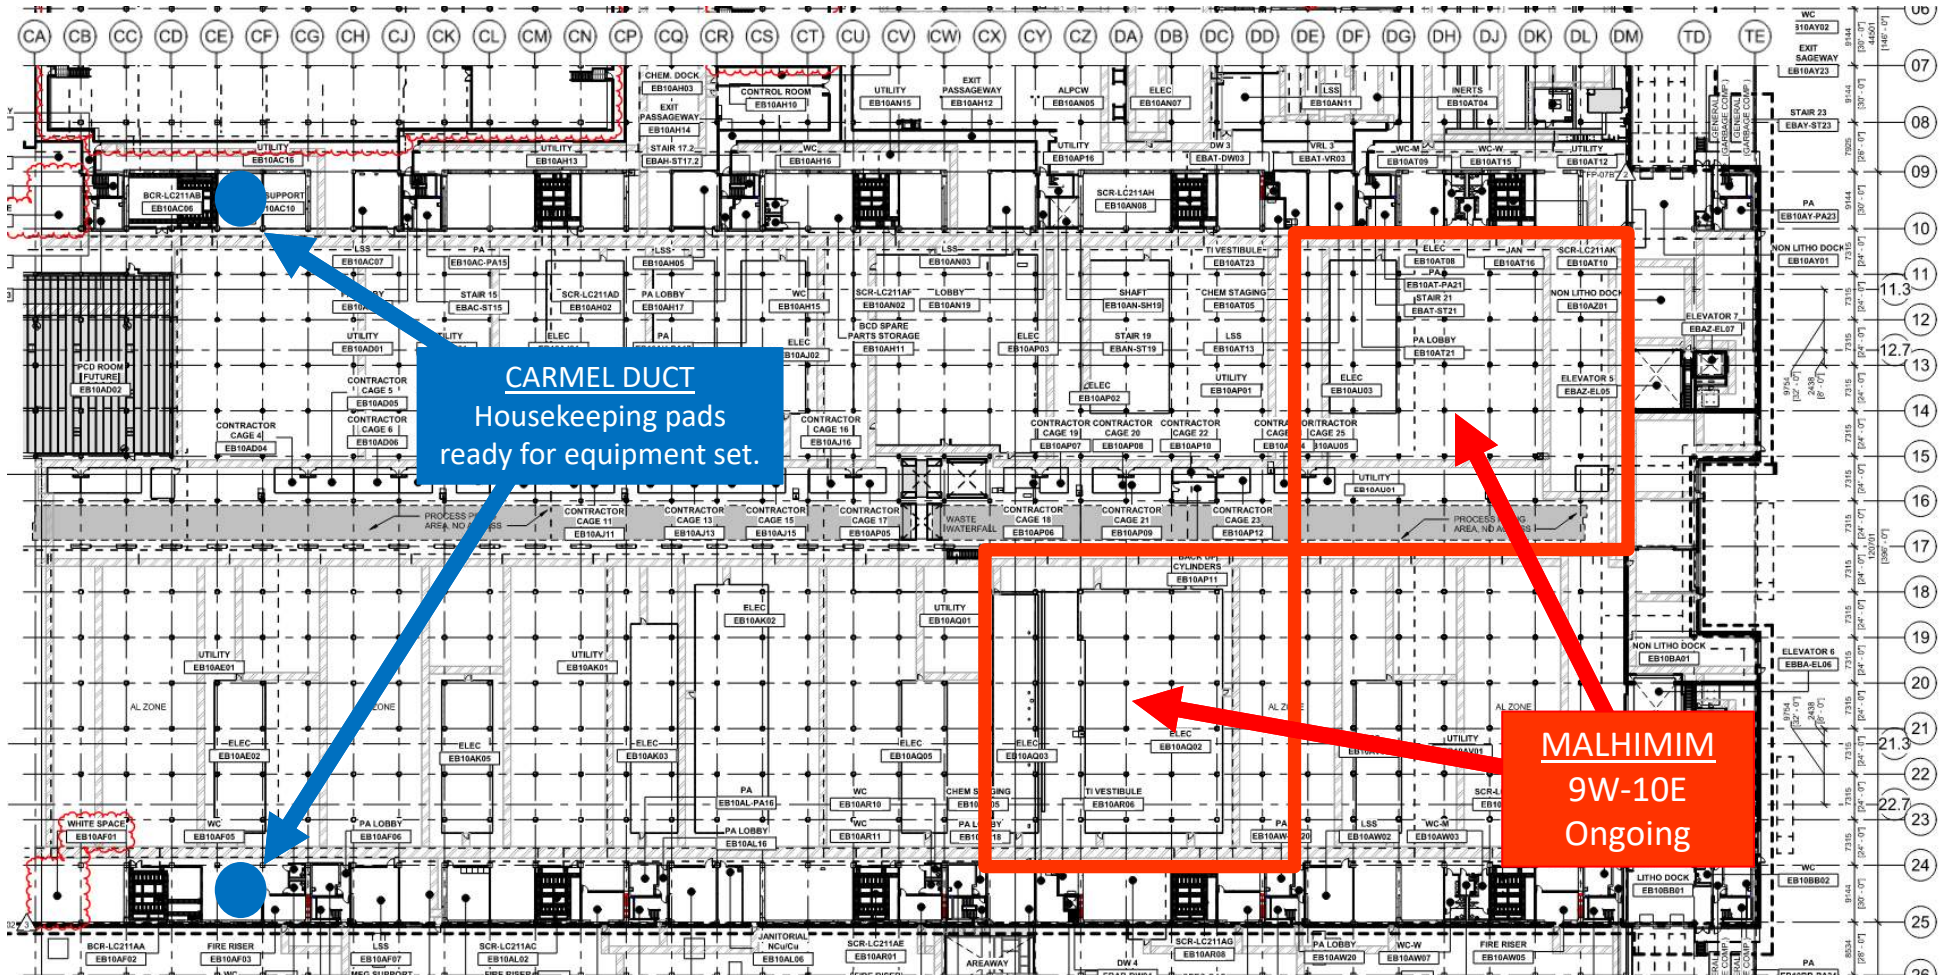

SUT 38.1 LEVEL




Solvent room.
CRC

Topping slab Schedule
 Pour 1 - 1/9 - 1/13
 Pour 2 - 1/15 - 1/20
 Pour 3 - 1/22 - 1/27
 Pour 4 - 1/29 - 2/4

SUT 38.2 LEVEL

Rack 4b
Lifting
schedule
#6 –

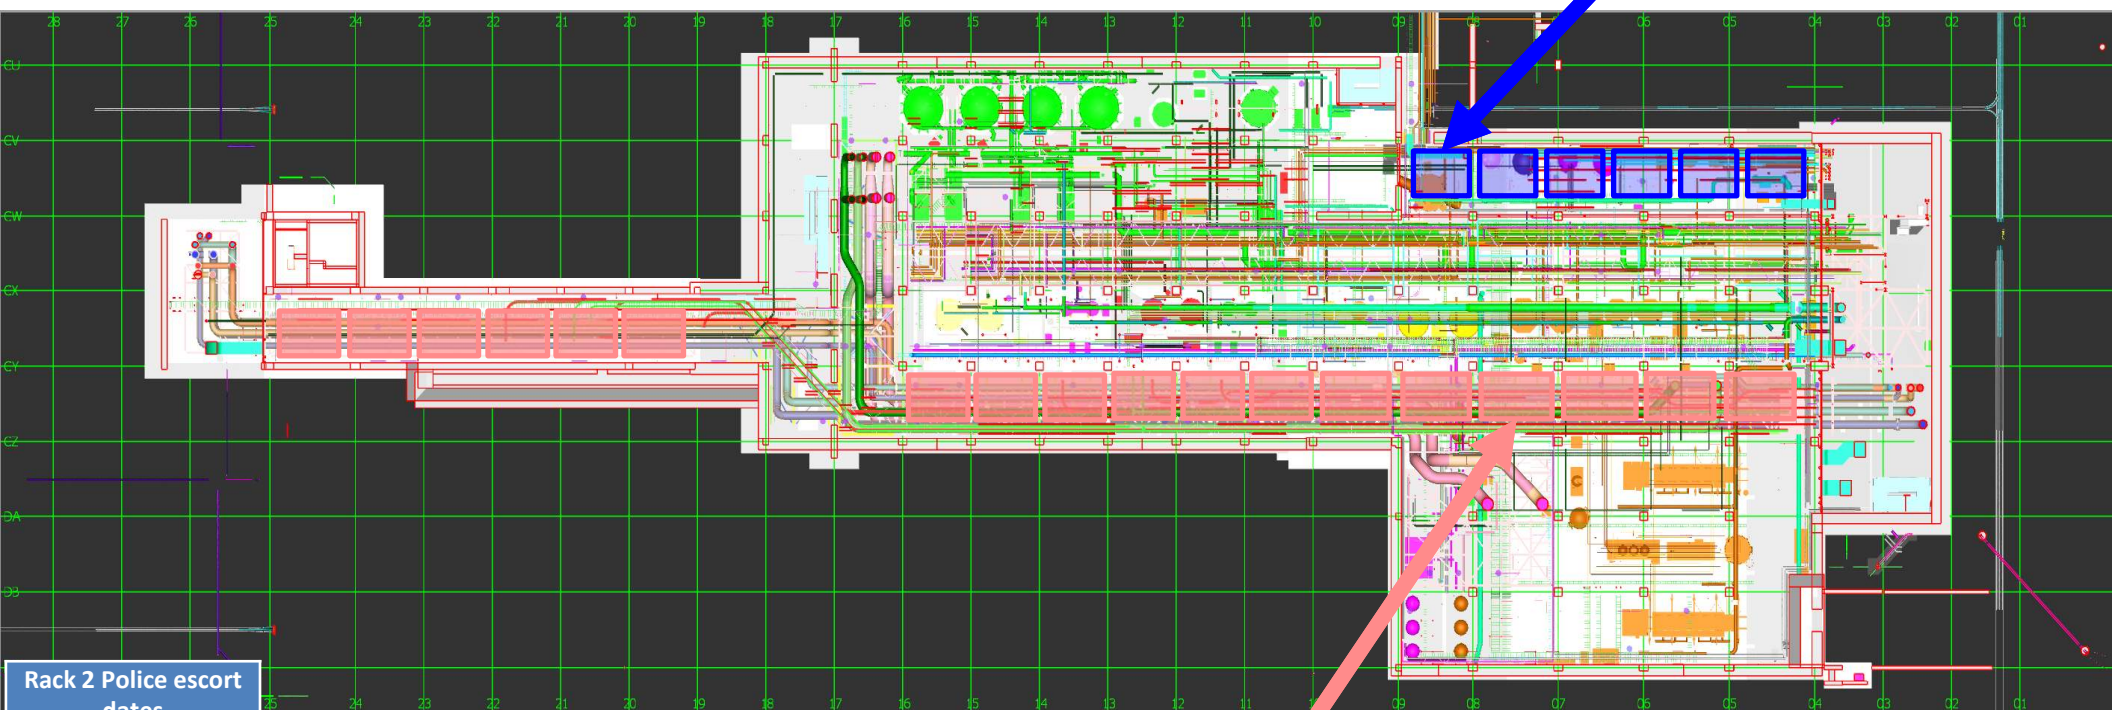


Rack 2
MIMO -
Module #9
5th of Jan


Rack 2 Police escort
dates

- v24.11.24
- v25.11.24
- v3.12.24
- v9.12.24
- v12.12.24
- v15.12.24
- v17.12.24
- v22.12.24
- 5.1.25
- ~~14.1.25~~ > 2.2.25
- 3.2.25
- 9.2.25


SUBFAB BUILDOUT MOD 1

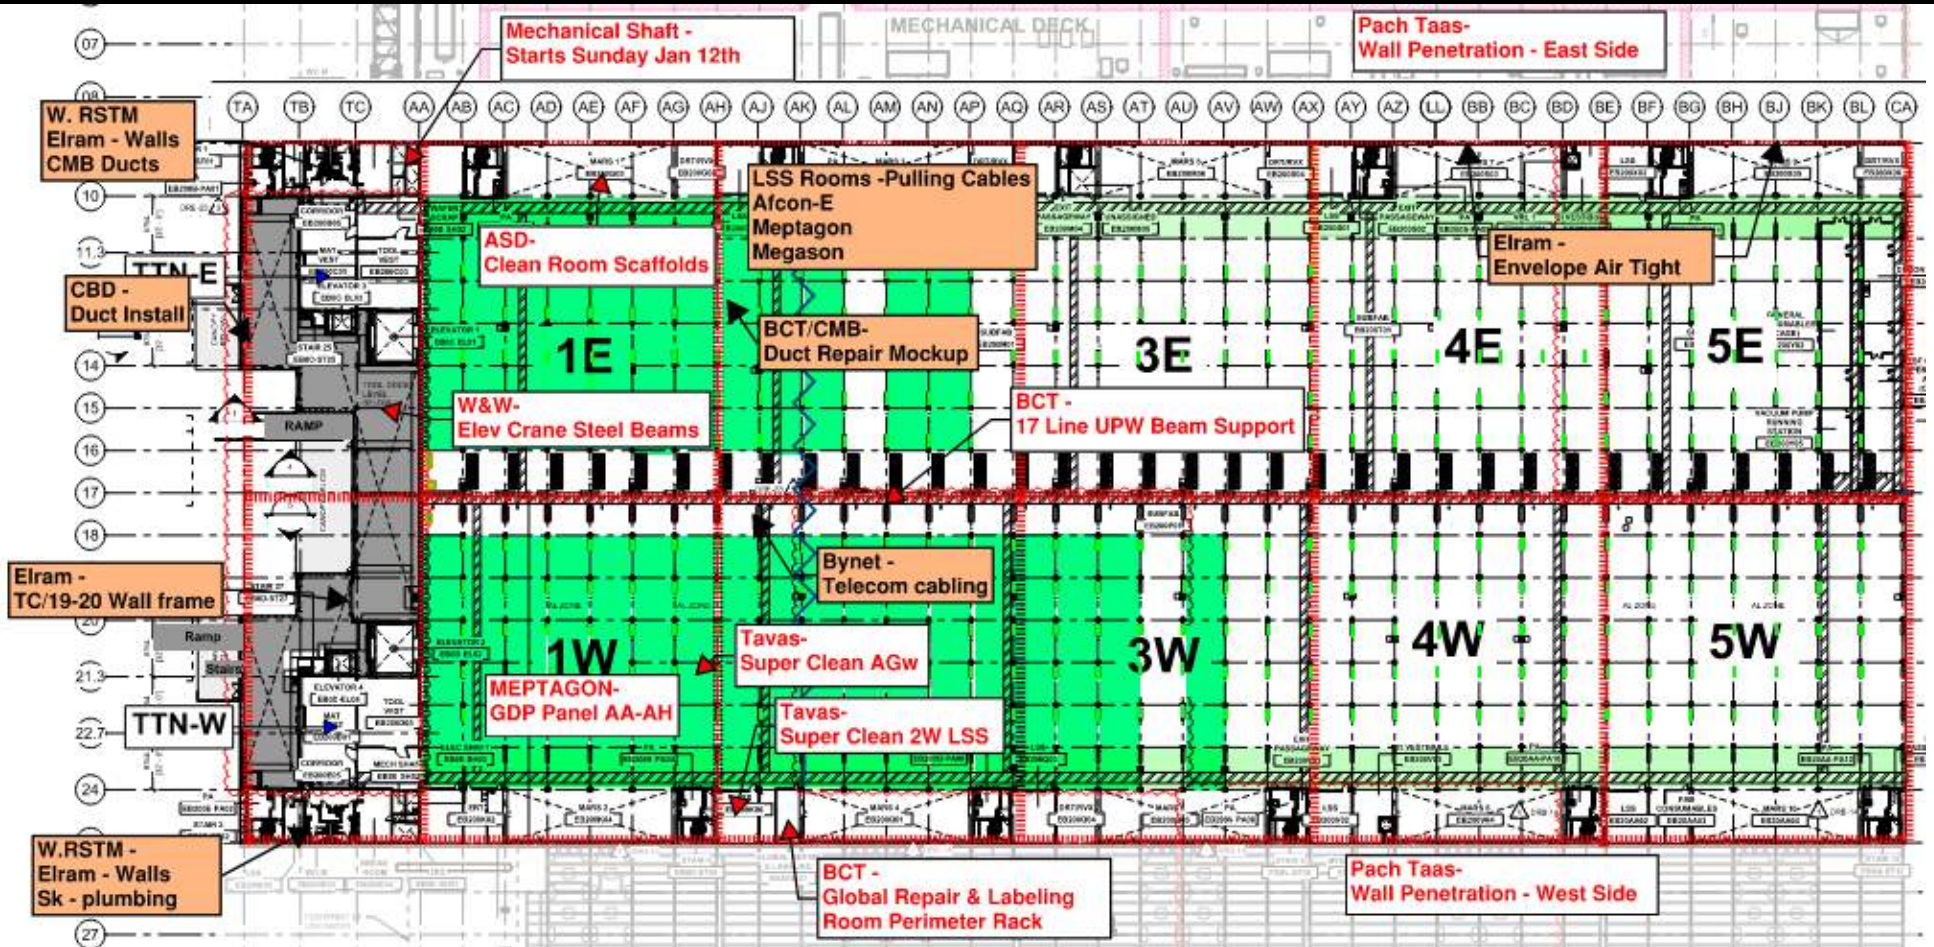


SUBFAB CRC TOPCOAT

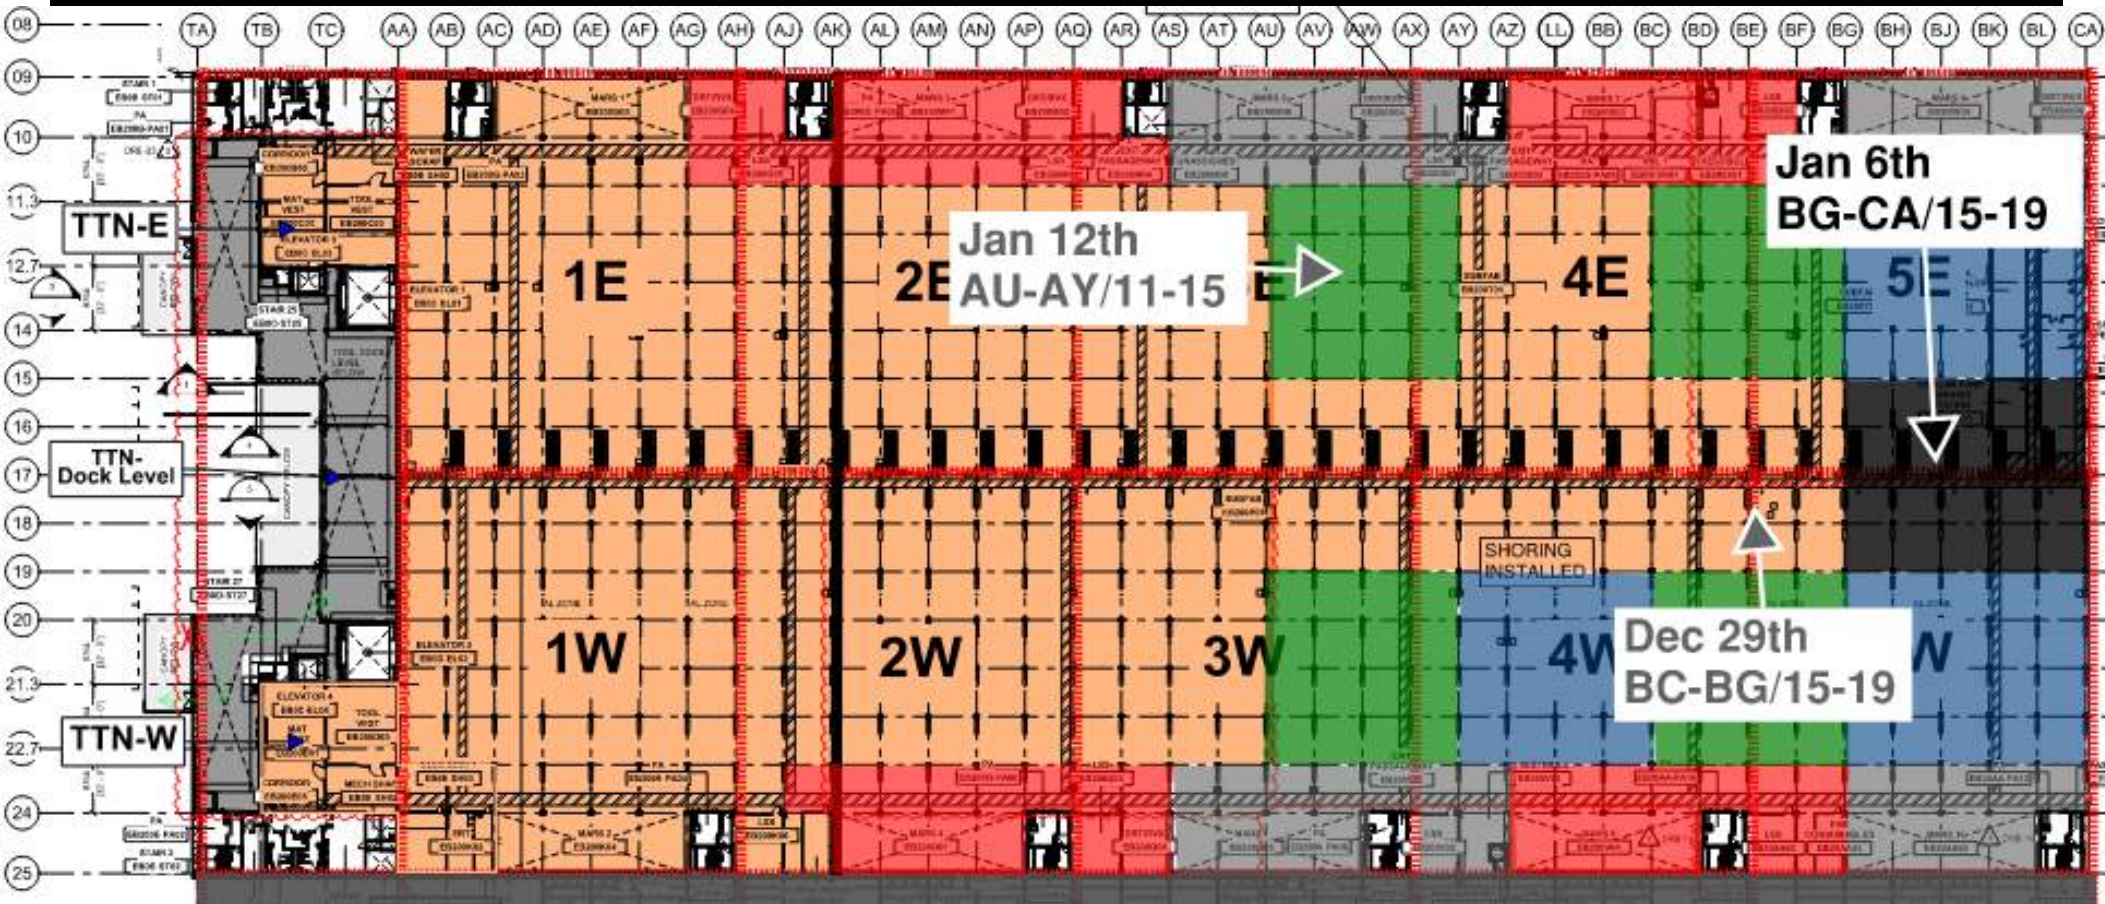


BCT Pressure Test Today

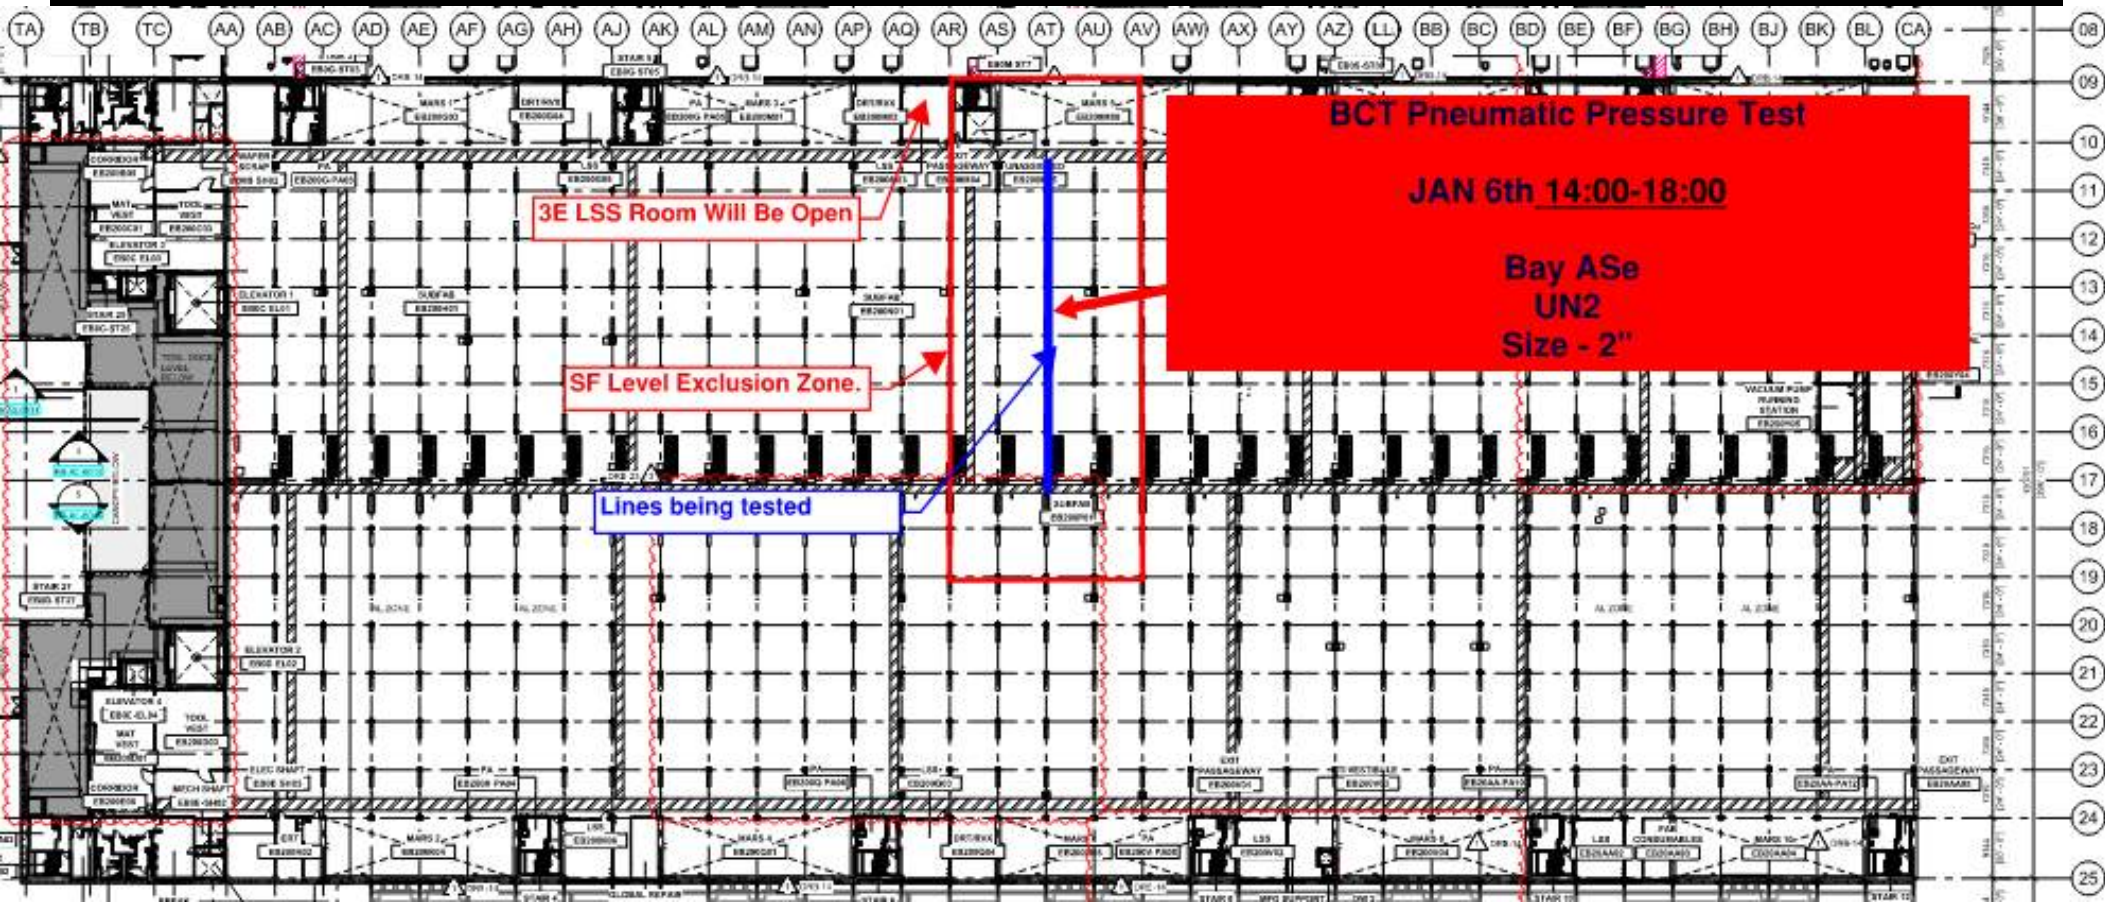



BCT Pressure Test Tomorrow

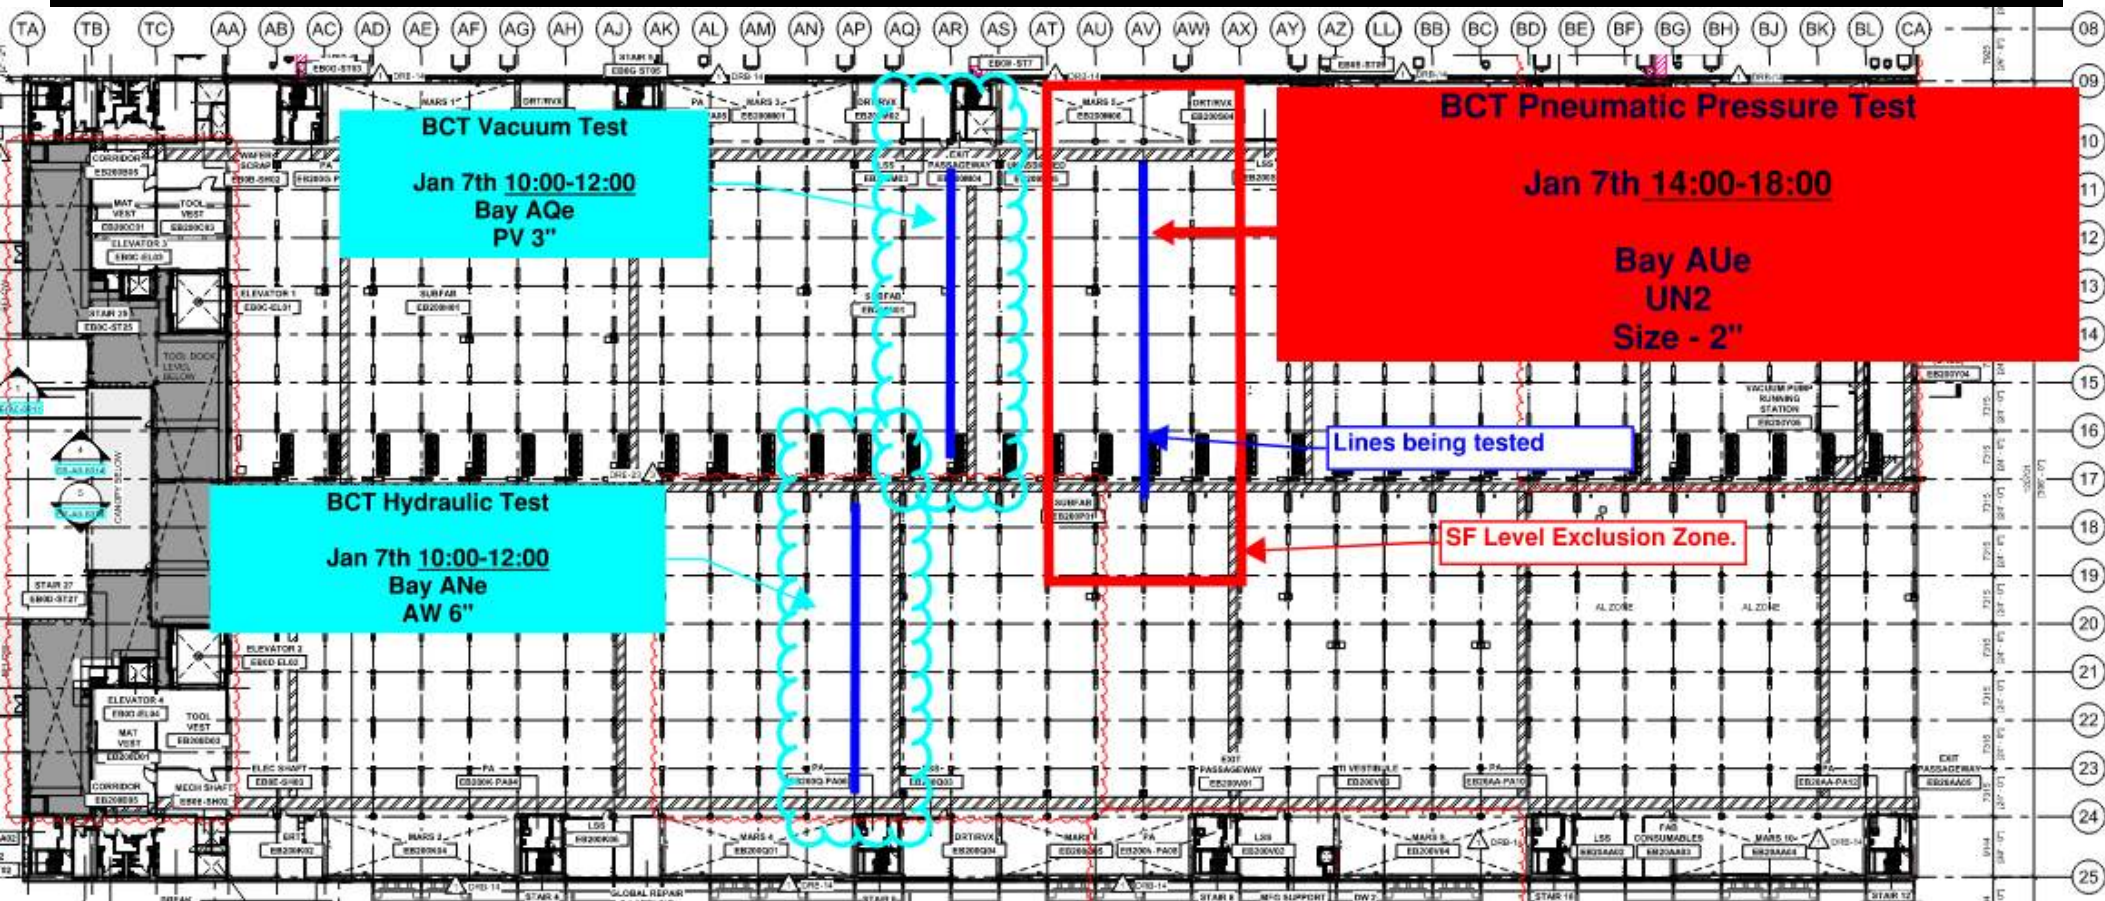

SUBFAB BUILDOUT MOD 2

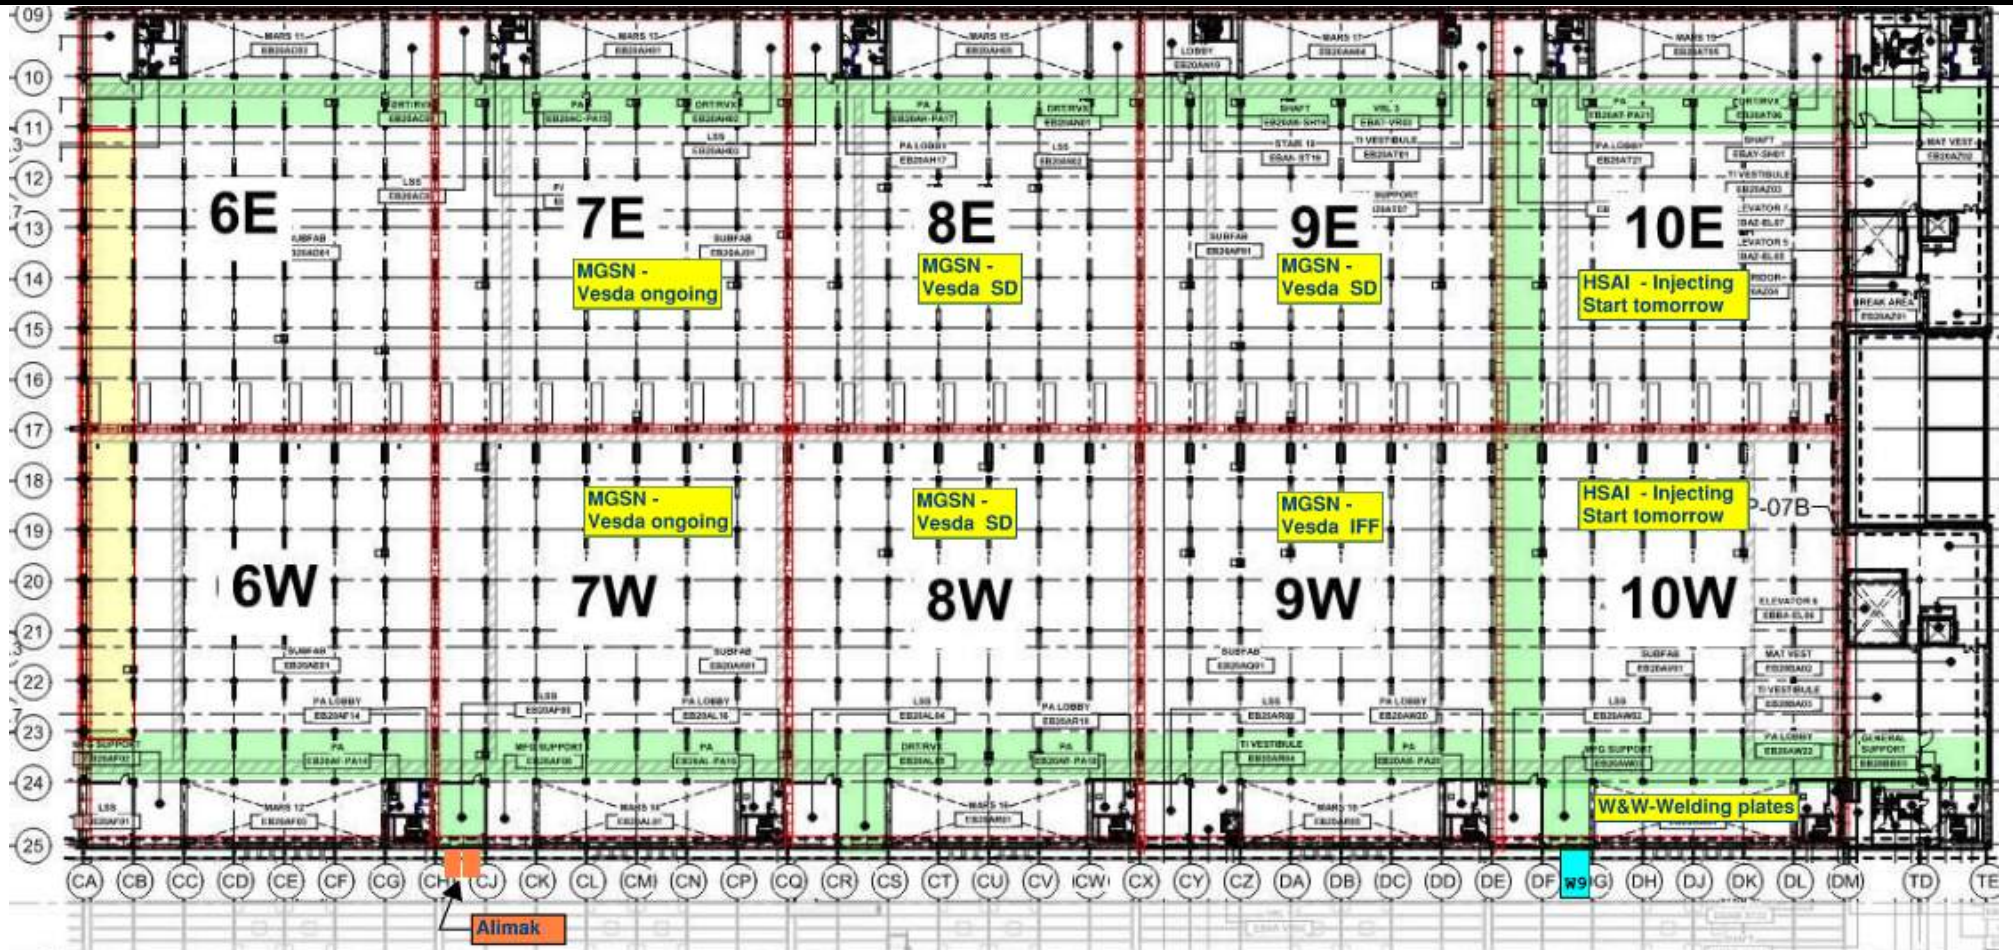

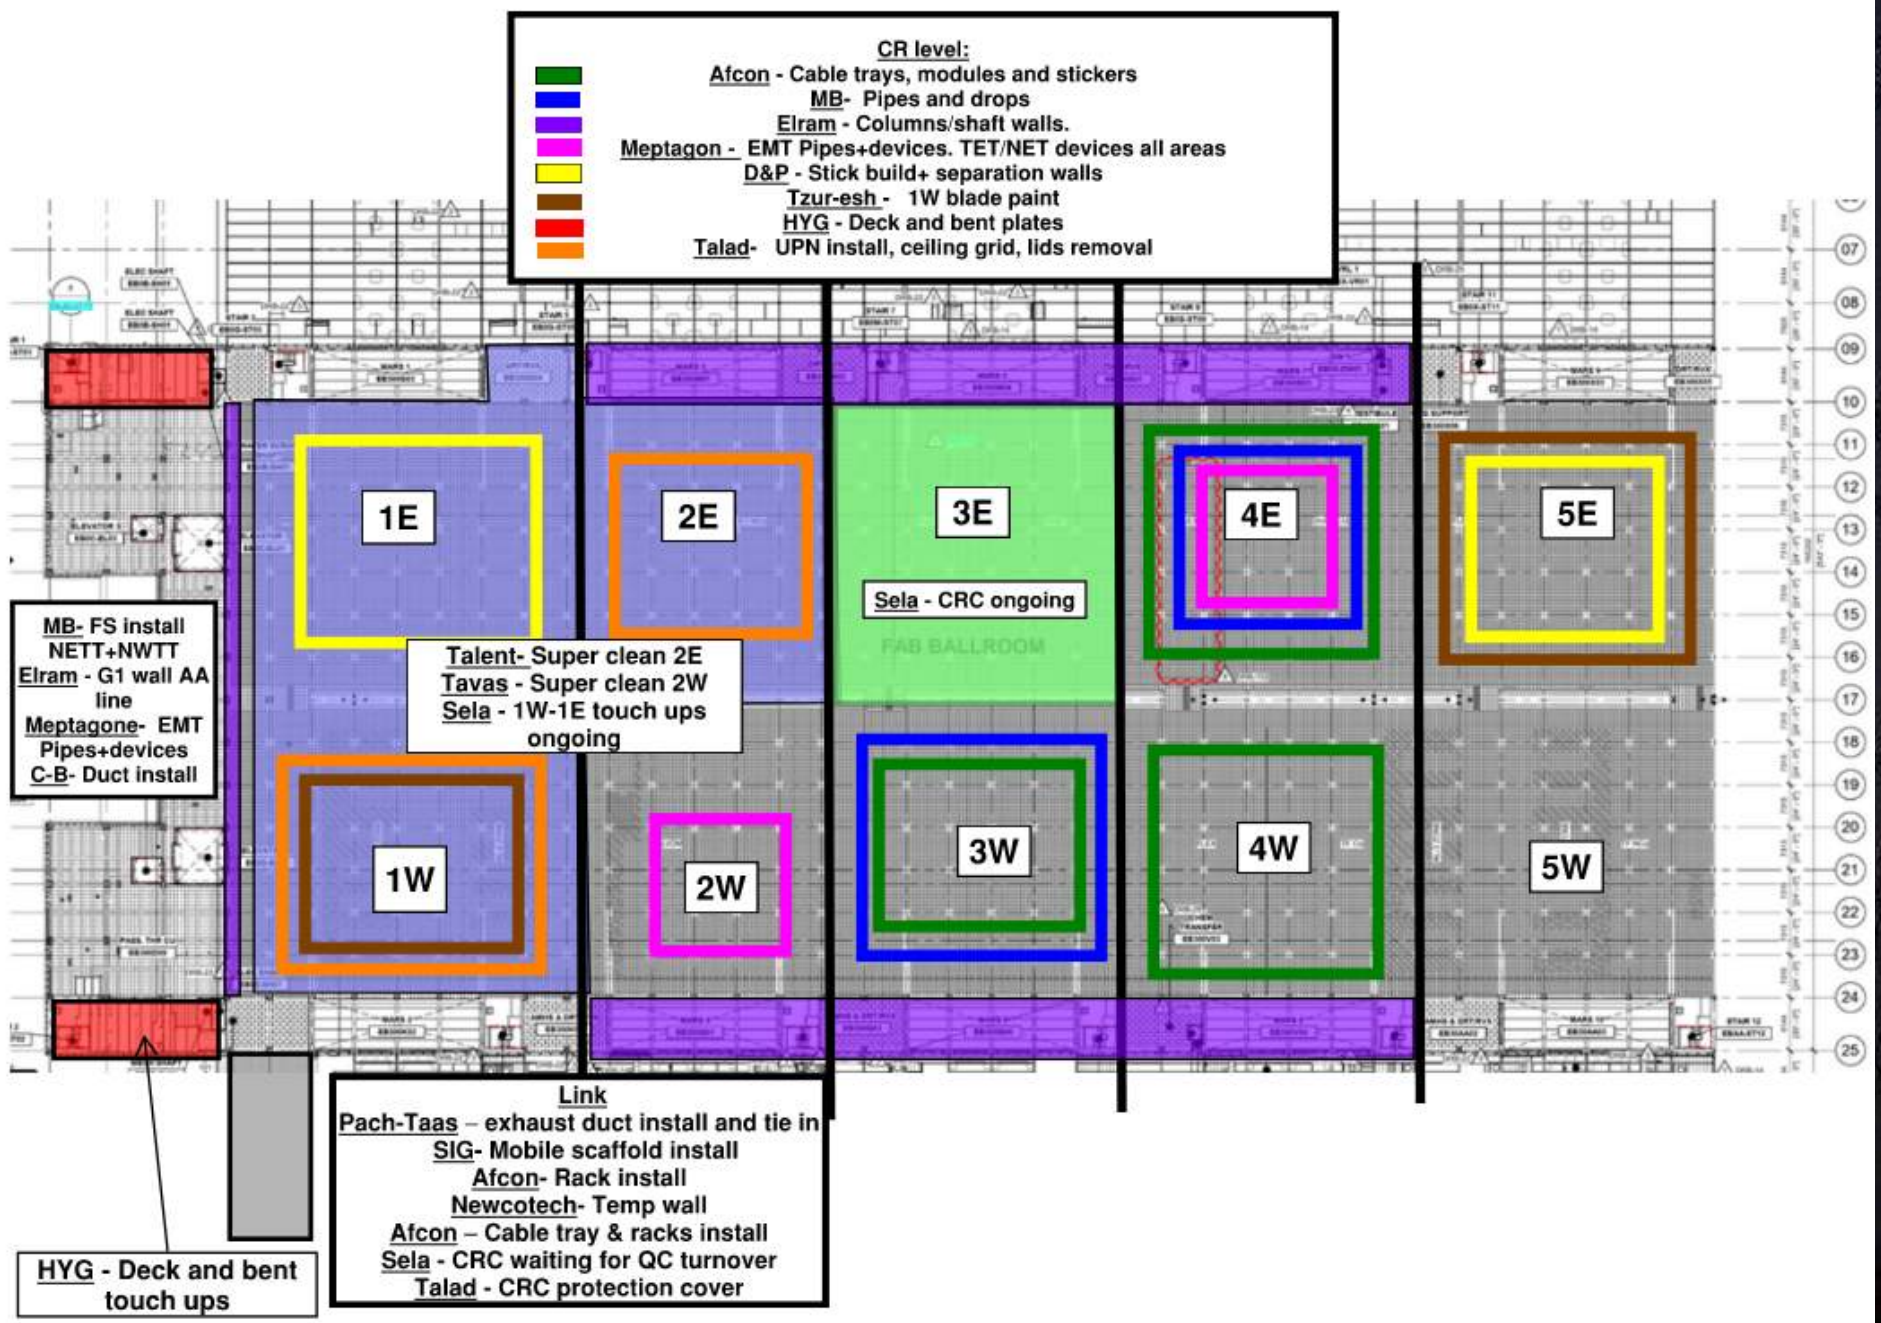

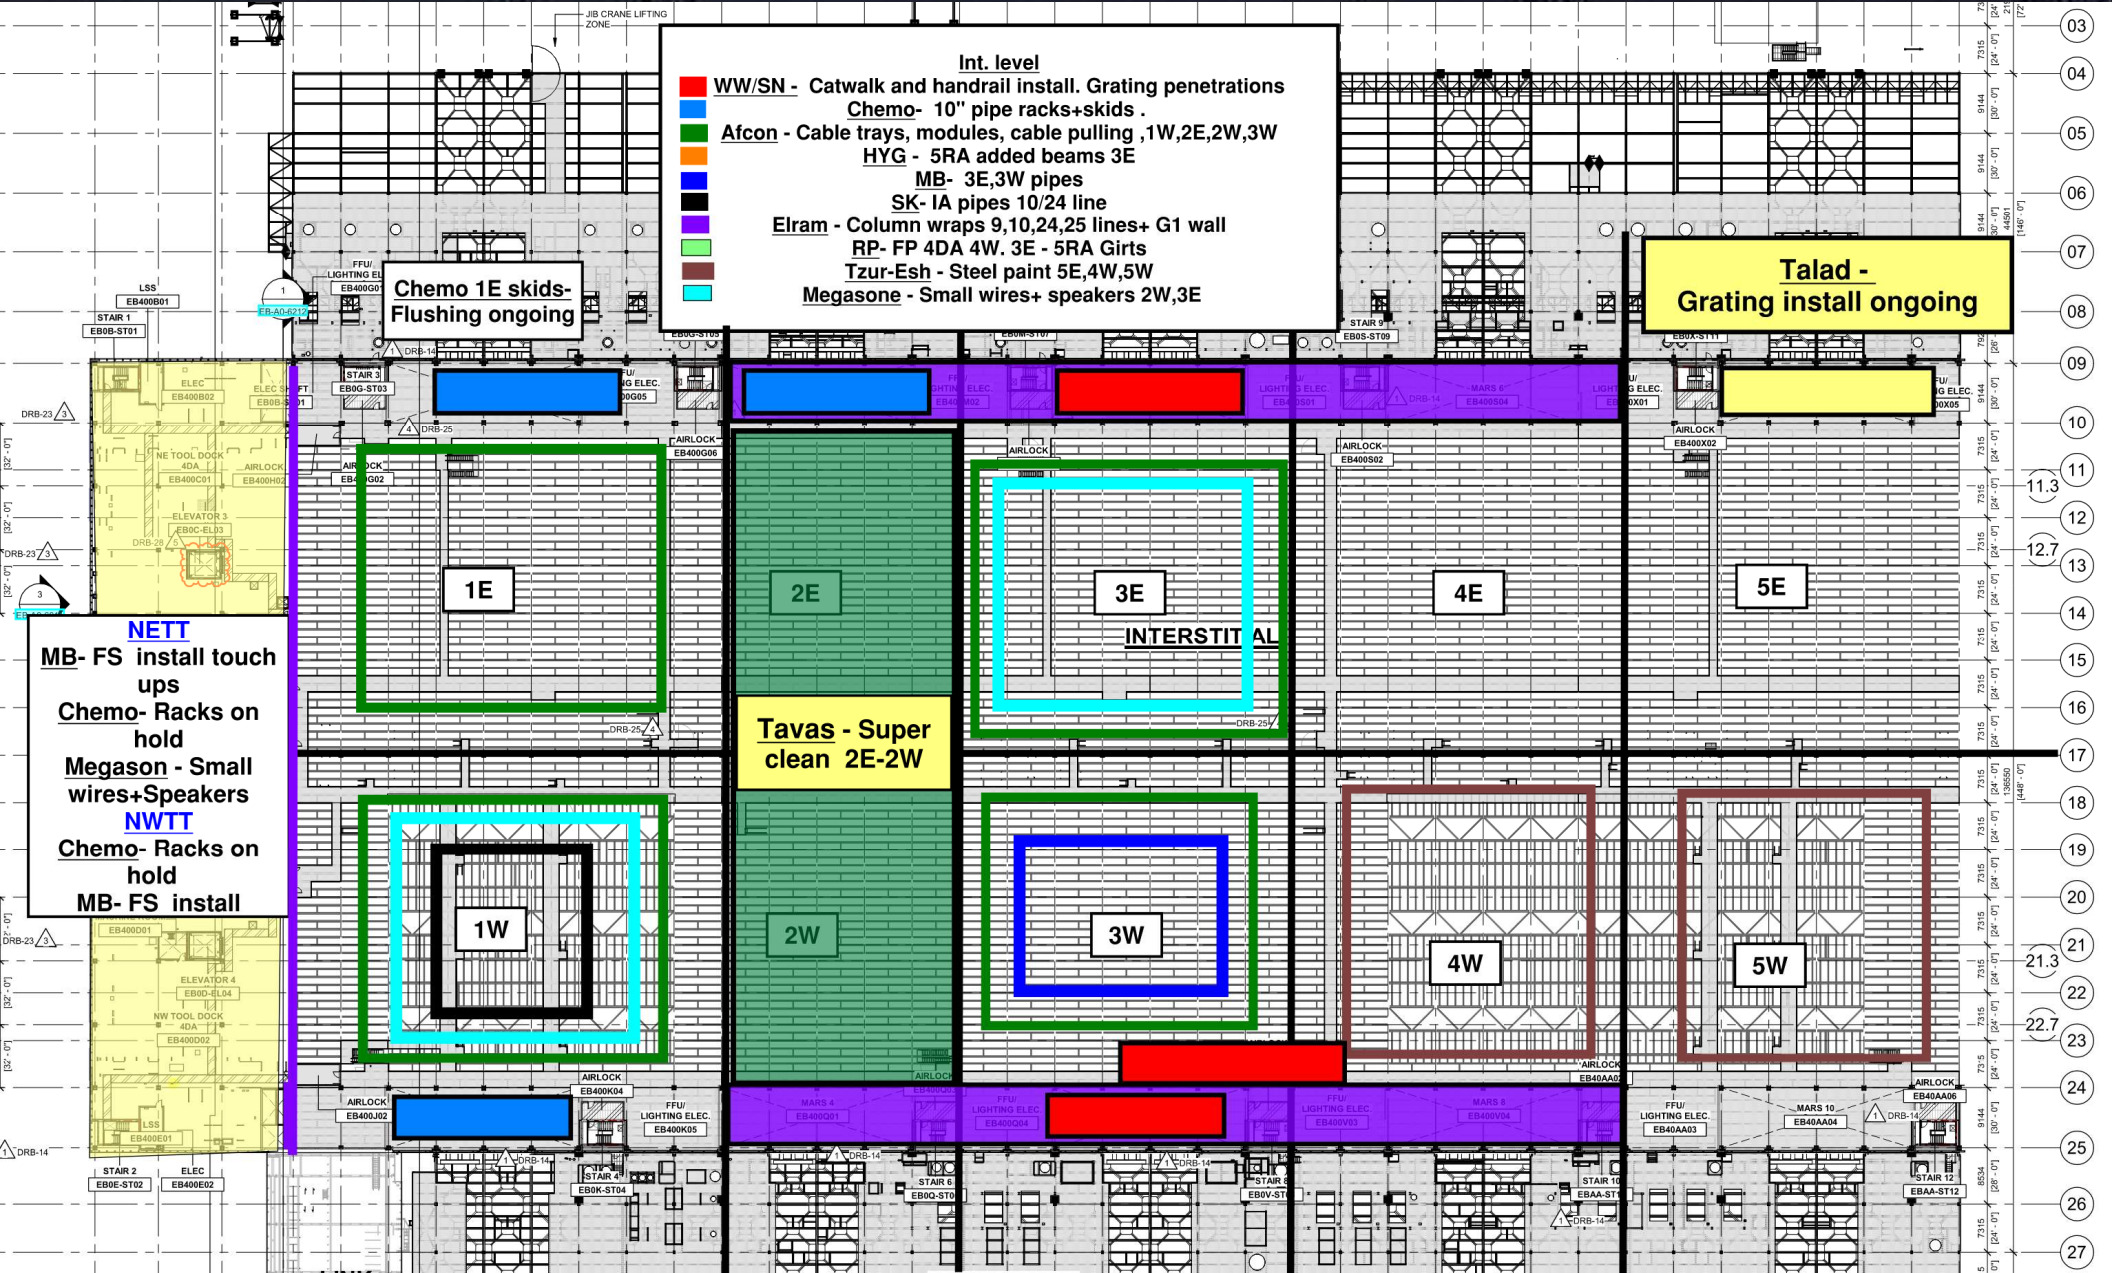

Int. level

- **WW/SN** - Catwalk and handrail install. Grating penetrations
- **Chemo**- 10" pipe racks+skids .
- **Afcon** - Cable trays, modules, cable pulling ,1W,2E,2W,3W
- **HYG** - 5RA added beams 3E
- **MB**- 3E,3W pipes
- **SK**- IA pipes 10/24 line
- **Elram** - Column wraps 9,10,24,25 lines+ G1 wall
- **RP**- FP 4DA 4W. 3E - 5RA Girts
- **Tzur-Esh** - Steel paint 5E,4W,5W
- **Megason** - Small wires+ speakers 2W,3E

**Chemo 1E skids-
Flushing ongoing**


**Talad -
Grating install ongoing**


NETT
MB- FS install touch ups
Chemo- Racks on hold
Megason - Small wires+Speakers
NWTT
Chemo- Racks on hold
MB- FS install

Tavas - Super clean 2E-2W

INTERSTITIAL

- 03
- 04
- 05
- 06
- 07
- 08
- 09
- 10
- 11
- 11.3
- 12.7
- 13
- 14
- 15
- 16
- 17
- 18
- 19
- 20
- 21
- 21.3
- 22
- 22.7
- 23
- 24
- 25
- 26
- 27

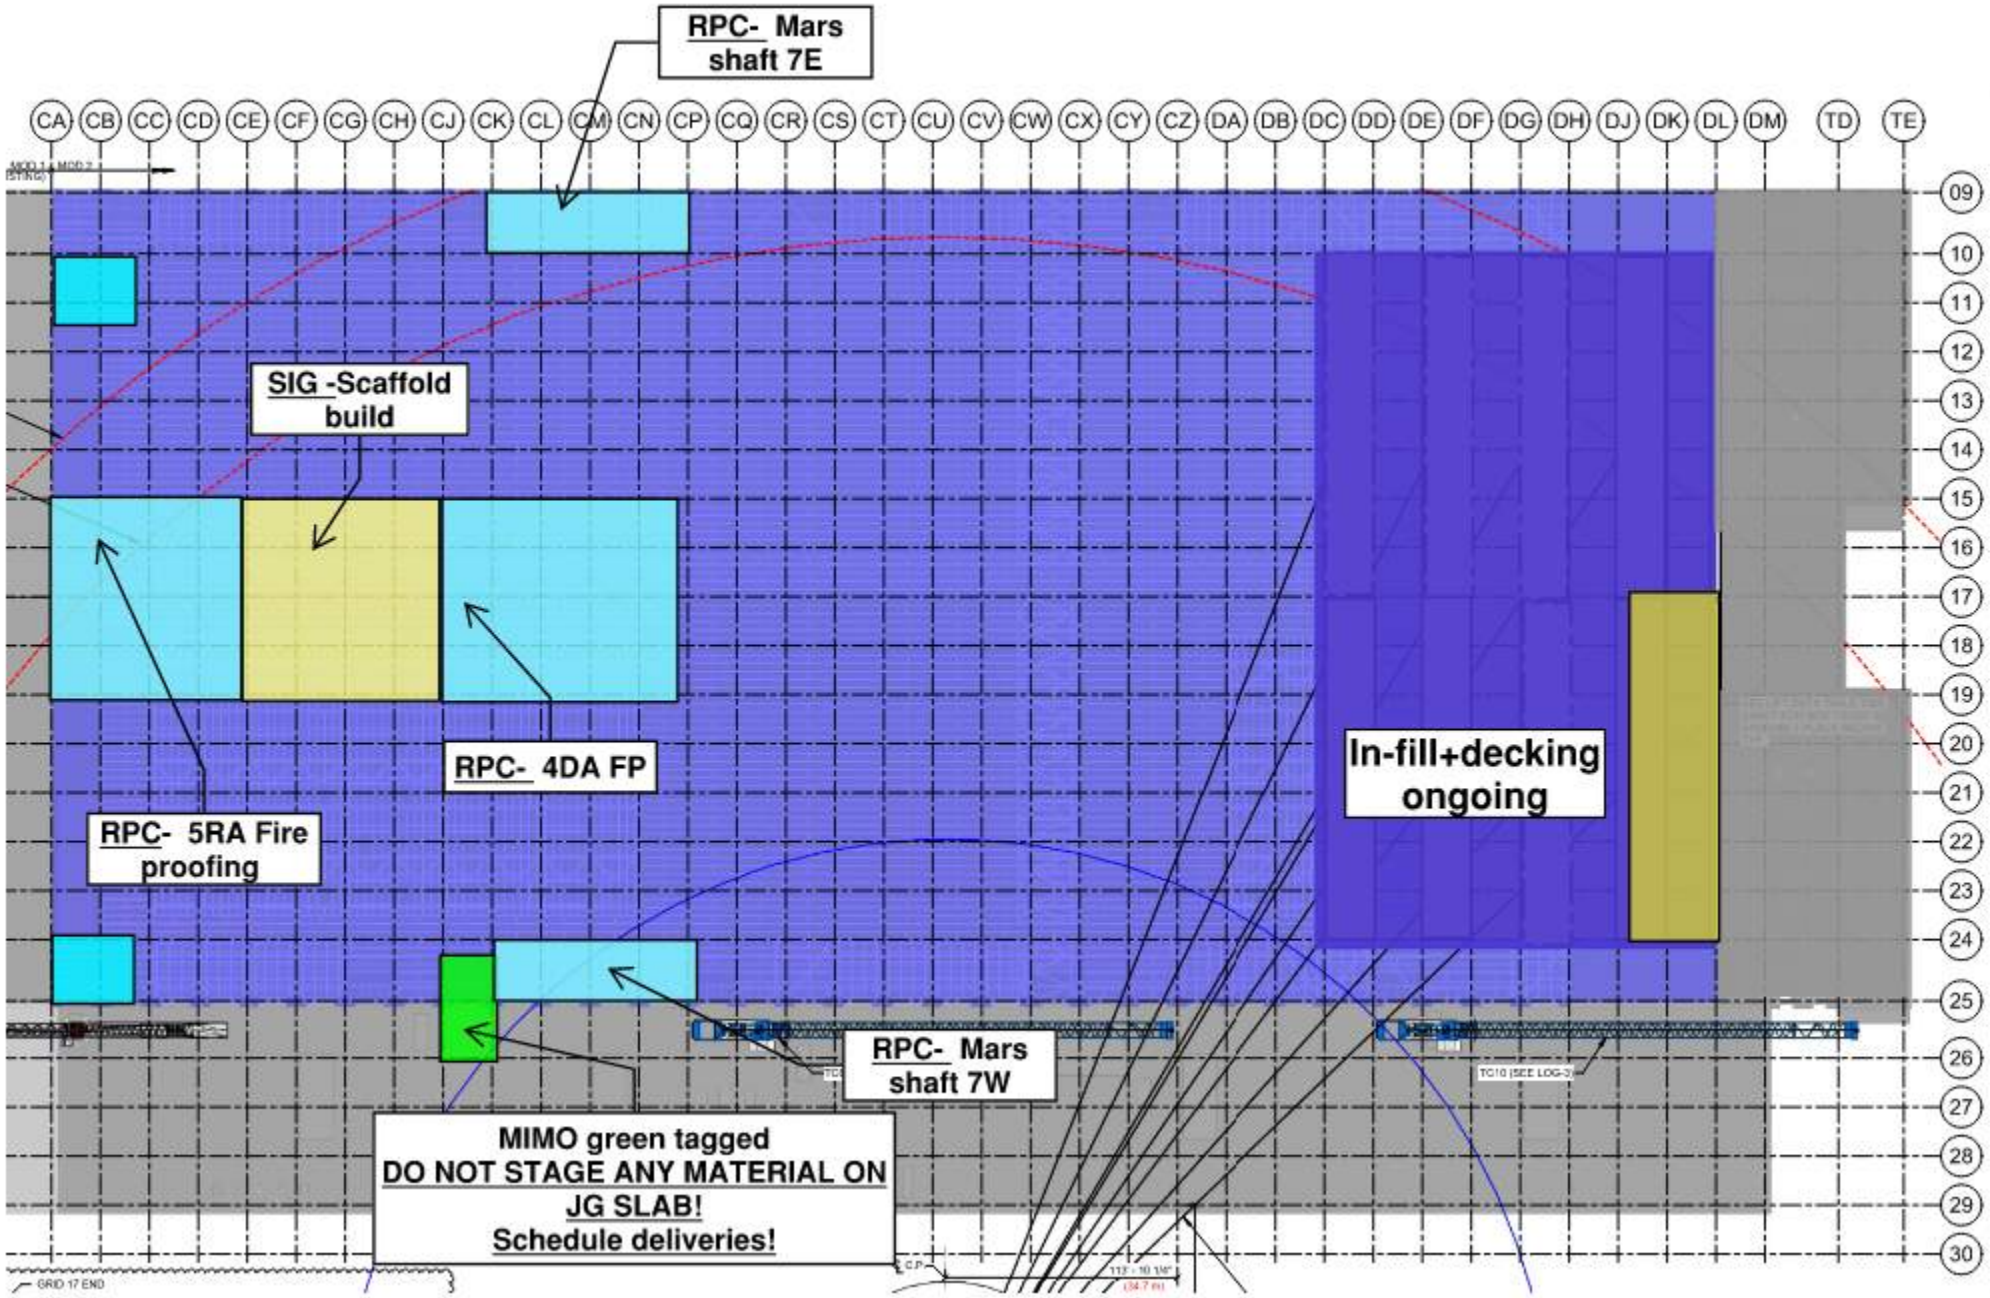

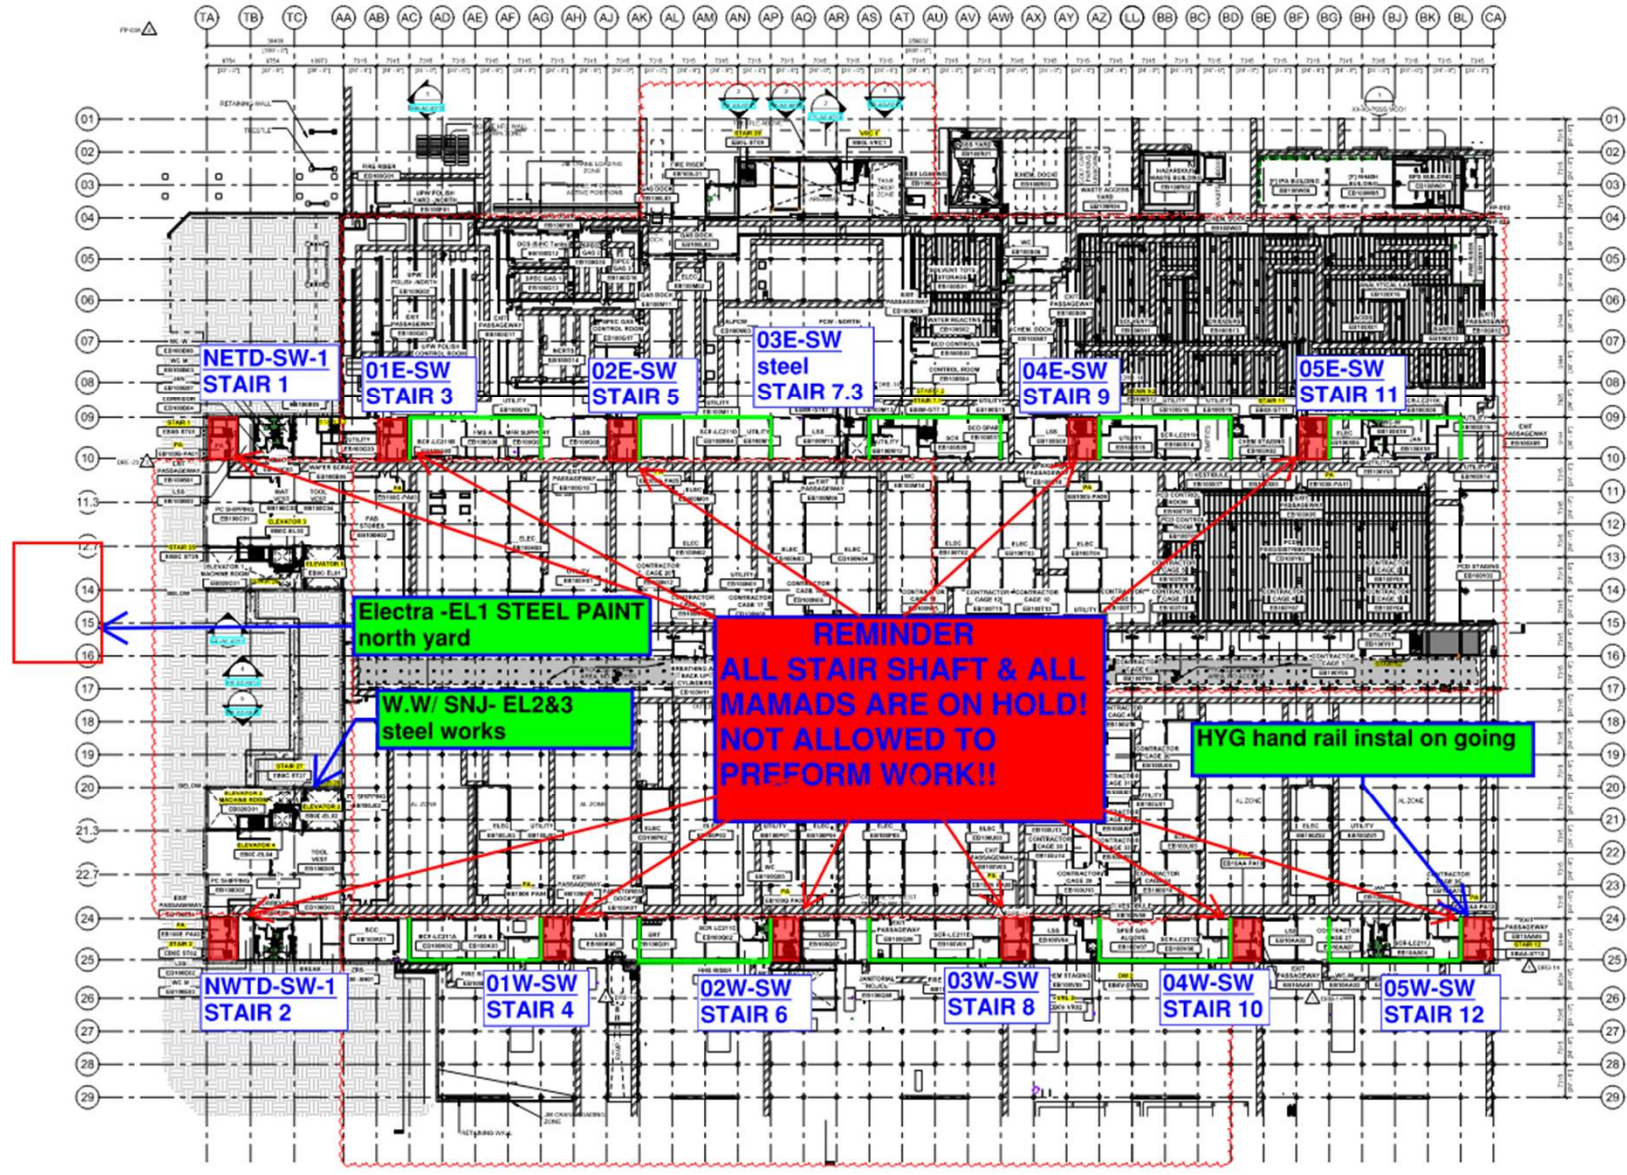

NETD-SW-1
STAIR 1

01E-SW
STAIR 3

02E-SW
STAIR 5

03E-SW
steel
STAIR 7.3

04E-SW
STAIR 9

05E-SW
STAIR 11

N2WD-SW-1
STAIR 2

01W-SW
STAIR 4

02W-SW
STAIR 6

03W-SW
STAIR 8

04W-SW
STAIR 10

05W-SW
STAIR 12

**REMINDER
ALL STAIR SHAFT & ALL
MAMADS ARE ON HOLD!
NOT ALLOWED TO
PREFORM WORK!!**

**Electra -EL1 STEEL PAINT
north yard**

**W.W/ SNJ- EL2&3
steel works**


HYG hand rail instal on going


Mod 2 E House Roof
Picks.

Jan 7th @ 4:00 AM
Jan 8th @ 4:00 AM

Area to be
Closed for
Swing

Condensed
Barricade
for Bolting.

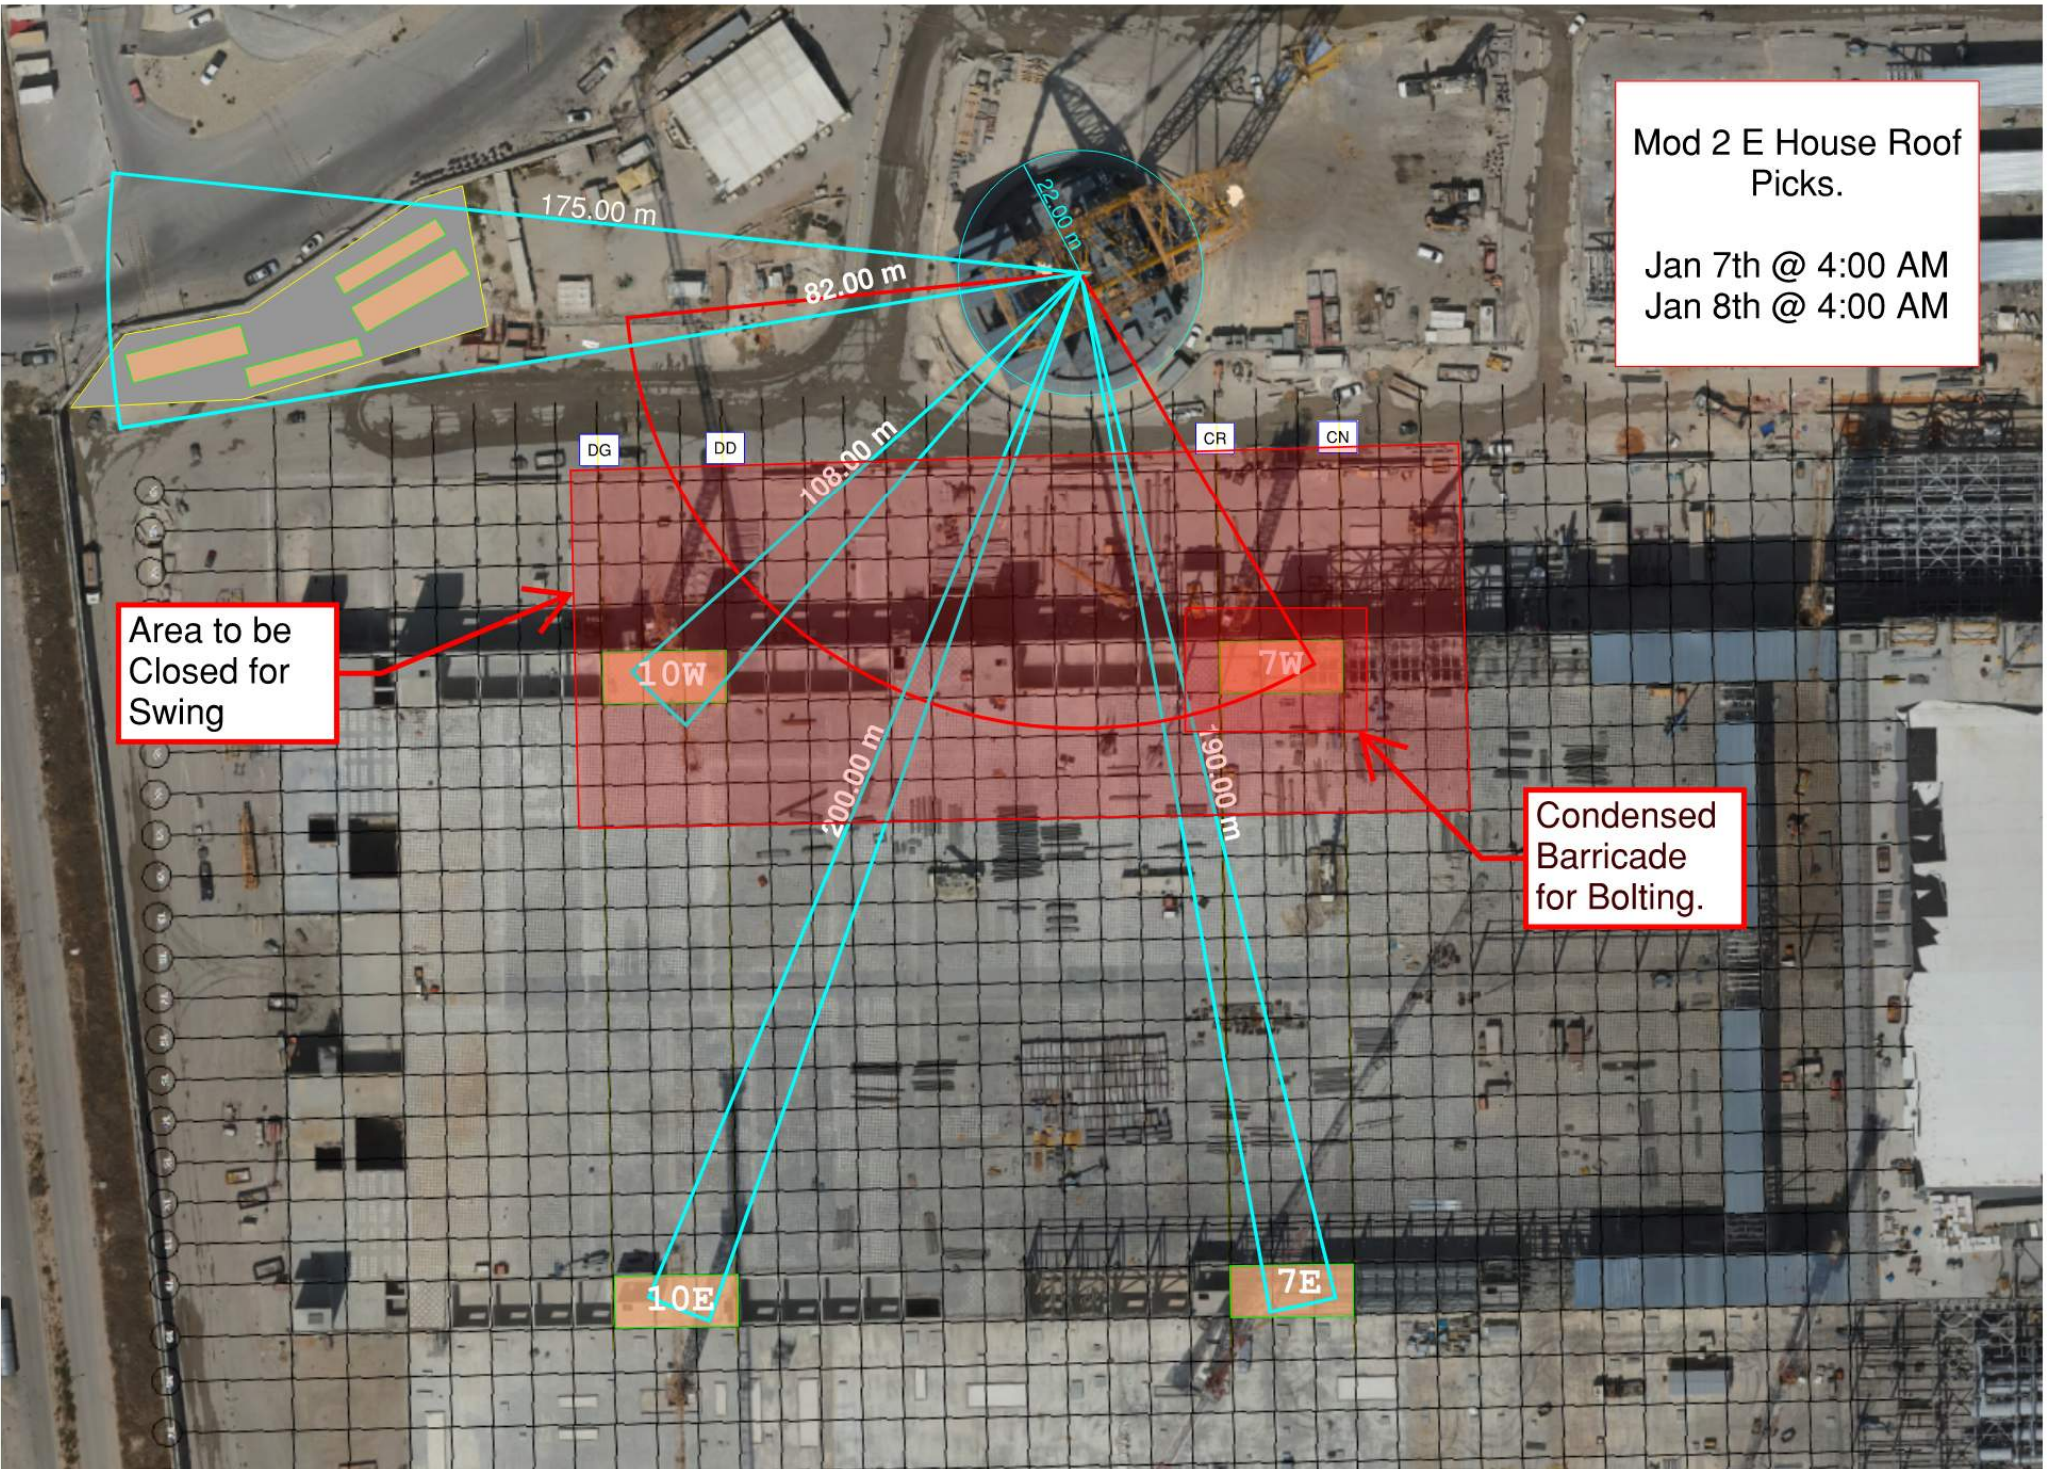

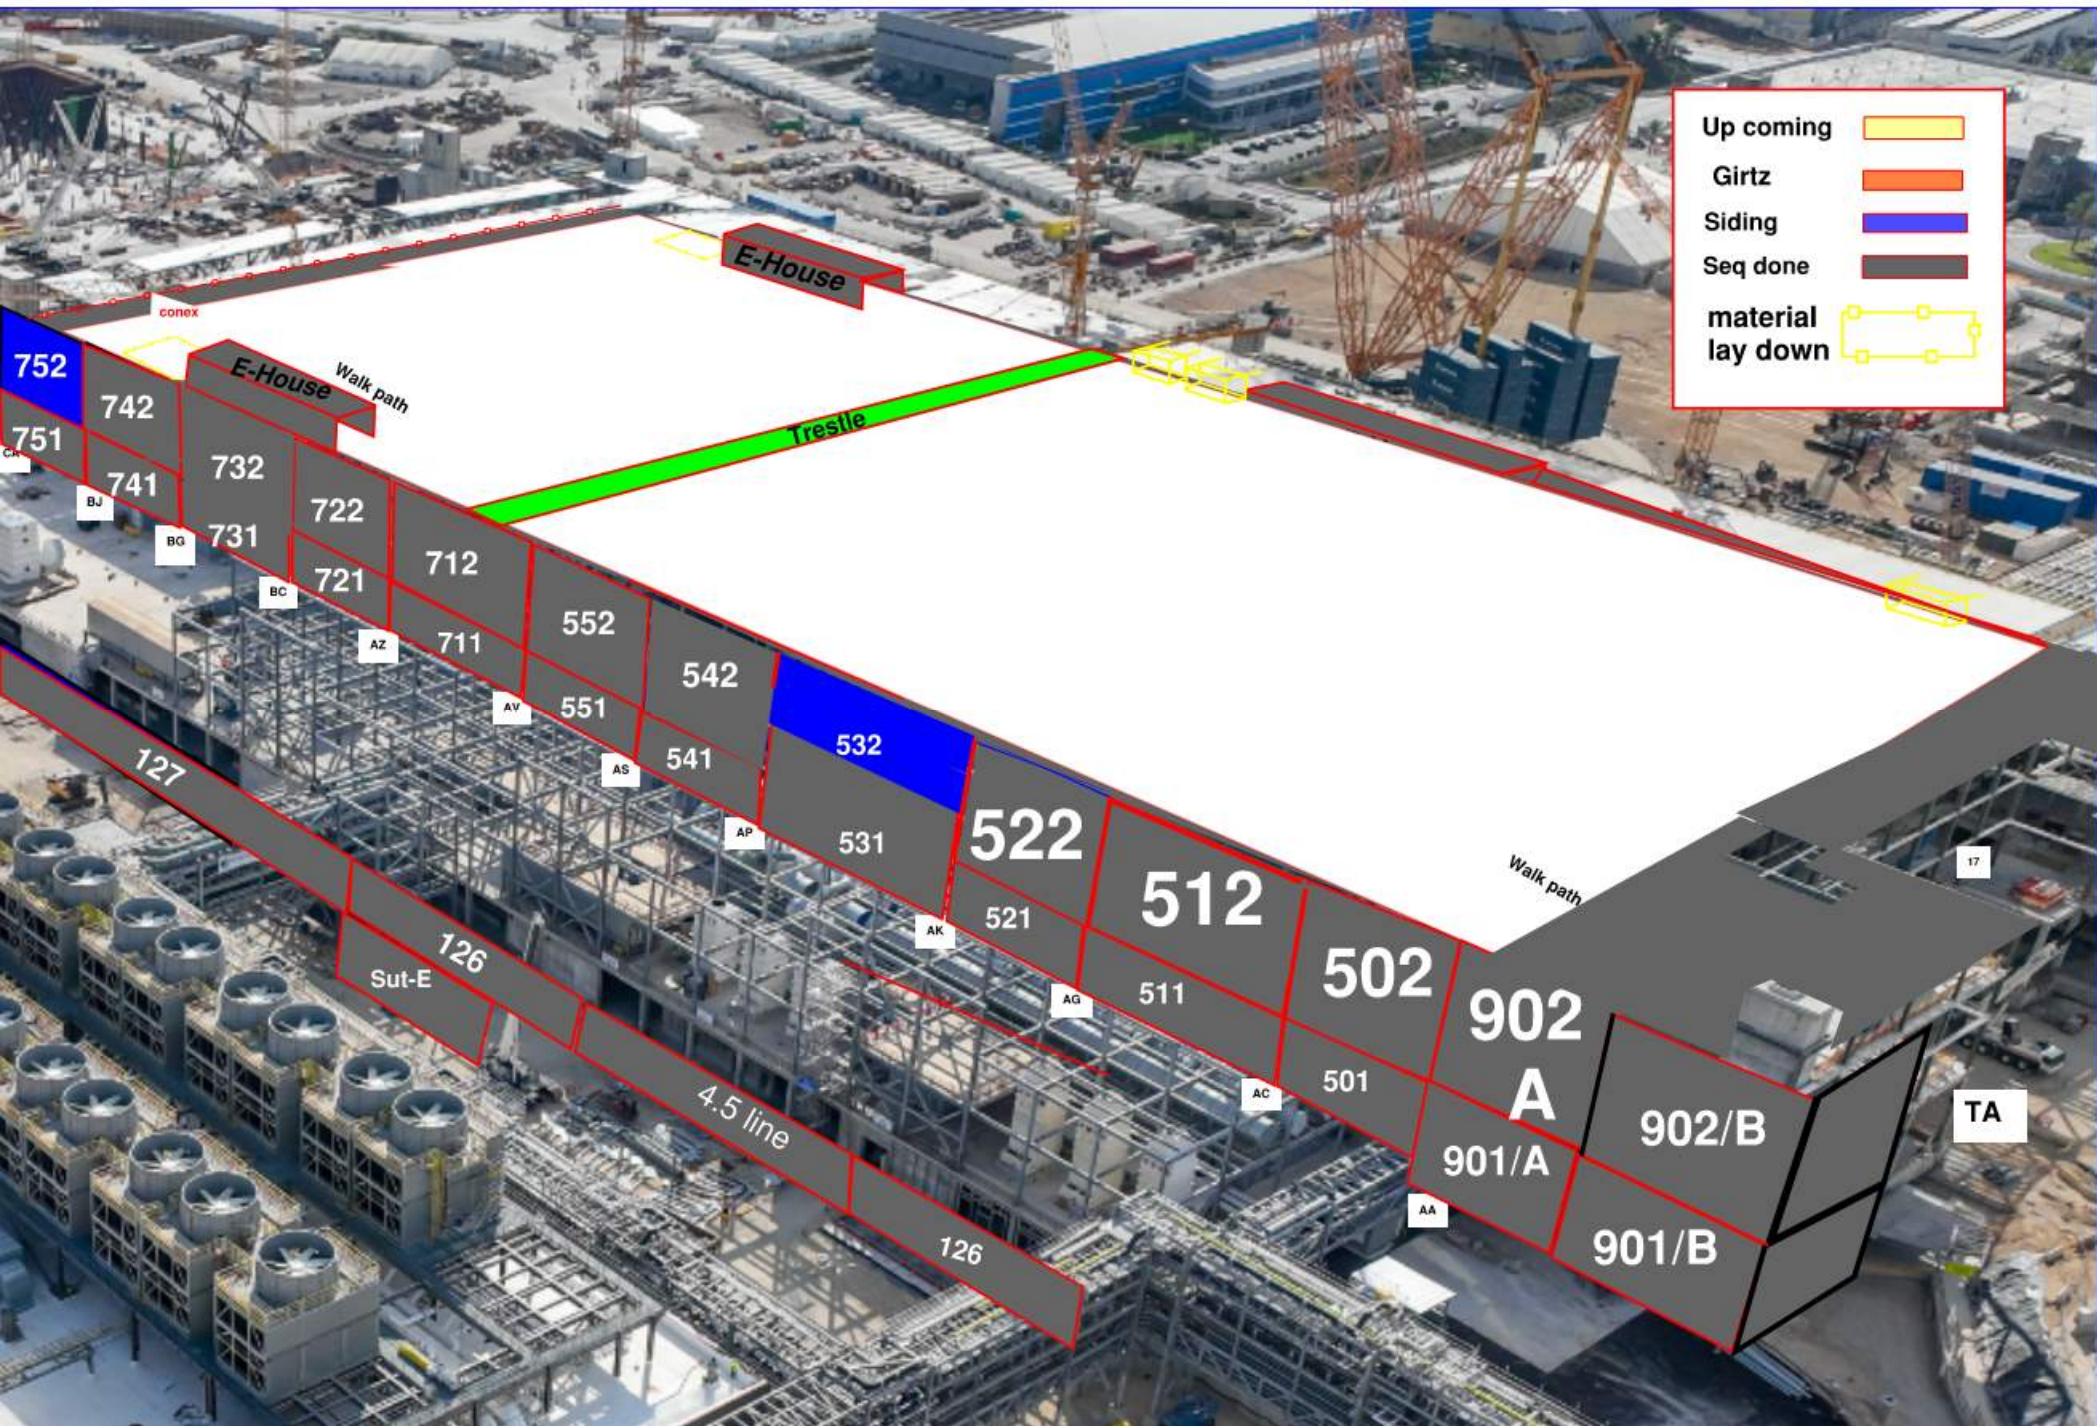


Up coming	
Girtz	
Siding	
Seq done	
material lay down	

752
751
742
741
732
731
722
721
712
711
552
542
532
522
512
502
902
901/A
901/B

E-House
E-House
Trestle
Sut-E
4.5 line

Walk path
Walk path

conex
BJ
BG
BC
AZ
AV
AS
AP
AK
AG
AC
AA
TA
17

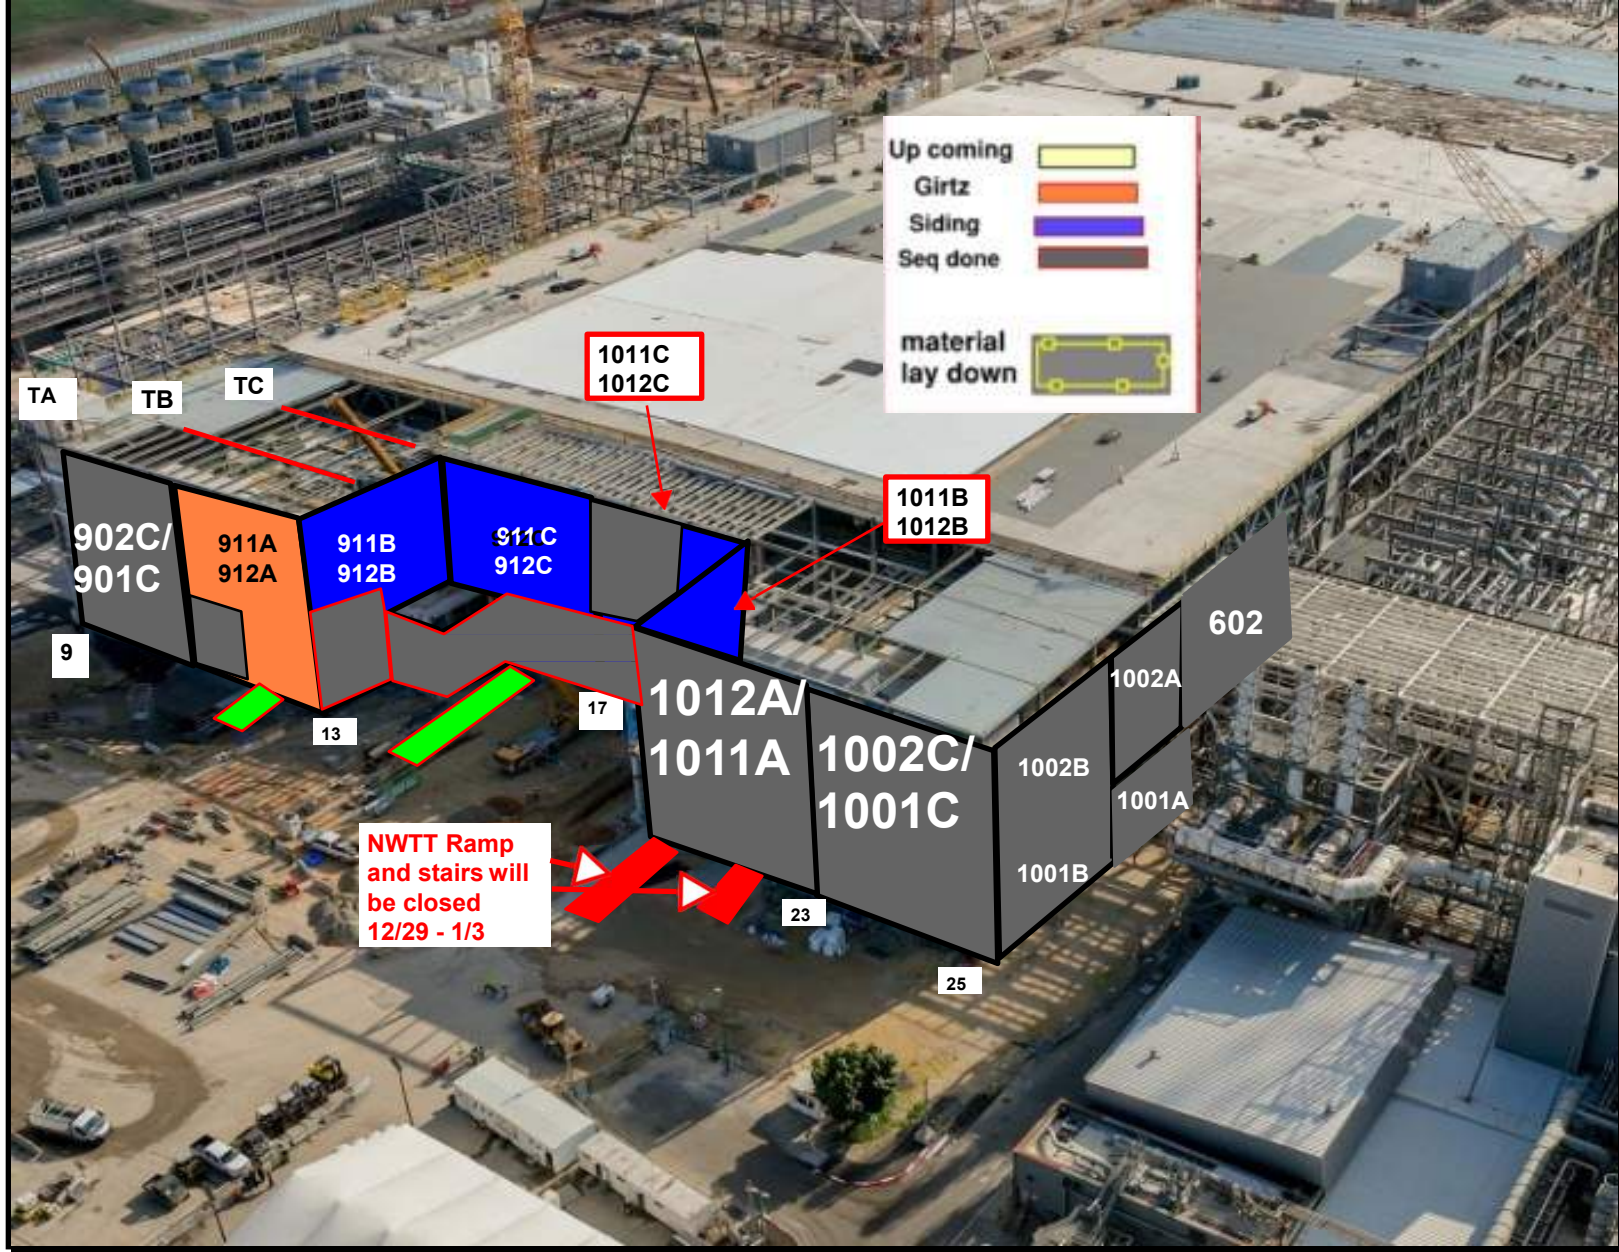

Up coming
Girtz
Siding
Seq done

material lay down

1011C
1012C

1011B
1012B

NWTT Ramp
and stairs will
be closed
12/29 - 1/3

TA

TB

TC

902C/
901C

911A
912A

911B
912B

911C
912C

9

13

17

1012A/
1011A

1002C/
1001C

602

1002A


1002B

1001A

1001B

23

25

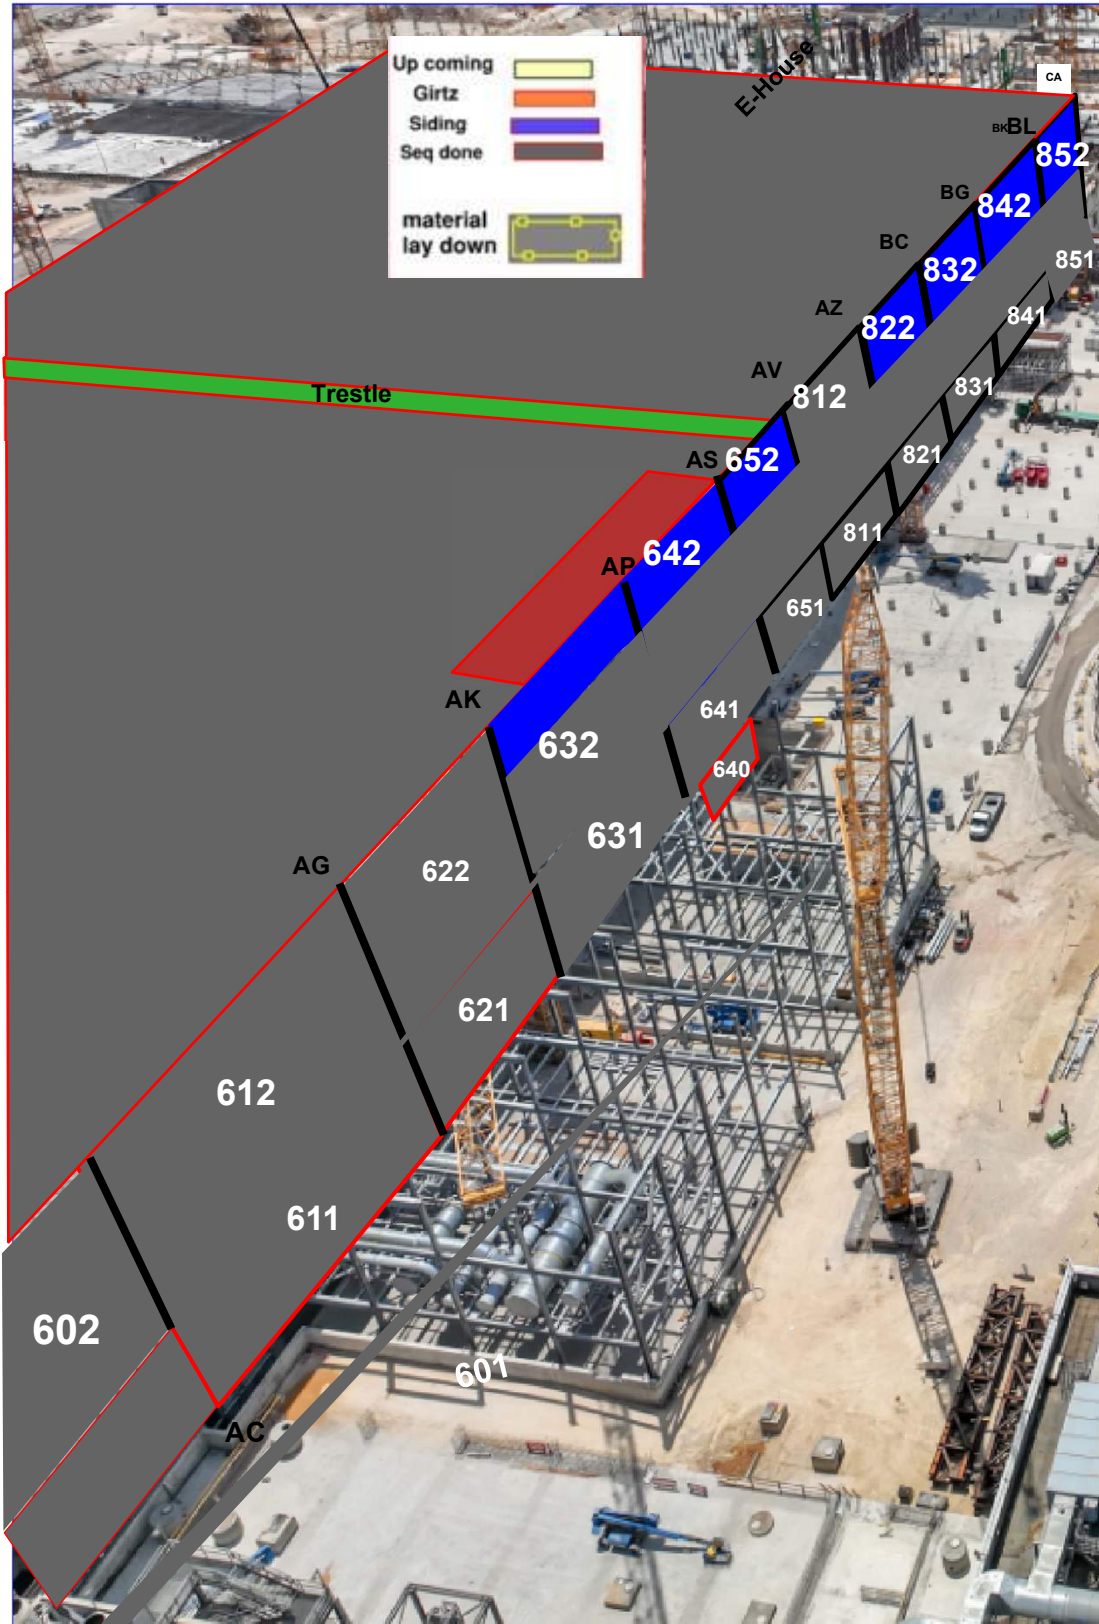

Up coming	
Girtz	
Siding	
Seq done	
material lay down	

602

612

611

601

AG

622

621

631

AK

632

641

640

AP

642

AS

652

AV

812

AZ

822

BC

832

BG

842

BL

852

CA


Trestle

E-House

PSSS.1

Utility Level 1YA

PSSS Roof 2SA

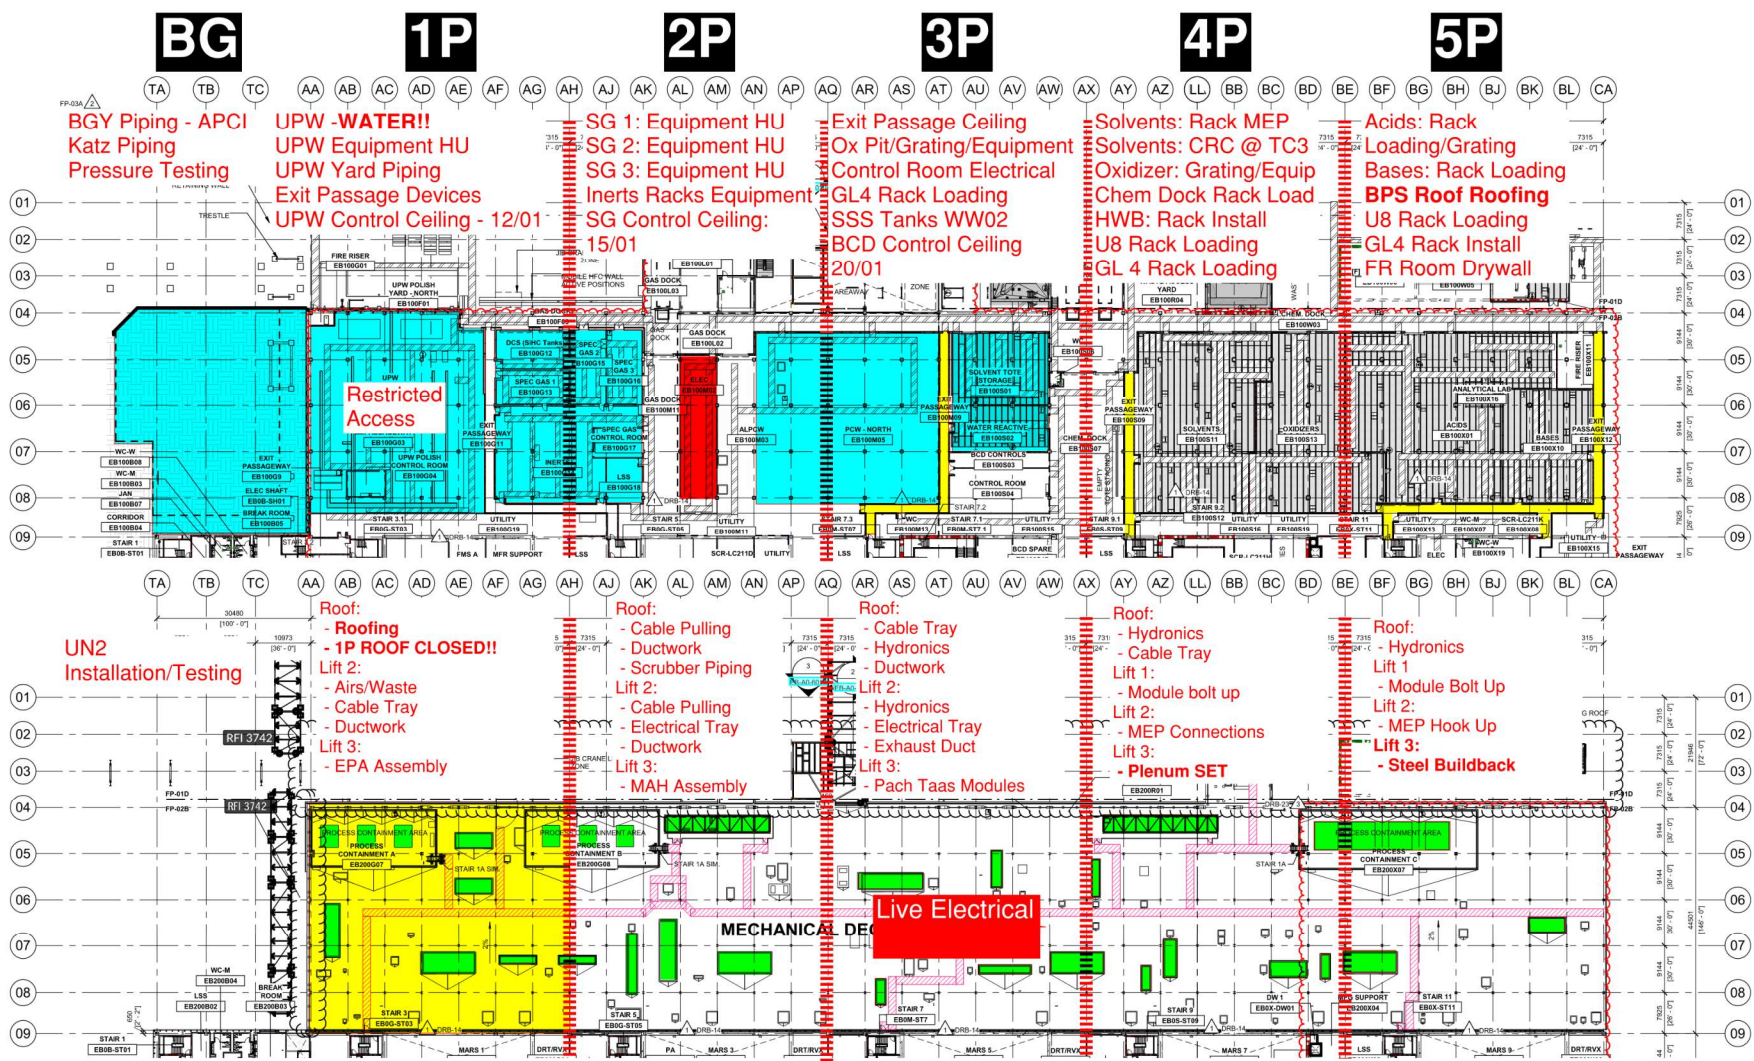

PSSS.2

6P


7P

8P


9P

10P


Utility Level
1YA

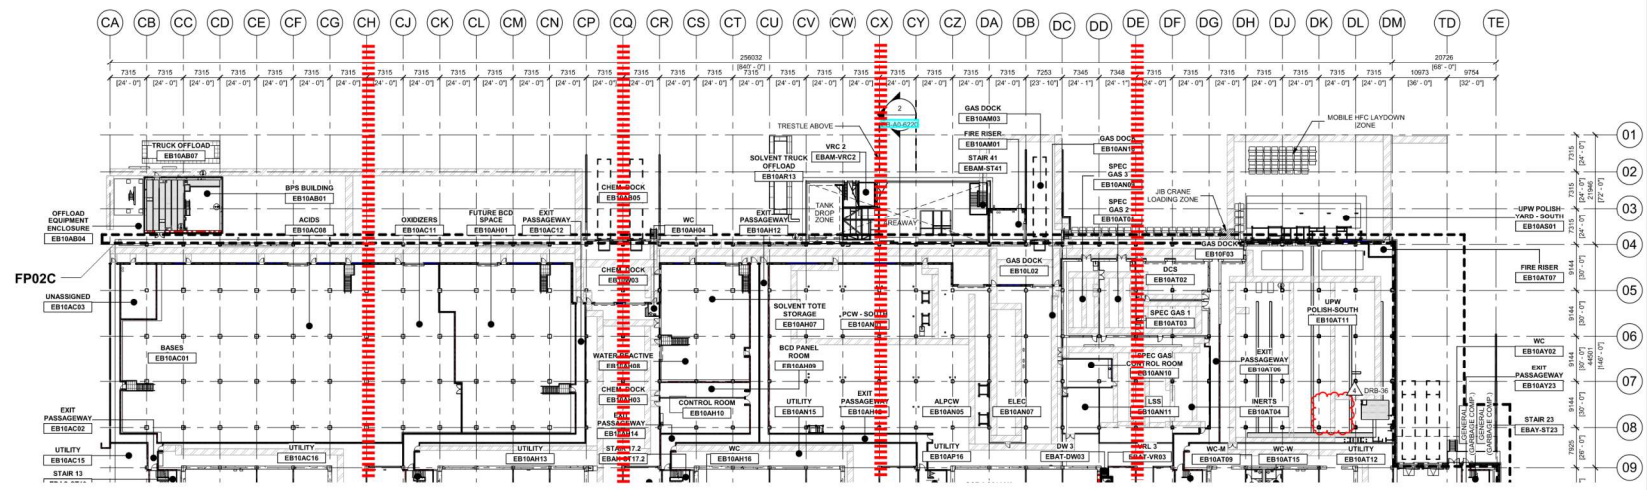

PSSS Roof
2SA

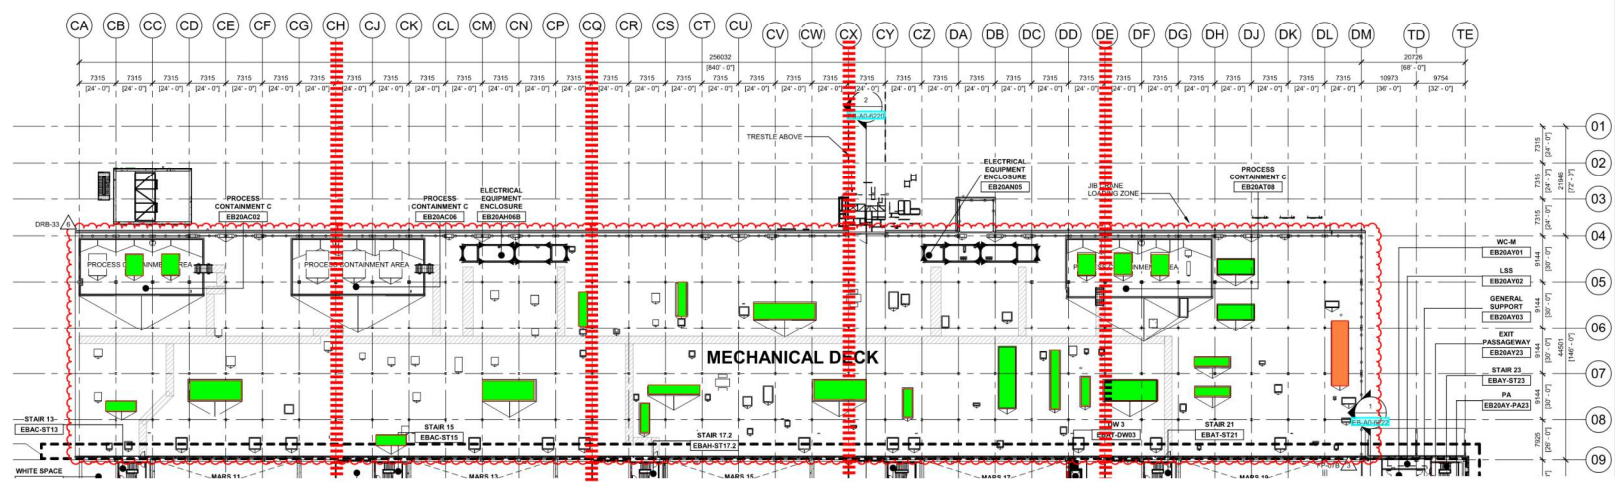


PSSS Pressure Tests

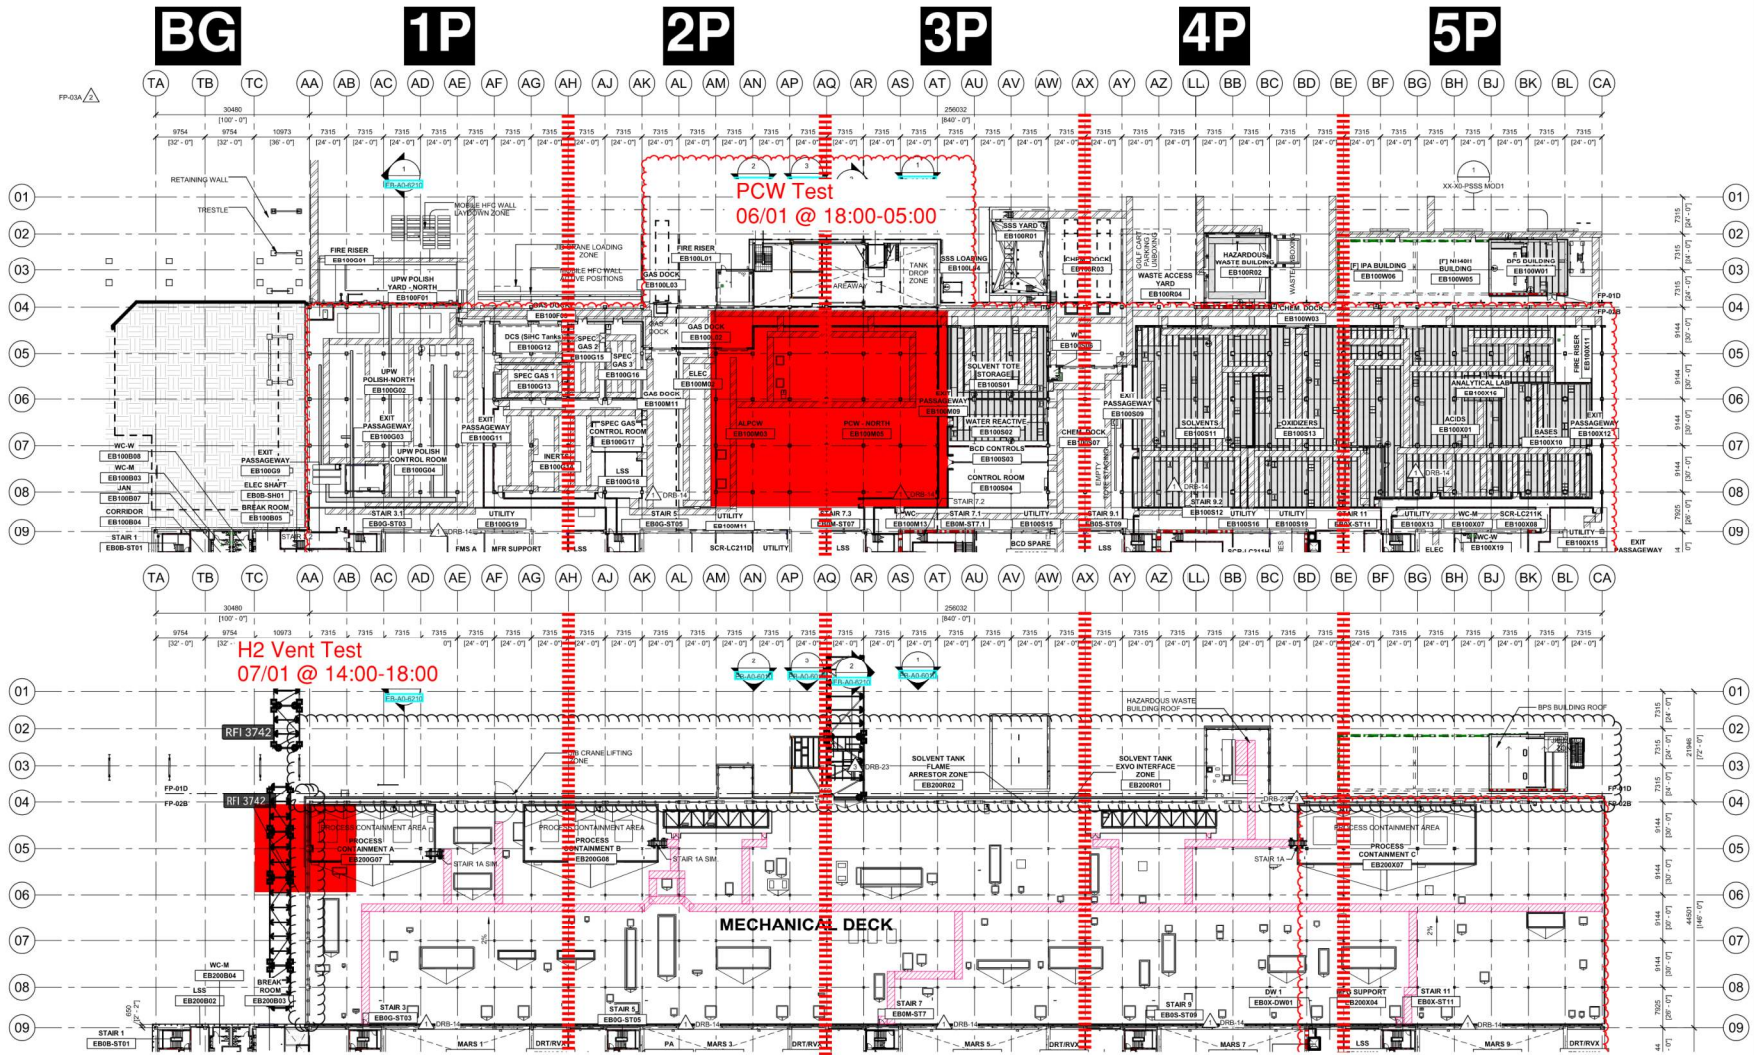

Utility Level
1YA


PSSS Roof
2SA

3800 Hoisting WW02




3800 Activity after 17:00
6/1 - Plenum
7/1 - MAH
9/1 - MAH


WJG 01J, 02J LIFT 2 & 3

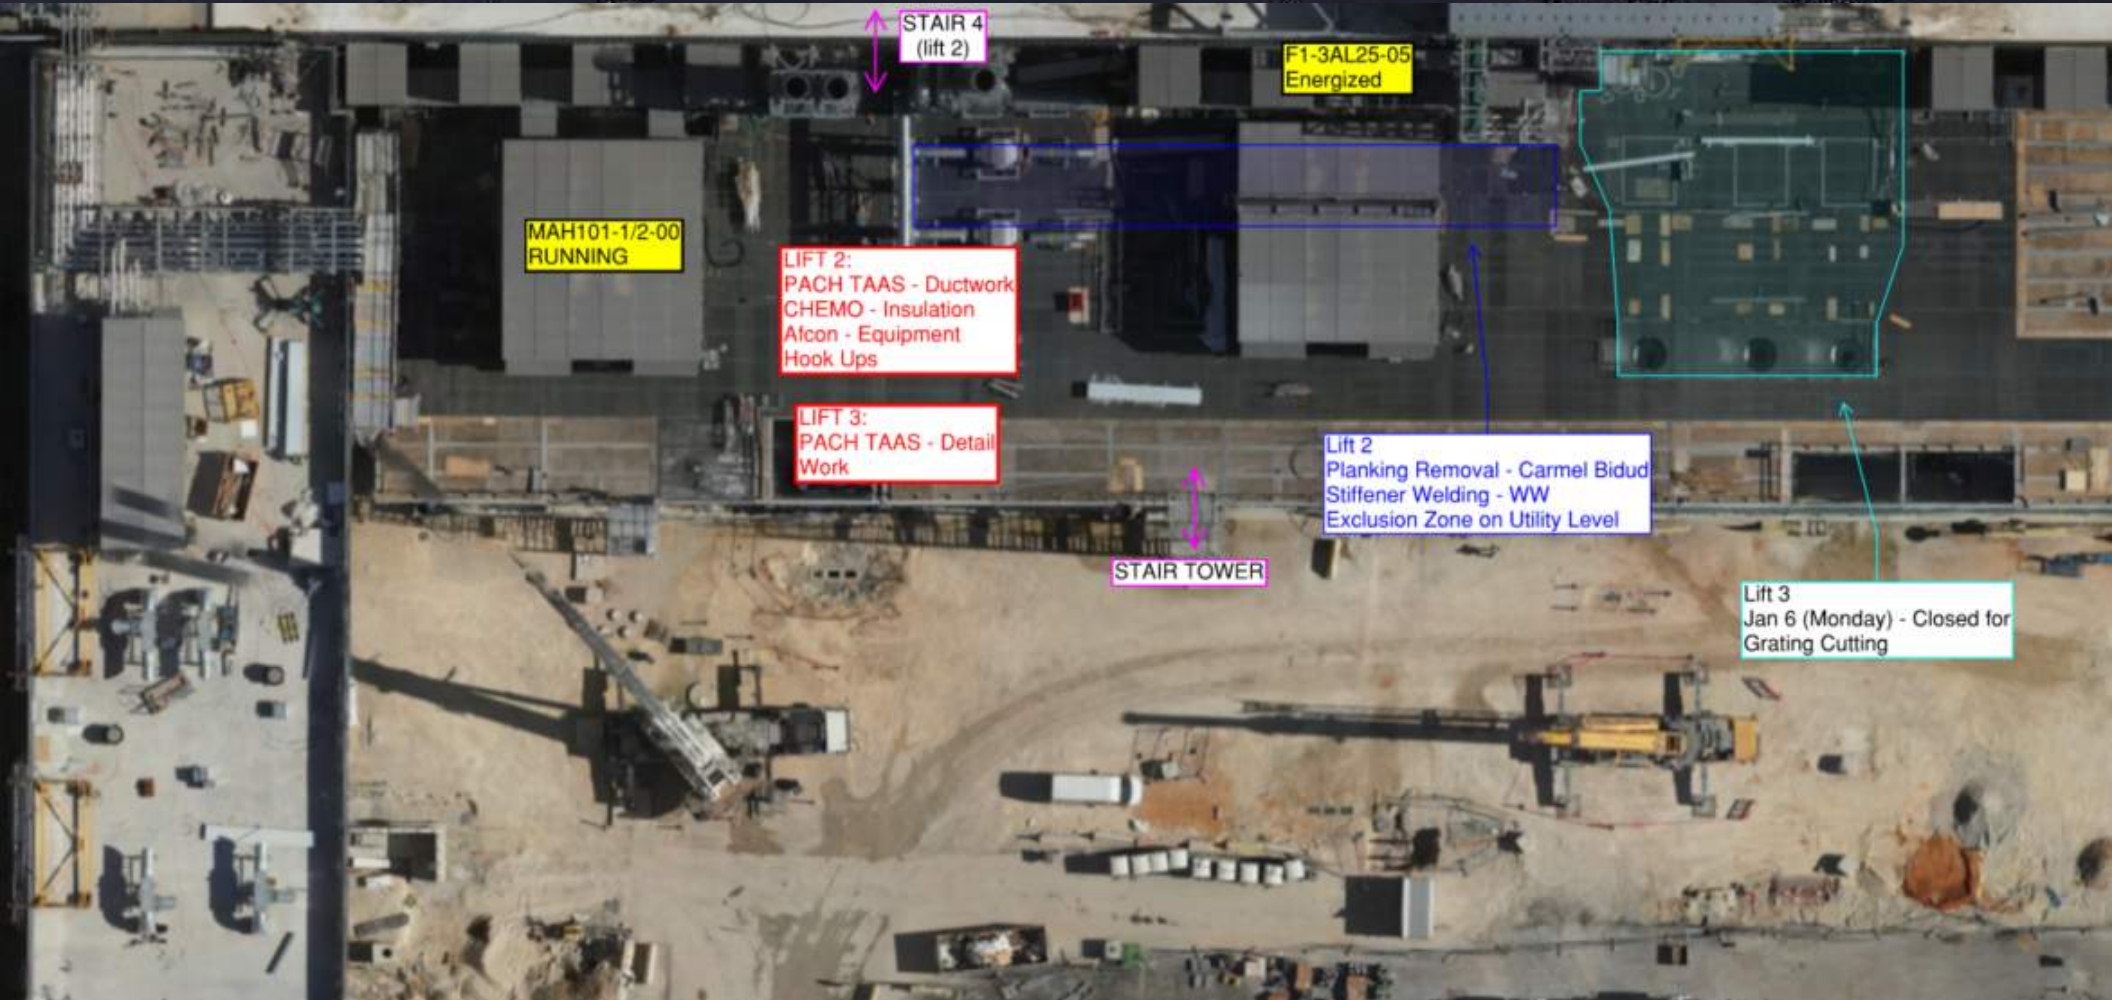

WJG 03J, 04J, 05J LIFT 2 & 3

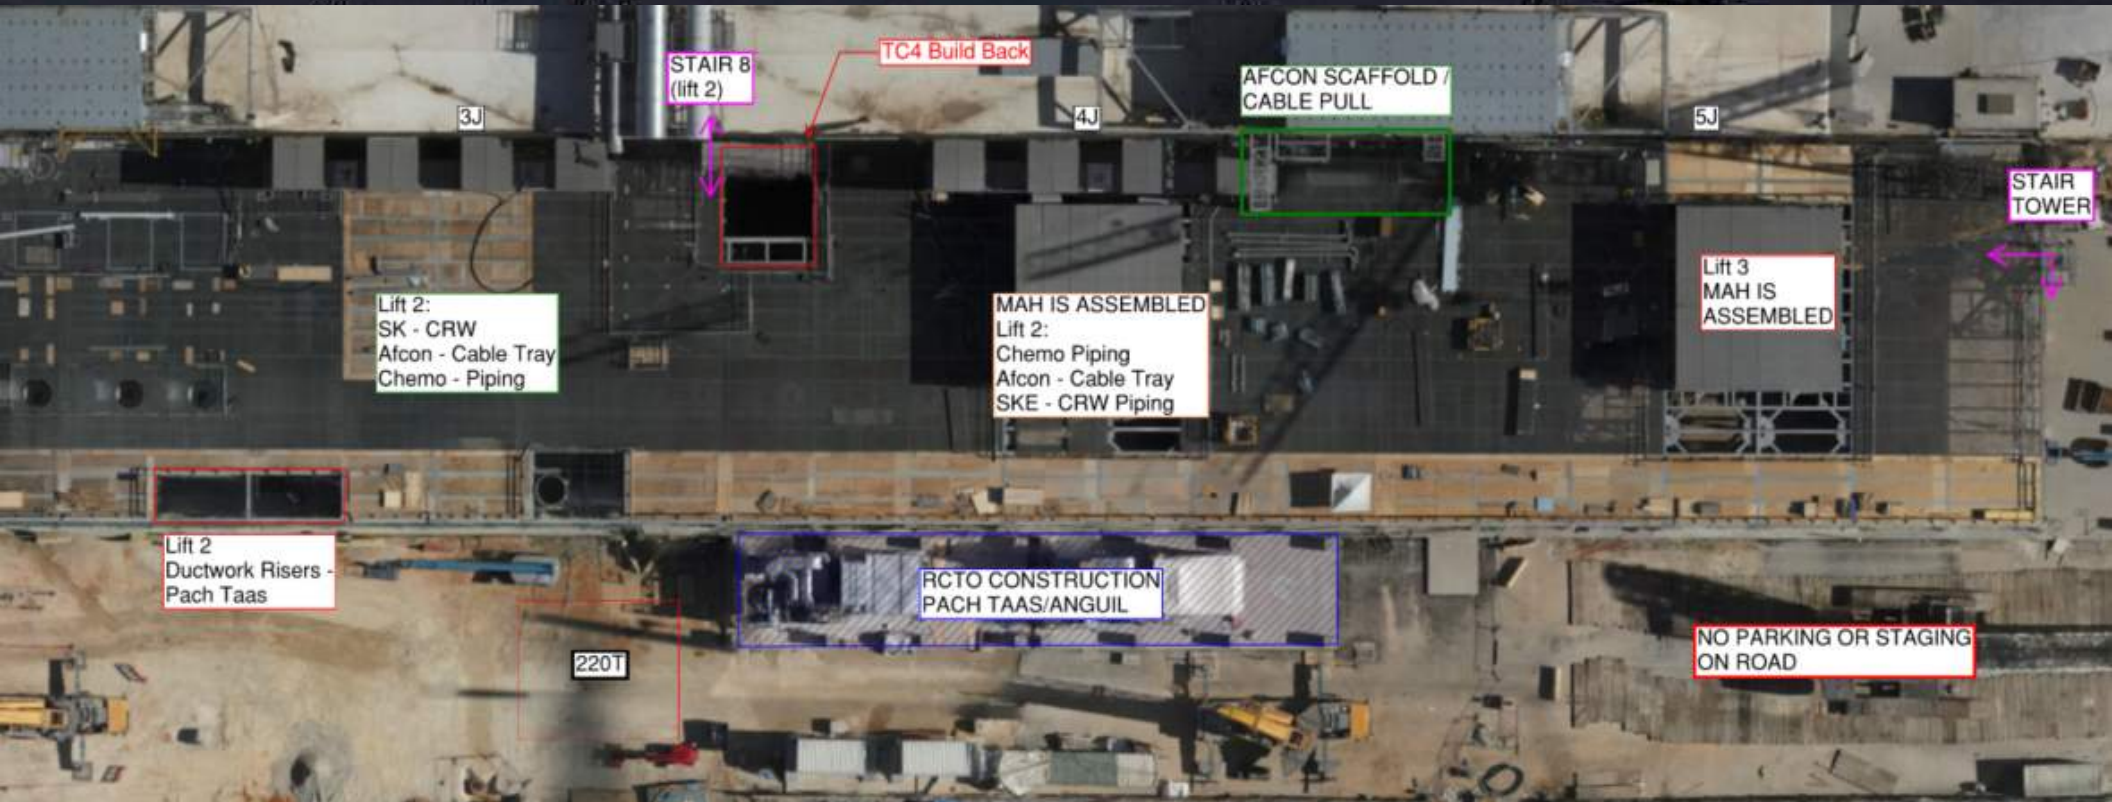


WJG UTILITY LEVEL BUILD OUT

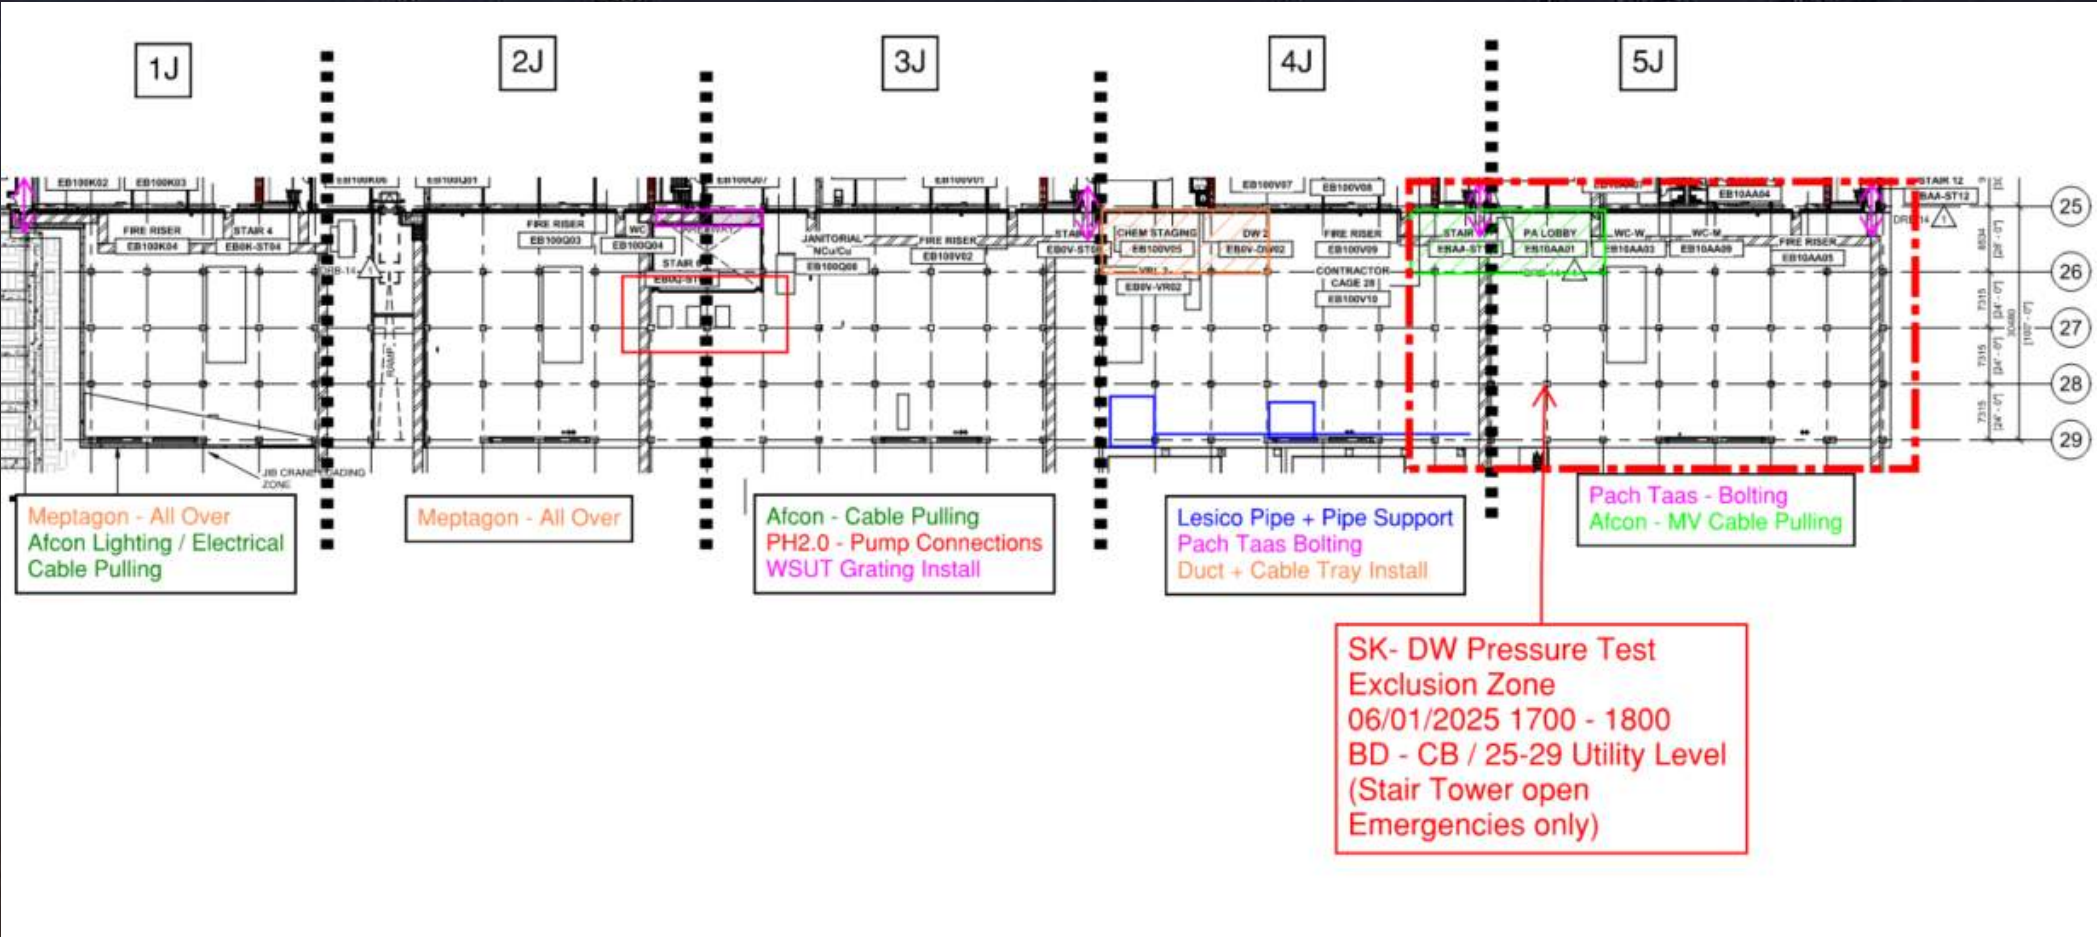


CUB 1 Intel Fuel Off-Load




CUB 1

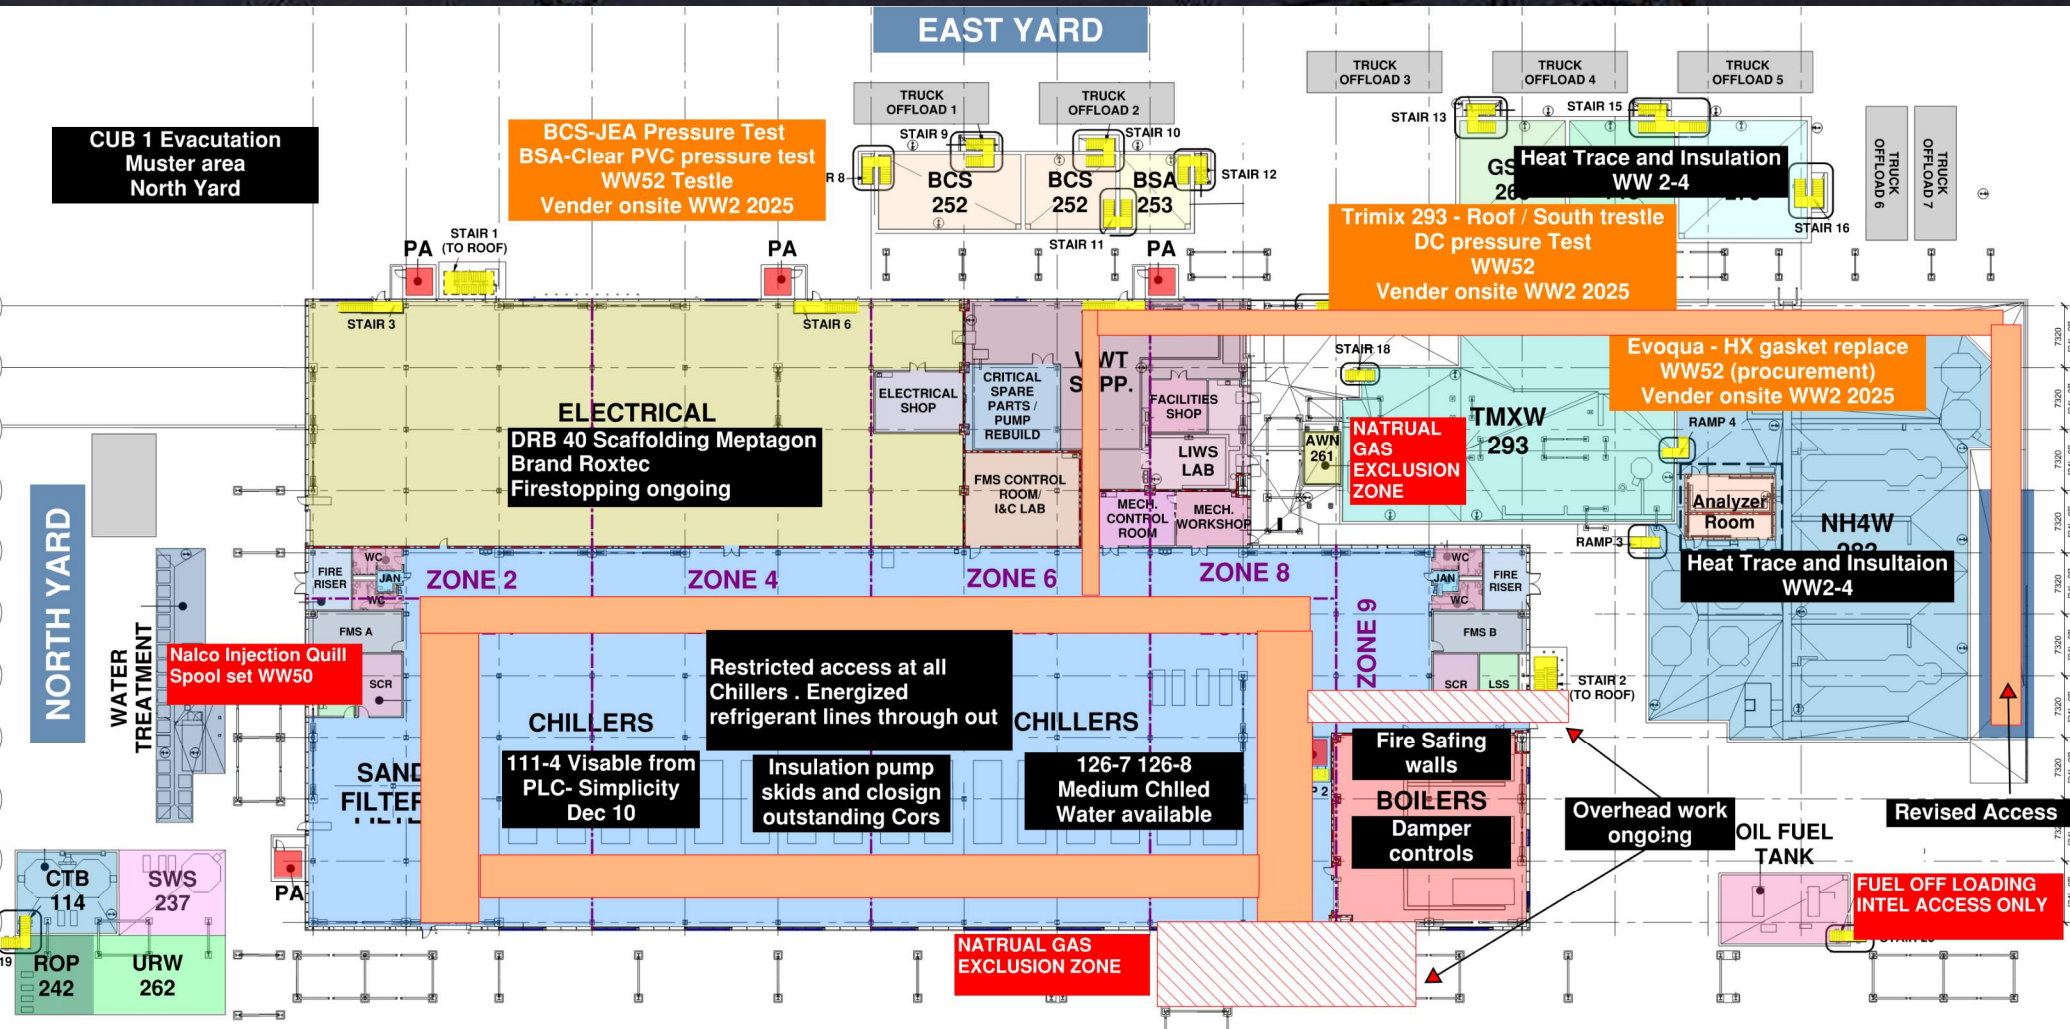

CUB 1 – EXTERIOR/ROOF

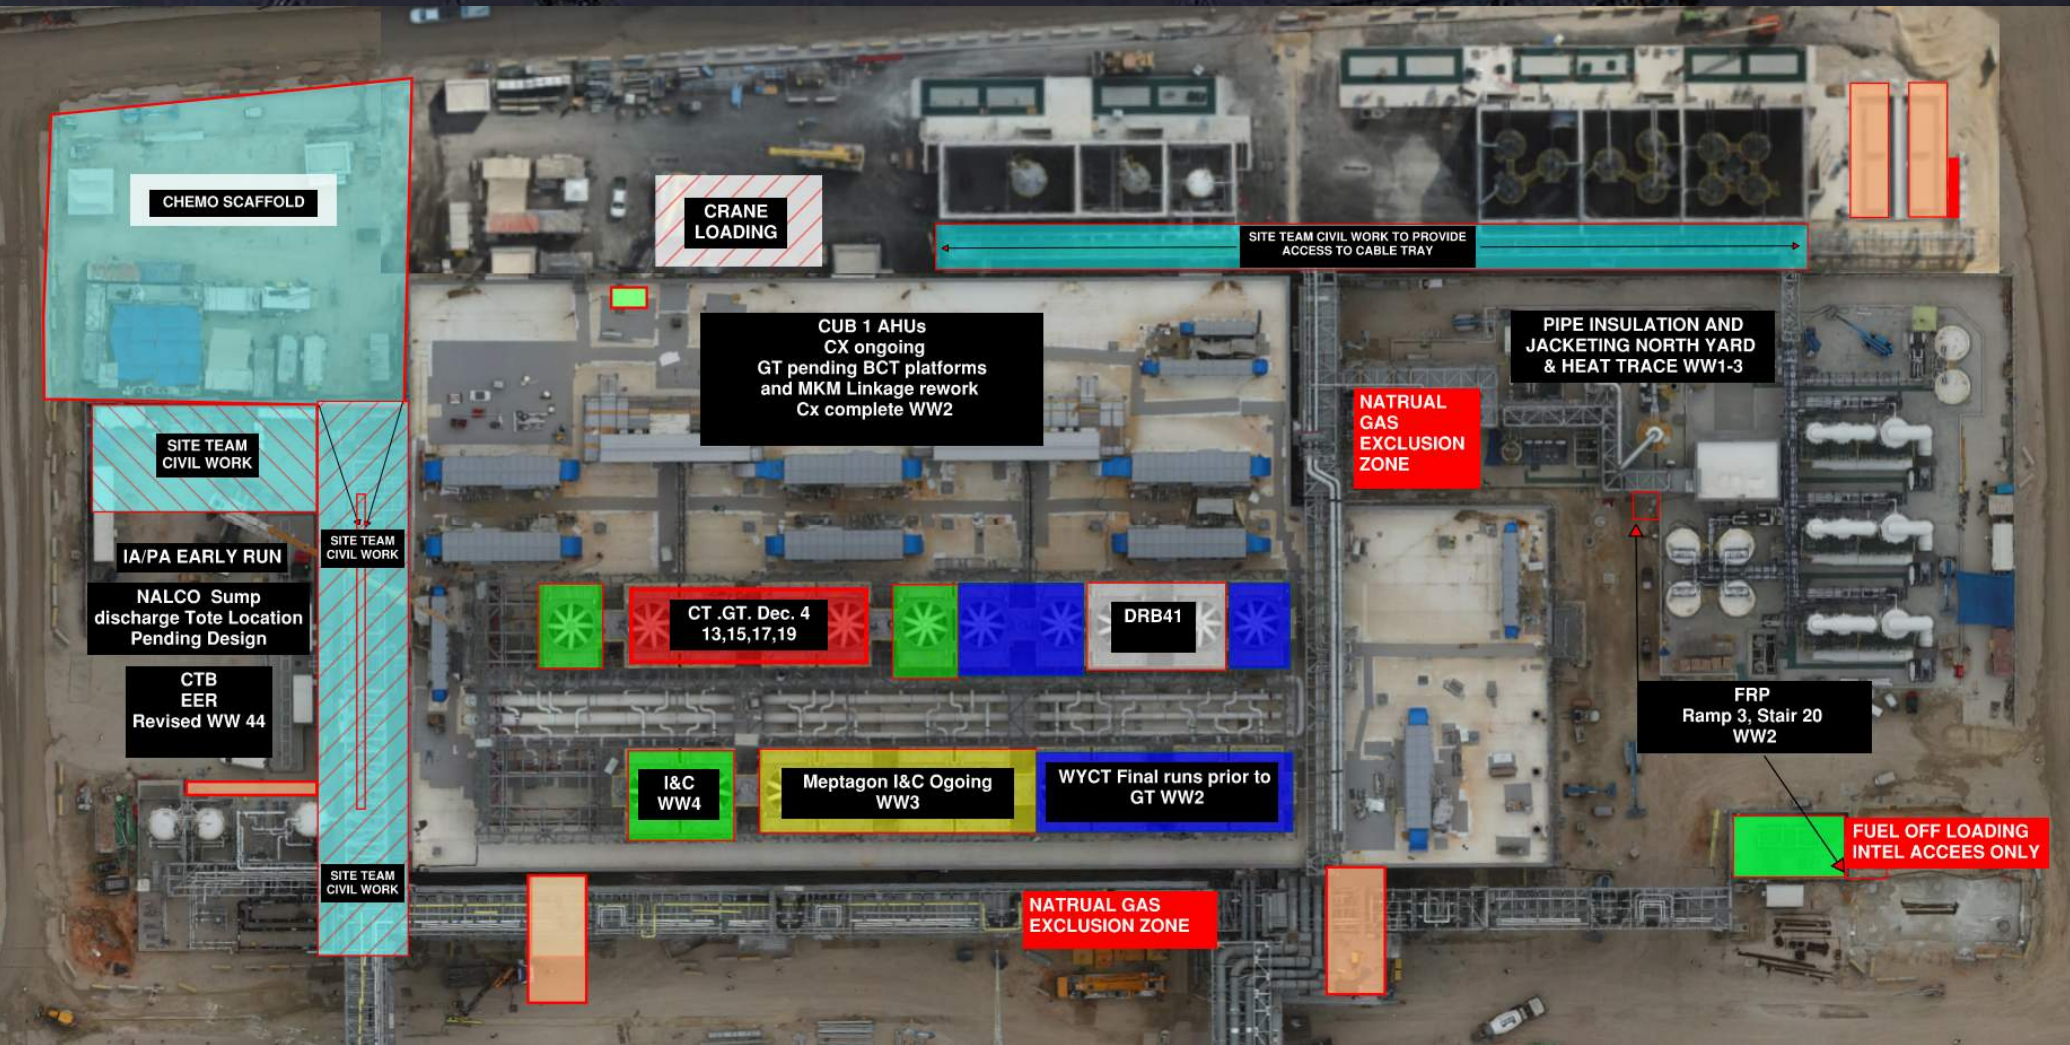


CUB 2- Load in ,H&T, Framing and Sheetrock

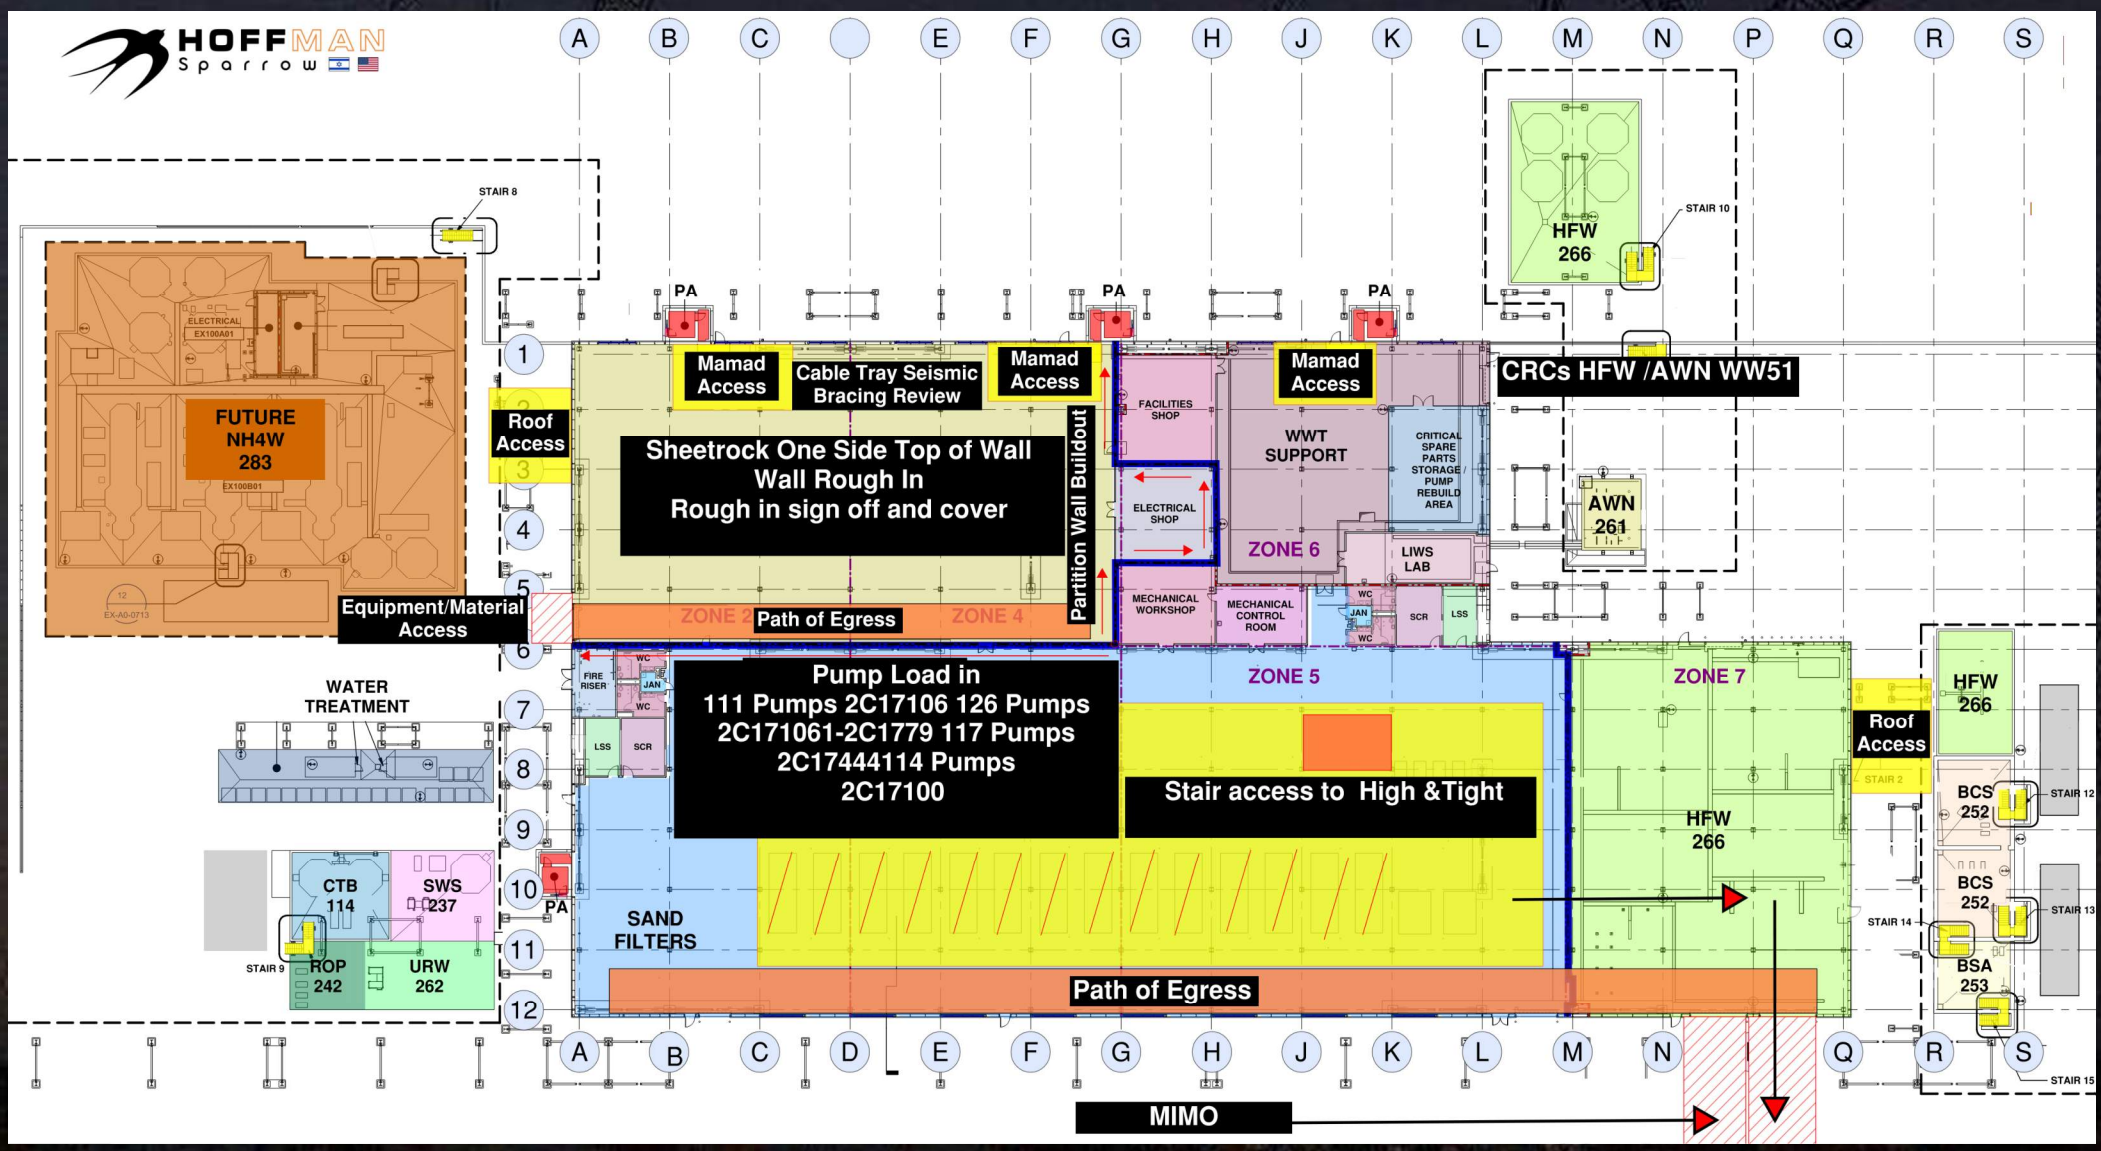

CUB 2 – EXTERIOR/ROOF



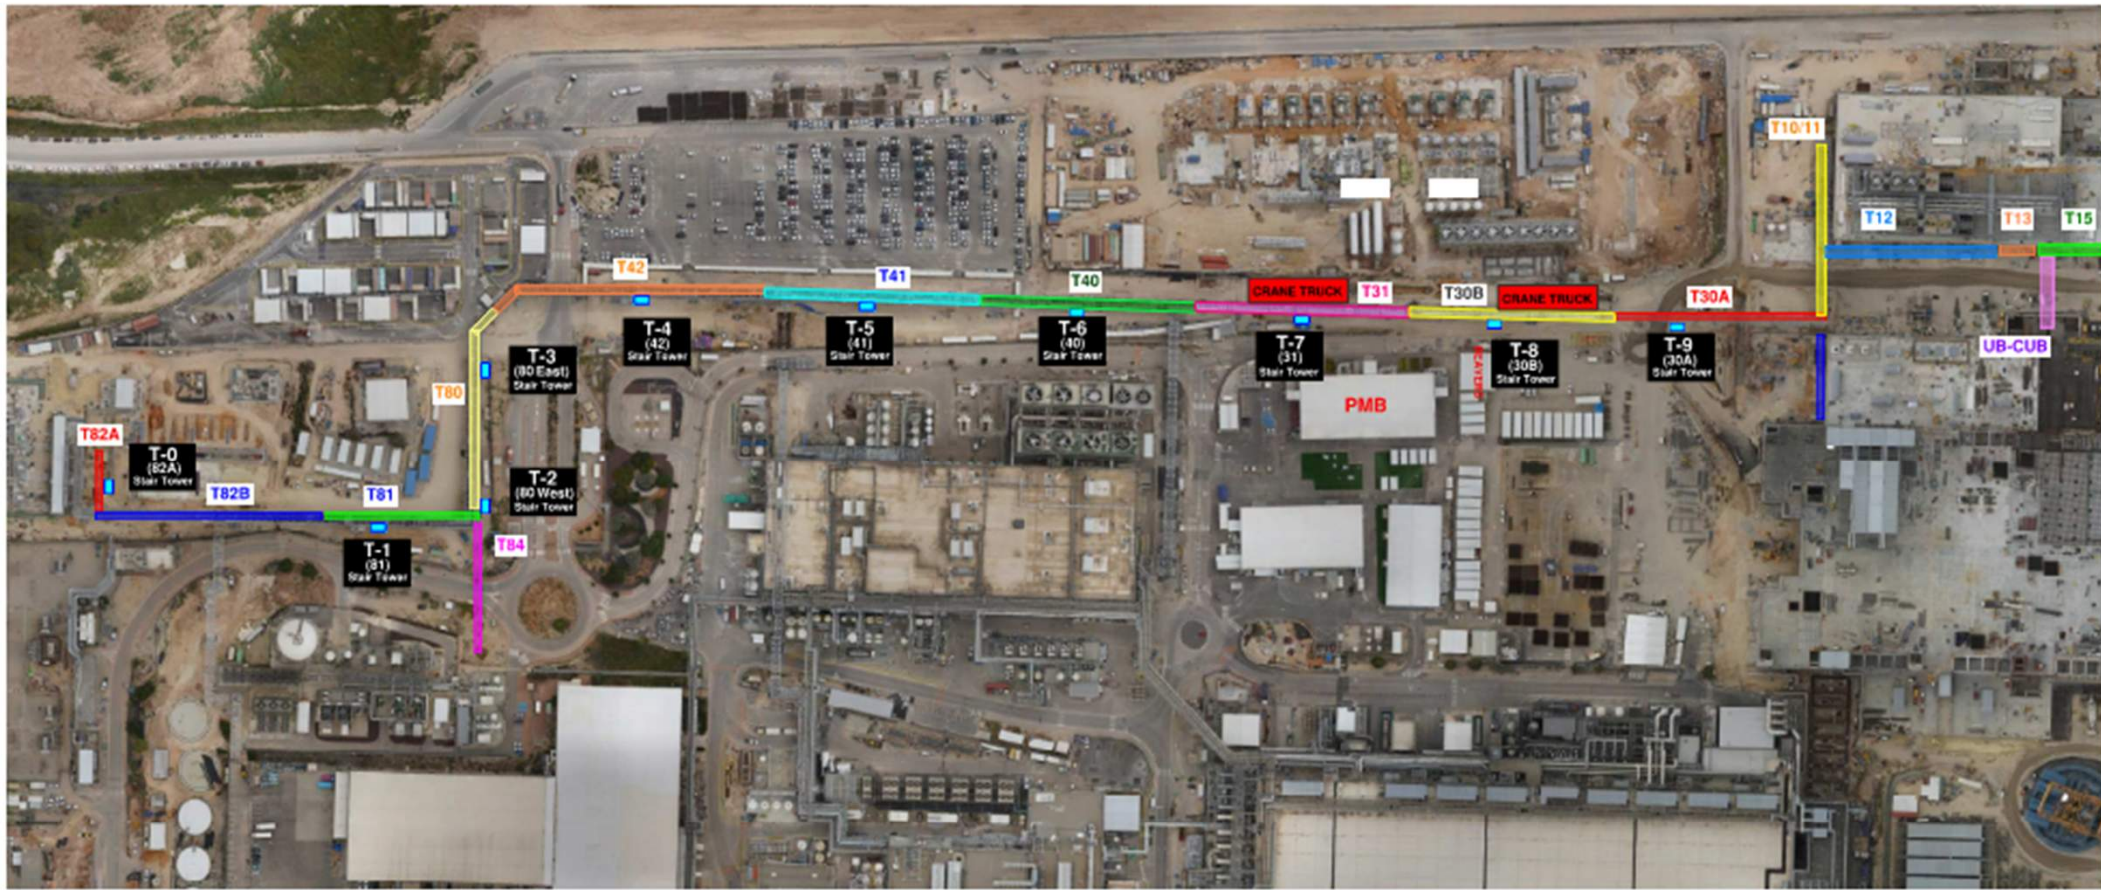

Starting –Monday Jan 6th night at 19:00
Finish Tuesday Jan 7th at 05:00am.

Starting –Tuesday Jan 7th at 19:00
Finish Wednesday Jan 8th at 05:00am

Starting –Wednesday Jan 8th at 19:00
Finish Thursday Jan 9th at 05:00am


BGC - NDT


Safety spotter

No impact on PMB
entrance\Exit

Safety spotter

Safety spotter

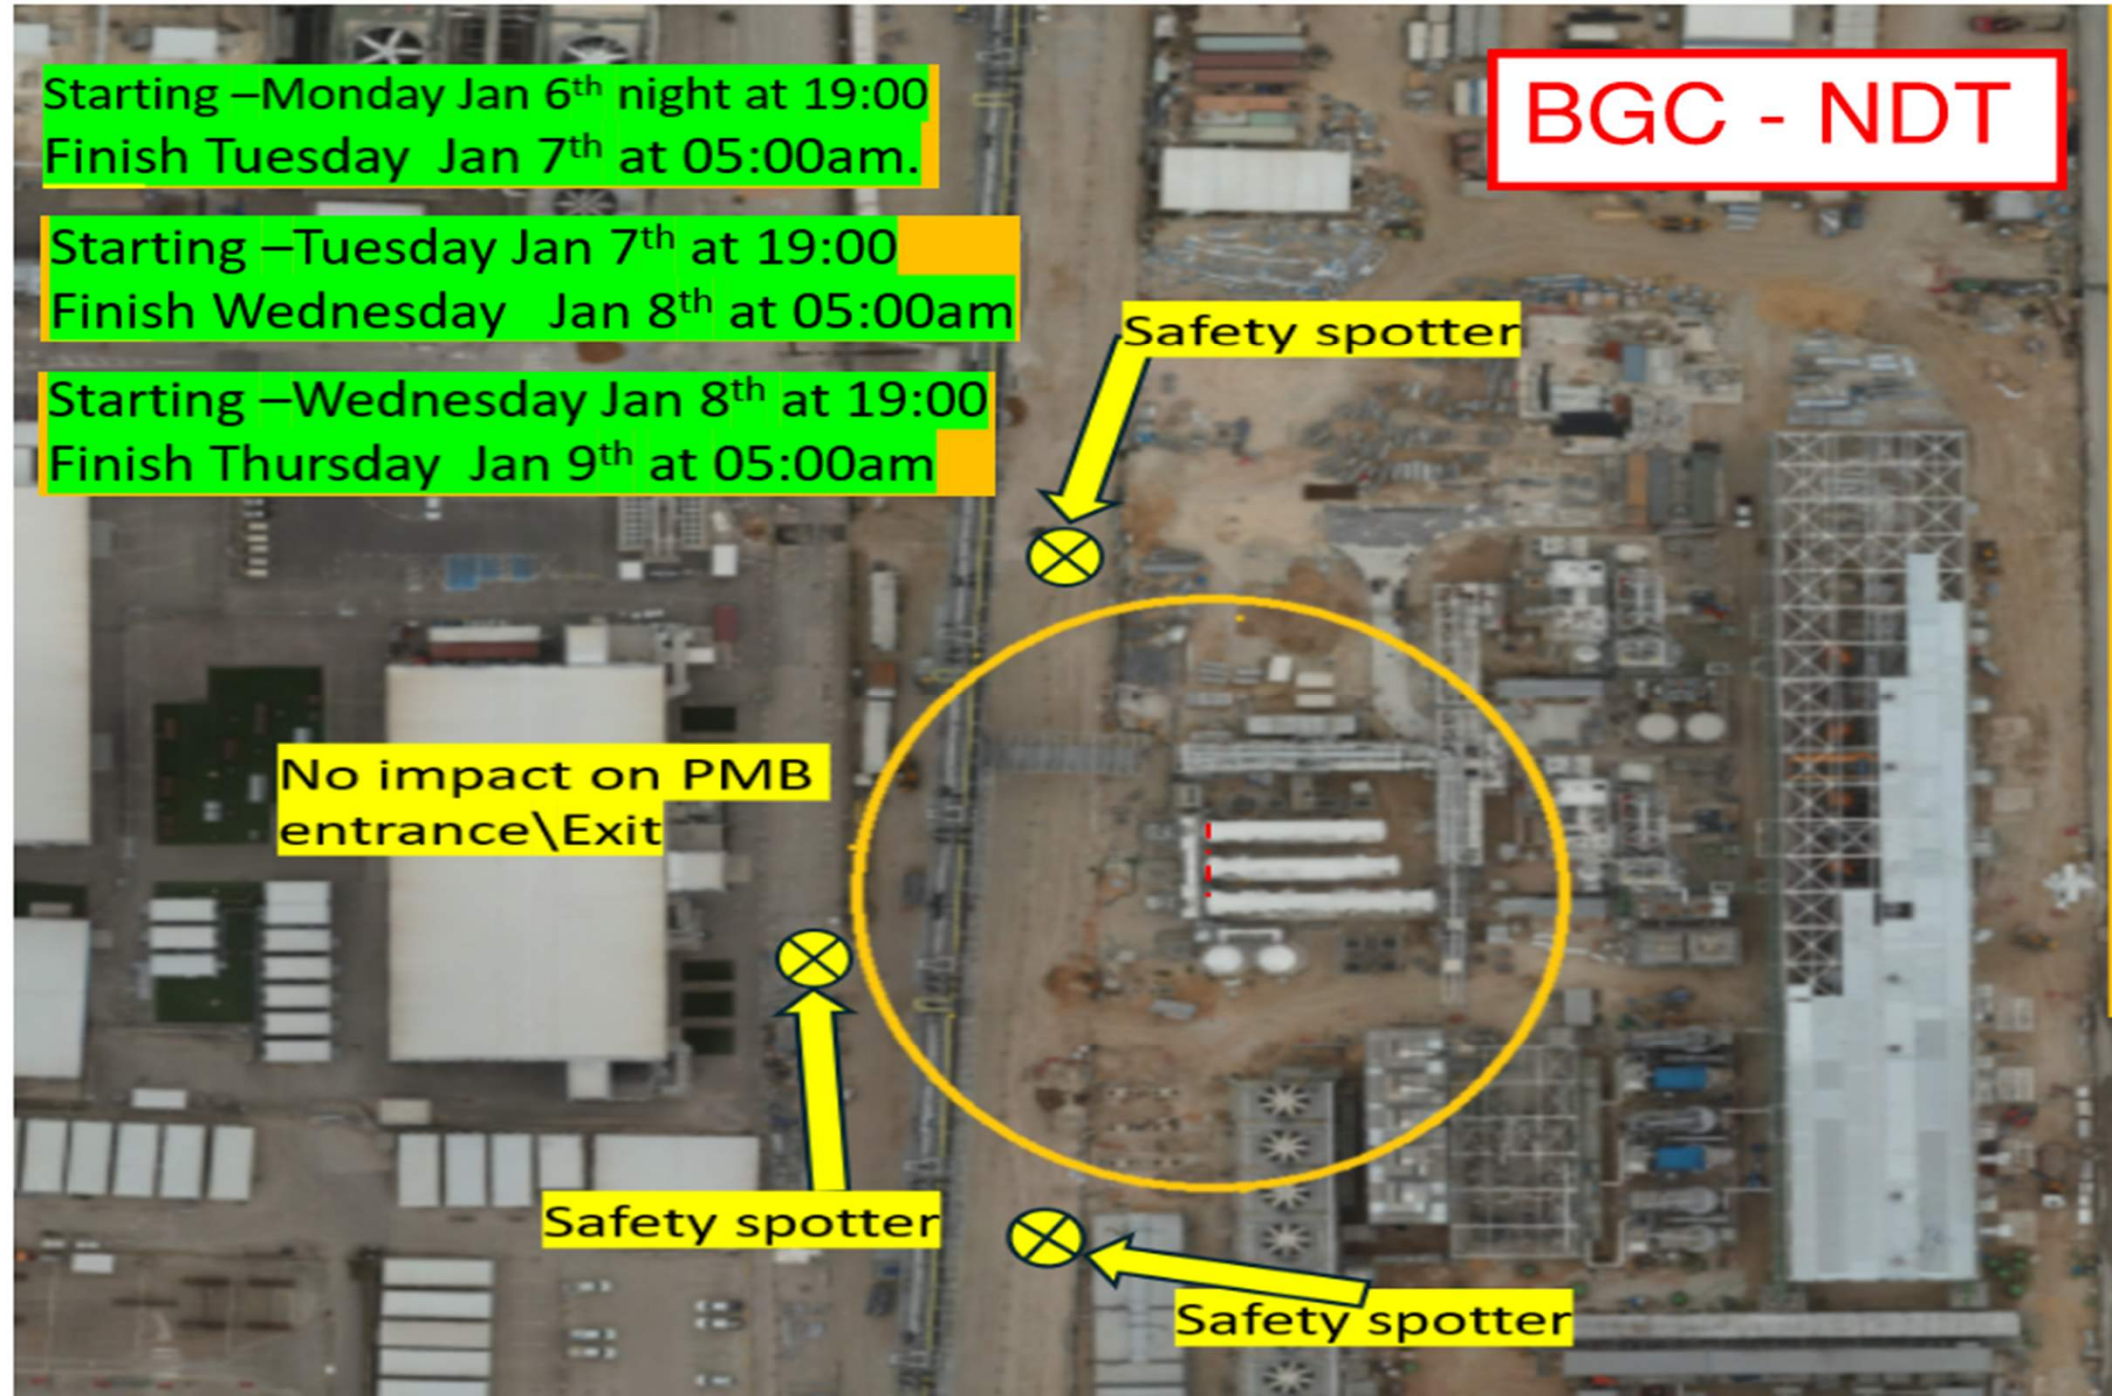

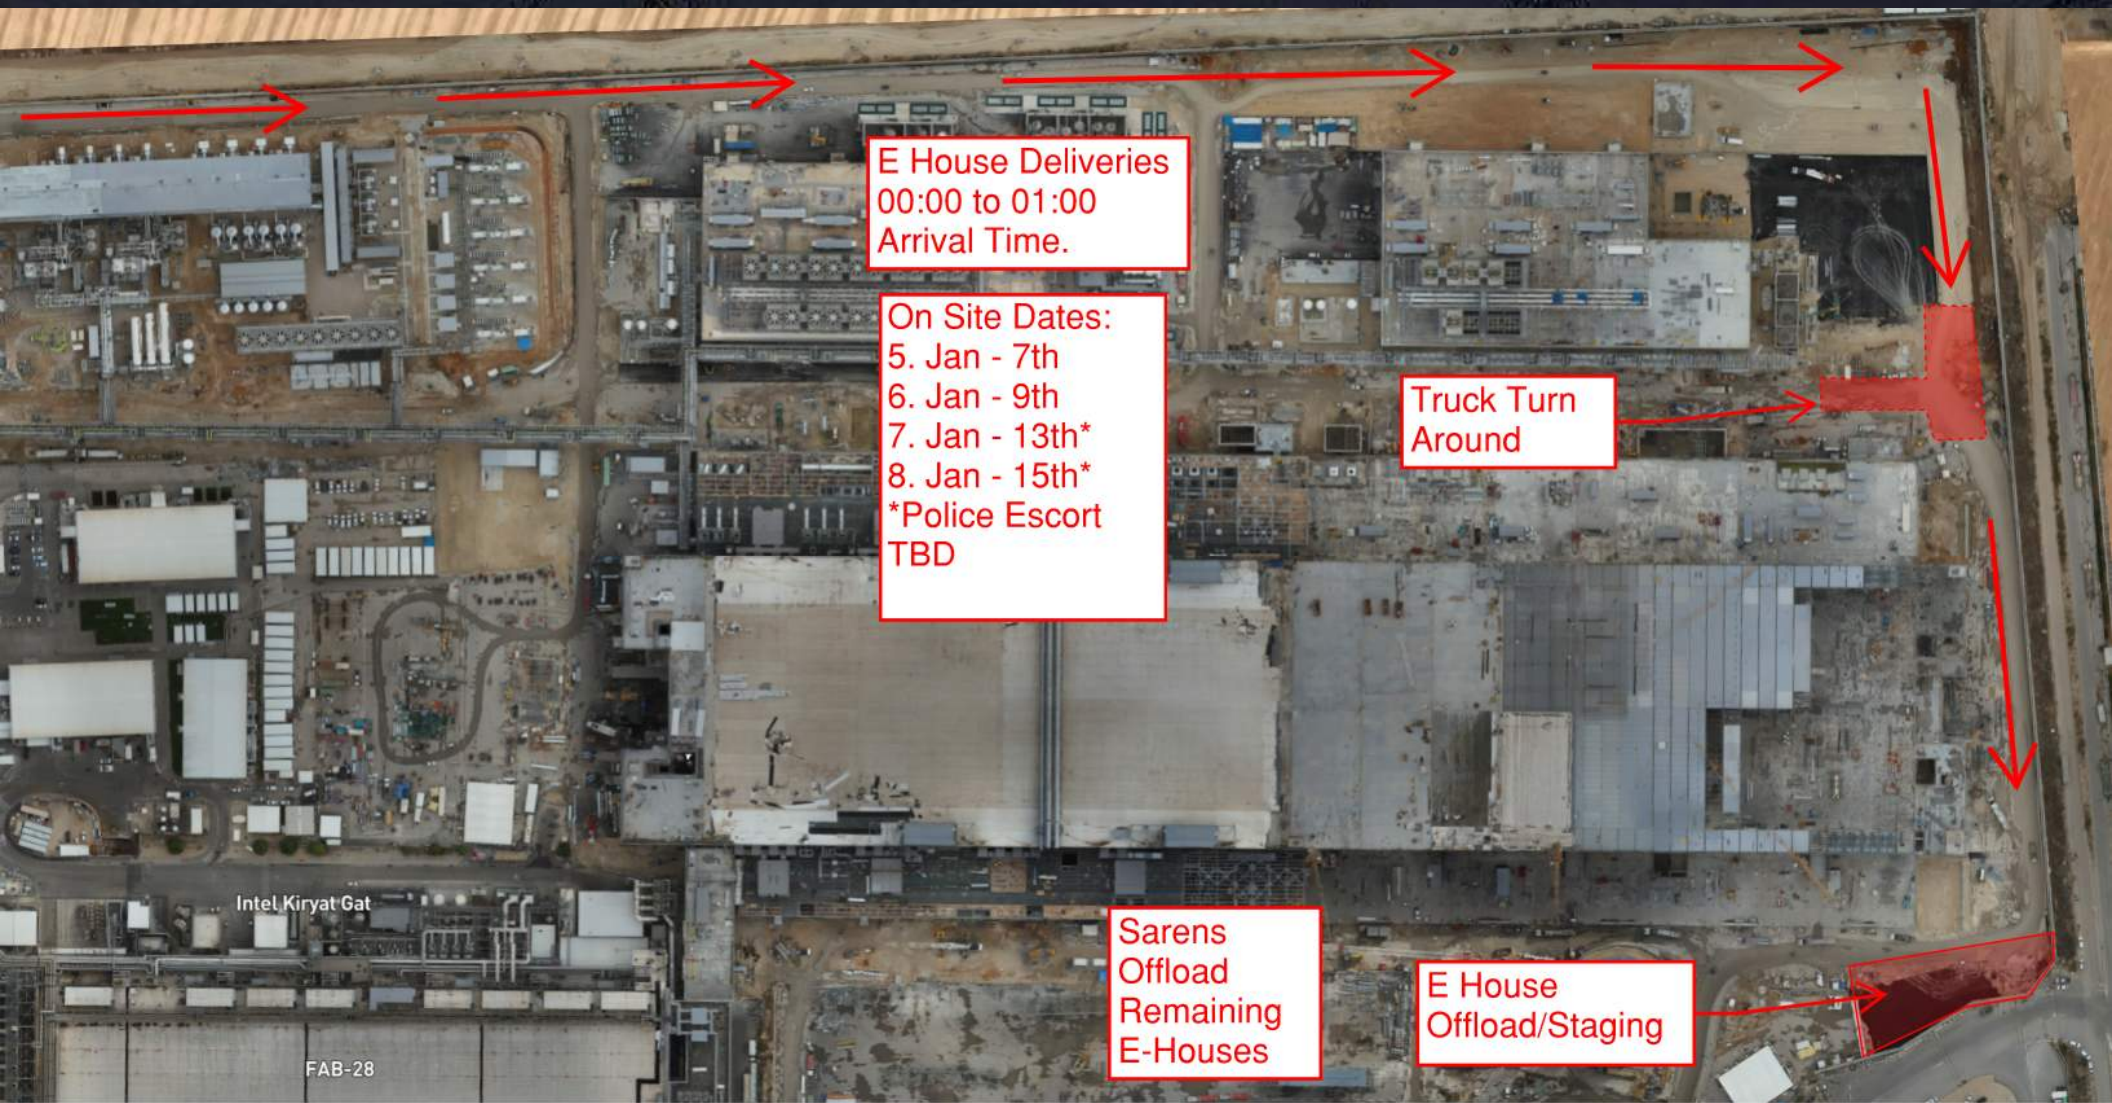

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:
5. Jan - 7th
6. Jan - 9th
7. Jan - 13th*
8. Jan - 15th*
*Police Escort
TBD


Truck Turn
Around

Sarens
Offload
Remaining
E-Houses

E House
Offload/Staging

Intel, Kiryat Gat

FAB-28

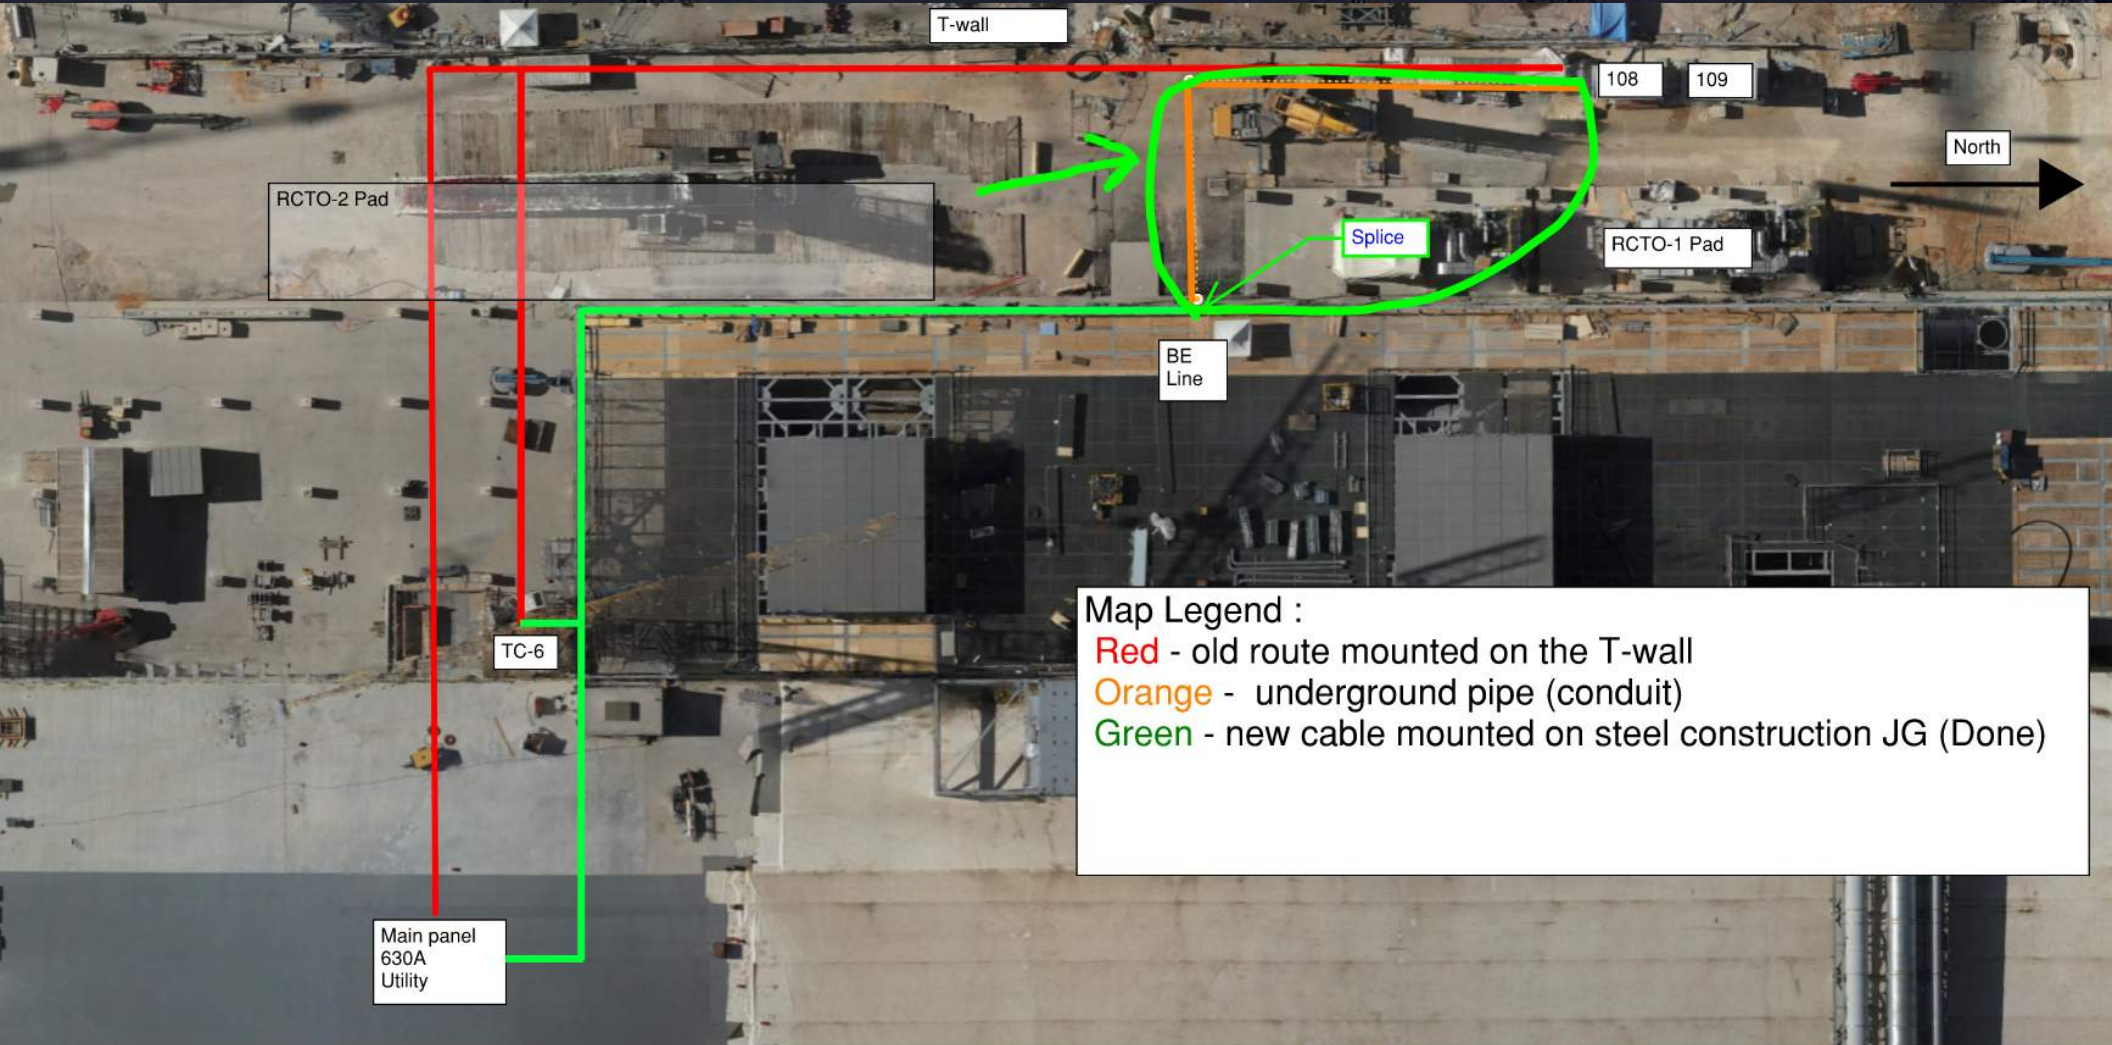


Map Legend :

- Red - old route mounted on the T-wall
- Orange - underground pipe (conduit)
- Green - new cable mounted on steel construction JG (Done)

Daily Coordination Meeting

Site Logistics
600 Car Park
Boring

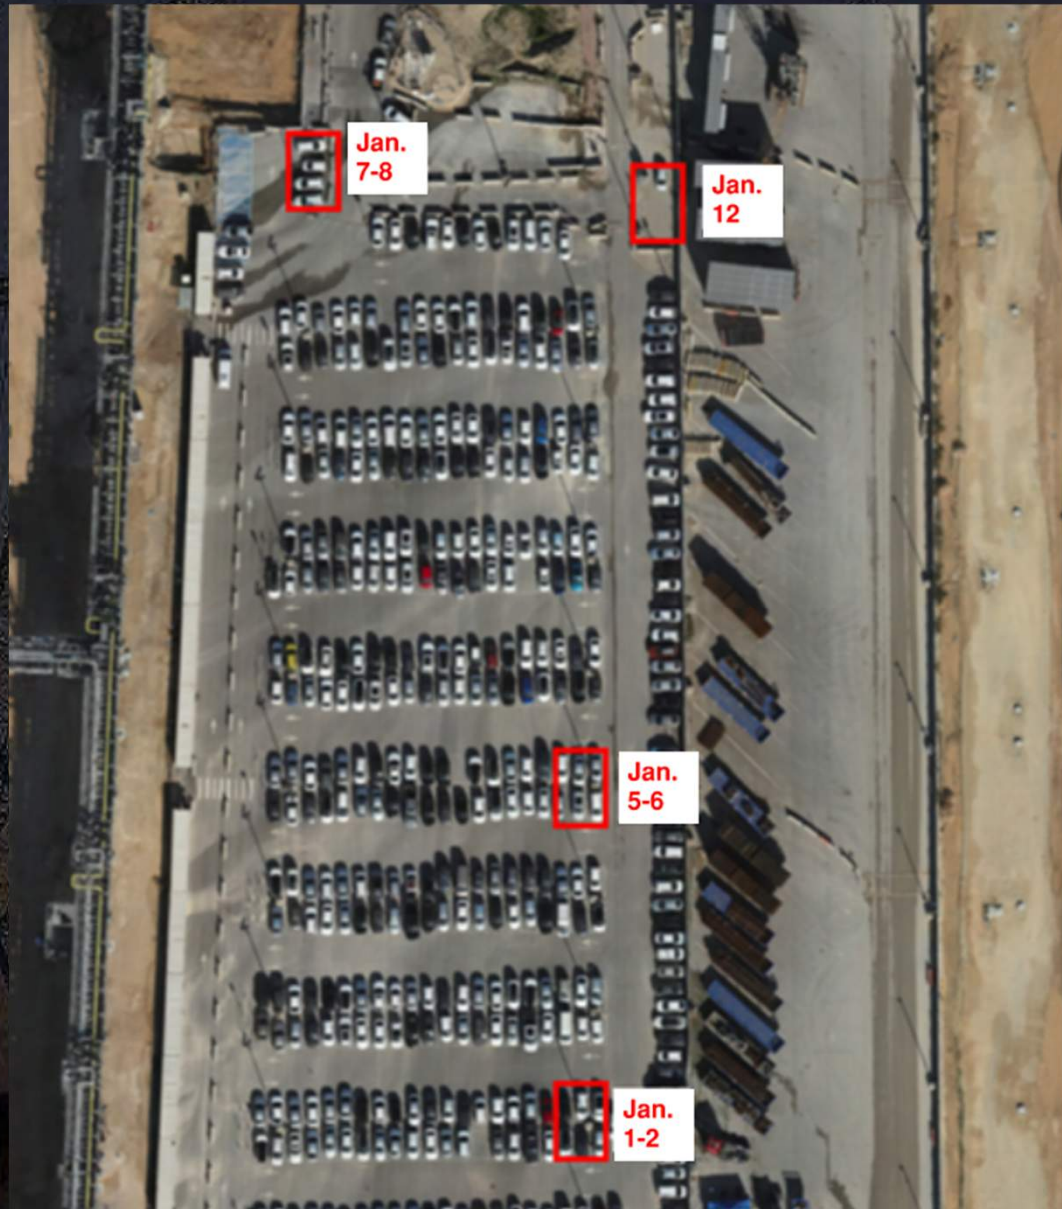

Daily Coordination Meeting

Site Logistics
North



Daily Coordination Meeting

Site Logistics
South



Reducing Stress

- Mental health is a huge part of our overall health and our safety.
- One of the most common mental health challenges people face is managing stress.
- A good strategy for managing stress, is to reduce it when possible. There are hundreds of techniques for this and different strategies work for different people.
- Next Monday, we would like to present one strategy in reducing stress, and that is through learning how to communicate differently to reduce stress from miscommunications and misunderstandings.



THE POWER OF WORDS:

REDUCING STRESS THROUGH CLEAR COMMUNICATION

Workshop by Lisa Rabinowitz

HOW WE COMMUNICATE CAN EITHER CREATE OR REDUCE STRESS IN OUR LIVES

We all experience stress. But what if there were ways that you were communicating that were creating more stress for you, or the people that you interact with regularly? Join us in this workshop exploring how we can reduce the stress in our lives with the power of words.

The workshop will be held Monday January 13th in Kadima BUM from 10:30-12:00.

Please sign up to receive the meeting invite.



JANUARY 13TH
10:30 - 12:00



KADIMA
BUM

PLEASE SIGN UP HERE TO
RECEIVE THE CALENDAR INVITE

HCC/EHS Weekend Work- 03.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Shelby Standefer 052-3440752

Yakov Malka 052-3459250

Yakov Alon 052-4671271

CSA CM

Charlie Aitken 052-6041443

Ilyssa Ingenthron 052-5732553

MEP

David Chavez 052-2756390

Denis Ryan 052-2962447

Pauric O'Reilly 052-3571665

Lara Salaymeh 052-2410953

Abhilash Parameswaran 052-6938827

Cranes

Craig Mowry 052-300-2769

Safety

Safety Foreman- Mohammad Zakakti- 054-8121212 Mohammad-Zakakti@Hoffmancorp.com

Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com

Safety Professional- Nassim Yones- [052-2208434](tel:052-2208434) Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 03.01.2025

FAB

Utility Level / Roof / Stair Shaft

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Megason

Subfab

Pach Taas

BAe Wall Penetration

Itamar 0509301917

Afcon E

MARSes, E LSS Rooms

Avi Eli: 0526008487

Chemo

TTNW

Tomi: 0523759408

SELA

AY-BC 15-19

Avihen 0548155302

MEGASON

LSS Rooms

Israel 0526869393

Clean Room

Talad – CR 2 E – UPN Install, 4E Grating (EHS Marcelo 0523540242, Super Igor 0544509386)

Sig – 10 GUYS 5W INT 4W, 3E Handrails (EHS Beni 0506232032, Super Shmulik 0549205966)

Afcon – CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Rolling Plains – 20 guys INT NWTT 5RA, Marshaft 4W, 5RA, MOD2 CA CH 17,24,10 (Super oleg +353873794553 , 0542689370 , EHS MARCOV 0546596857)

Chemo –30 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)

Megason - 16 GUYS INT LEVEL + 7 GUYS ON UTILITY LEVEL FOREMAN ISRAEL BITON 0526869393 EHS GUY ISHBIT

Sela – 2E CRC (Supervisor yoav 0548076339 , EHS SERGEY 0526650046)

Protocol - aa+ak lines.

Talent solution 1w_+ 1e + interstitial.

Subcontractor Weekend Work- 03.01.2025

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2 1-3P

Foreman – Itamar – 050-9301917

Safety – Offek – 050-2161429

Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2

Foreman – Pradeep - 055-2742935

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-5P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcelo – 054-5210133

Safety – Majdi – 054-6192581

WJG

Afcon – Lift 2 and Utility Level Cable Tray

Foreman: Montu 055 911 6973

Safety: Pradeep 055 274 2935

Chemo: 4J/5J Lift 2 Piping & Link Roof

Foreman: Maor 050 988 9071

Safety: Erez 054 971 6840

Pach Taas: All over

Foreman: Tomer 050 767 0585

Safety: Jad 050 5405016

Subcontractor Weekend Work- 03.01.2025

CUB

S.K.E - CUB 1:

Renato - 0548991623

Marzuk - 0548830263

Chemo Aharon - CUB 1:

Dudu - 0509808846

Leonid - 0548883878

D&P - CUB 2:

Constantino - 0545501602

David - 0548894447

Sami Najami - CUB 1 test + CUB 2:

Husein - 0526917461

Faiz - 0502227962

Alon - 0509895008

HSAl:

Sergey - 0552728807

Trestle

Siding

Sami Najami

Forman- Abed Kilani 054-5501880

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Elmor – Site Lighting Underground

Supervision = Shlomi: 050-9182260

EHS = Daniel: 052-2584171

Olizki – Offload 18 & CUB1 trench drains, South GUT road excavation

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

Daily Coordination Meeting



14:00 Sign In
