

# Daily Coordination Meeting




# Daily Coordination Meeting

## General Topics:

- **Work To Be Done**
- **MEWP's to be removed; Gate B; coordinate relo with EHS.**
- **Hot weather, Be prepared.**




UTILITY LEVEL MOD1

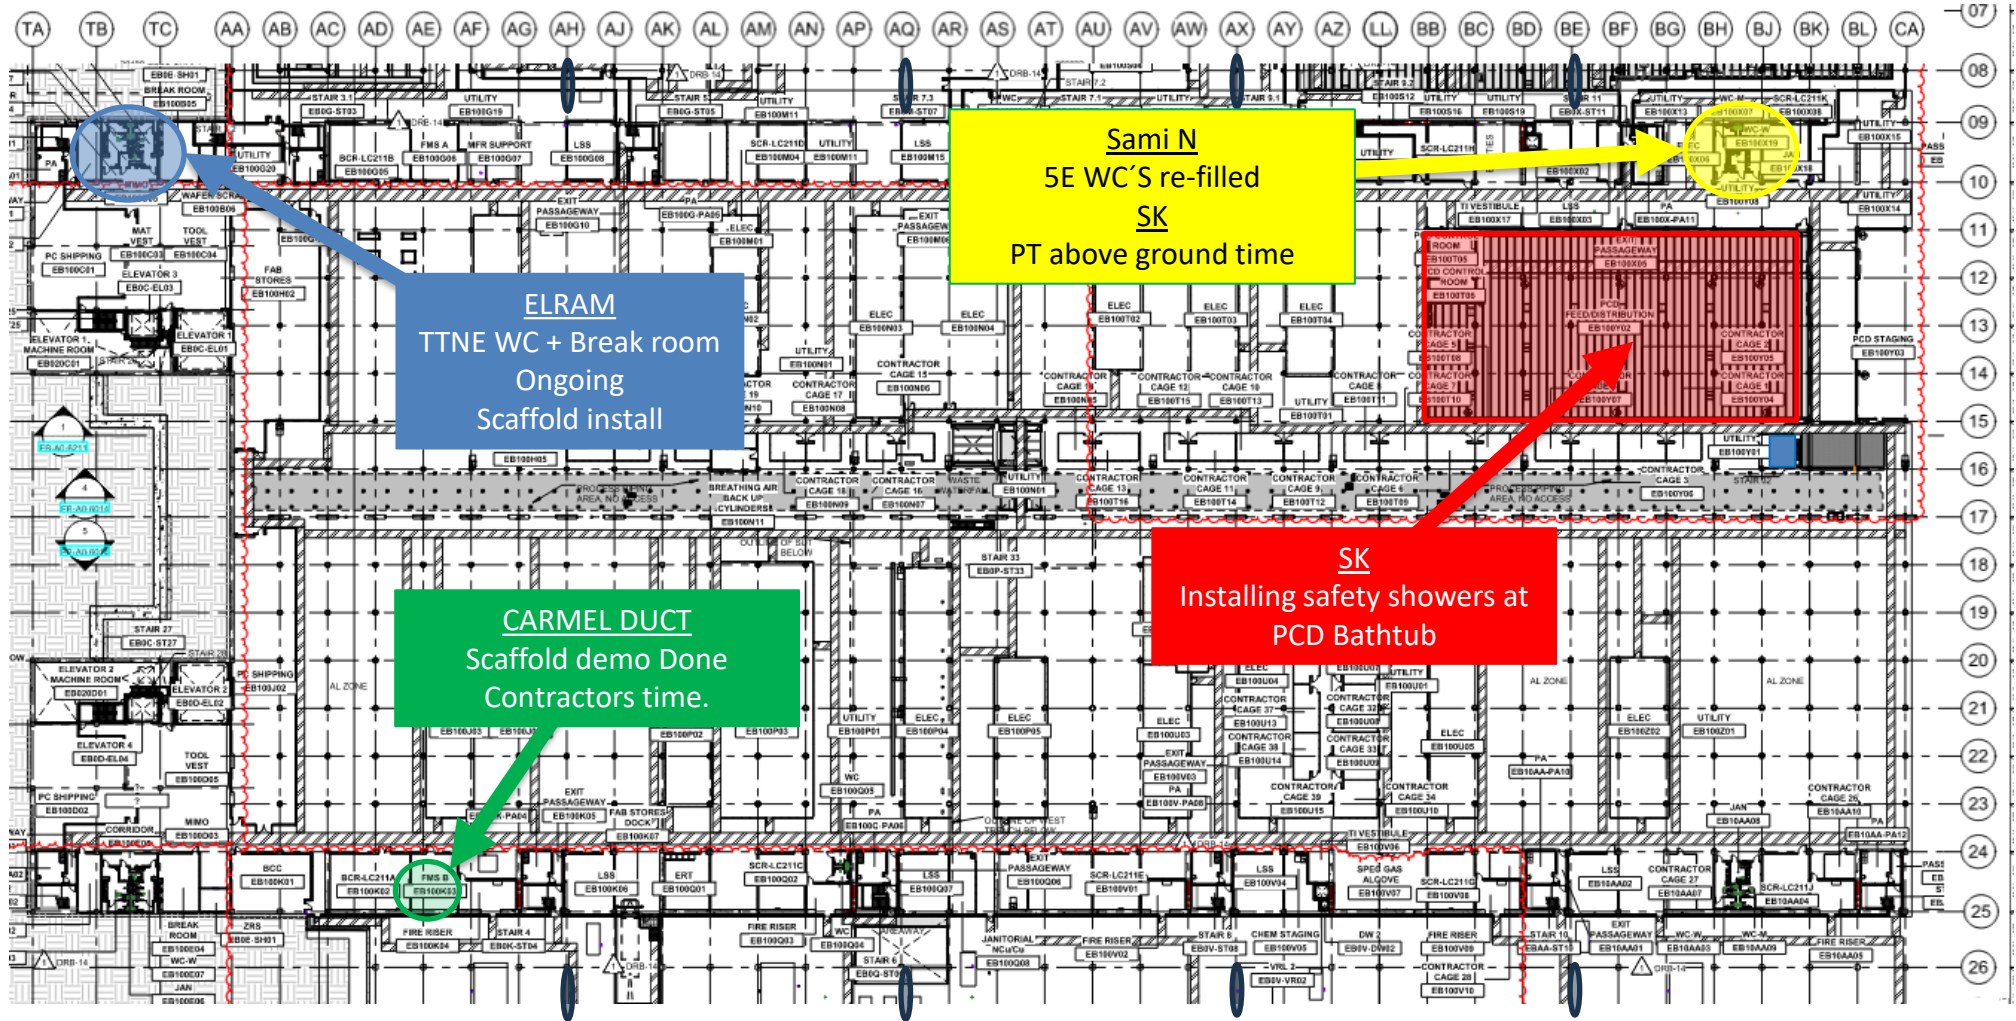



# SUT 38.1 LEVEL

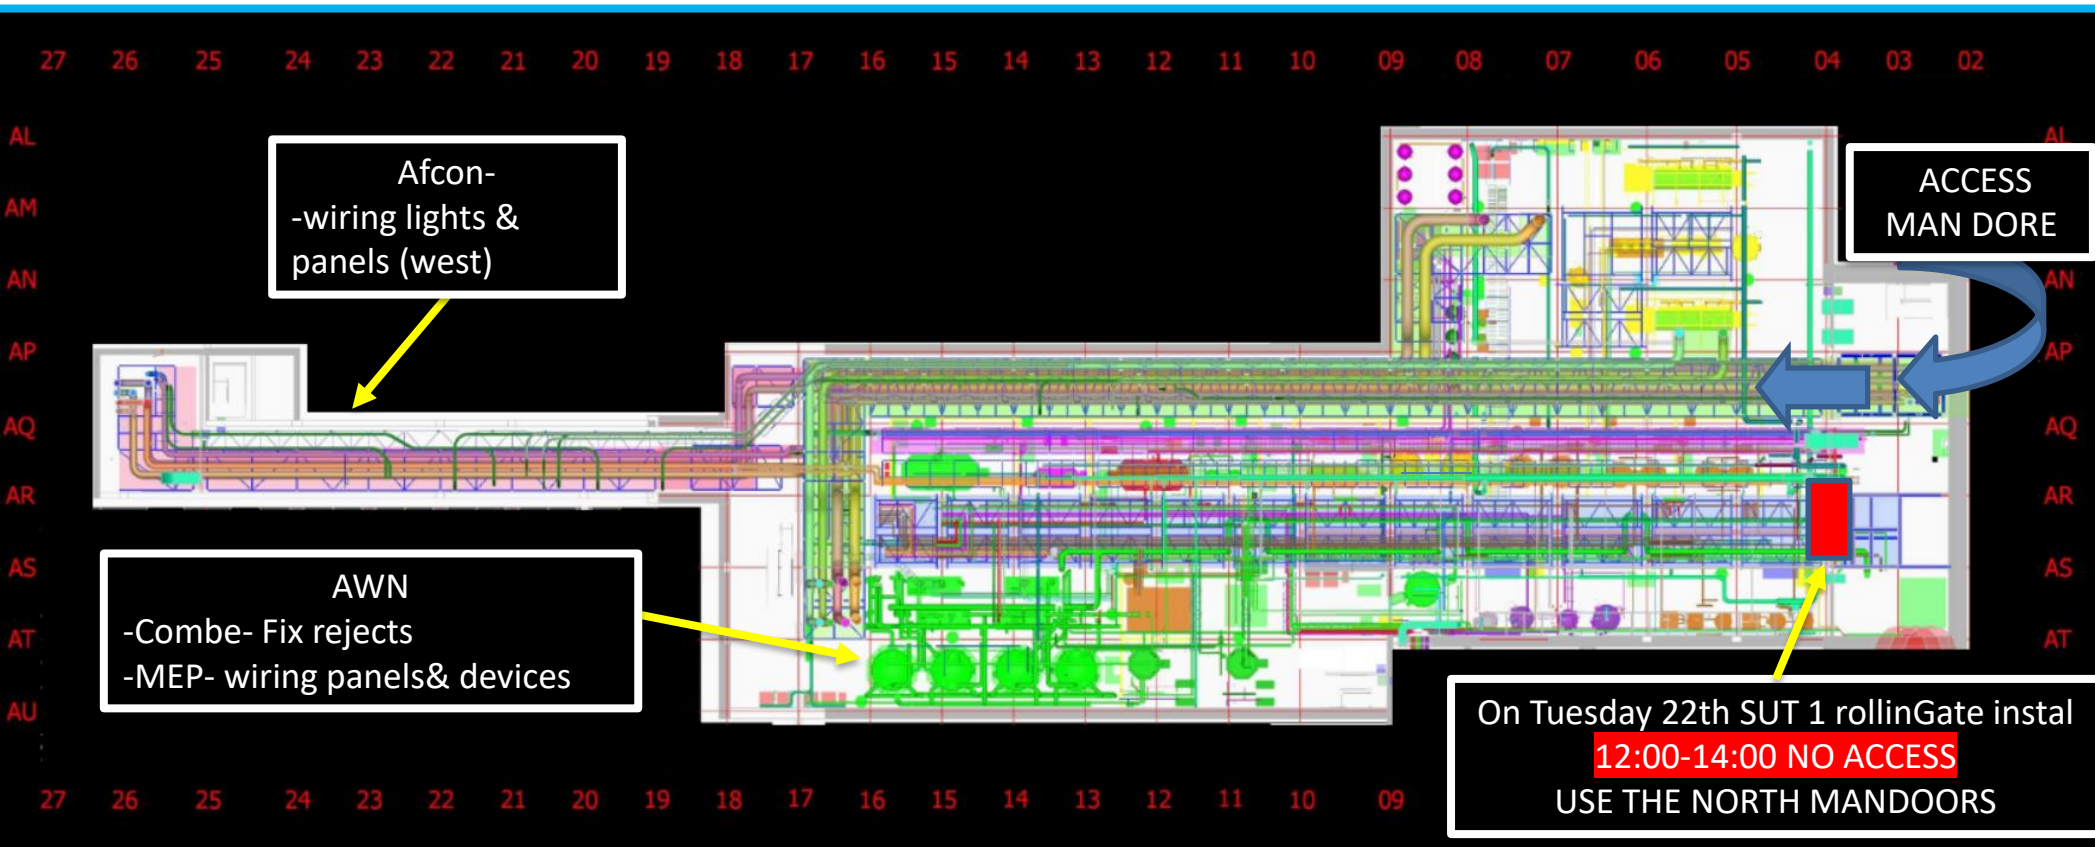



**Evacuate materials not enough !!!  
On Wednesday 23 th  
Job service cleanup& evacuate  
unapproved materials to the dumpster**






**Evacuate materials not enough !!!  
On Wednesday 23 th  
Job service cleanup& evacuate  
unapproved materials to the dumpster**





# SUBFAB BUILDOUT MOD 1

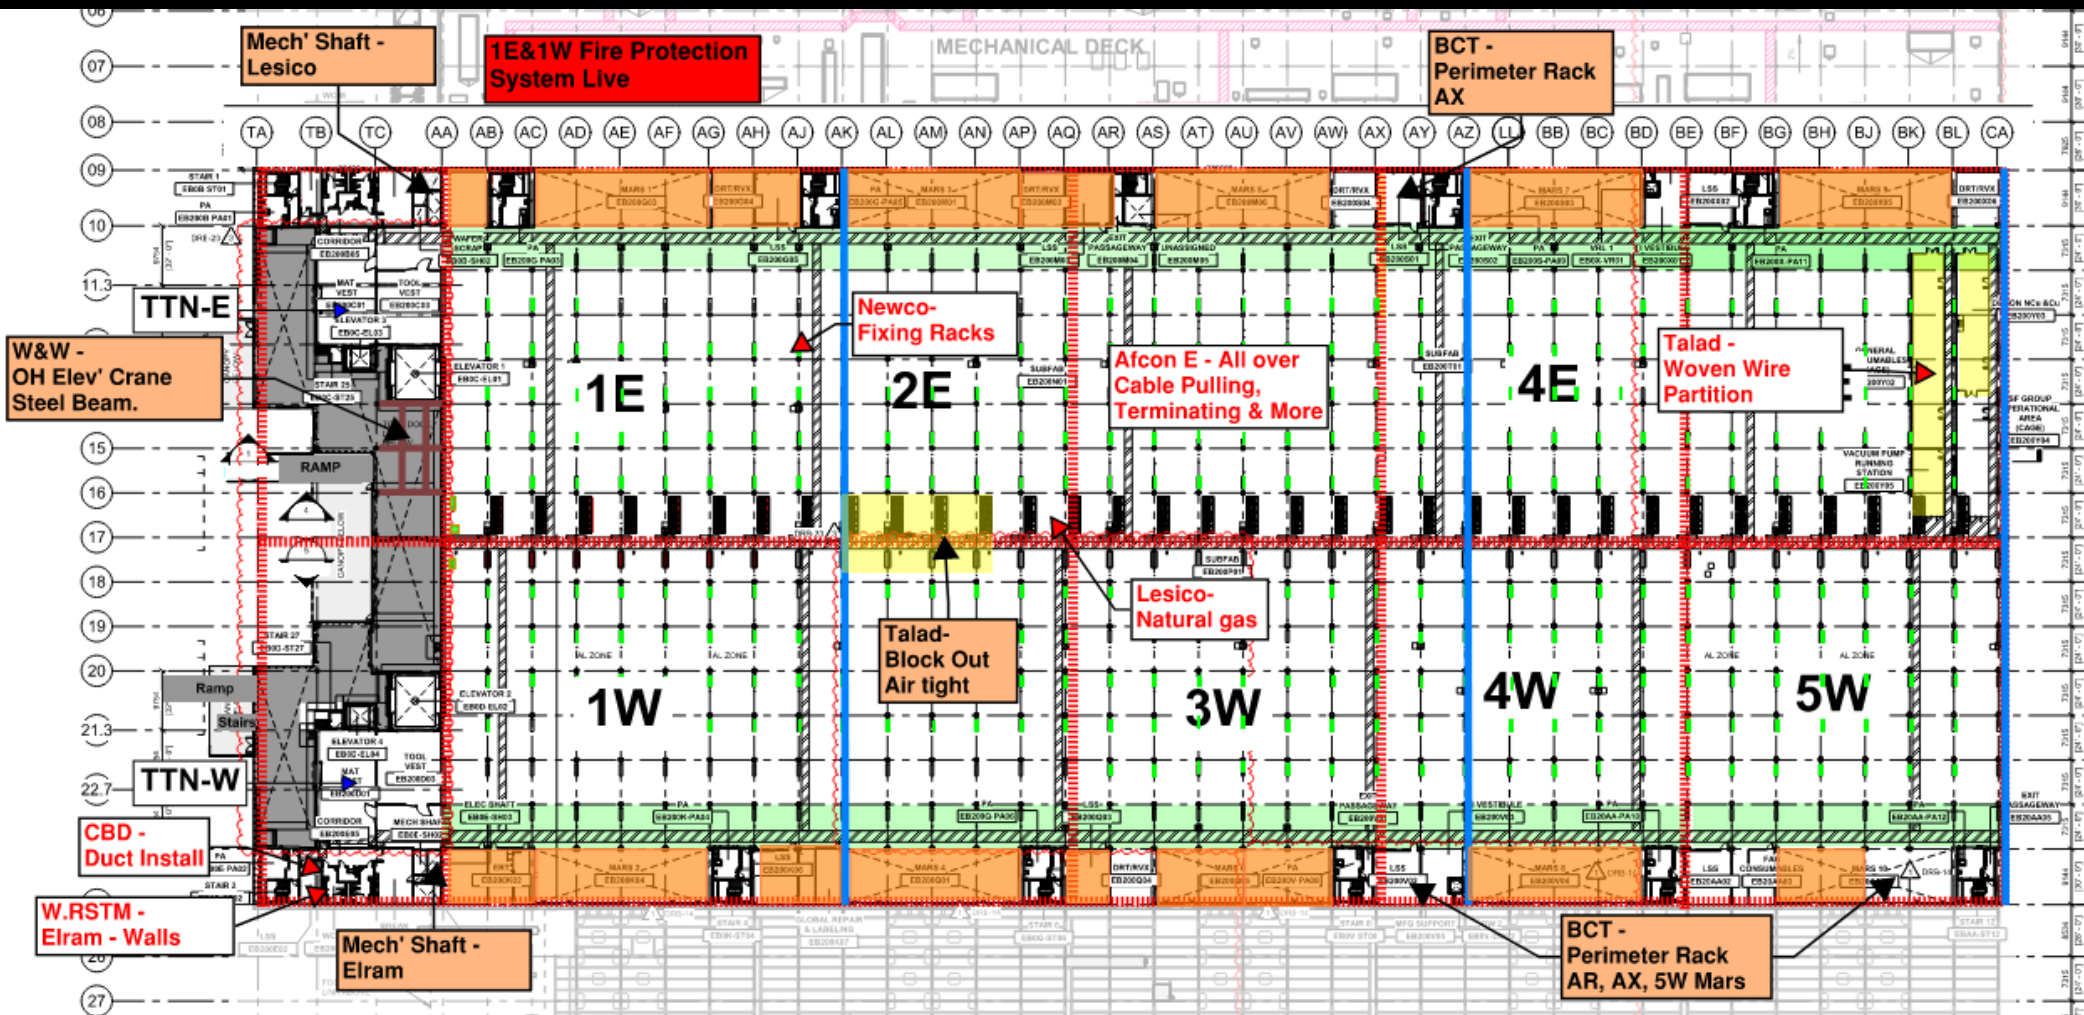



## SUBFAB BUILDOUT MOD 2

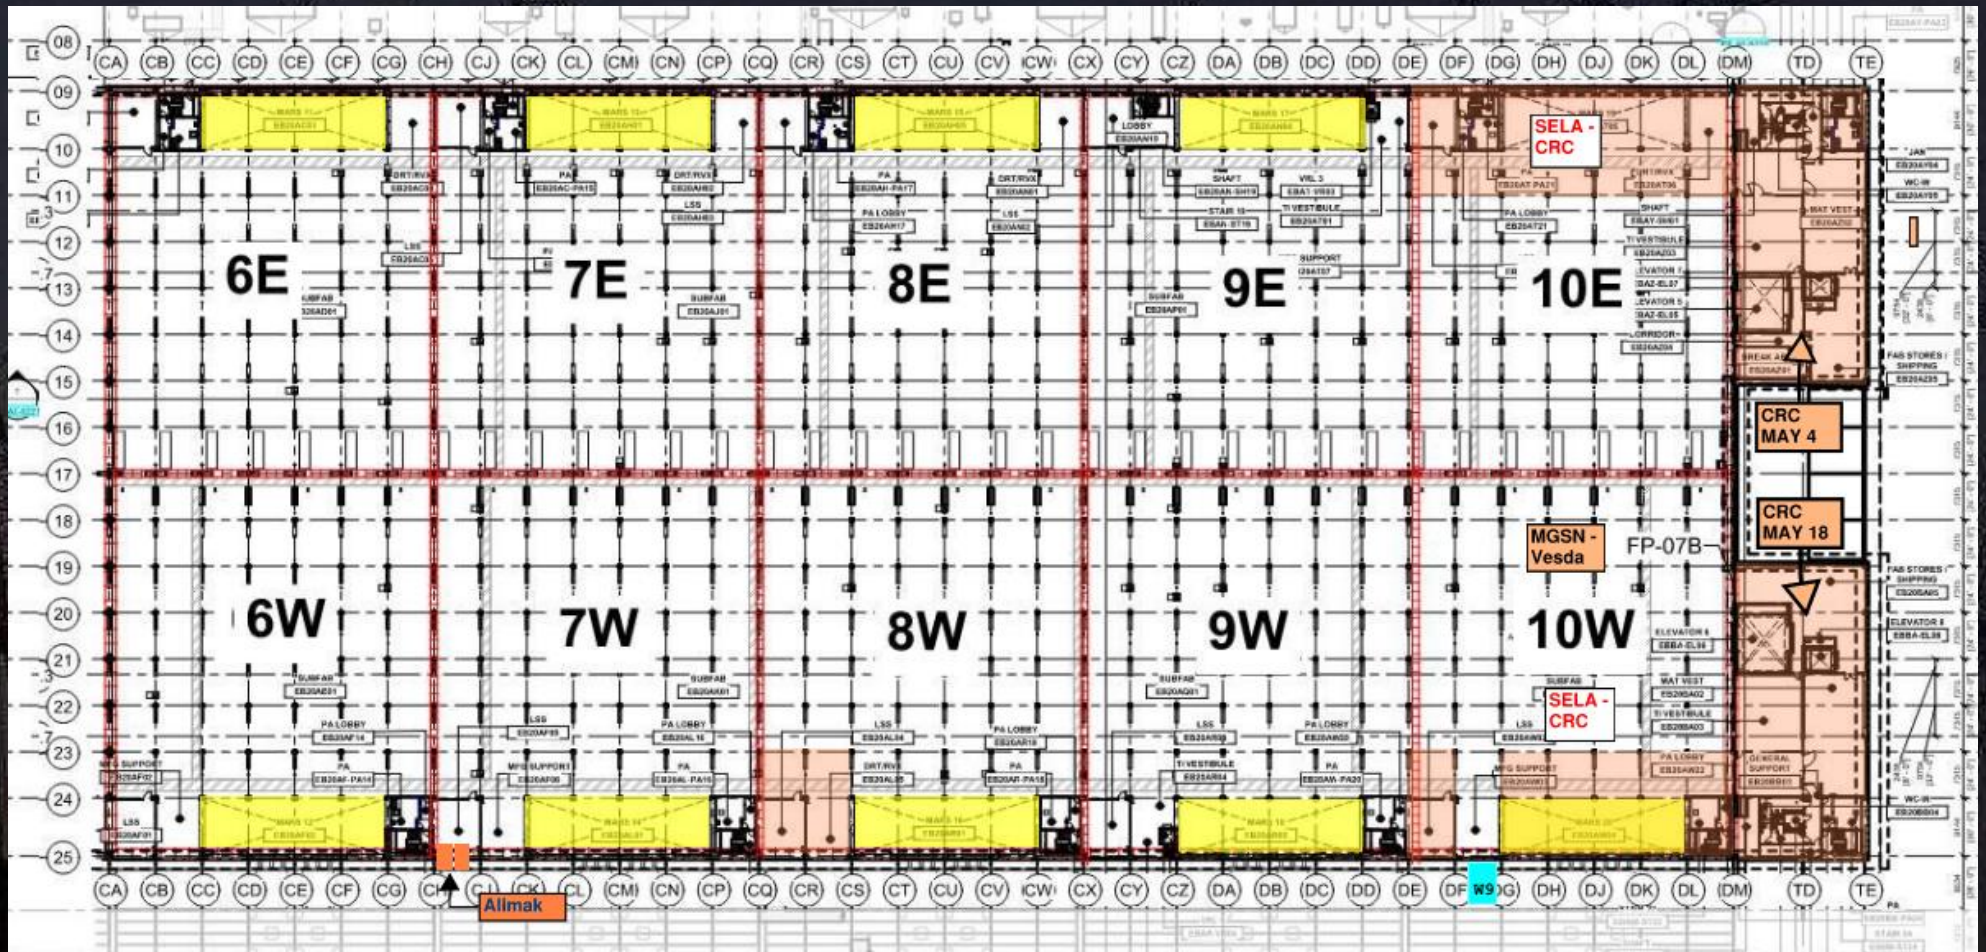

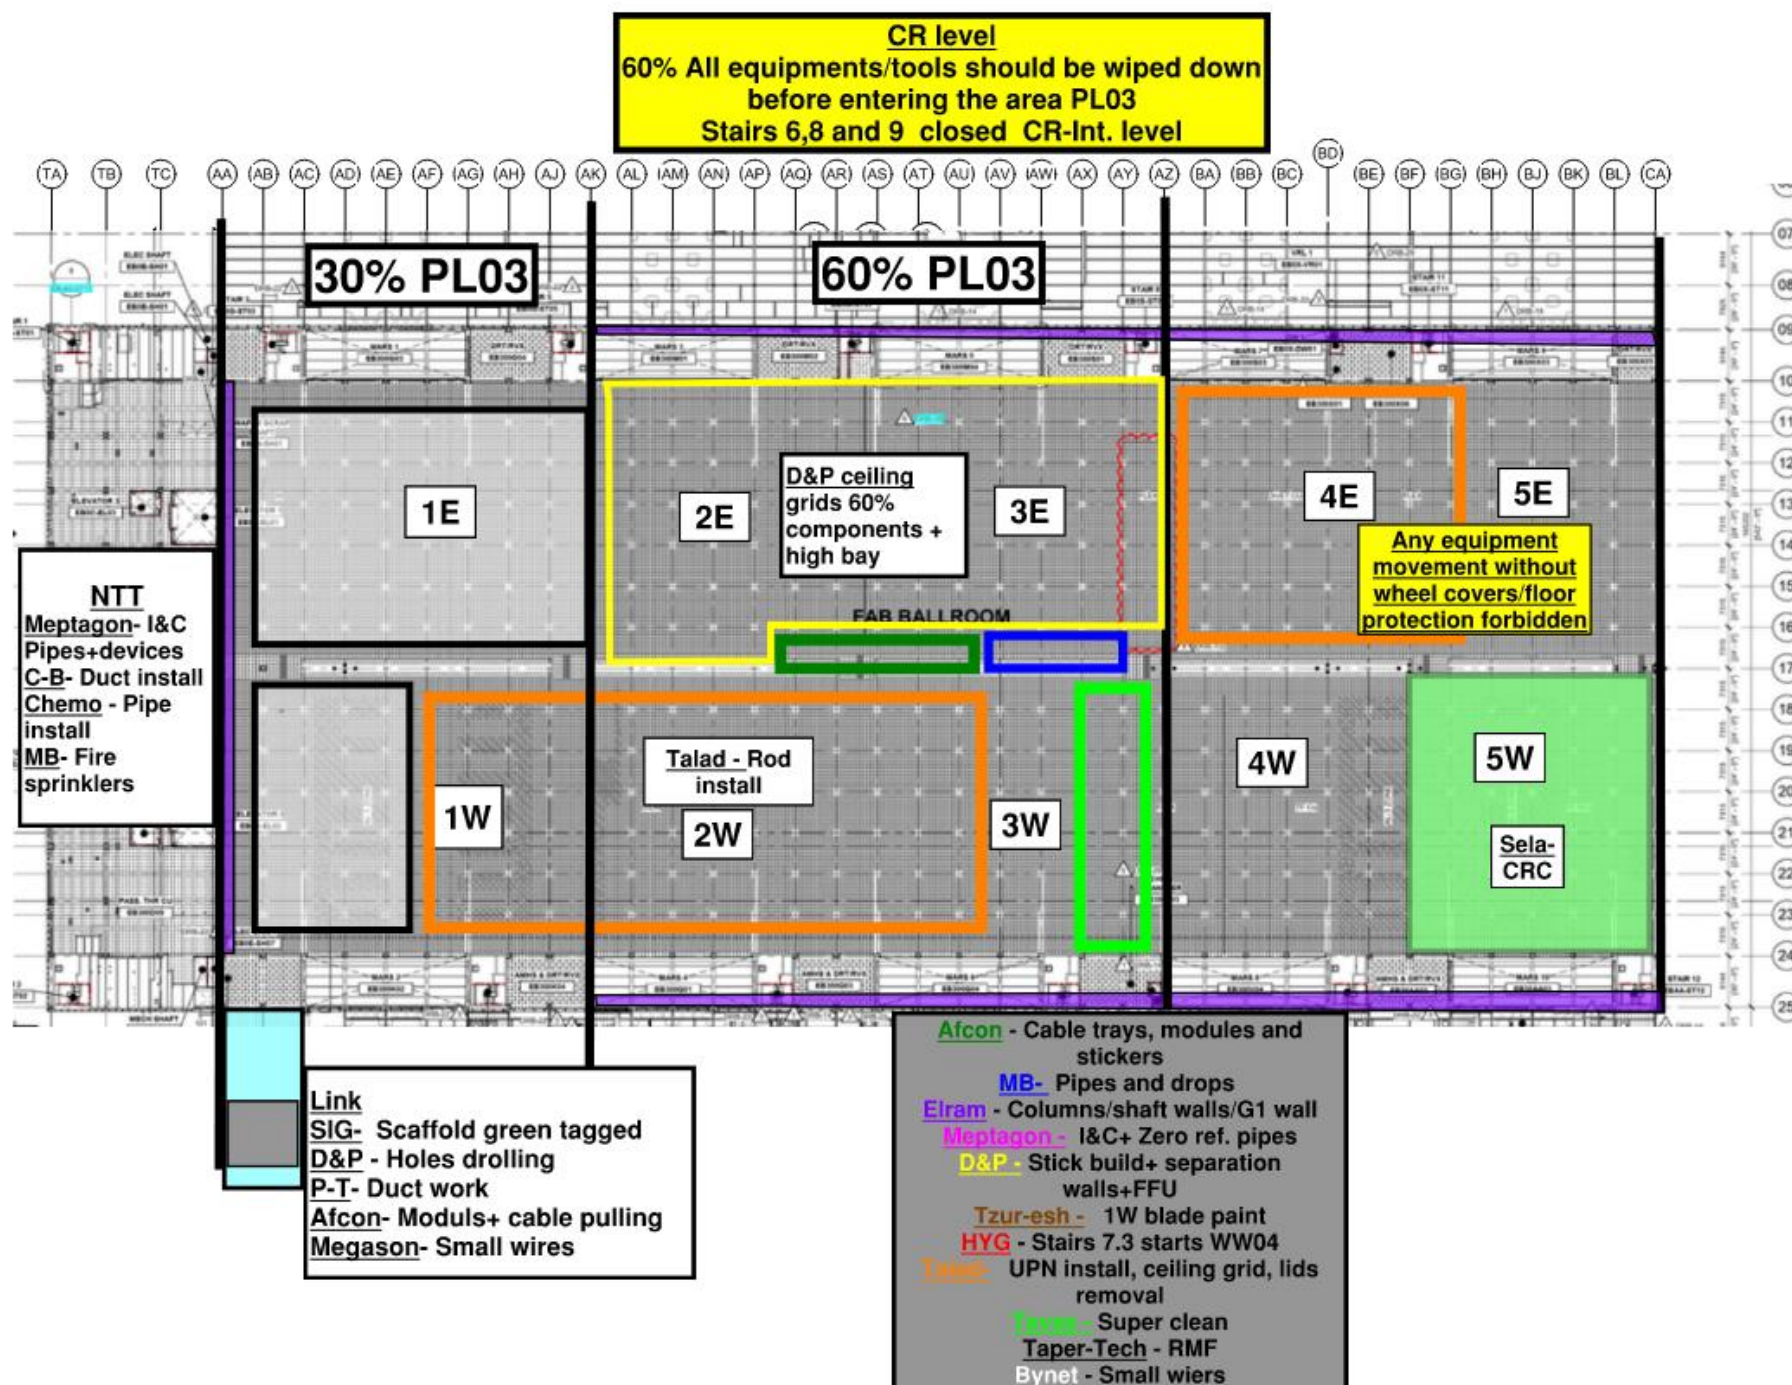




**Meptagon- I&C**



**Do not move carts/ stage material without plywood**




30%


60%

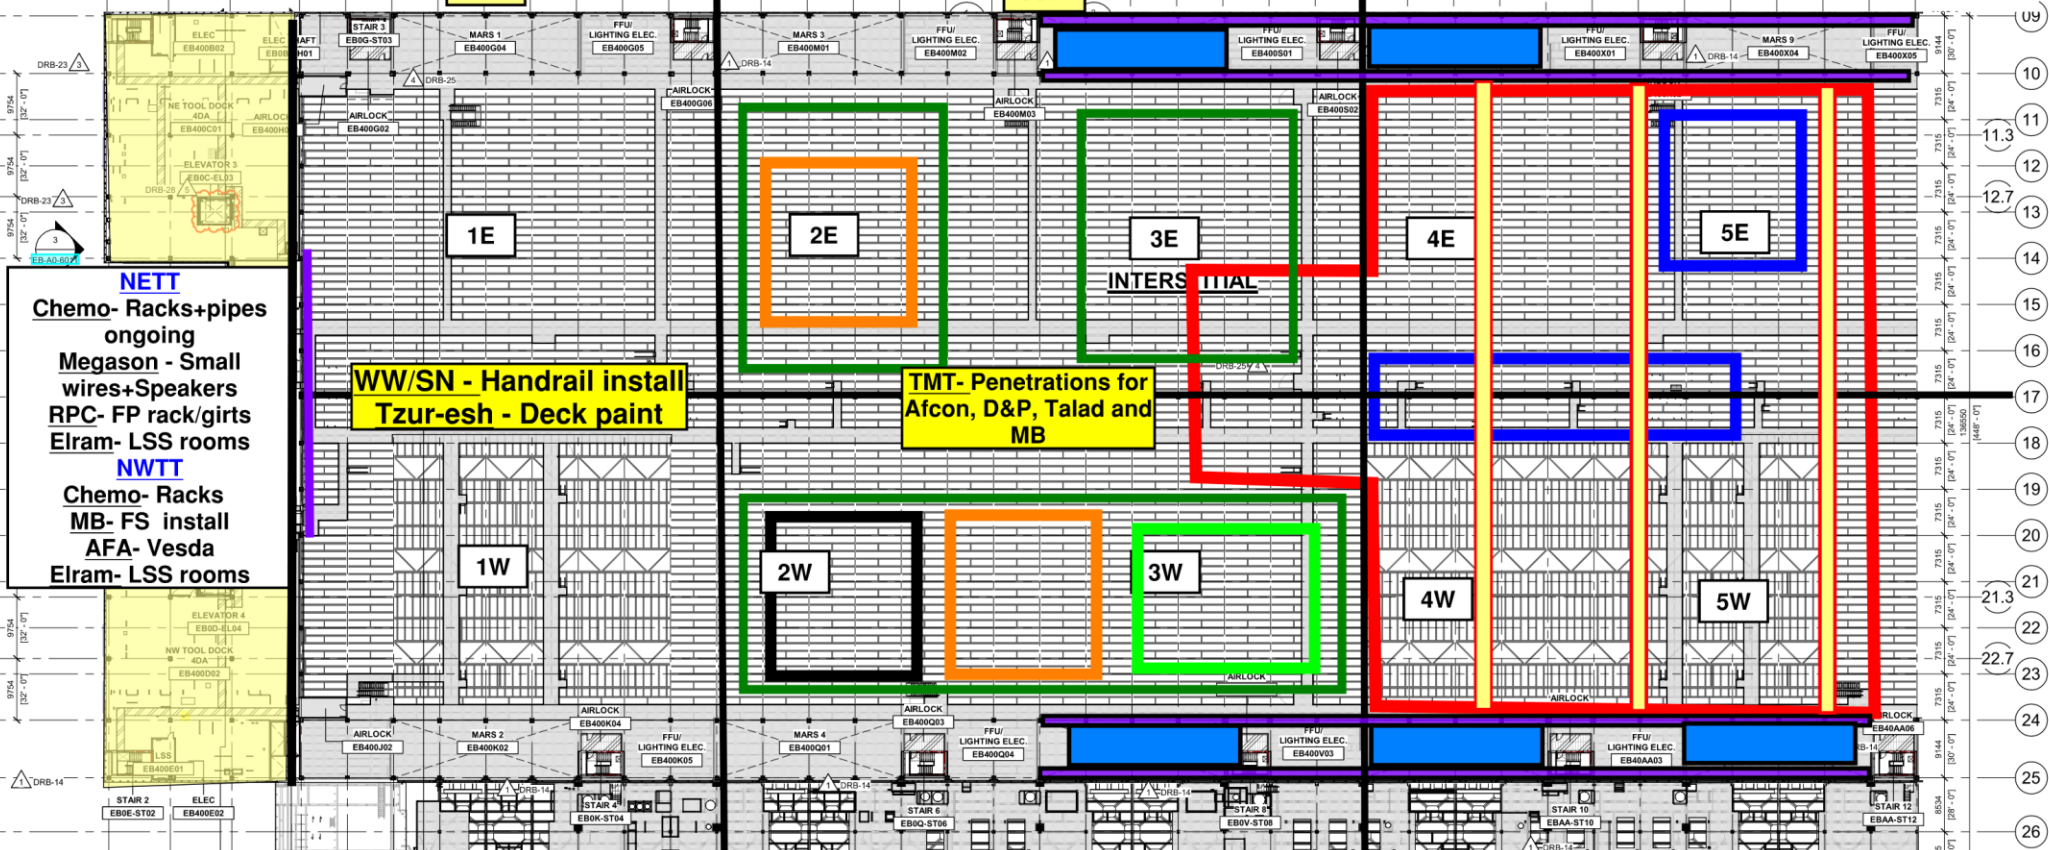

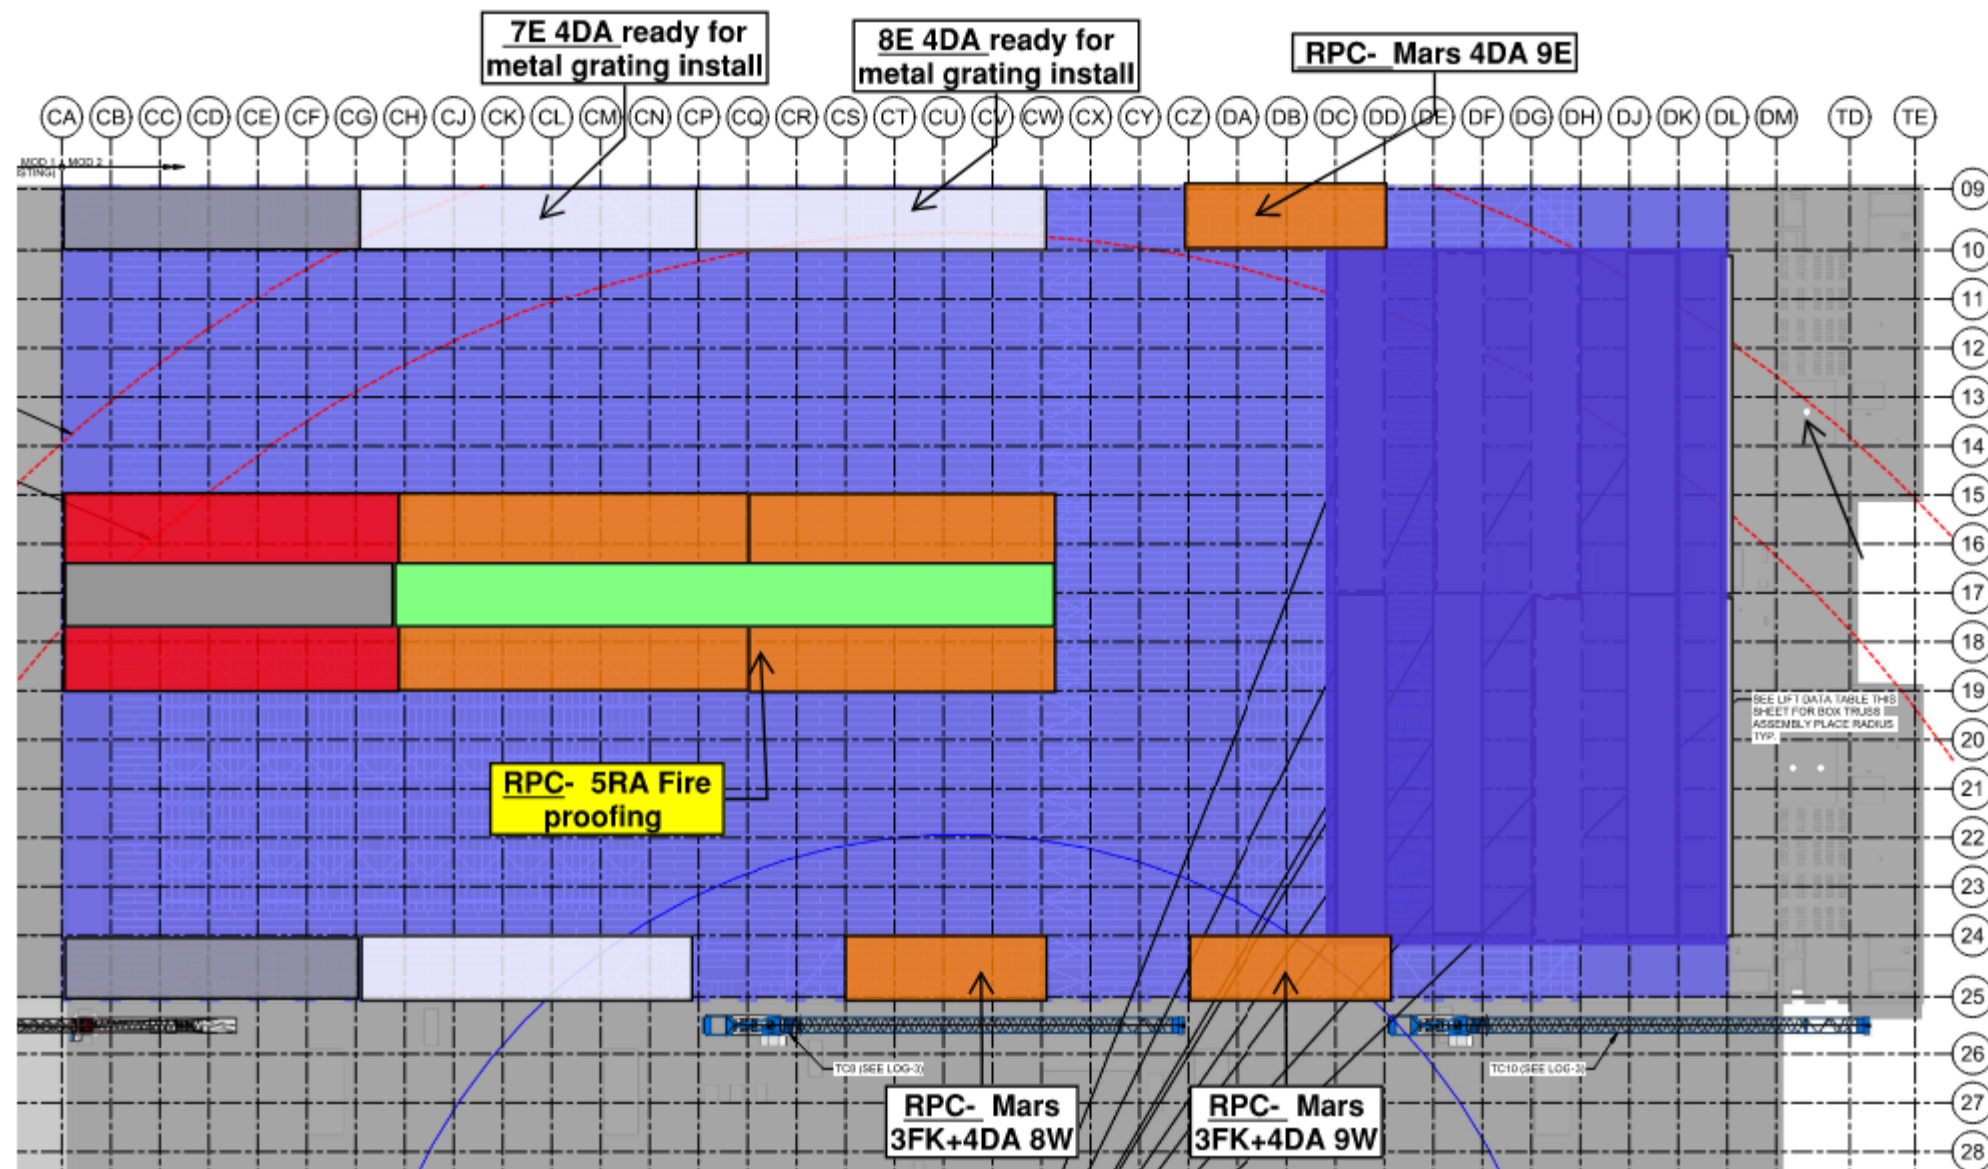


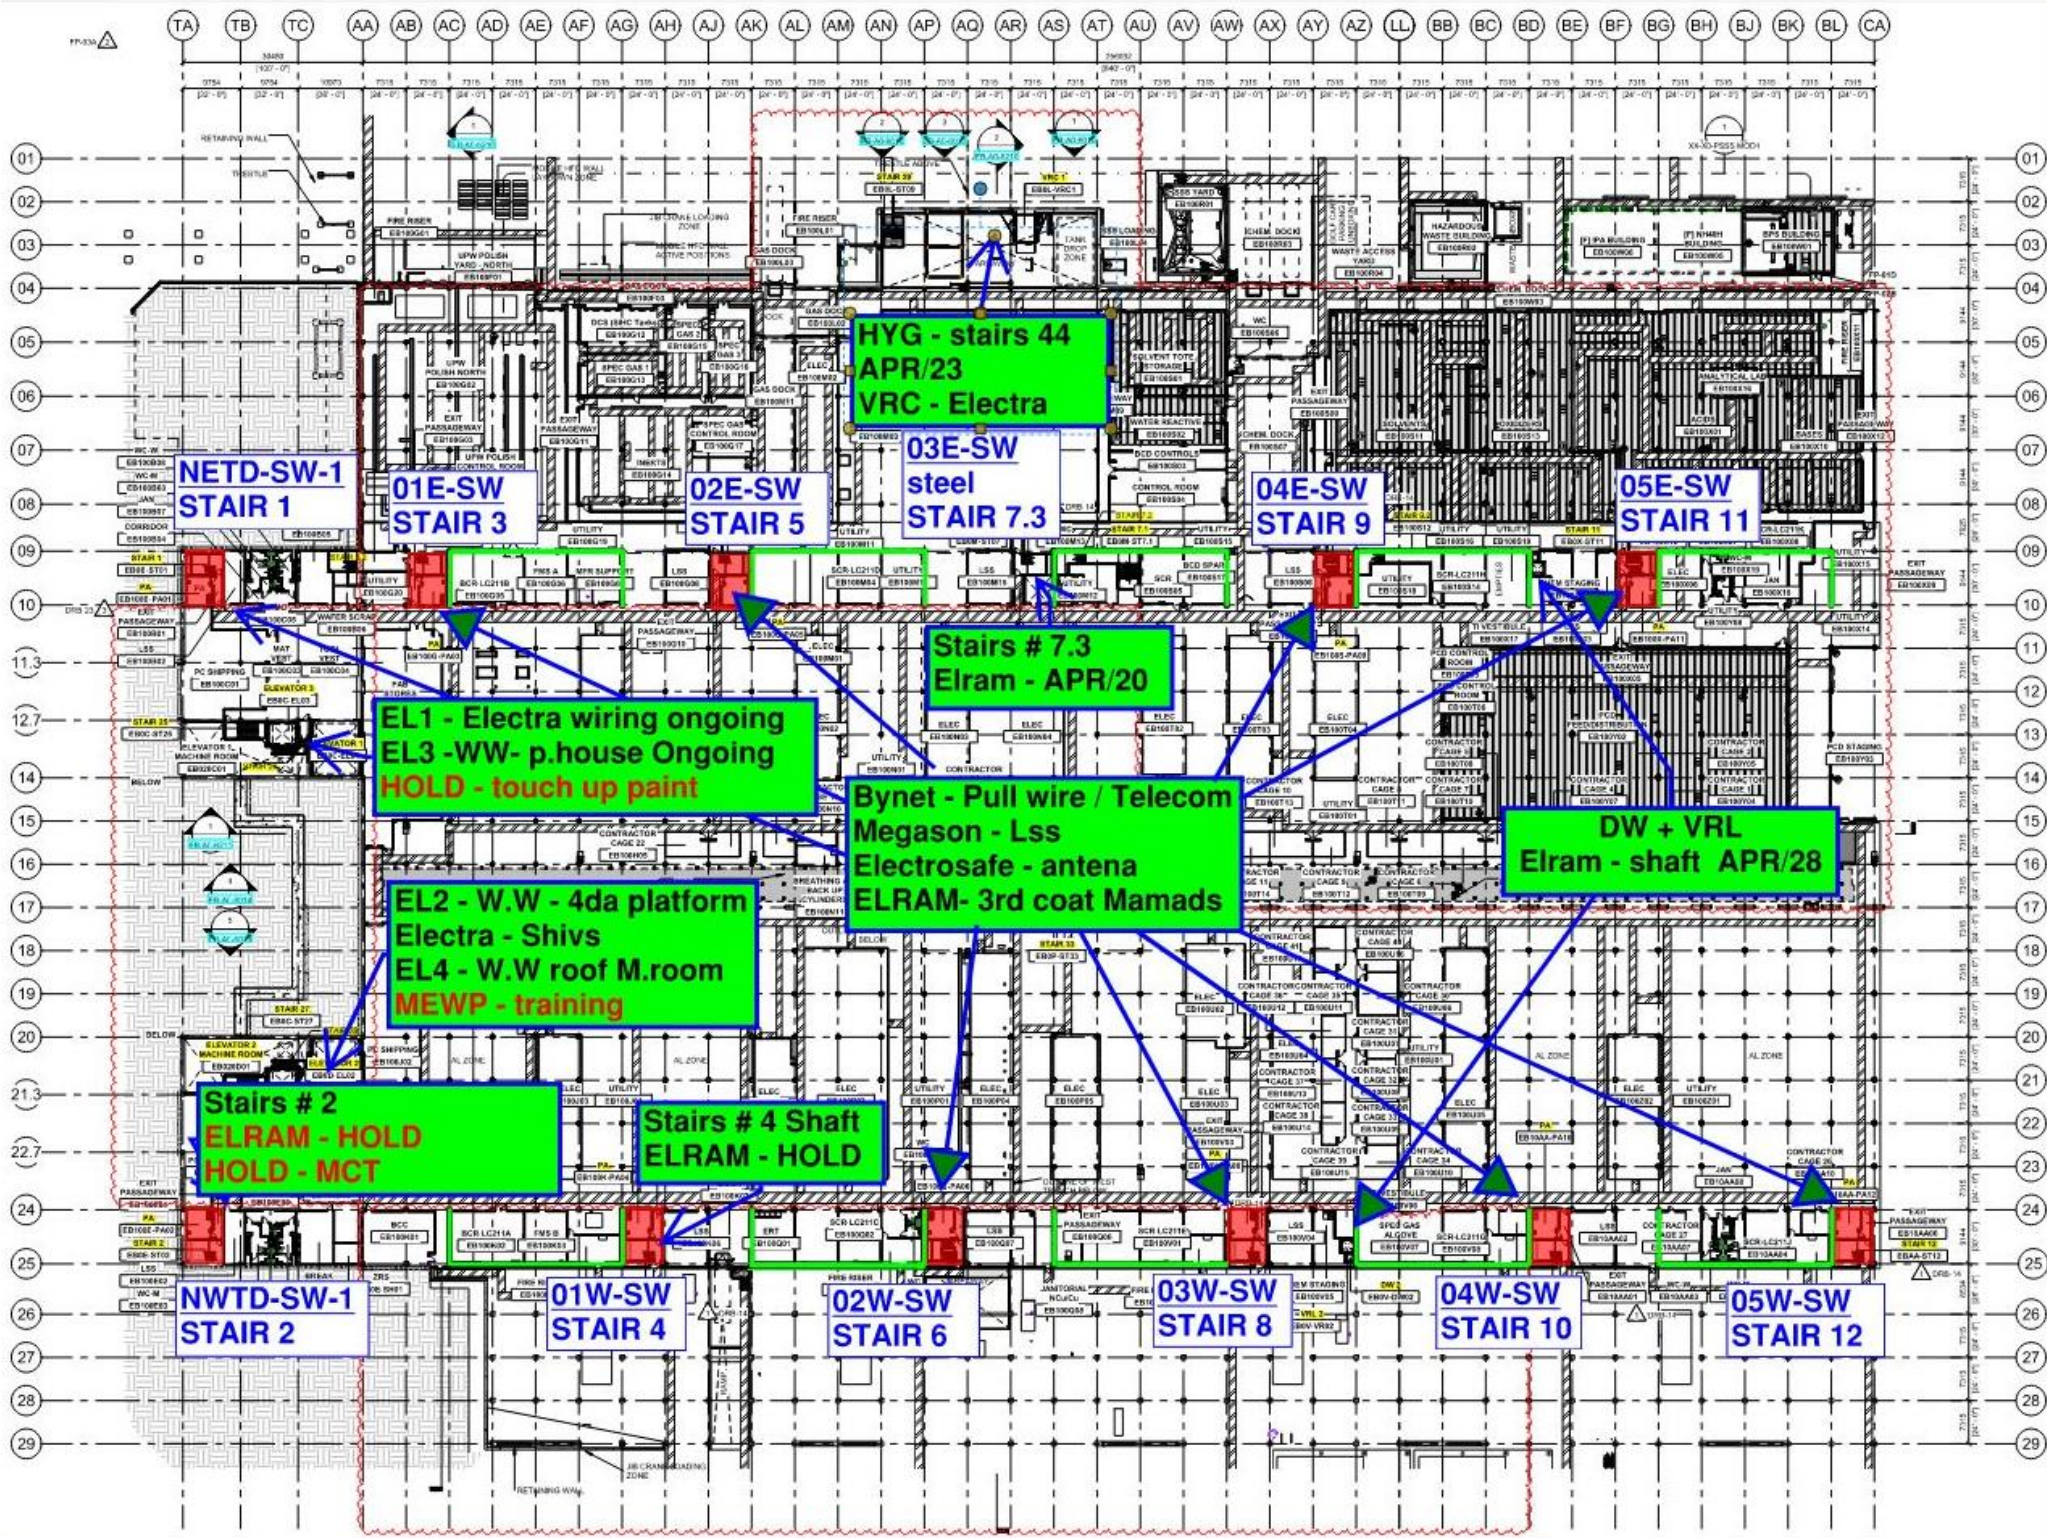

# Request Form



Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

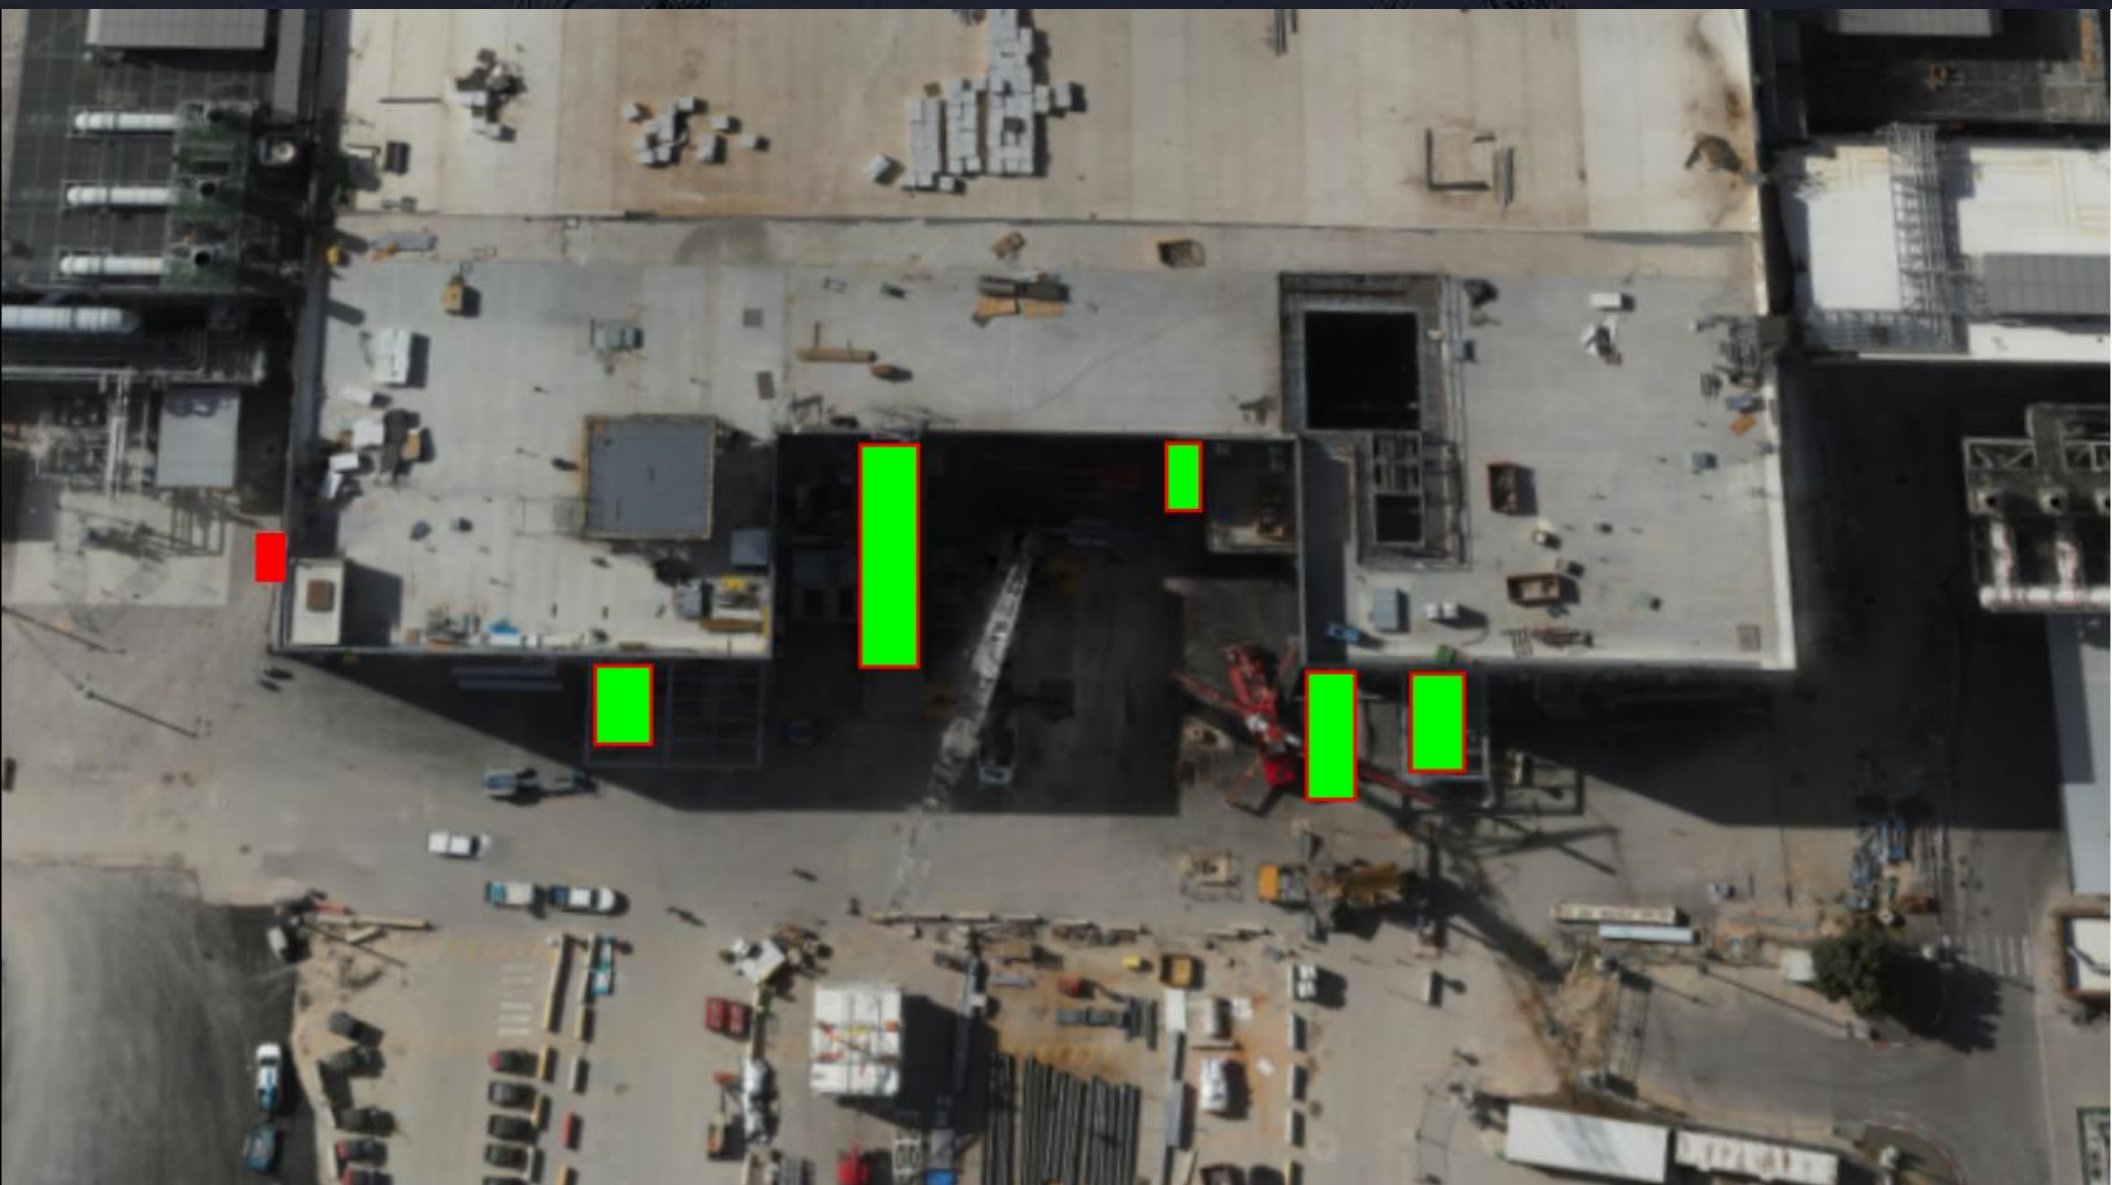



## MOD 2 EASTSIDE GIRTS/SIDING




2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501
---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

# PSSS.1

Utility Level  
1YA


PSSS Roof  
2SA

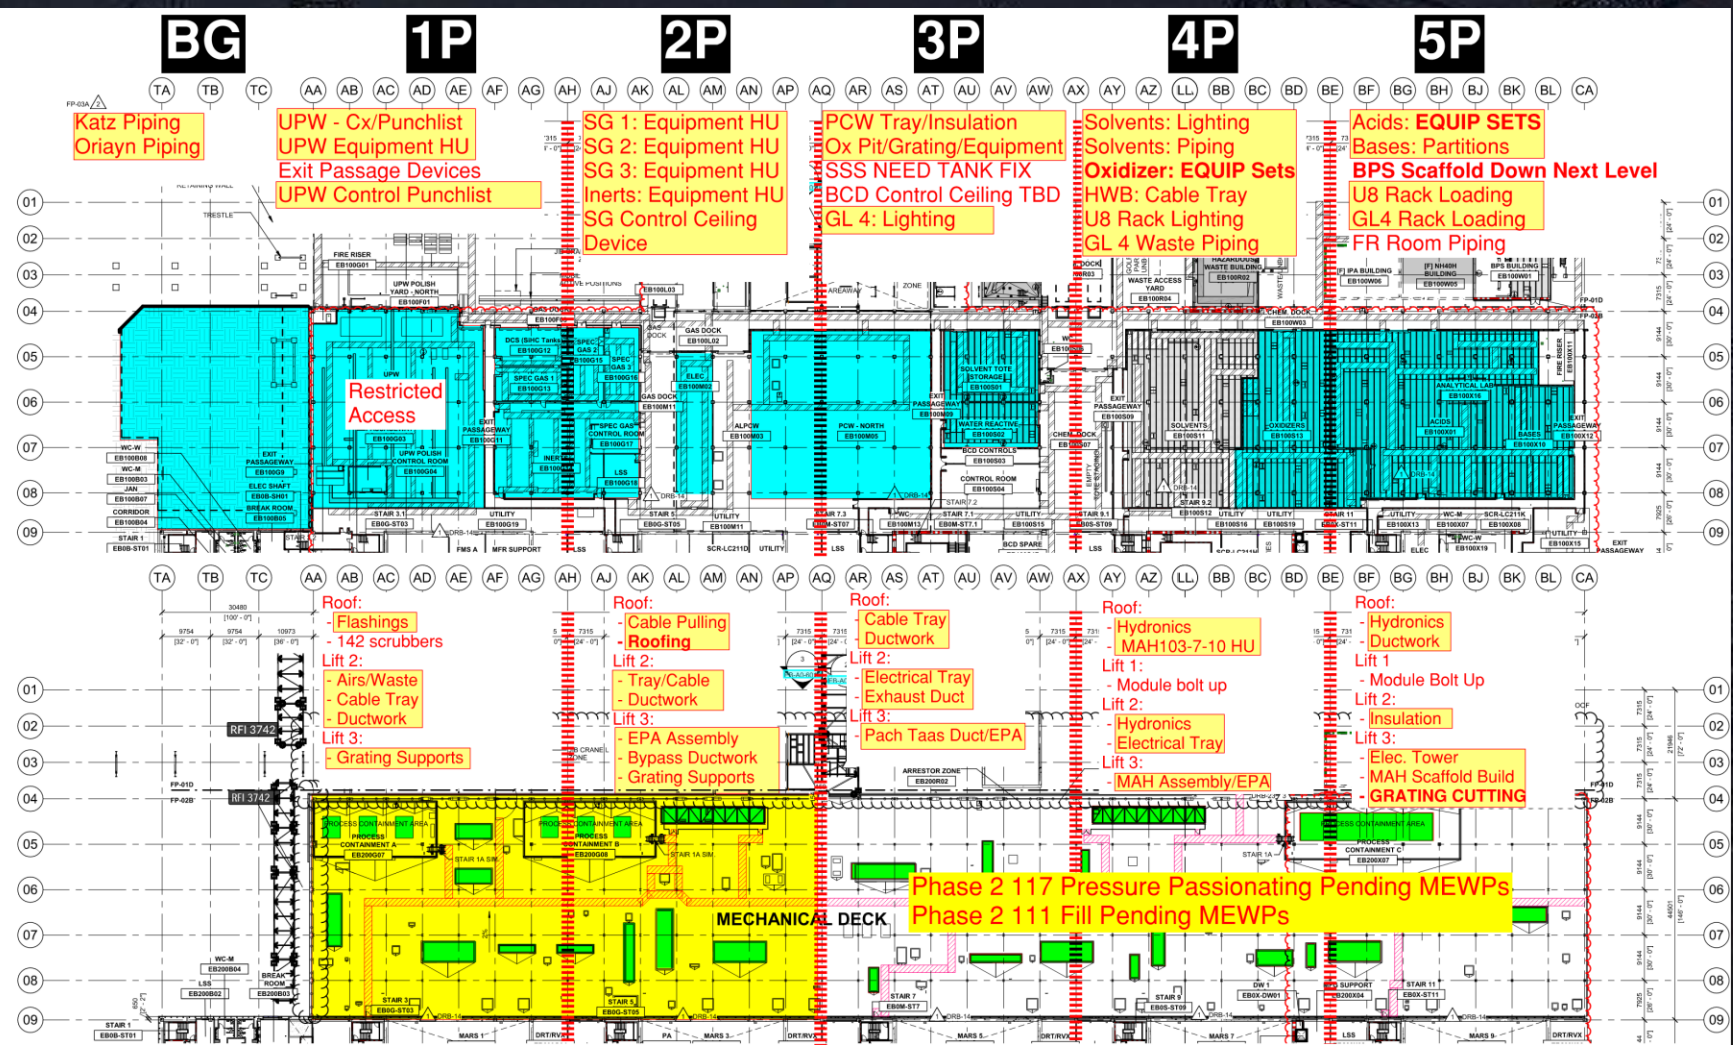

# PSSS.2

## Utility Level 1YA

PSSS Roof  
2SA

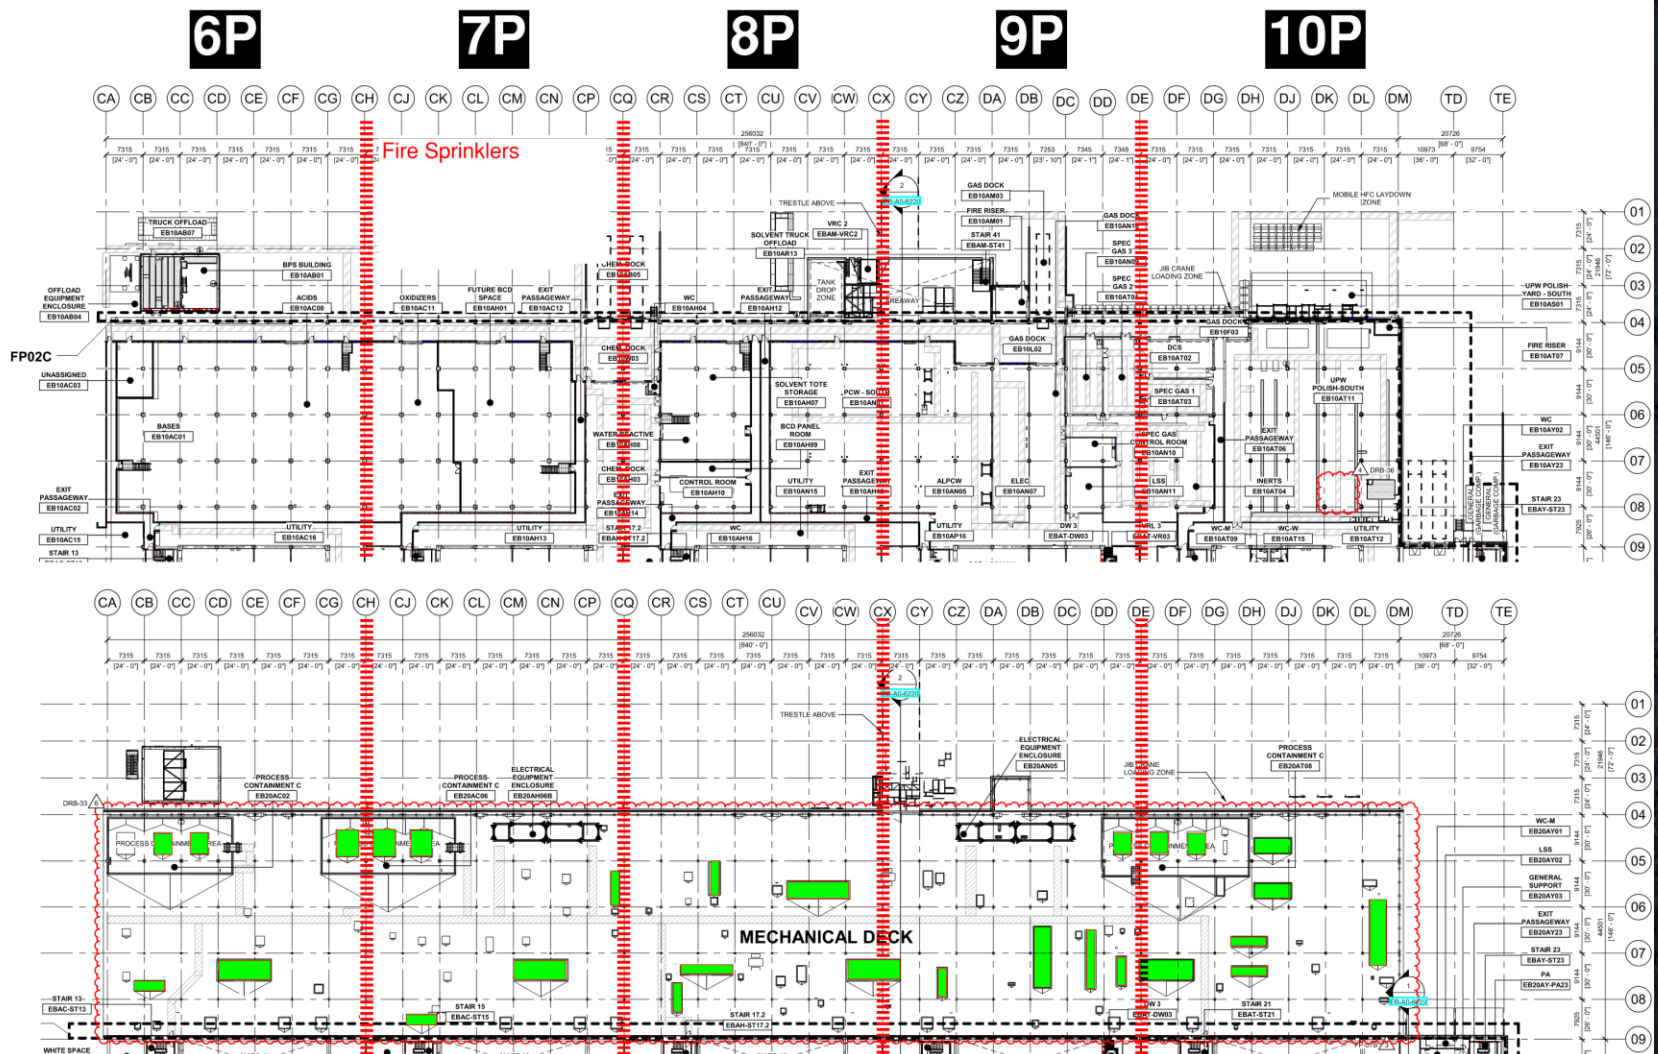

# BGY GN2 Purging

21<sup>st</sup>-24<sup>th</sup>  
continuous  
noise  
BGY Closed






## WJG – UL

\* Carmel Bidud - erection of  
scaffold in the west SUT

\* Carmel Bidud - measurements  
for final duct connections to FAB  
\*Lesico - welding and grouting pipe  
support

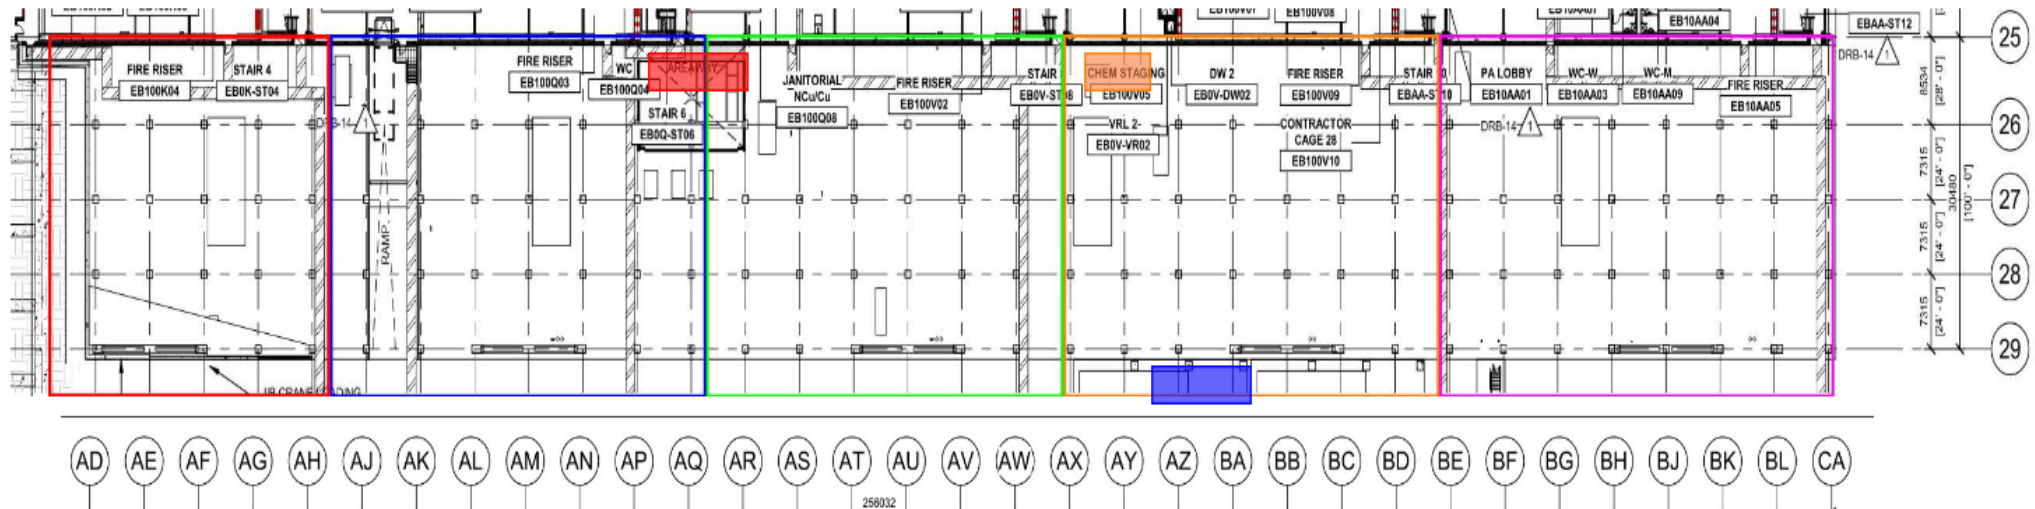




## WJG – Lift 2

\* Taper tech - fixing planking after stiffeners installation

\* Chemo - finished restoration on UPN 113

\* SK - working on connections to MAH  
\* Afcon - installation of cable tray underneath MAH and finishing cable pulling to VFD

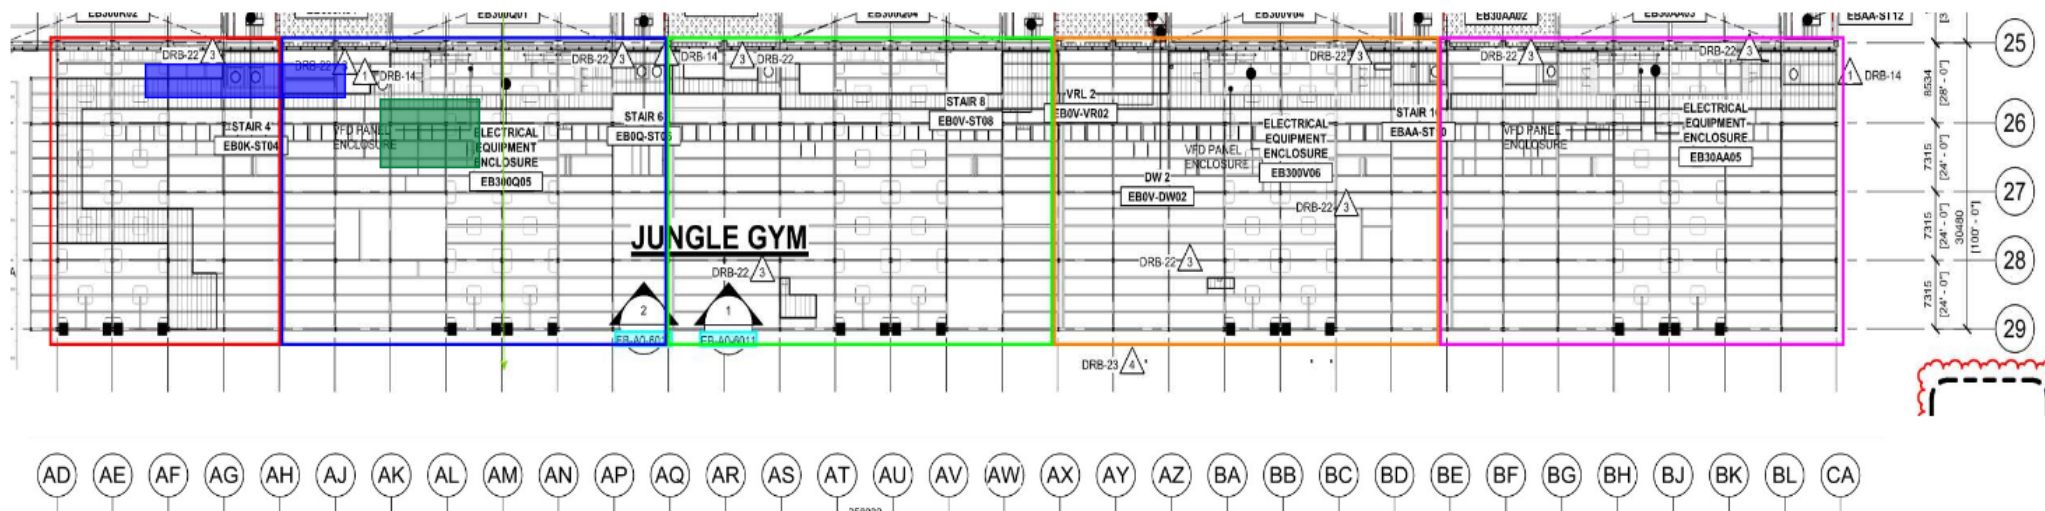


## WJG – Lift 3

\* SN - installing and welding penetrations supports


\* Taper tech - performing planking penetrations and removing ramps for permanent handrails  
\* SN - handrails installation

\* Pach Taas - hoisting and installing fans




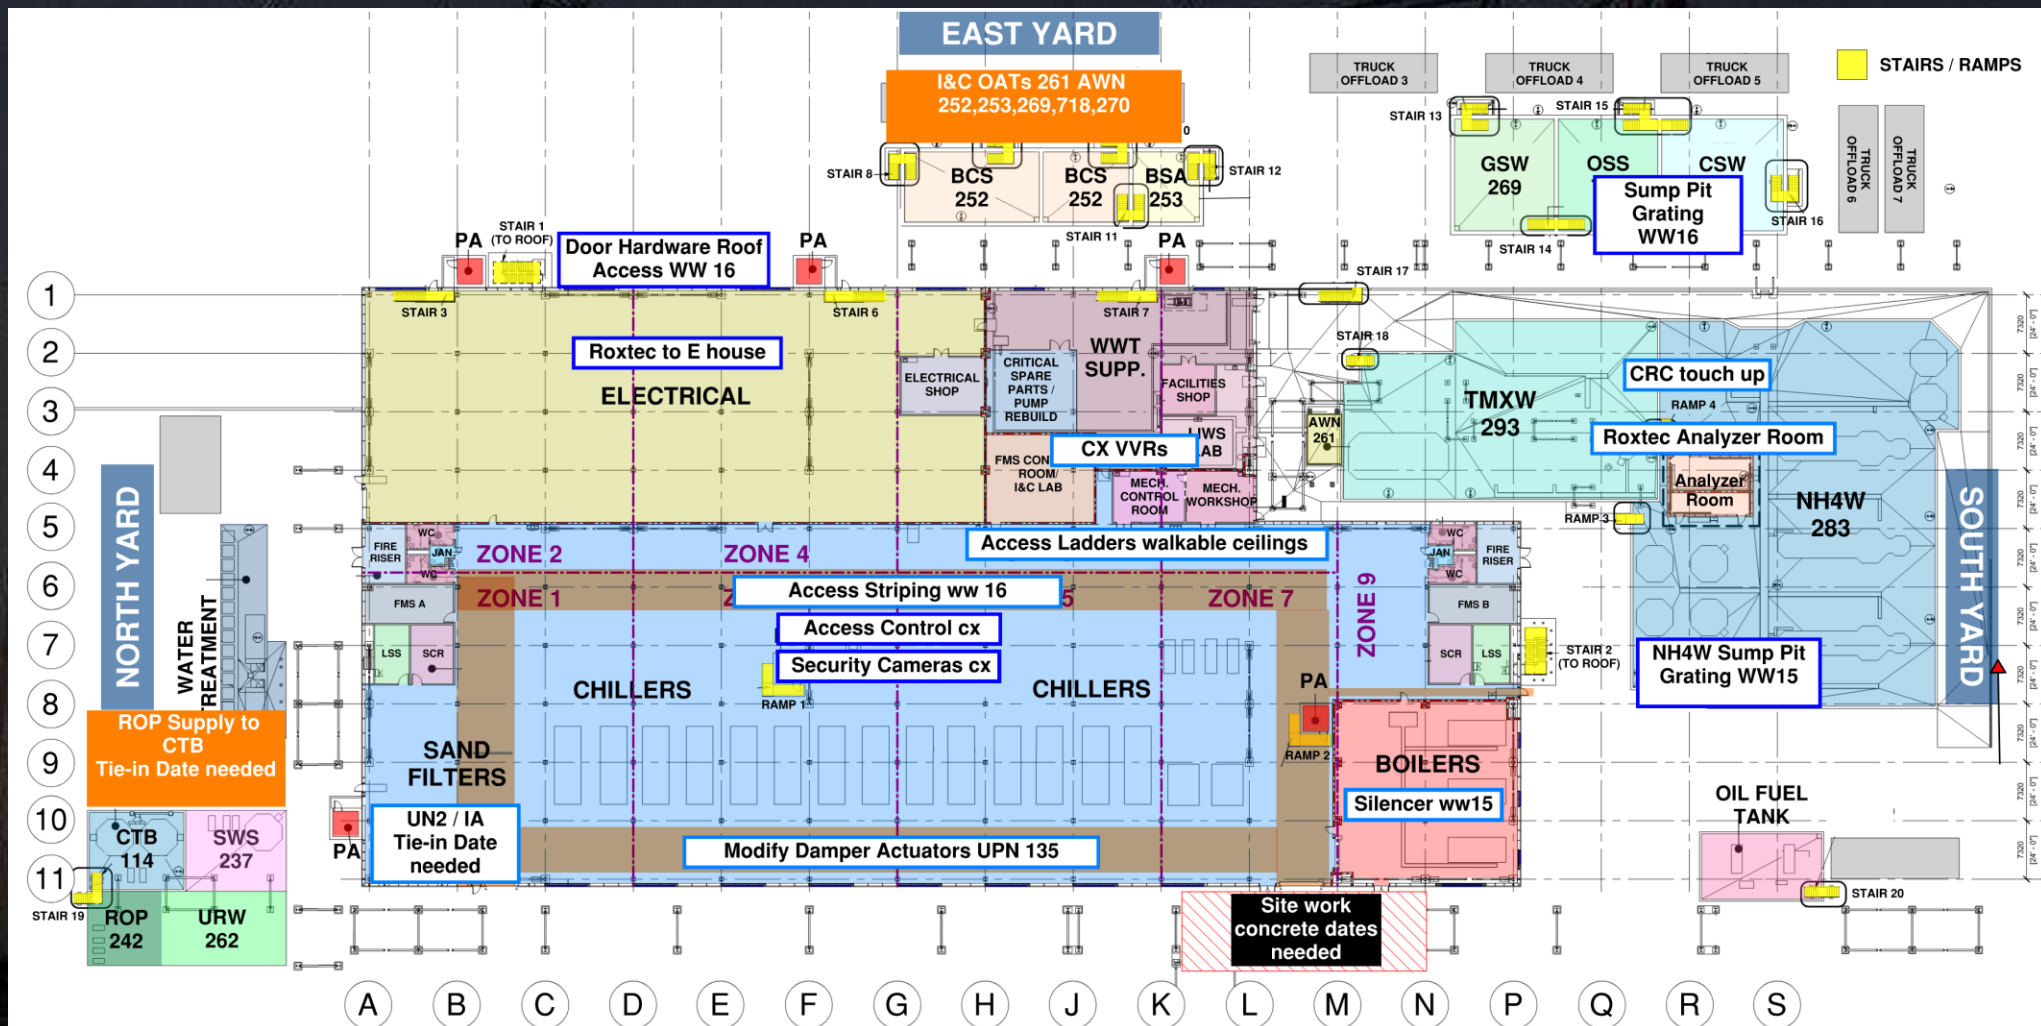


# CUB 1 – EXTERIOR/ROOF

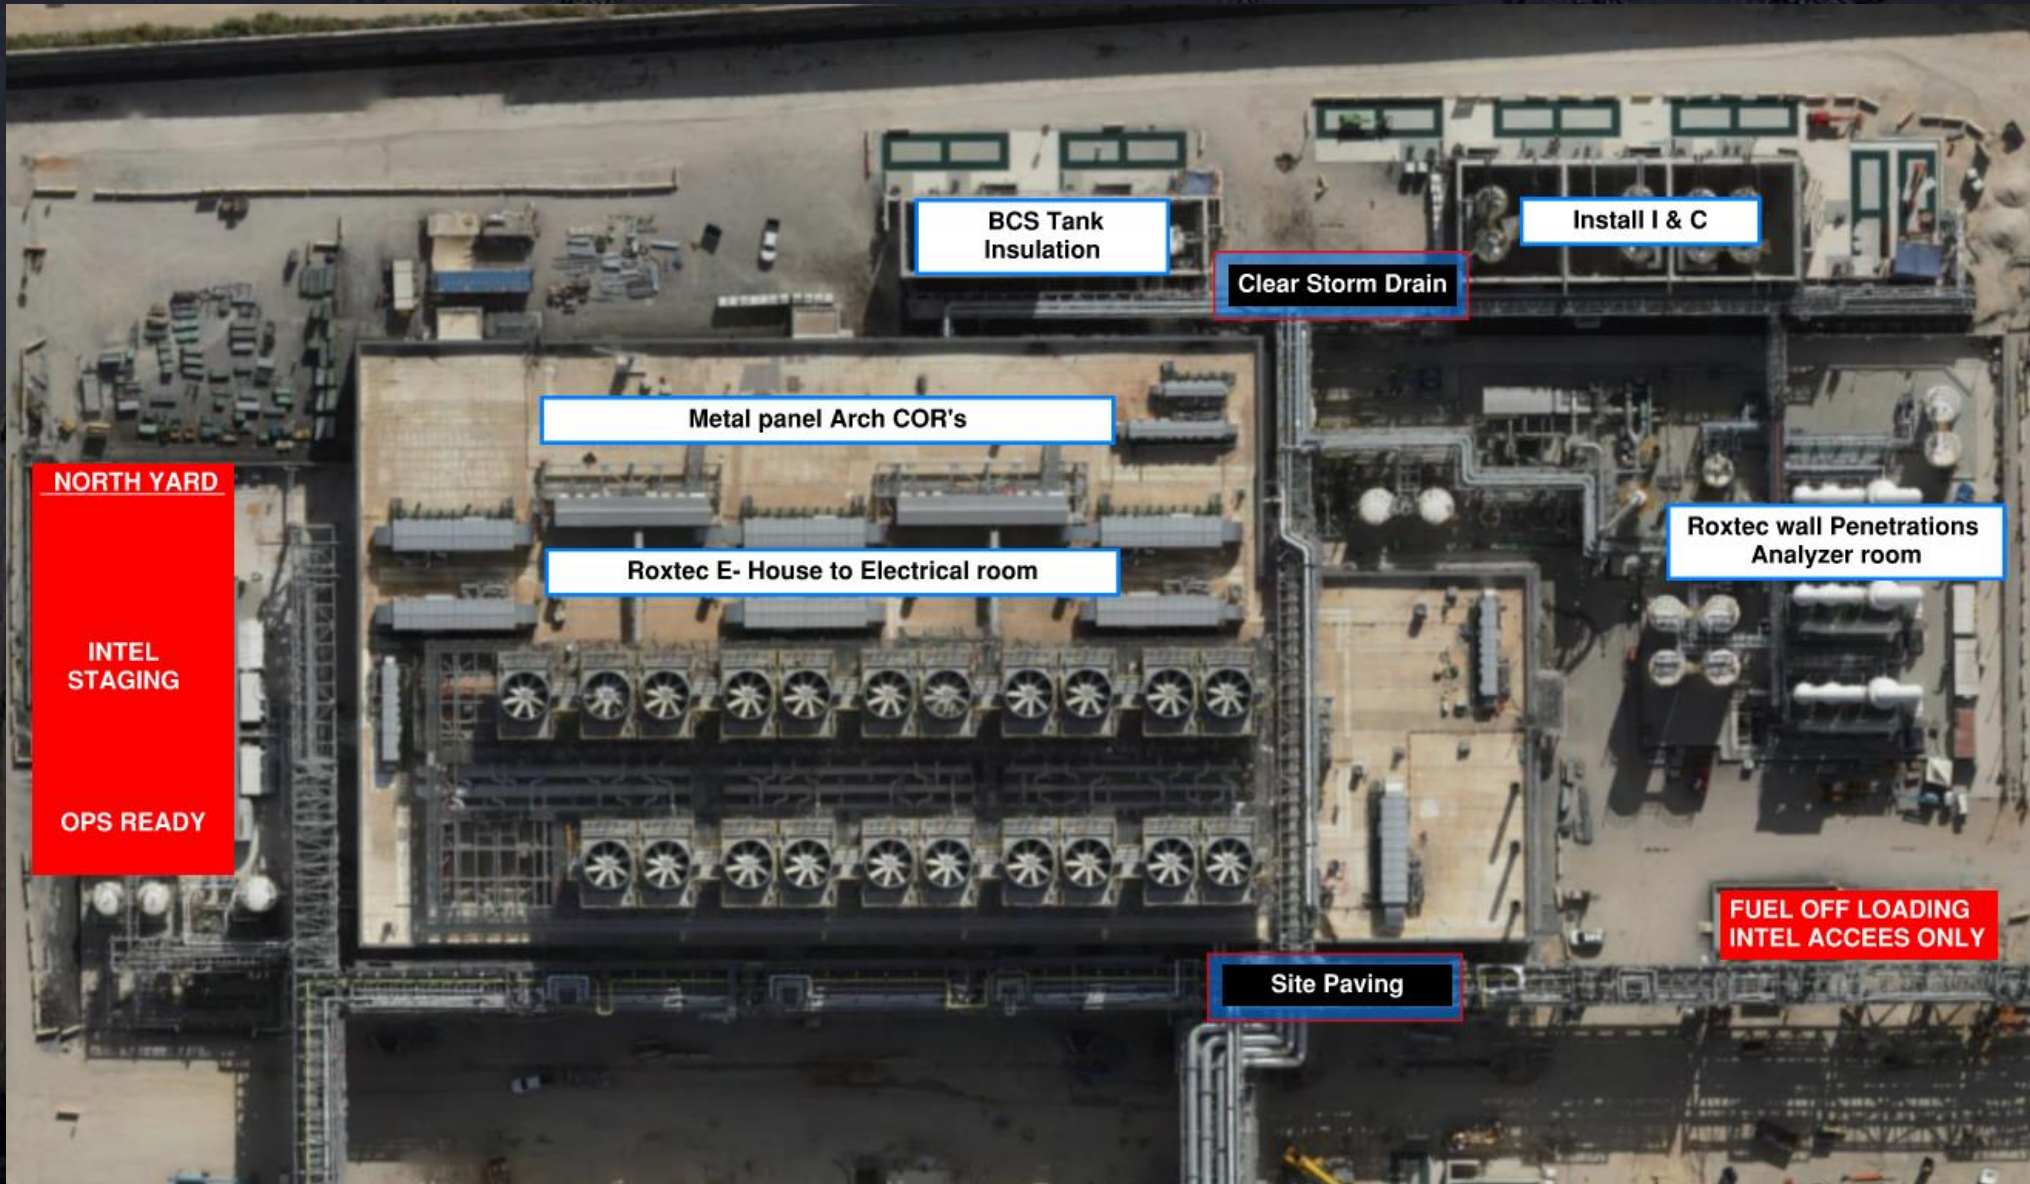




# CUB 2- Load in & H&T

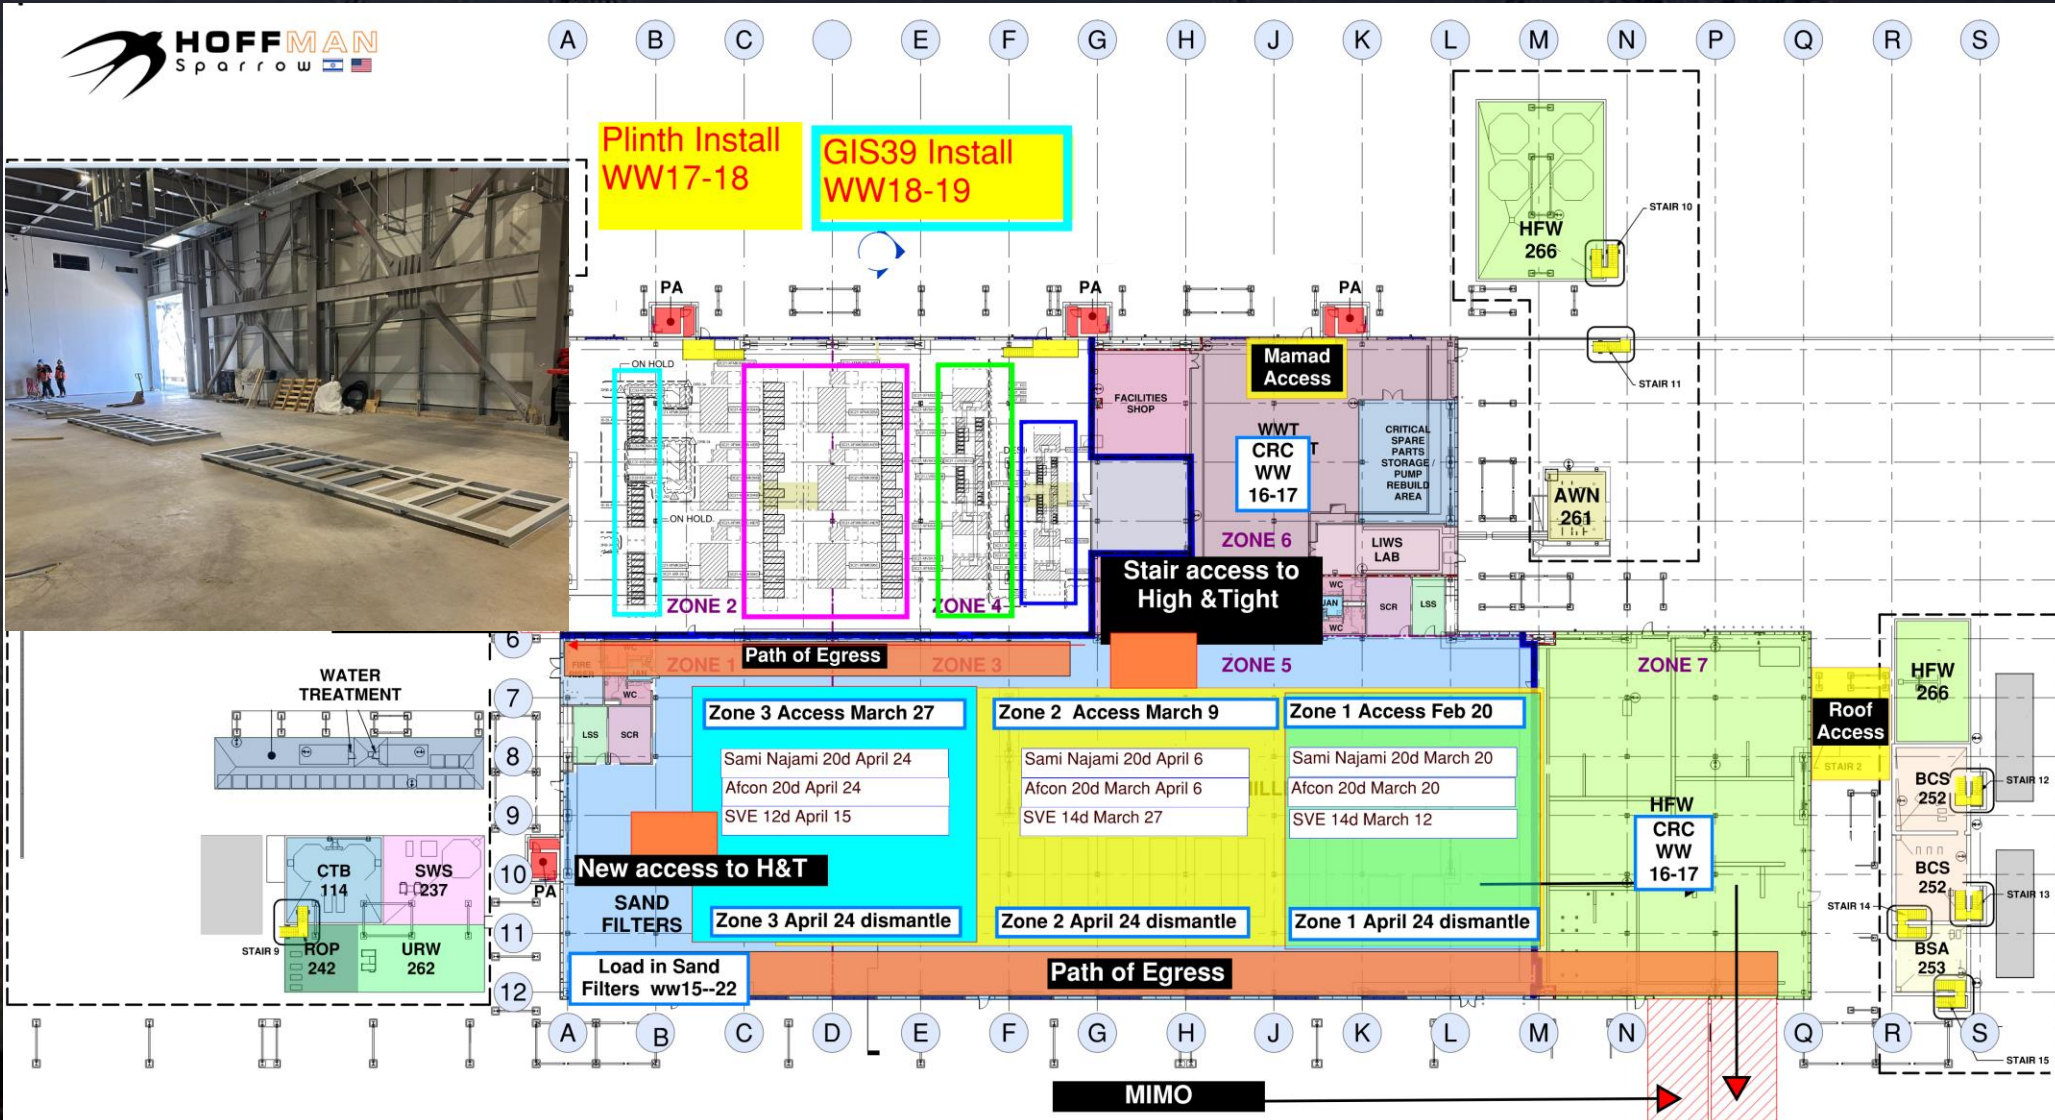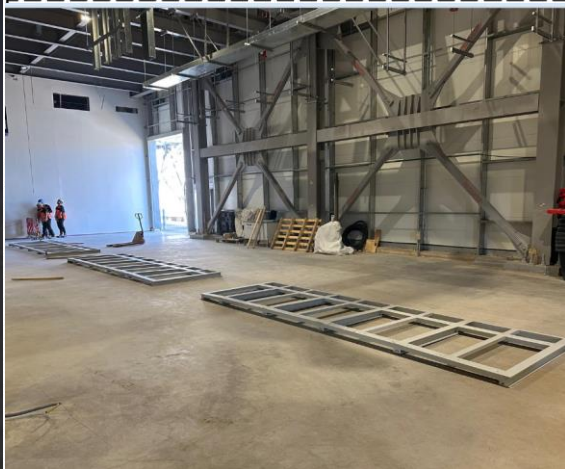


# CUB 2- Trestles/Roof/Guardrails

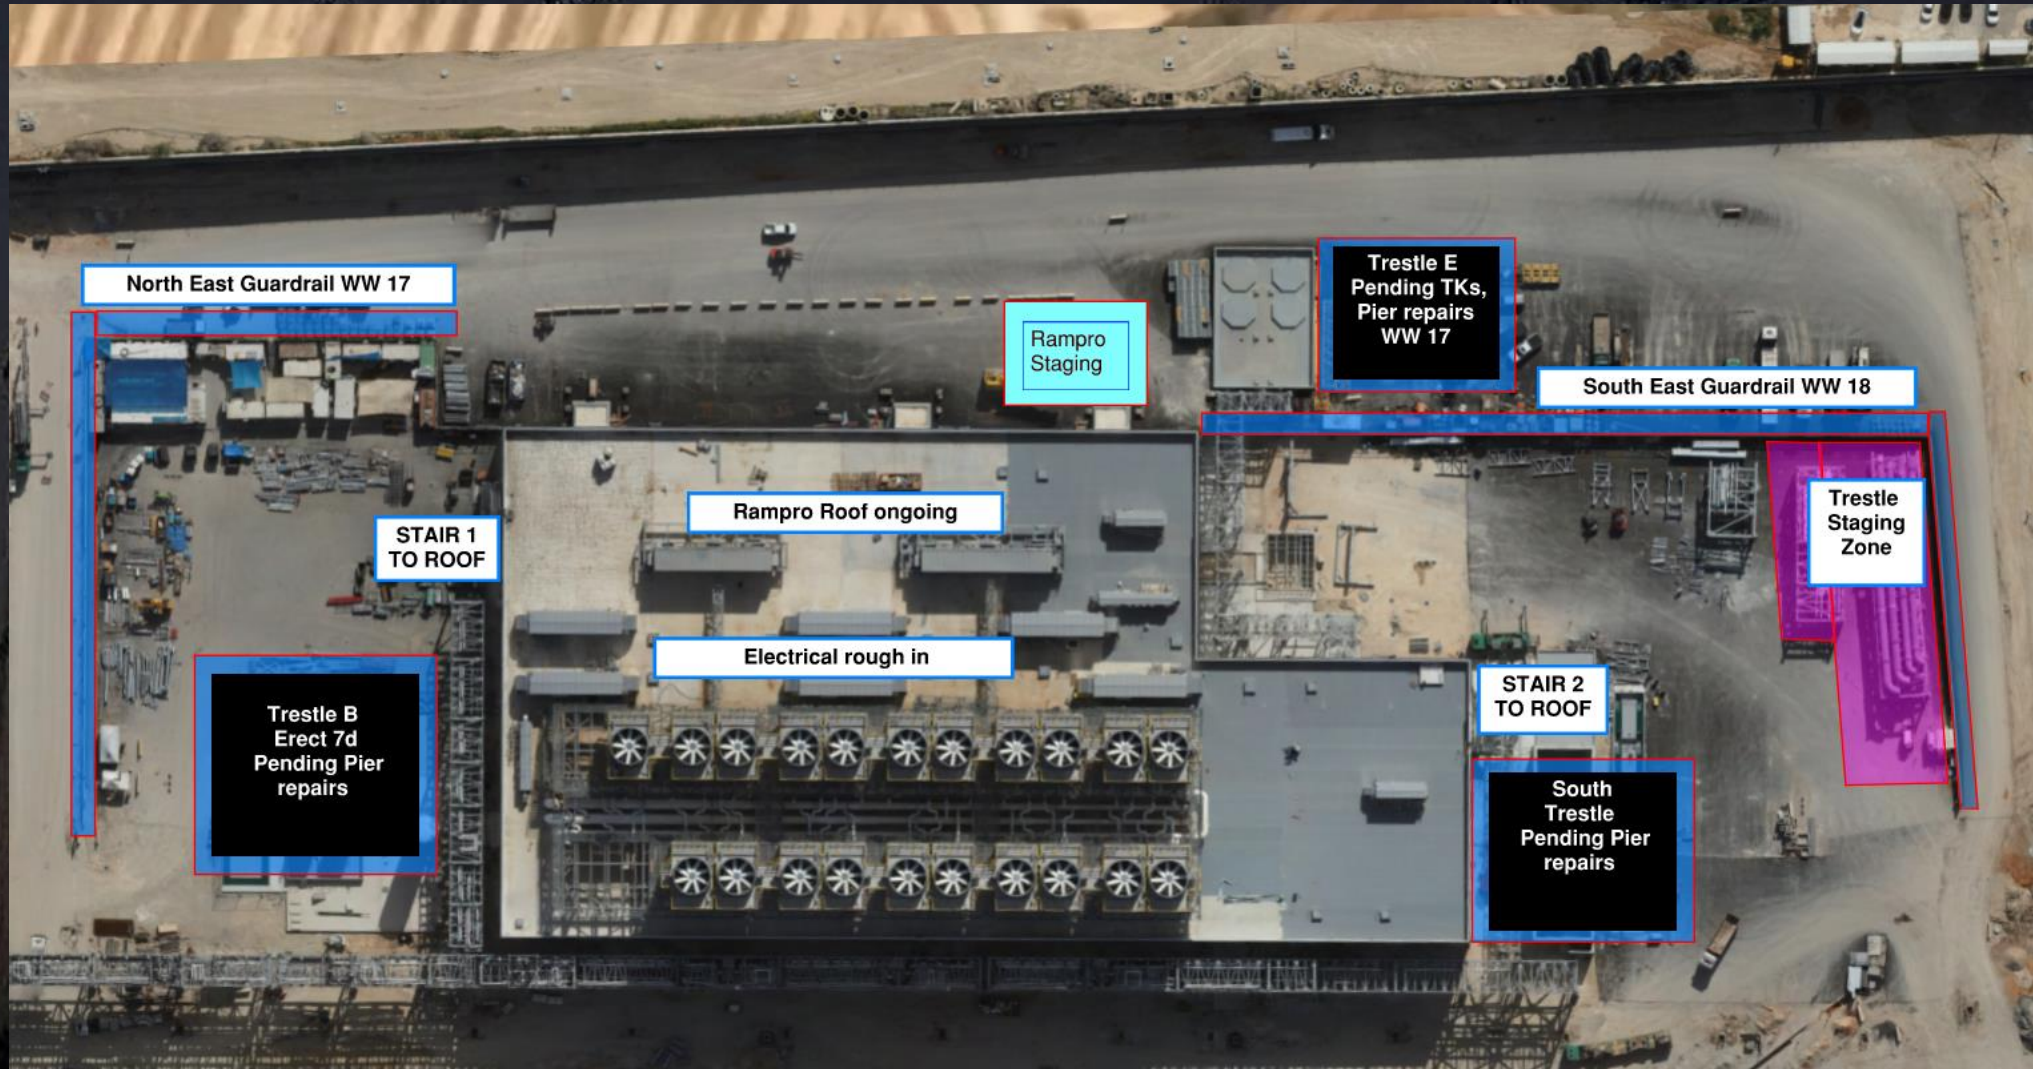



# Daily Coordination Meeting

## Site Logistics

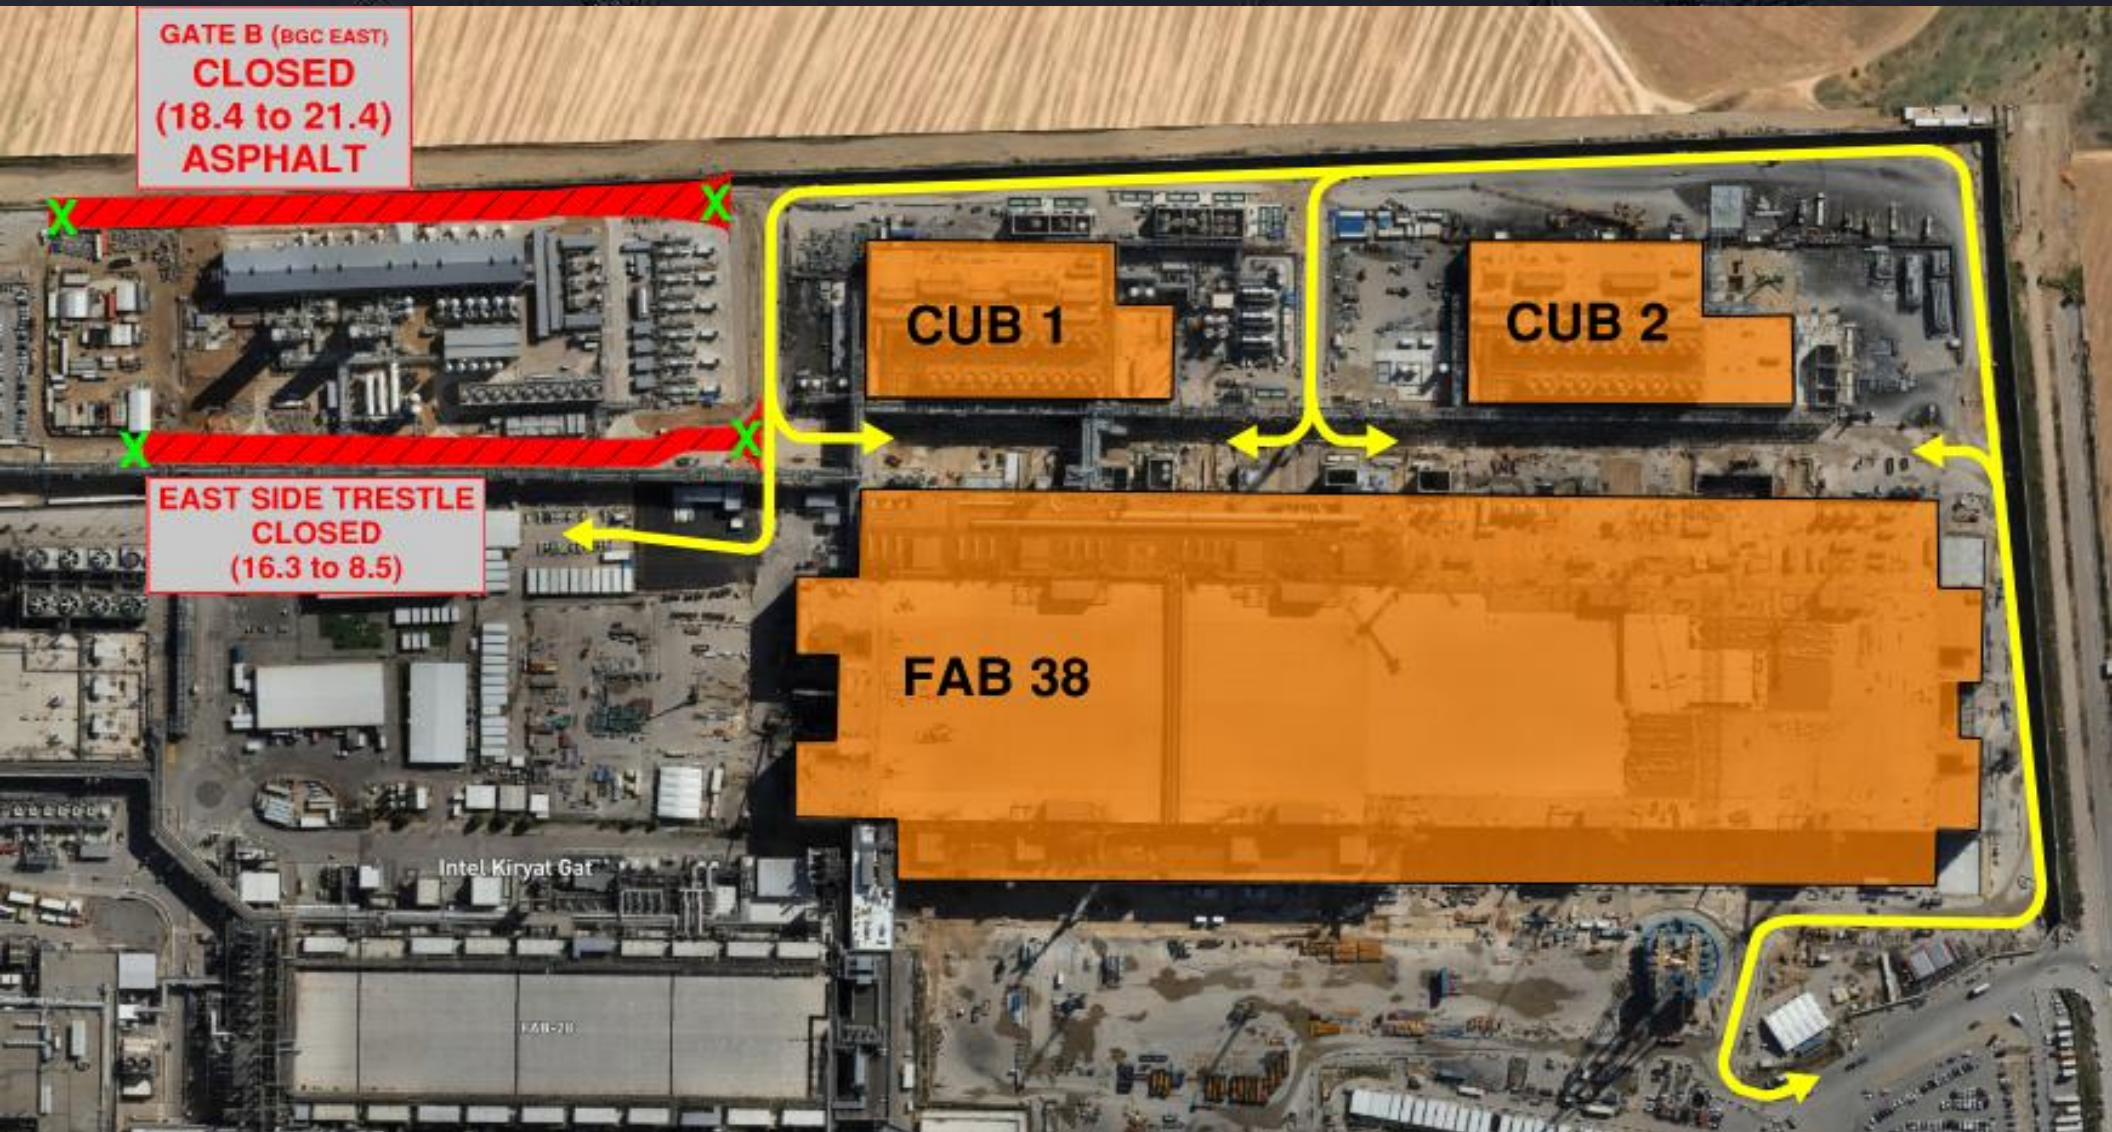

# Daily Coordination Meeting

## Site Logistics: North





# Daily Coordination Meeting


## Site Logistics: South



# Daily Coordination Meeting

## MAMAD Locations


MAMAD LOCATIONS (19-March-2025)  
■ LARGE  
■ SMALL  
■ BUILDING

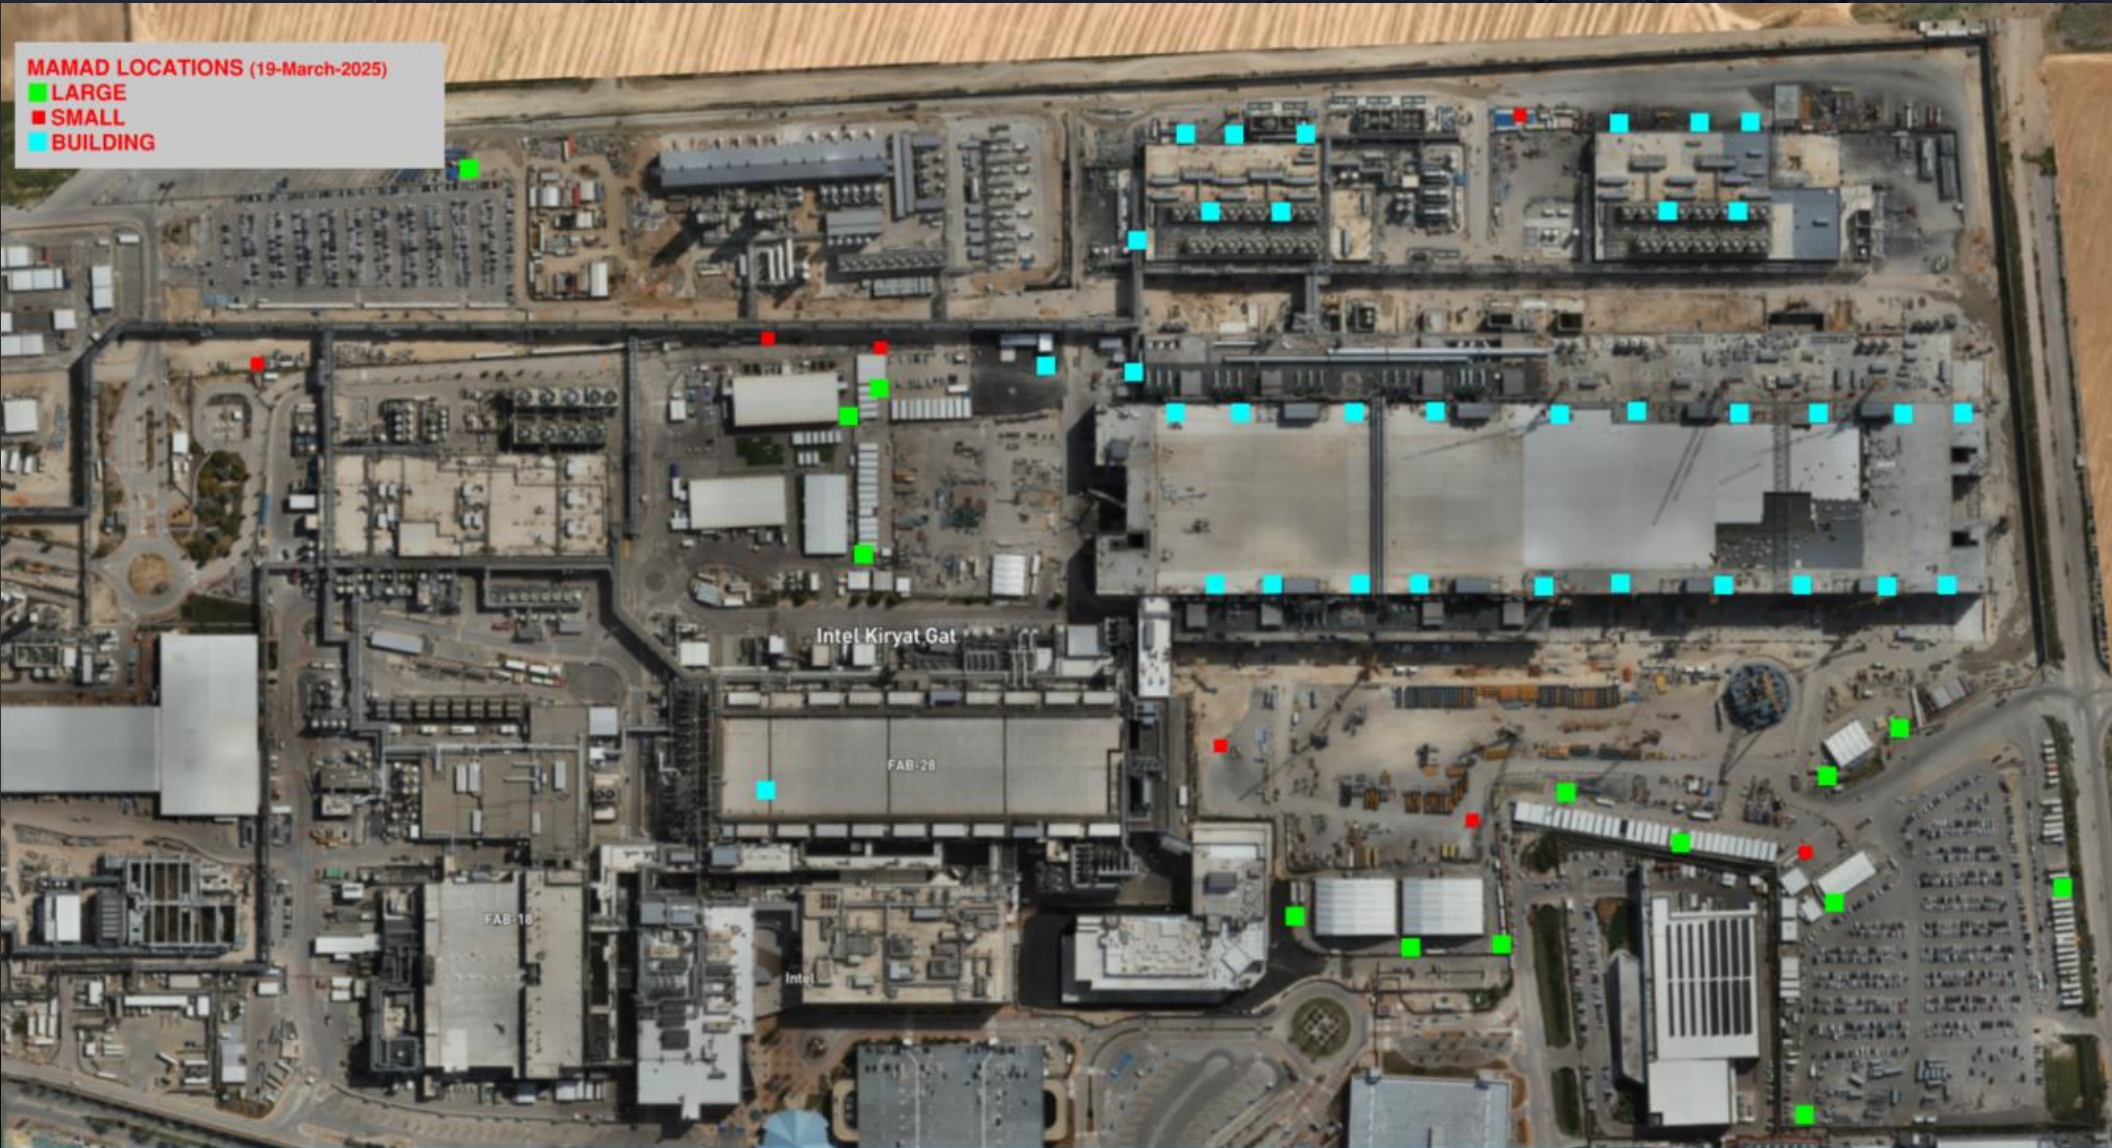

# Daily Coordination Meeting

## WATER BOTTLE FILLING STATIONS

## WATER BOTTLE FILLING STATIONS

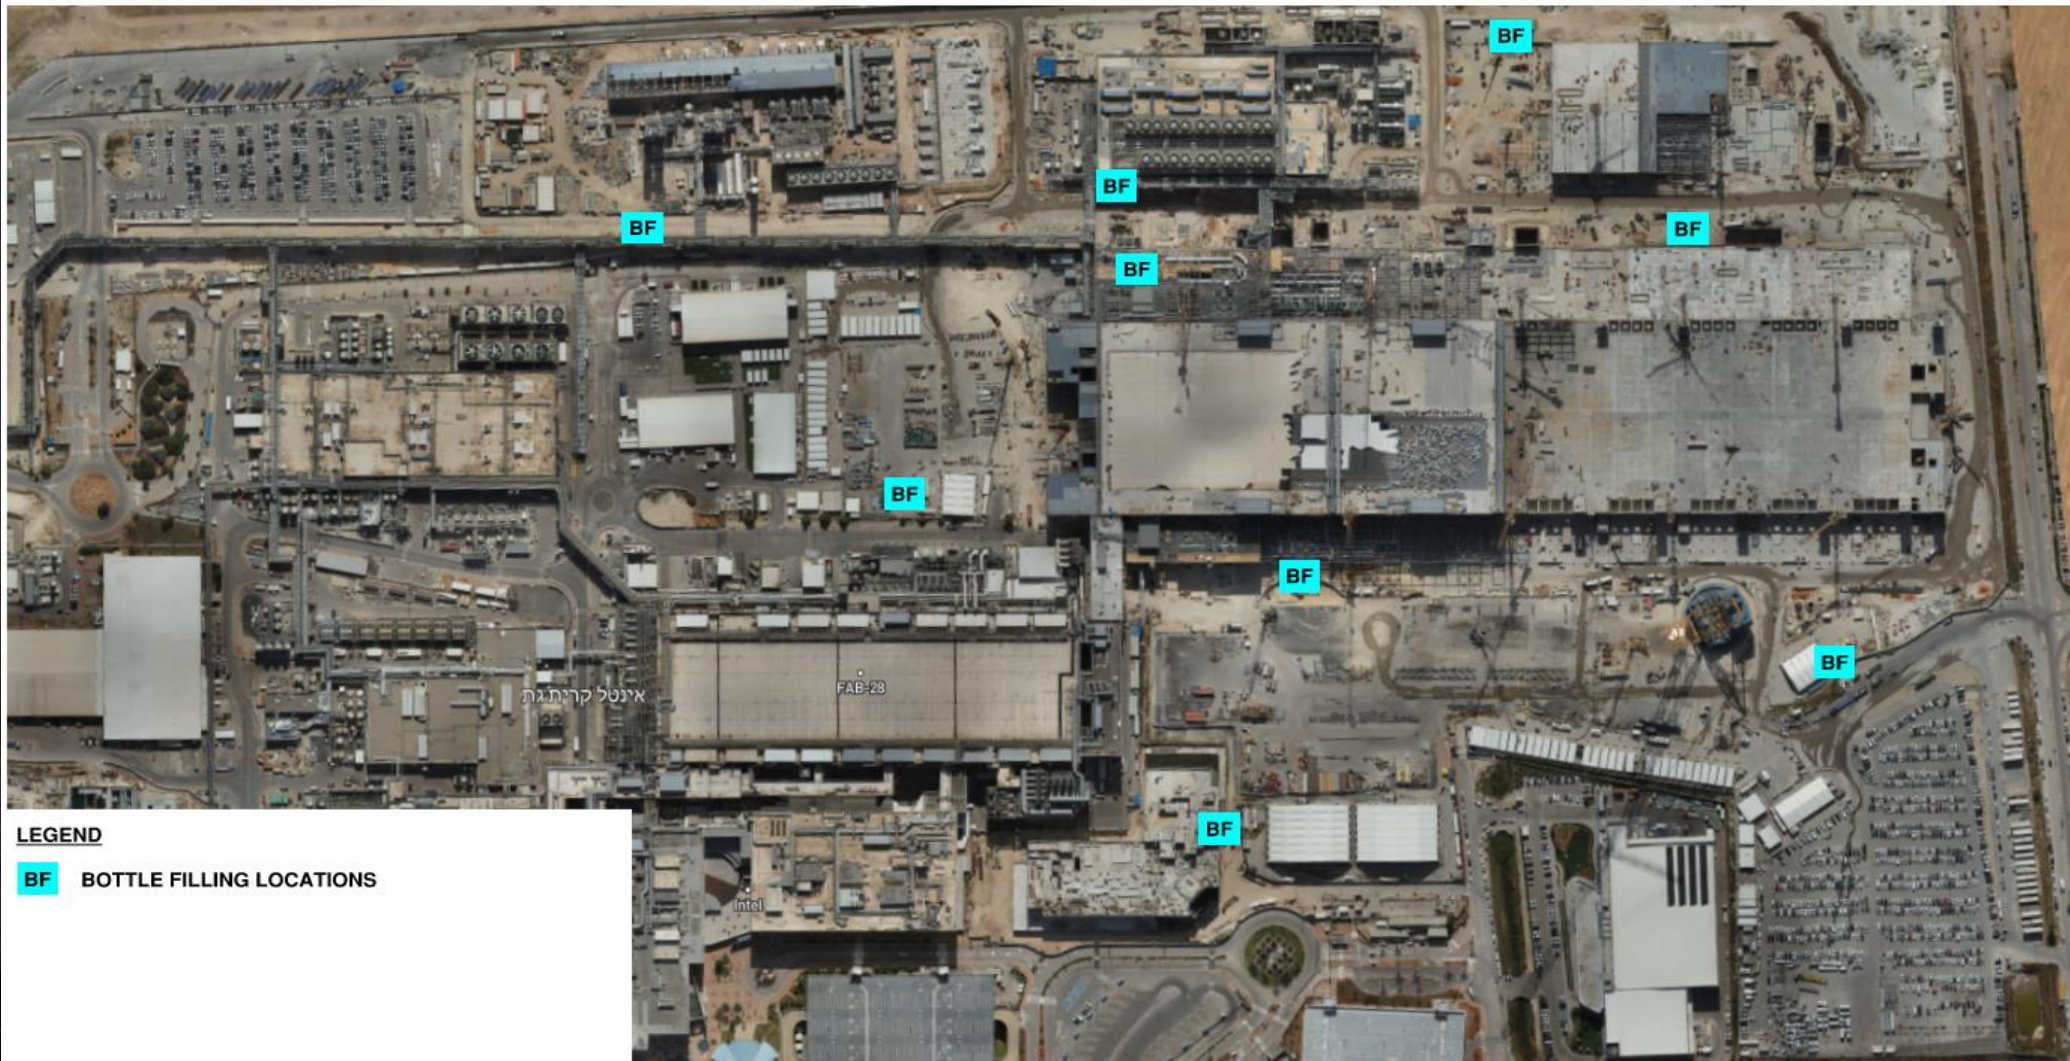



**HOFFMAN CONSTRUCTION COMPANY**



# BACK TO MEWP WORK

A.S Barzel	1	2	Cub 1 + 2	Ready to schedule   ממתין לקביעת זימון בדיקה				
BRAND INDUSTRIAL LTD		3	1843 cub2 3731...3667 cub1	Ready to schedule   ממתין לקביעת זימון בדיקה				
D&P Clean Room Ltd	15		CR	Approved   מאושר	04/20/25	1 PM	Approved	Monday 21, 9 AM
ELECTROSAFE LTD	1		Utility 14 AU	Approved   מאושר	04/17/25		Approved	Monday 21, 8 AM
ELRAM PROJECT LTD				Ready to schedule   ממתין לקביעת זימון בדיקה	04/22/25	AM		
ETC Systems LTD	2		Utility CA14 \ PSSS roof	Scheduled   נקבע זימון לבדיקה	04/21/25	13:15		
HYG STEEL 1990 LTD		1	buggy parking	Approved   מאושר	04/20/25		Scheduled	Tuesday 22, AM
Katz Arie Stainless Steel	13	4	CUB 2 / SITE CLOSE TO PMP / UTILITY	Not ready to schedule   לא מוכן לקביעת זימון בדיקה				
Newco - Tec LTD	2		clean room	Scheduled   נקבע זימון לבדיקה	04/22/25	9:30		
Rolling Plains Constriction Inc	3	4	clean room	Approved   מאושר	04/20/25		Approved	Monday 21, 10 AM
SIG Industrial LTD	3		clean room	Fixes pending   ממתין לתיקון	04/20/25	12:30		
SK ENGINEERING & PROJECT (C	11	5		Scheduled   נקבע זימון לבדיקה	04/21/25	14:00		
Sami Najami WW Tooldock	2	4	North Tooldock Outside	Ready to schedule   ממתין לקביעת זימון בדיקה				
TM TEAM LTD	1		clean room	Scheduled   נקבע זימון לבדיקה	04/21/25	15:00		
W&W - AFCO Steel LLC	5	13	wjg/ south fan deck / ut / tool tower / sub fab / psss	Scheduled   נקבע זימון לבדיקה	04/21/25		Scheduled	Monday 21, 1 PM

## Update after Intel walks:

- Working at heights permit.
- Contact information on MEWP.

**Get 100% ready → Contact us → Get your MEWP approved**

# BACK TO MEWP WORK

## 1. Documentation available on the equipment in the field:

- I. Equipment registration document (Rishayon).
- II. Valid Bodek inspection report (Tasker) – must be valid within 6 months of inspection.
- III. Equipment insurance document (Bituach). The identification number for this equipment must be written in the insurance.
- IV. Supplier inspection report – signed and available for review.
- V. Supplier training certificate for equipment operation.
- VI. 18C designation letter listing approved operators and spotters for the specific equipment.
- VII. Equipment manual – must be available in Hebrew and in the language of the operator (QR code acceptable for one language).
- VIII. Working on heights permit.

## 2. Equipment marking:

Each MEWP must be clearly marked with:

- I. The company name and contact information.
- II. A printed list of approved operators and spotters assigned to that equipment.

# BACK TO MEWP WORK

## 3. Intel MEWP Checklist:

Must be fully completed and signed for each piece of equipment and ready for review in the field.

## 4. Intel MEWP Assessment:

Must be available in the field and ready for review.

## 5. Visual Inspection of the MEWP:

- I. All handrails and doors must function properly and be free of damage.
- II. MEWP oil diapers must be properly installed. No red/yellow ropes or wires are permitted.
- III. No temporary or improvised fixes are allowed on any operational system.
- IV. The MEWP must be clean, including the operator's remote control.
- V. Please make sure all items are ready before the scheduled inspection.

# Daily Coordination Meeting



14:00 Sign In
