

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- **Weekend Work**




CUB2 Flat work
Sunday morning,
3:00 am

Link Ramp
Sunday morning,
1:00 am

West SUT2
Sunday morning,
5:00 am

SWTT 4DA SOMD
10:00 pm, tonight

UTILITY LEVEL MOD1

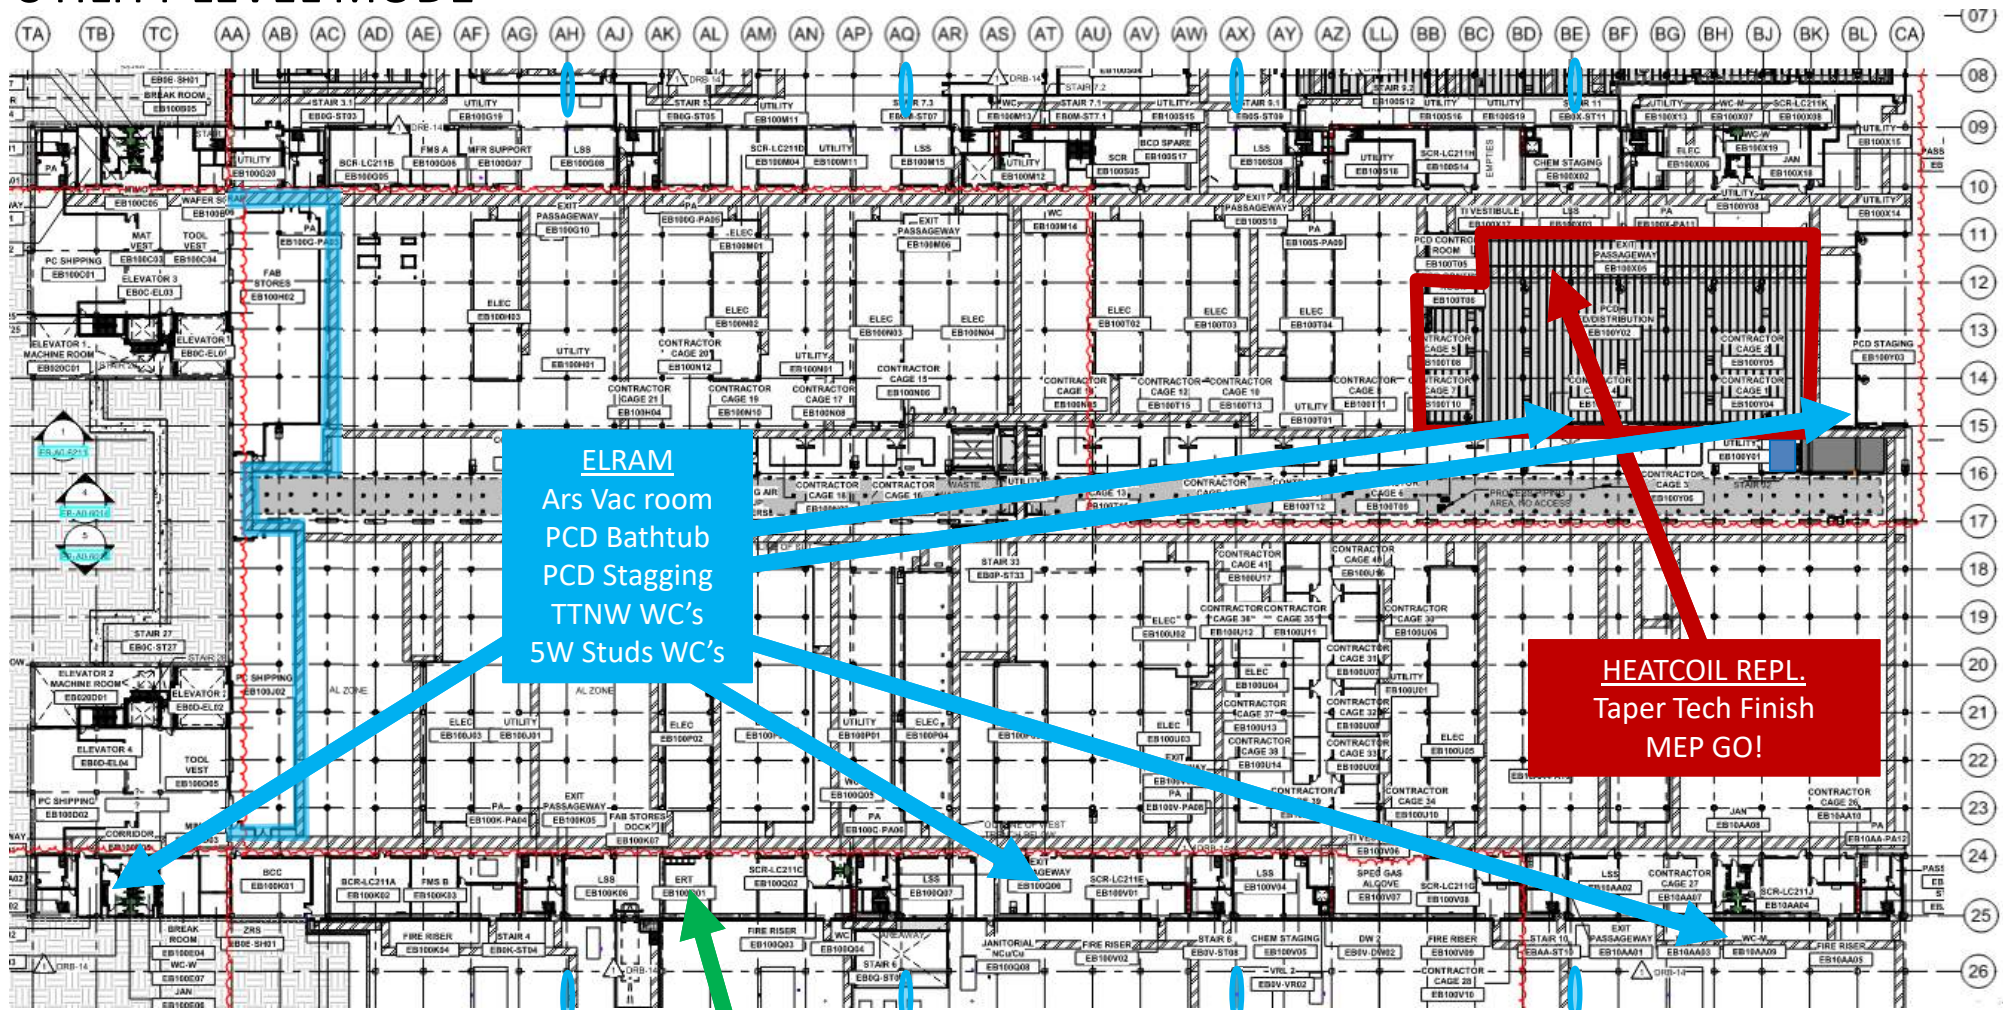



Utility Level MOD2

Don't bring any material without coordination with Oscar M.

Staggering material is possible but must be coordinated and must follow the rules (no combustibles, nothing touch the floor ETC.)

Thanks.


Don't bring any material without coordination with Oscar M.

Staggering material is possible but must be coordinated and must follow the rules (no combustibles, nothing touch the floor ETC.)

Thanks.

SUT 38.1 LEVEL

OH roll-up door
Install ???

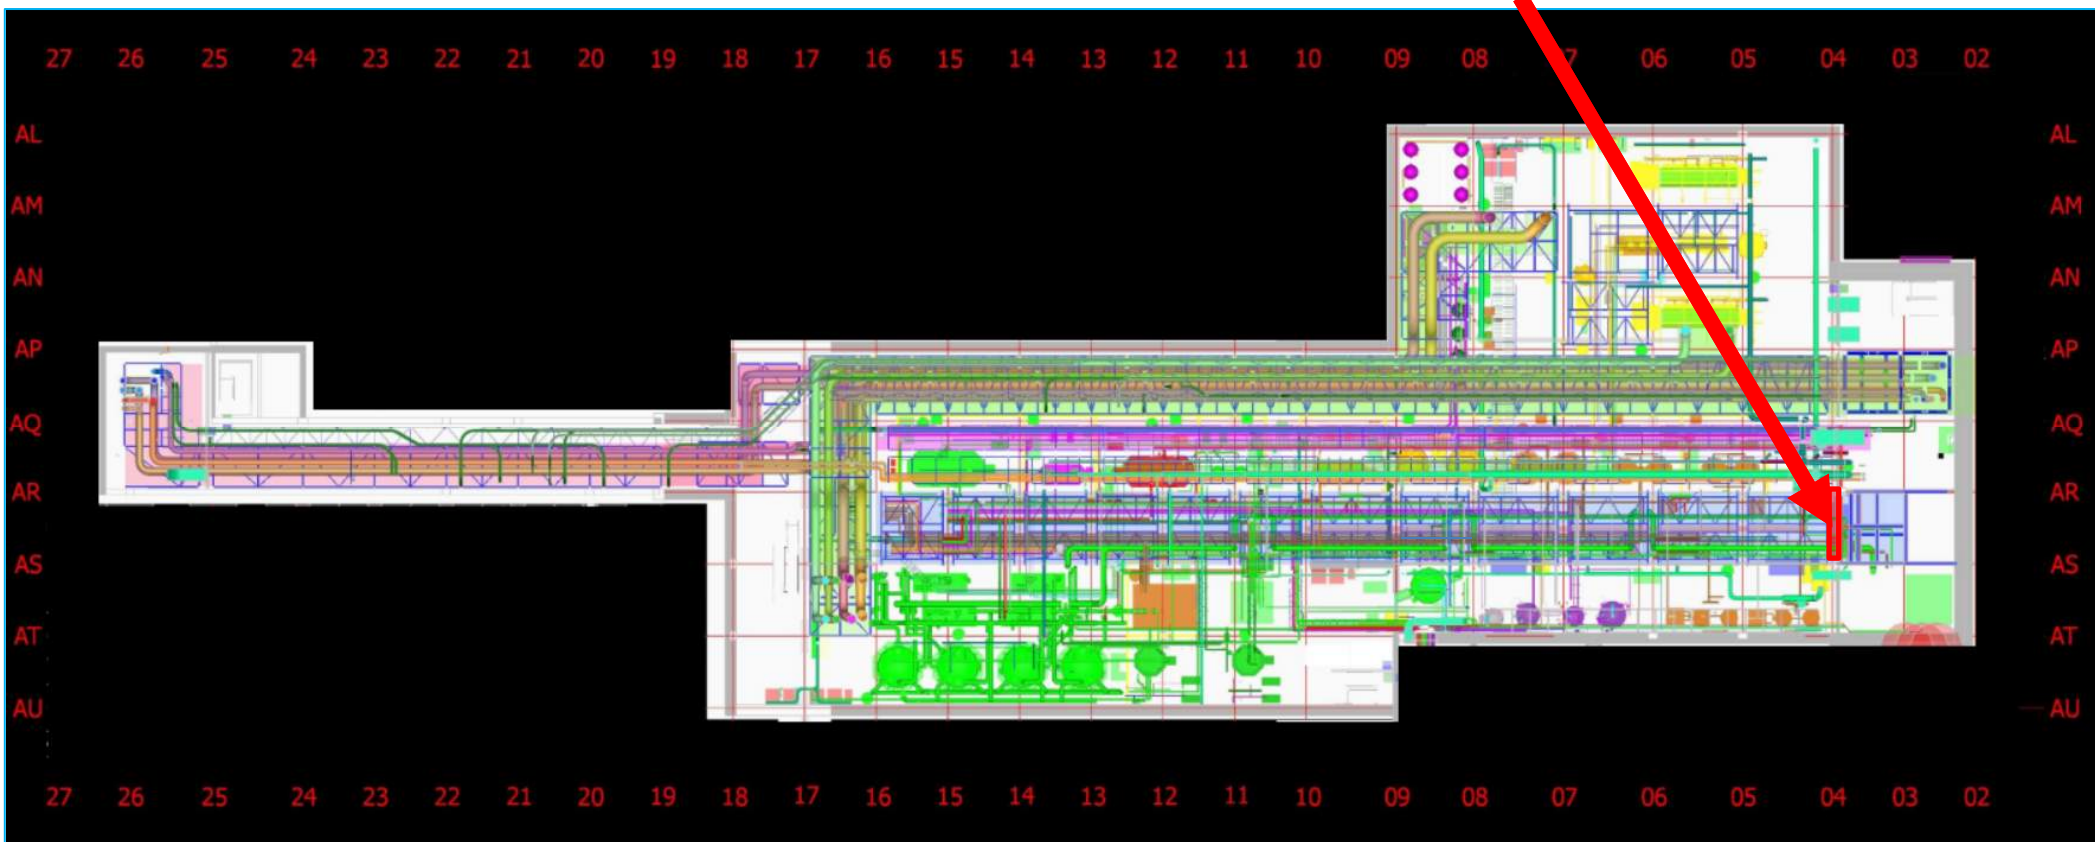





HOFFMAN CONSTRUCTION COMPANY




SUT 38.2 LEVEL

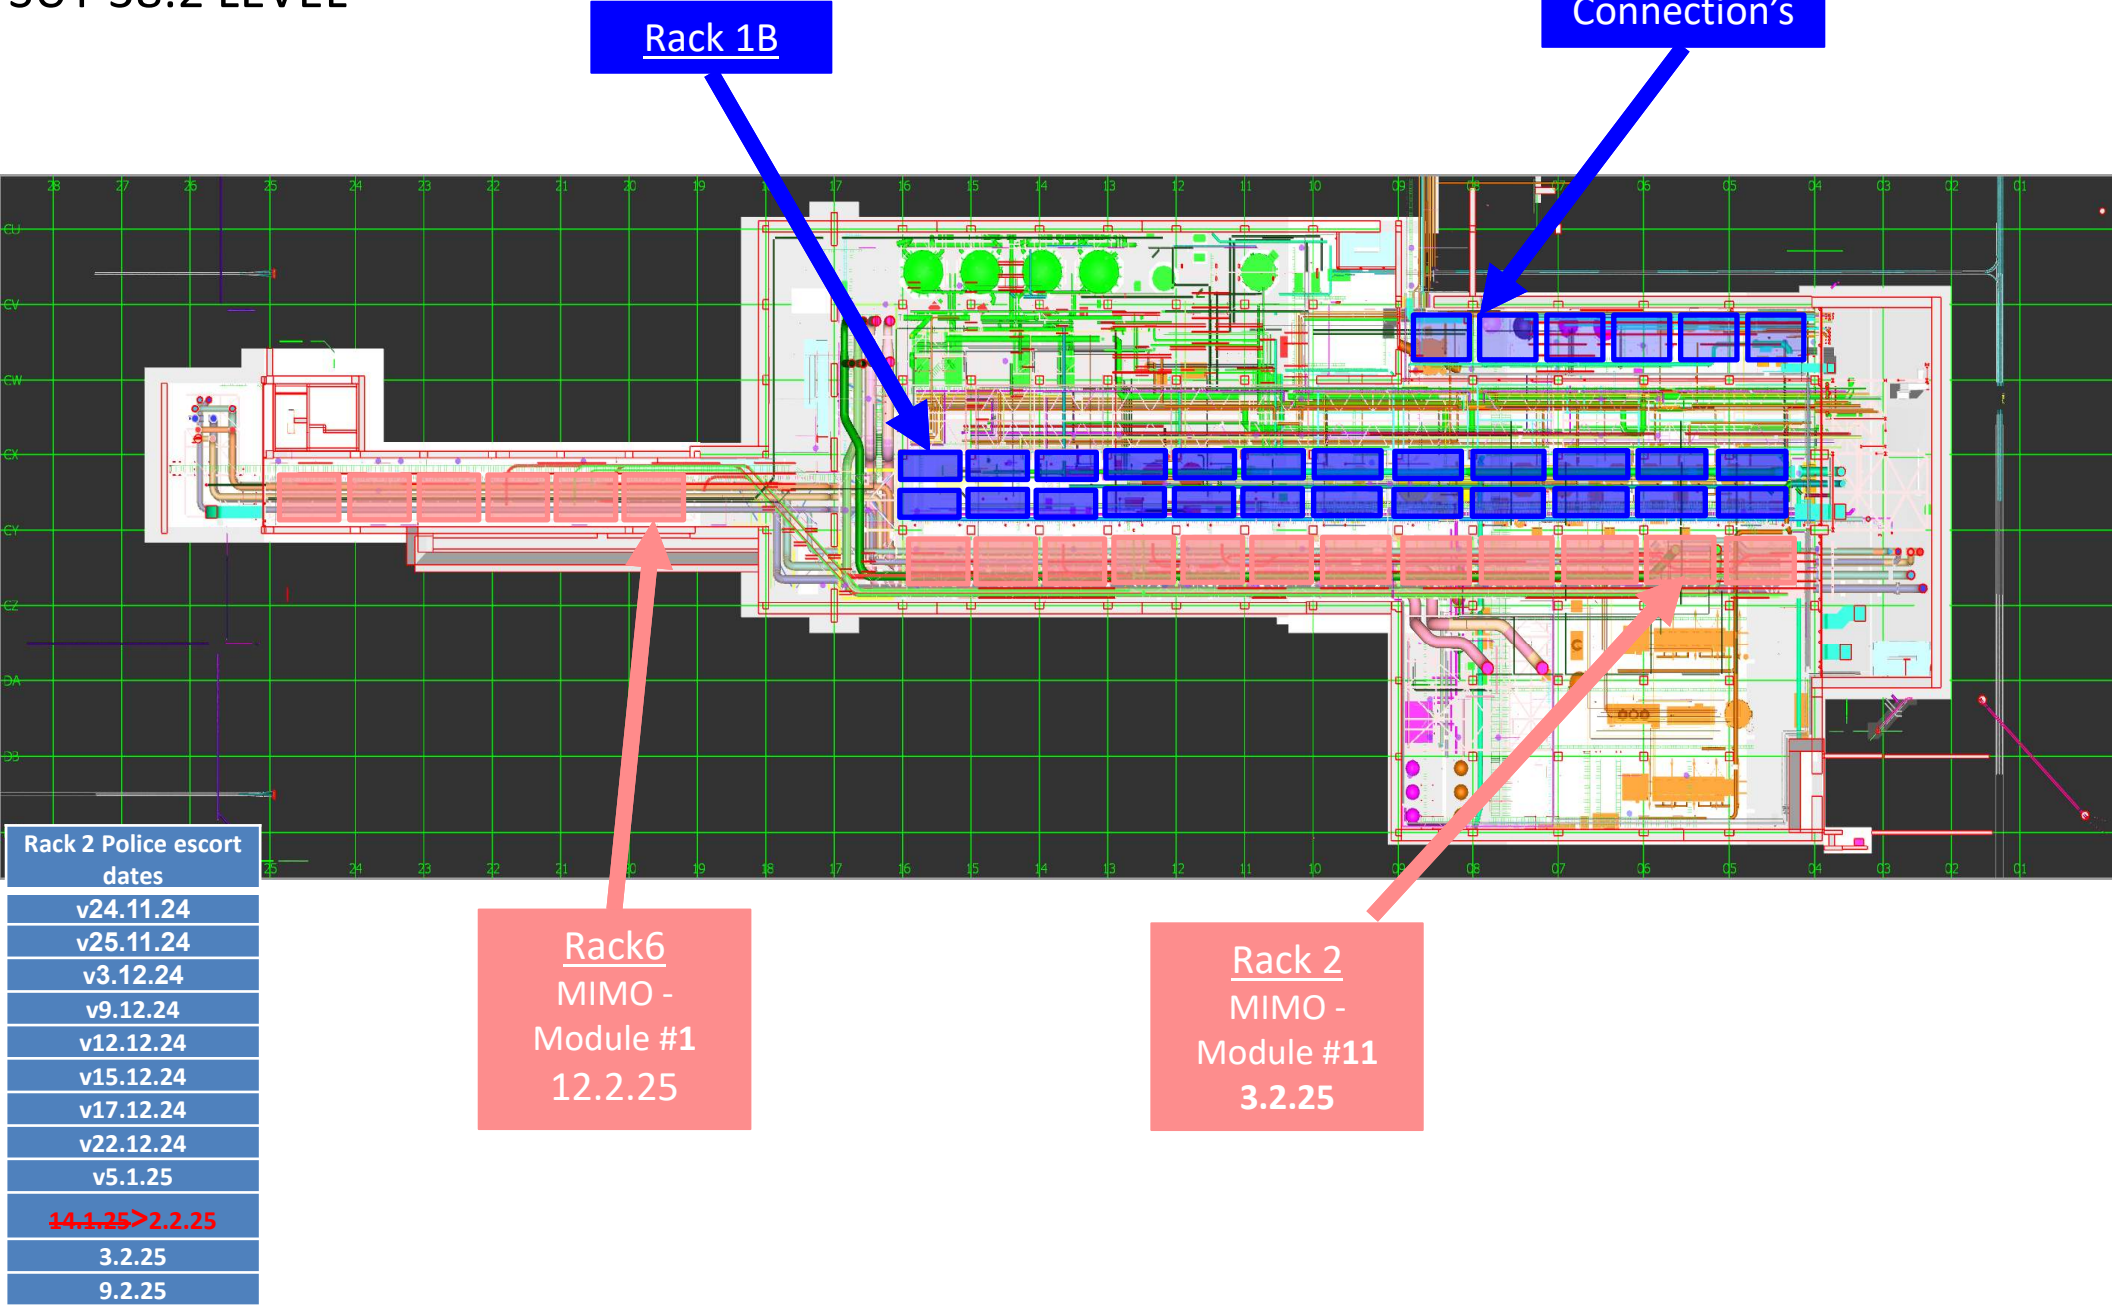


SUBFAB BUILDOUT MOD 1

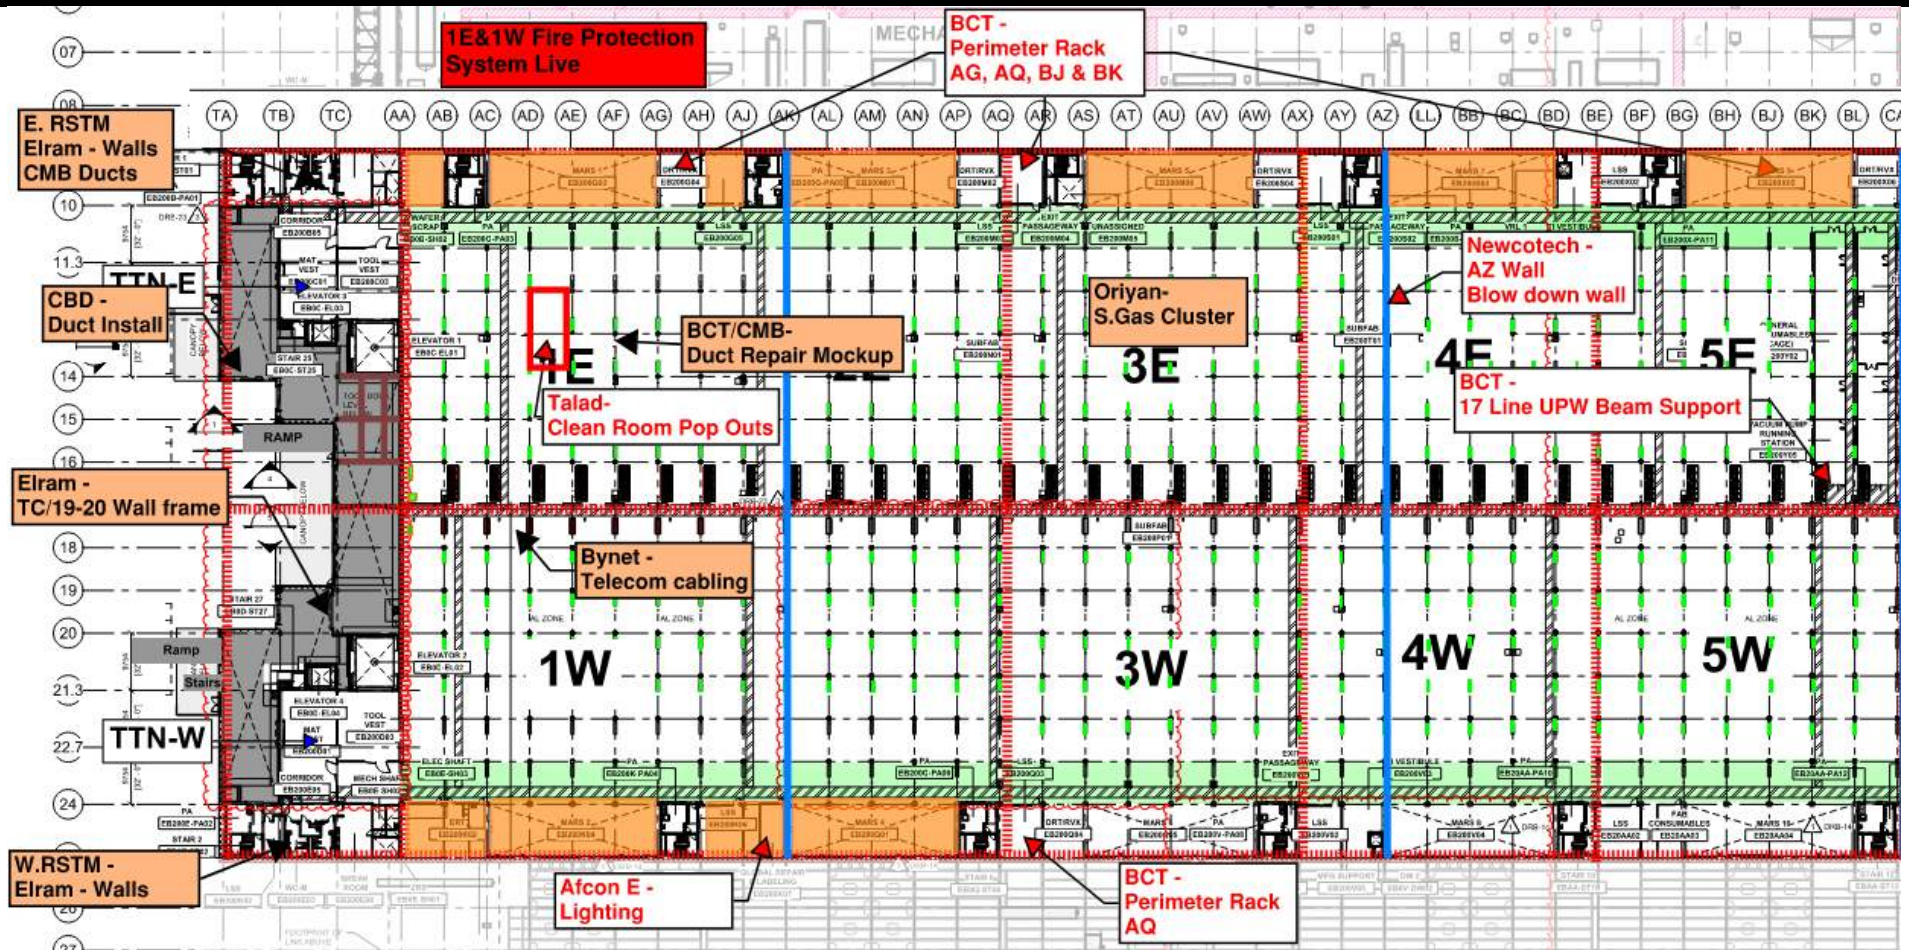



SUBFAB CRC TOPCOAT

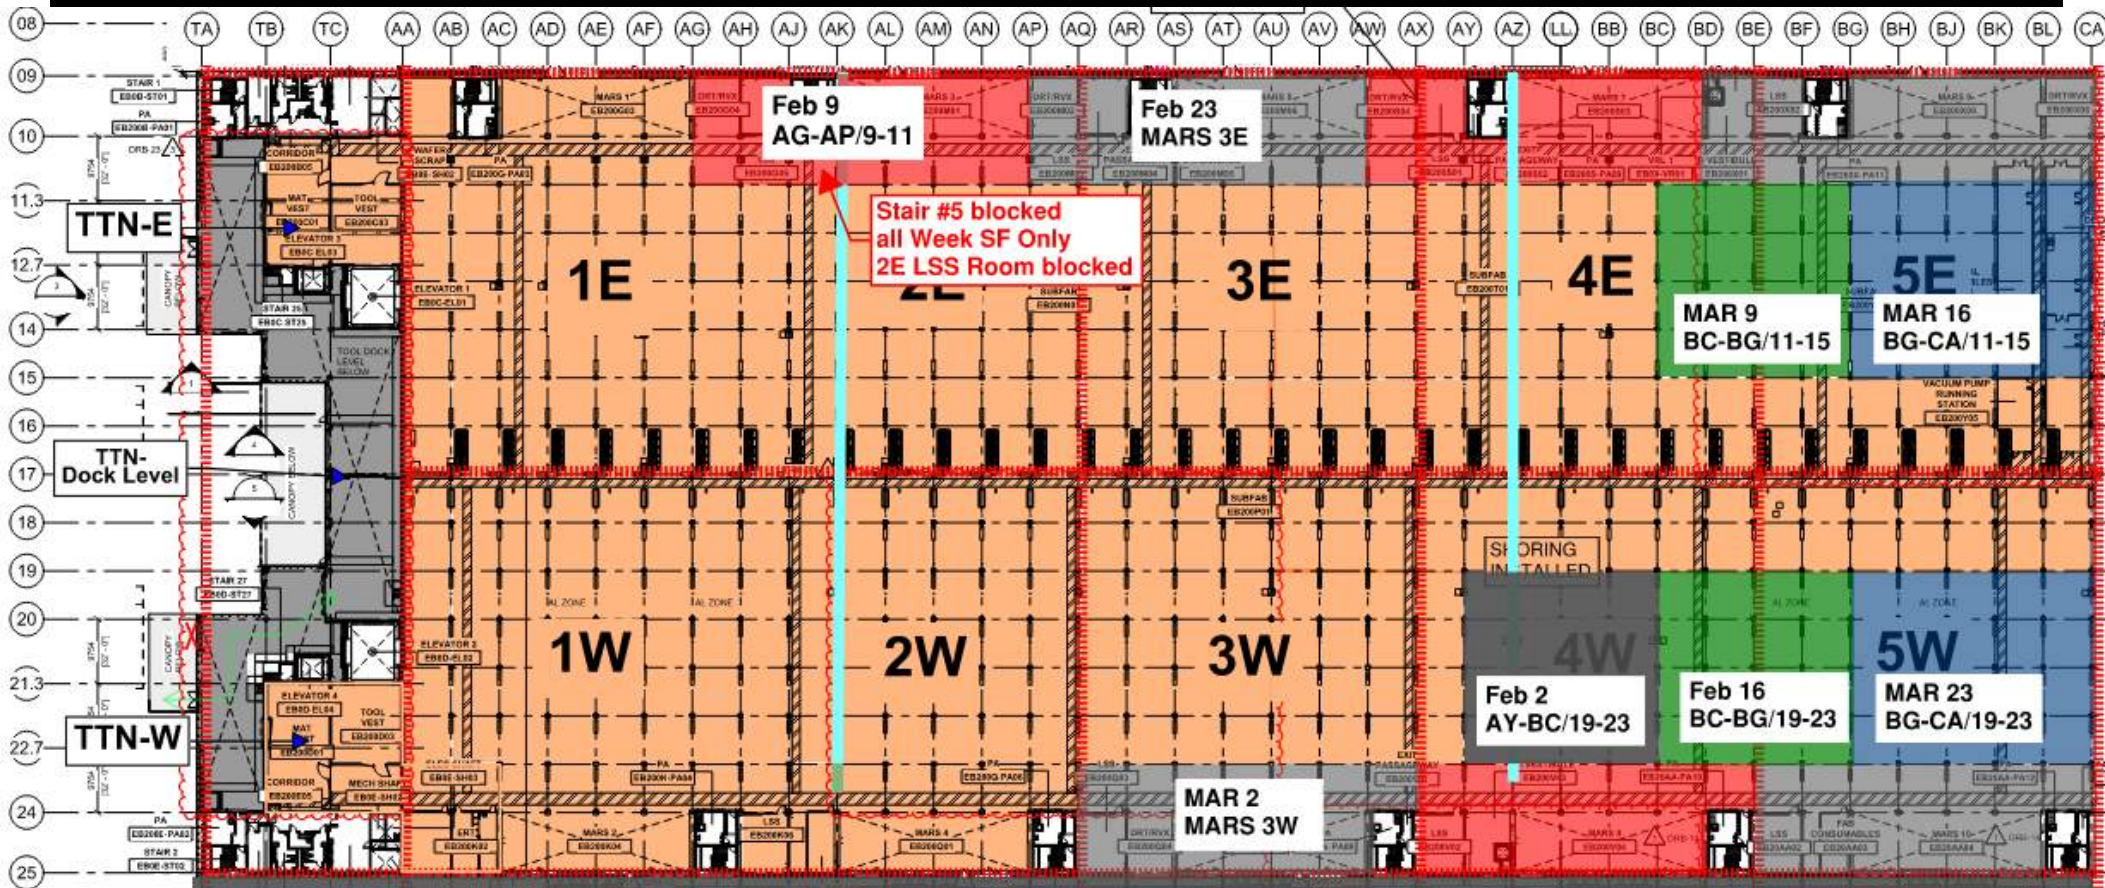


SUBFAB BUILDOUT MOD 2

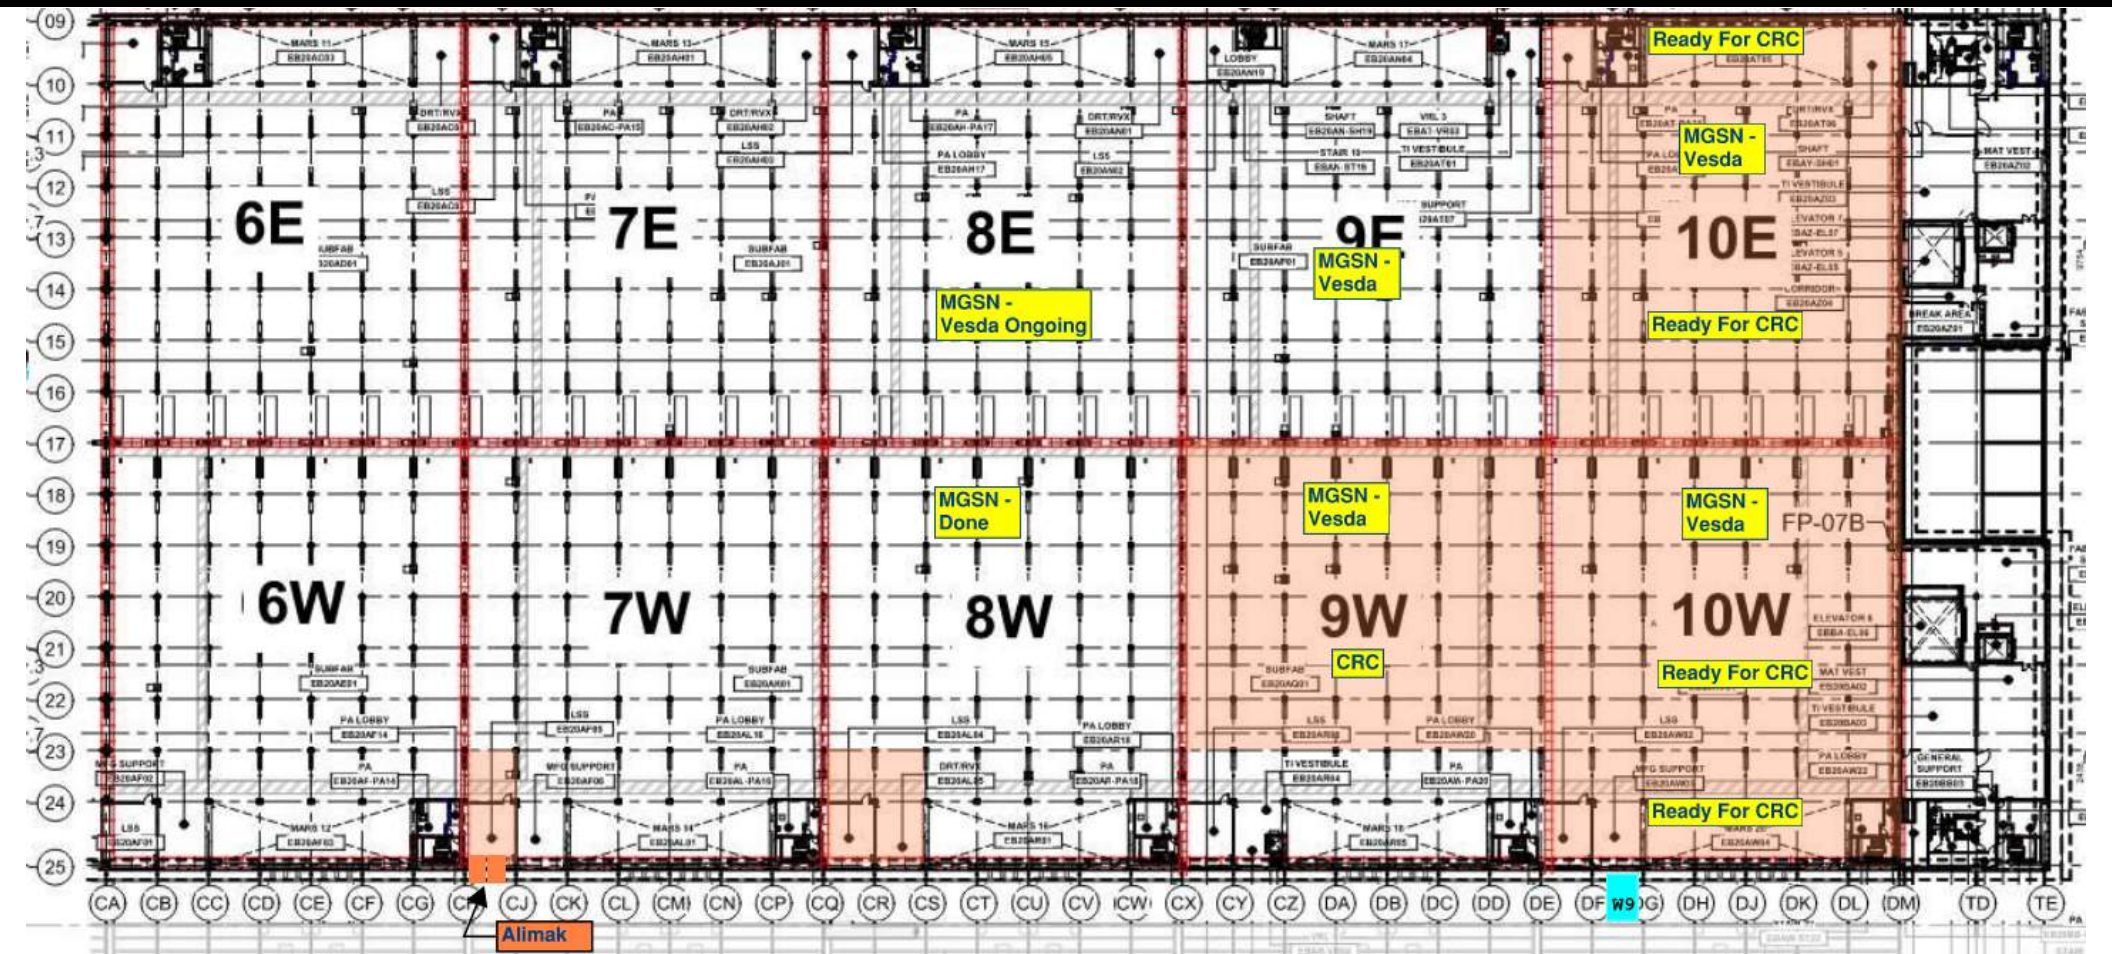

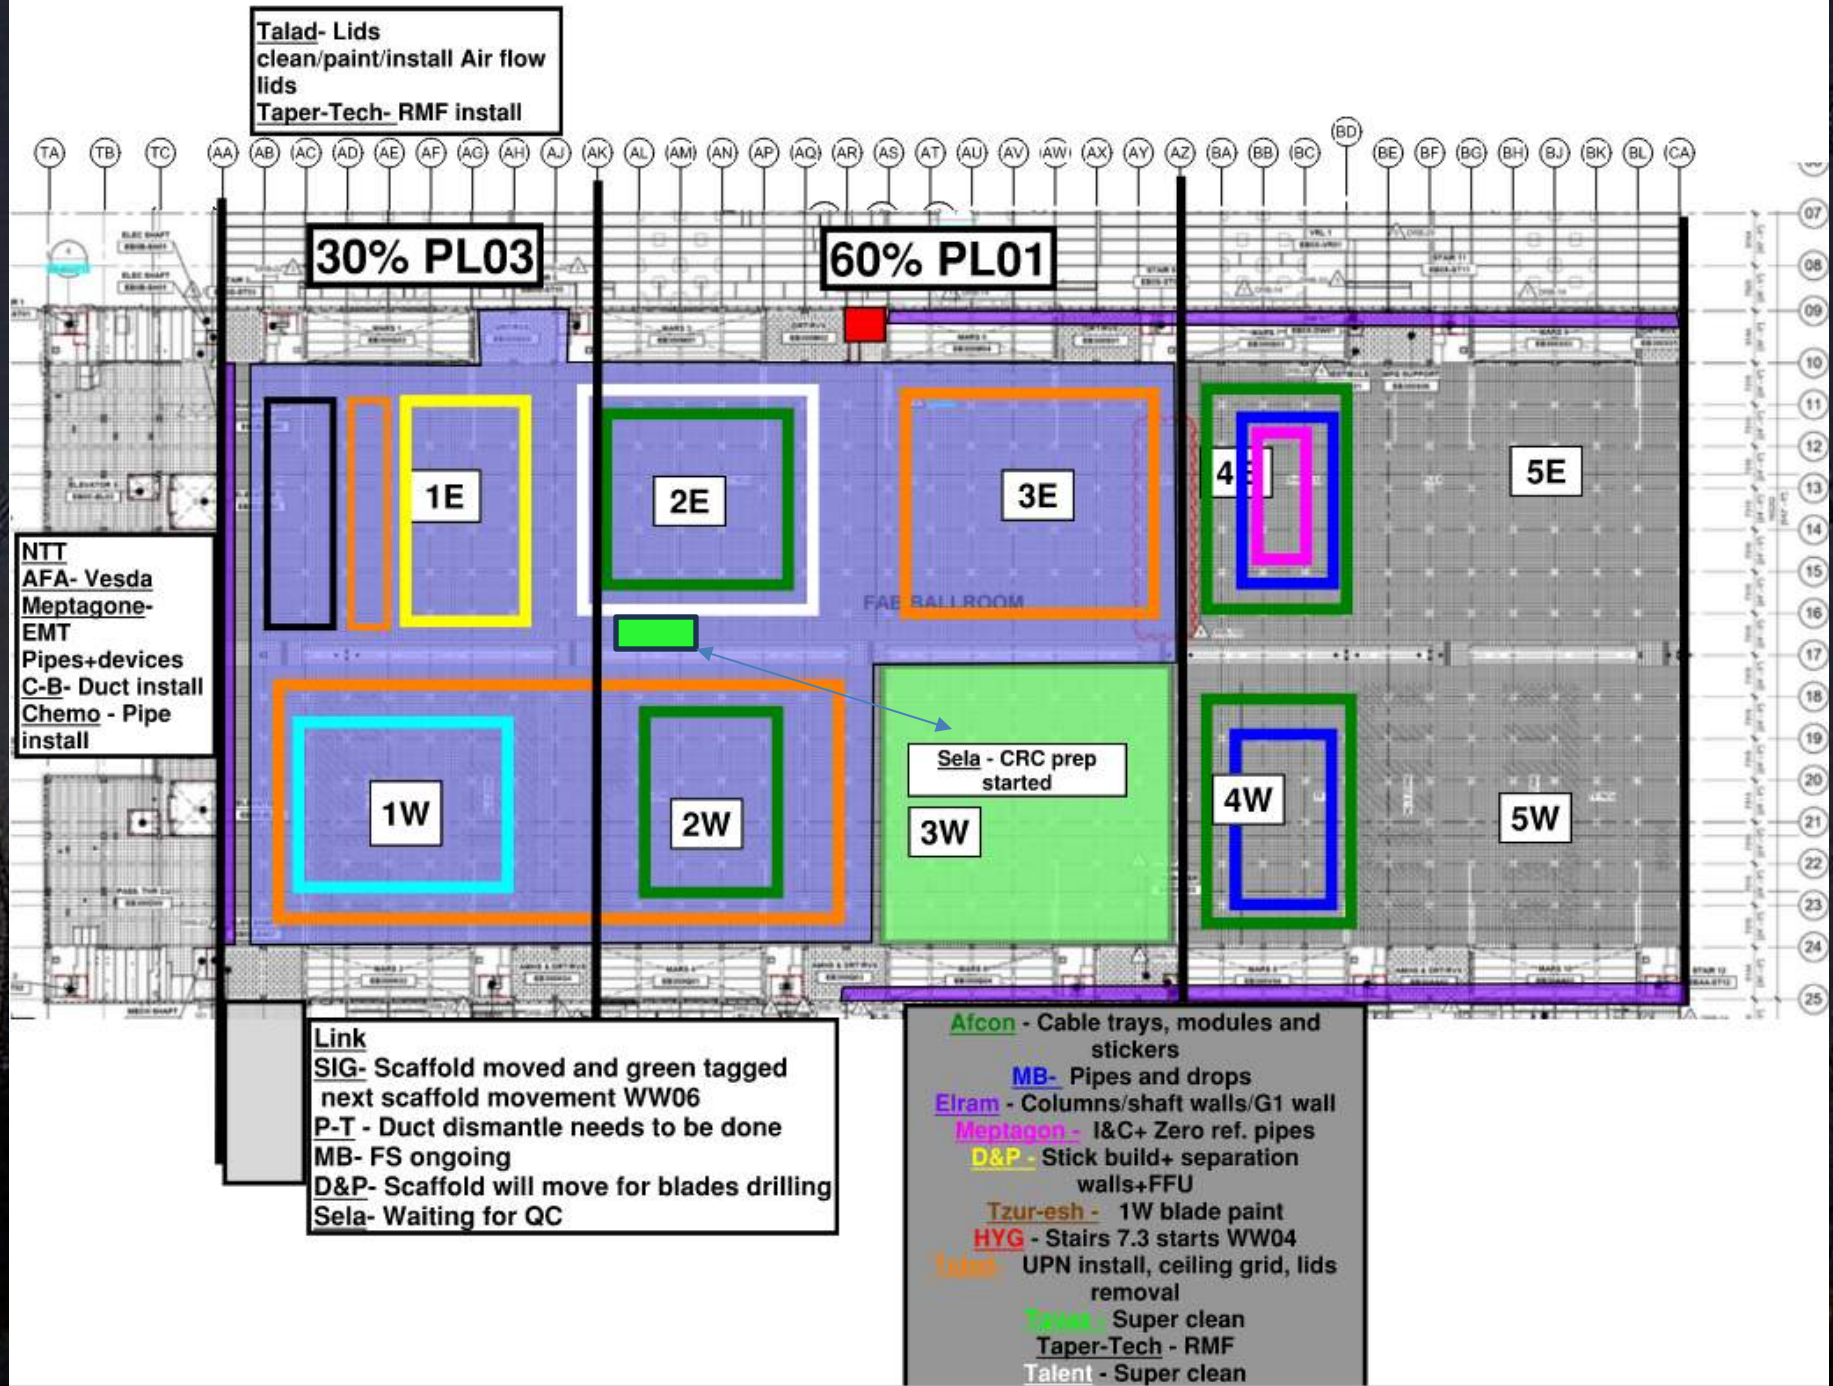


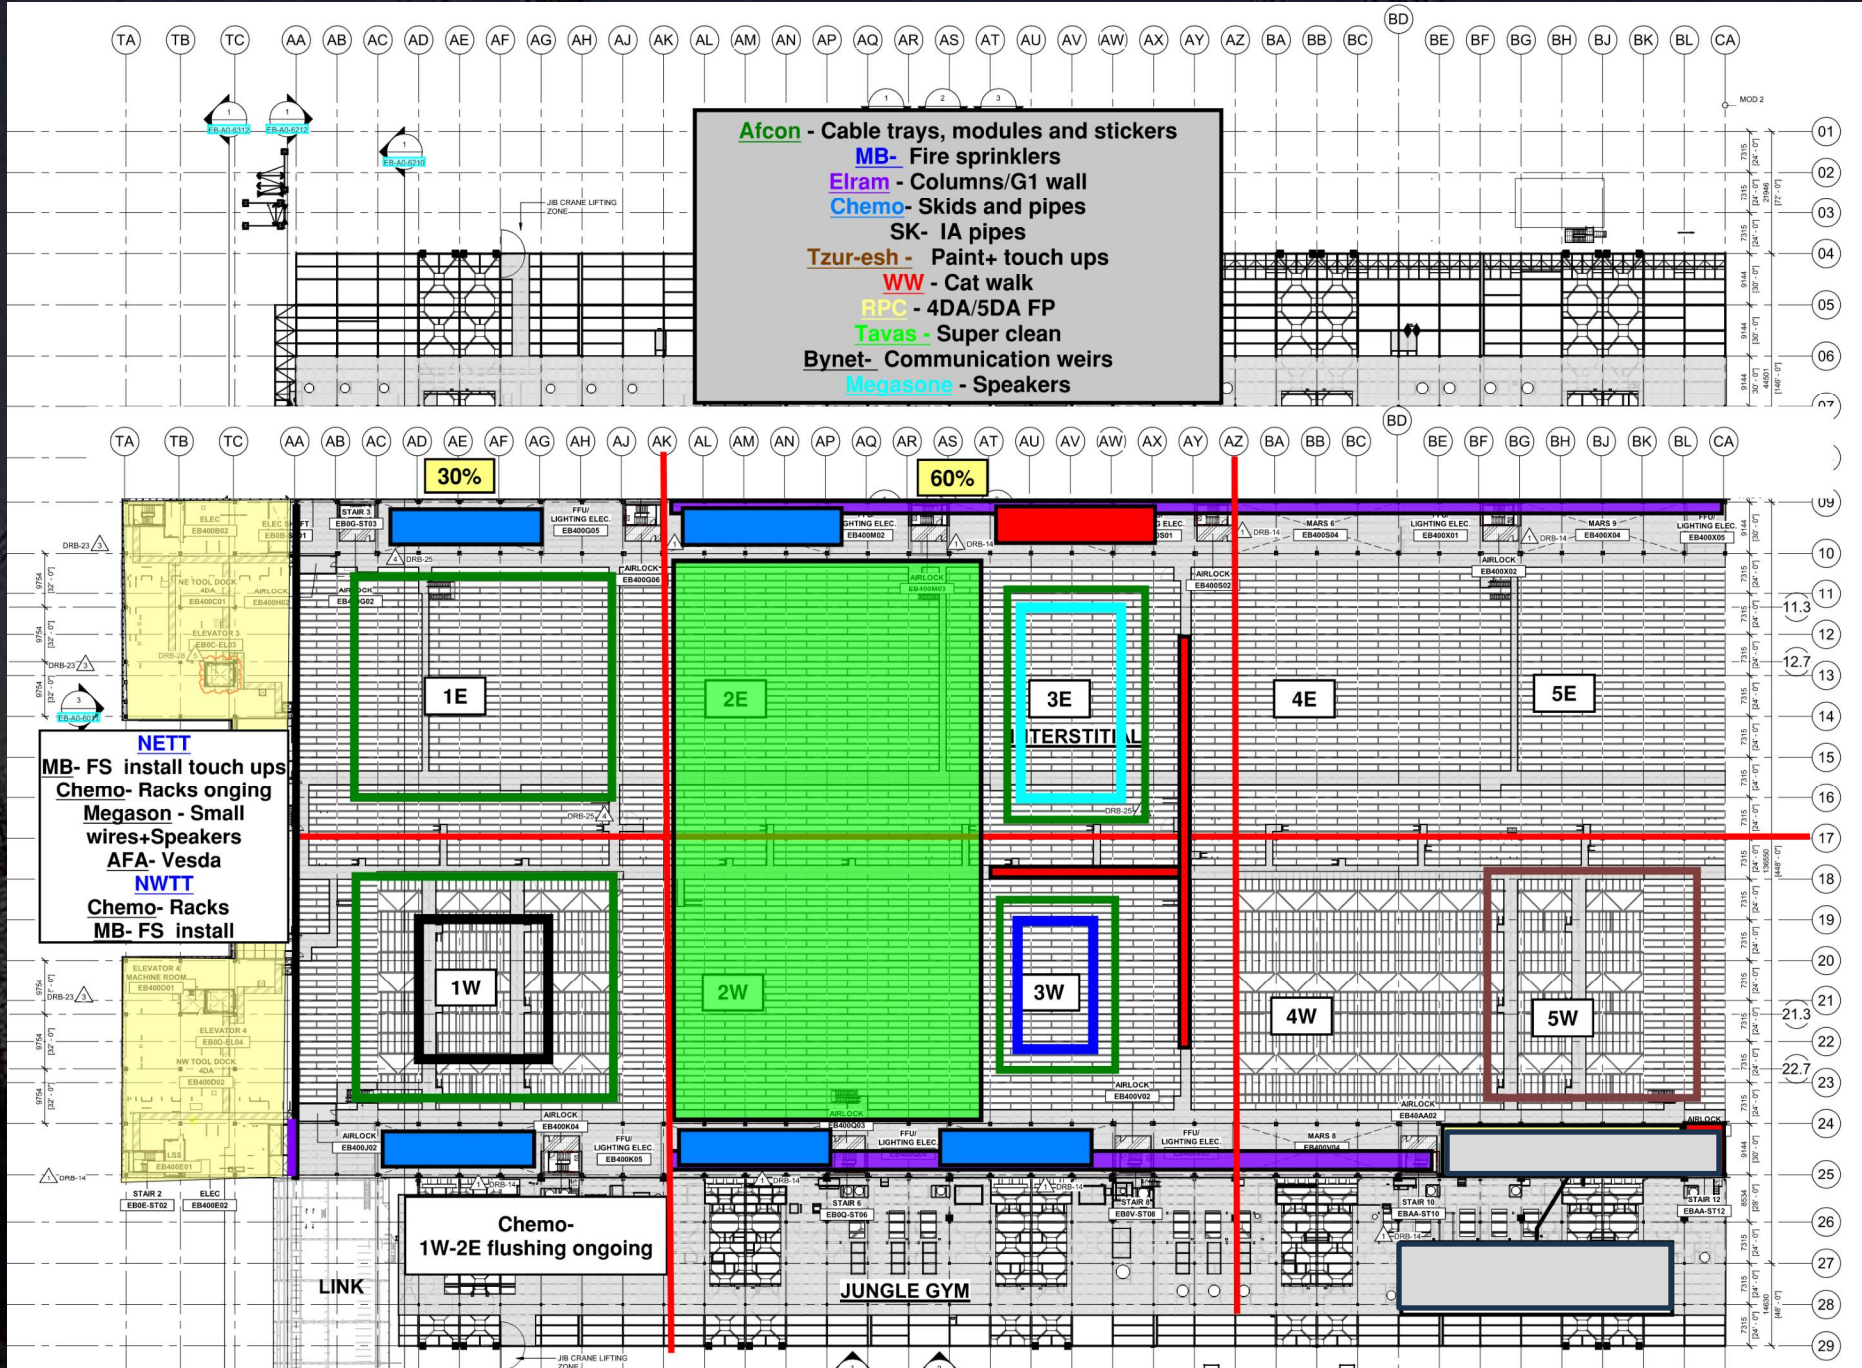

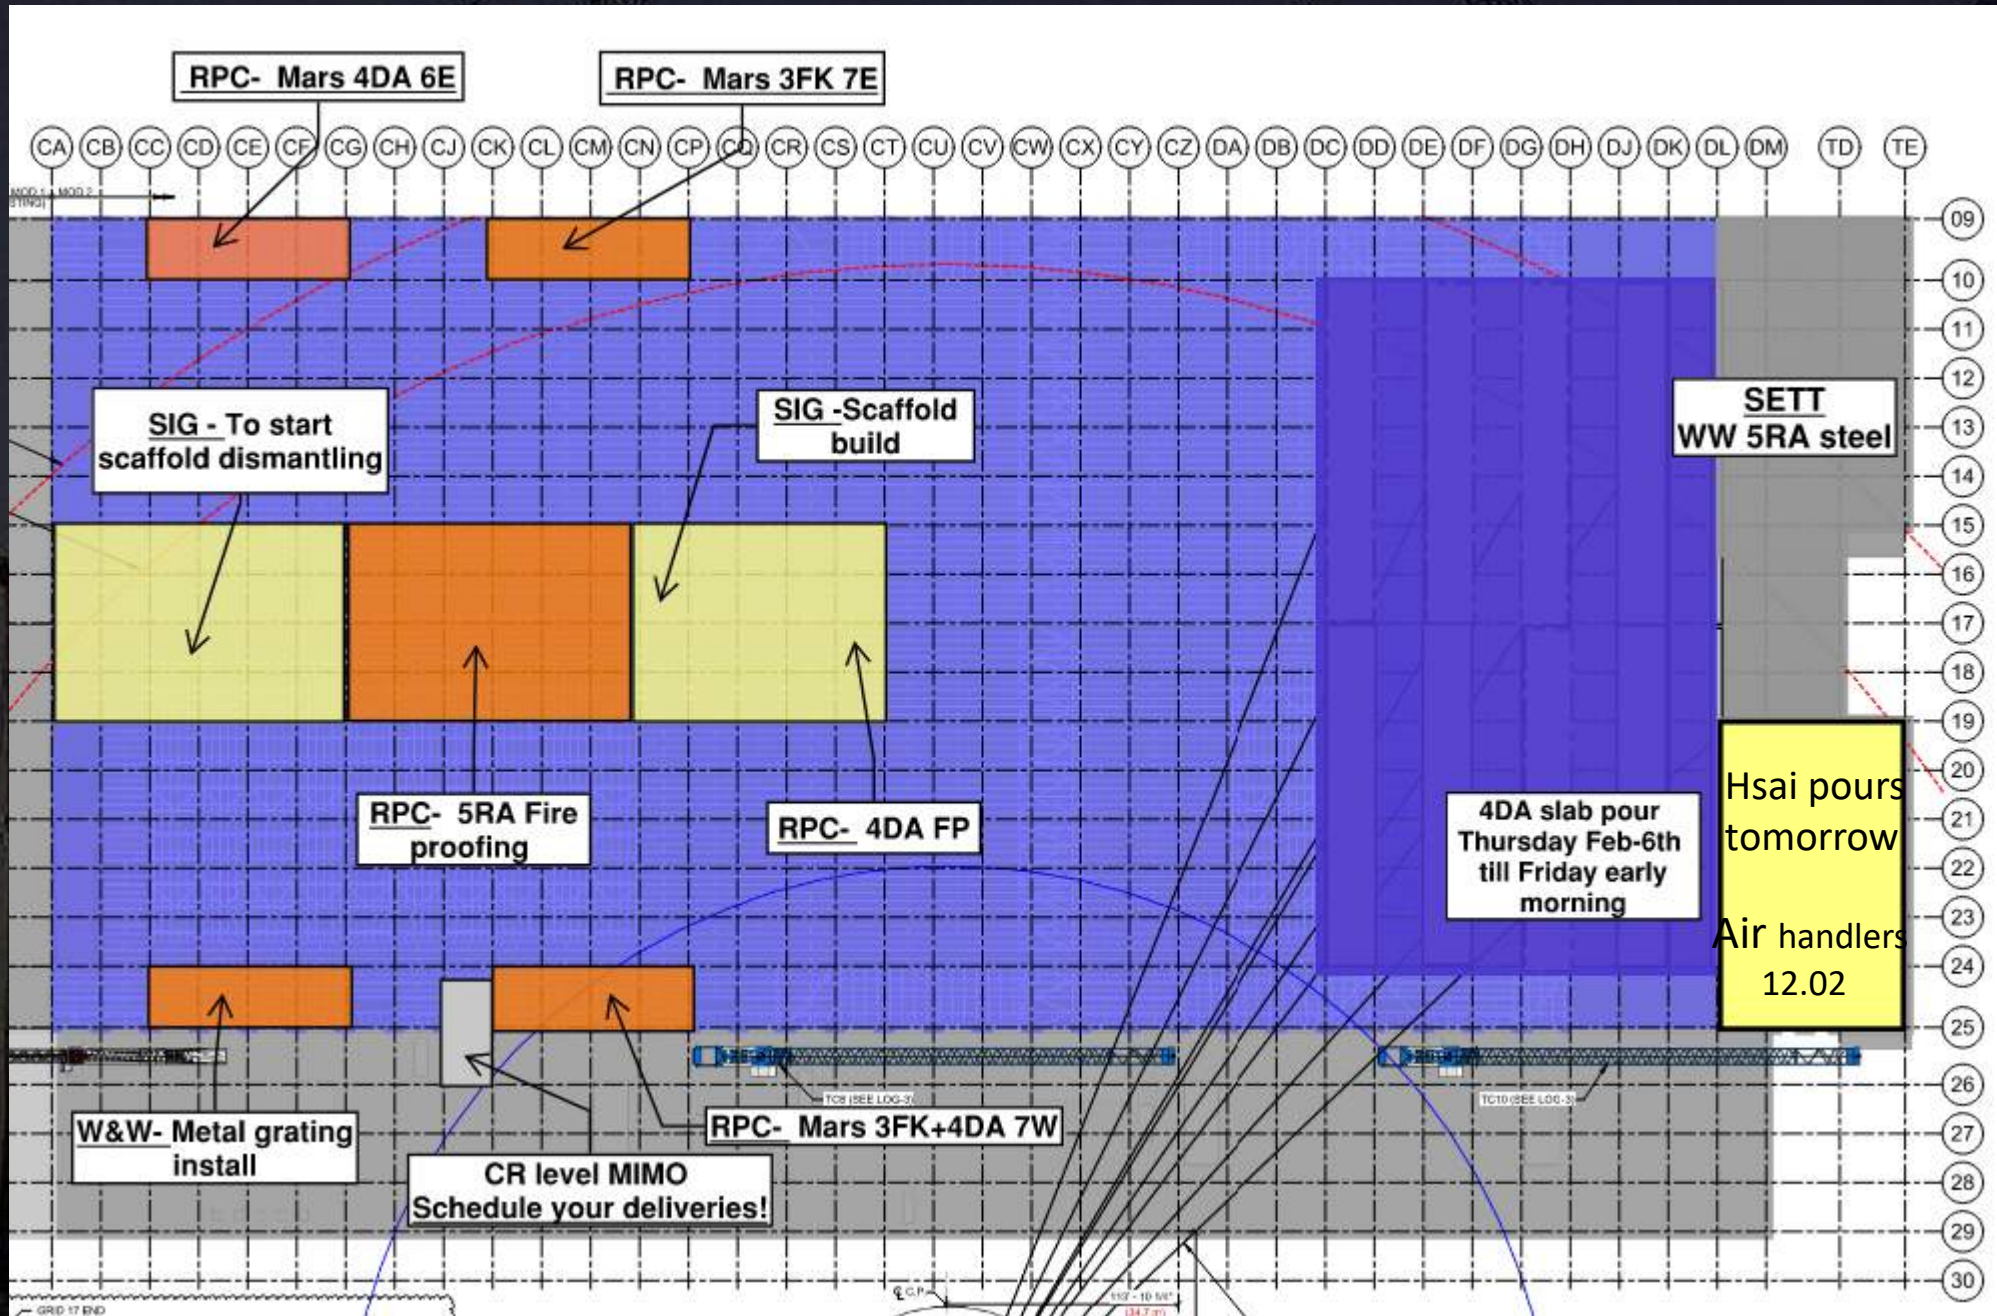



Alimak Shut Down
night Shift
Sunday + Monday
FEB/09~10
from 16:00 p.m till 05:00 a.m

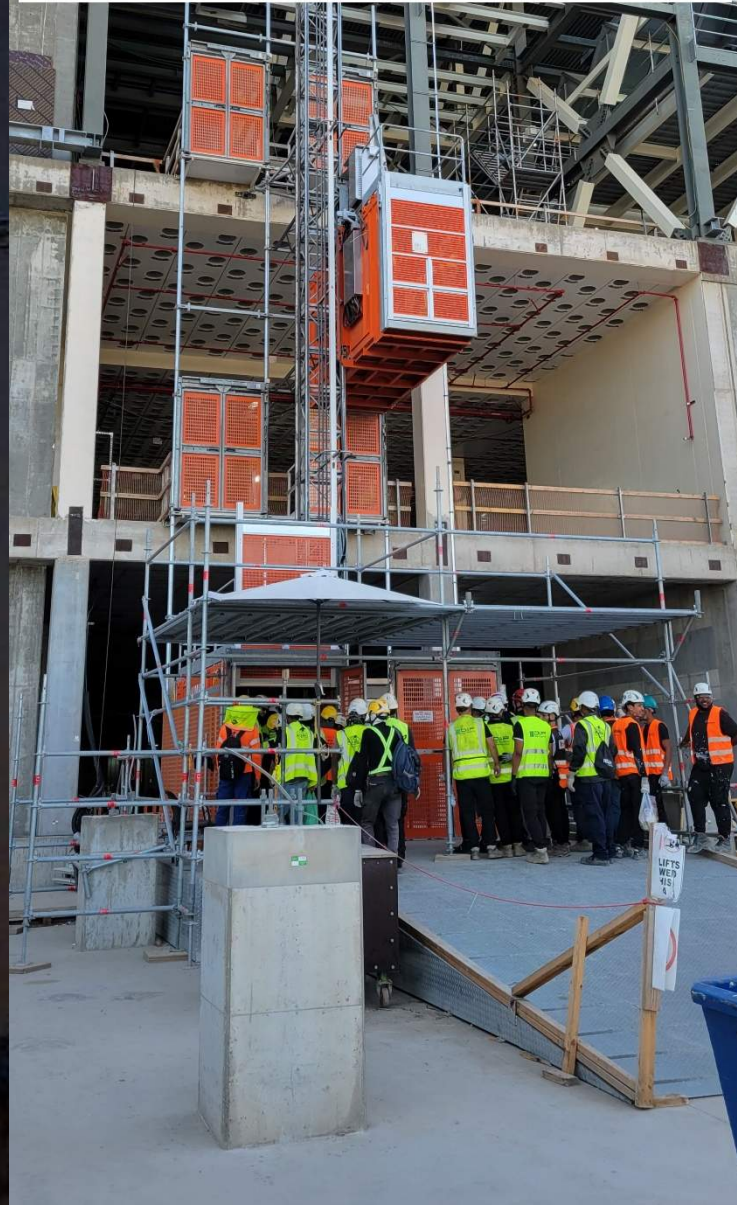

1.5 TON טון

ONLY **ELECTRICAL** PALLET JACK ALLOW


עומס שימושי מותר על הרמפה עד 500 קילו !!!


עומס מקסימלי על המעלית 1.5 טון



Maximum load on the ramp up to 500kg

Maximum load on the ALIMAK 1.5 ton

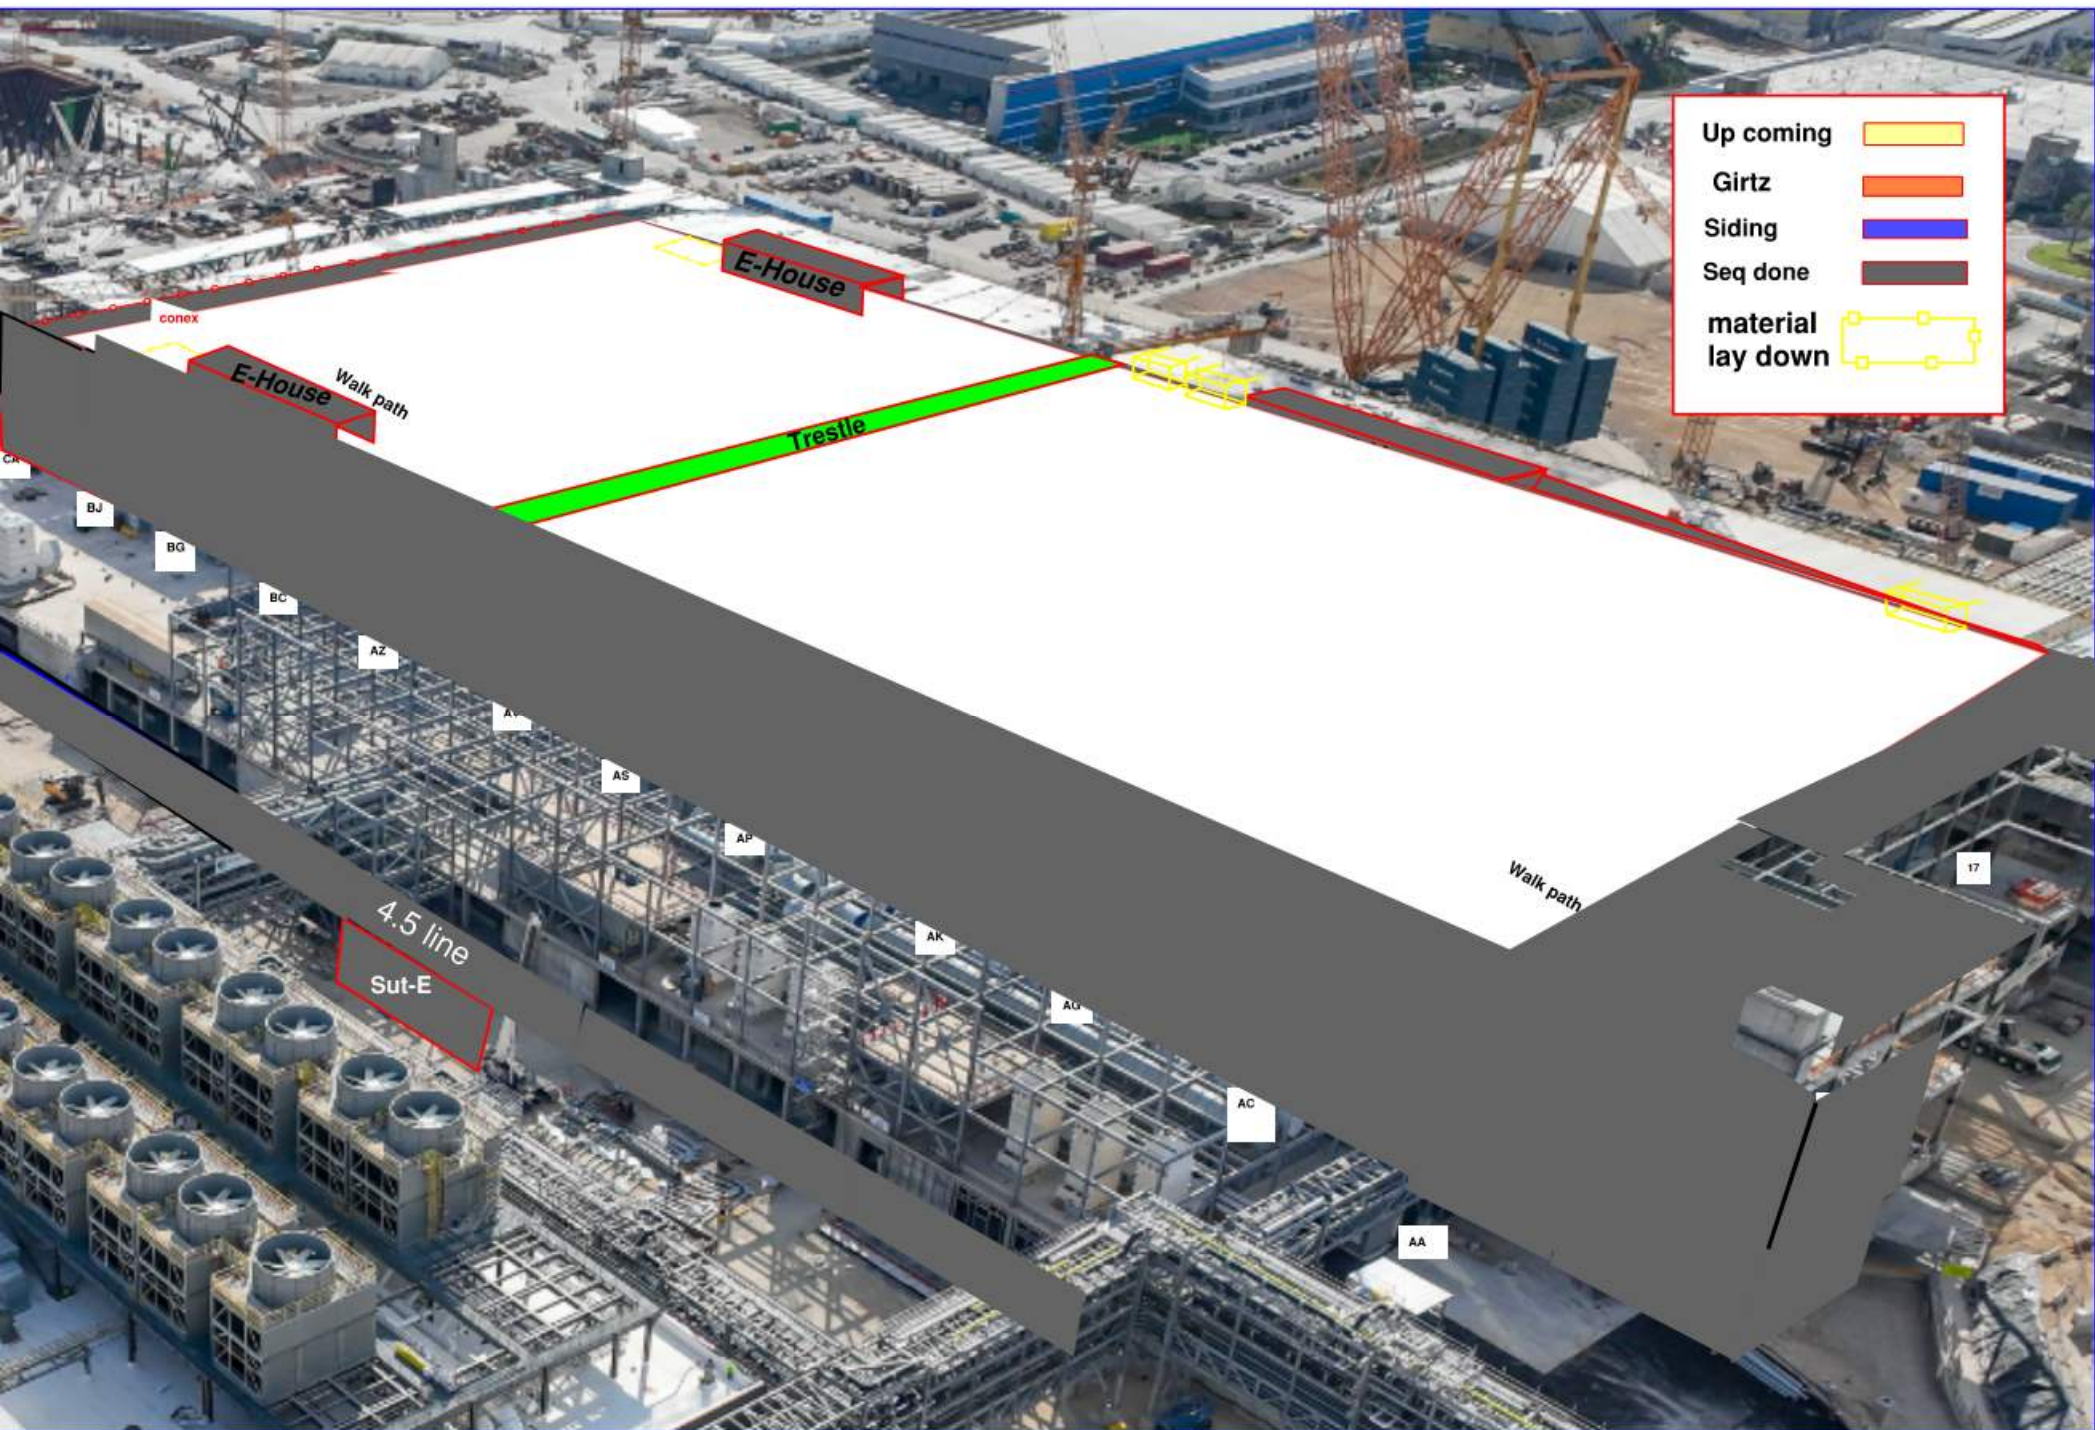

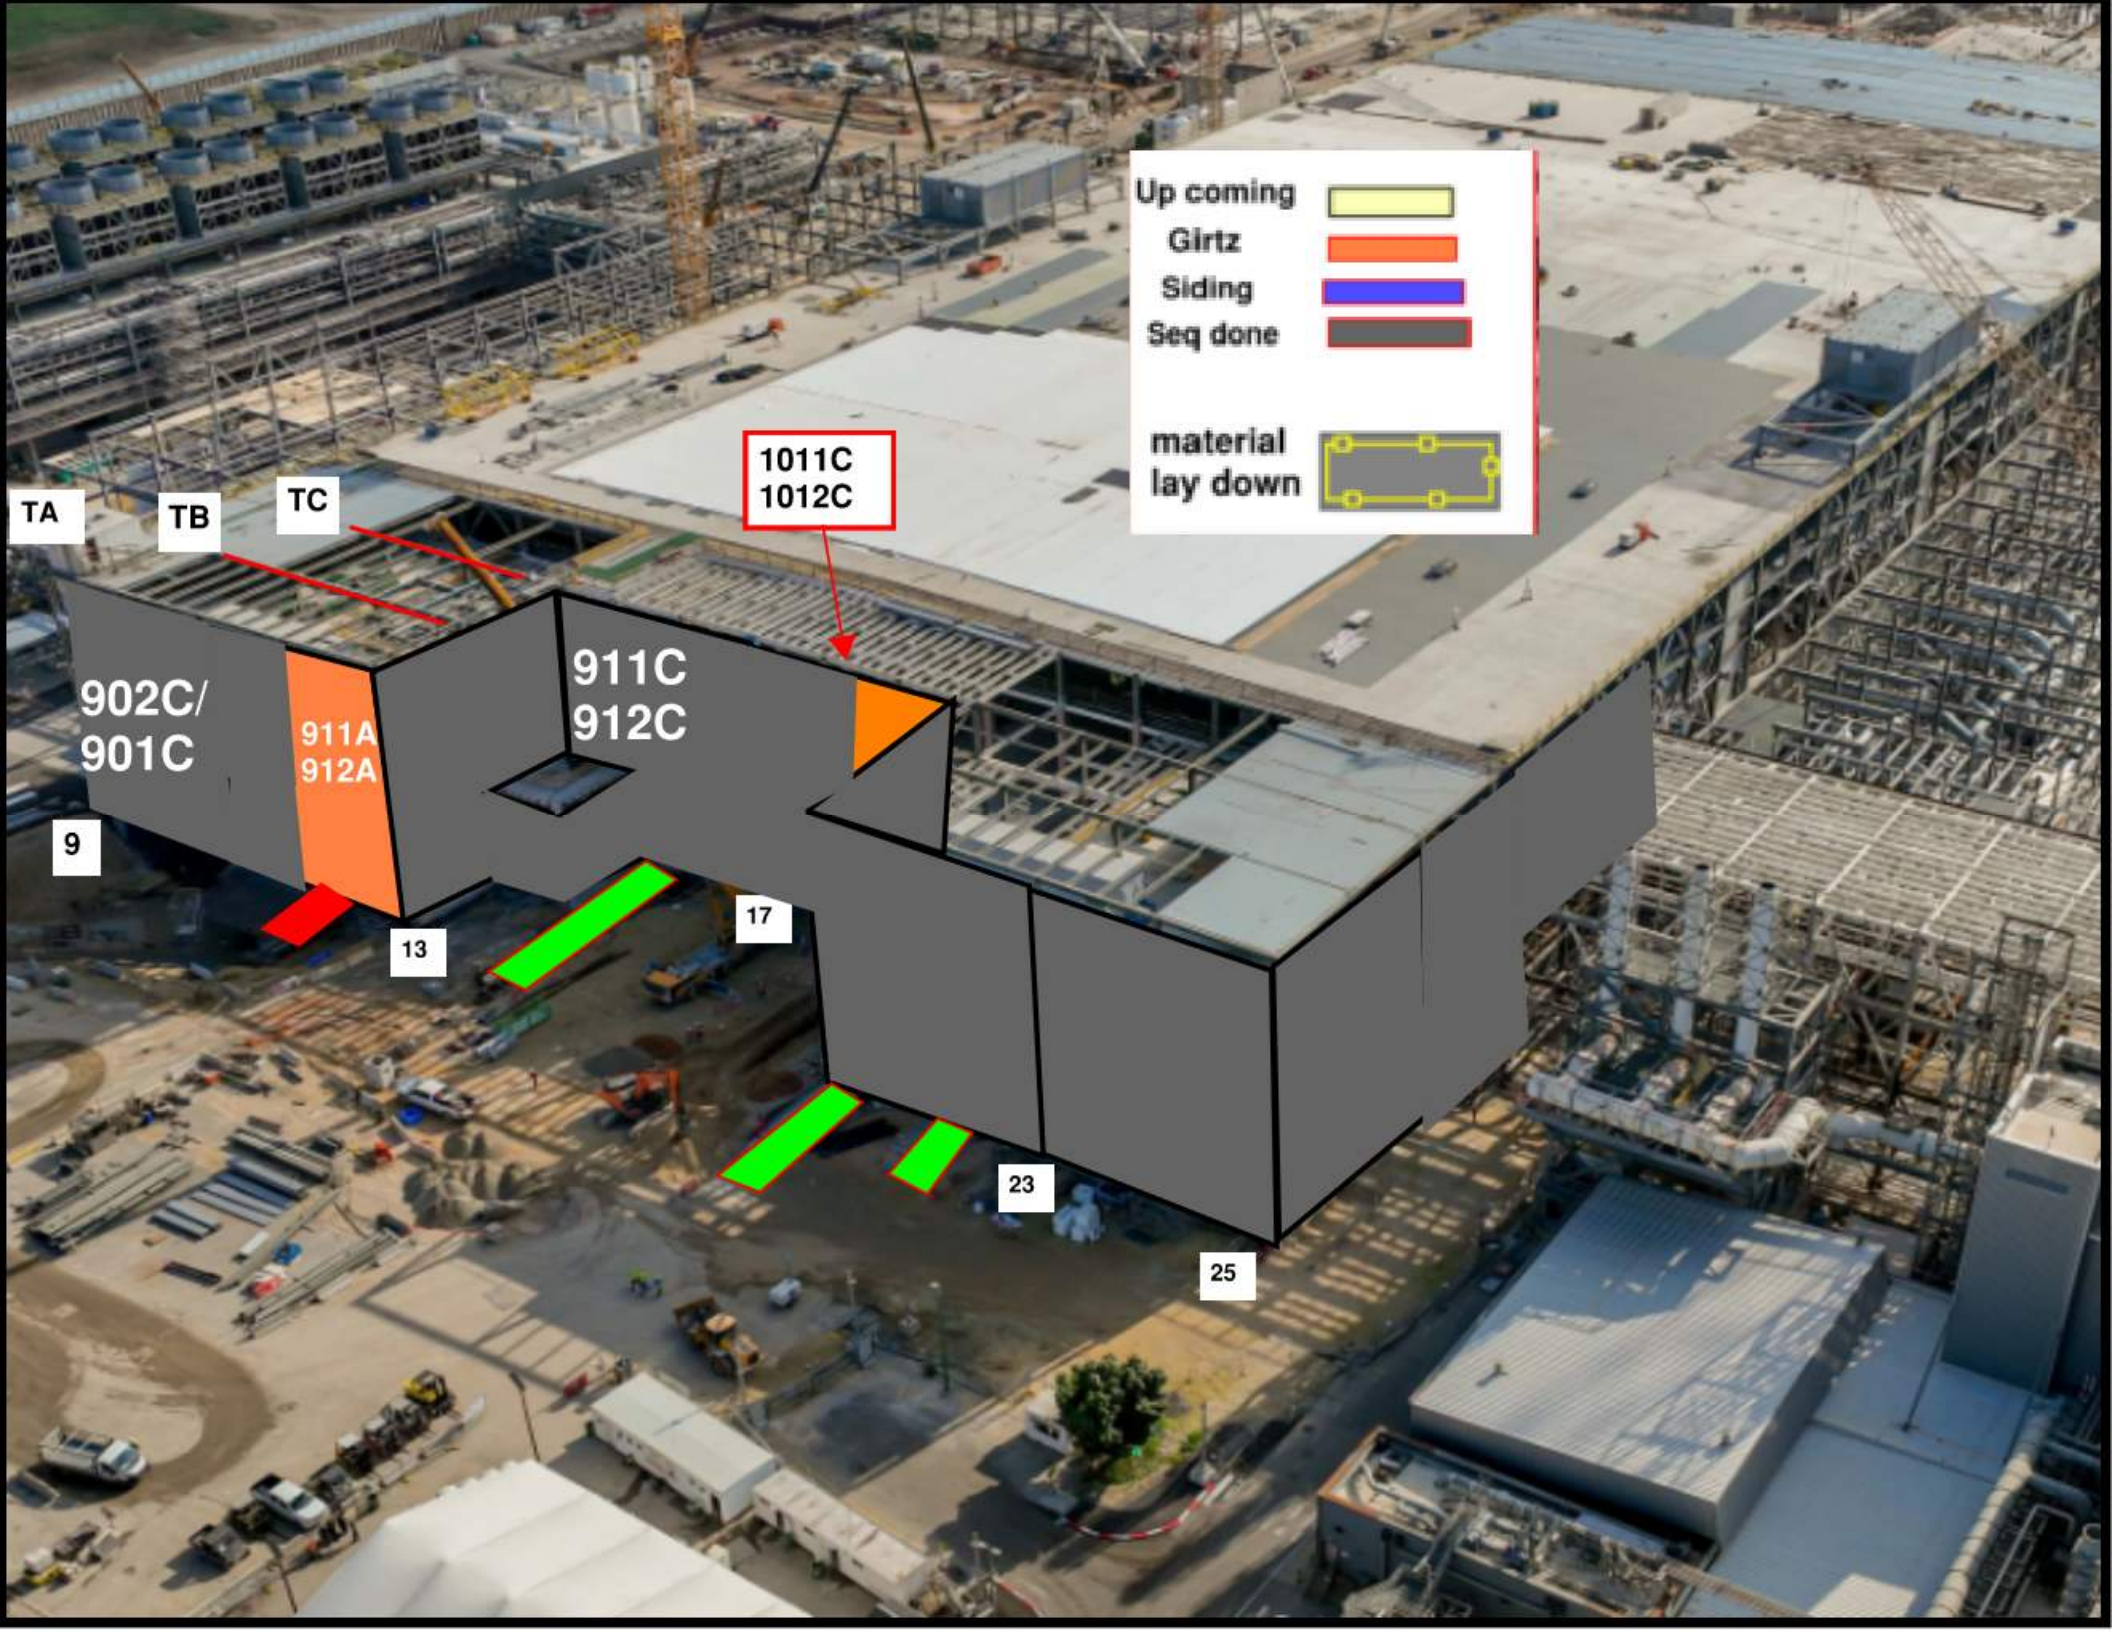

Up coming



Girtz




Siding



Seq done



material
lay down



1011C
1012C

TA

TB

TC

902C/
901C

911A
912A

911C
912C

9

13

17

23


25



PSSS.1


Utility Level 1YA

PSSS Roof 2SA

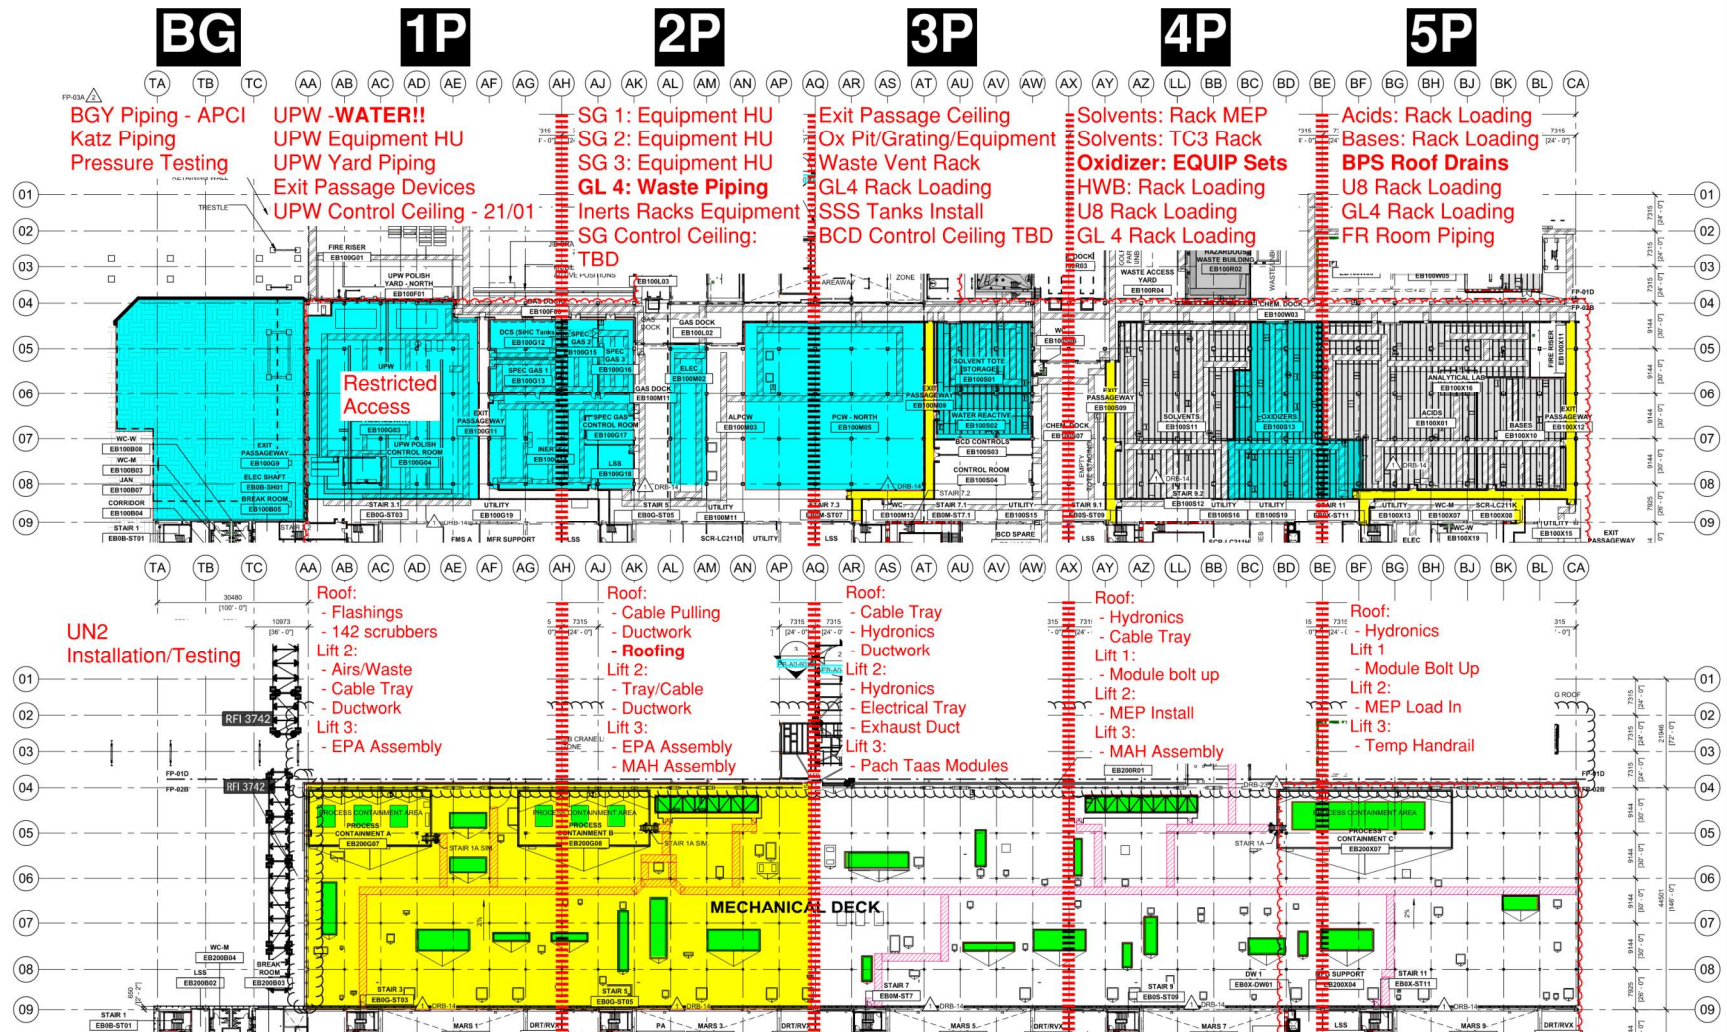


PSSS.2


Utility Level 1YA

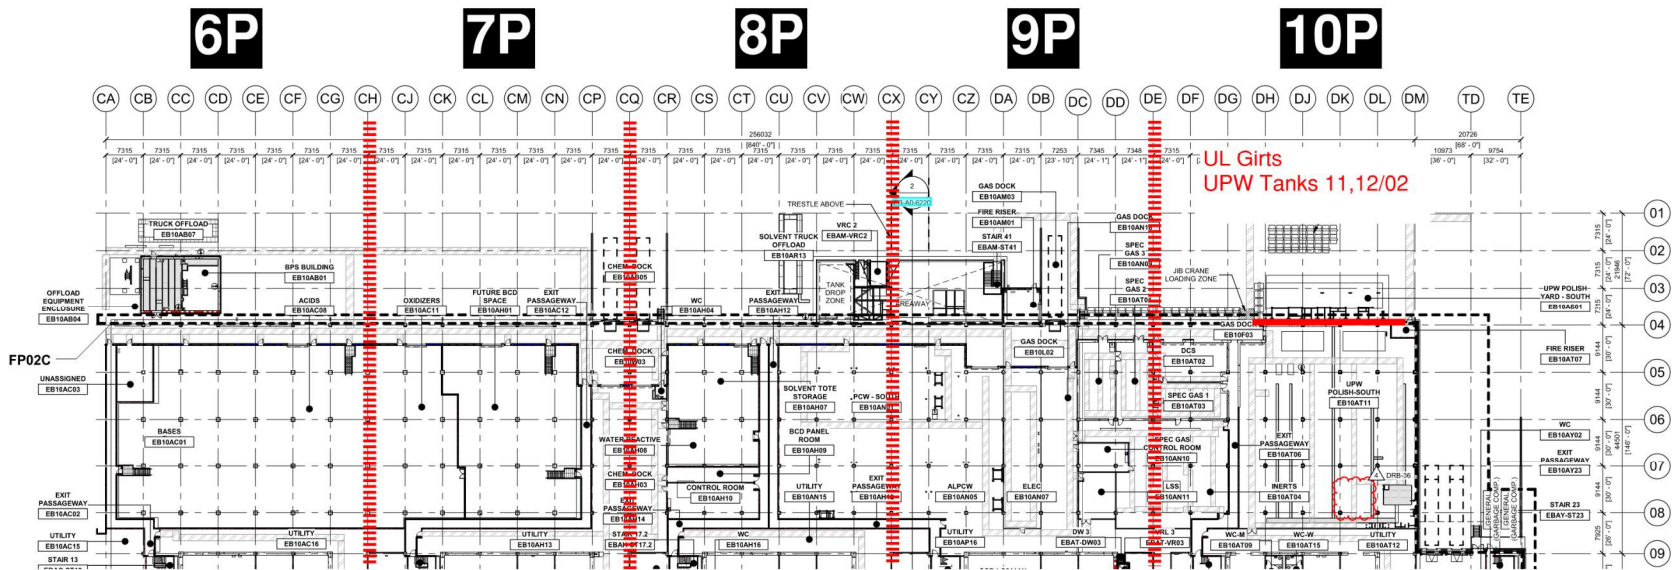

PSSS Roof 2SA

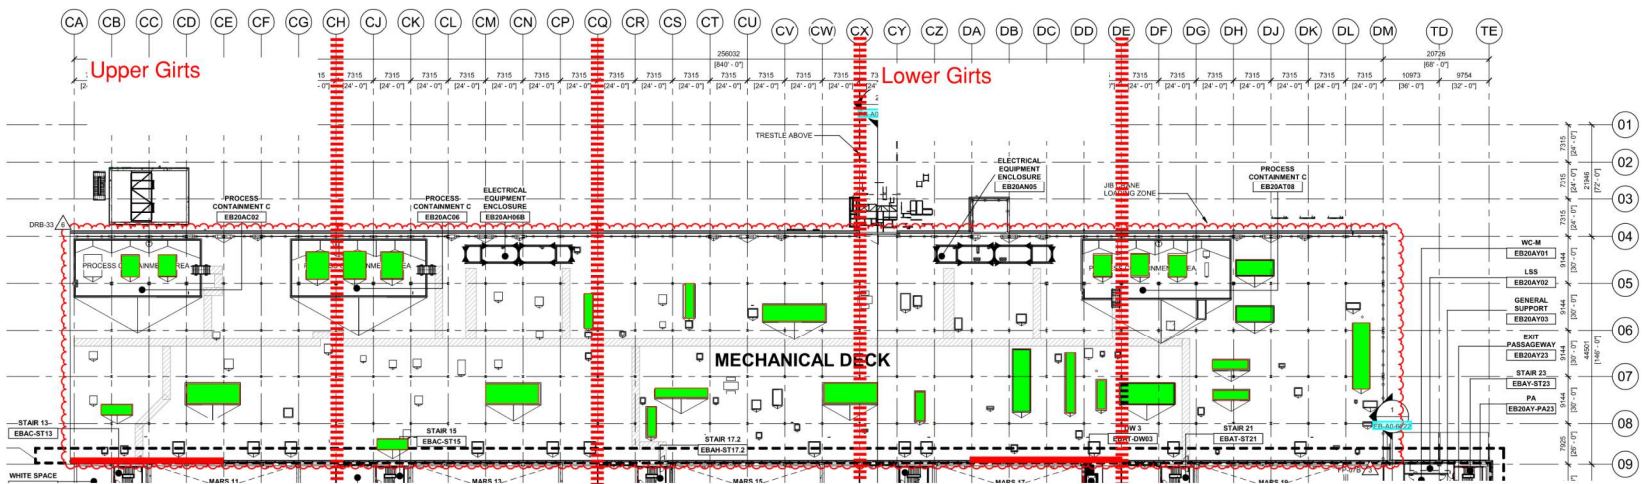

PSSS 05/02 Pressure Tests

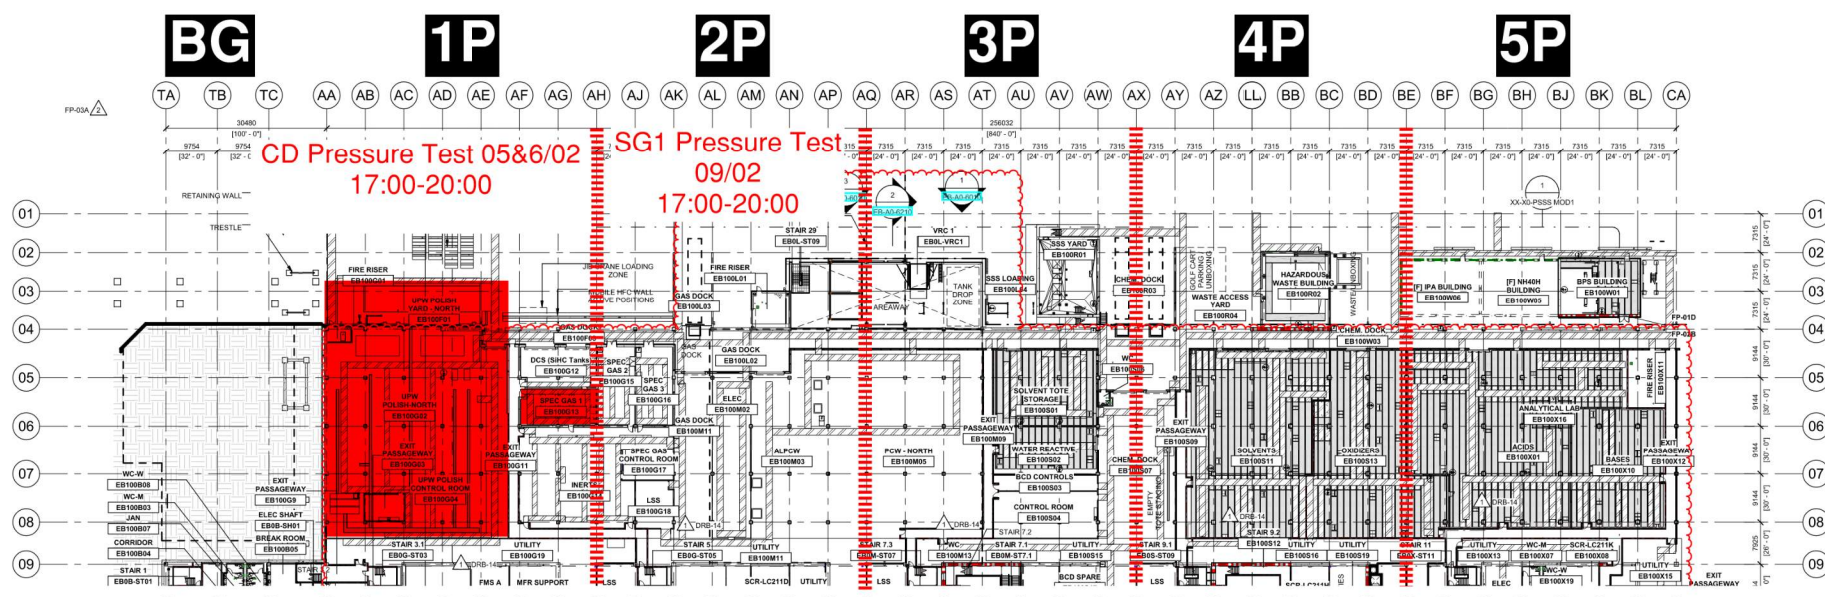

Utility Level

1YA


H2 Vent Pressure Test


05&6/02 17:00-05:00




PSSS Jungle Gym
Closures: ALL LEVELS
BGY Closed
Trestle and Road Closed

GUT ROAD
CLOSURE
06/02 @
12:00 Thru
09/02 @
09:00

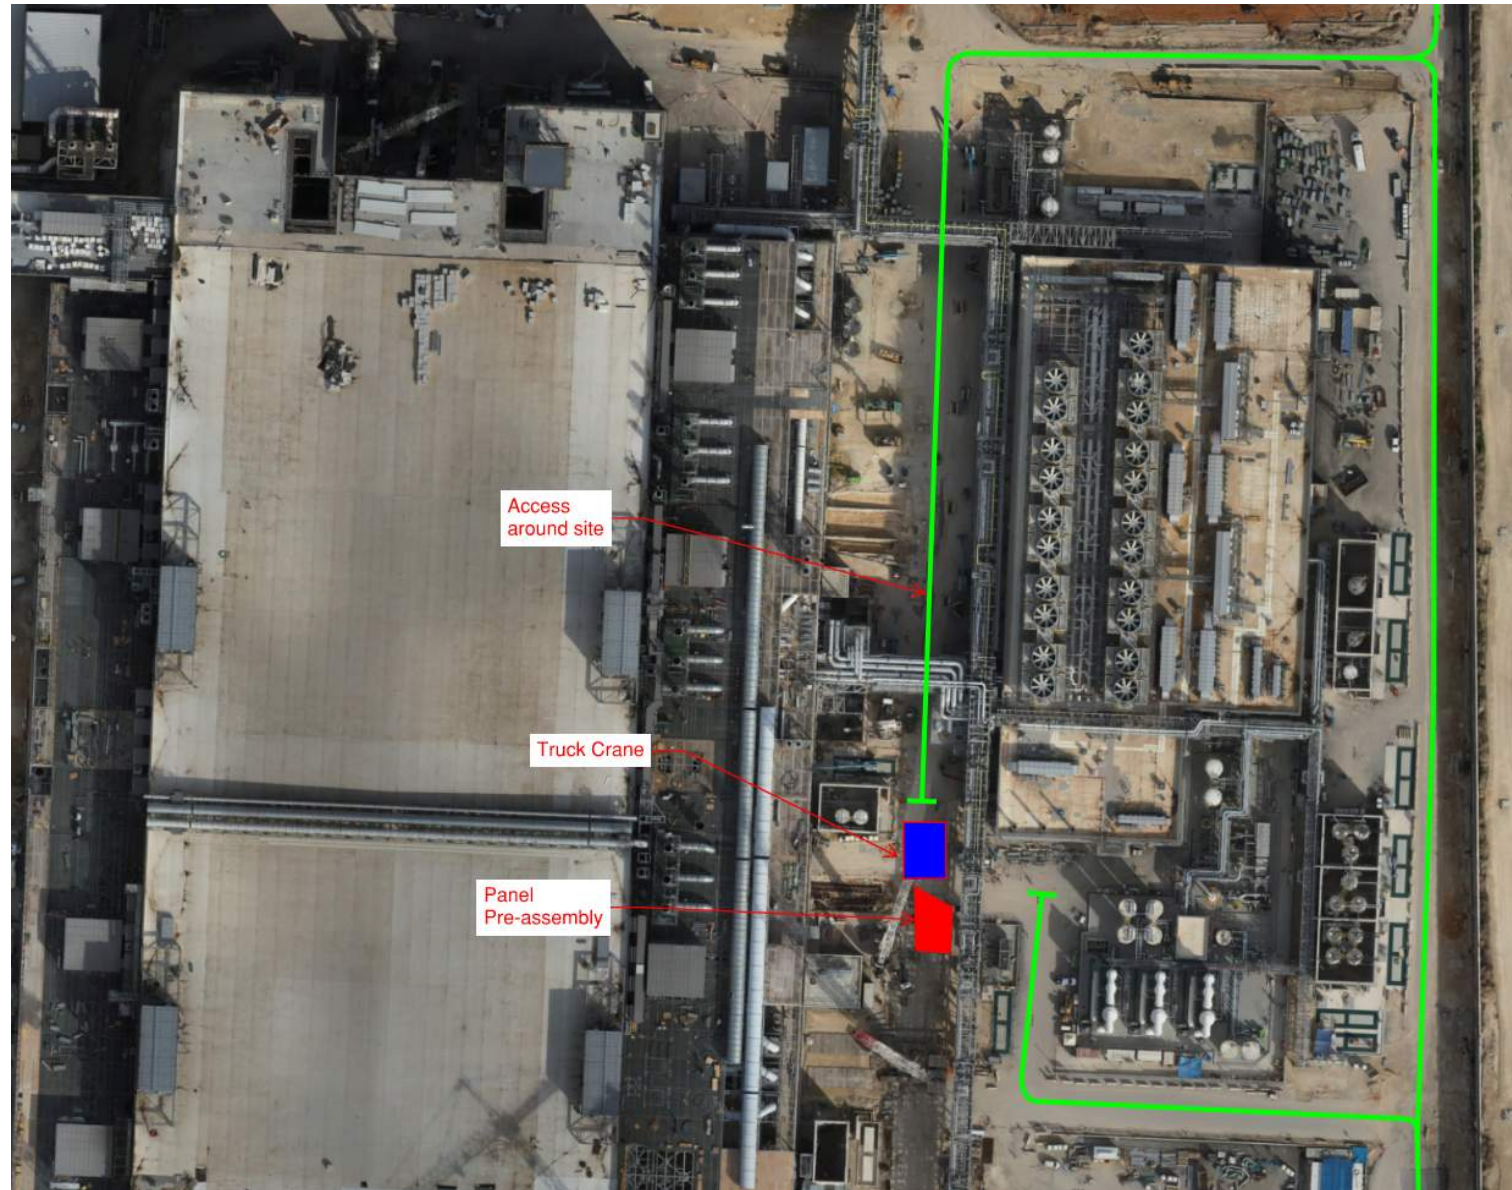




WJG 01J, 02J LIFT 2 & 3

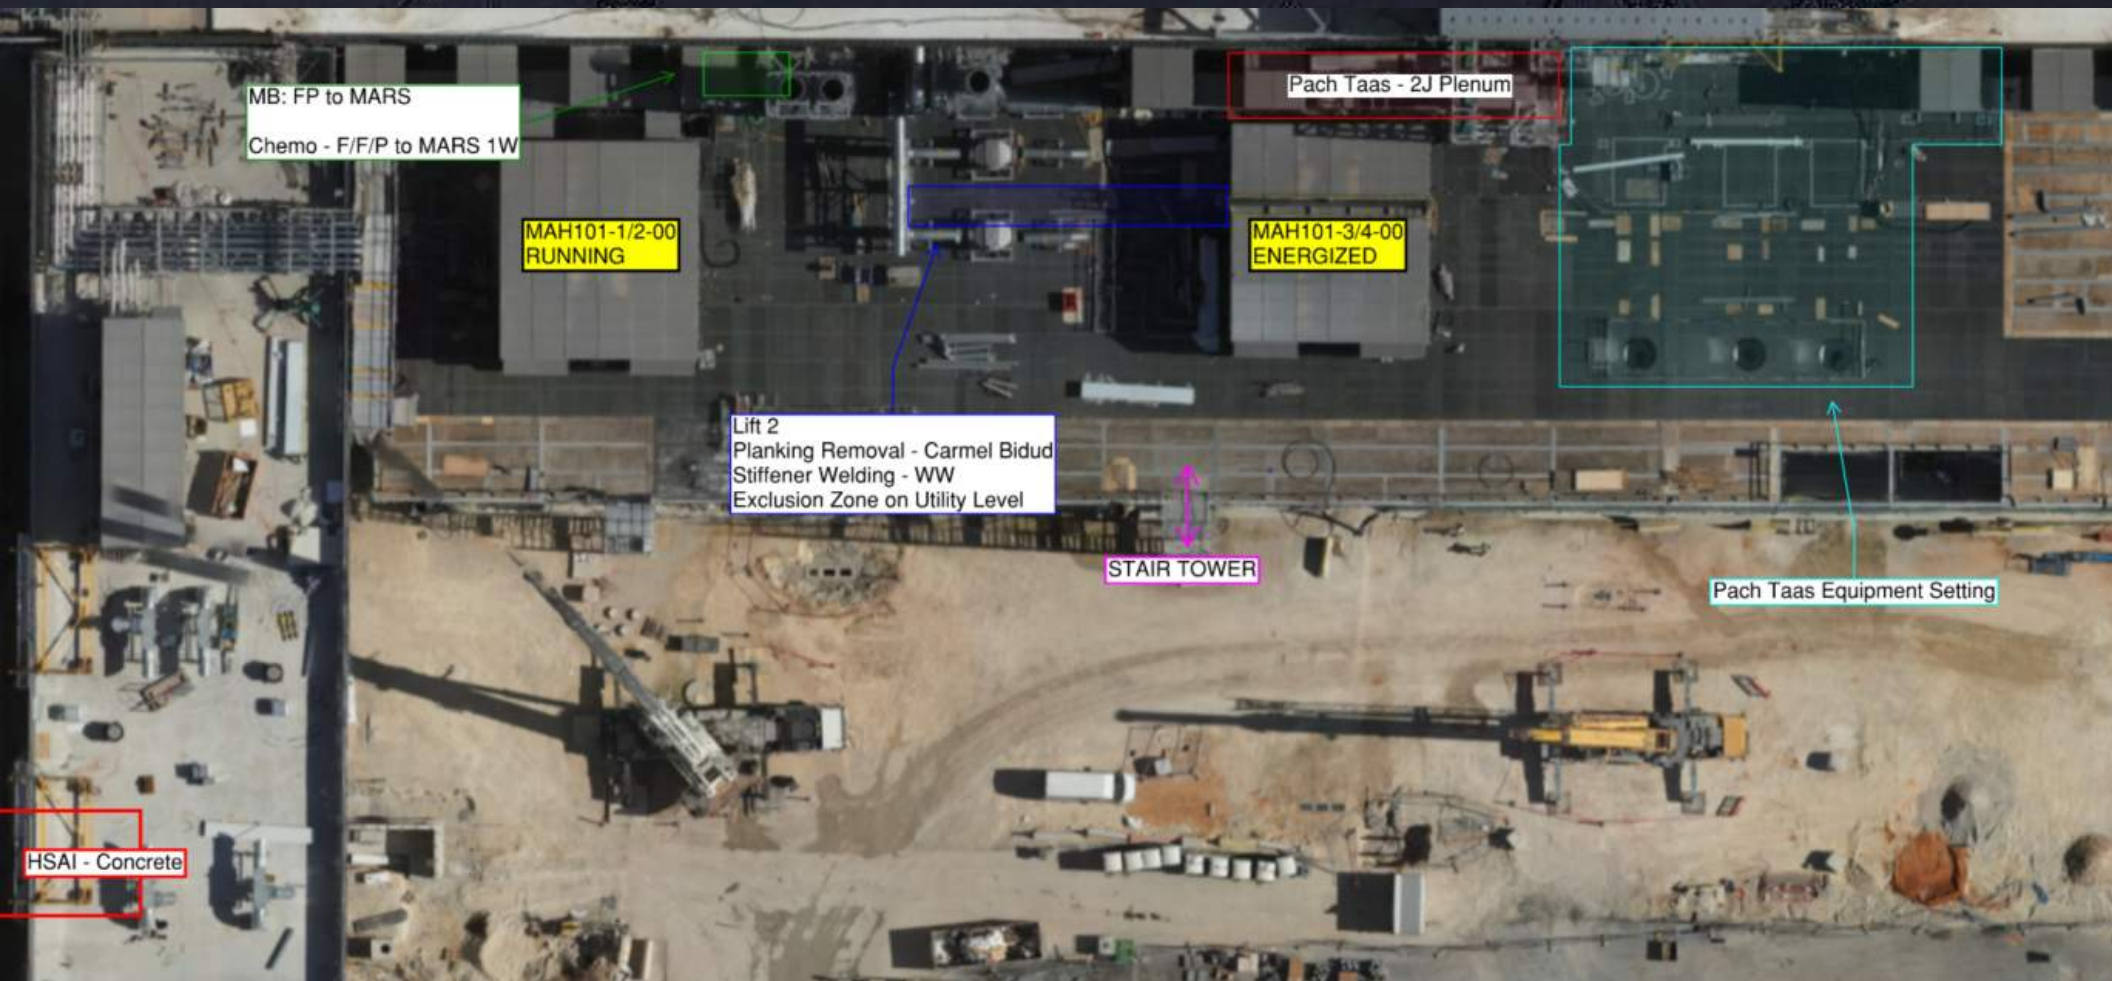



WJG 03J, 04J, 05J LIFT 2 & 3






WJG UTILITY LEVEL BUILD OUT

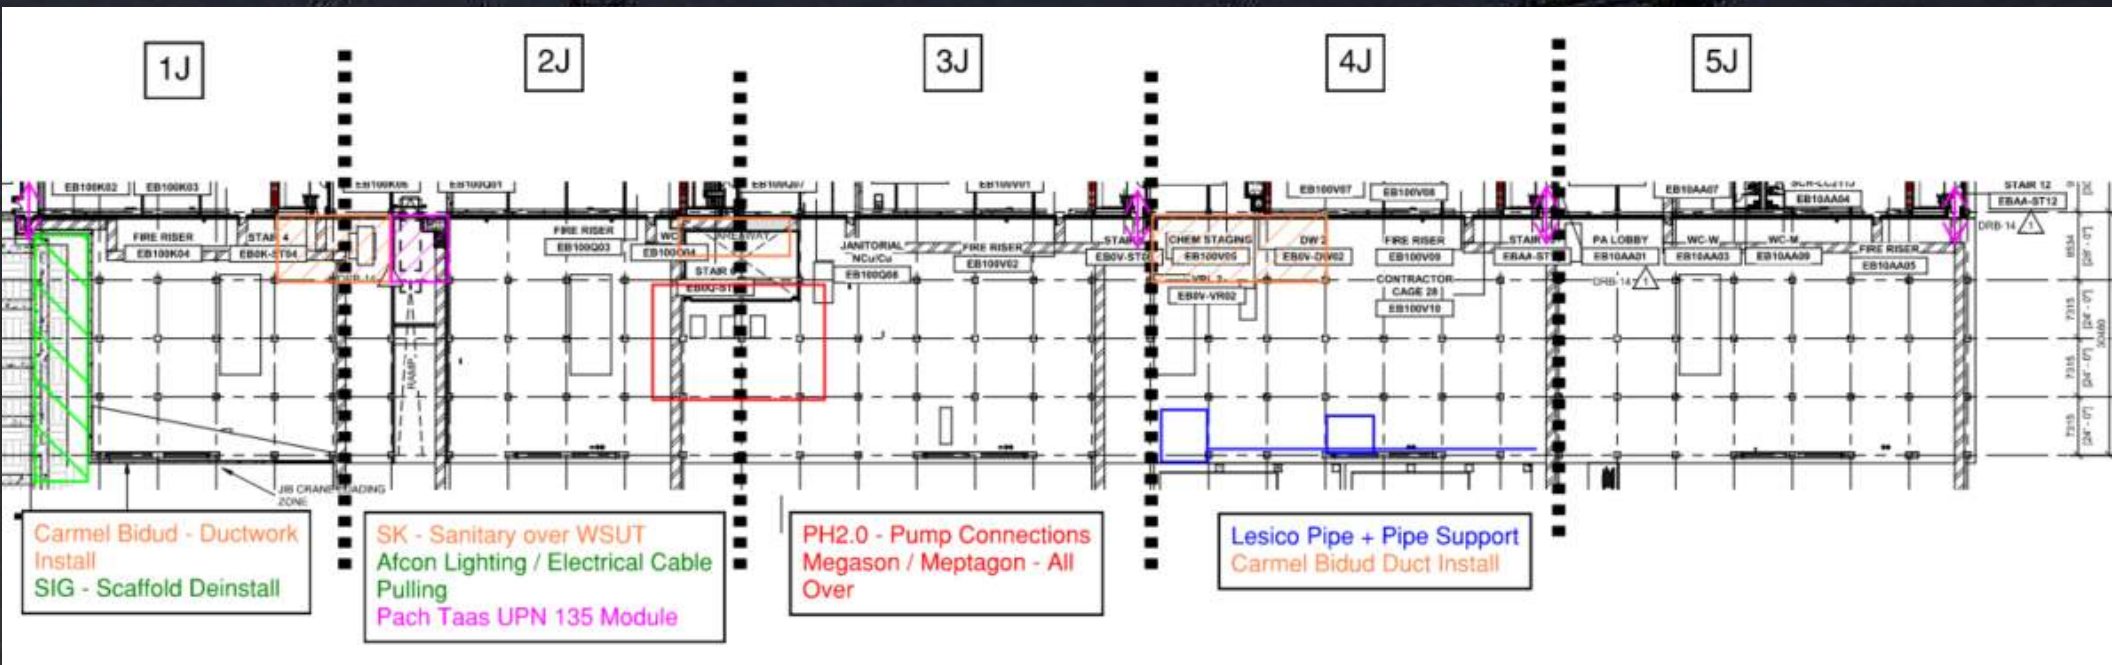

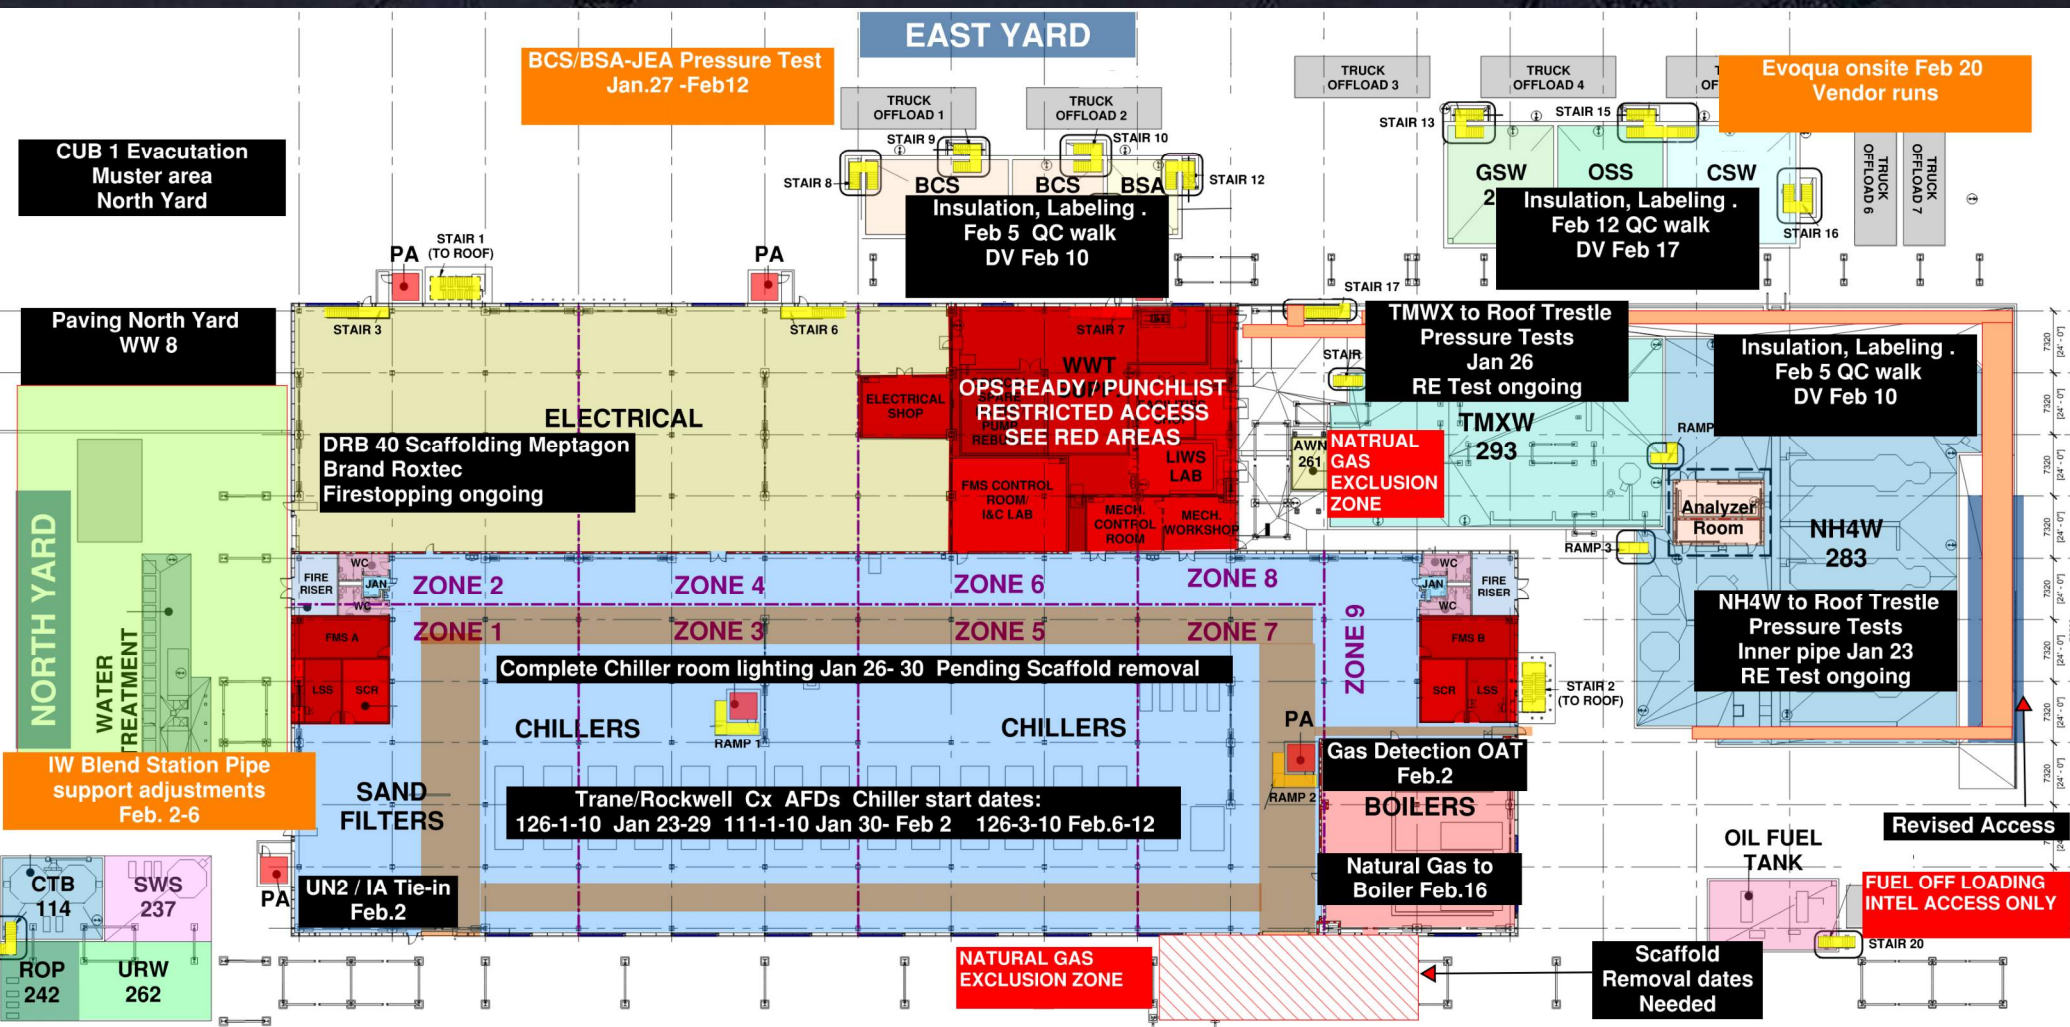





CUB 1 Exterior Pre-Punch Status

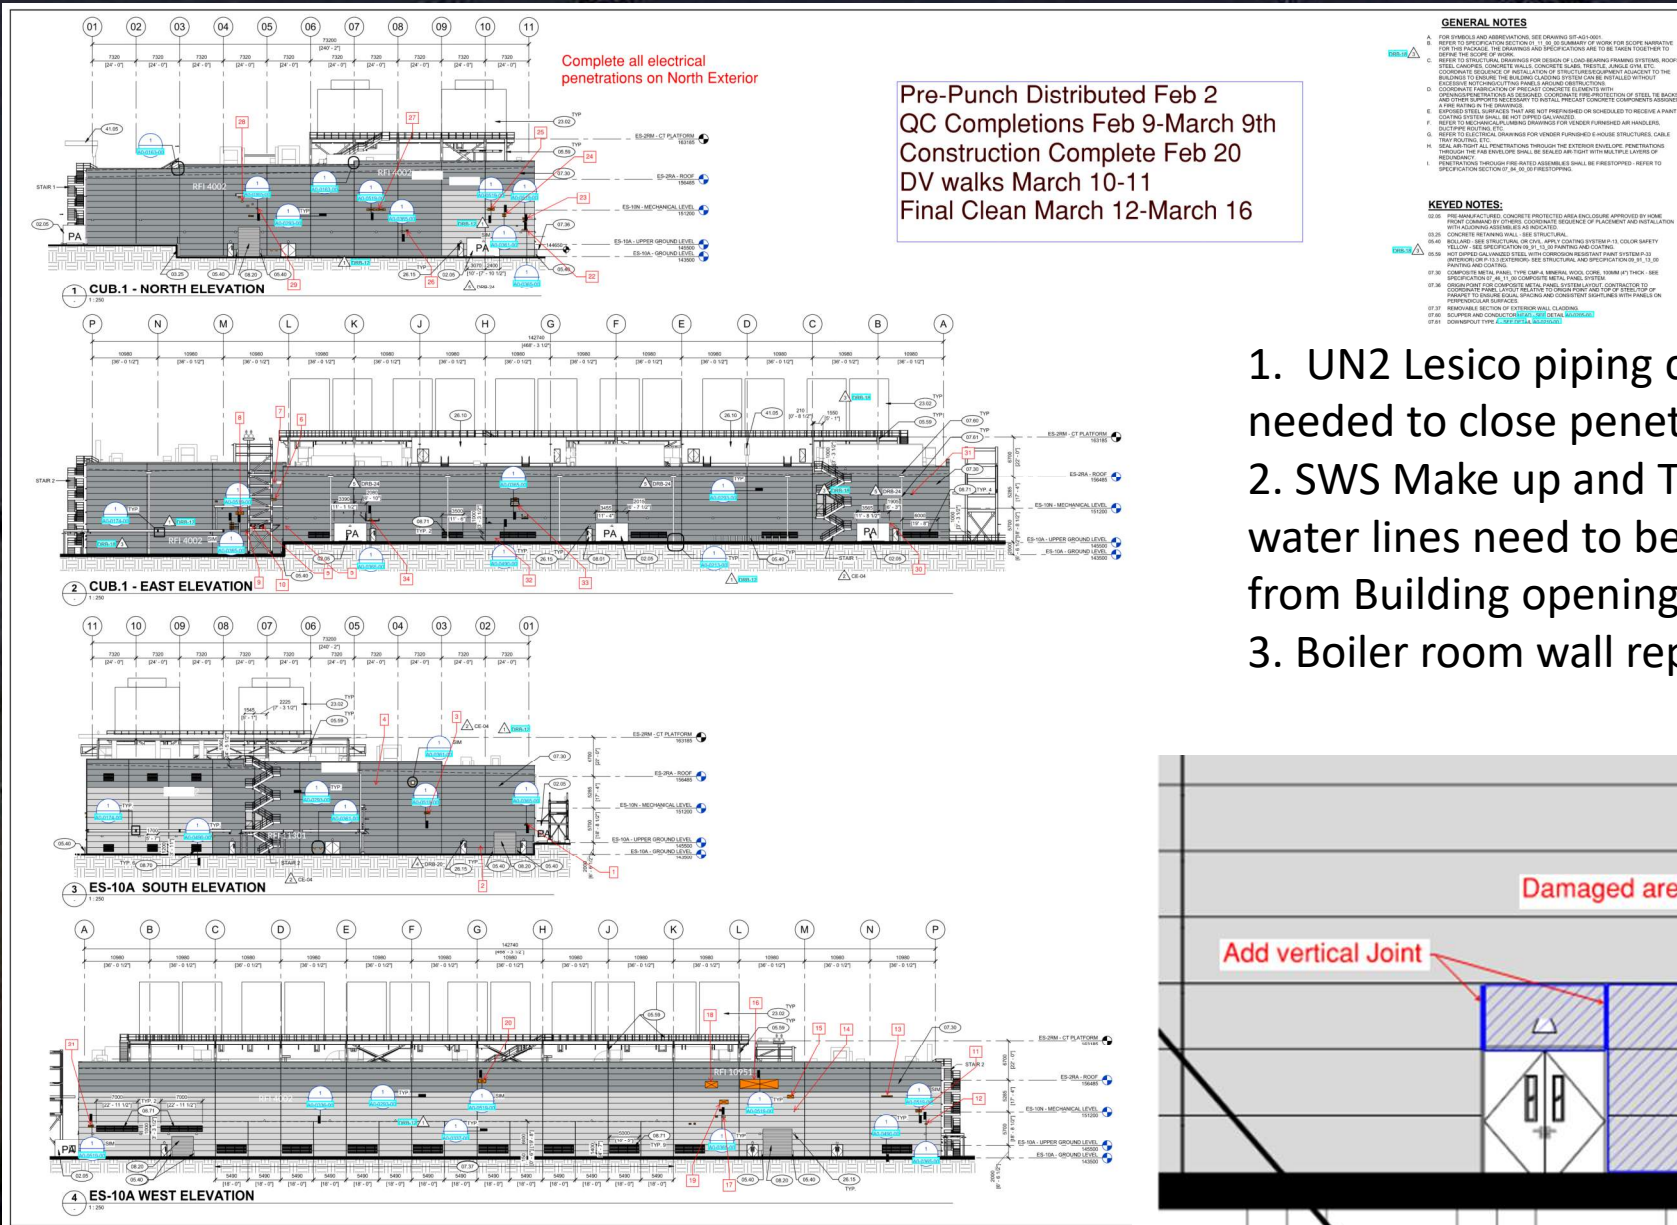


1. UN2 Lesico piping complete needed to close penetrations
2. SWS Make up and Temp shower water lines need to be removed from Building openings
3. Boiler room wall repairs Feb 9-19

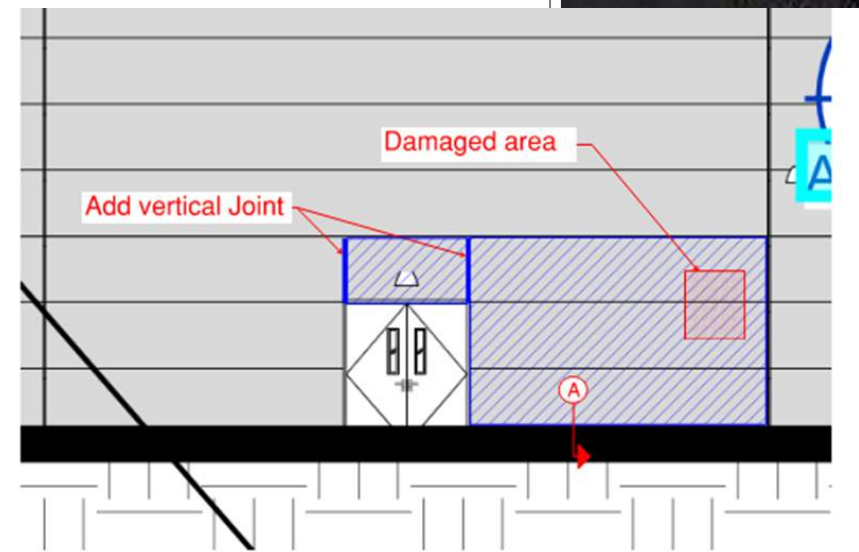


CUB 1 – EXTERIOR/ROOF

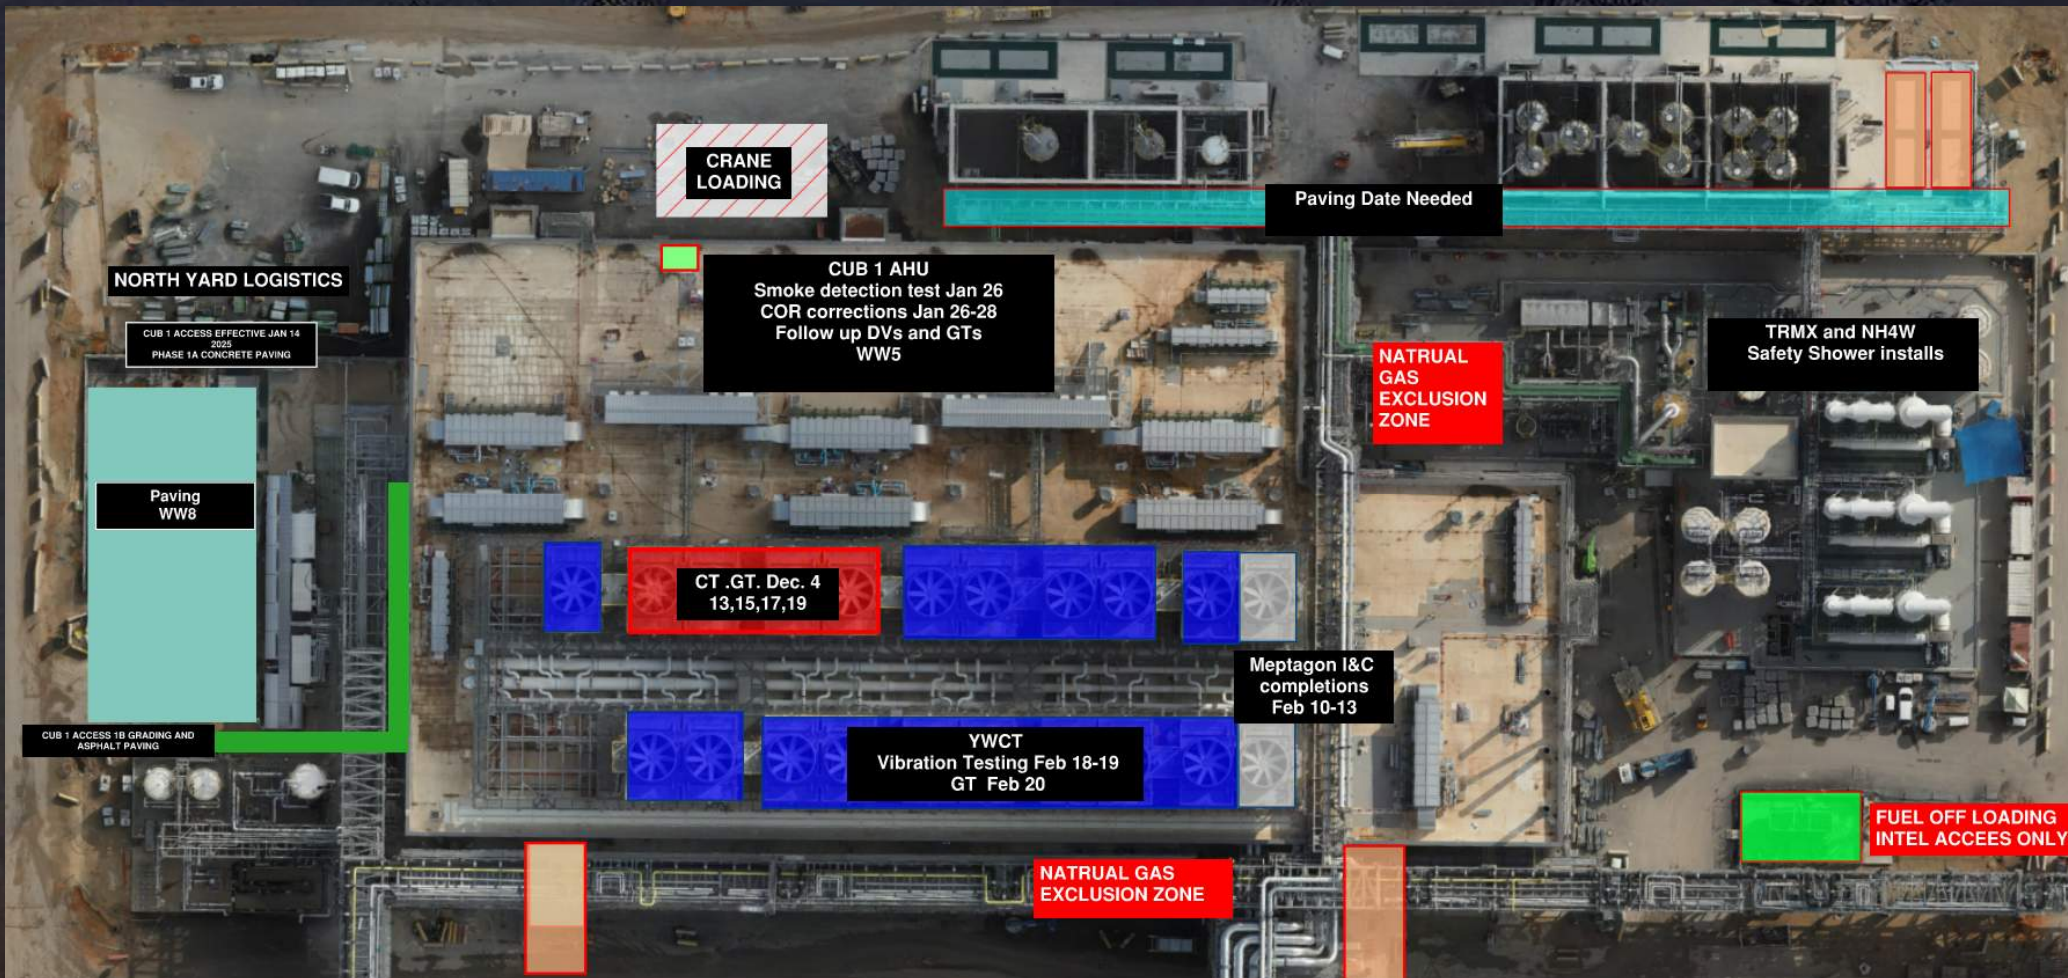


CUB 2 – EXTERIOR/ROOF

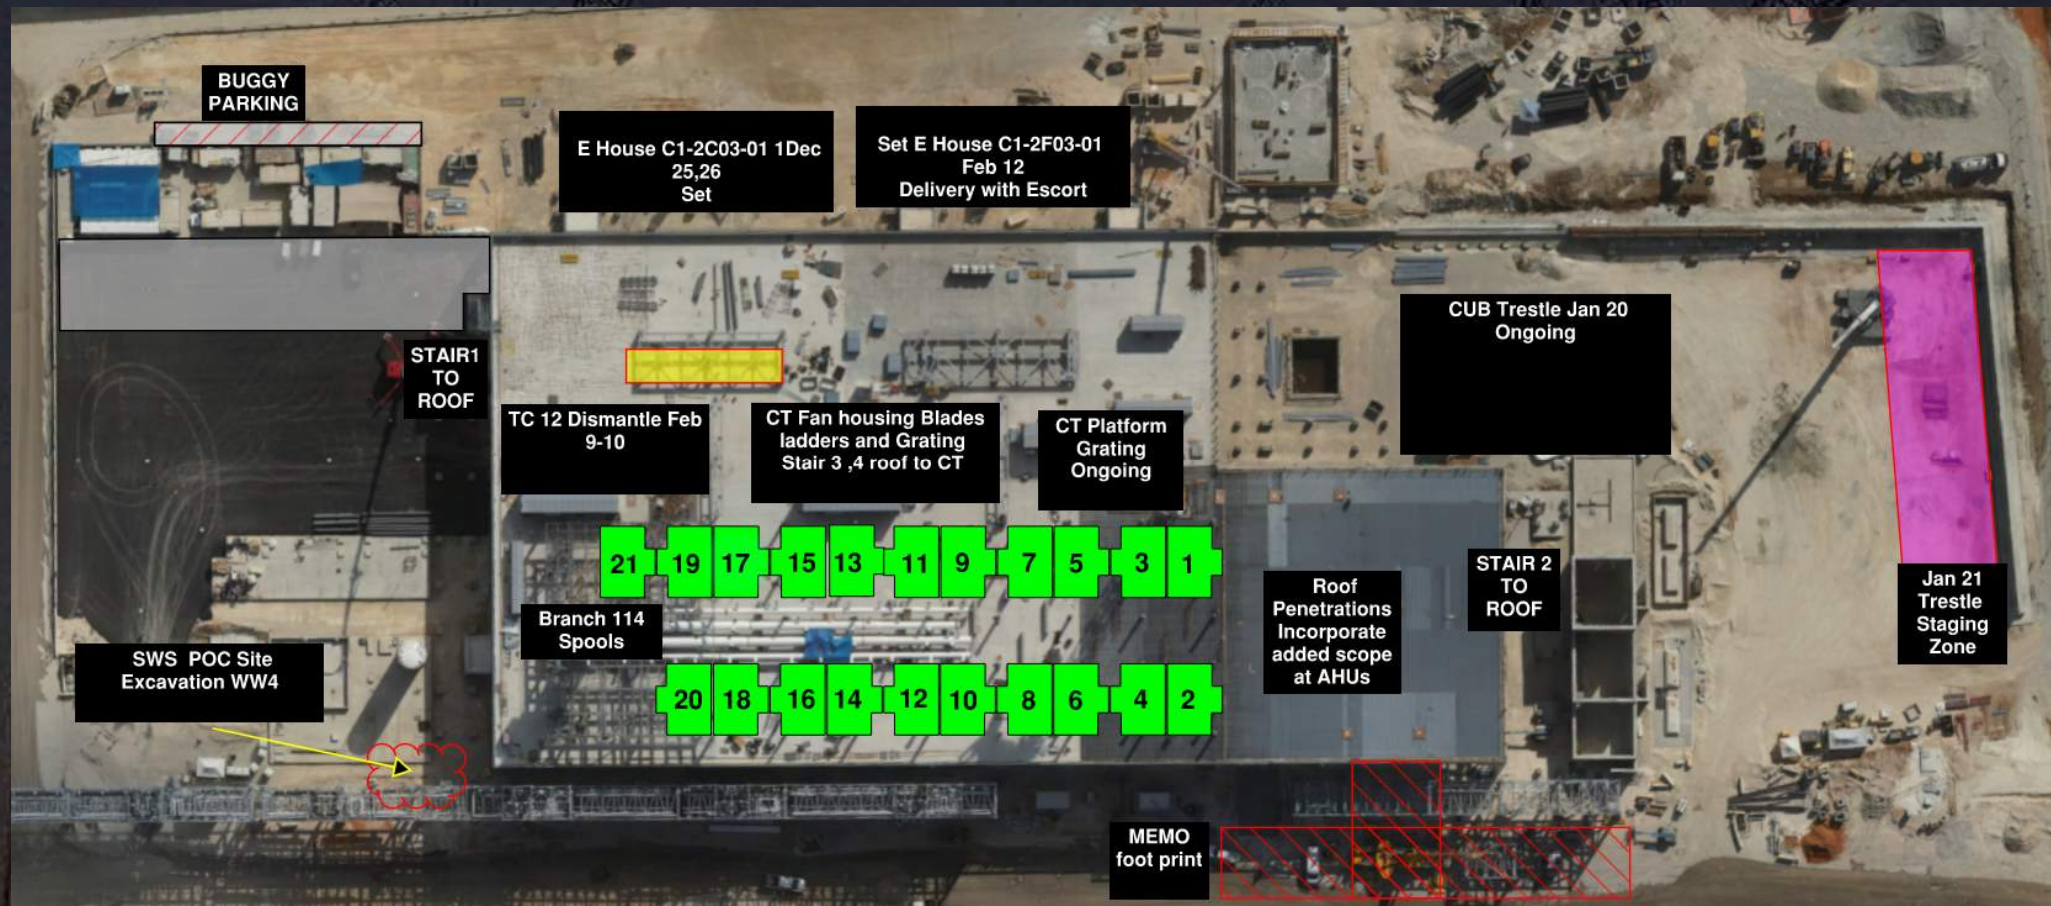



HOFFMAN CONSTRUCTION COMPANY

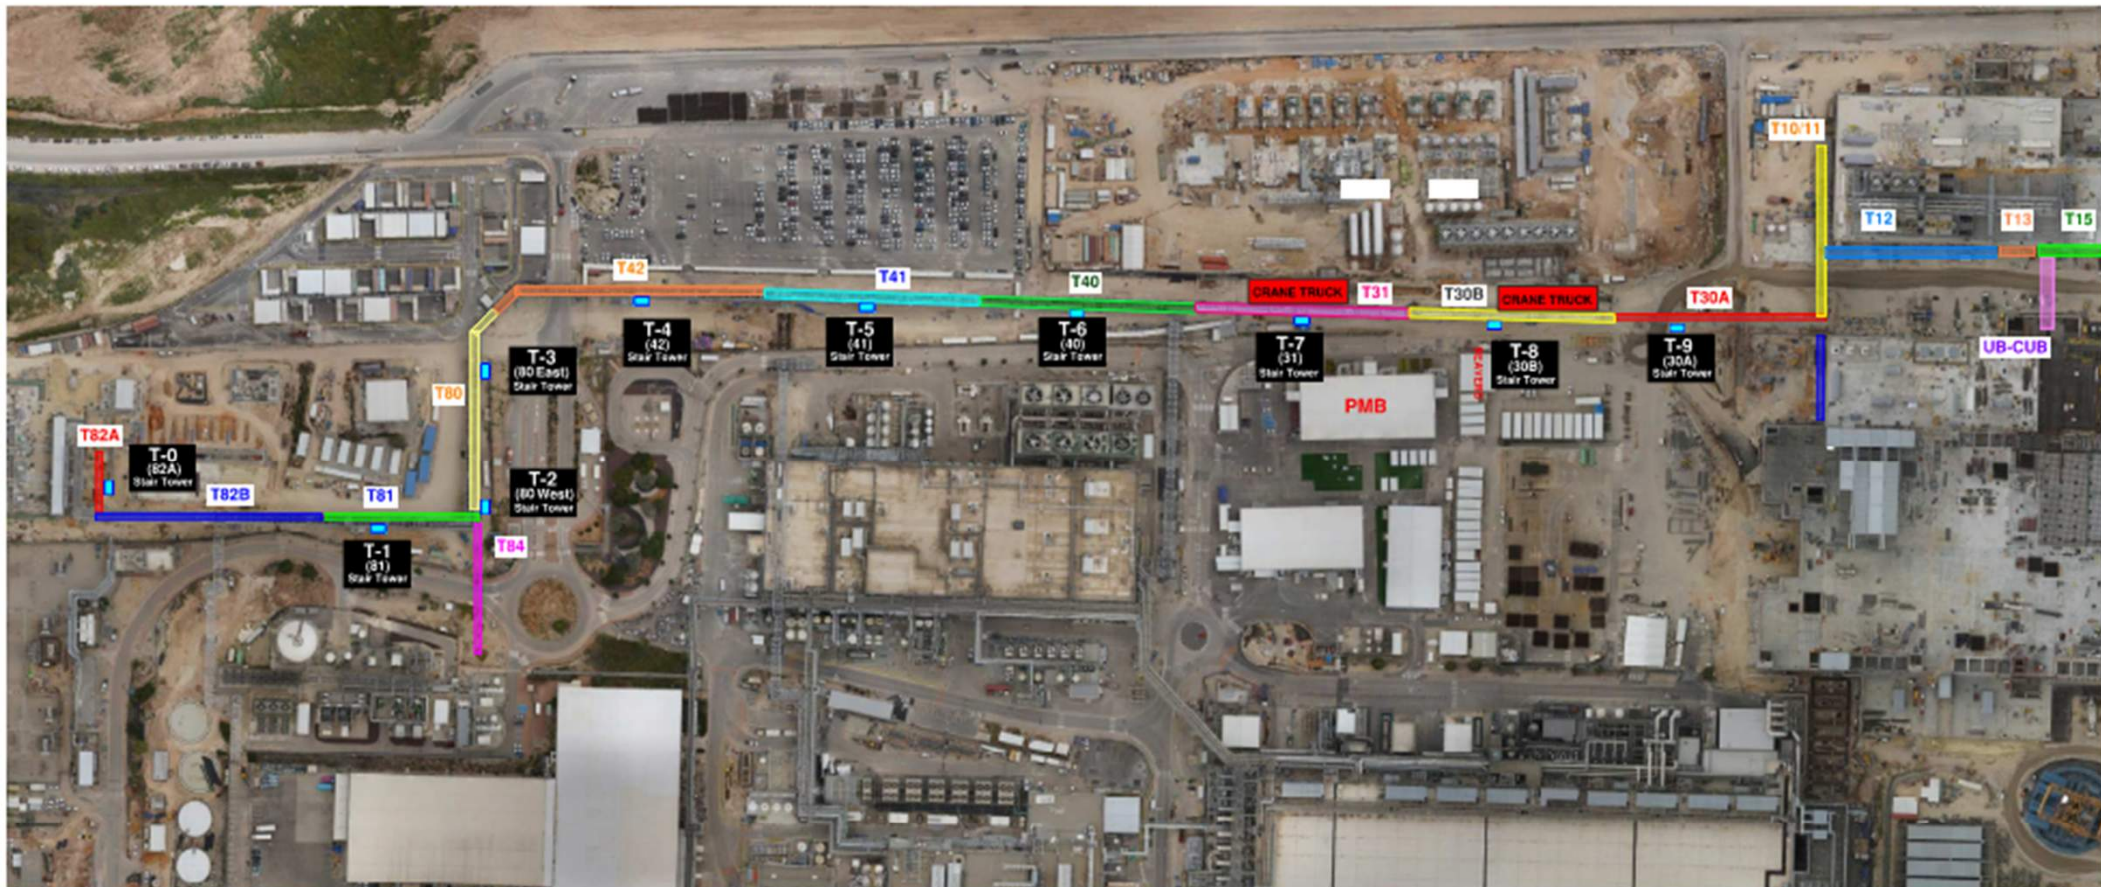



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North Entry





Daily Coordination Meeting

Site Logistics North






Daily Coordination Meeting

Site Logistics

South

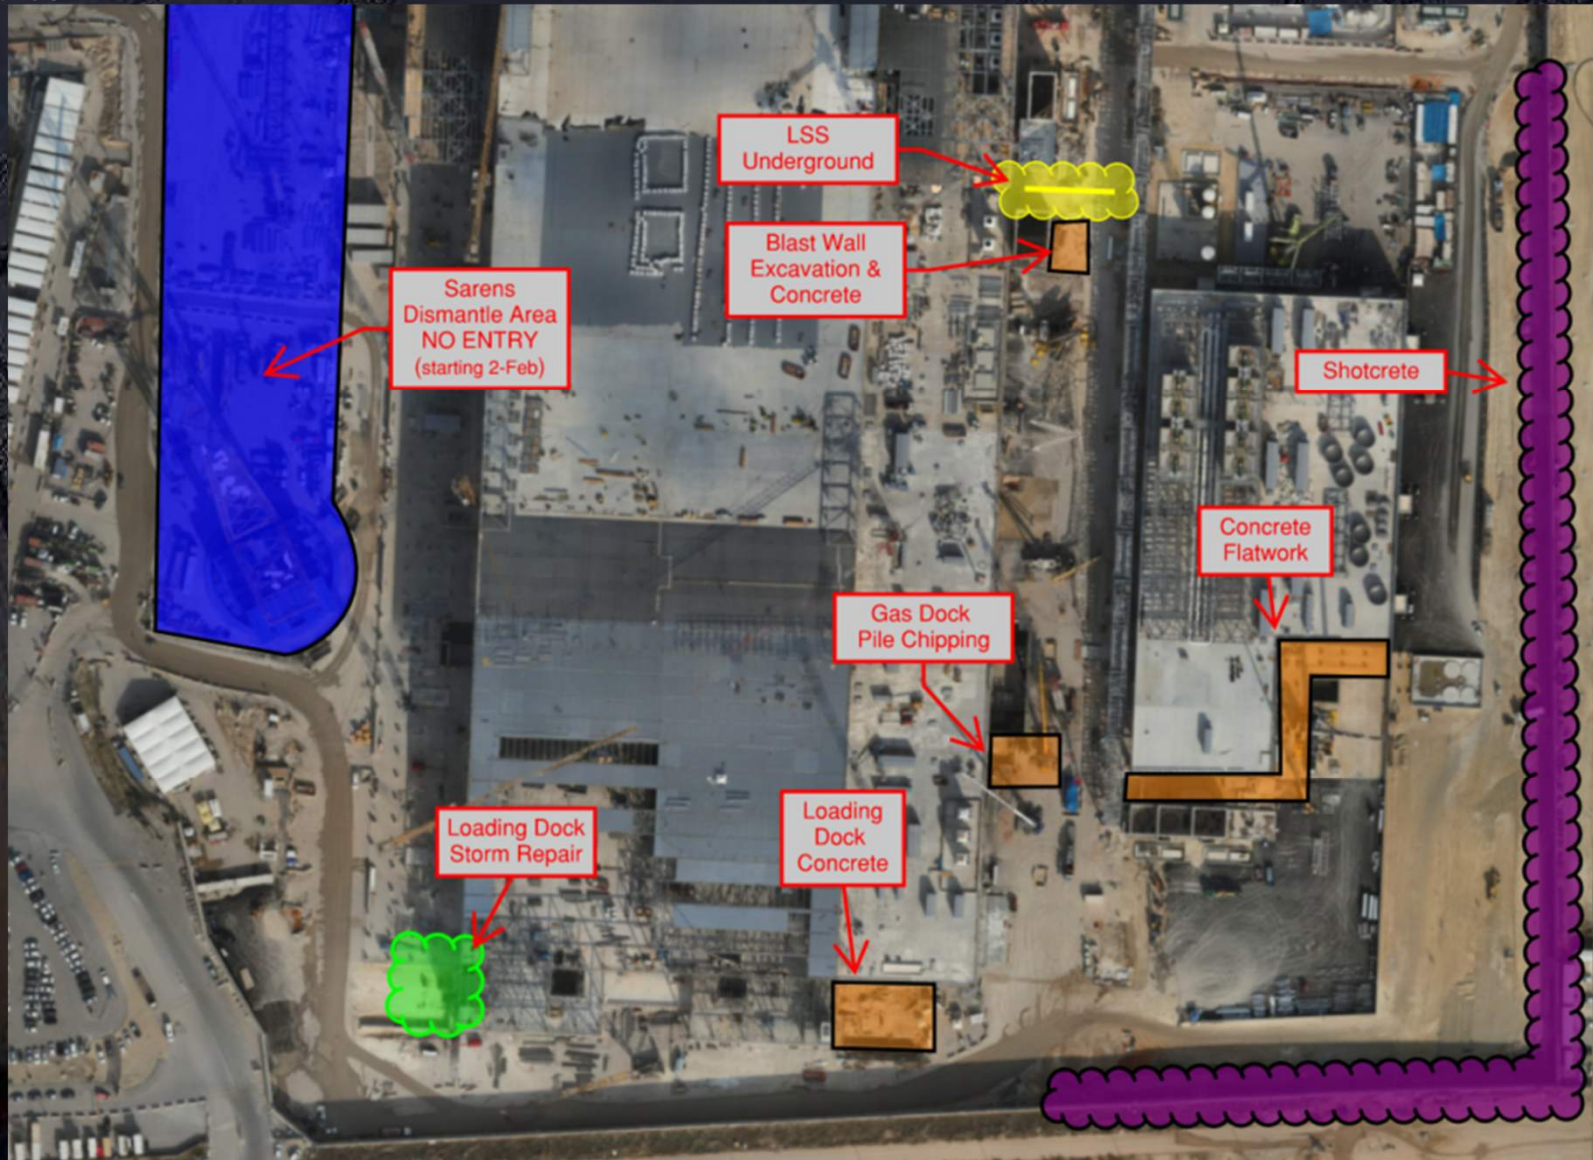

Wind- Secure Materials

- When weather moves in we need to ensure that we are securing our materials, even if we are in the area with them.
- Wind can start in a flash and if we aren't prepared we risk material becoming airborne and possibly injuring someone.
- When we are leaving for the day we need to double check that everything has been secured.
- There is potential to cause serious damage to live systems if something is to hit them at speed with high winds.

HCC/EHS Weekend Work- 07.02.2025

White Board Meeting in Beavers at 06:30

Superintendents

Nir Gueta - 054-3324775

Josh Noll - 052-5590653

Paschalis Papadopoulos - 052-2168215

Anas Dakkak - 052-2328086

David Jollands - 052-3961675

Khaled H

Yossi Atias - 052-3060790

CSA CM

Idan Dahan - 052-5949702

Gregory Leal - 052-5102705

Dan F

MEP

Evgeniy Stam - 052-9765294

Cx

Cranes

Safety

- Safety Foreman- Adir Elmakayes- 054-7254767 Adir-Elmakayes@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 07.02.2025

FAB

Utility level/ SUT

Clean Room

- Talad – 25 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Mati 0504887477, Super Shlomi 0508633562)
- Chemo – 35 GUYS INT -TNTNE/W Supports, 5RA Racks, 3W Skids (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Sela – 6 guys, 1E, 3E CRC (Supervisor Yoav 0548076339, EHS Sergey 0526650046)
- Protocol 2 guys (Roni 0542496363, Elisha 0587963704)
- Talent solution 8 guys CR 2E 1E/W maintenance cleaning (EHS Yosiel 0508777611, Super Super Evgeniy 0528328859)
- W&W 20 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- Megason 6 guys 4DA 4W-4E FOREMAN ISRAEL BITON 0526869393 EHS GUY ISHBIT
- Sig – 16 GUYS MOD2- 17 Line, MOD1 2E-2W scaffold (EHS Beni 0506232032, Super Shmulik 0549205966)
- Rolling Plains – 24 guys 7W, CA to CG17 MOD2- Grid 17 4DA (Super Oleg 0542689370 , EHS MARCOV 0546596857)

Subfab

- Pach Taas
 - W-E MARSes
 - Natan: 0556862261
 - Nuriel: 0549012343
- Afcon E
 - All over SF
 - Avi Eli: 0526008487
- MEGASON
 - MOD 2,LSS Rooms
 - Israel: 0526869393
- SELA
 - 4W
 - David: 0524382997

Subcontractor Weekend Work- 07.02.2025

PSSS

- **Pach Taas** – Module bolting PSSS Roof, Lift 2 3-5P
 - Foreman – Vadim – 053-5552472
 - Safety – Offek – 050-2161429
- **Afcon Electrical** – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- **Chemo A.** – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112
- **Combe Waste** – 2P Waste Piping at GL4/SSS Building
 - Foreman – Chaim – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Lesico** – UN2 Pressure Test
 - Foreman – Suju Pally – 052-7755967
 - Safety – Tal Madar – 052-8229109
- **Carmel Duct** – Spec Gas, BCD, and 2P Roof
 - Foreman –
 - Safety –
- **HSAl** – Chem Dock Retaining Wall
 - Foreman – Dave – 052-4121028
 - Safety – Hiam

WJG

- **Afcon** – Lift 2 Cable Tray and Utility Level Lighting
 - Foreman: Montu 055 911 6973
 - Safety: Pradeep 055 274 2935
- **Pach Taas**: All over
 - Foreman: Netanel 055 686 2261
 - Safety: Adiv 050 690 9390

Subcontractor Weekend Work- 07.02.2025

CUB

Chemo Aharon:

Dudu - 050-9808846

Leonid - 054-8883878

Carmel Bidud:

Fahri - 0526105266

Moyat - 0524335060

David - 0548894447

Megason:

Osama - 0522851458

Israel - 0526869393

S.K:

Reynato - 0548991623

Marzuk- 0548830263

Pach Taas:

Nathan - 0556862261

Adiv - 0506909390

HSI:

Sergey - 0552728807

Trestle

SNJ:

PIPES –T40 - UB CUB - 15 workers (3 teams)

STEEL –Galvanized paint + T30 A+B - 8 workers (2 teams)

Steel adjustment - 7 workers (3 teams)

SAFETY TRESTLE-

Aviram shrike - 0509059920

FORMAN

Adiv asaly- 0526017477

Site

Derech afar :

Shotcrete south wall, 7 workers

Safety- Alex 054-5403849

Team lead – Igor 058-6093776

Olizki:

BSGS spry bitumen

Safety – Matania 052-5108711

Team lead- Fami 052-4025766

Daily Coordination Meeting



14:00 Sign In
