

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting

General Topics:

- Weather changing- keep materials secured
- Weekend work

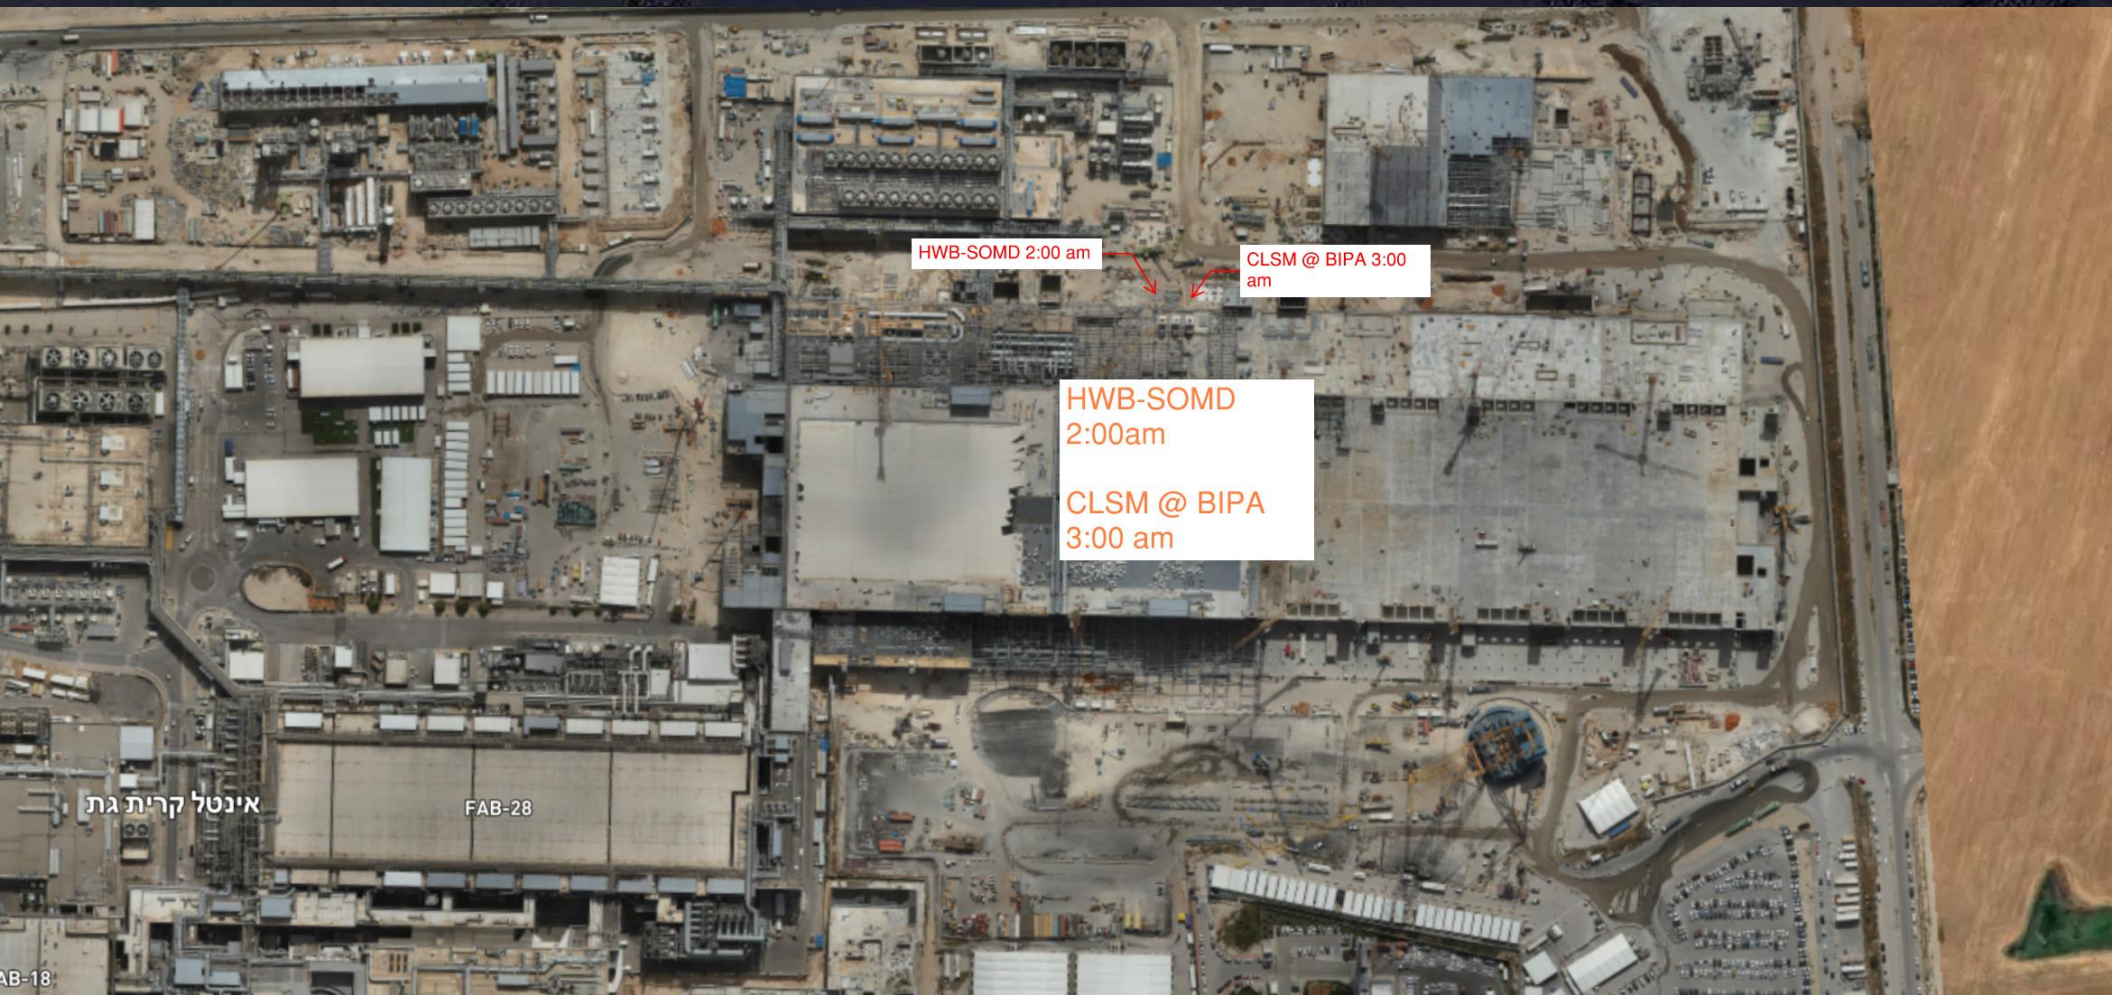

HWB-SOMD 2:00 am

CLSM @ BIPA 3:00
am

HWB-SOMD
2:00am

CLSM @ BIPA
3:00 am

אינטל קרית גת


FAB-28

AB-18




UTILITY LEVEL P.Test

SK
Press. Test
9/19
From 17:00

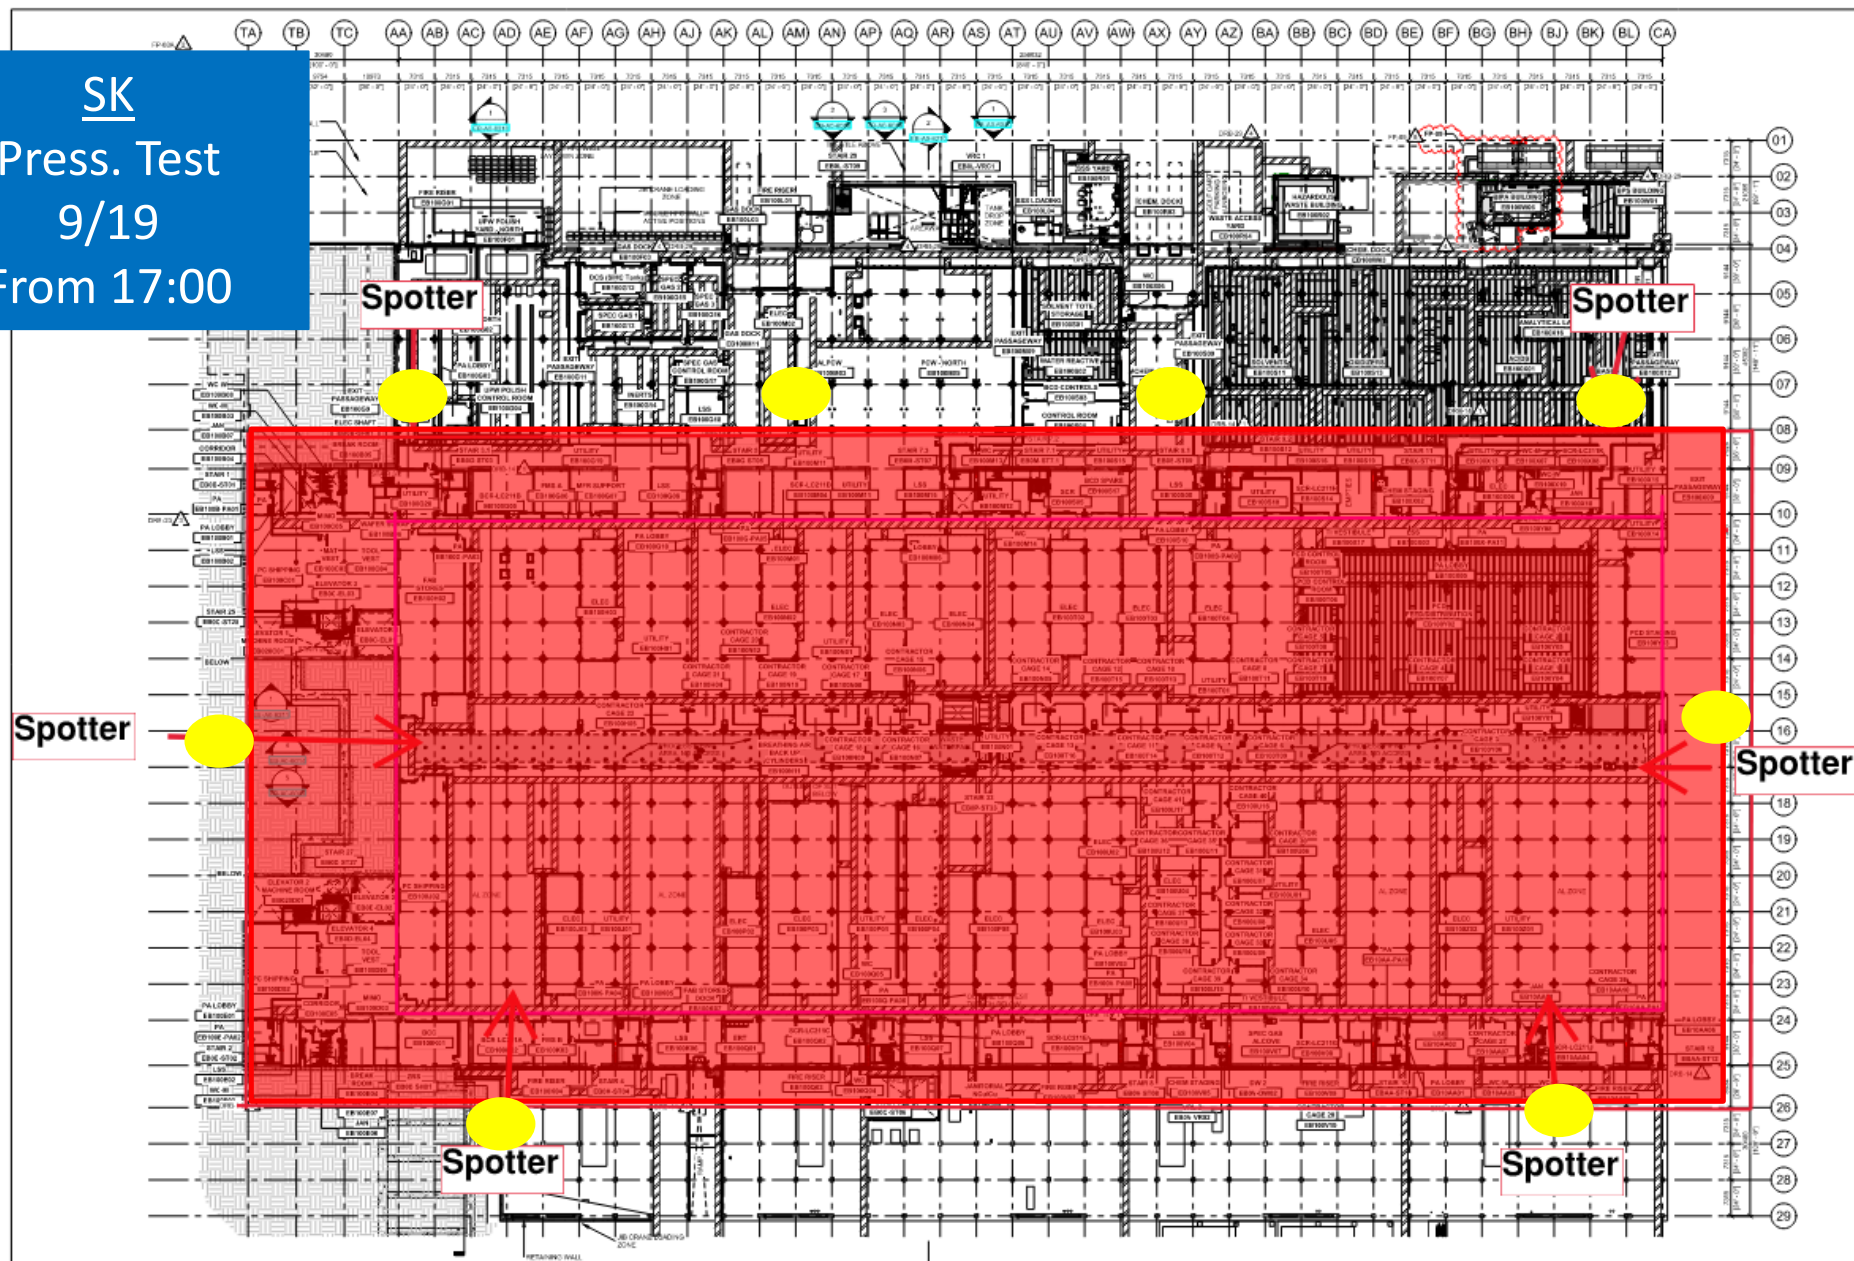

UTILITY LEVEL MOD1

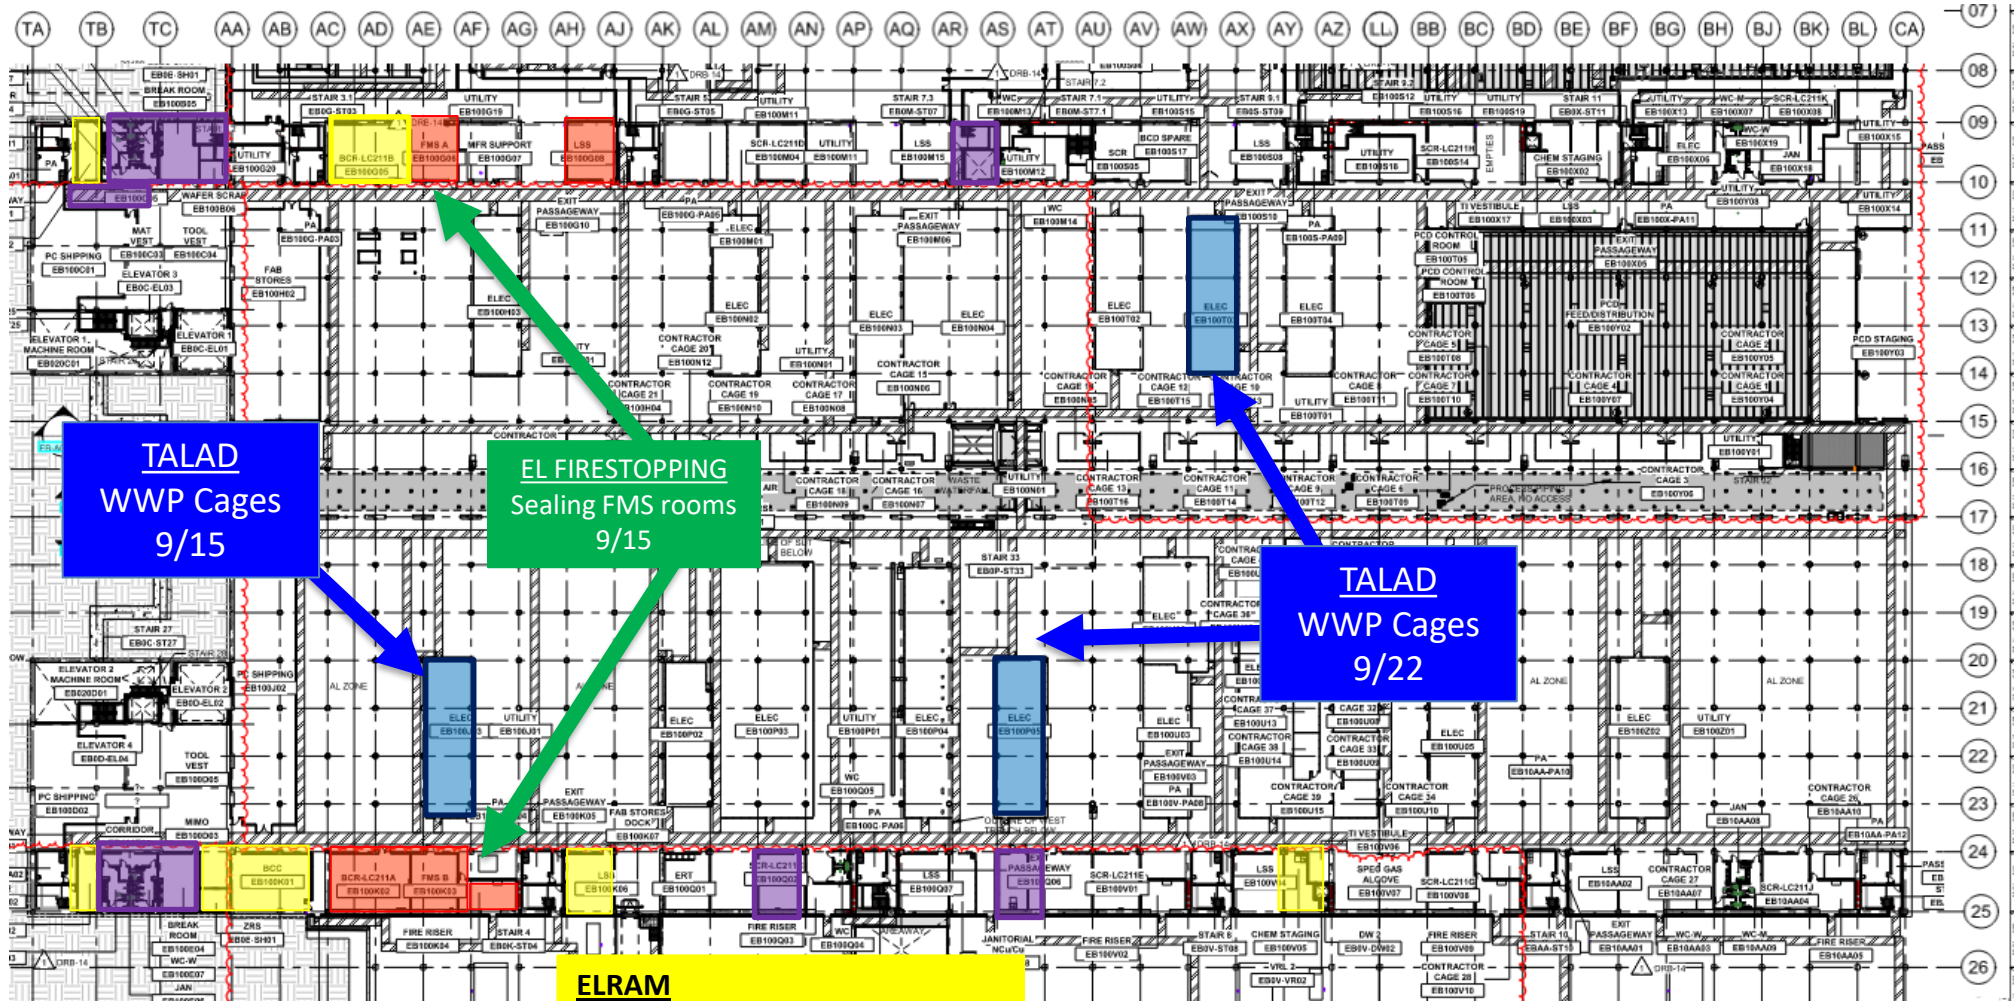

TALAD
WWP Cages
9/15

EL FIRESTOPPING
Sealing FMS rooms
9/15

TALAD
WWP Cages
9/22

ELRAM

Ongoing
LSS TTNW + TTNE
BCR 1E
CHEN STAGING
LSS 2W
Chem staging
BACKING
BCR 1E+1W – Pending funding
LSS's


BELFOR

TTNE - Corridor + Toilets + Break R
Stairs 7.3
Wafer scrap
TTNW - Toilets + Break R
SCR 2W
Exit pass 3W

MEP+Electrical


Ready for re-install
FMS A 1E
FMS B 1W
Fire Risers 1W
BCC

UTILITY LEVEL MOD2

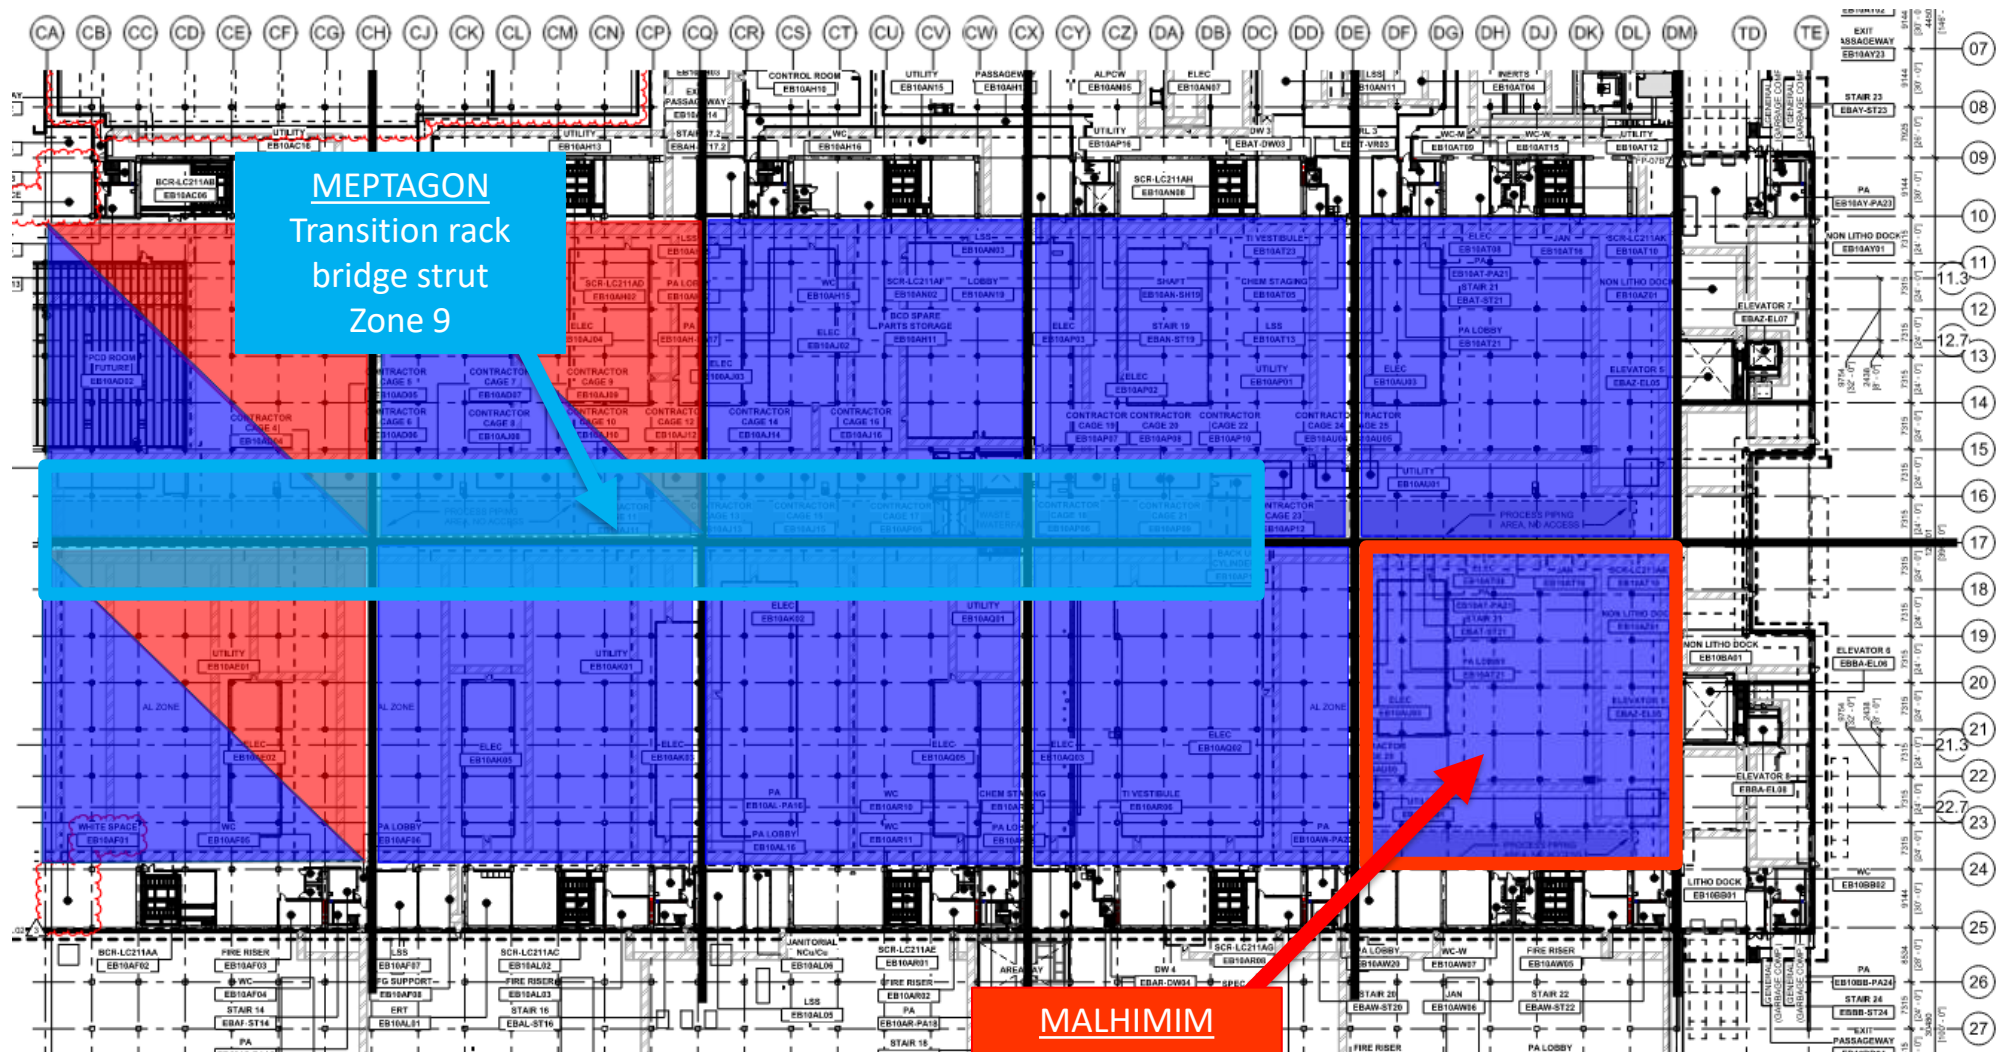




SUT 38.1 LEVEL

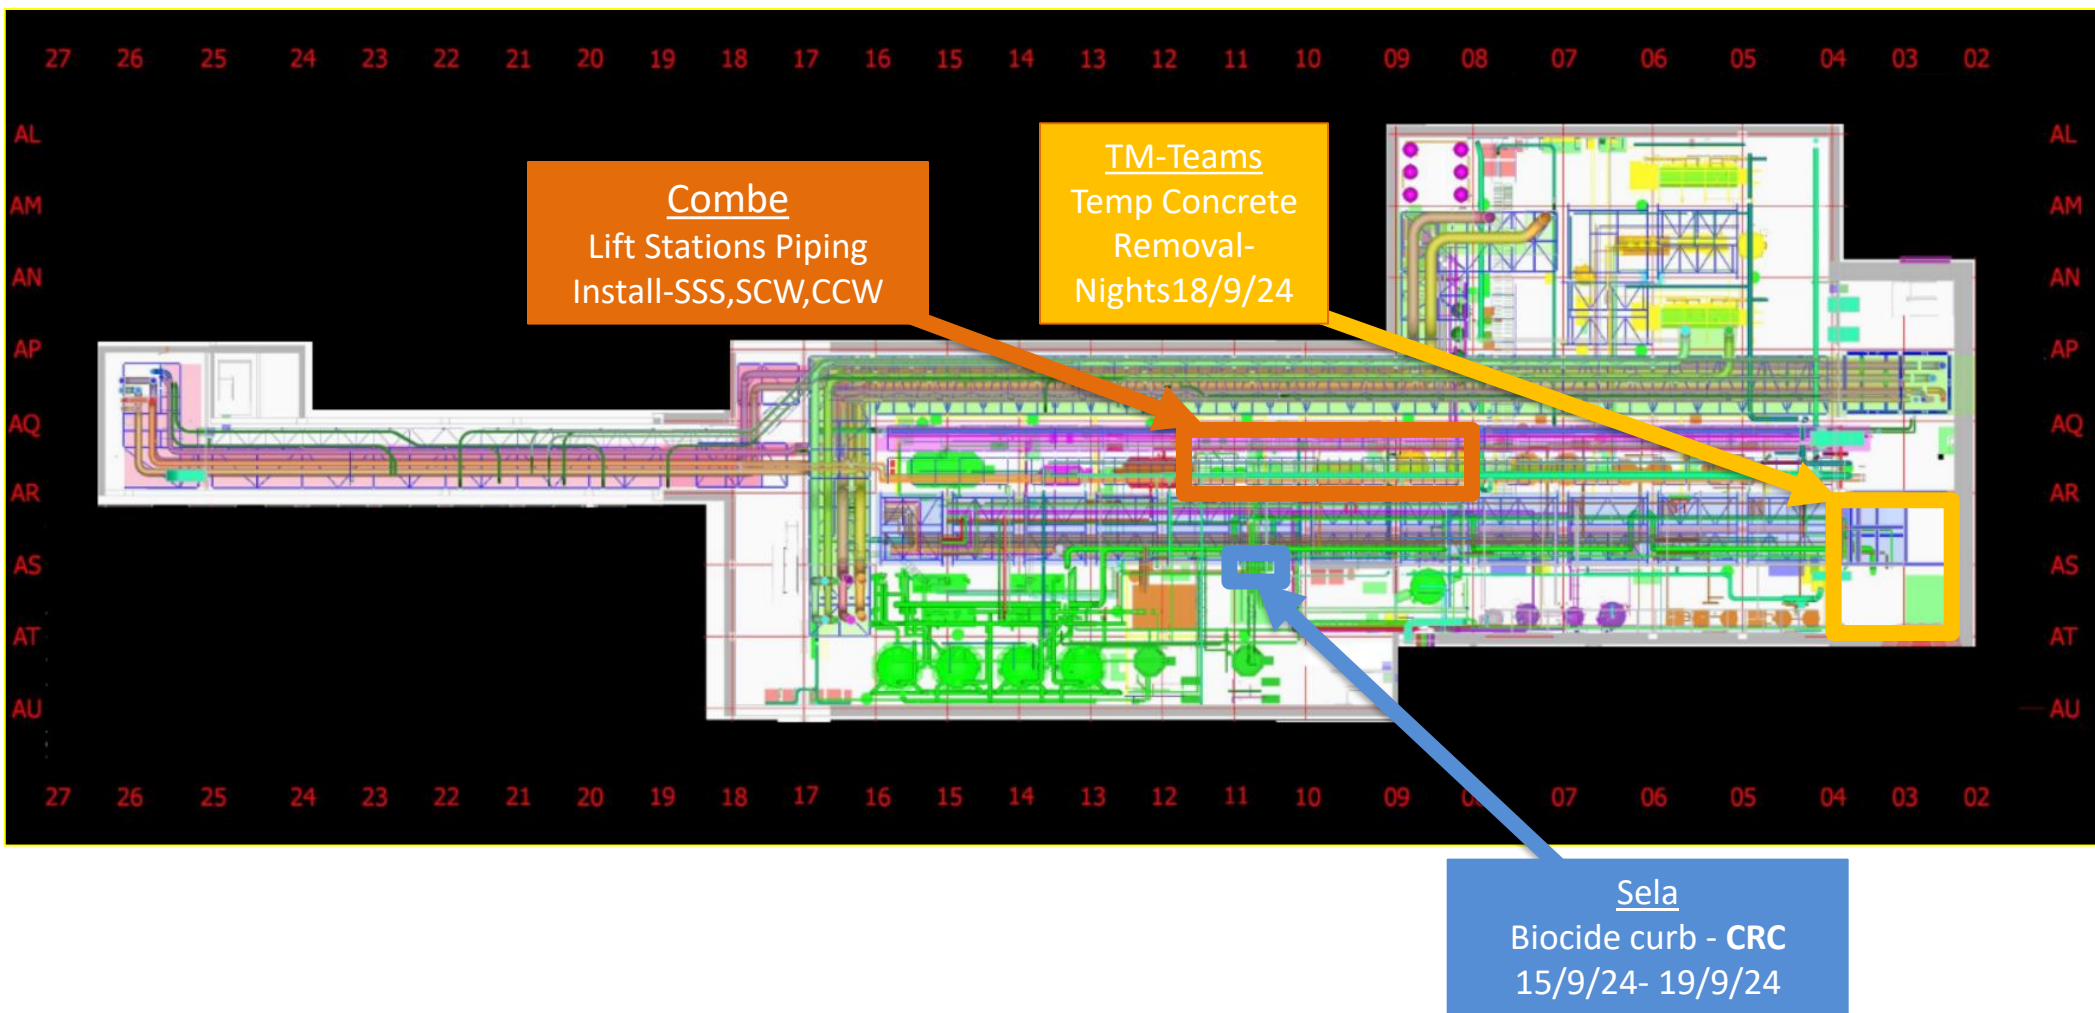

SUT 38.2 LEVEL

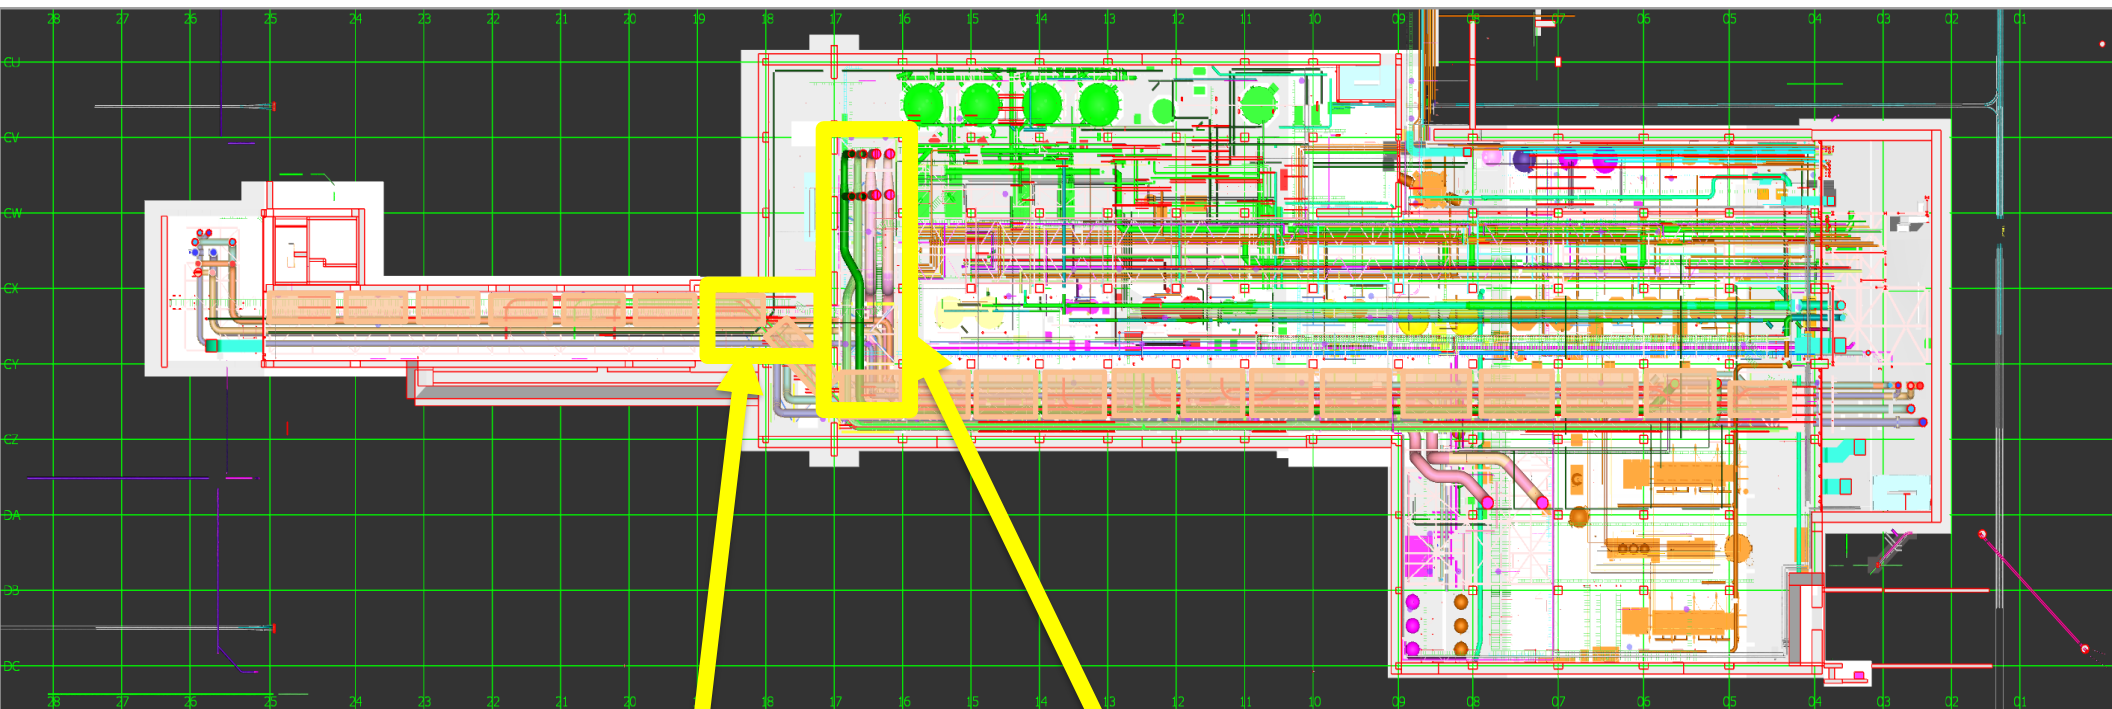


CRW
H&T
NEED PIPING

17-18 line
Bore Loading


16-17 line
lvl2+3
bed lift: Need a
Date

Vesda
H&T
Not actively installing


SUBFAB BUILDOUT MOD 1

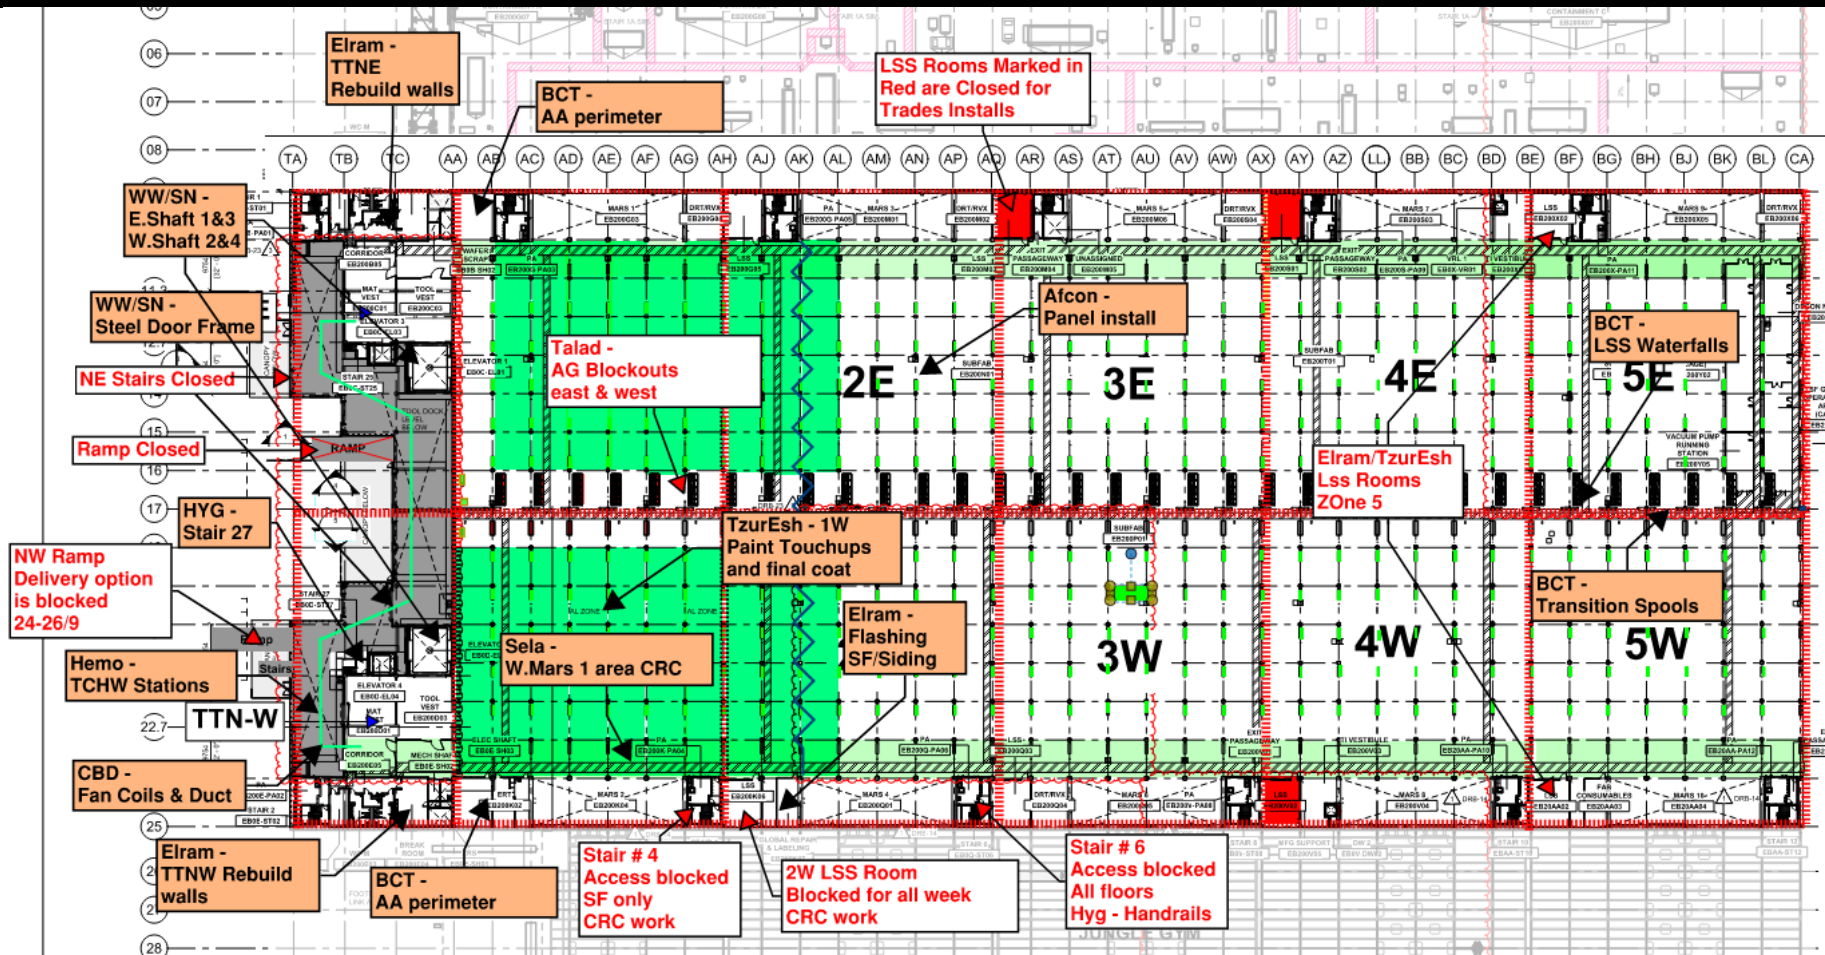


SUBFAB CRC TOPCOAT

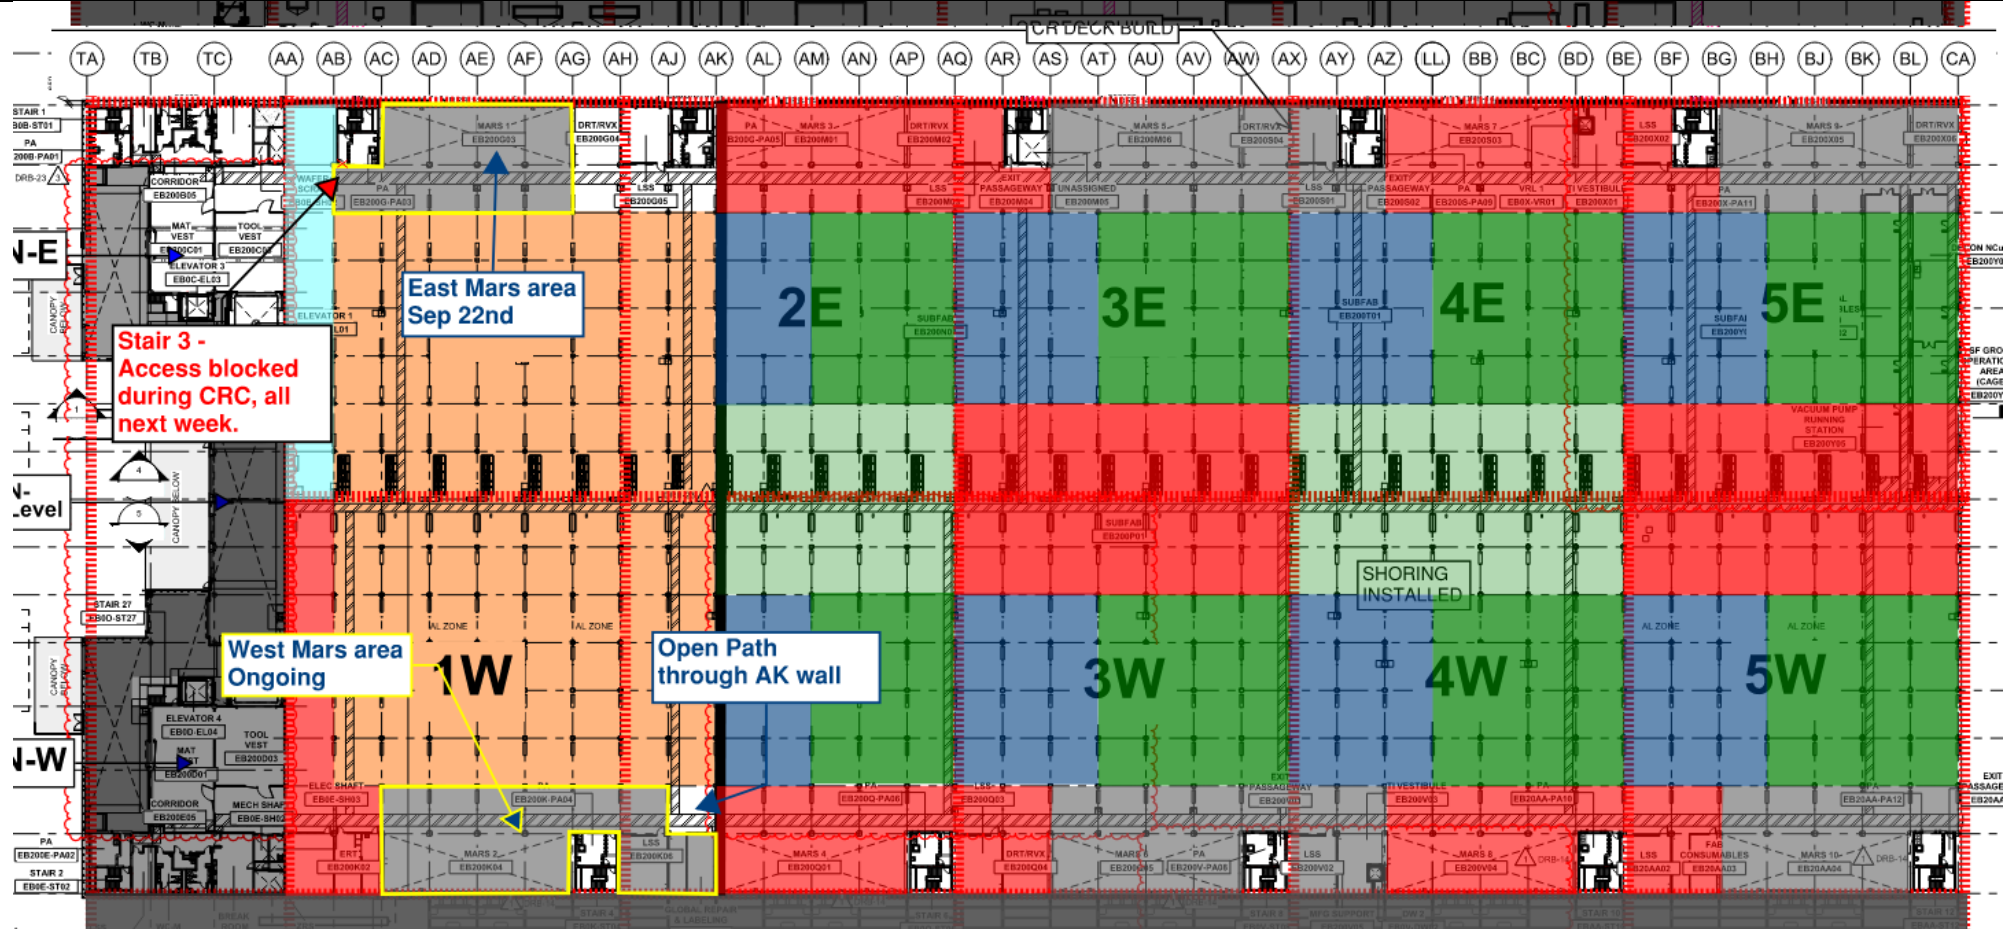



SUBFUB PRESSURE TEST EXCLUSION ZONES

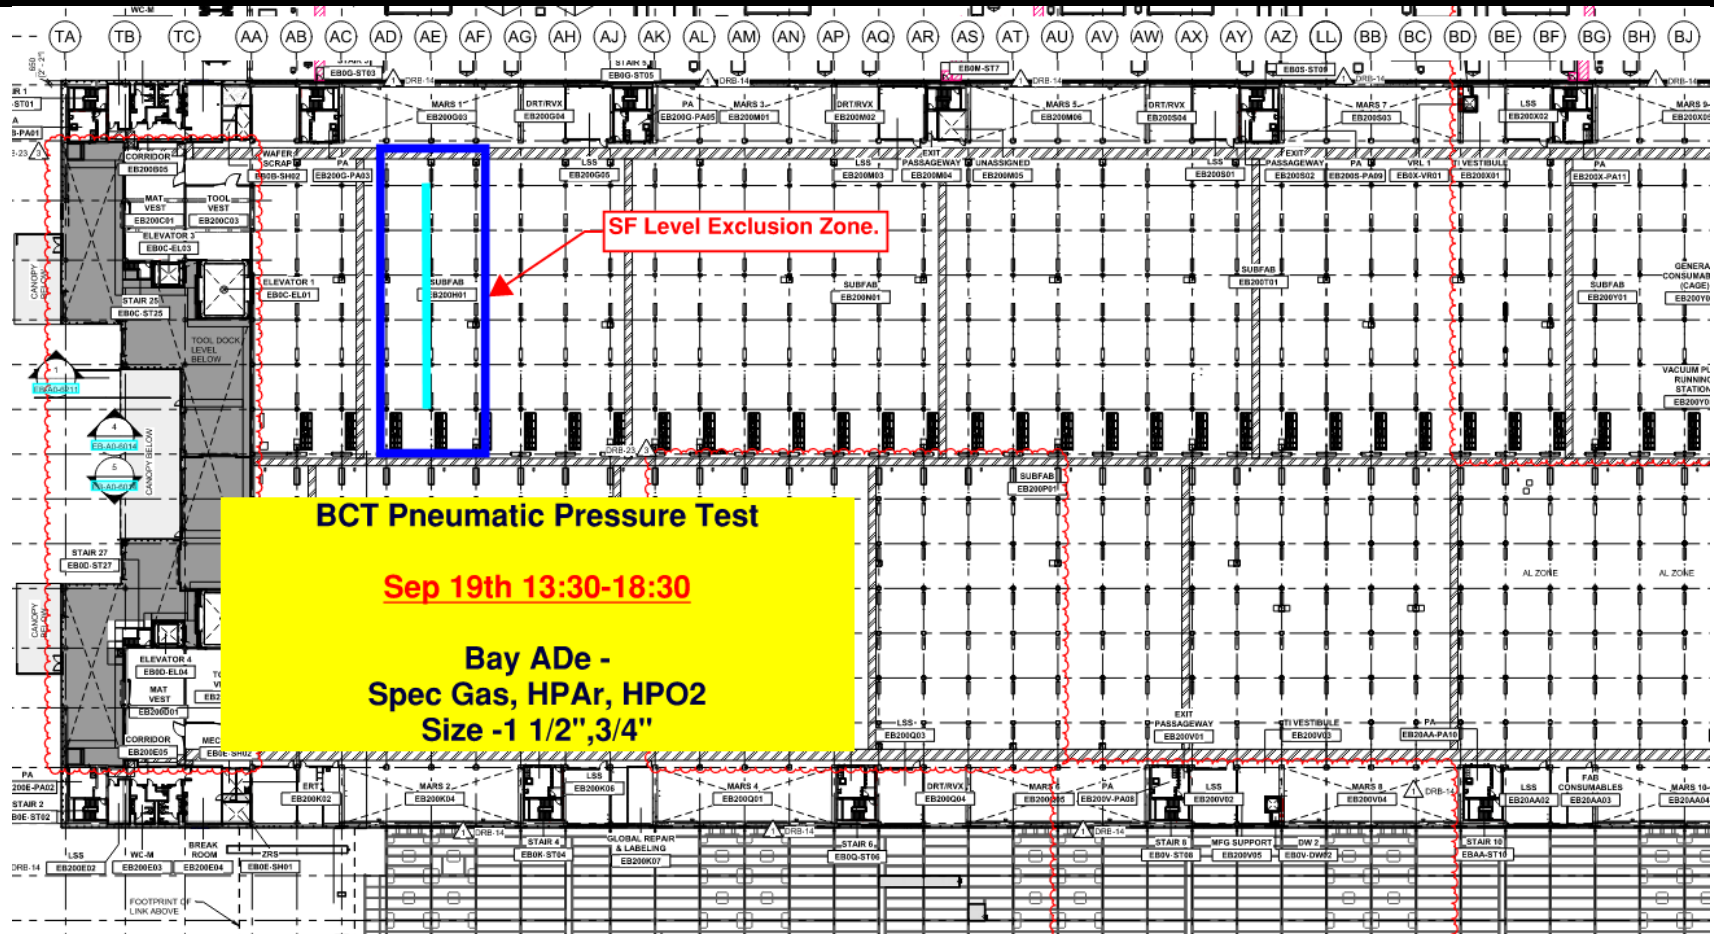




SUBFAB BUILDOUT MOD 2

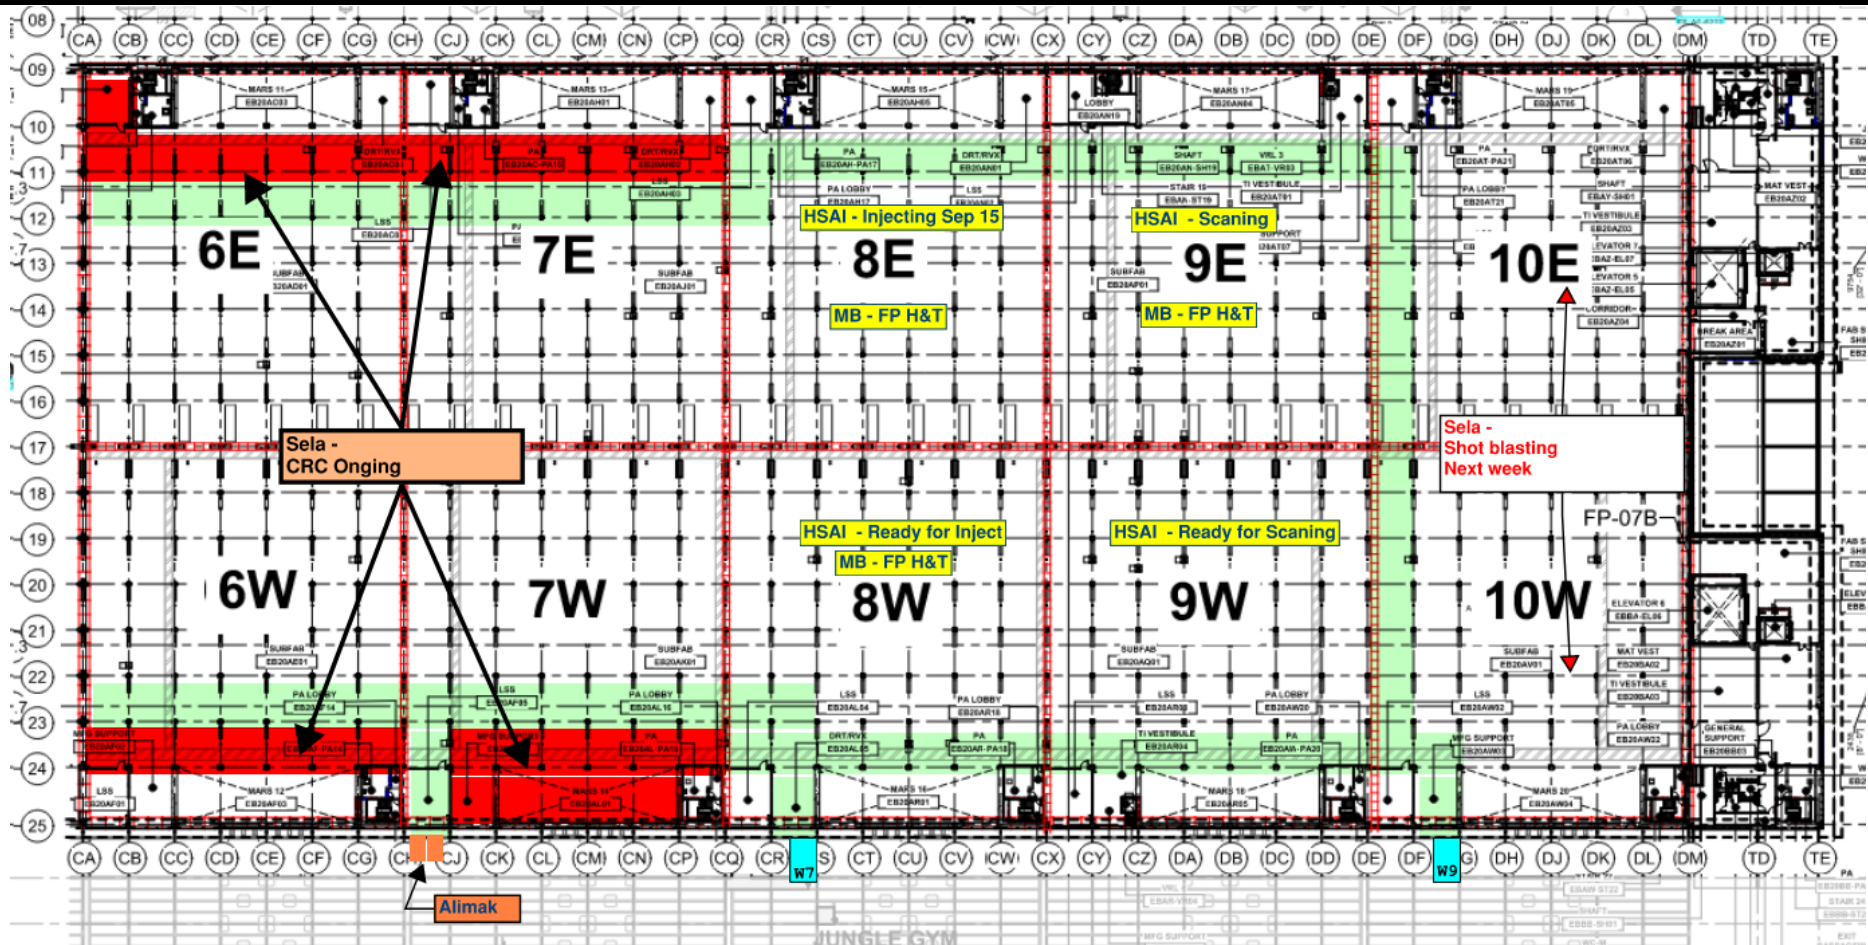

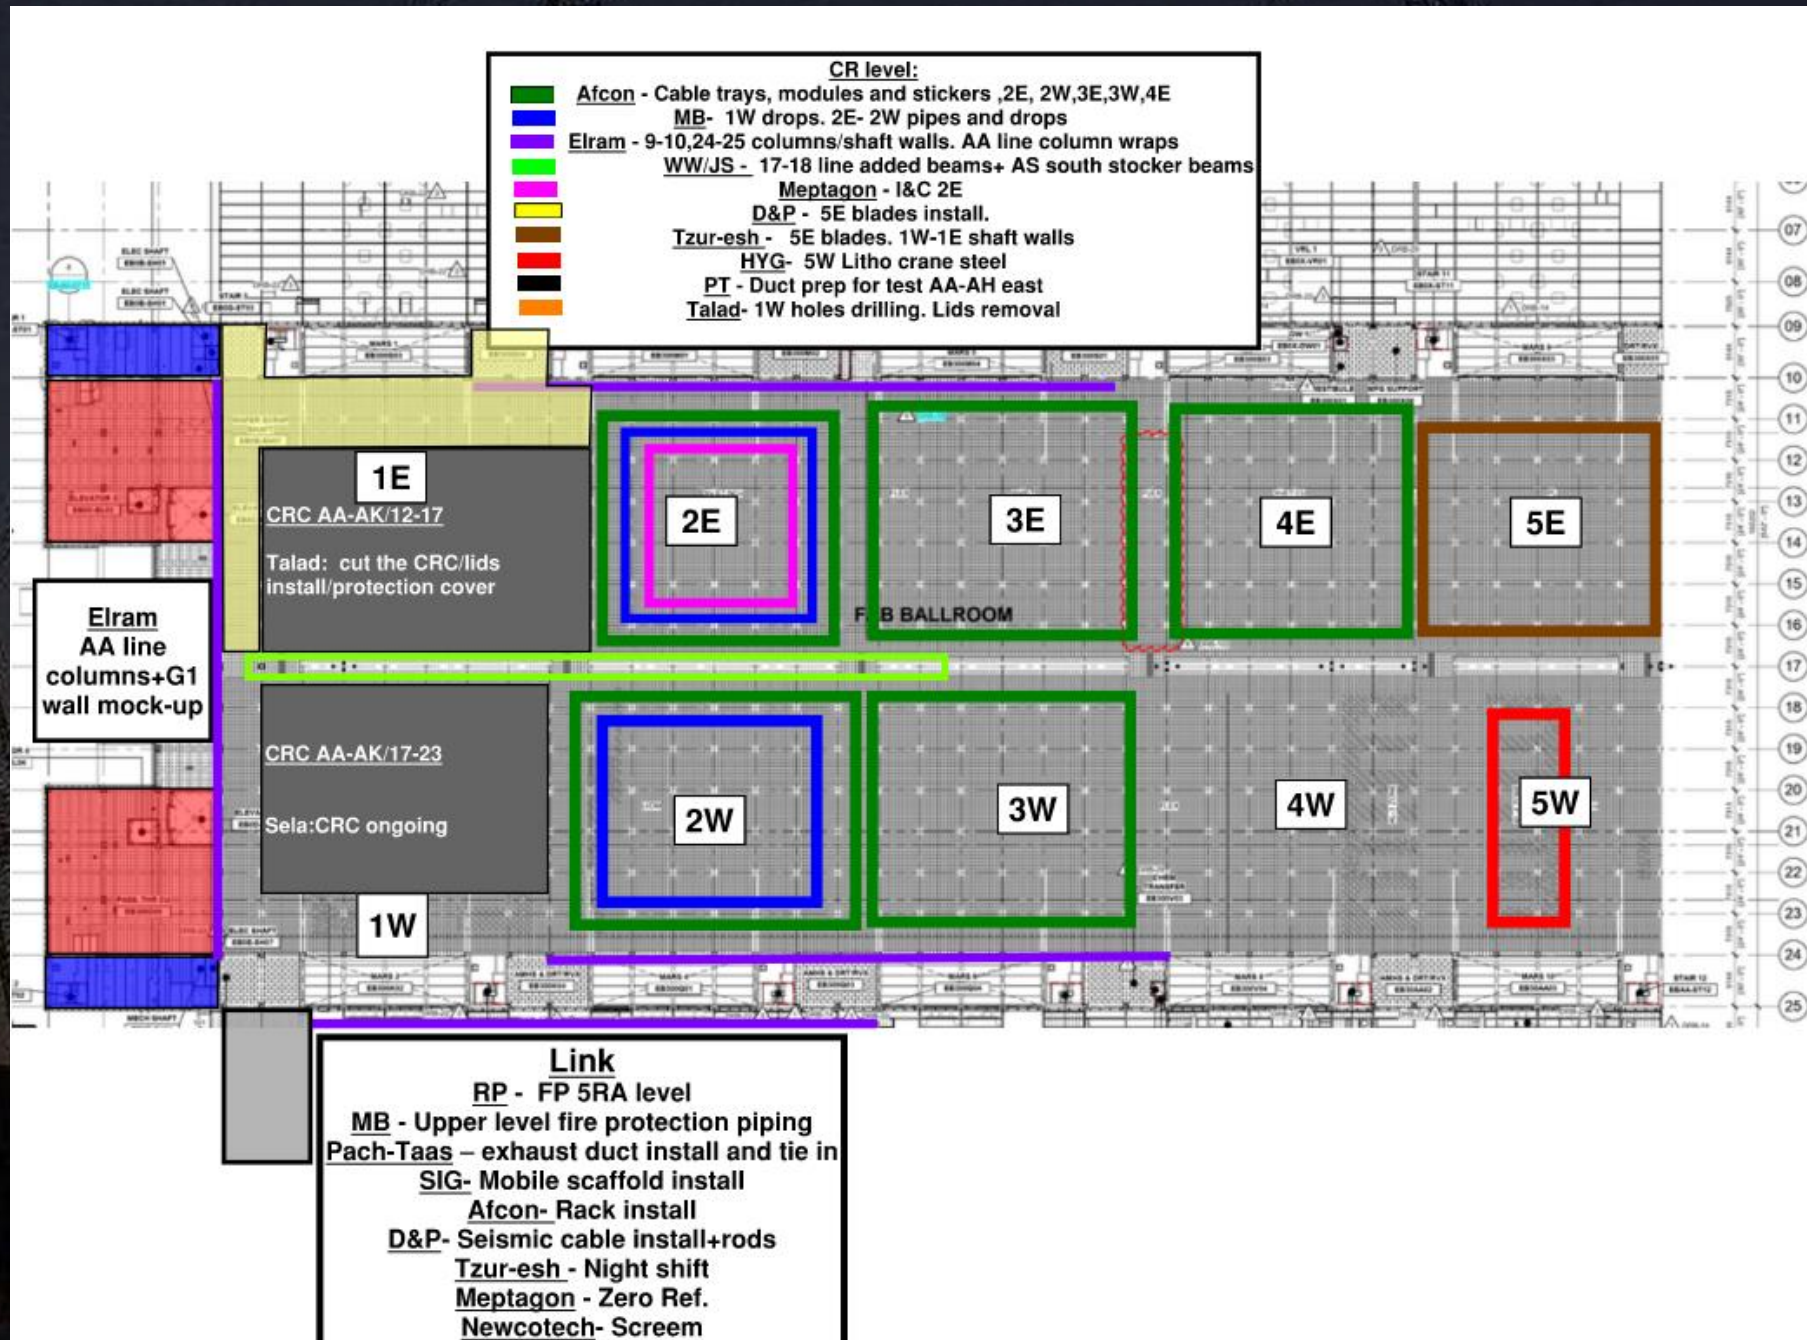

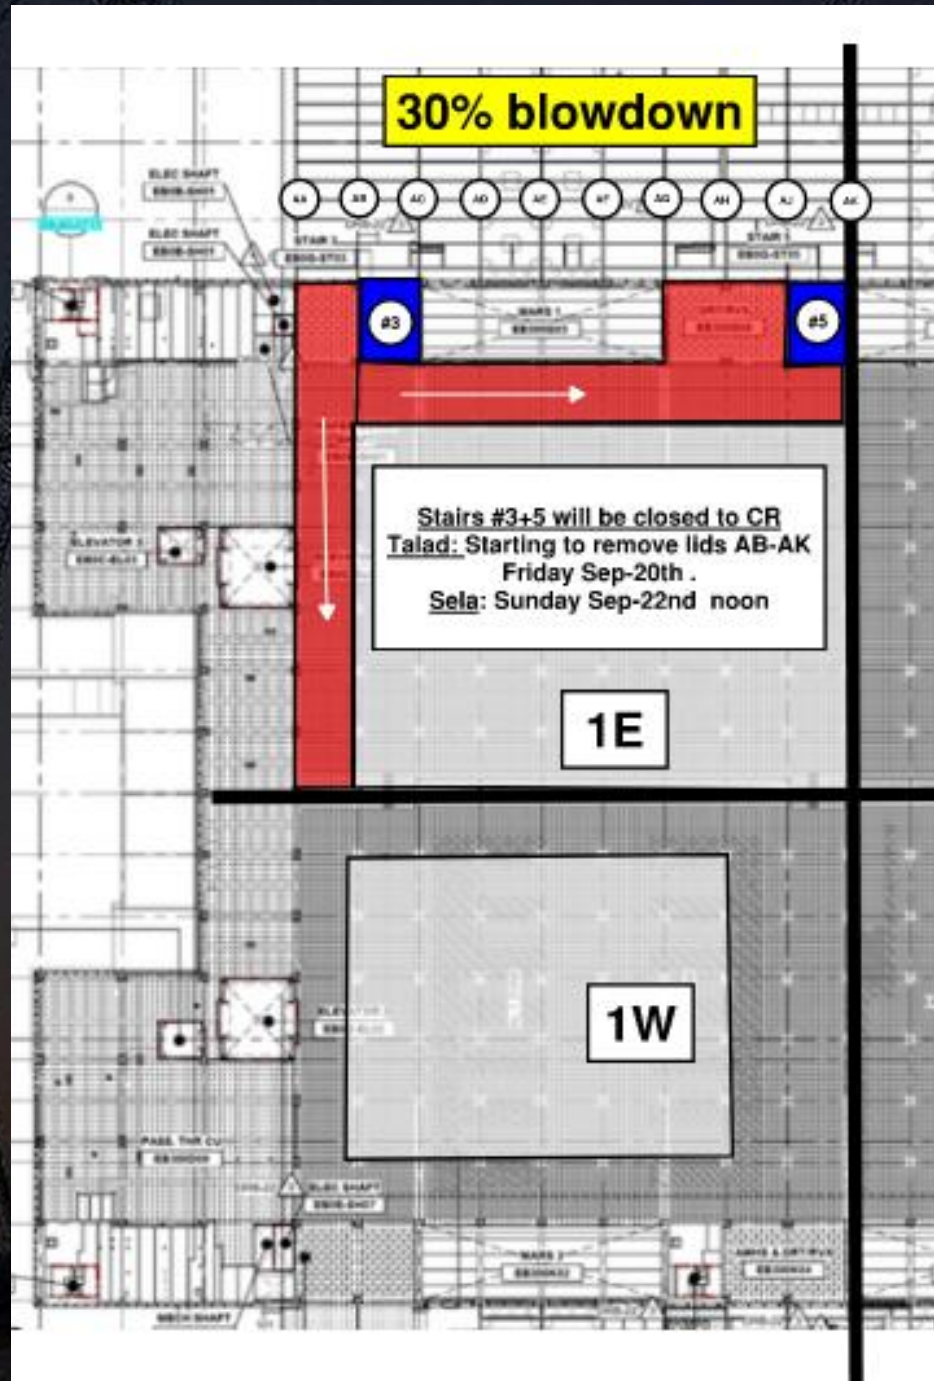

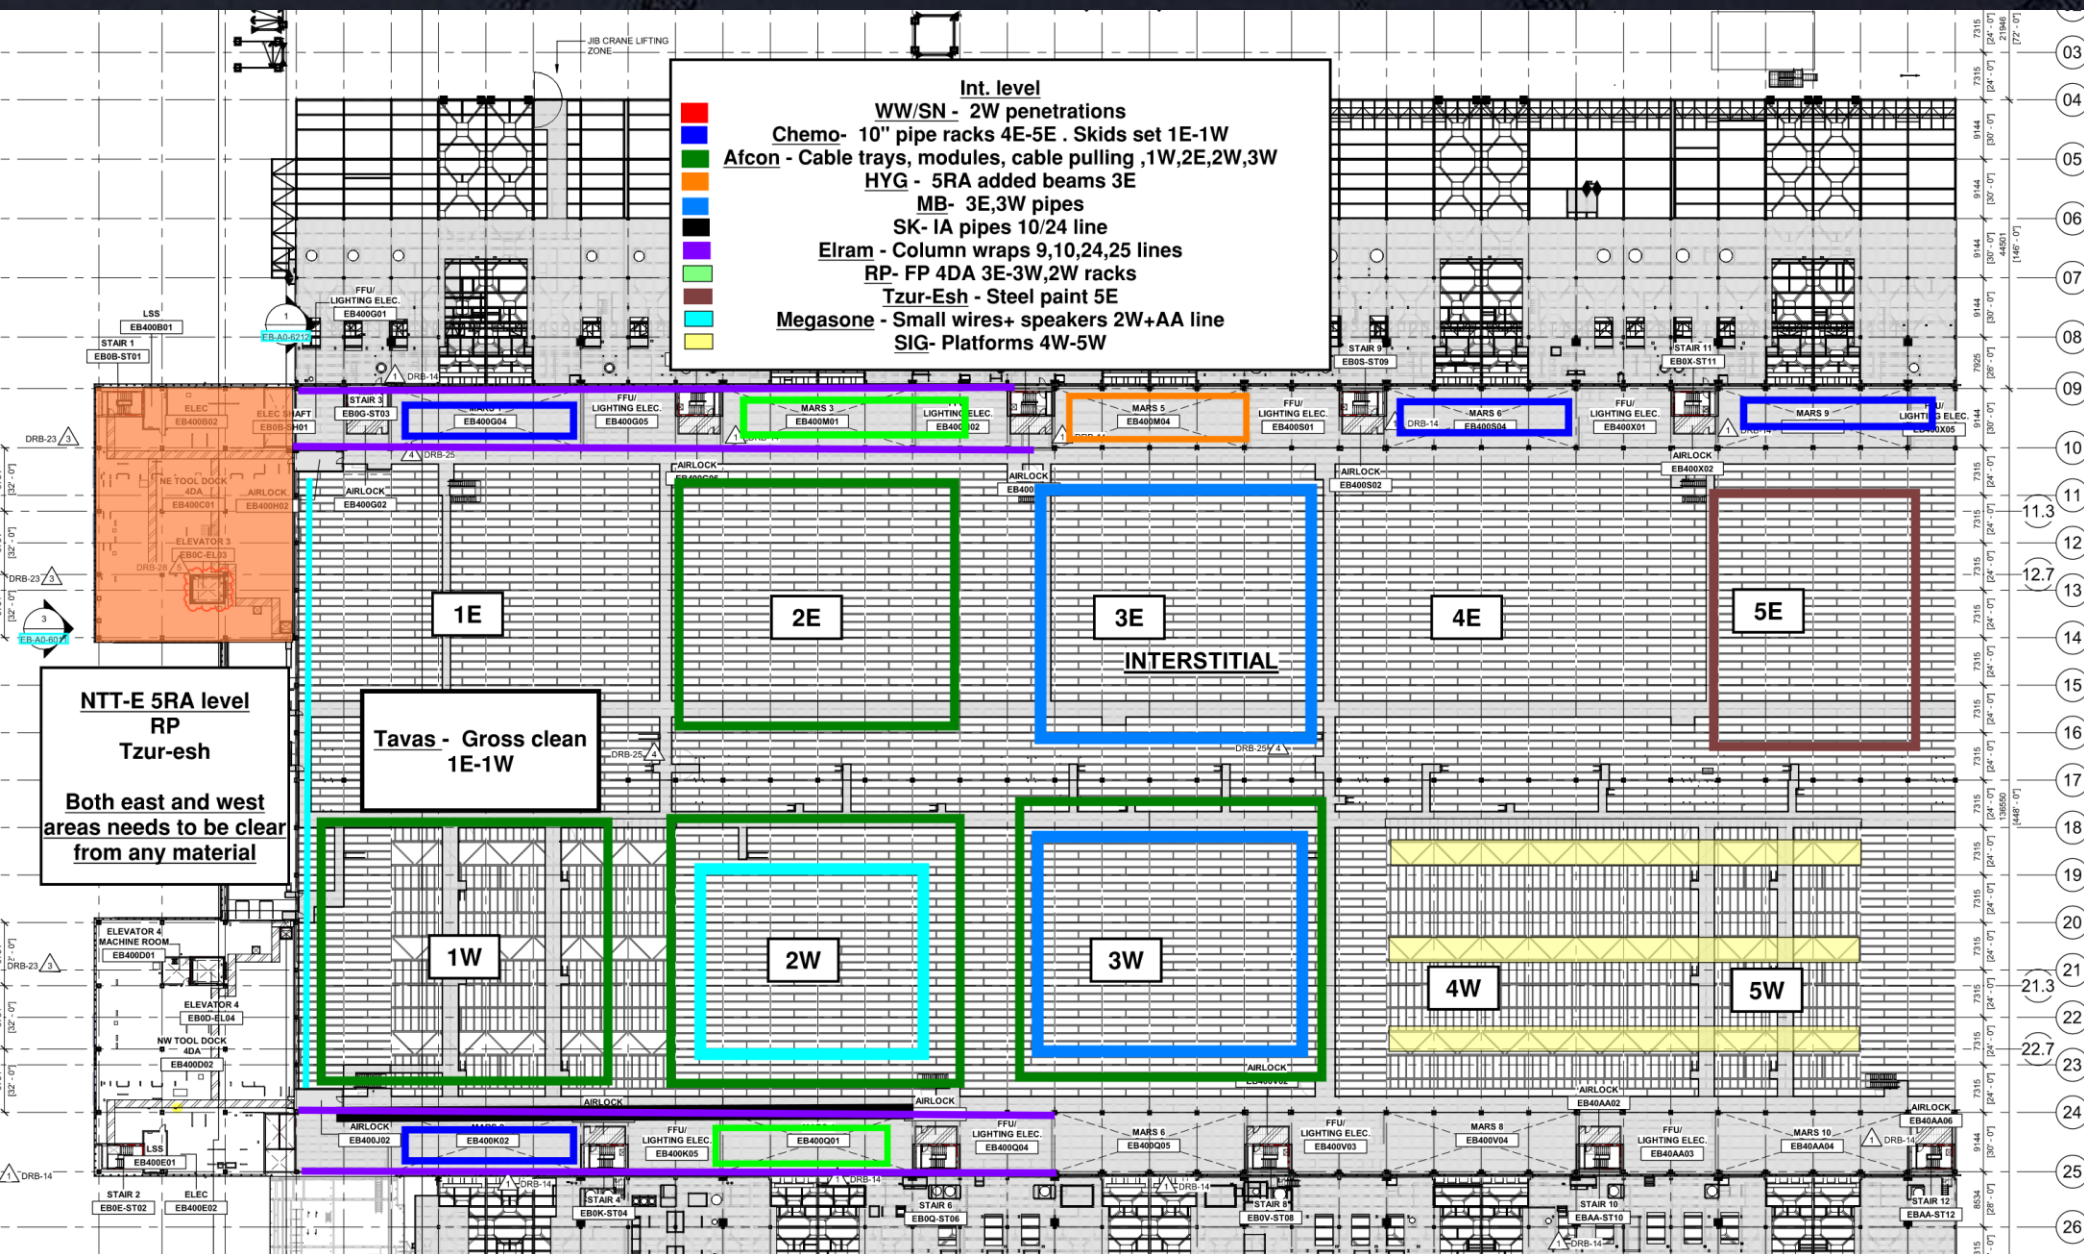

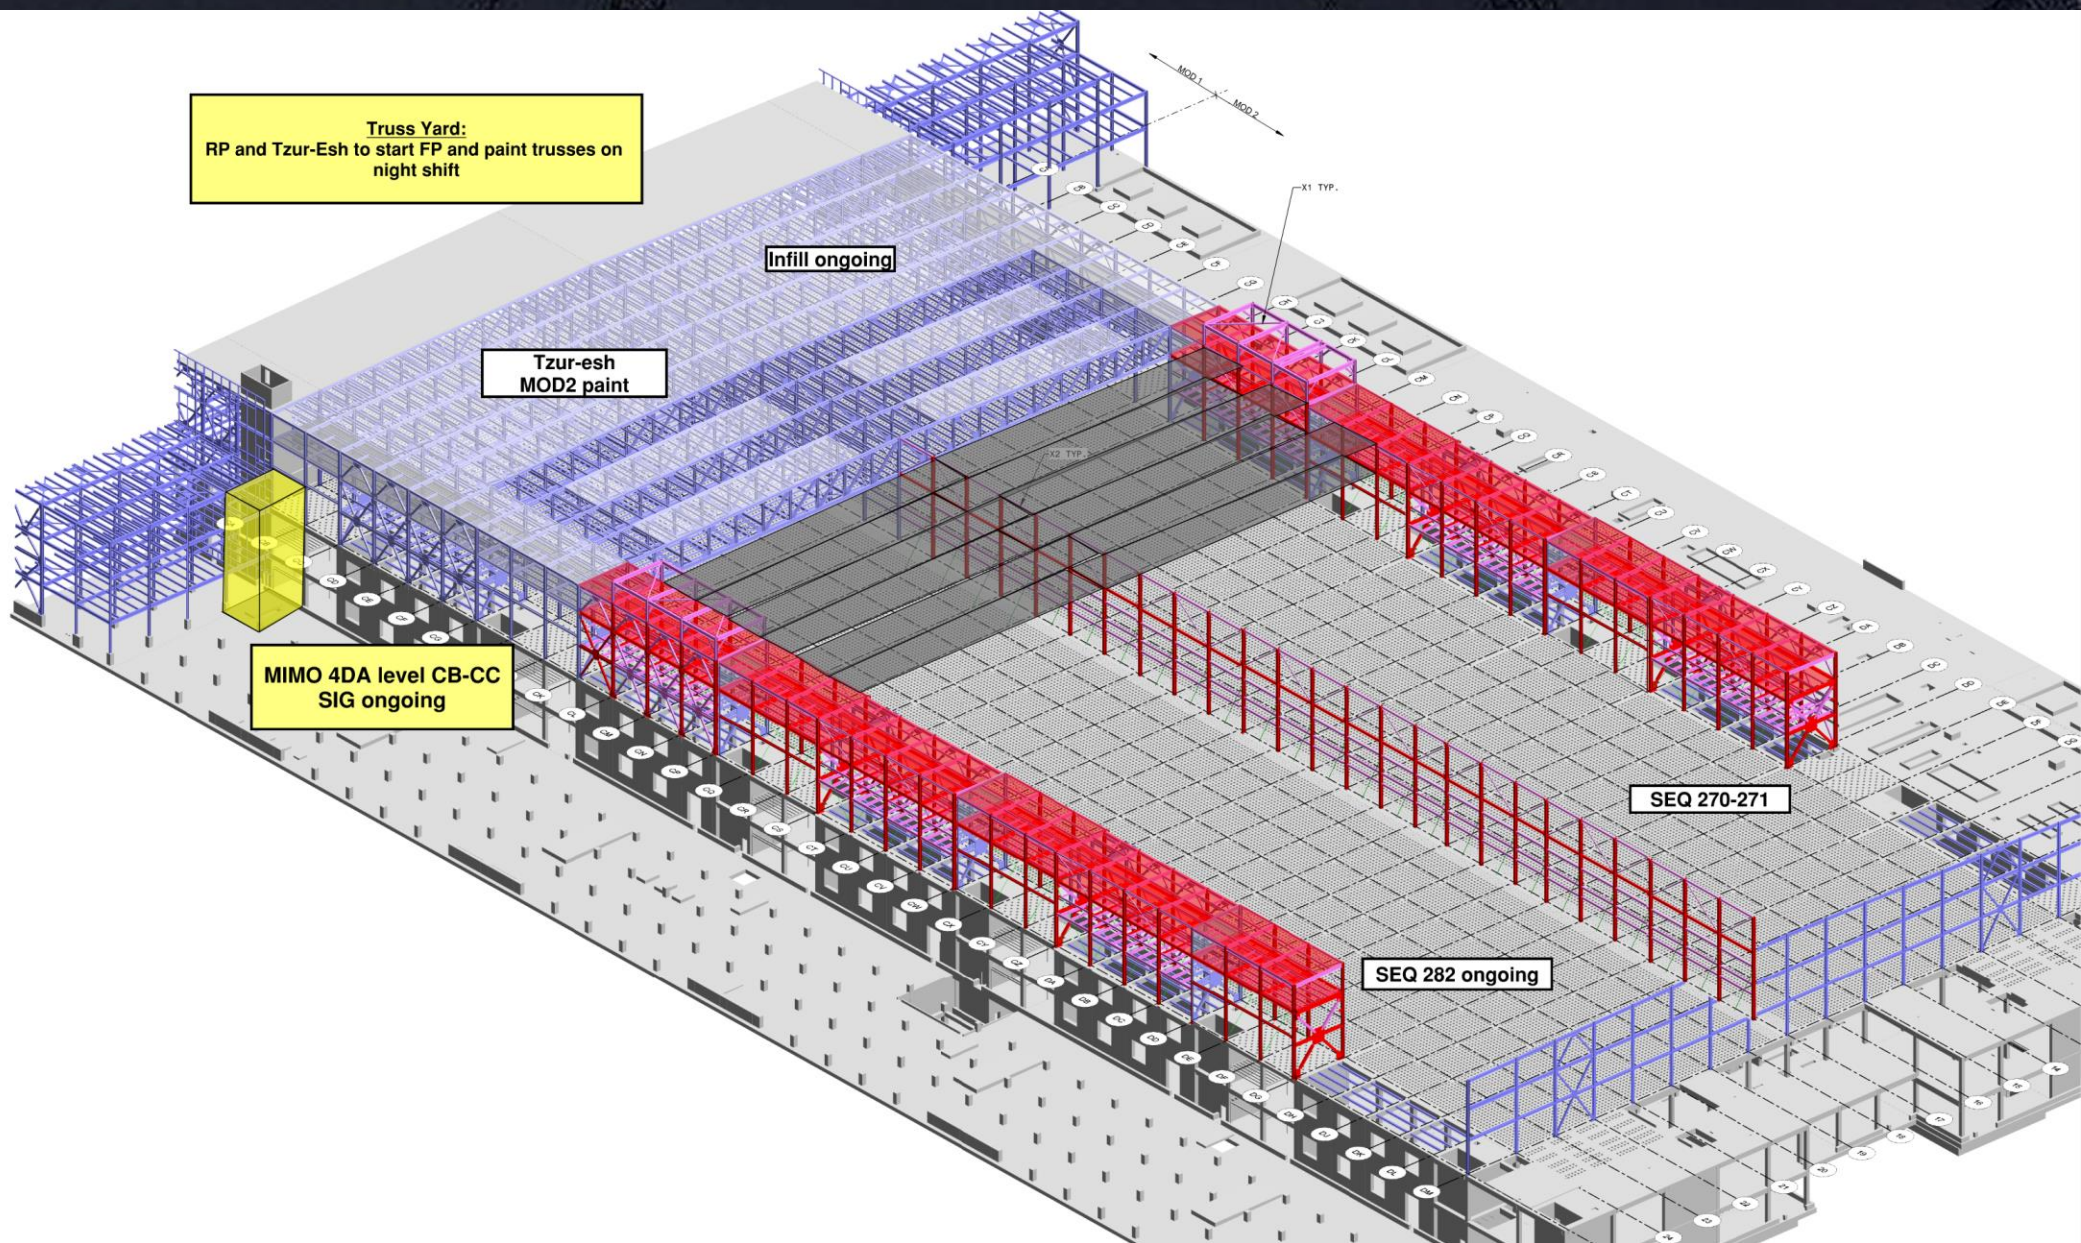



Clean Room Wall Of Shame

SN- Girts





Sela





Elram



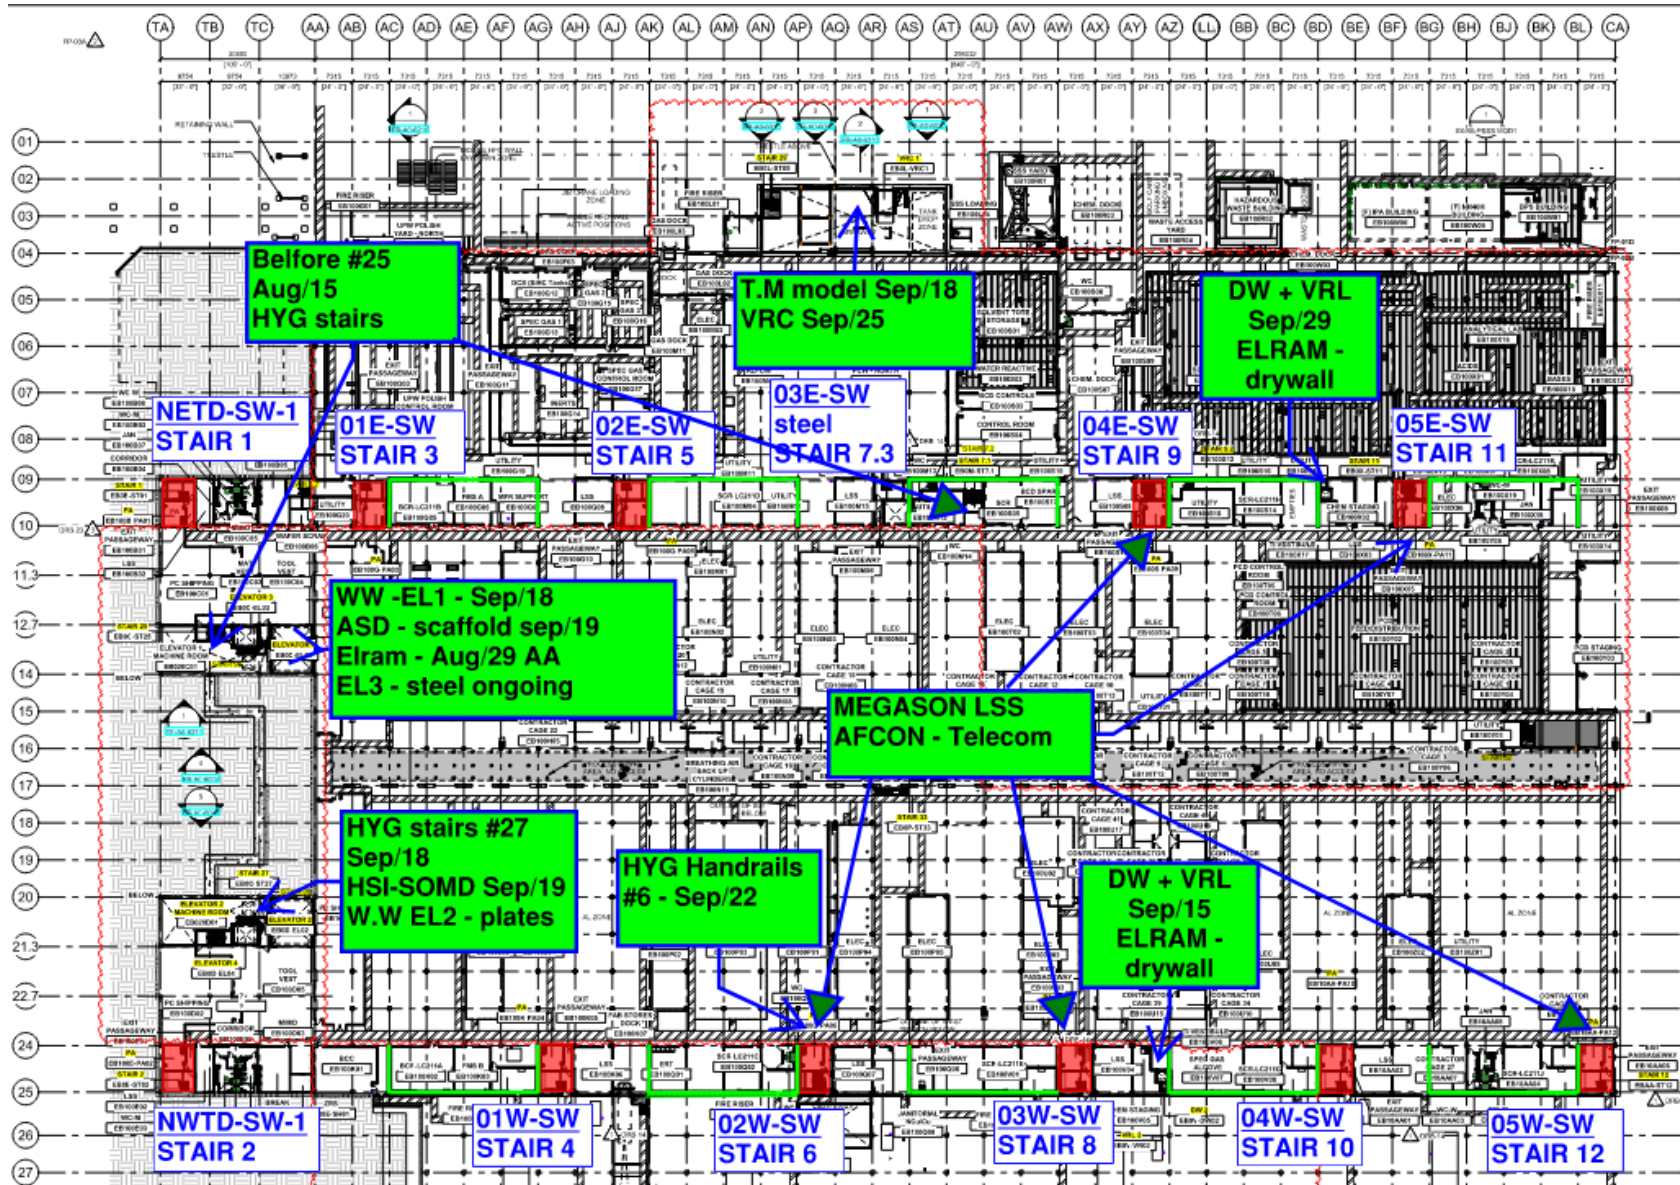

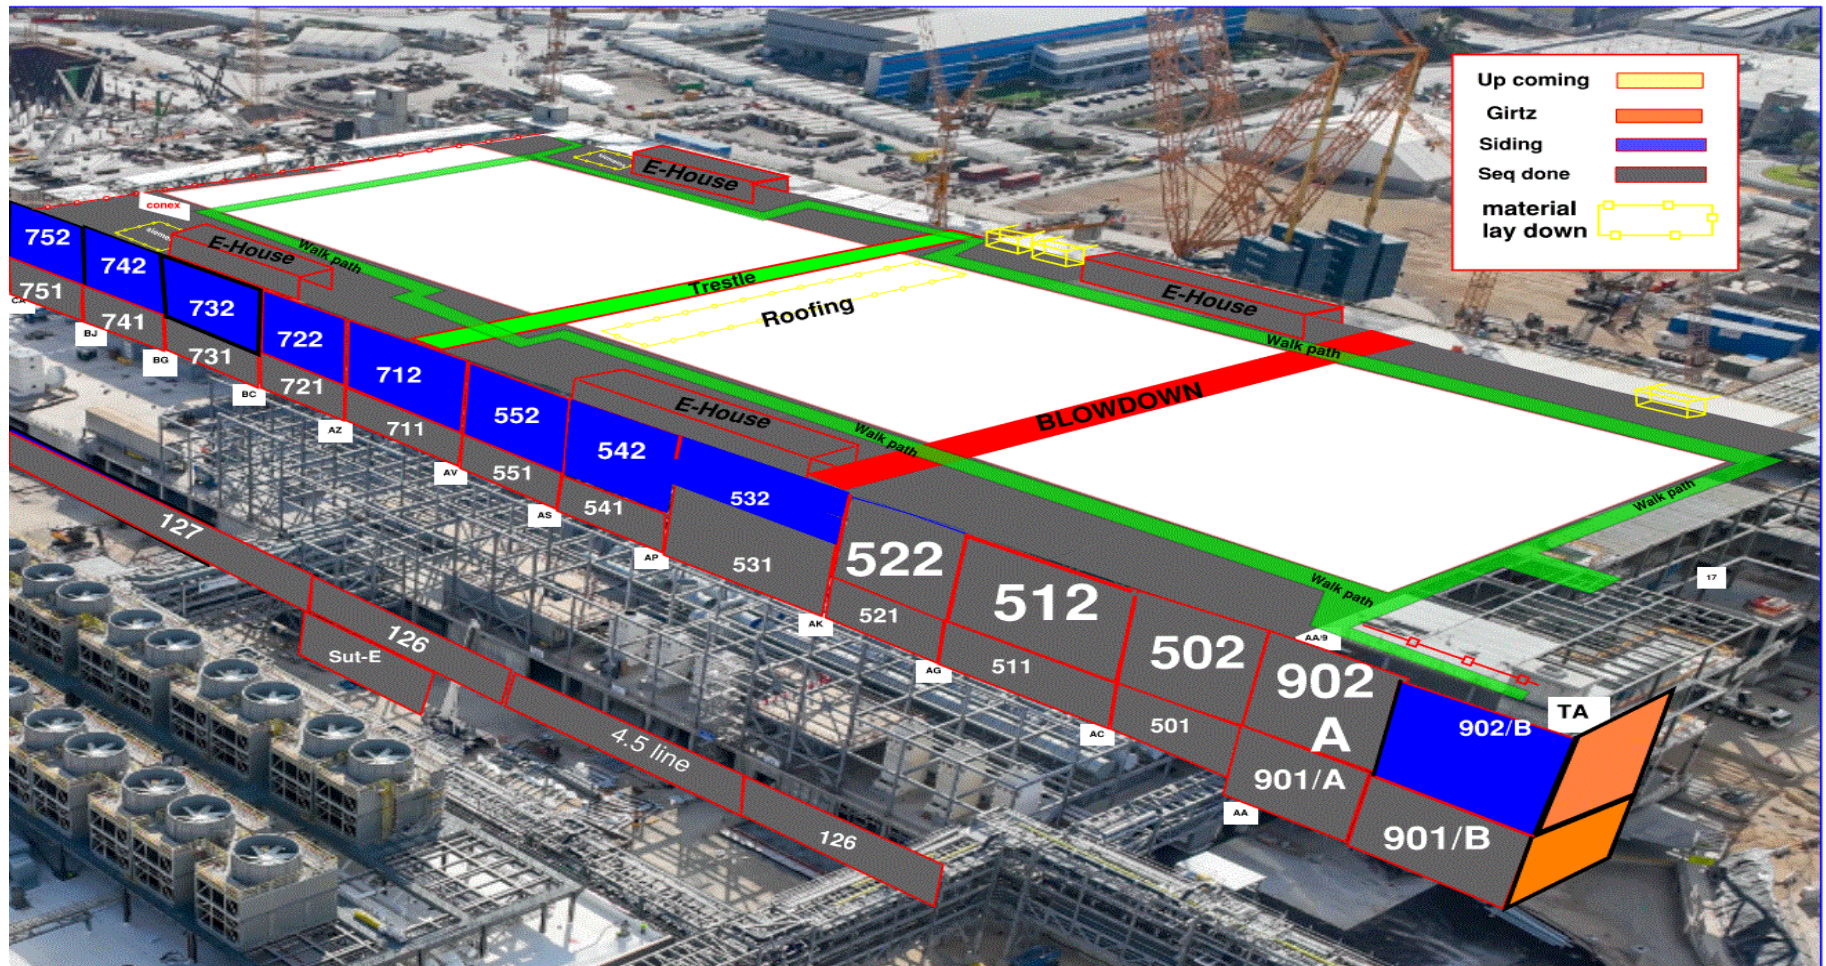

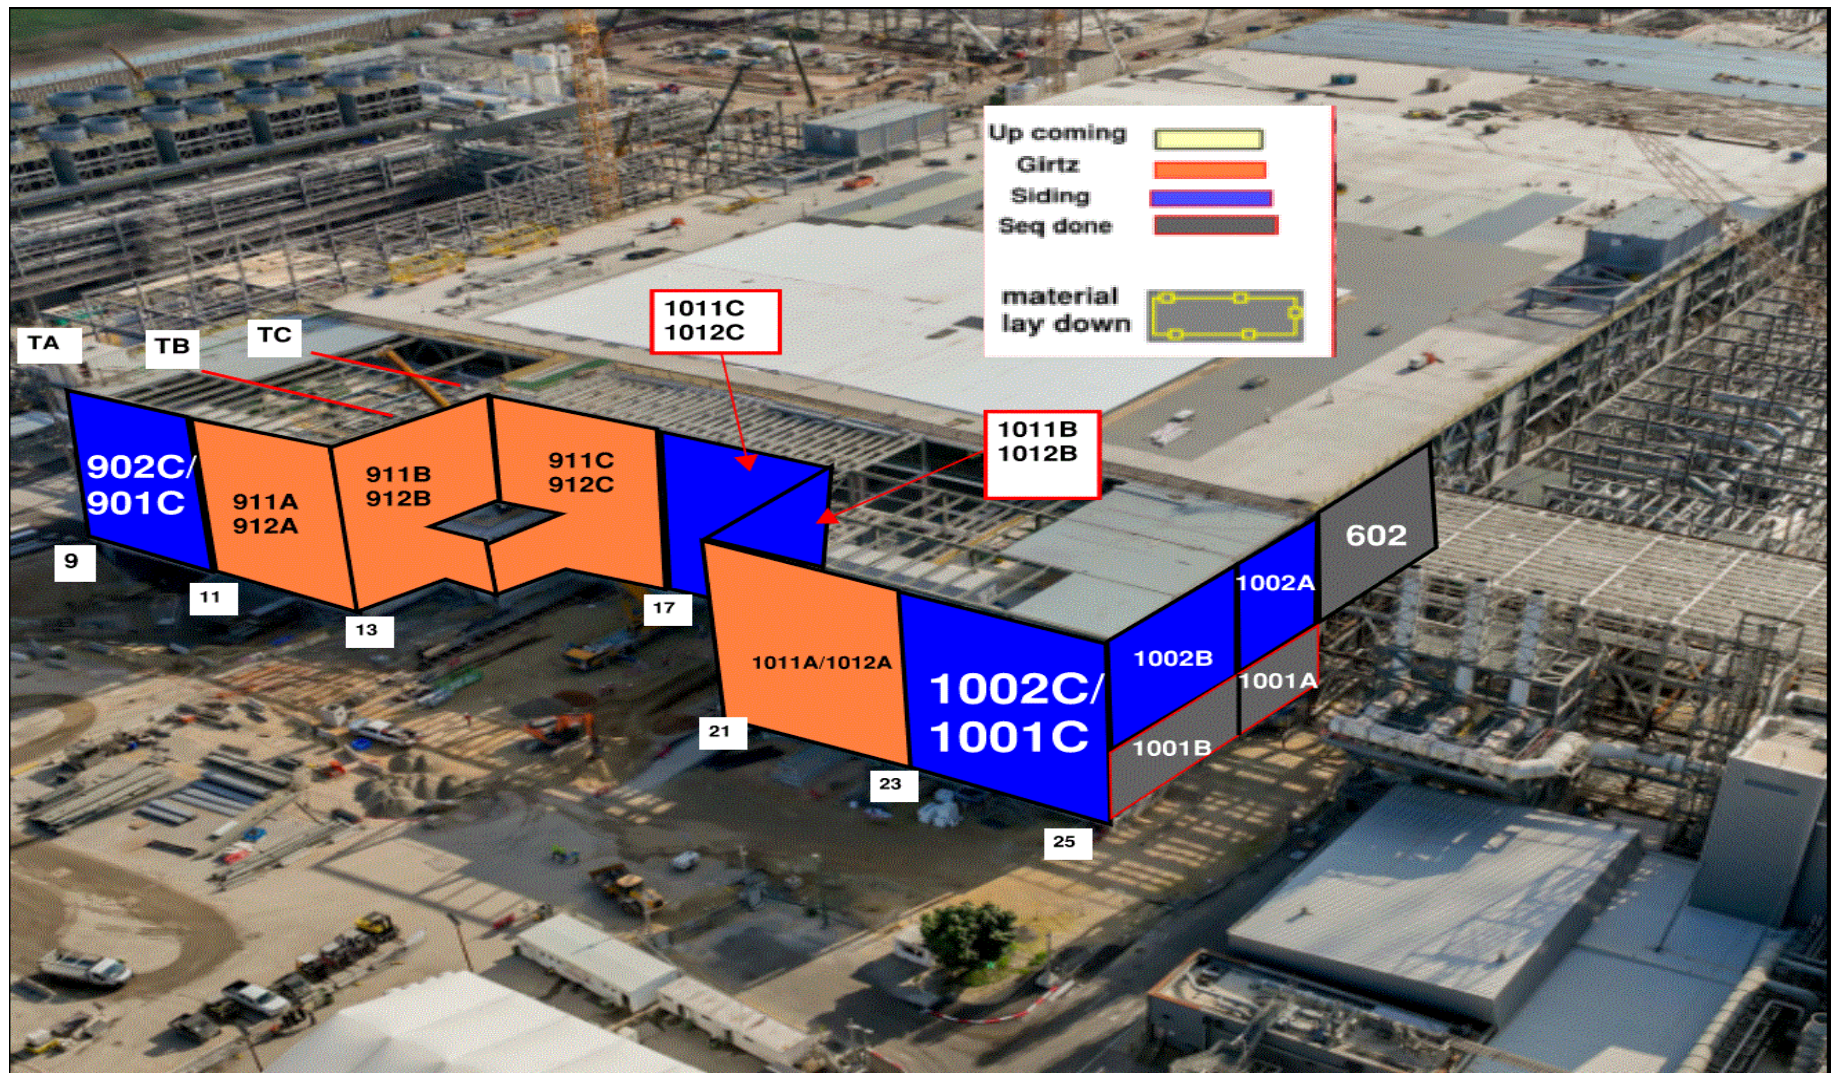

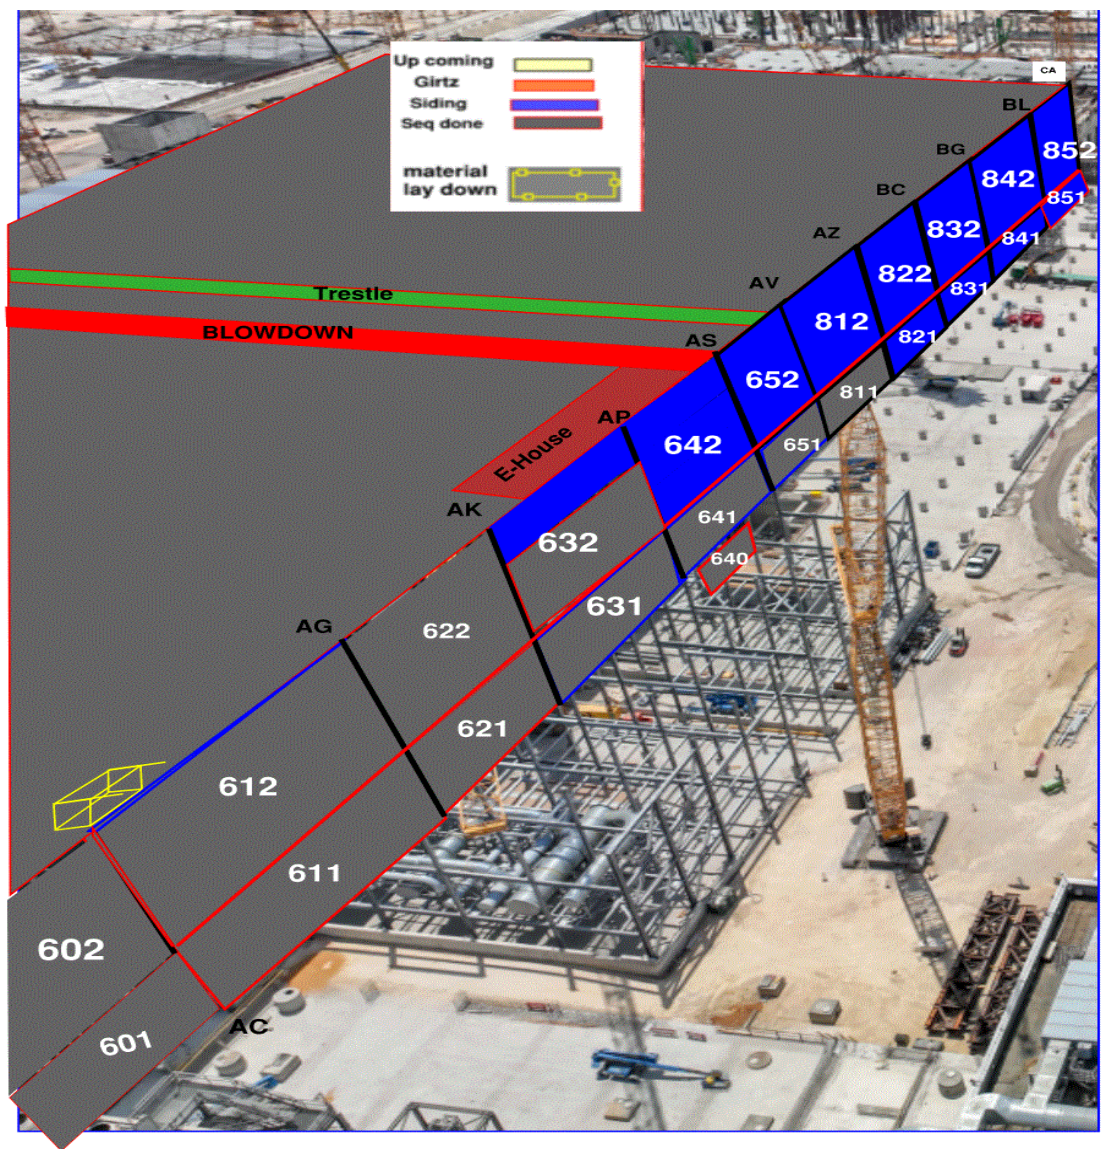

Siding - West FAB - JYG

BLOWDOWN 30%

	Below 100%																																												
	TA	TB	TC	AA	AB	AC	AD	AE	AF	AG	AH	AJ	AK	AL	AM	AN	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA	BB	BC	BD	BE	BF	BG	BH	BI	BK	BL	CA						
	1001 / 1002			601 / 602		611 / 612				621 / 622				631 / 632				641 / 642				651 / 652				811 / 812				821 / 822				831 / 832				841 / 842				851 / 852			
Total	20	20	20	15	10	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31					
Installed	8	14	10	12	10	31	31	31	31	31	31	31	31	31	24	23	13	14	14	14	6	6	6	6	14	14	14	14	14	6	6	9	13	1	1	1	1	1	0	0	0	0			
%	29%	50%	36%	80%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	77%	74%	42%	45%	45%	45%	19%	19%	19%	19%	45%	45%	45%	45%	45%	19%	19%	29%	42%	3%	3%	3%	3%	8%	8%	8%	8%				
SRA	0	0	0		1		1	1	1	1	1	1	1	1		0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0			
	0	0	0	1	1											0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0			
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0			
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0			
4DA	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
3FK	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
3FA	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0													0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
2SA SF	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		
UL	0	0	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0		


Link

[illegible]

PSSS.1

Utility Level
1YA


PSSS Roof
2SA

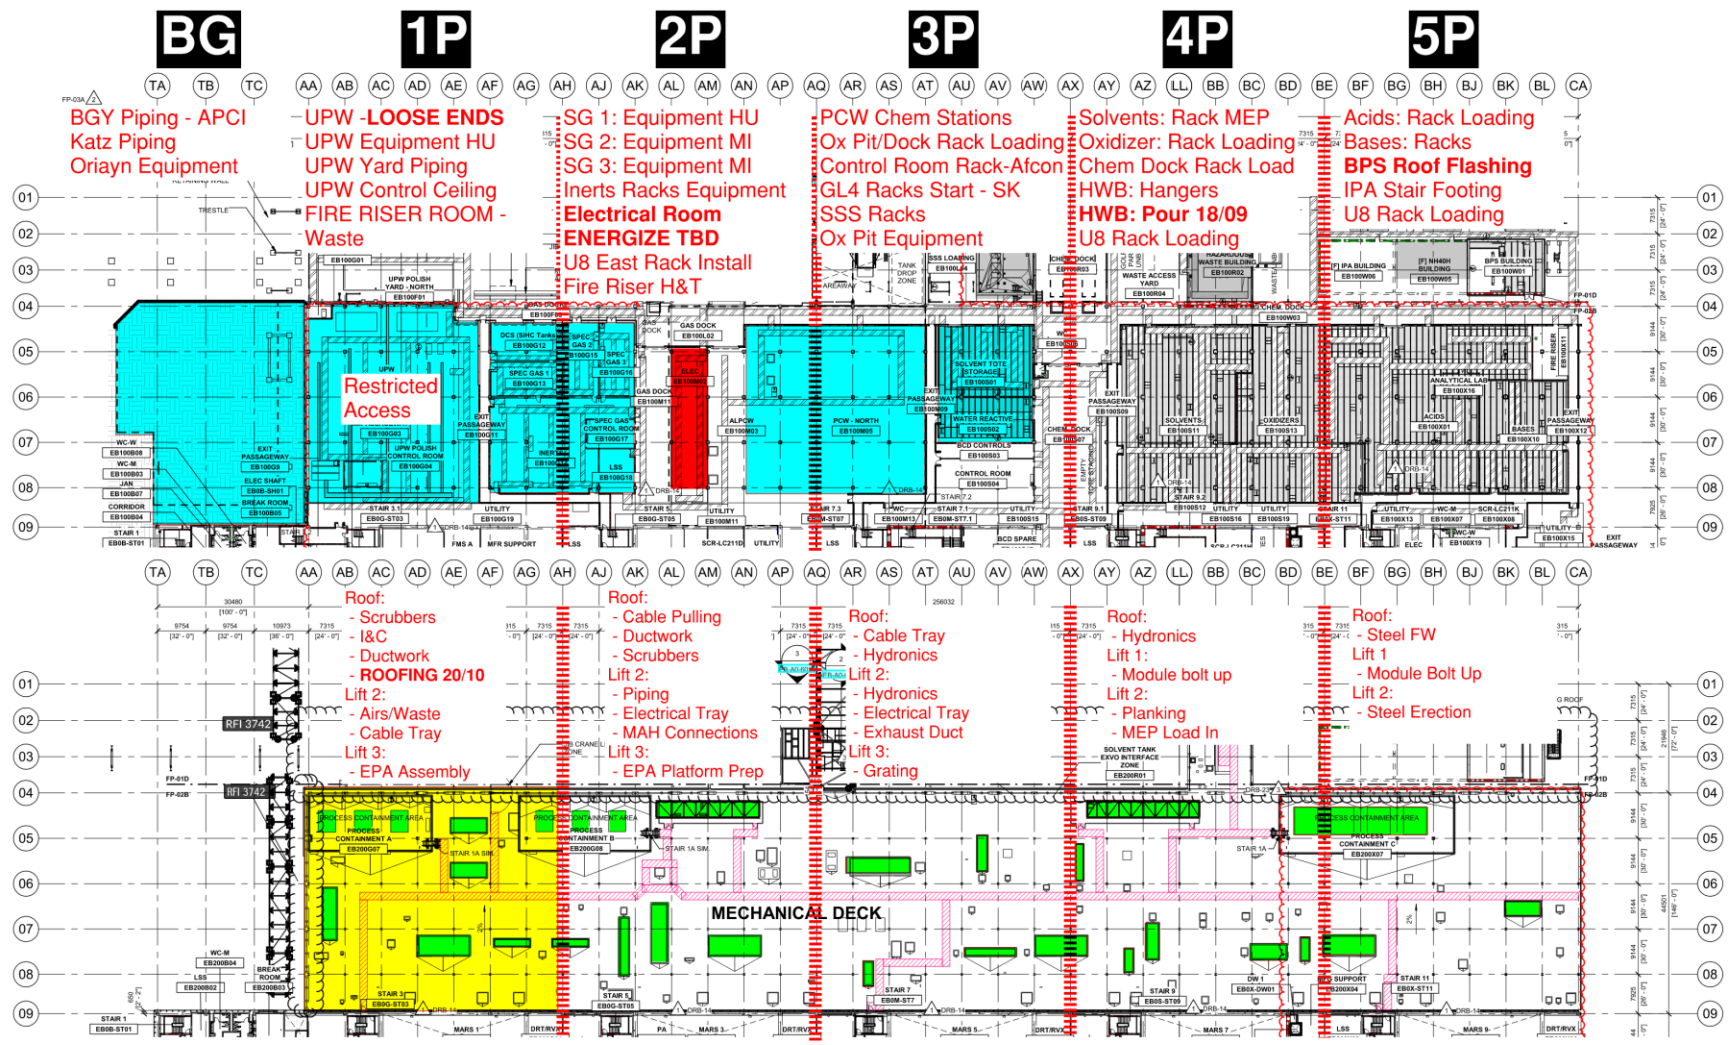

PSSS.2

Utility Level
1YA

PSSS Roof
2SA

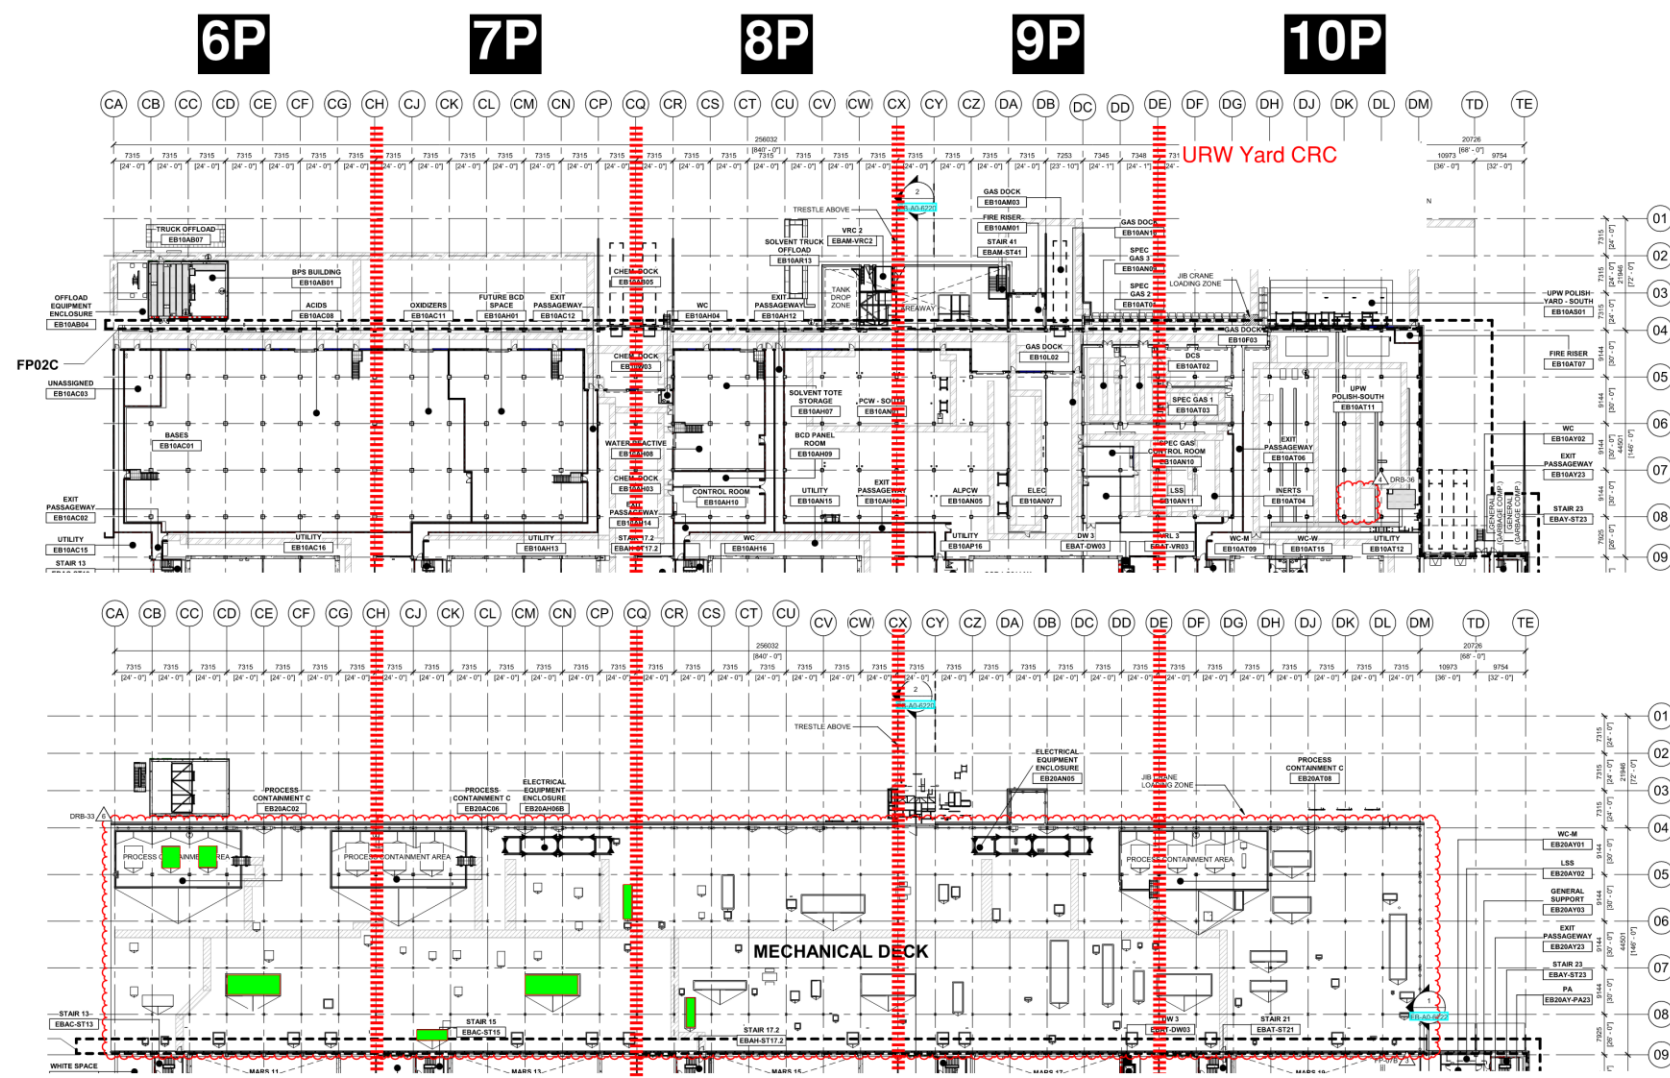

PSSS

4P VFD Set


Crane Mats – 19/09

DMAG Move – 20/09


Hoist VFD – 24/09




PSSS DMAG ROAD CLOSURES

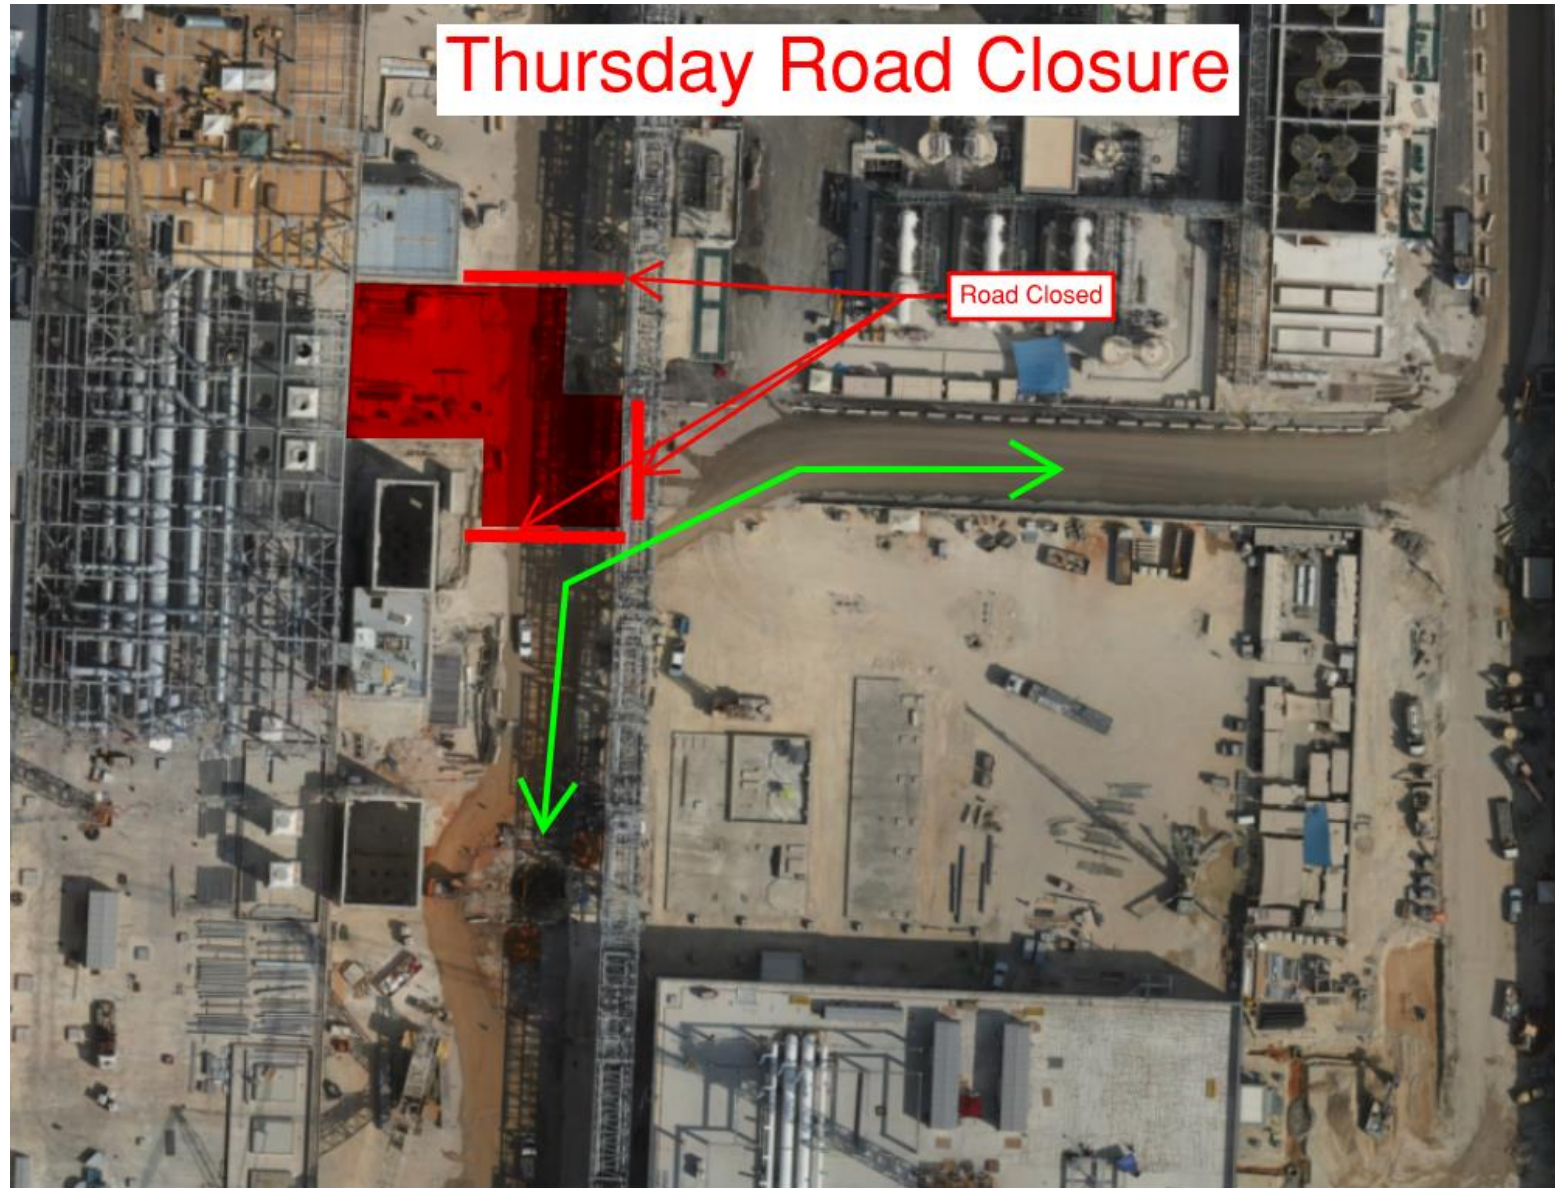


PSSS DMAG ROAD CLOSURES

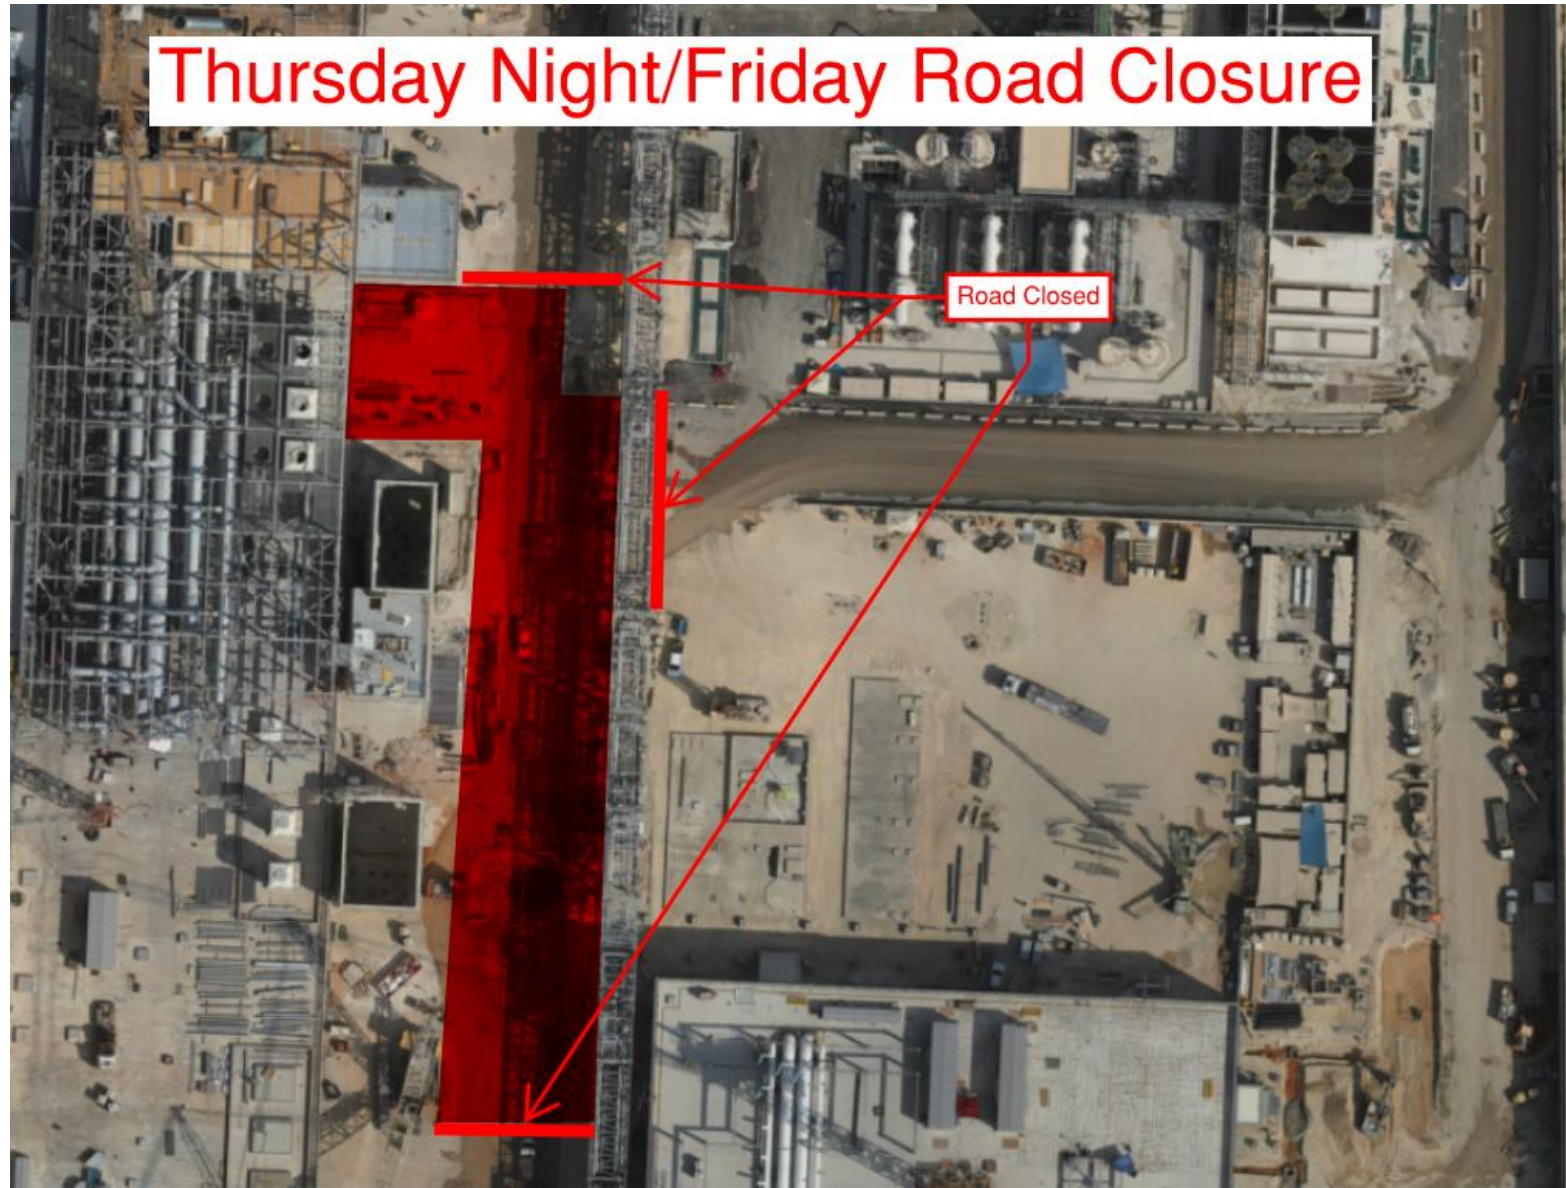

PSSS DMAG ROAD CLOSURES

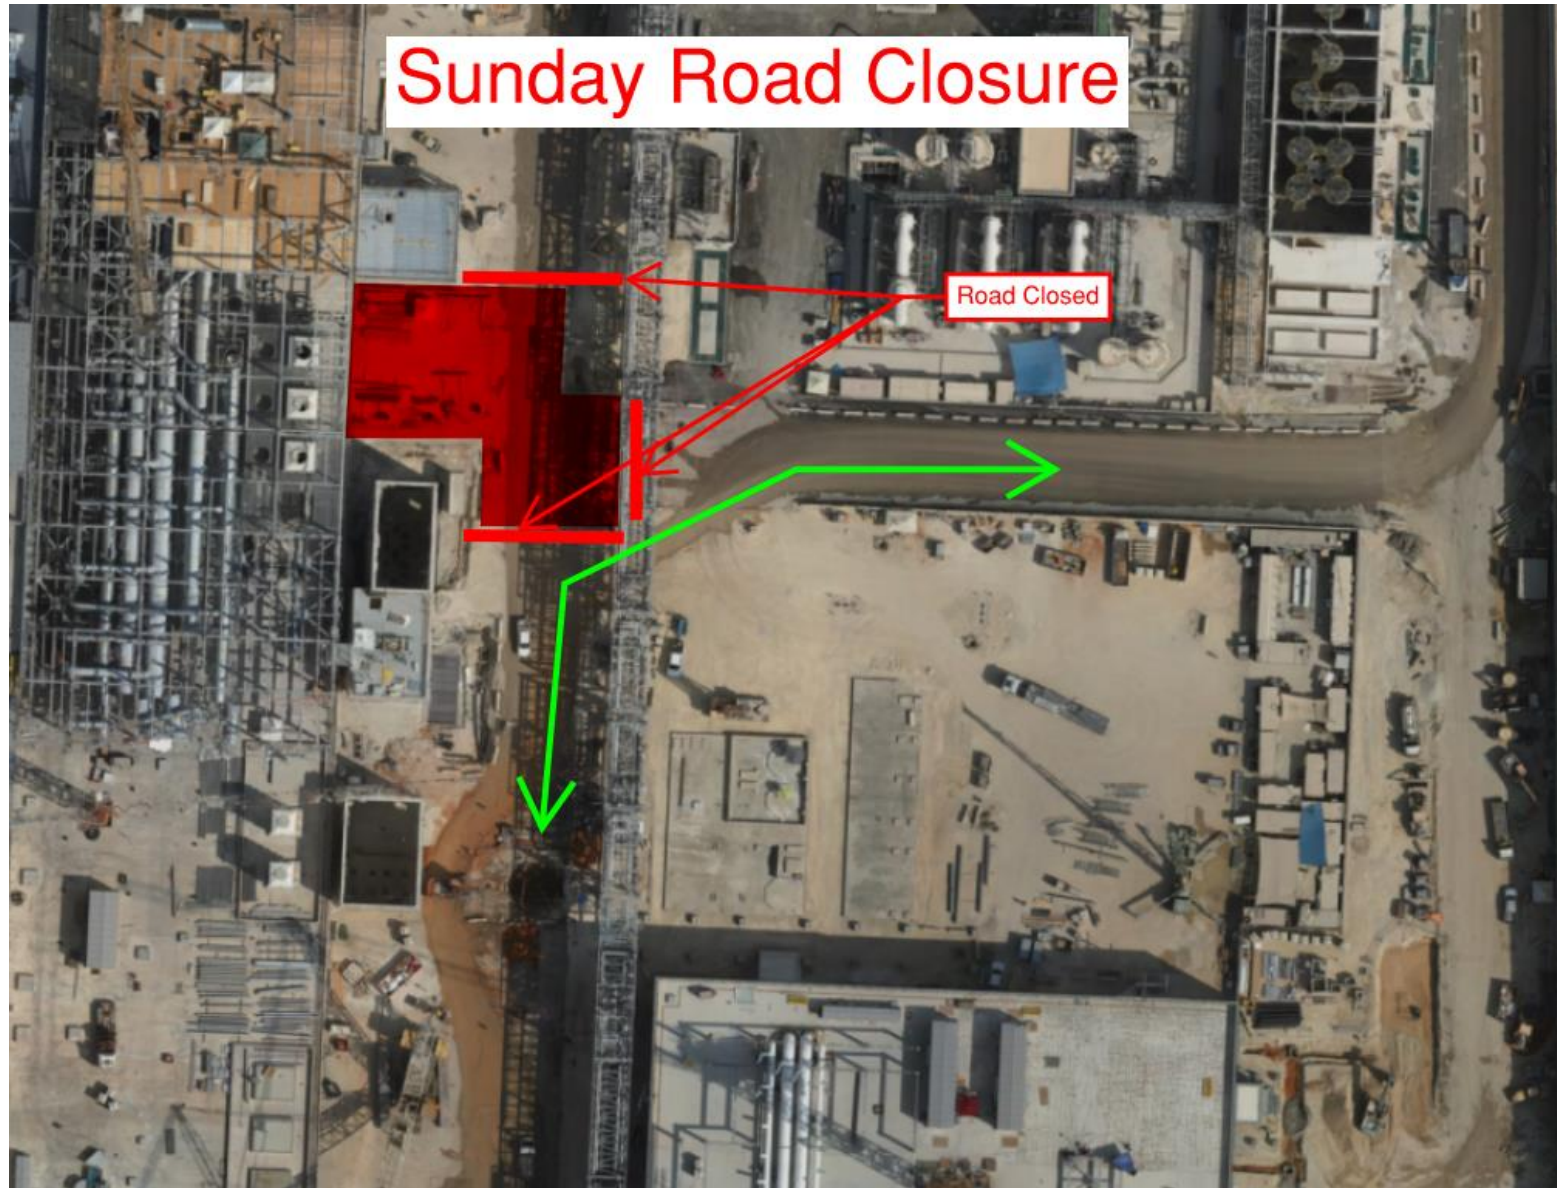



WJG 01J, 02J LIFT 2 & 3






WJG 03J, 04J, 05J LIFT 2 & 3





WJG UTILITY LEVEL BUILD OUT

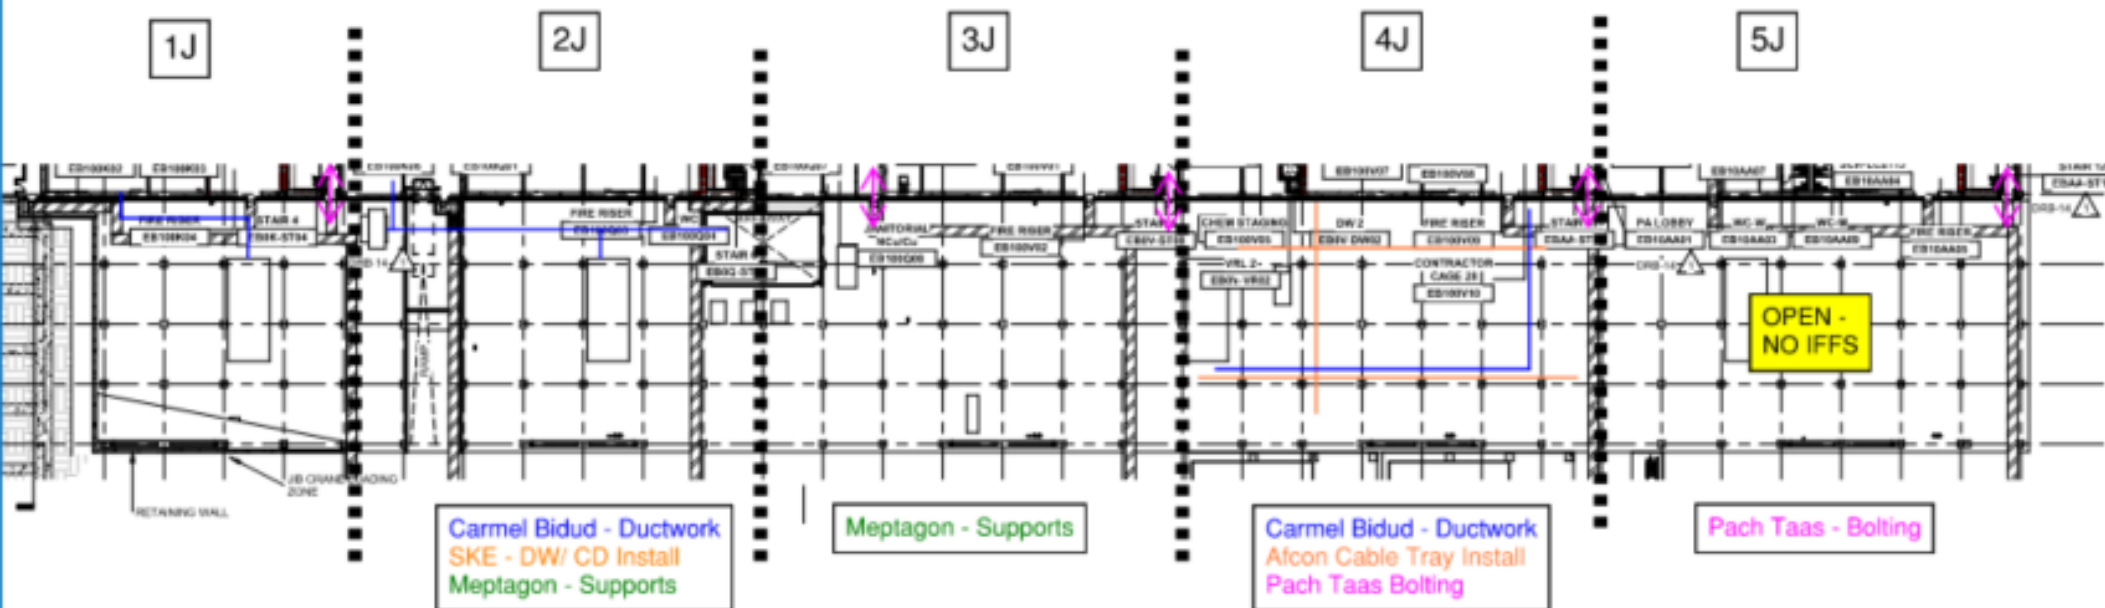






WJG Closed Night Shift 19/09/2024

SKE IA/PA PNEUMATIC TEST
138 PSI - 8 Hour
30m EXCLUSION ZONE
MAIN GL 28 @ UTILITY LEVEL
Date - 19/09/2024 20:00 - 06:00



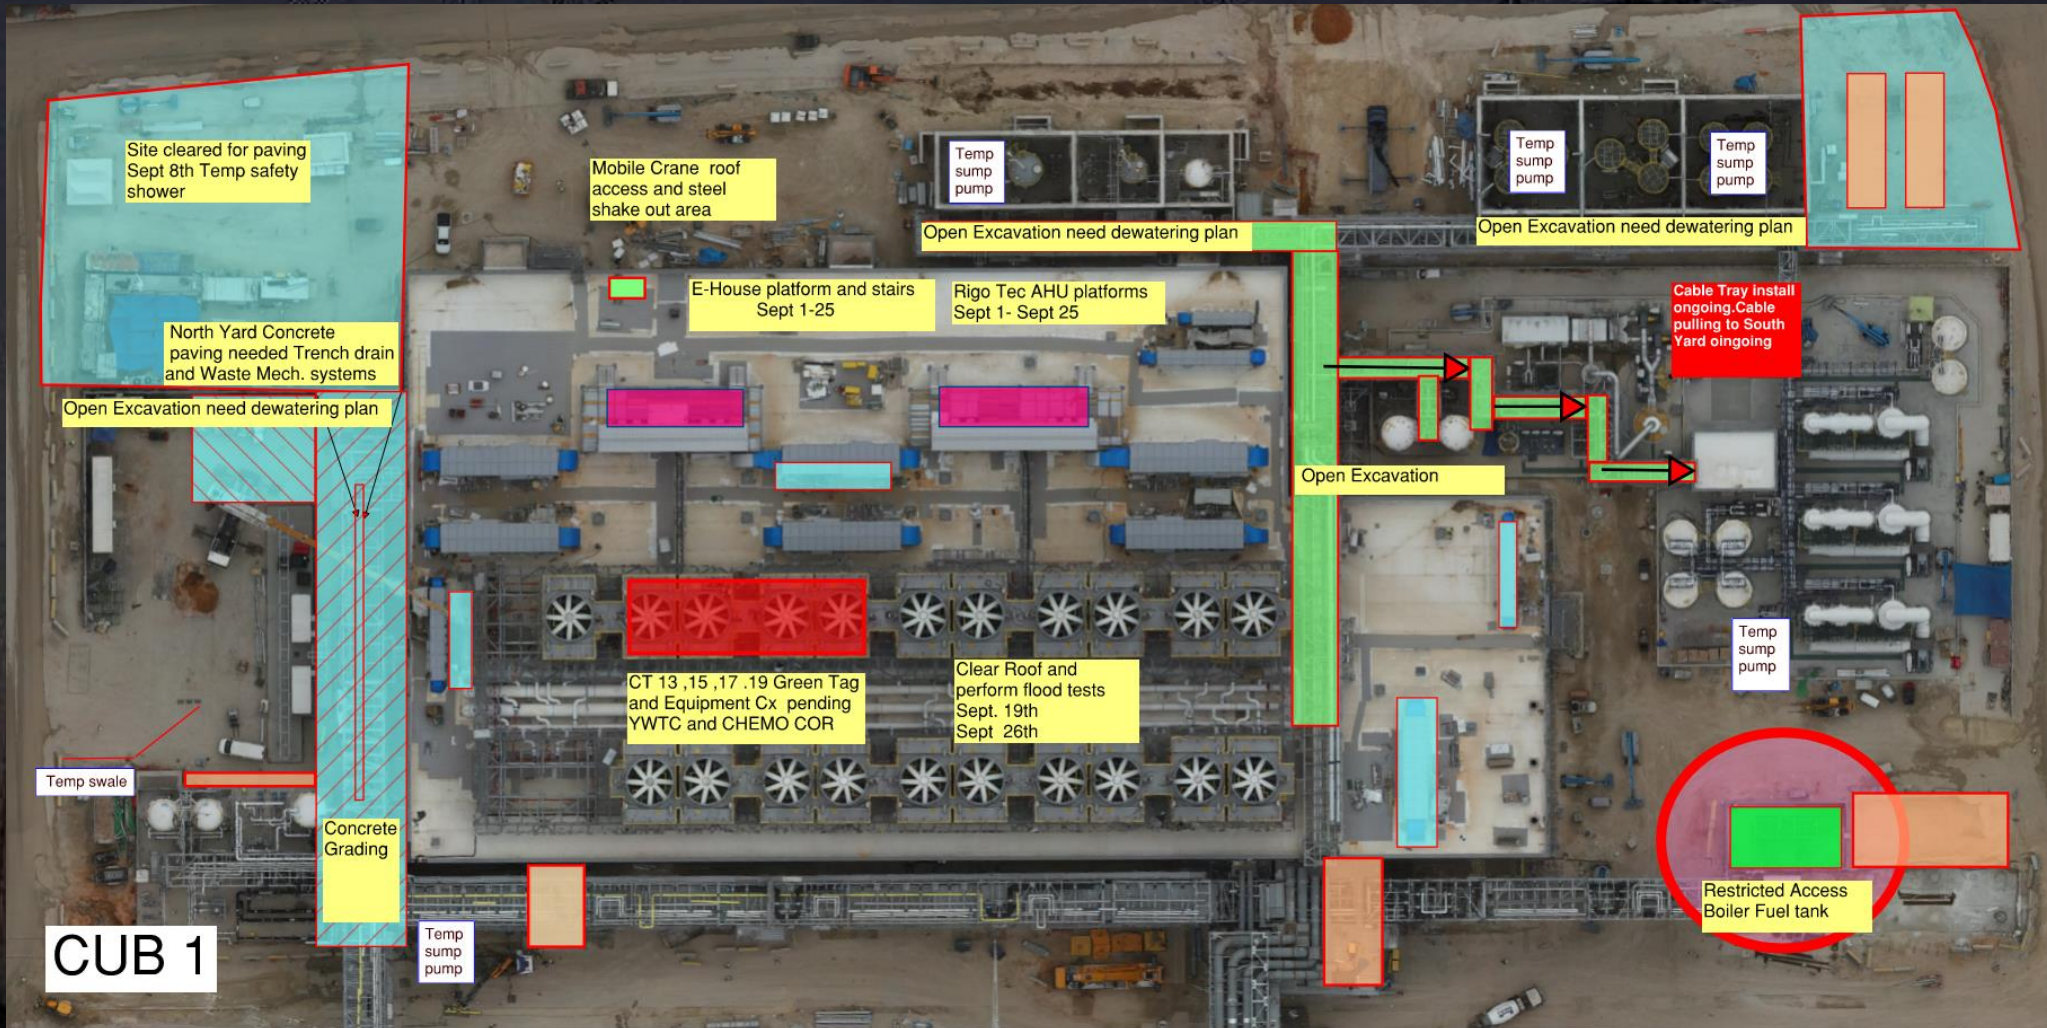


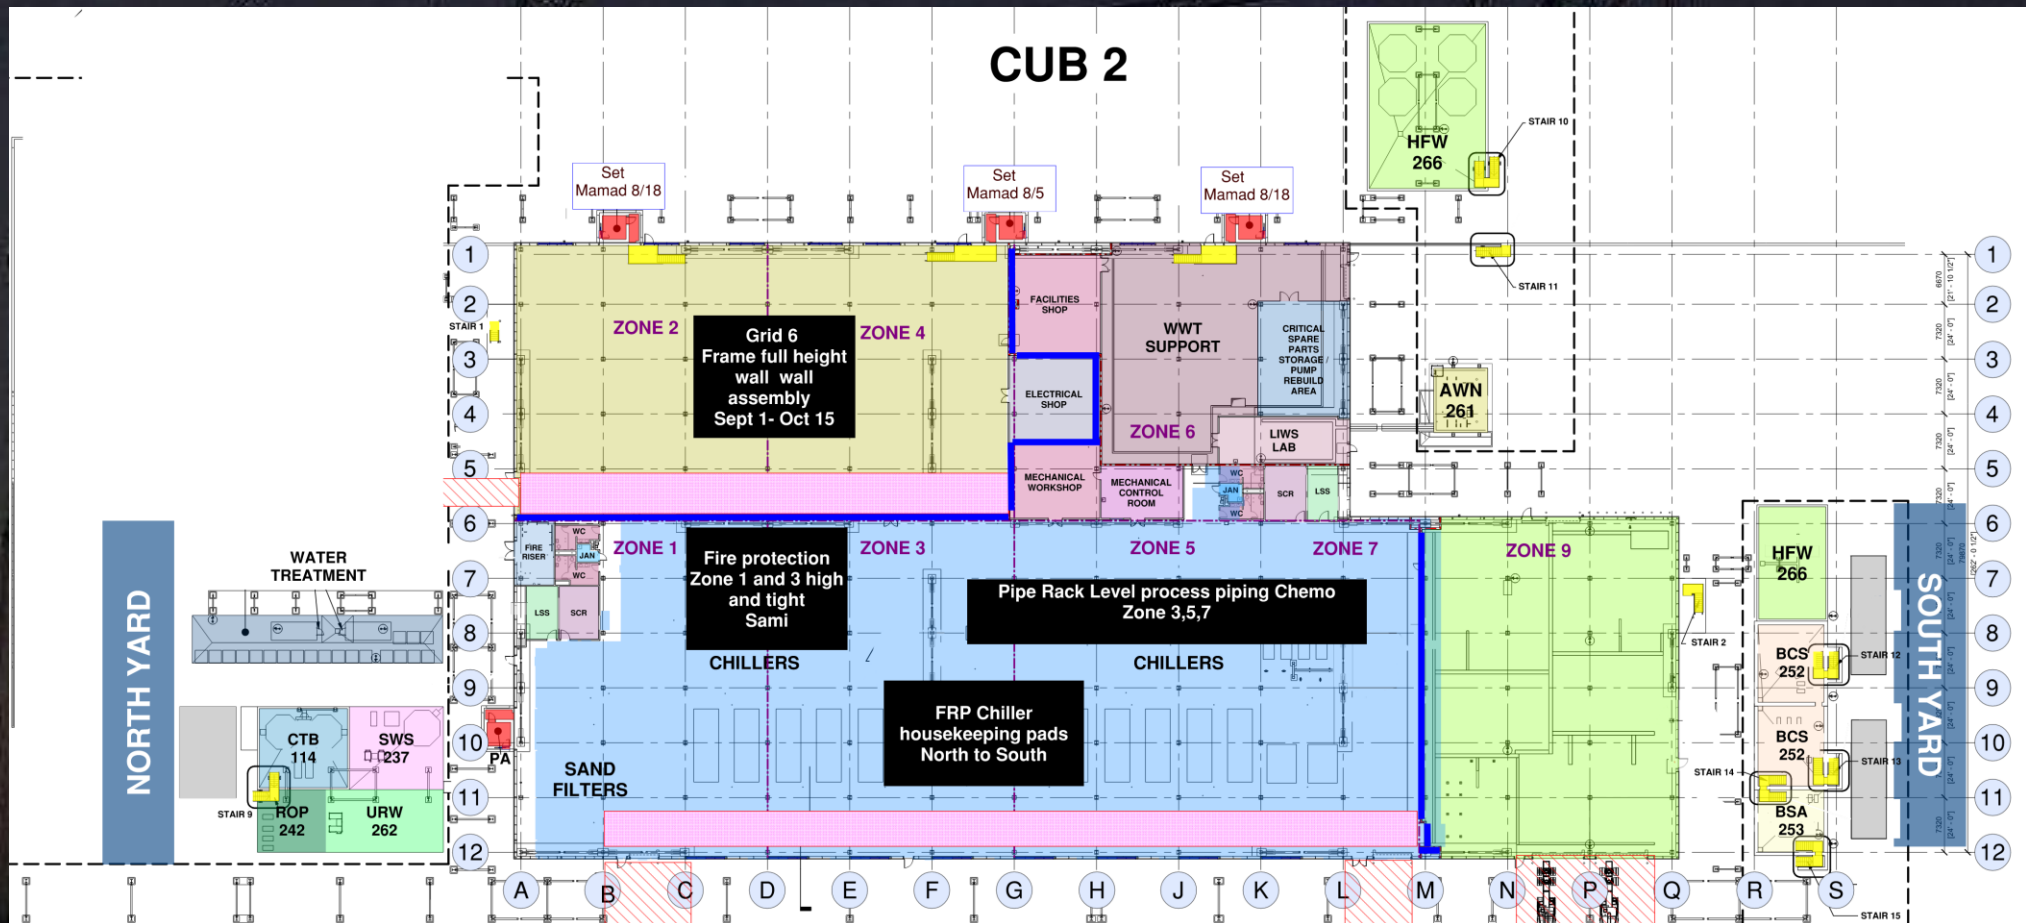

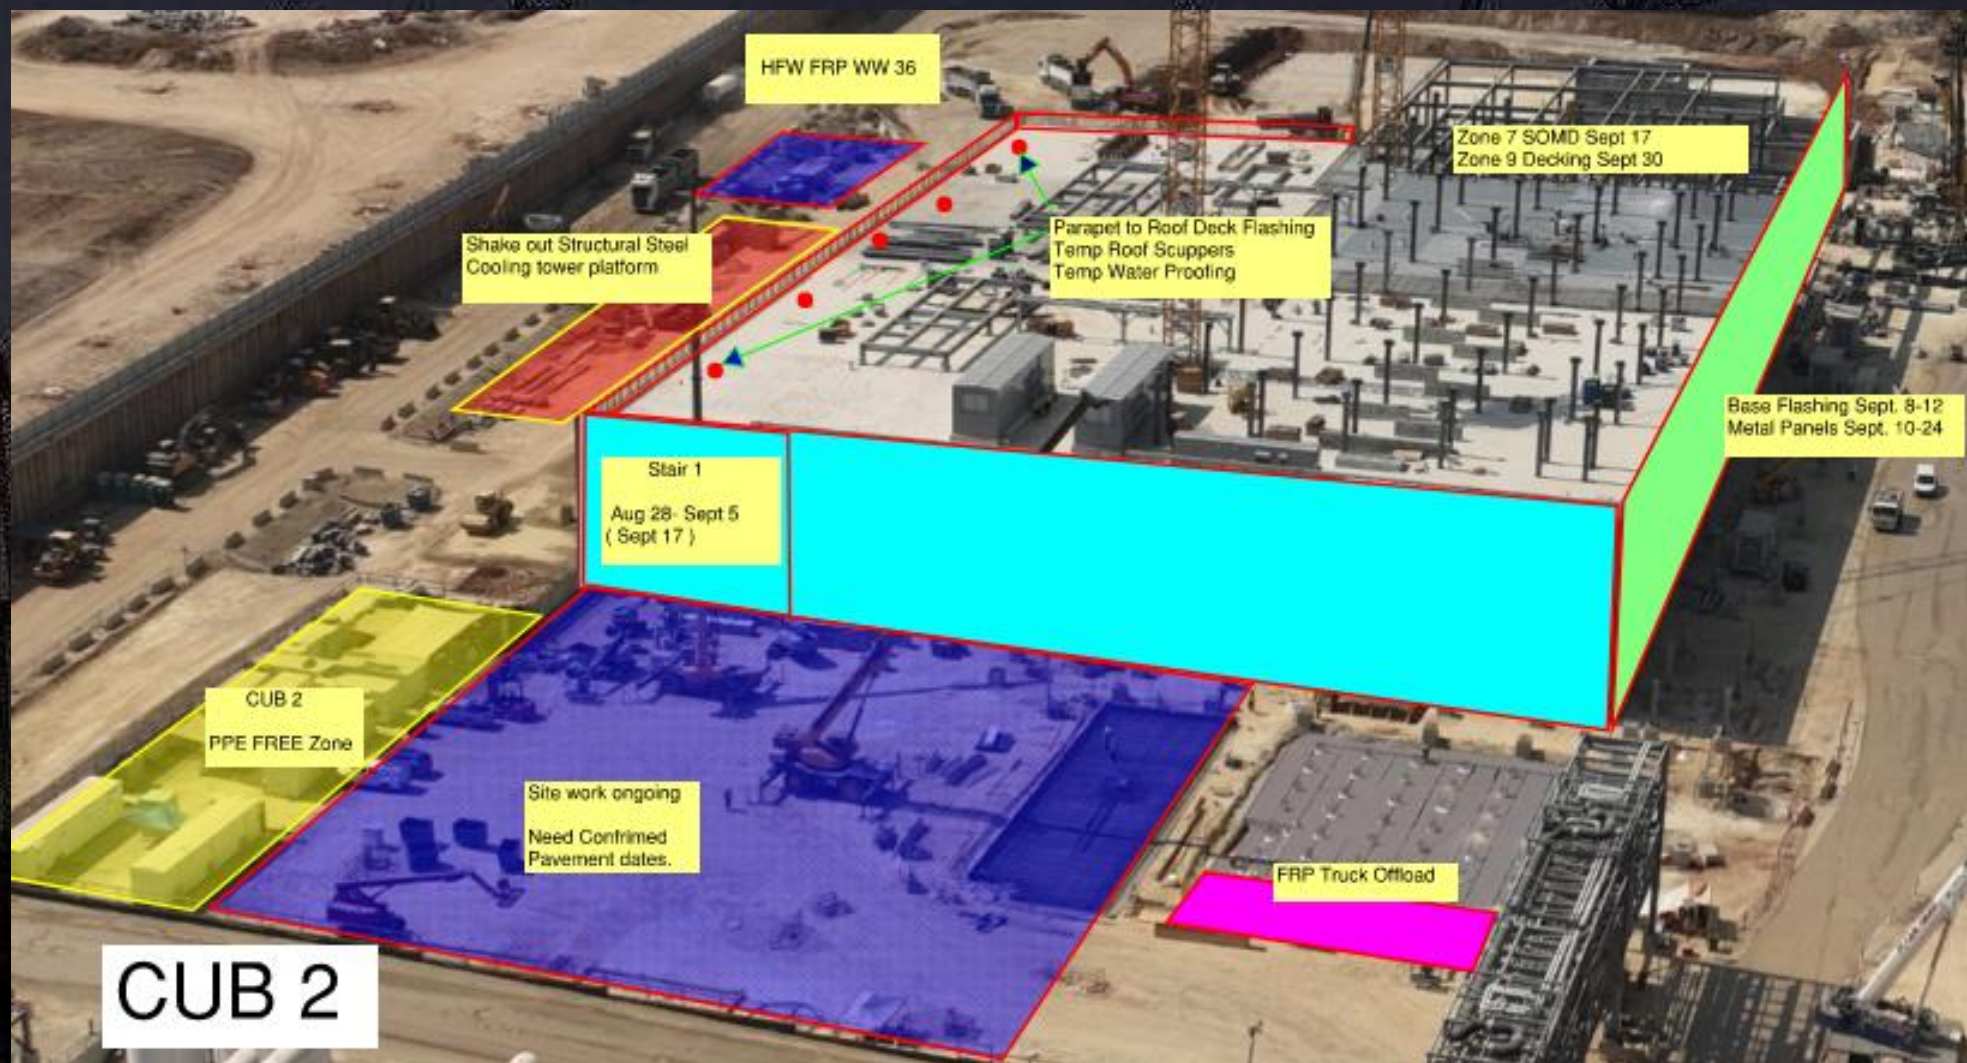



Sept. 9 1200-1400
AHU 104-2-10
CC2800
60 meter radius
29 ton capacity
22 ton AHU = 75% capacity

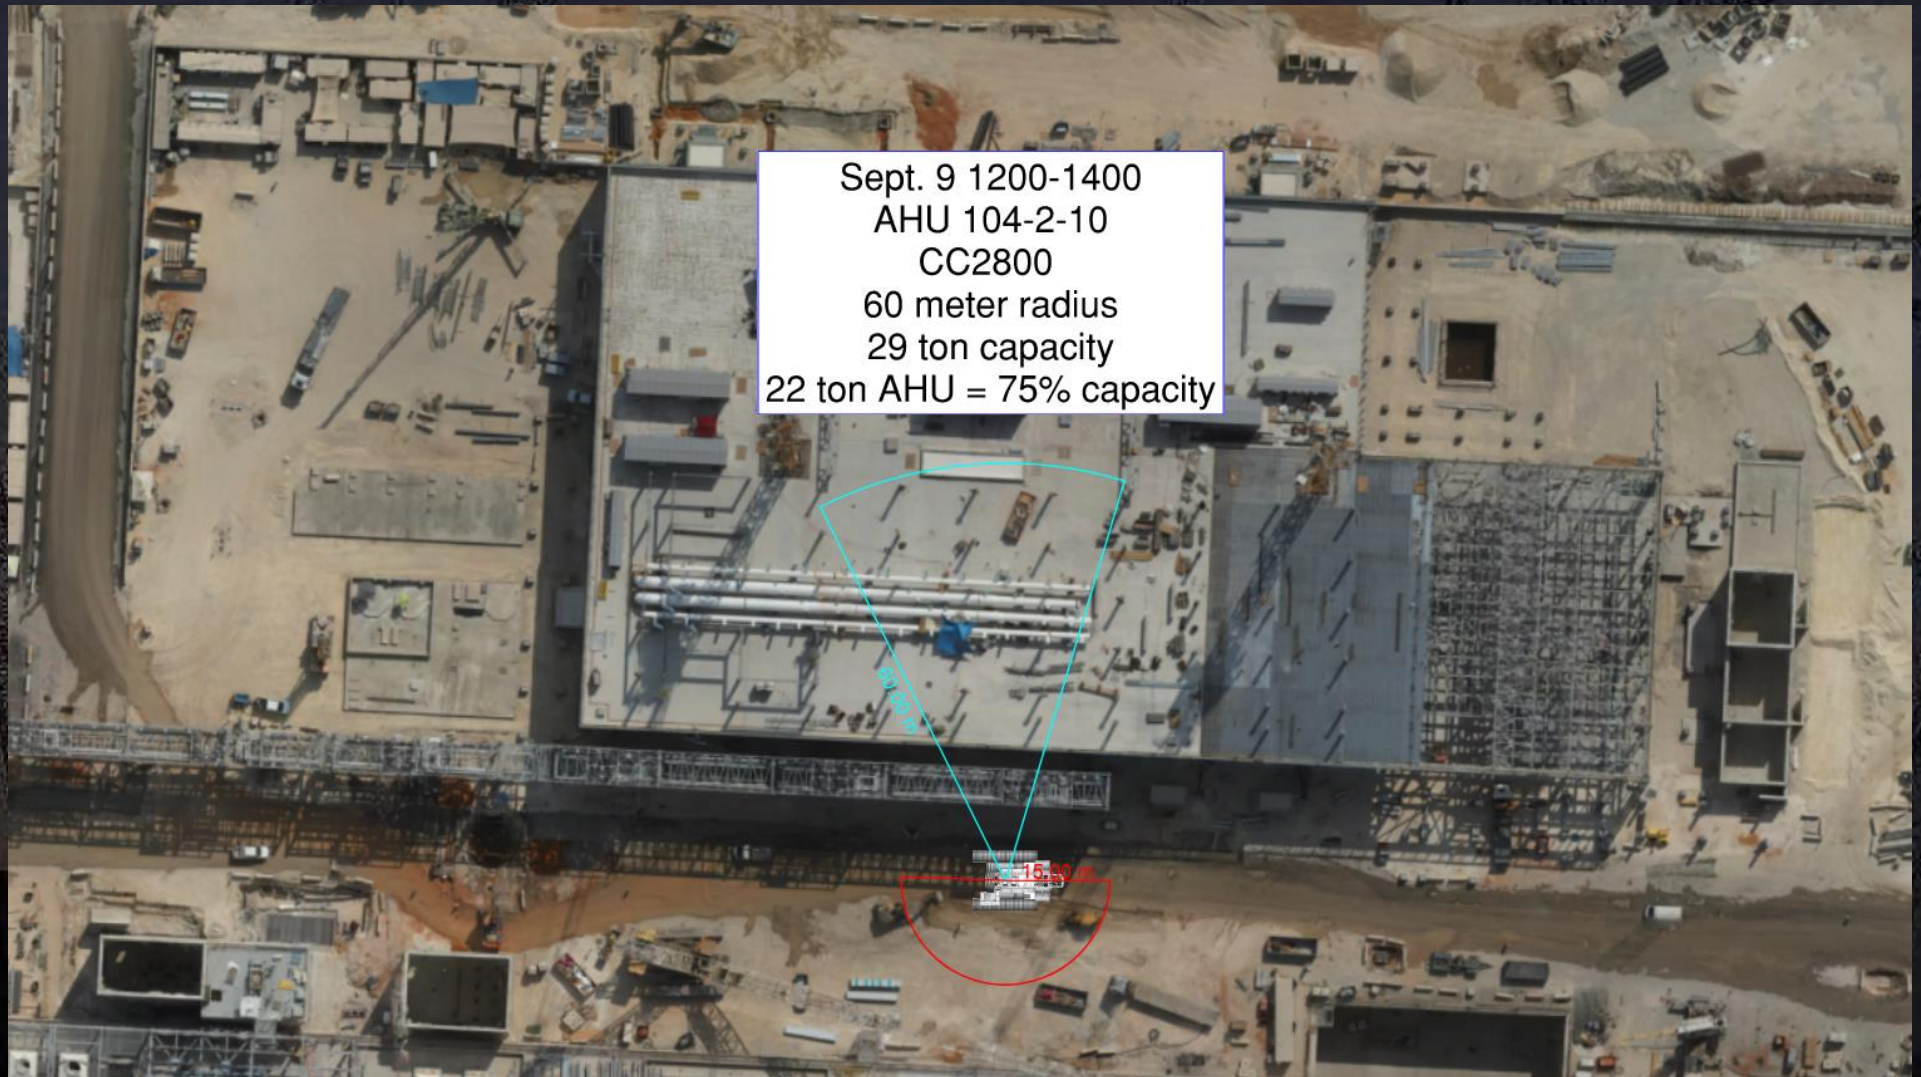



NO ACCESS
HV ENERGIZED AREA

EL-MOR
zones 2,4,7 red valves
cables testing

F.K Electra
testings & running
Gens


TMTeam
hardscapes work



Thurs. 19/9 09:00 -11:00
Sun. 22/9 09:00 -11:00

CRANE

MODULE

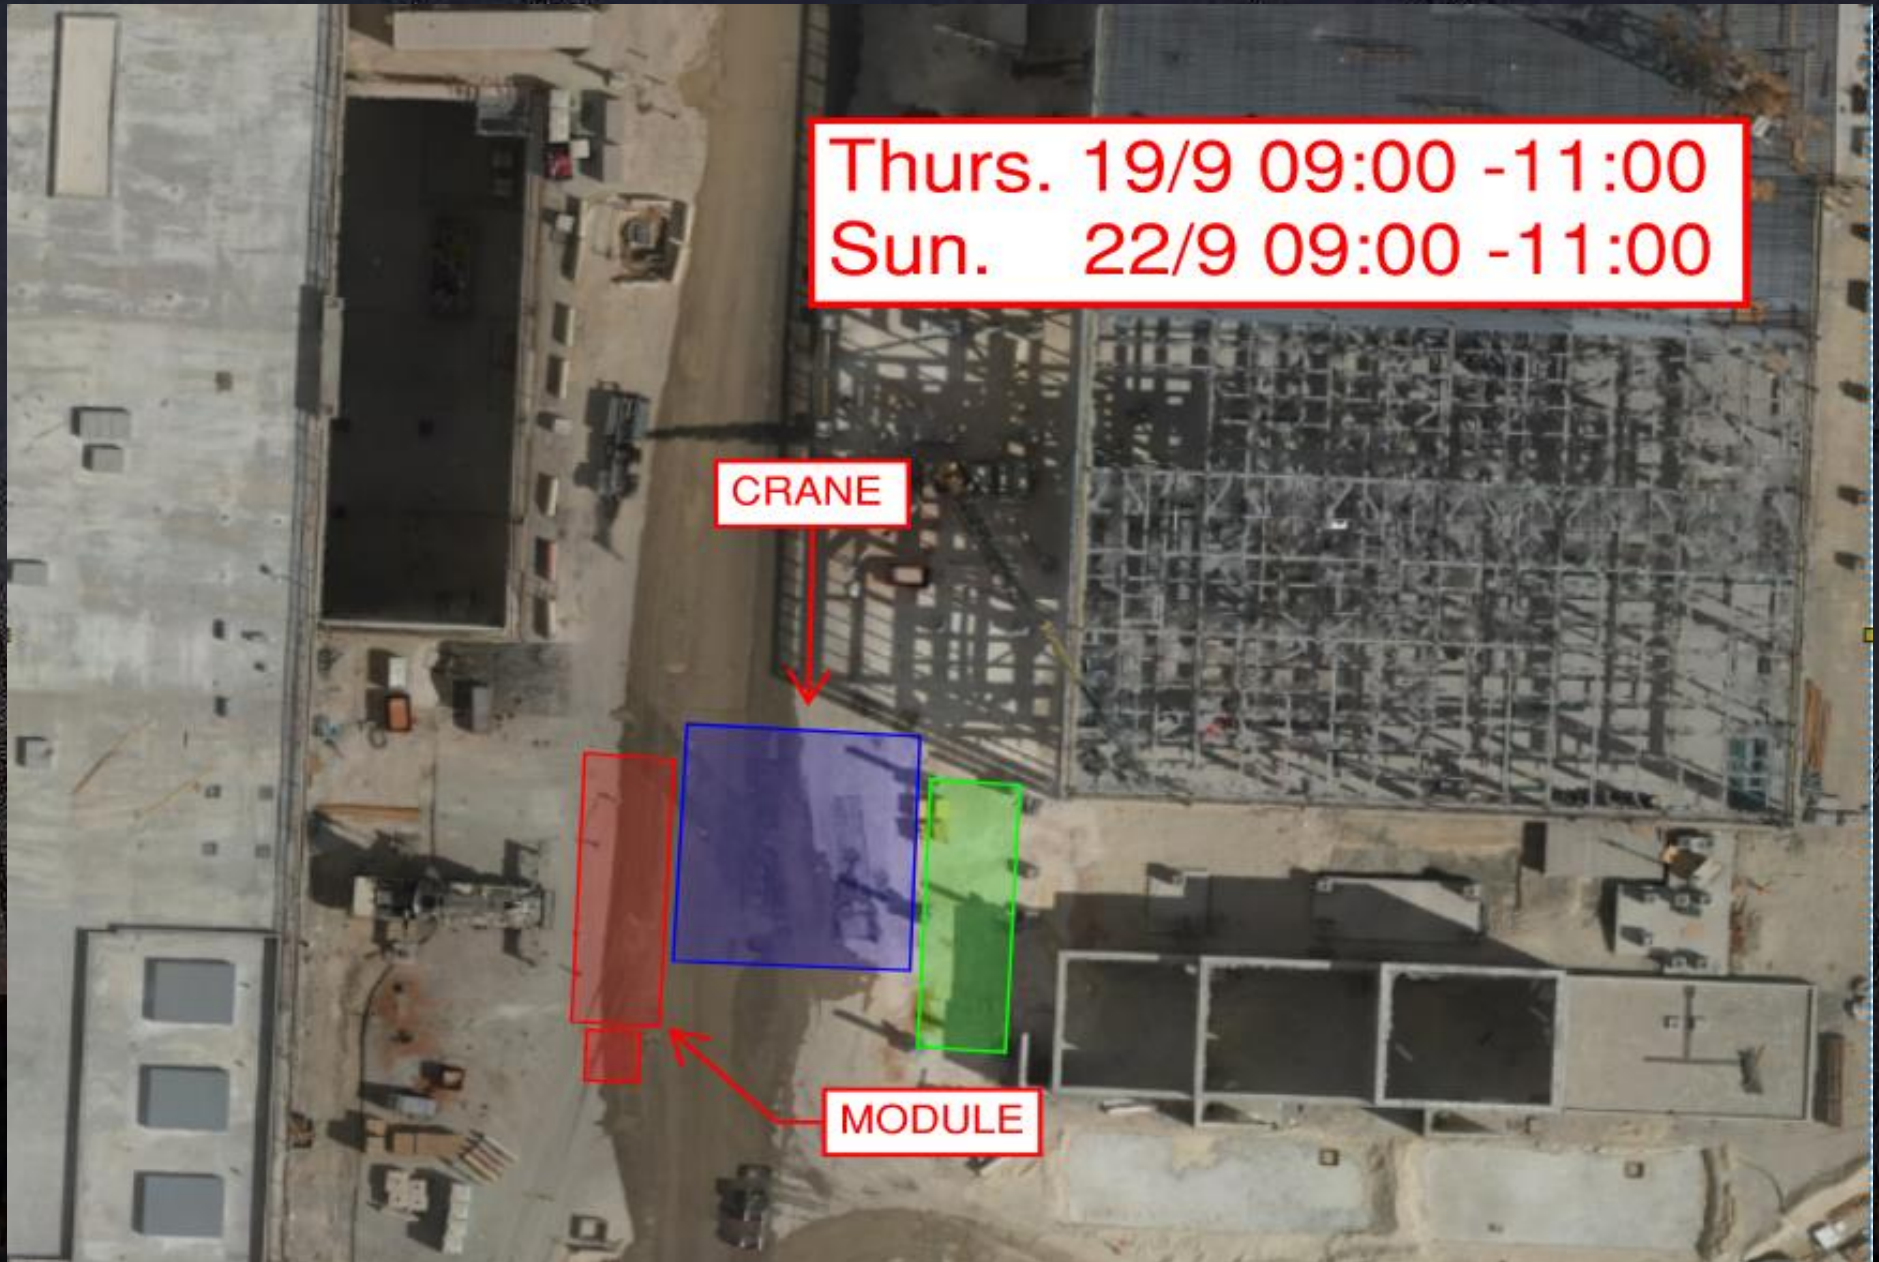




HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

NO PARKING OR MATERIAL STORAGE

BSGS

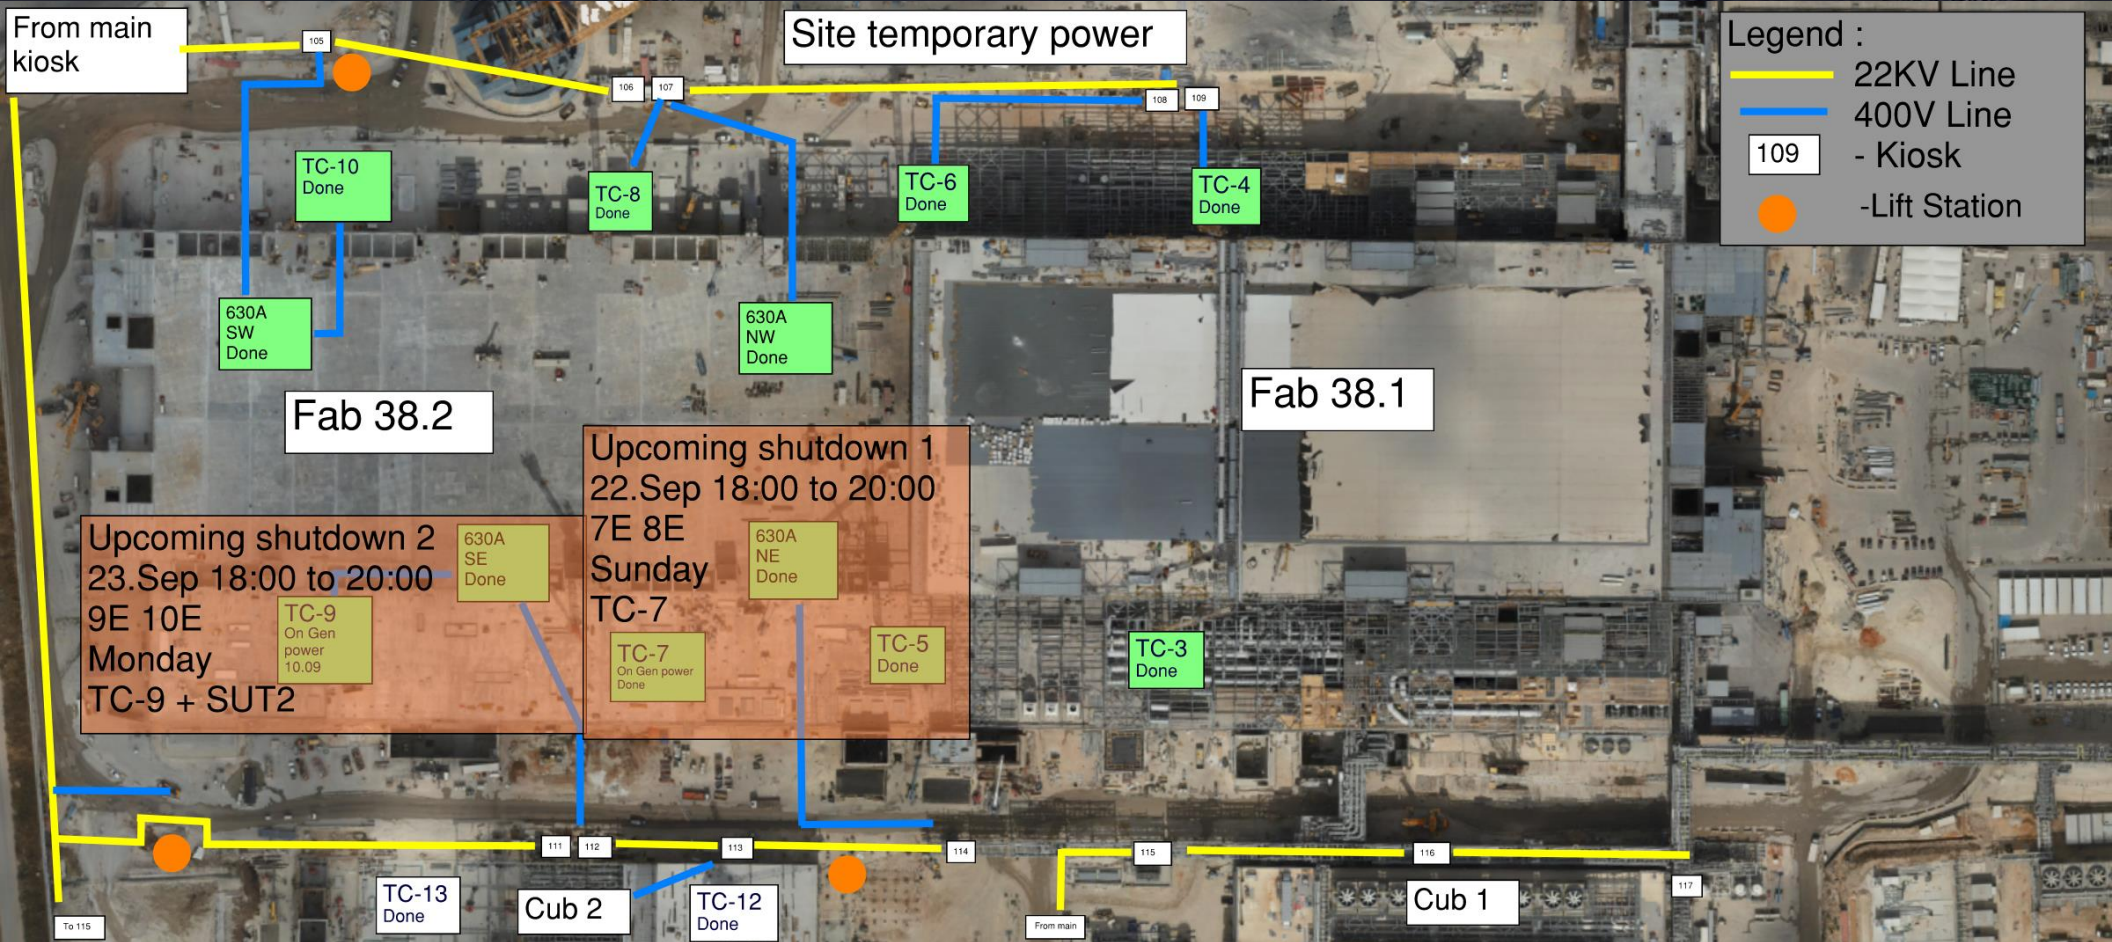

Daily Coordination Meeting

Site Logistics
North Gate B





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North





Daily Coordination Meeting

Site Logistics

South



Assess Your Travel Paths

- Before we fly a load, move a rack, relocate a piece of equipment, etc. the travel path must be assessed.
- This can't always be a simple walk of the planned route, sometimes we need to take measurements to verify and ensure that we have clearance or we need to request that objects are relocated so that we can more safely travel through the planned route.
- We need to plan our routes to encounter the fewest obstacles, not just the most convenient route.
- While moving, even along a planned route, we must have spotters to help us make sure that we don't collide with anything or anyone while we are moving.
- Tag lines need to be used in congested areas to control where the load is.

HCC/EHS Weekend Work- 20.09.2024

White Board Meeting in Beavers at 06:30

Superintendents

- Mike Rotter 052-5204493
- Ori Klain 052-3764728
- Tsurriel Evgi 052-3718851
- Eyad Abd Al Wely 052-3287236

CSA CM

- Asher Vaknin 052-2356079

MEP

- Andy Jollands 052-9659290
- Ken Power 052-2531428
- Abhilash Parameswaran 052-6938827
- David Young 052-2241683

OSM

- Nissim Najar 052-5420249

CX/QA

Cranes

- Maksym Panov 055-9181086

Safety

- Safety Foreman- Nadav Alfasi- 052-5115772 Nadav-Alfasi@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 20.09.2024

FAB

- Dvir- HSAI, utility asbuilts and control.
Manager - Efraim Herbst

Utility Level

- Lesico
Ehs Michel 0526060223
Foreman Manoj 0522450258
Chemo
Ehs lilach 0547886704
Foreman sergey 0544659688

Elram

Foreman: Shlomo 0545551702
Ehs: shy 0523632132
Afcon electrical
Ehs Steven 0559129333
Foreman Perdit 0552742935

Subfab

- Pach Taas
Perim Rack AAe
Team Lead : ??
Afcon E
LSS Rooms / PA
Team Lead : Raz david 0546838626
Avi Eli 0526008487
SELA
MOD2 6-7E/6-7W
Team Lead: David Benshetrit 0524382997
Safety: Sergey 0526650046
Chemo
TTNW
Team lead: Tommy 0523759408
Safety: Lilah 0547886704
Lesico
BA-AL Transitions
Team Lead: Gabi 0549892929

HYG

SF Zones 3- White steel touchup paint, Stair # 6
Salah 0507773119

WW Steel

Elevator 1 &3
Teddy 0522392473

Clean Room

- Chemo – INT -4E+5E 10” pipe install +racks 1W-1E (EHS Lila - 0547886704, Supervisor Winai – 0528090588)
- W&W 17-18 Line added the beams 10-24 line – catwalks, MOD2: steel fan deck east west, infill ongoing (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- Talad – CR 1W – Drilling holes, 1 metal lids removal (EHS Guy 0544915407, Super Igor 0544509386)
- Sig – 5W INT Platforms MIMO CB-CC/25 (EHS Beni 0506232032, Super Nodar 0546313261)
- Elram – CR Level 9,25 line, AA line 2W shafts walls INT level 9,10,17,24 column wrap (EHS Royi 0538312234, Super Bonio 0544236899)
- Rolling Plains – Mars shaft 5W 3FK, BD,BE,BF, 9+25 both, NTT 5RA level (Super Cordin 0546594273, EHS Oleg 0542689370)
- Pach Taas – INT 17 line duct (EHS Avigdor 0542010393, Super Netanel 0543301880)

Subcontractor Weekend Work- 20.09.2024

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2, and EPA Platform 1&2P
- Foreman – Vadim – 052-6229005
- Safety – Offek – 050-7838486
- Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-2P Roof & Lift 2
- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 1-4P
- Foreman – Maor – 050-955-9071
- Safety – Rotem – 054-447-7112
- W&W – SEQ 135, 137
- Foreman – Willie – 052-6145521
- Safety – Gary Lambert – 1-405-833-8910
- Elram – 5P Corridor, UPW Ceiling
- Foreman – Willie – 052-6145521
- Safety – Gary Lambert – 1-405-833-8910
- Carmel Bidud – HWB Hangers
- Foreman – Hitim – 052-7053353
- Safety – Michael – 054-2634700
- Combe UPW – UPW Room Piping and Yard
- Foreman – Boris – 054-8346412
- Safety – Abed – 052-5148747
- SNJ Flashing – BPS Roof
- HSAI – BPS Blast Walls
- Foreman – Dave – 052-4121028
- Safety – Sam – 052-5259268

WJG

W&W – Steel Erection 4J, Hot work – Road, 4J/5J lift 2
Foreman: Chris Isaac 052 588 3215
Safety: Moshe 054 801 2959

Afcon – 4J UL Cable Tray
Foreman: Sarat 055 274 0190
Safety: Pradeep 055 274 2935

Pach Taas: 1J UL, 2J Lift 2 Module Bolting
Foreman: Nuriel 054 901 2343
Safety:

Chemo: 5J Lift 2 Piping
Foreman: Sergey 054 465 9688
Safety: Lilach 054 788 6704

OAT testing in CUB 1, Boiler area & in North Electrical Yard.

David Young - HCC
Tony Dixon – HCC
Zack Oestereich – Rockwell
Olesia Solianik – Rockwell
Plus Meptagon Cx team

Siding

Subcontractor Weekend Work- 20.09.2024

CUB

Sami Najami CUB 2:
Husein - 0526917461
Alon - 0509895008

ETC south yard:
Yosef - 0506708990
Shlomi - 0528235757

Meptagon I+C:
Raziel - 0584360845
Netanel - 0538398999
HSAI
SIG:
Shmulik - 0549205966
Chemo Aharon:
Dudu - 0509808846
Leonid - 0548883878

Date: 20 September 2024

Dayshift Working time 07:00 to 19:00

CUB1

1.SOMSAK PAKPANUPAT, AC5253797, TEL 054-8112261 (Leader)

Nightshift Working time 19:00 to 07:00

CUB1

1.SARAWUT KHRUEASING, AC5094850, TEL 052-3628607 (Leader)

Date: 21 September 2024

Dayshift Working time 07:00 to 19:00

CUB1

1.SOMSAK PAKPANUPAT, AC5253797, TEL 054-8112261 (Leader)

Nightshift Working time 19:00 to 07:00

CUB1

1.YOTSAWAT PHUANGPHET, AC2254444, TEL 052-8104983 (Leader)

Sela

SUPERVISOR David Ben Shetrit 052 - 4382997

EHS Shmuel Kushnir 050-6306031

S.K.E:

Marzuk - 0548830263

Brand- CUB 2 – siding

Trestle

SNJ

PIPES –UB CUB

ISOLATION –UB CUB

FORMAN

ATEF - tel. 054-2287499

SAFETY TRESTLE

Alon Matan tel. +972 50-989-5008

Site

- **Derech Afar** – Shotcrete wall
Supervision = Raed: 054-2442030
EHS = Alex: 054-5403849
- **Olizki** – Sweepers and water trucks, grading for asphalt & concrete forming
Supervision = Or: 052-4917313
EHS = Ben: 052-4033565
- **TM Team** – LSS underground
Supervision = Rafi: 050-8723363
EHS = Alon: 054-7711469

GIS/NEY

Daily Coordination Meeting



14:00 Sign In
