

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:

- No night shift Thu 07 November, jobsite closes at 17:00, Jobsite reopens 06:30 Fri 08 Nov.



TRUSS SET
9E
Tomorrow
Start 4:00am

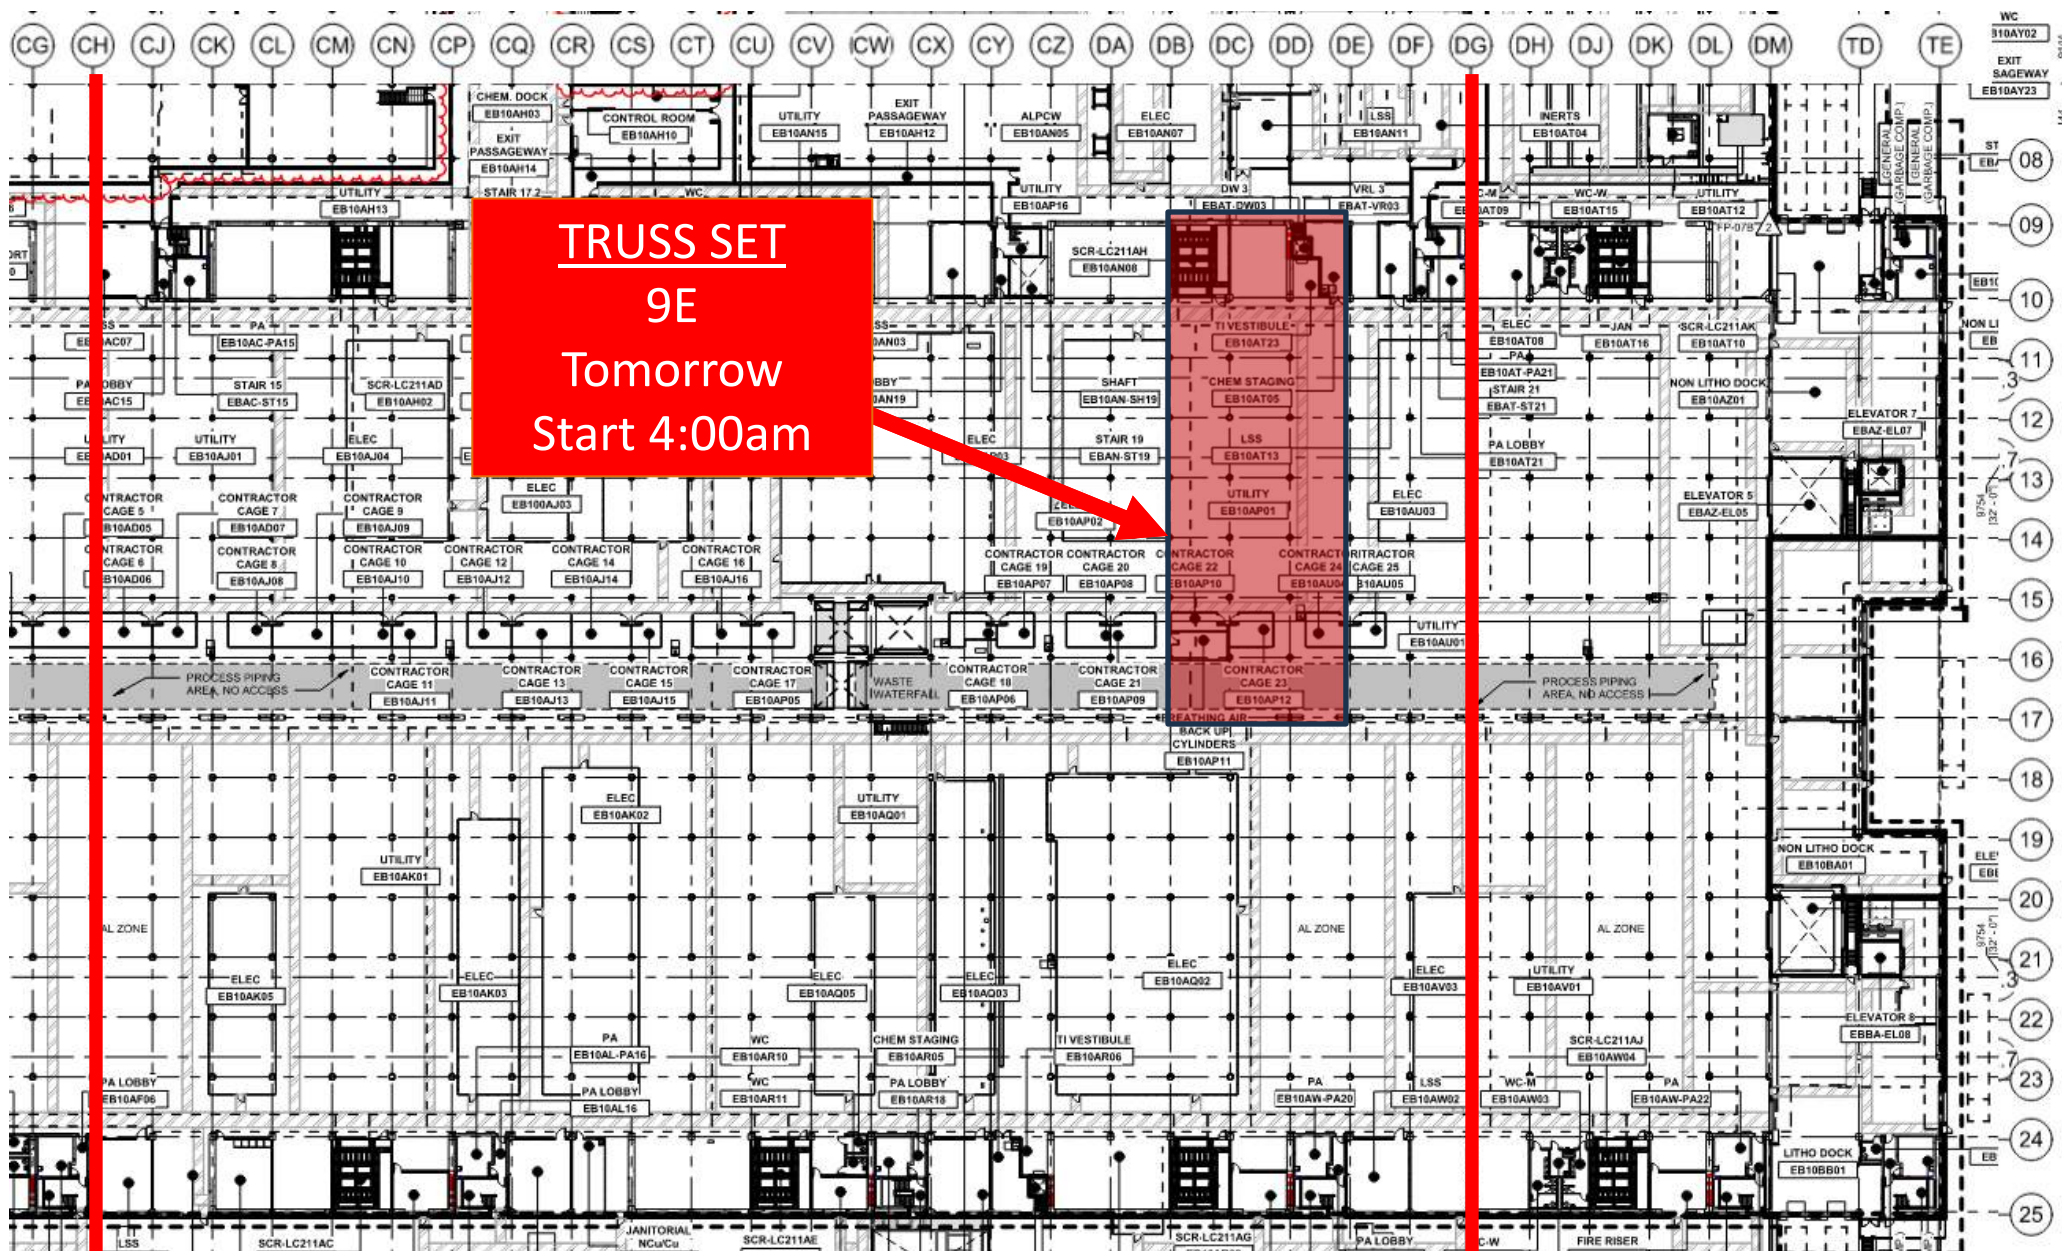



Pre-mold Rem dismantle
Should be uninstal


BELFOR Mold remediation

ELRAM


MEP+Elctrical
Ready for re-install




UTILITY LEVEL MOD2

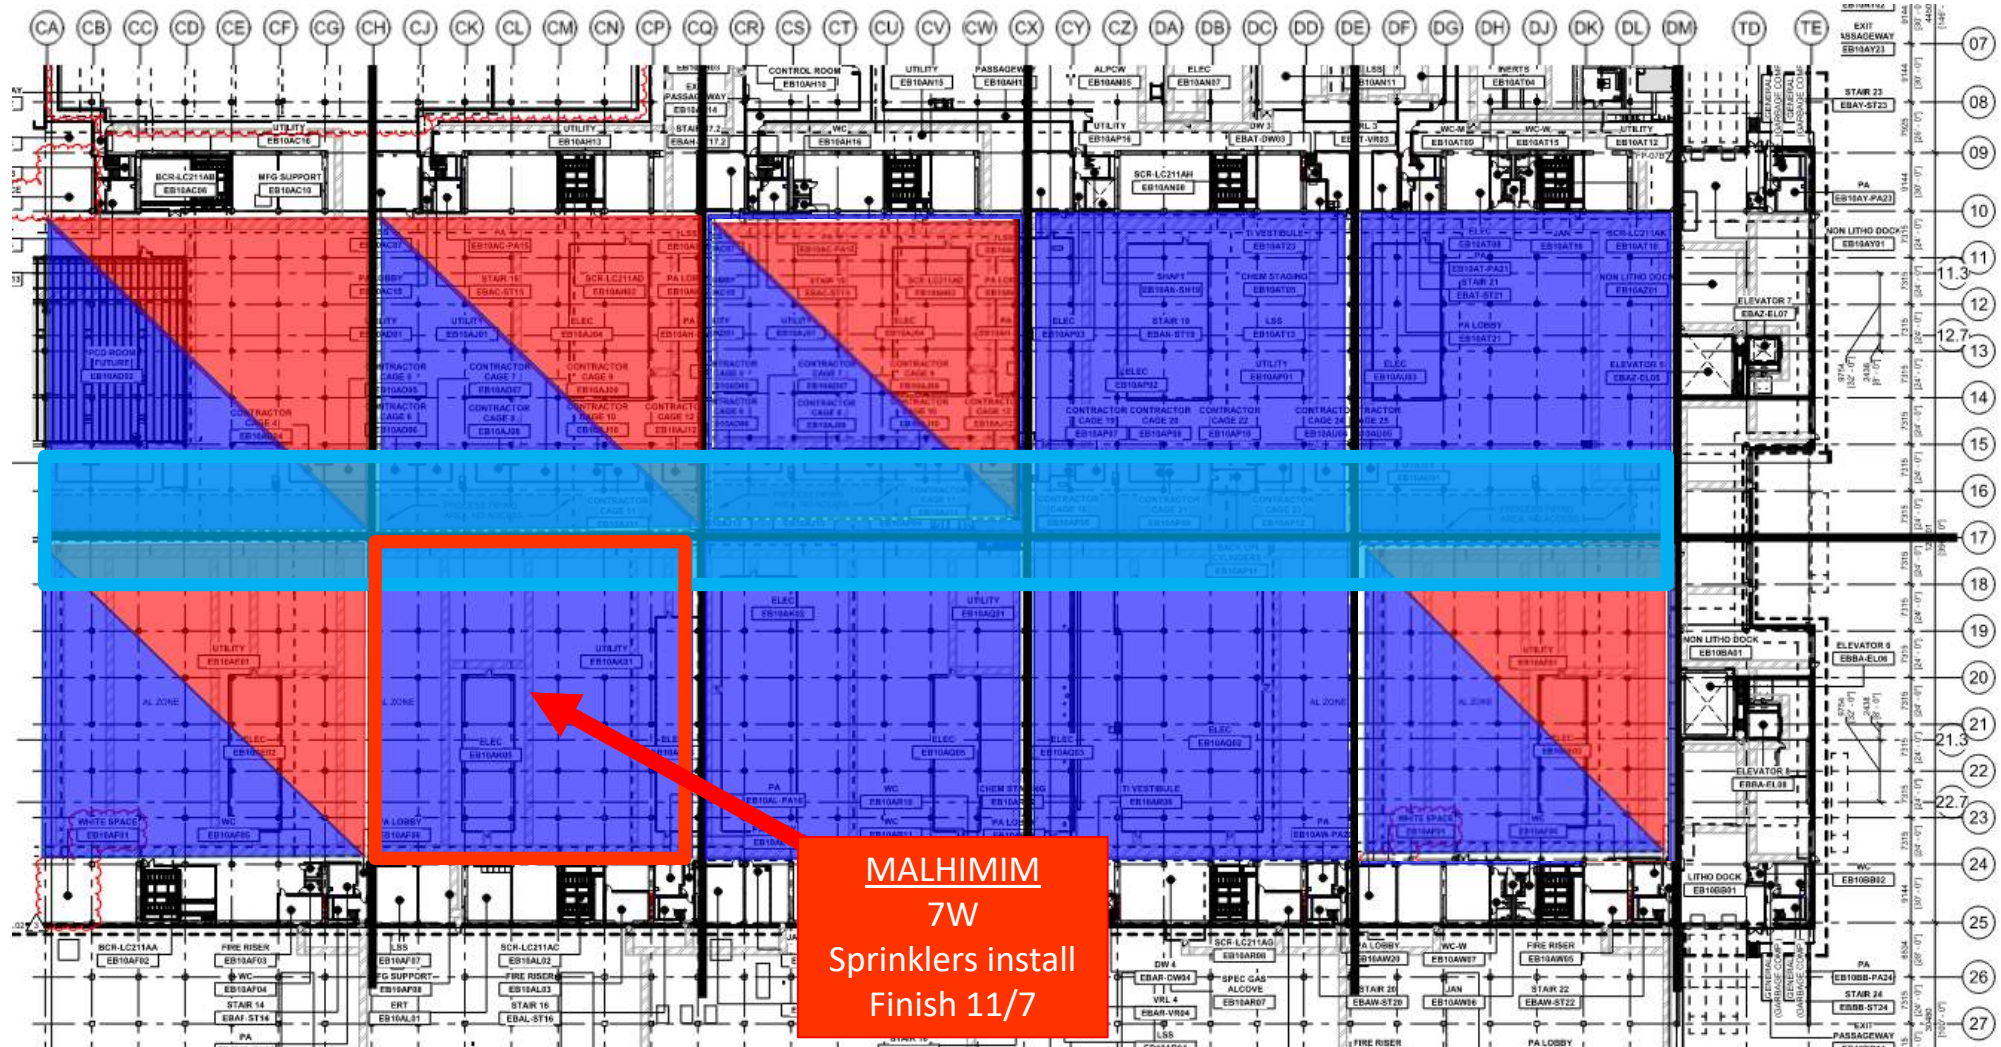


SUT 38.1 LEVEL

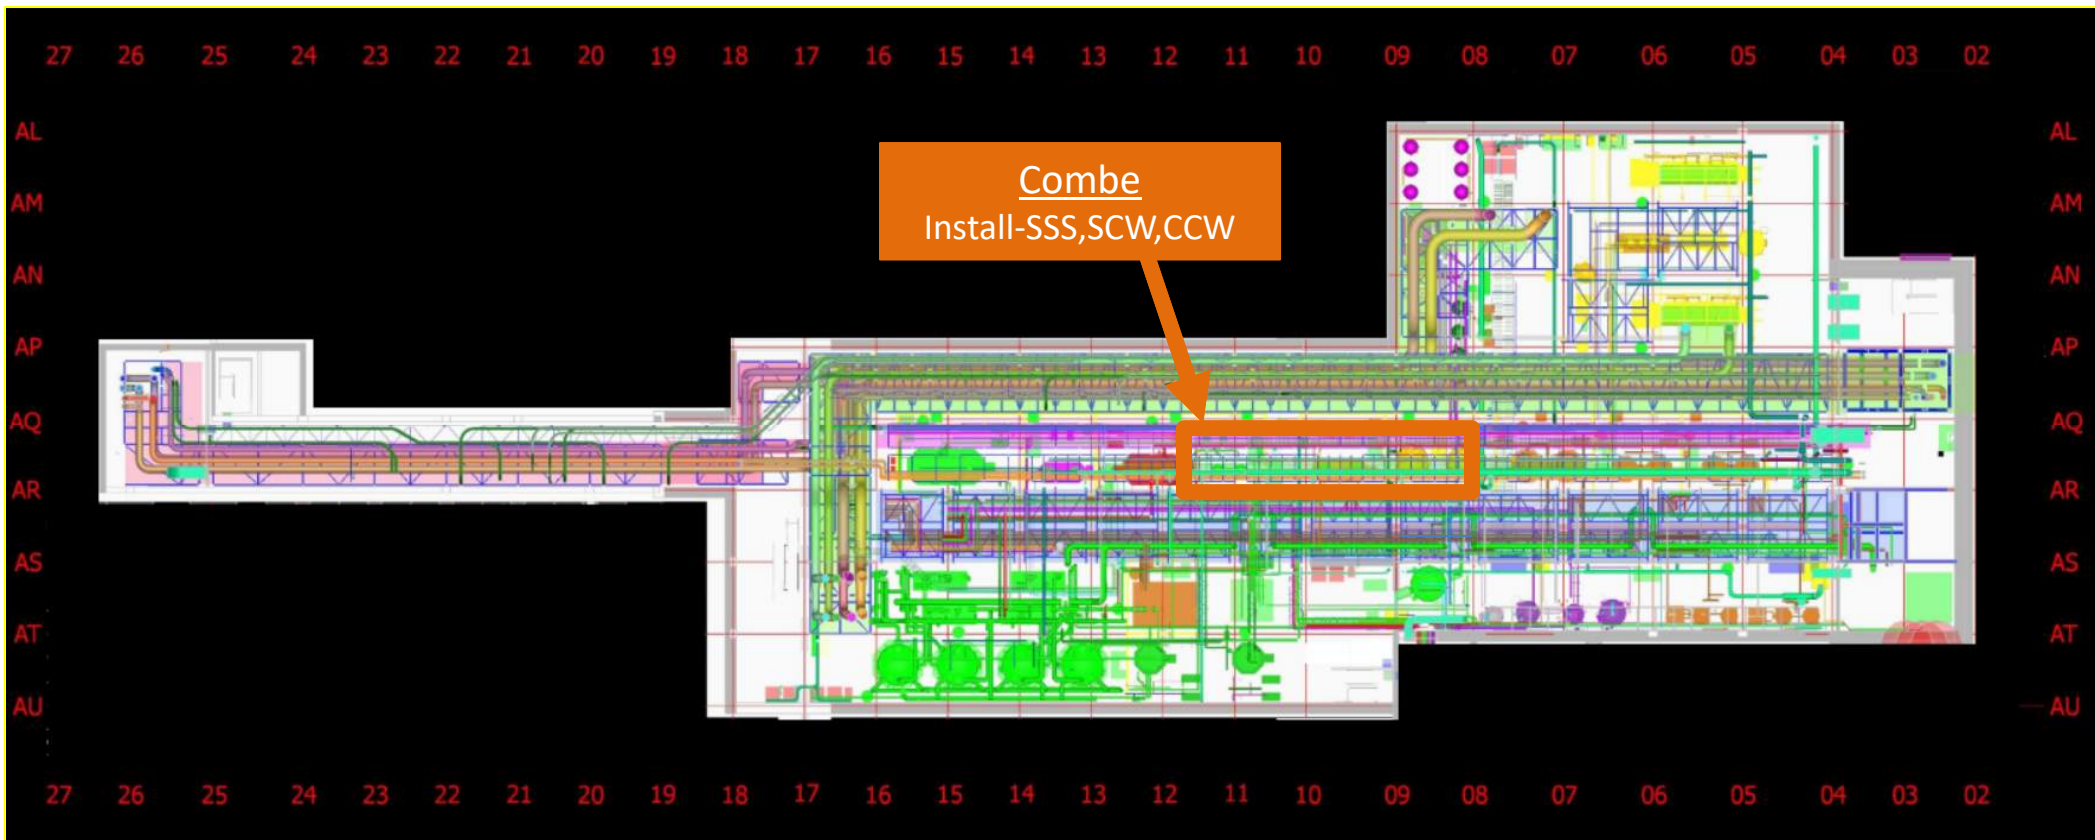


SUT 38.2 LEVEL

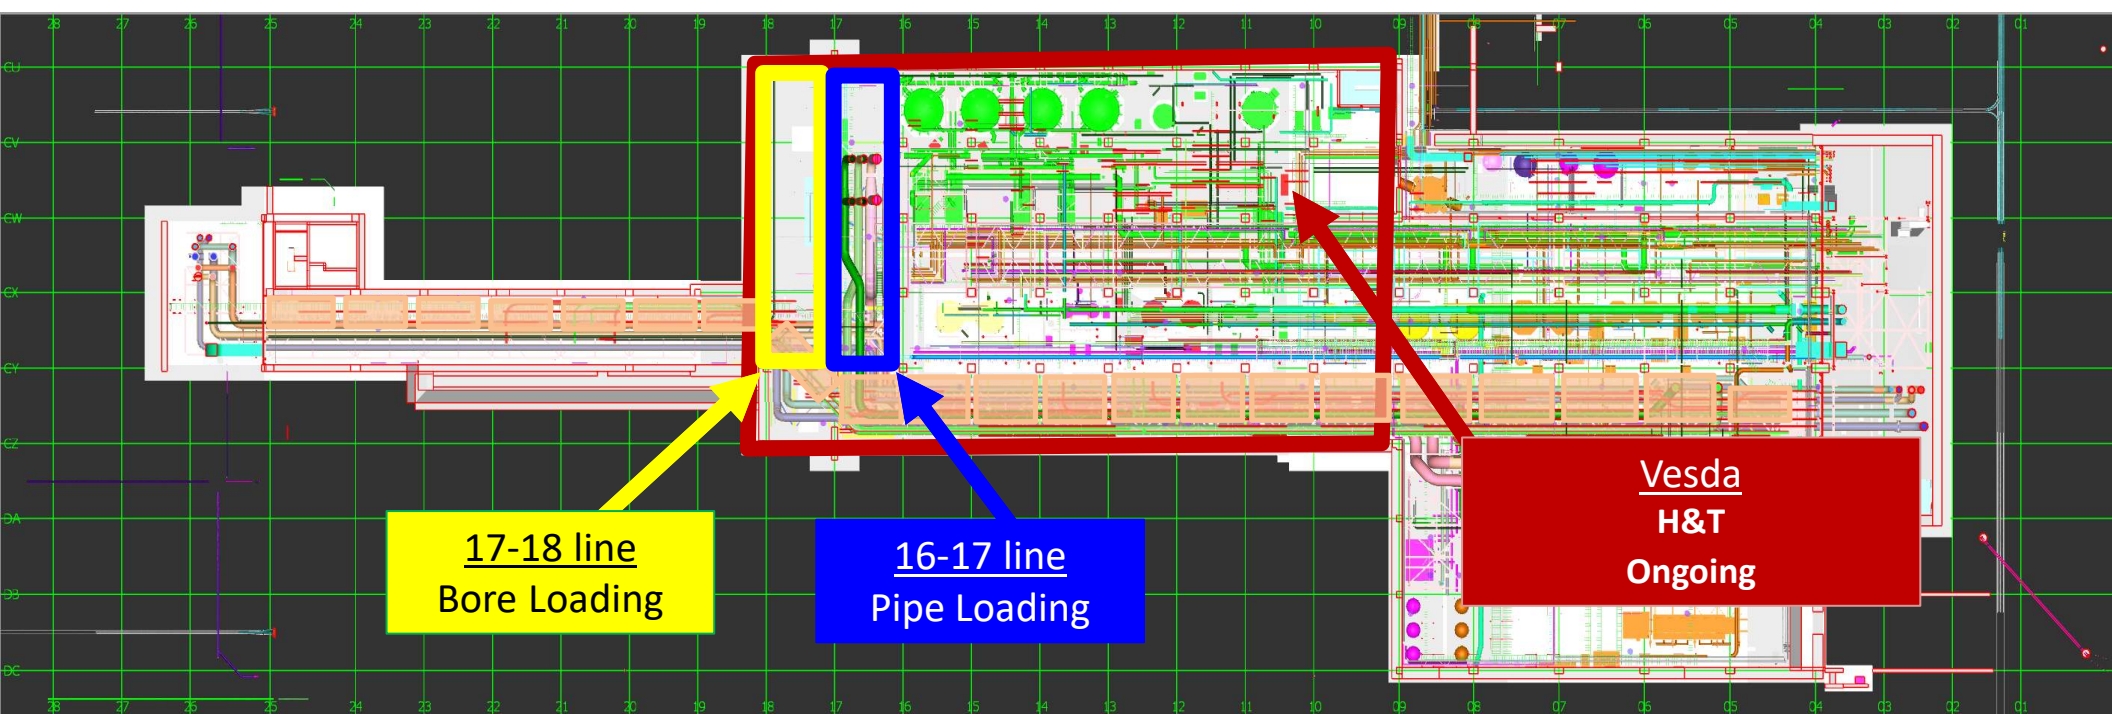

SUBFAB BUILDOUT MOD 1

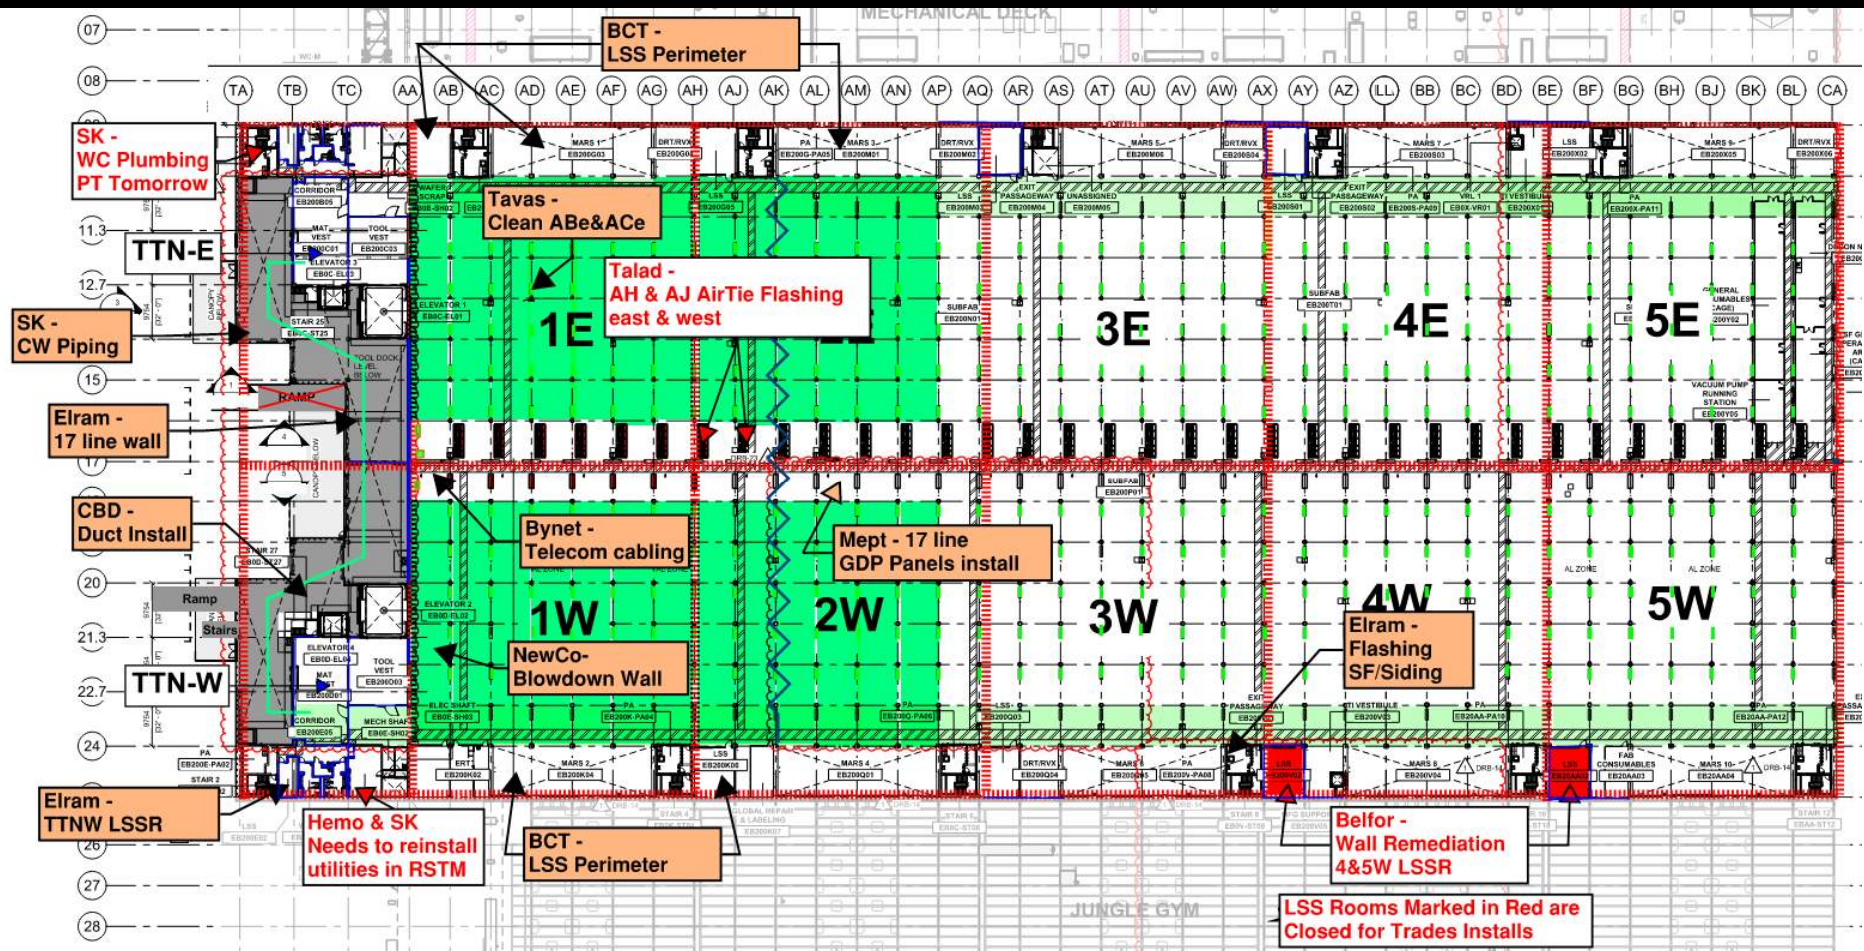


SUBFAB CRC TOPCOAT

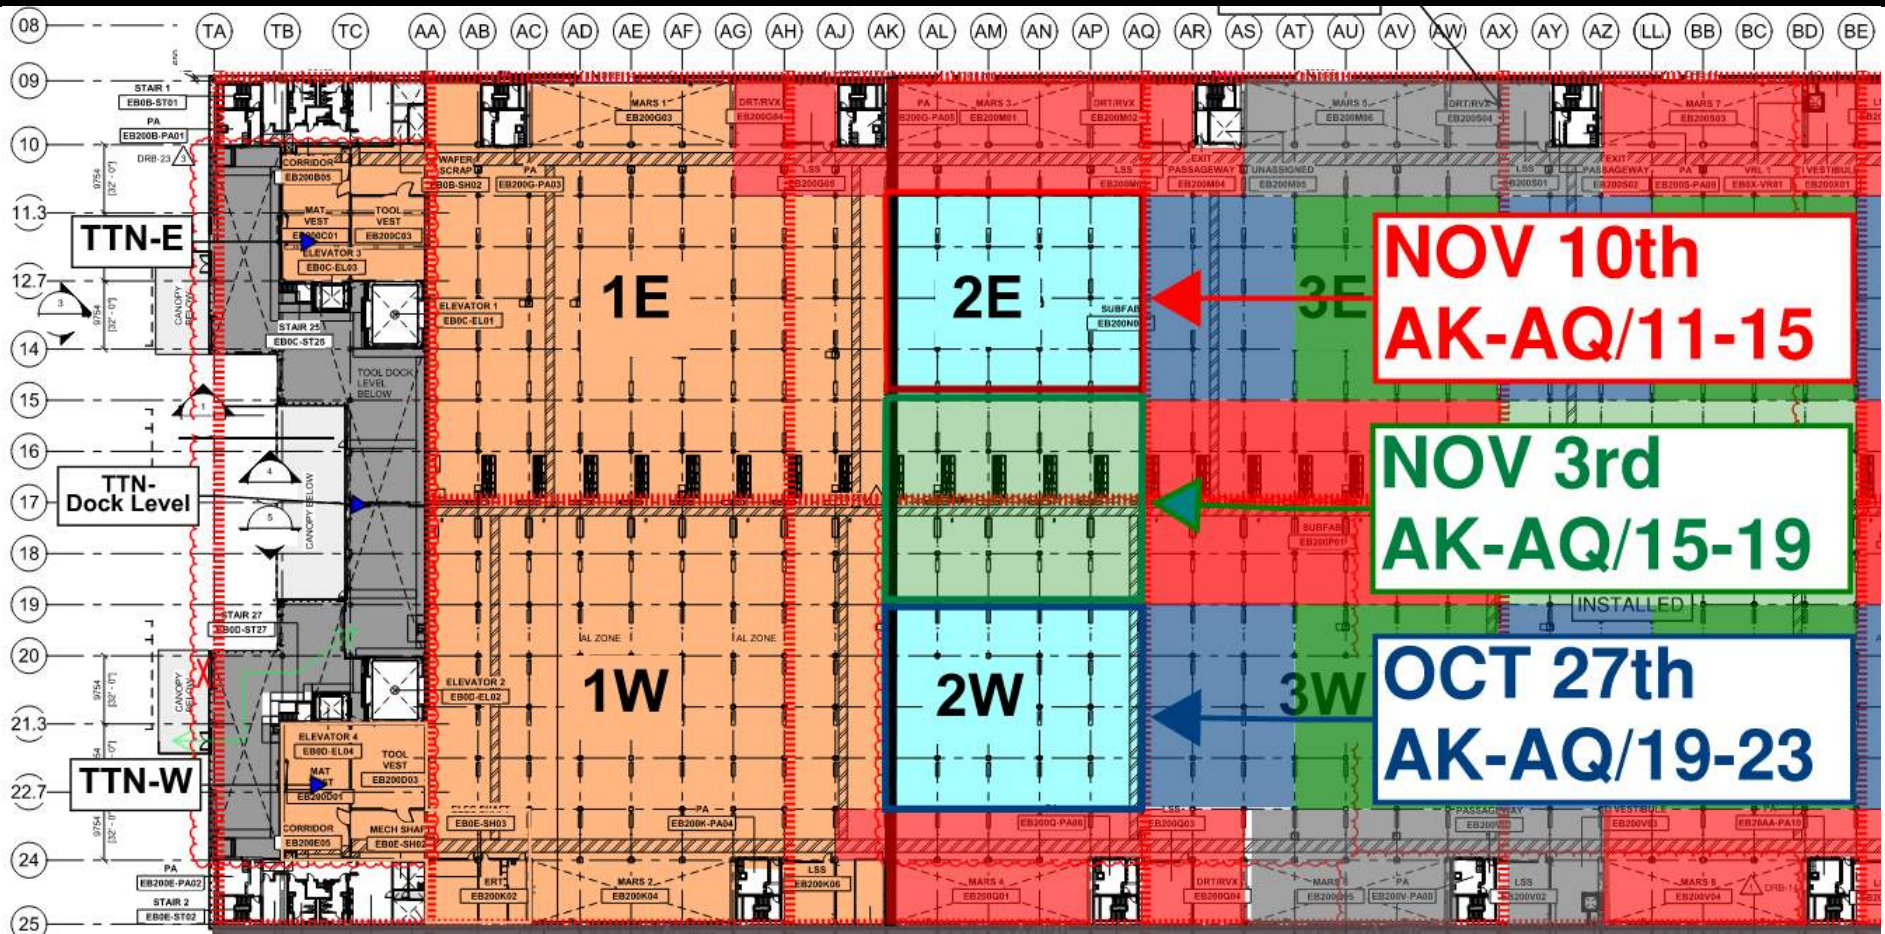

BCT Pressure Test

NOT TODAY

SUBFAB BUILDOUT MOD 2

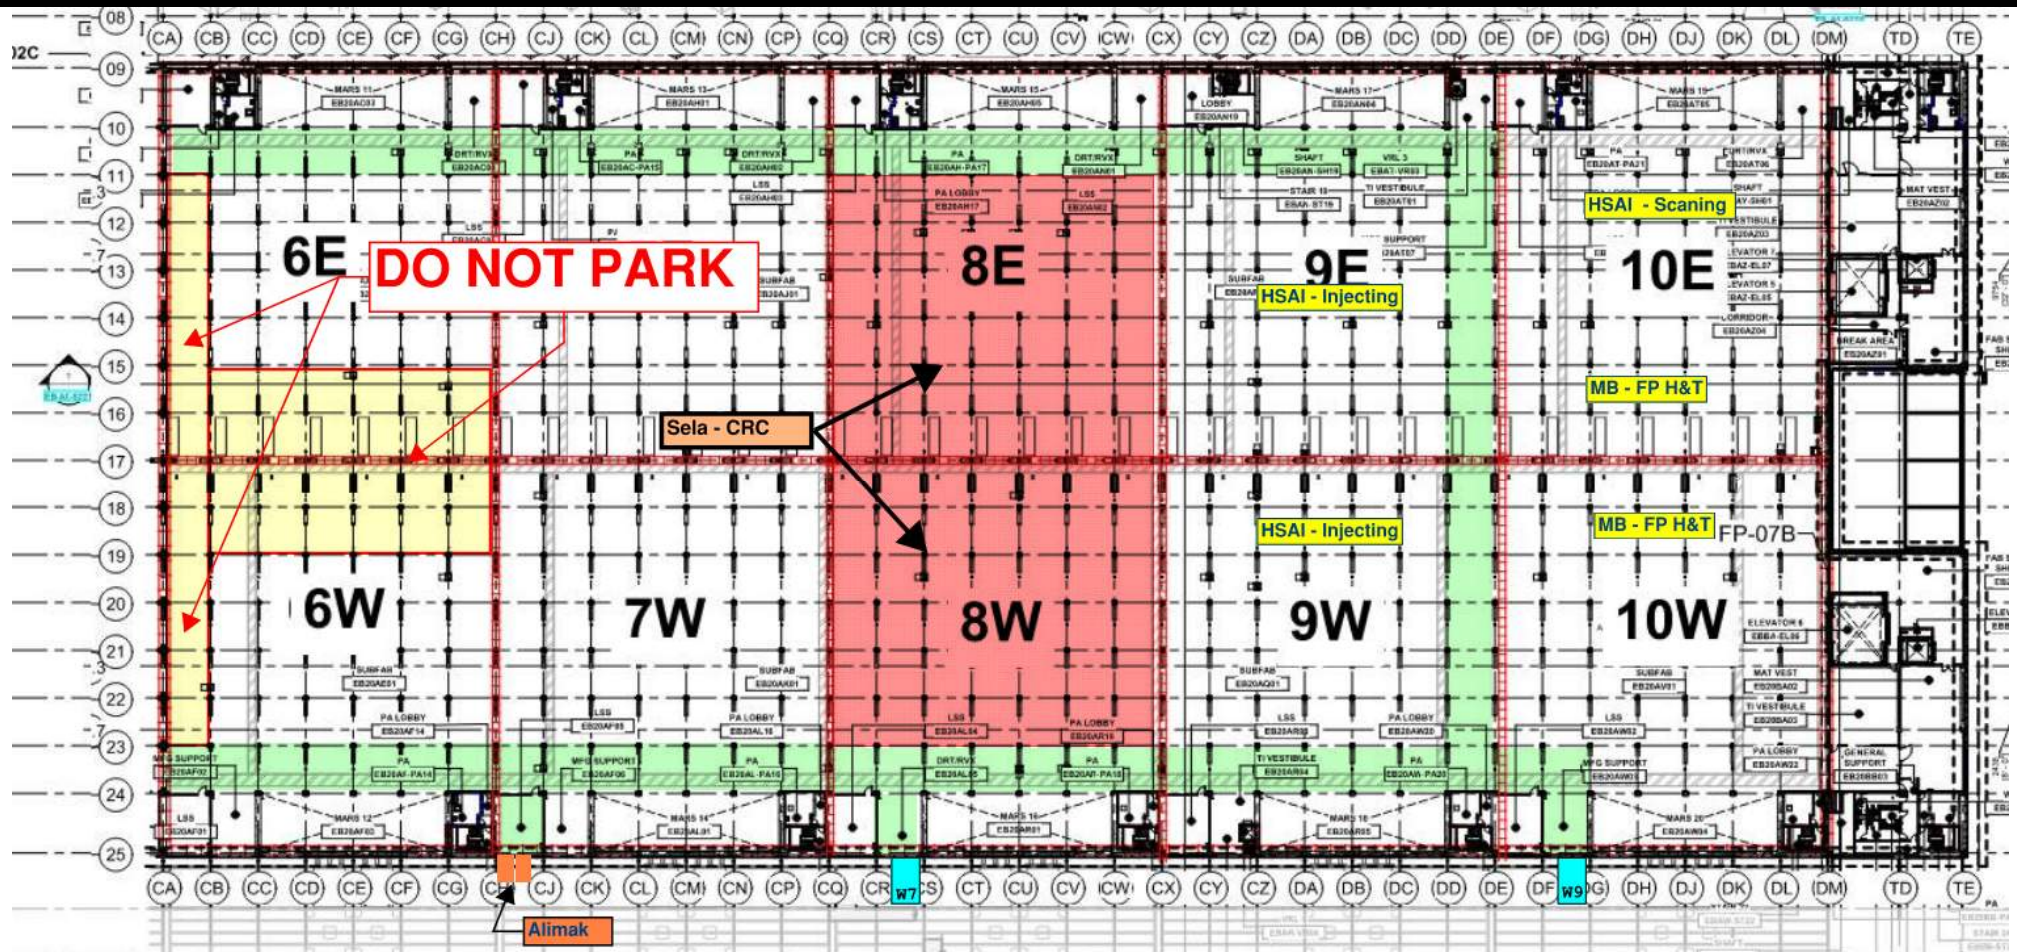

Tavas + Talent
solution
P1 cleaning
1E+1W

ELRAM started
installing rhs's 9:10 L

D&P 5RA
MISSING
BLADES

WW-TC
LINE HSS
FRAMIN
G

RPC FRP
PAINT 5RA
BEAMS+BLA
DES

Sela-Ww 45 shotblast
Starting sunday

D&P blades
install

Elram- AA line
columns+G1 wall
mock-up
Chemo- Hangers
install
SN - Beams layout

1E

All trades should do
training and use
correct equipment to
work in this area

CRC AA-AK/17-23

Sela: CRC Done

Talad- Cutting around lids

SELA CRC PREP

2

3

45

L
I
N
K

CR level:
Afcon - Cable trays, modules and stickers, 2E, 2W, 3E, 3W, 4E
MB - 1W drops, 2E - 2W pipes and drops
Elram - 9-10, 24-25 columns/shaft walls, AA line column wraps
VW/JS - 17-18 line added beams+ AS south stocker beams
Meptagon - I&C 2W
D&P - 5E blades install.
Talad - 5E blades, 1W-1E shaft walls
HYG - 5W Litho crane steel
T - Duct prep for test AA-AH east
Talad - 1W 4DA holes drilling, 1W cutting around steel, 17 line bracing
TMT - Safety net install

BLOWDOWN IS COMING
NOV 14TH! 10 WD LEFT.

2E

3E

4E

5E

Talad-ongoing beam bracing across 17 line+aa/ab

2W

3W

4W

5N


Link


Pach-Taas - exhaust duct install and tie in
SIG- Mobile scaffold install
Afcon- Rack install
Newcotech- temp wall
Afcon - cable tray & racks iNstall

Staircase # 4
Exit to cr level
blocked




HOFFMAN CONSTRUCTION COMPANY

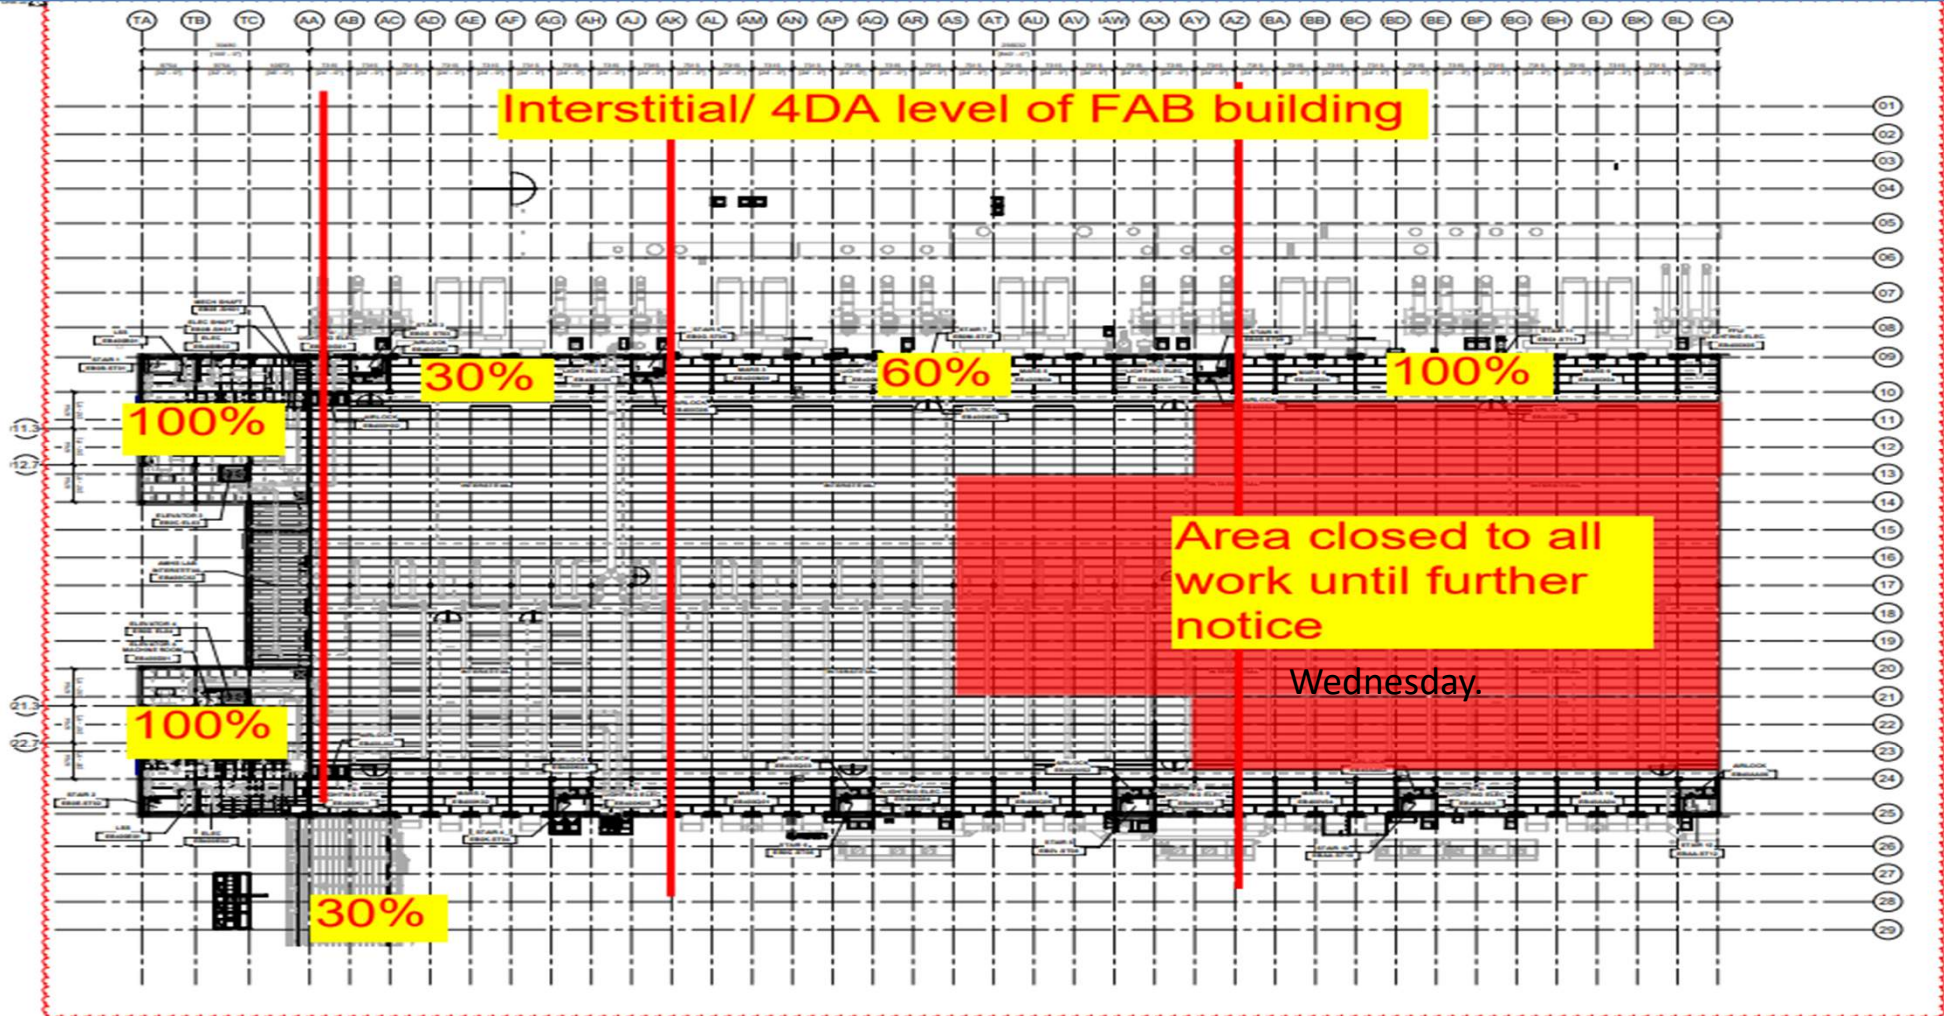

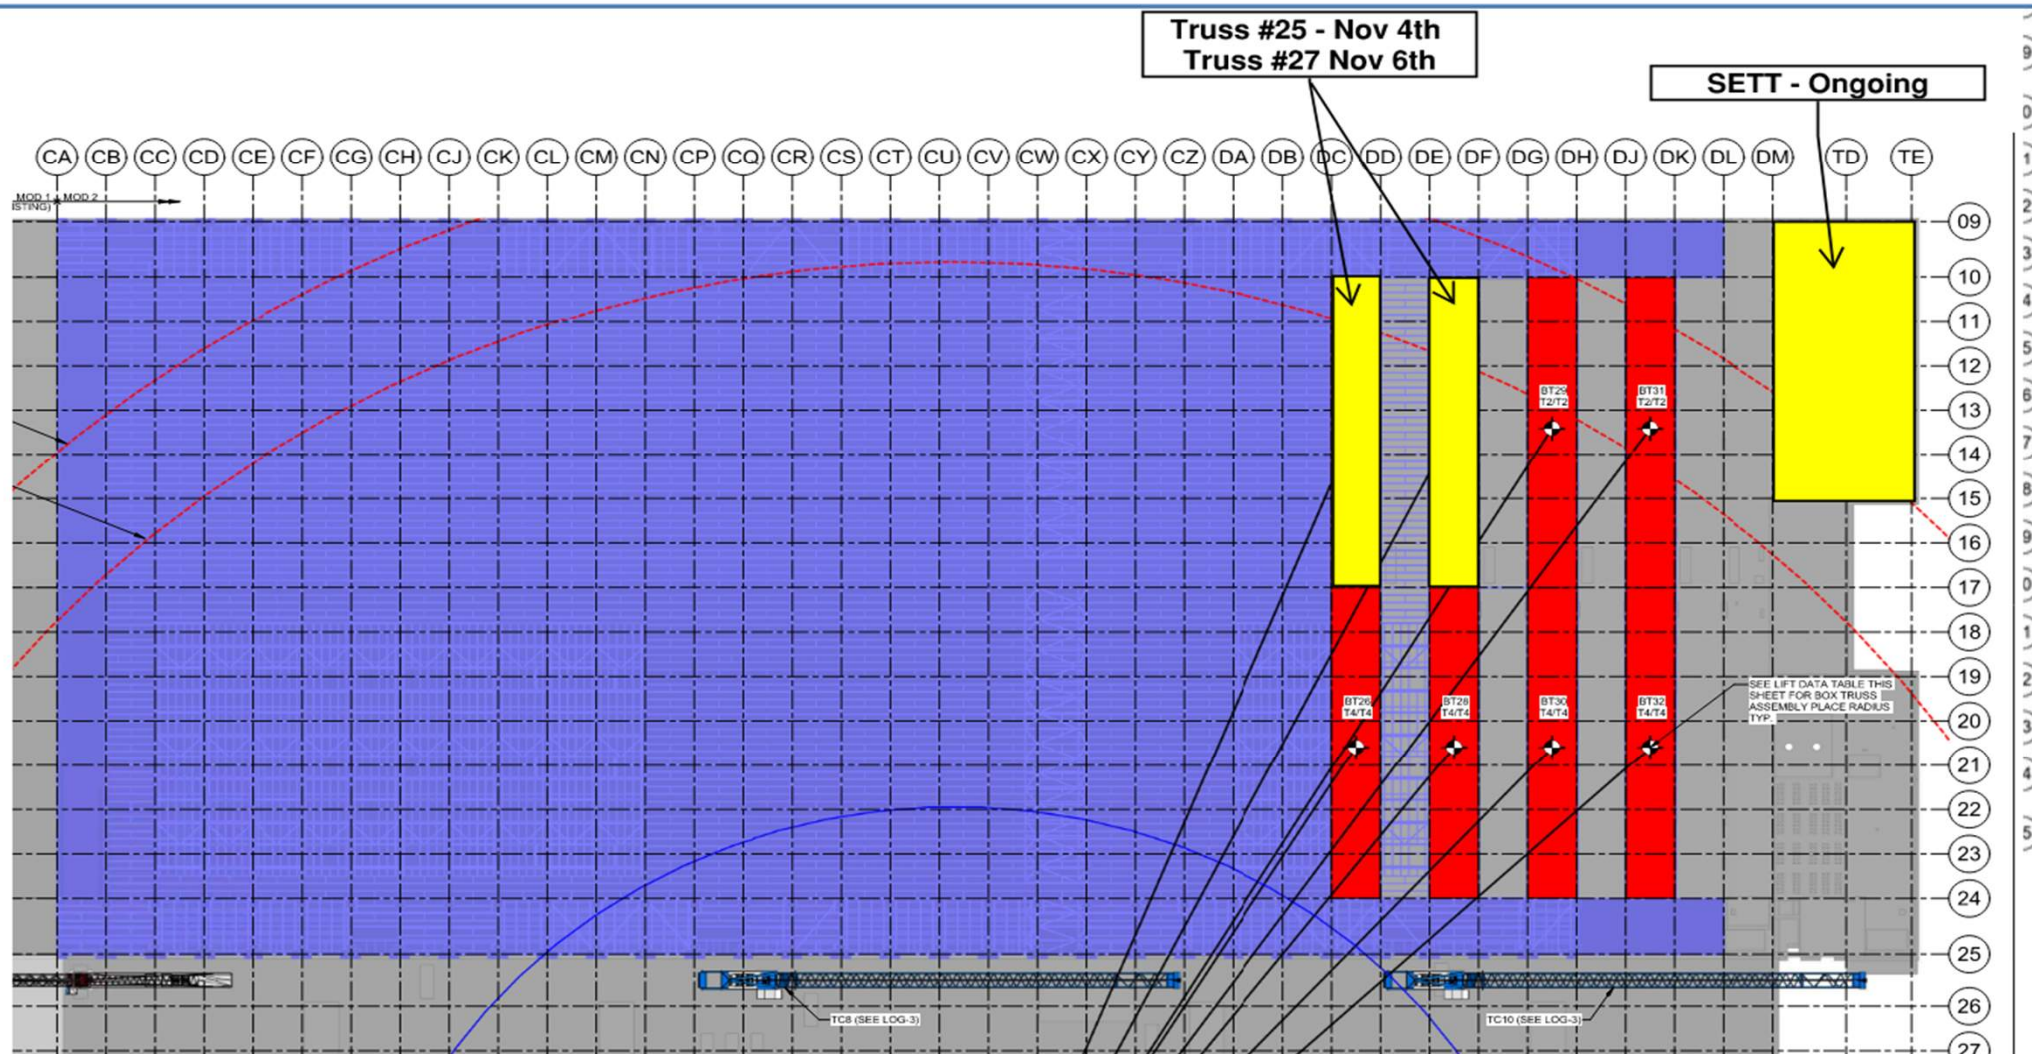


Clean Room Wall Of Shame

ELRAM

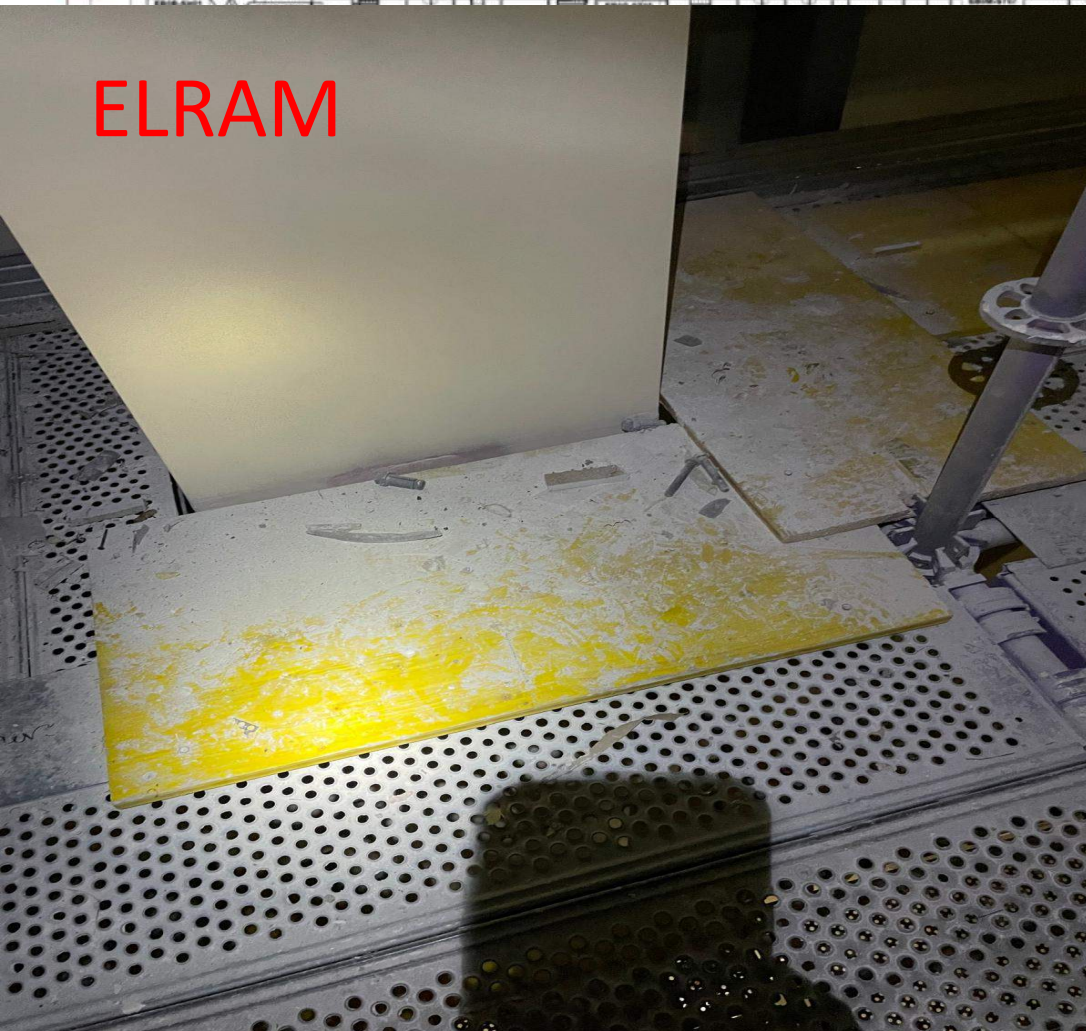

AFCON



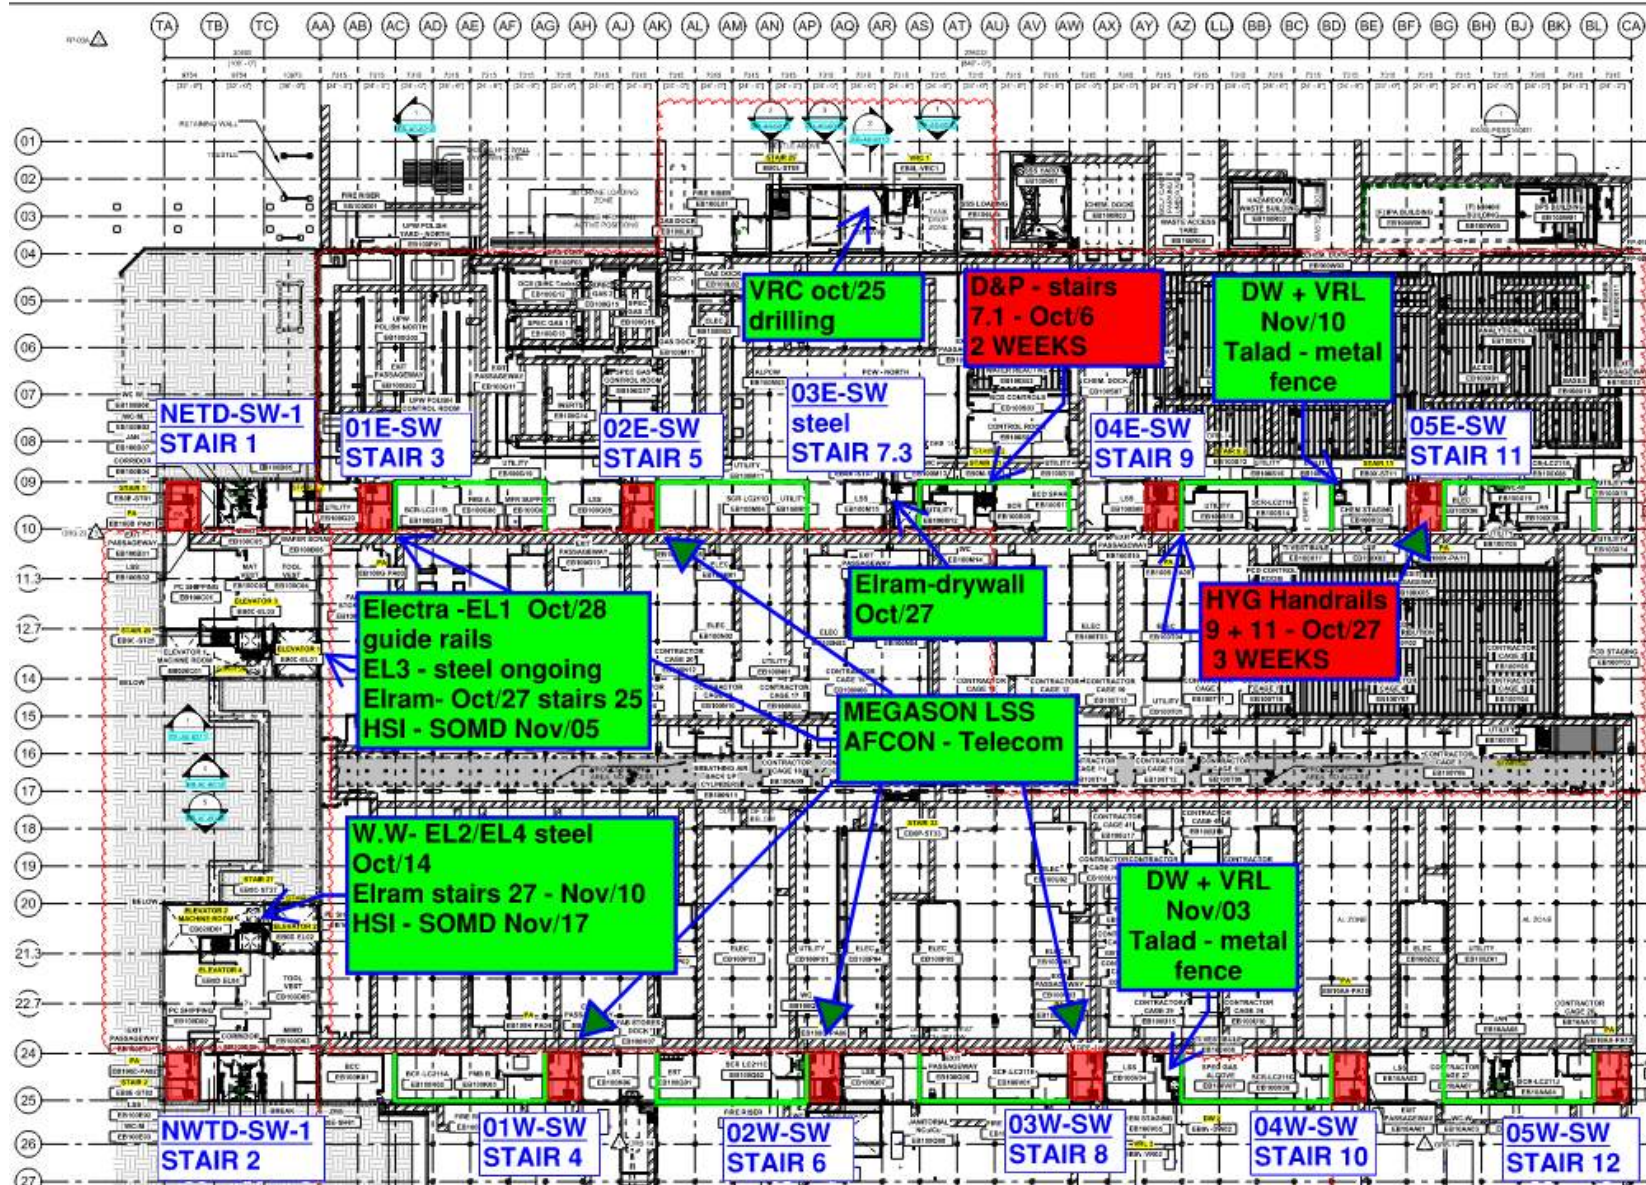

--

DEMO


Siding - West FAB - JYG


BLOWDOWN 30%


[illegible]

SUT - West			
AP		AO	AR
5		5	
5		5	
100%		100%	
1		1	
1		1	
1		1	
1		1	
1		1	
1		1	

ED-00A-SUB-UTILITY = 12,797

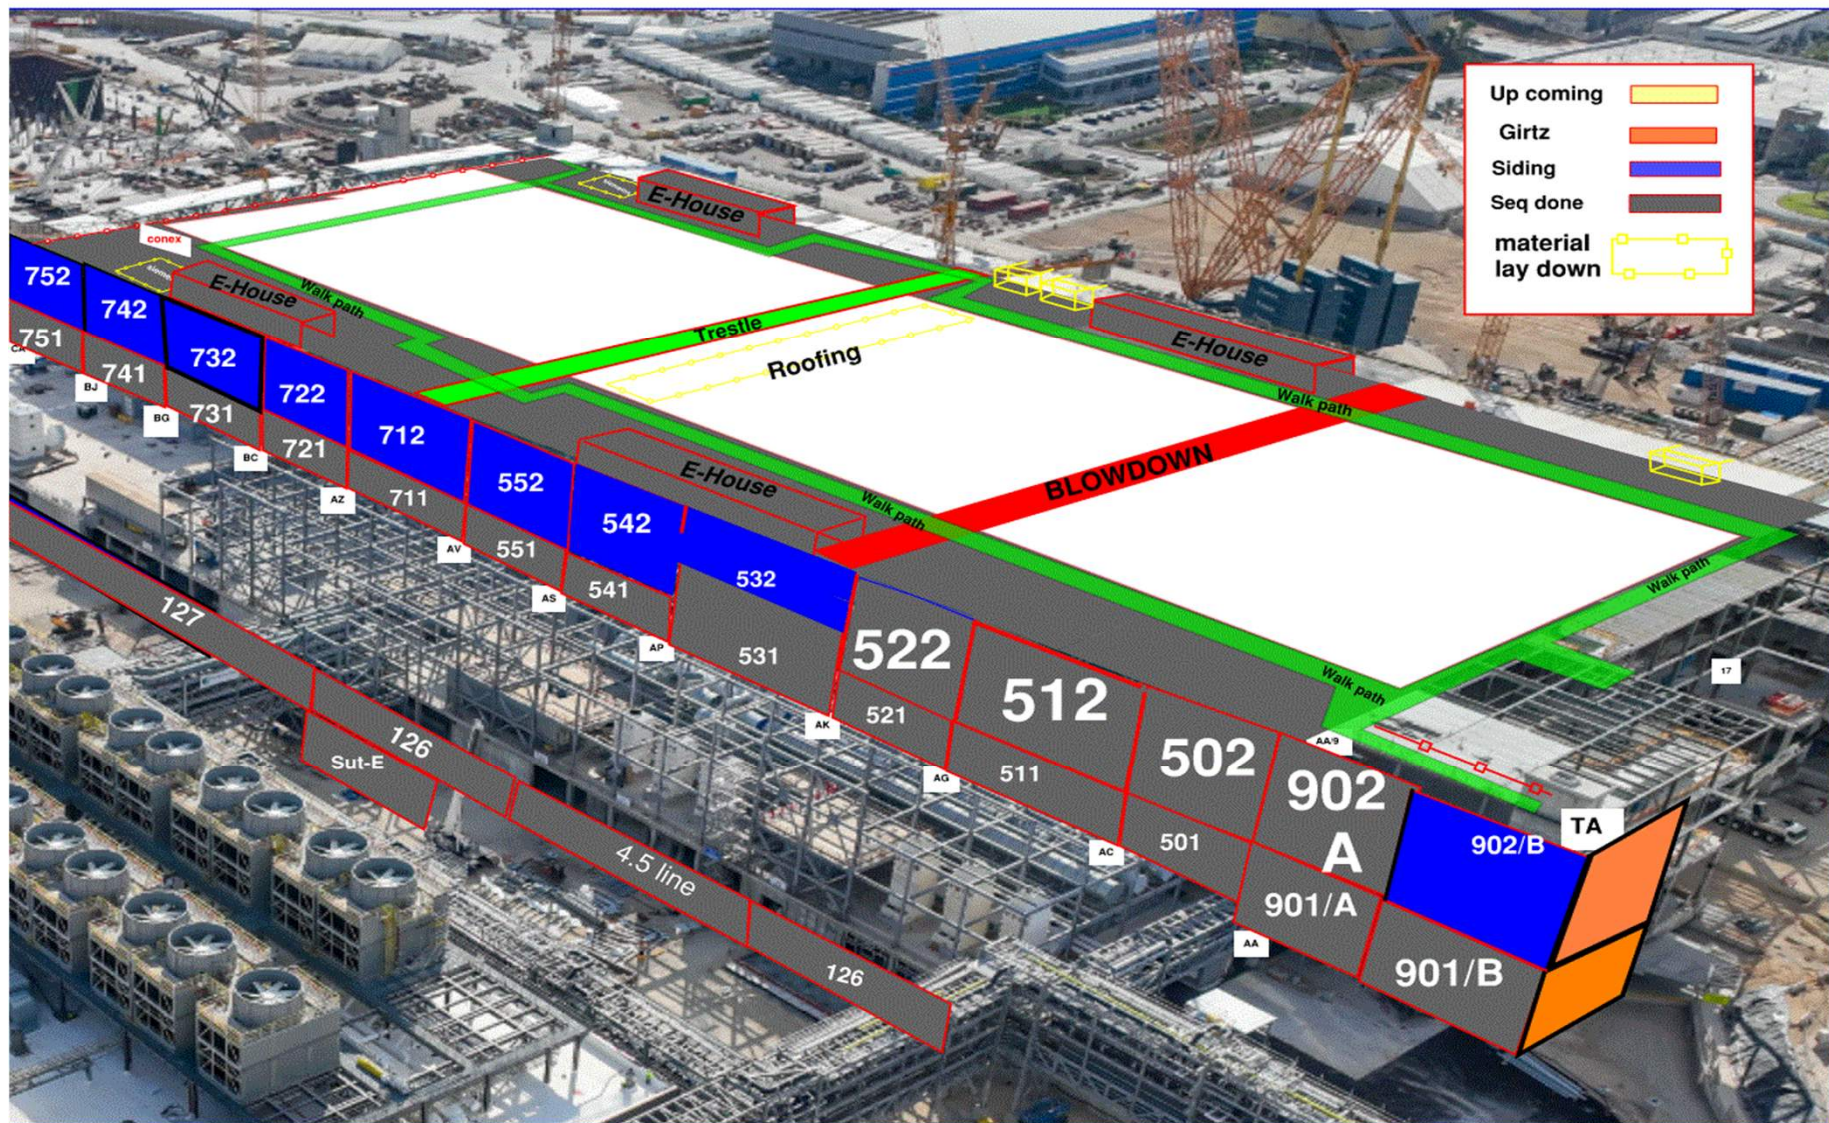

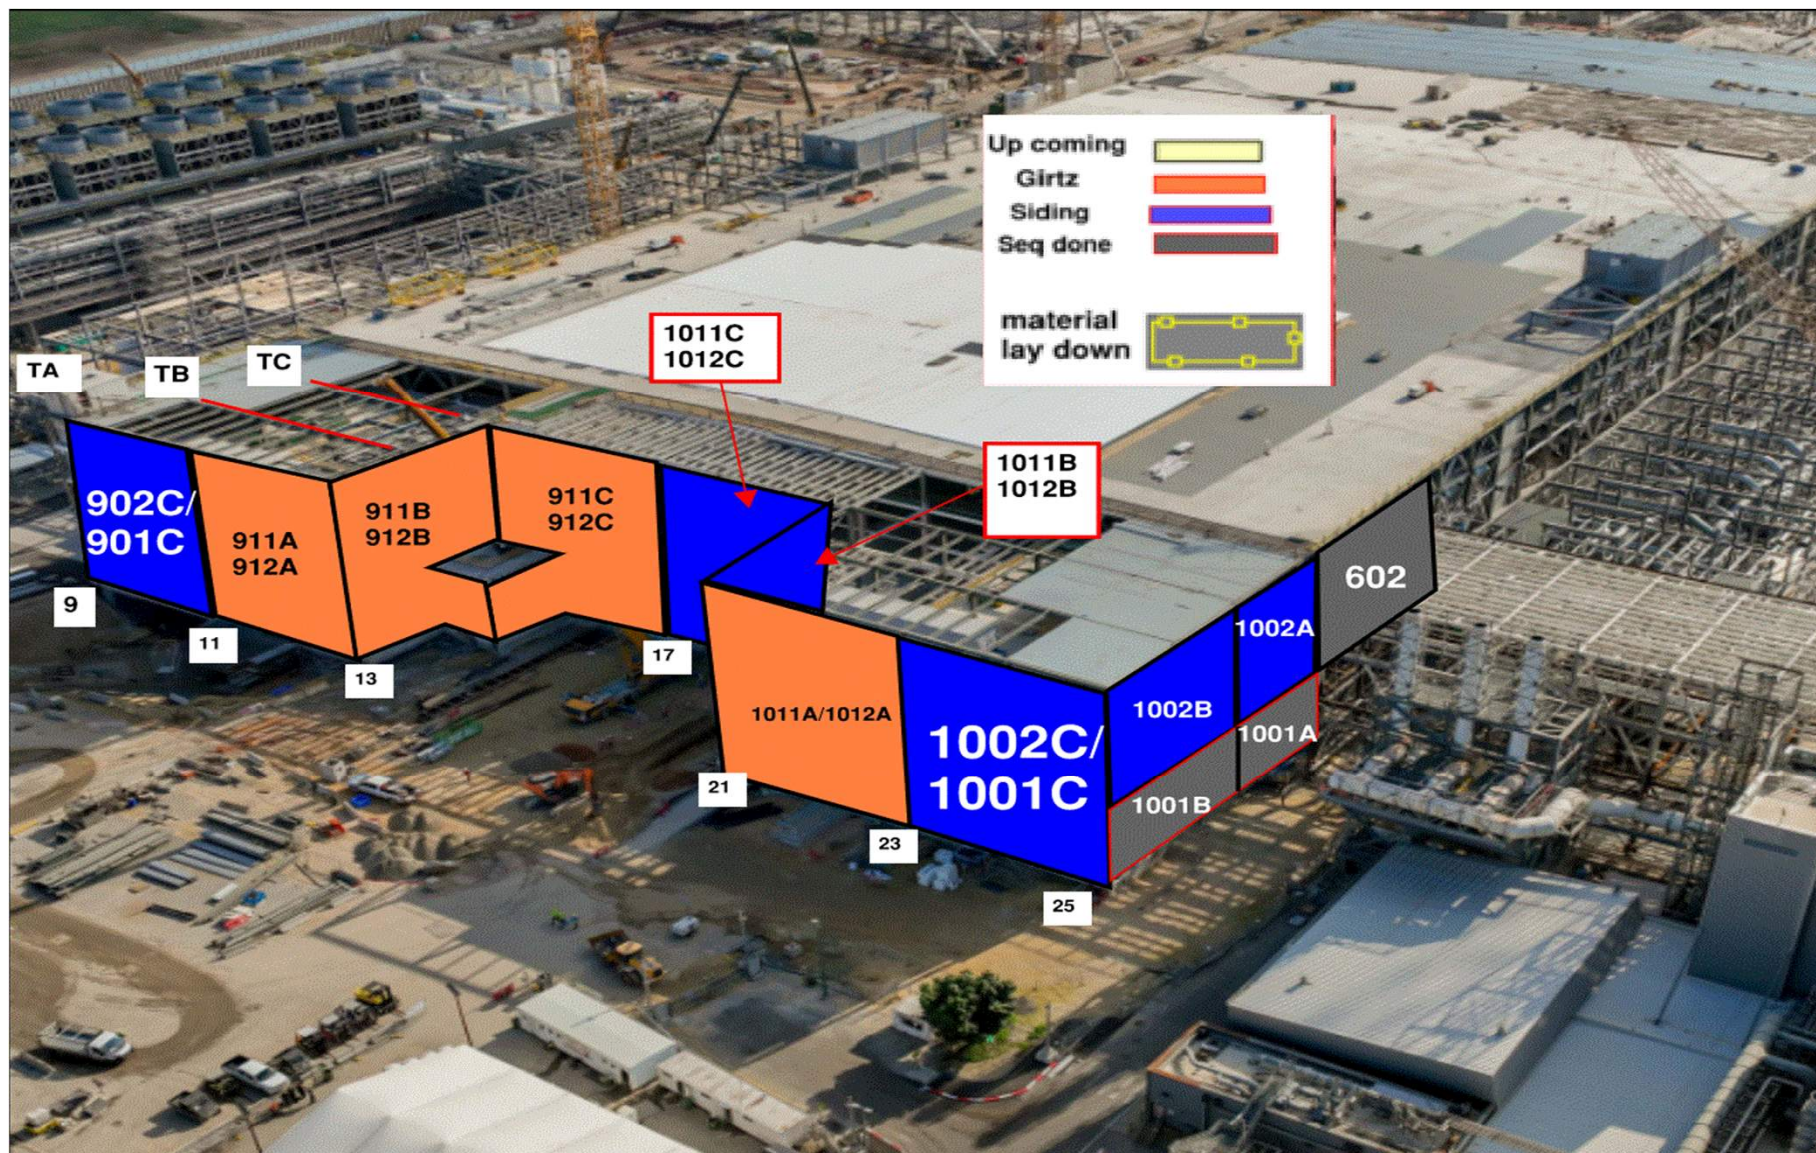

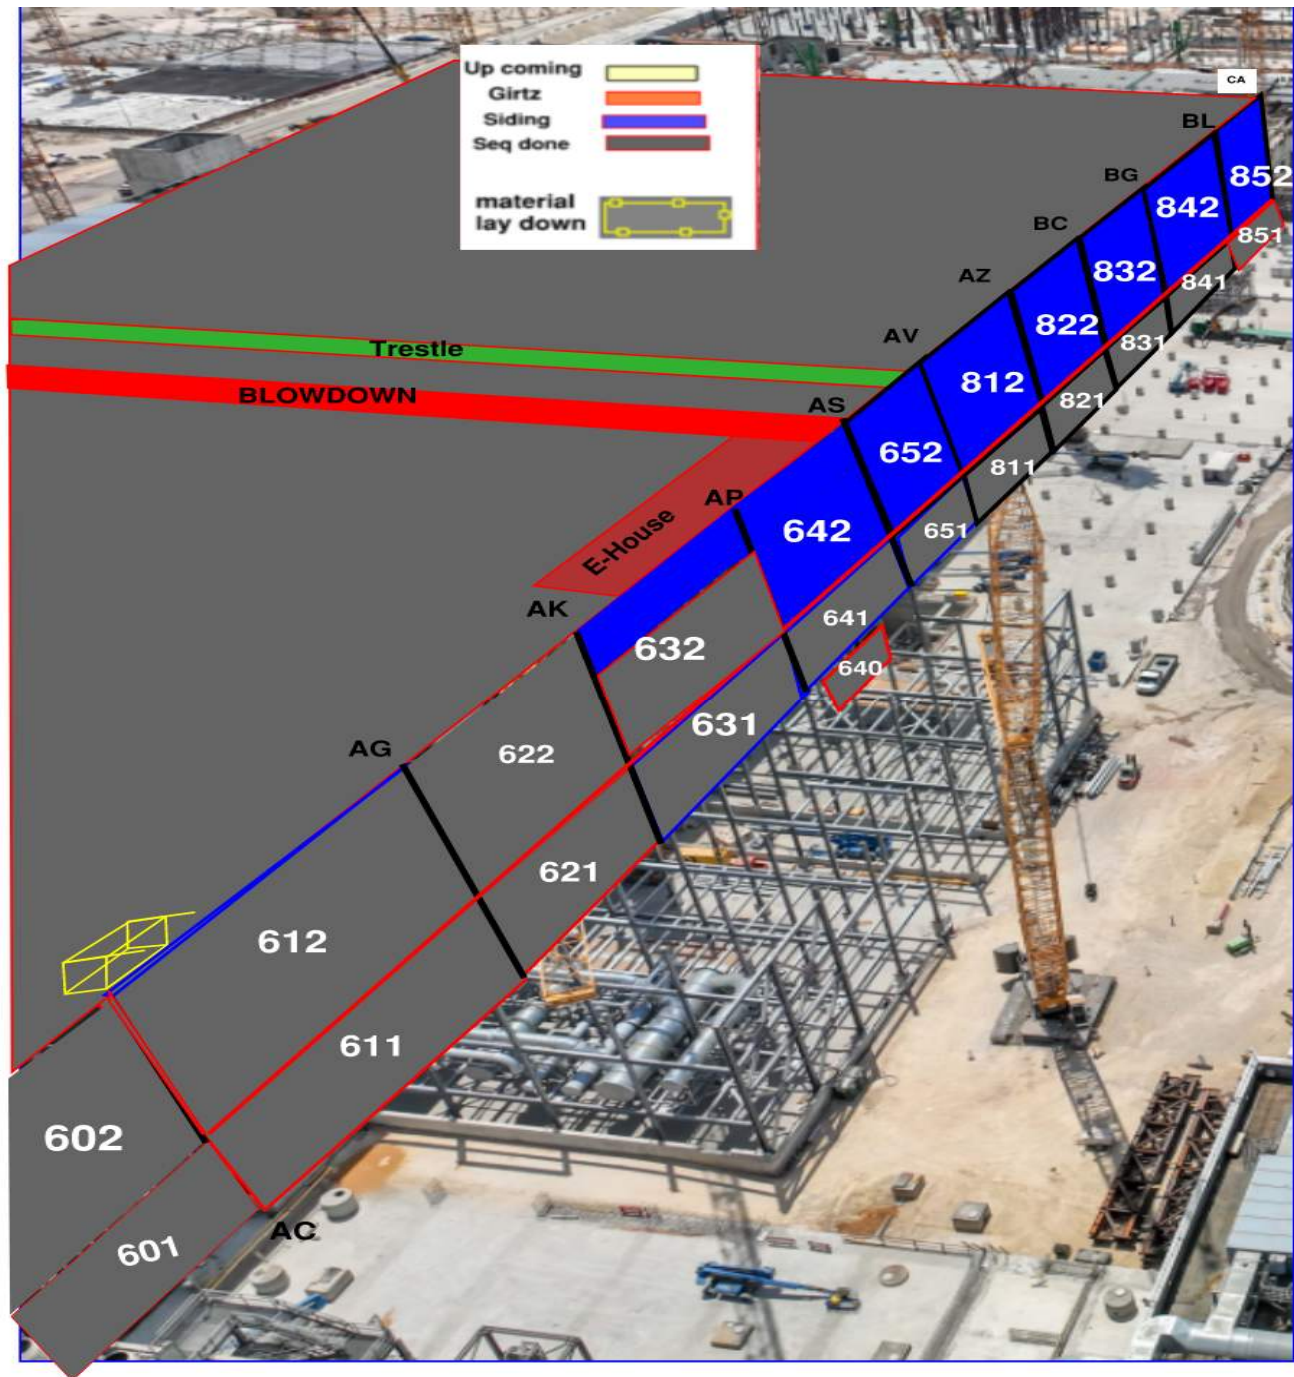




Garbage in
connex

PSSS.1

Utility Level
1YA

PSSS Roof
2SA

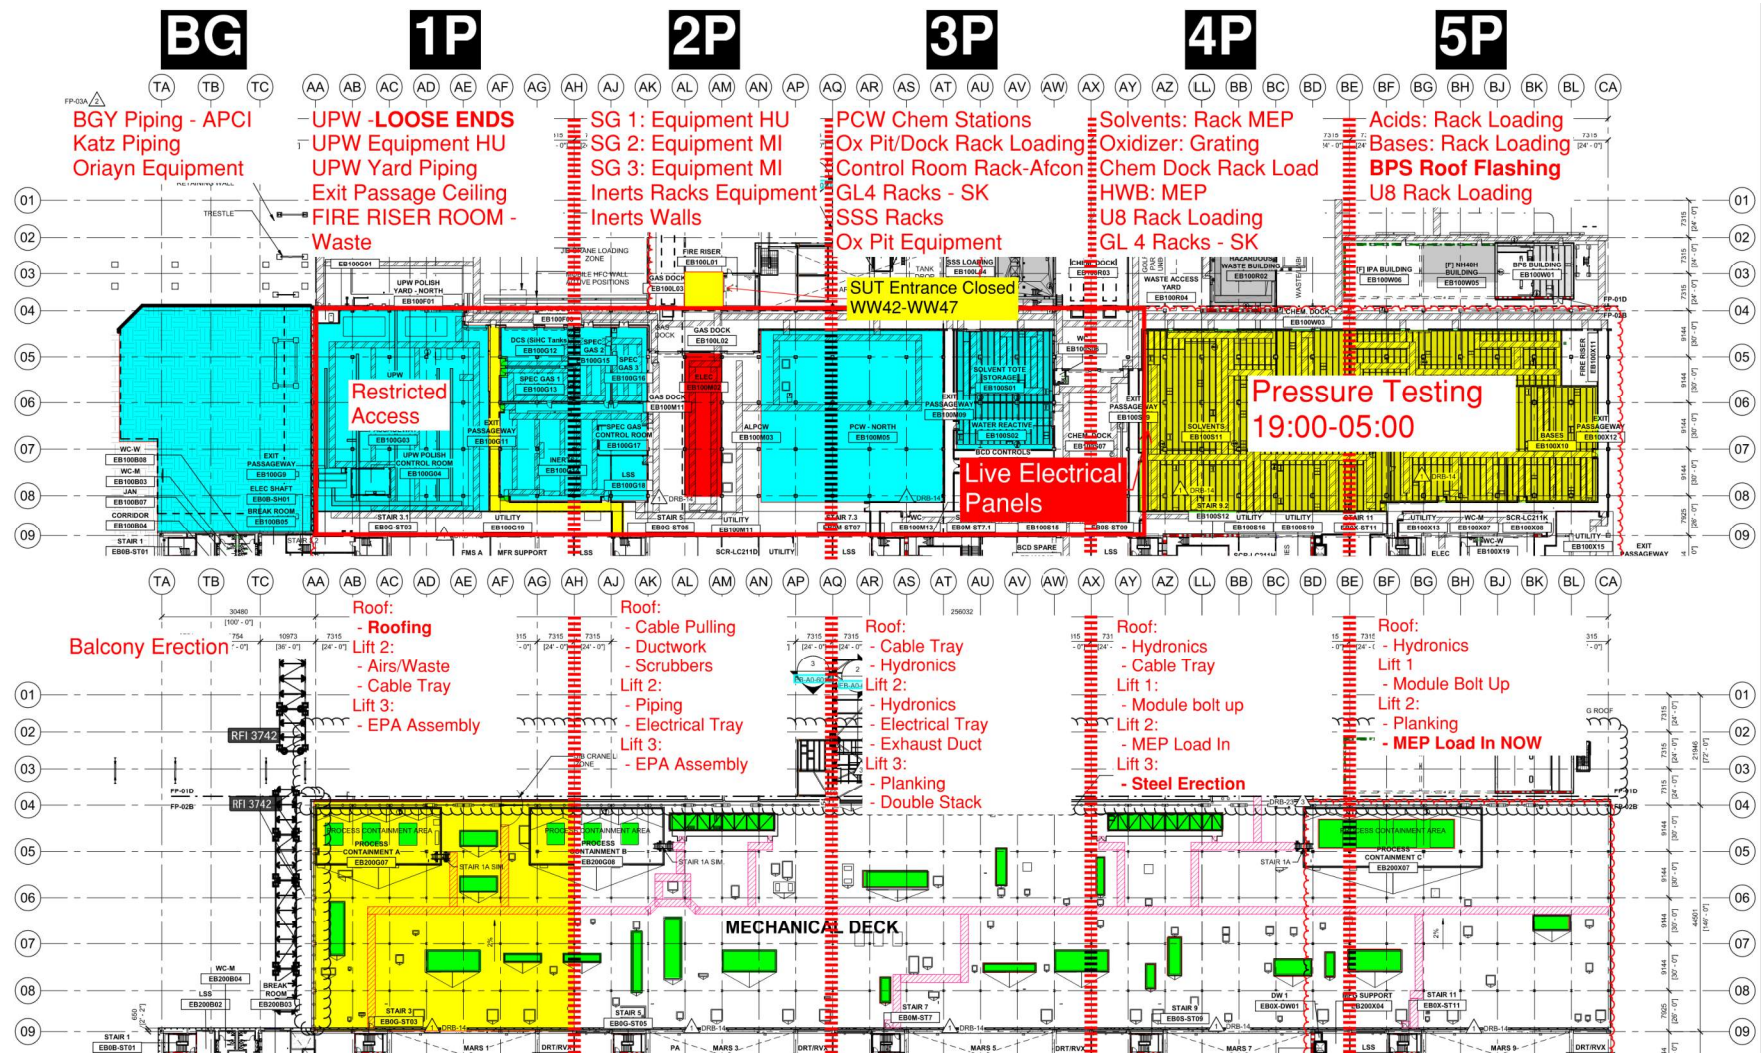

PSSS.2

6P


7P

8P


9P


10P

Utility Level
1YA

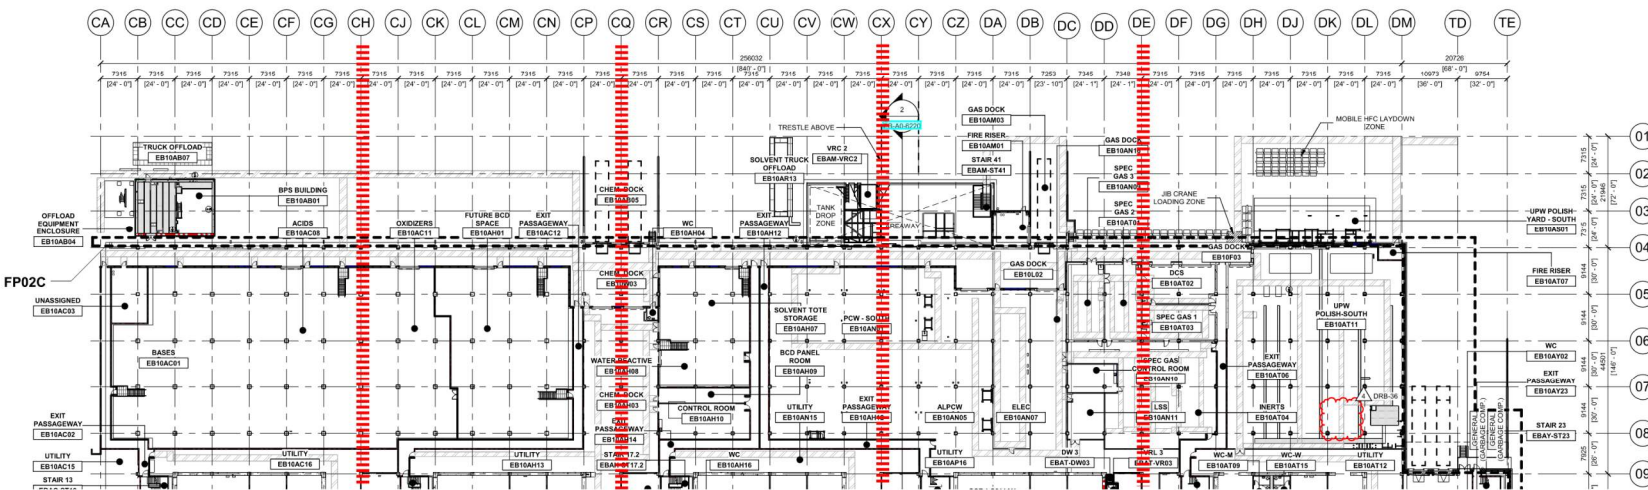

PSSS Roof
2SA

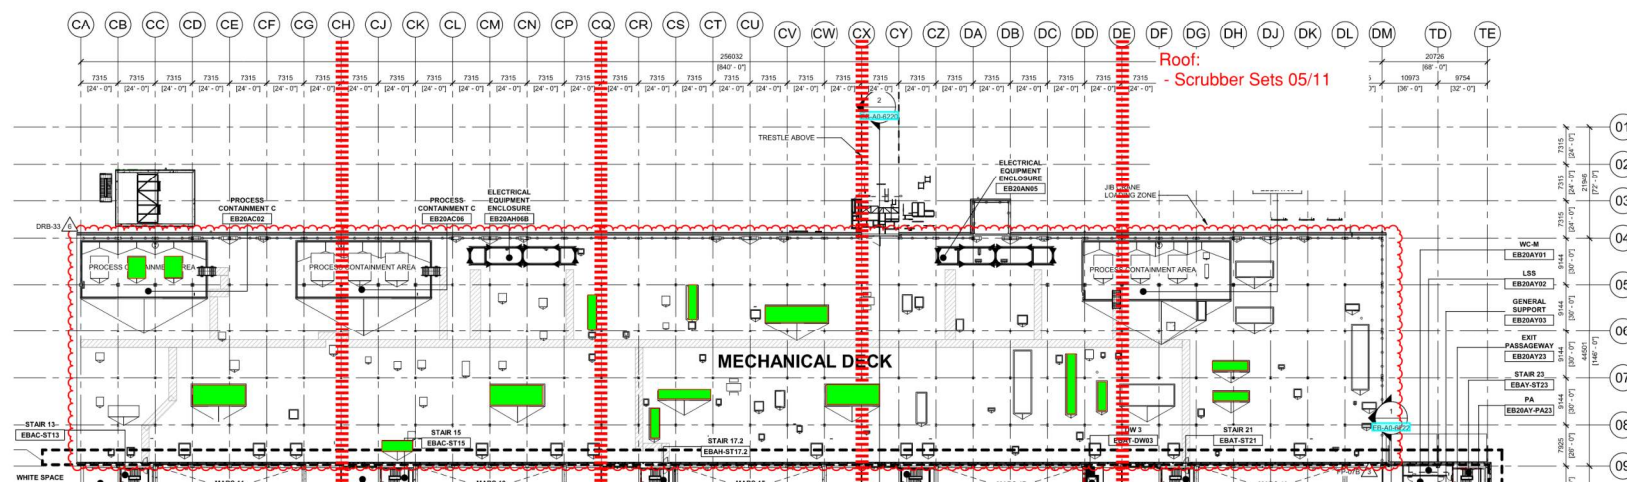



WJG 01J, 02J LIFT 2 & 3







WJG 03J, 04J, 05J LIFT 2 & 3




Walk Path Reroute

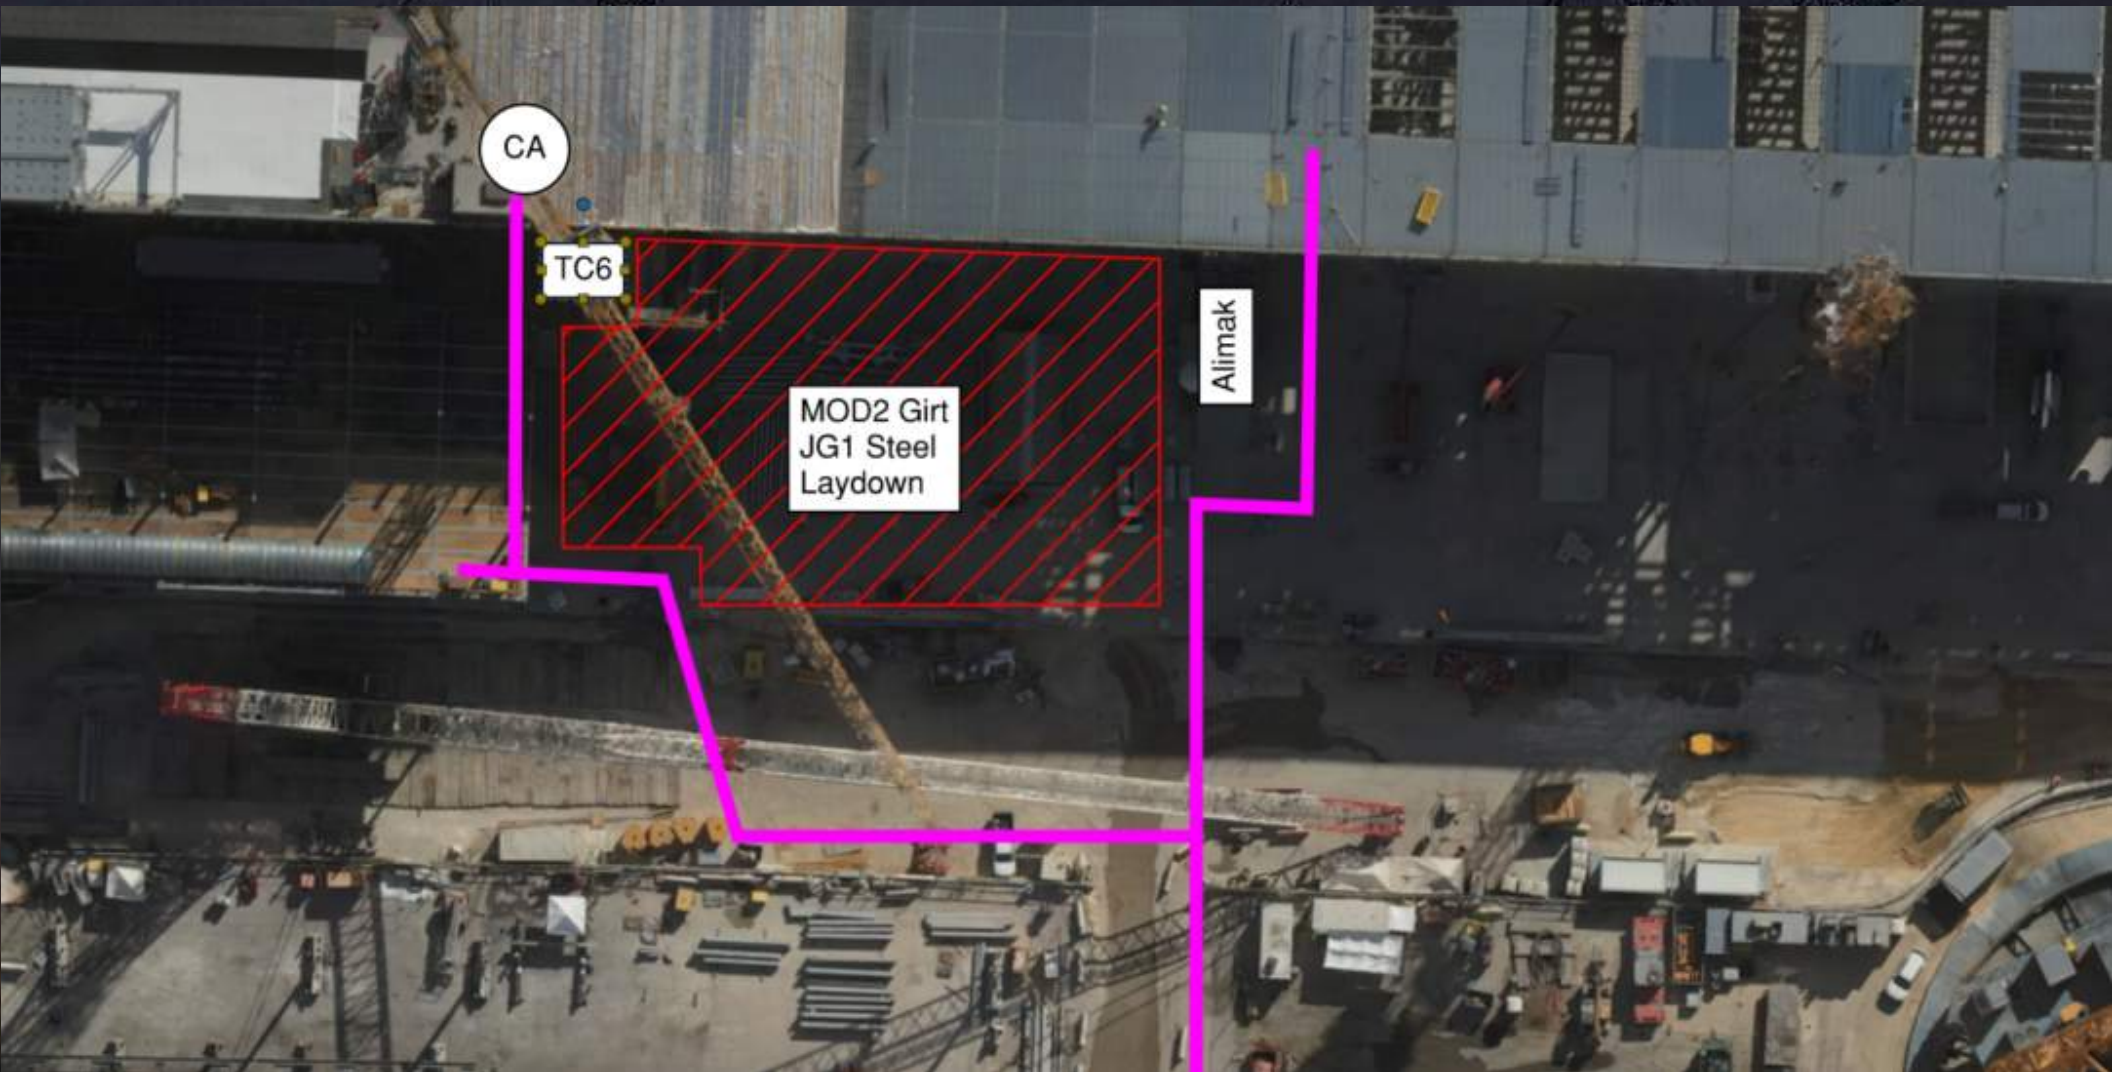



MAH101-7/8-00 SET 04/11 & 06/11

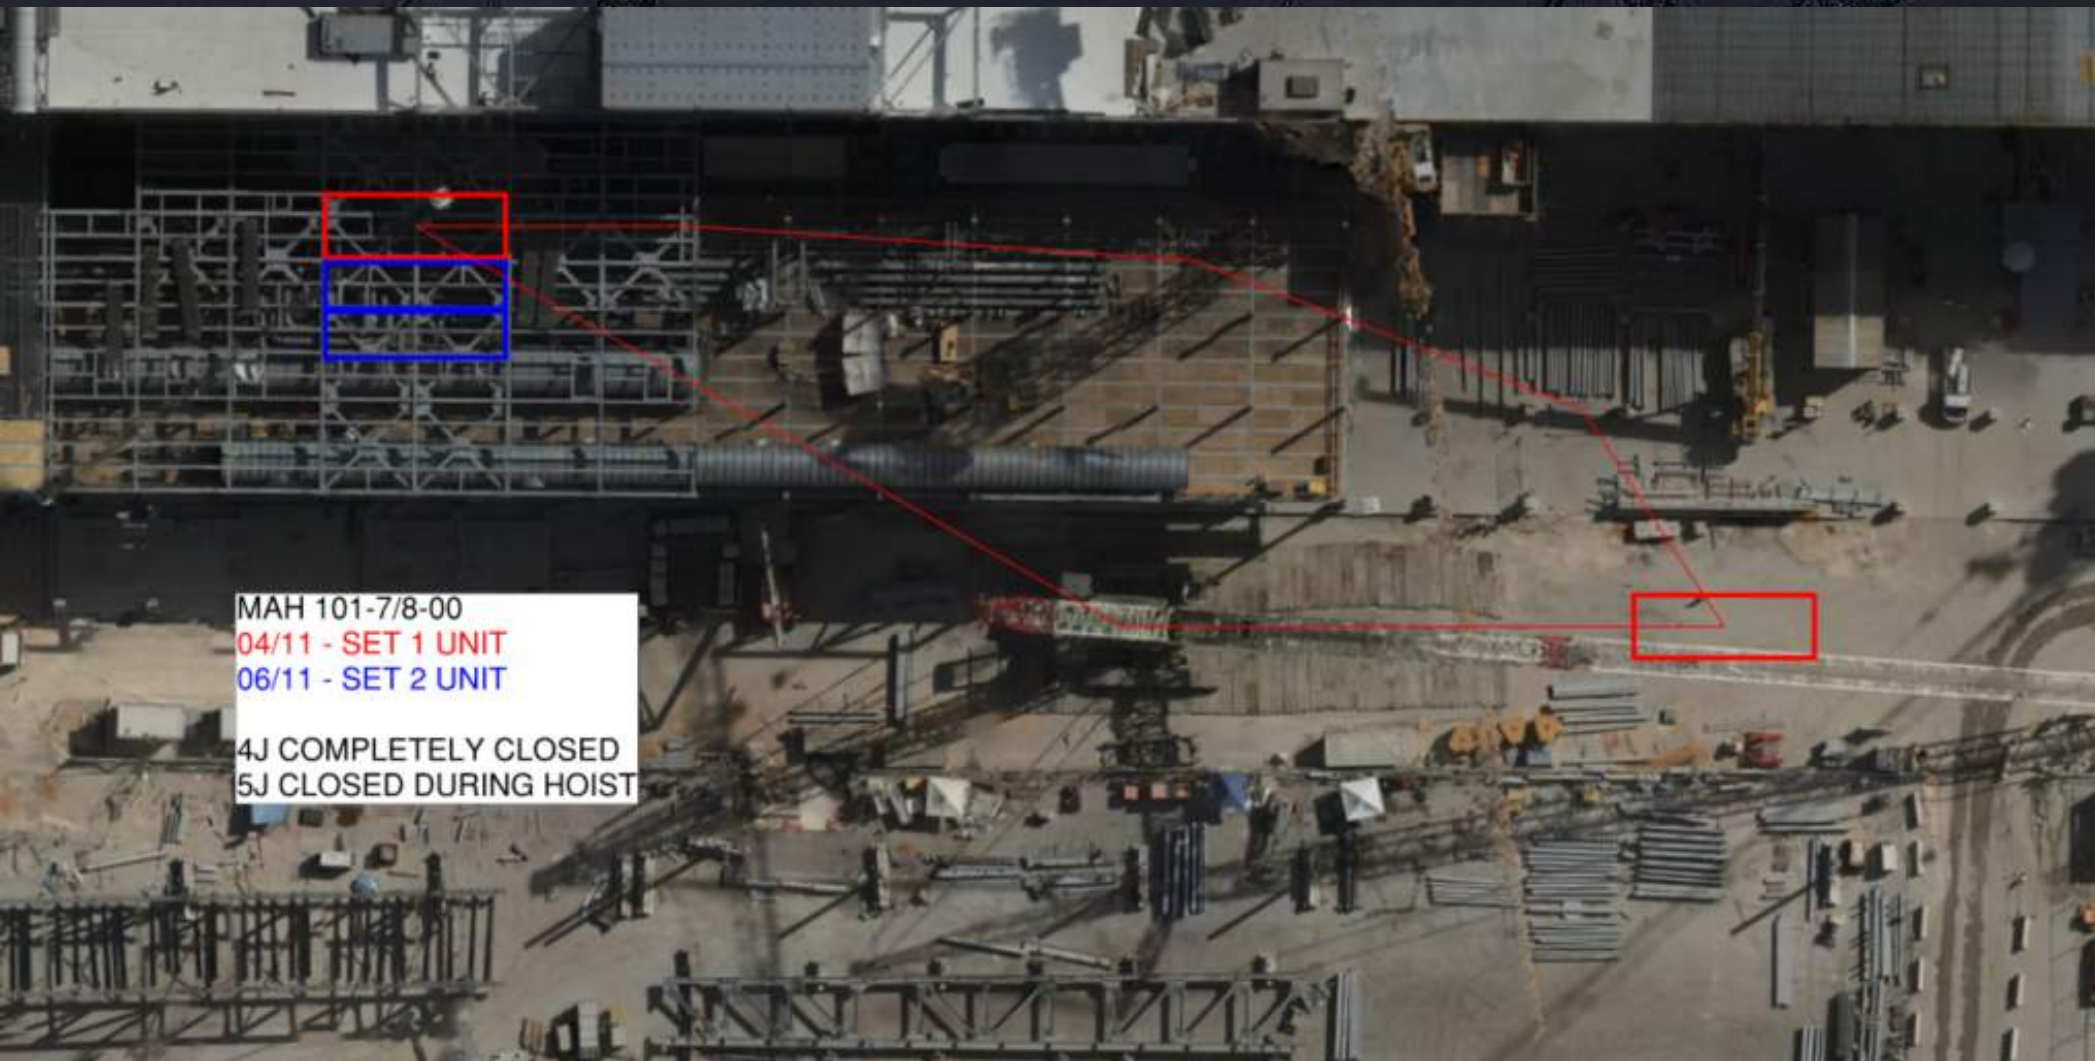

1J 2J 3J 4J 5J

EB100K02 EB100K03 EB100K04 EB100K05 EB100K06 EB100K07 EB100K08 EB100K09 EB100K10 EB100K11 EB100K12 EB100K13 EB100K14 EB100K15 EB100K16 EB100K17 EB100K18 EB100K19 EB100K20 EB100K21 EB100K22 EB100K23 EB100K24 EB100K25 EB100K26 EB100K27 EB100K28 EB100K29 EB100K30 EB100K31 EB100K32 EB100K33 EB100K34 EB100K35 EB100K36 EB100K37 EB100K38 EB100K39 EB100K40 EB100K41 EB100K42 EB100K43 EB100K44 EB100K45 EB100K46 EB100K47 EB100K48 EB100K49 EB100K50 EB100K51 EB100K52 EB100K53 EB100K54 EB100K55 EB100K56 EB100K57 EB100K58 EB100K59 EB100K60 EB100K61 EB100K62 EB100K63 EB100K64 EB100K65 EB100K66 EB100K67 EB100K68 EB100K69 EB100K70 EB100K71 EB100K72 EB100K73 EB100K74 EB100K75 EB100K76 EB100K77 EB100K78 EB100K79 EB100K80 EB100K81 EB100K82 EB100K83 EB100K84 EB100K85 EB100K86 EB100K87 EB100K88 EB100K89 EB100K90 EB100K91 EB100K92 EB100K93 EB100K94 EB100K95 EB100K96 EB100K97 EB100K98 EB100K99 EB100K100

Chemo - Insulation All over


WW - WSUT Steel Erection
Chemo - Insulation All over

WW - WSUT Steel Erection

Lesico Pipe + Pipe Support
Pach Taas Bolting


TC4 CONCRETE
POUR BACK

Pach Taas - Bolting




NDT TESTING

WEDNESDAY 31/10/2024: 2000 - 0500

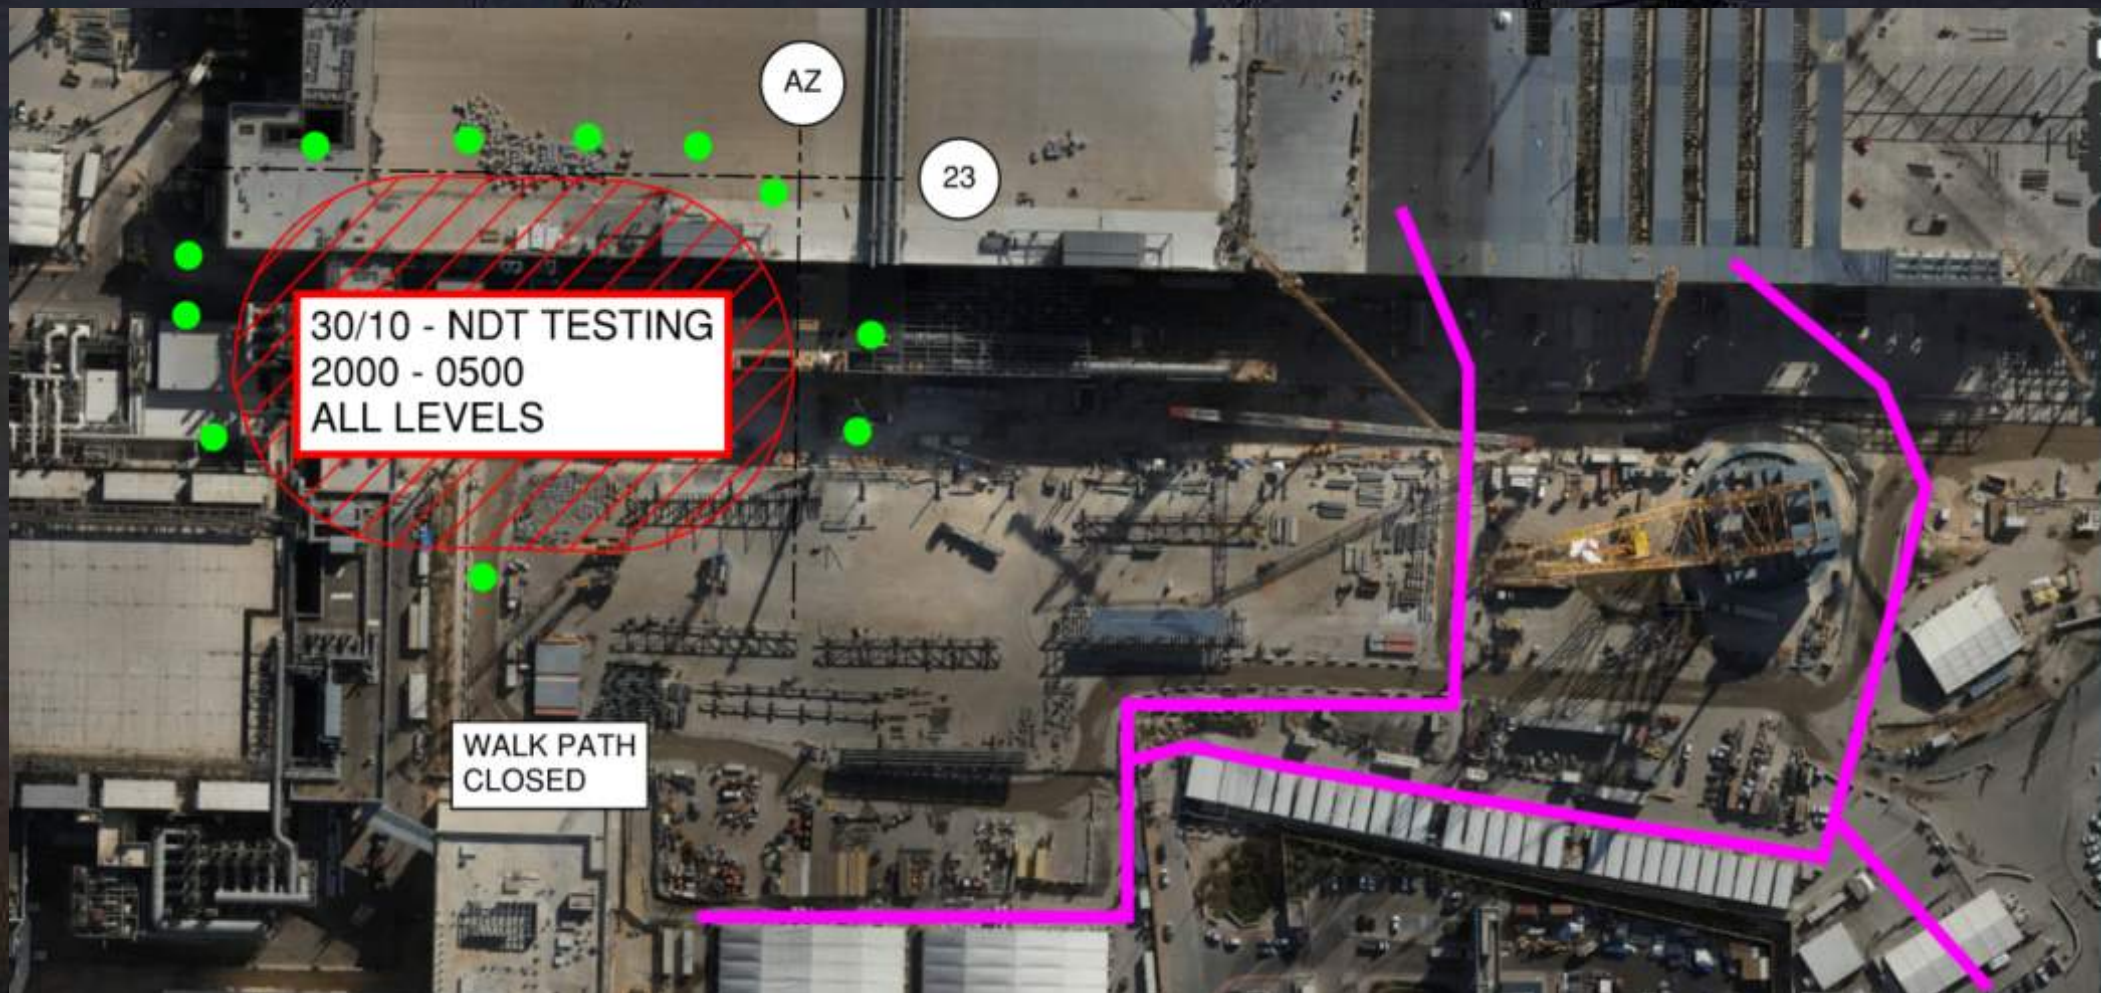



CUB 1

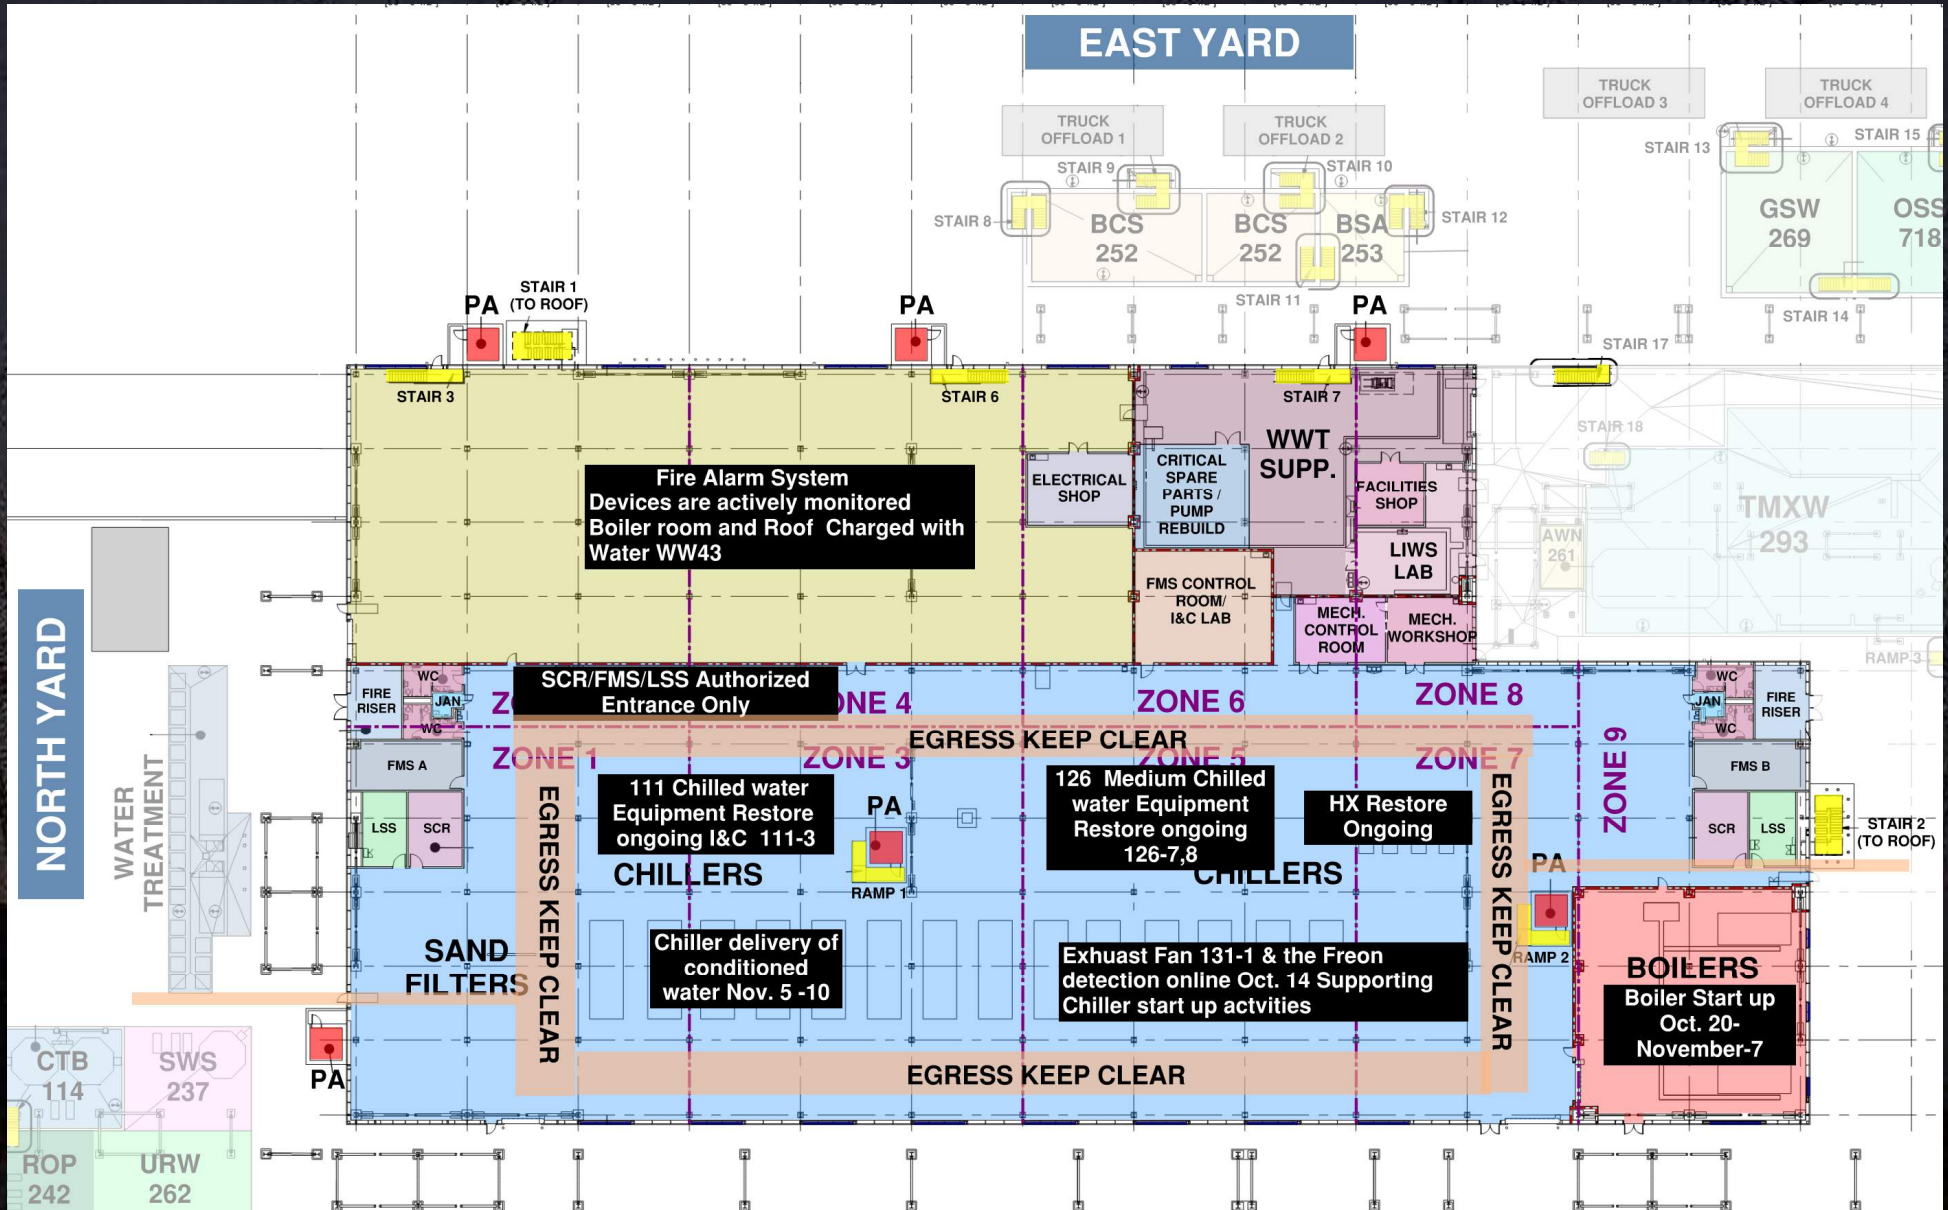


CUB 1 – Refrigerant Loading

CUB 1 COORDINATION MAP


A B C D E F G H J K L M N P Q R S

NOTES:


1. REFRIGERANT DETECTION SYSTEM IS LIVE.
2. IF ANY ALARM IS SOUNDED - ALL WORKERS MUST EVACUATE THE BUILDING. HORNS AND STROBES WILL SOUND AND INDICATE A GAS LEAK.
3. EVACUATION LOCATION TO BE IN NORTH YARD OF CUB 1. UNTIL AREA IS SAFE TO RETURN

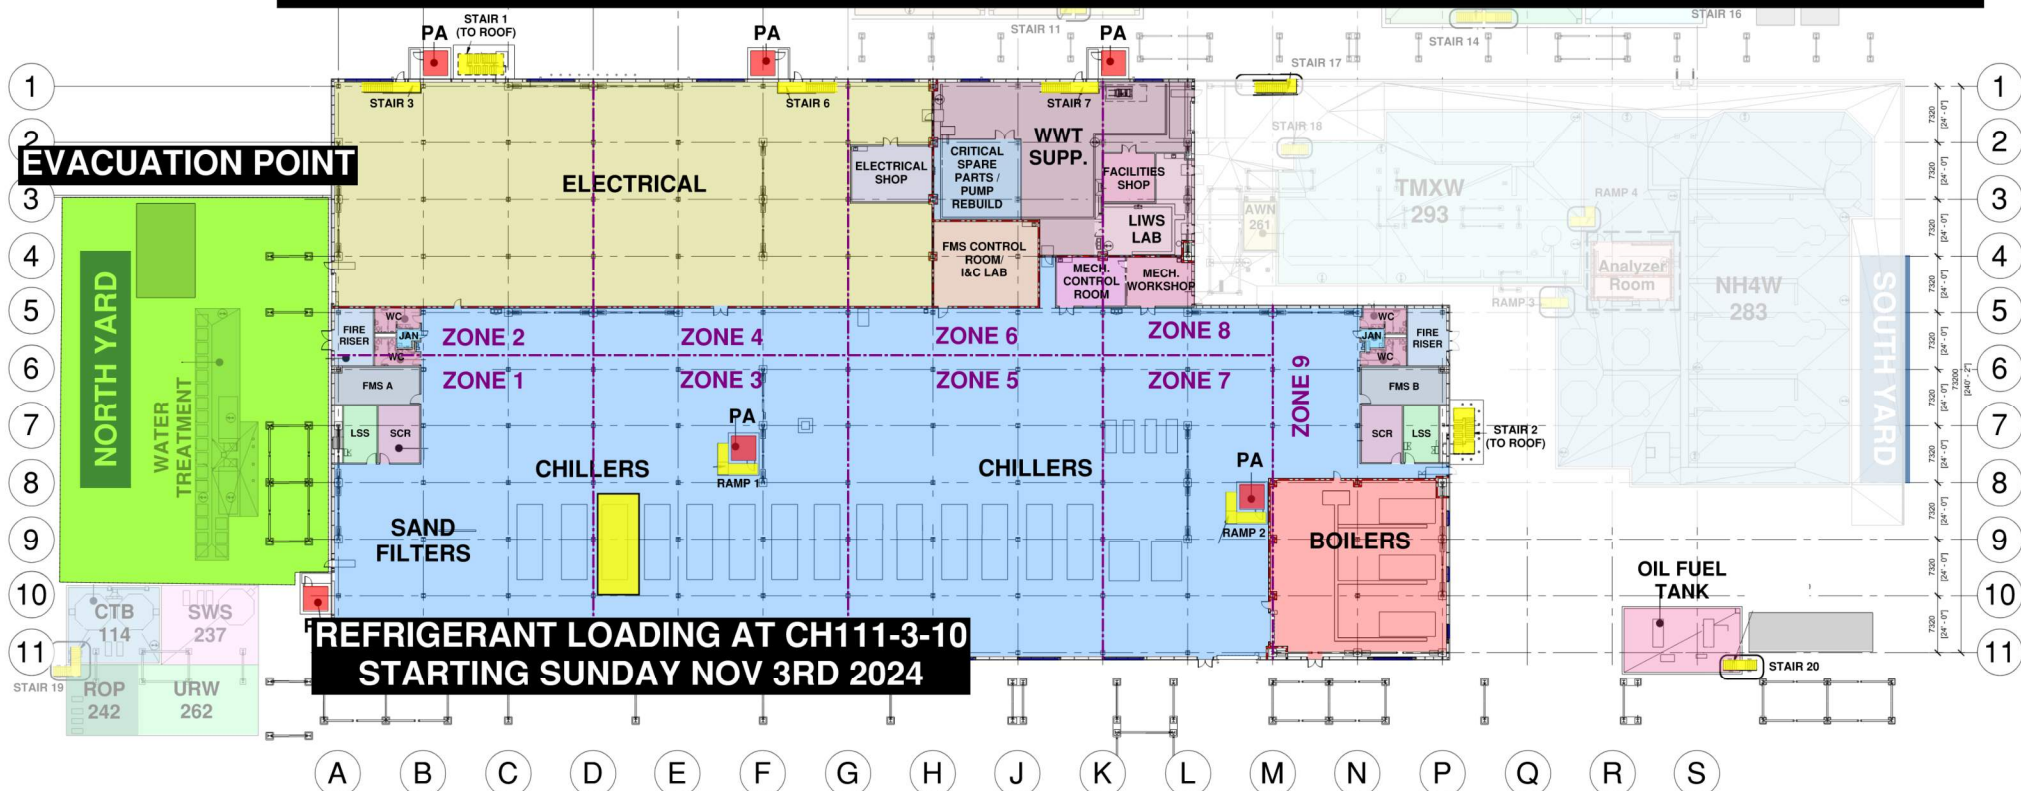


CUB 1 – EXTERIOR/ROOF

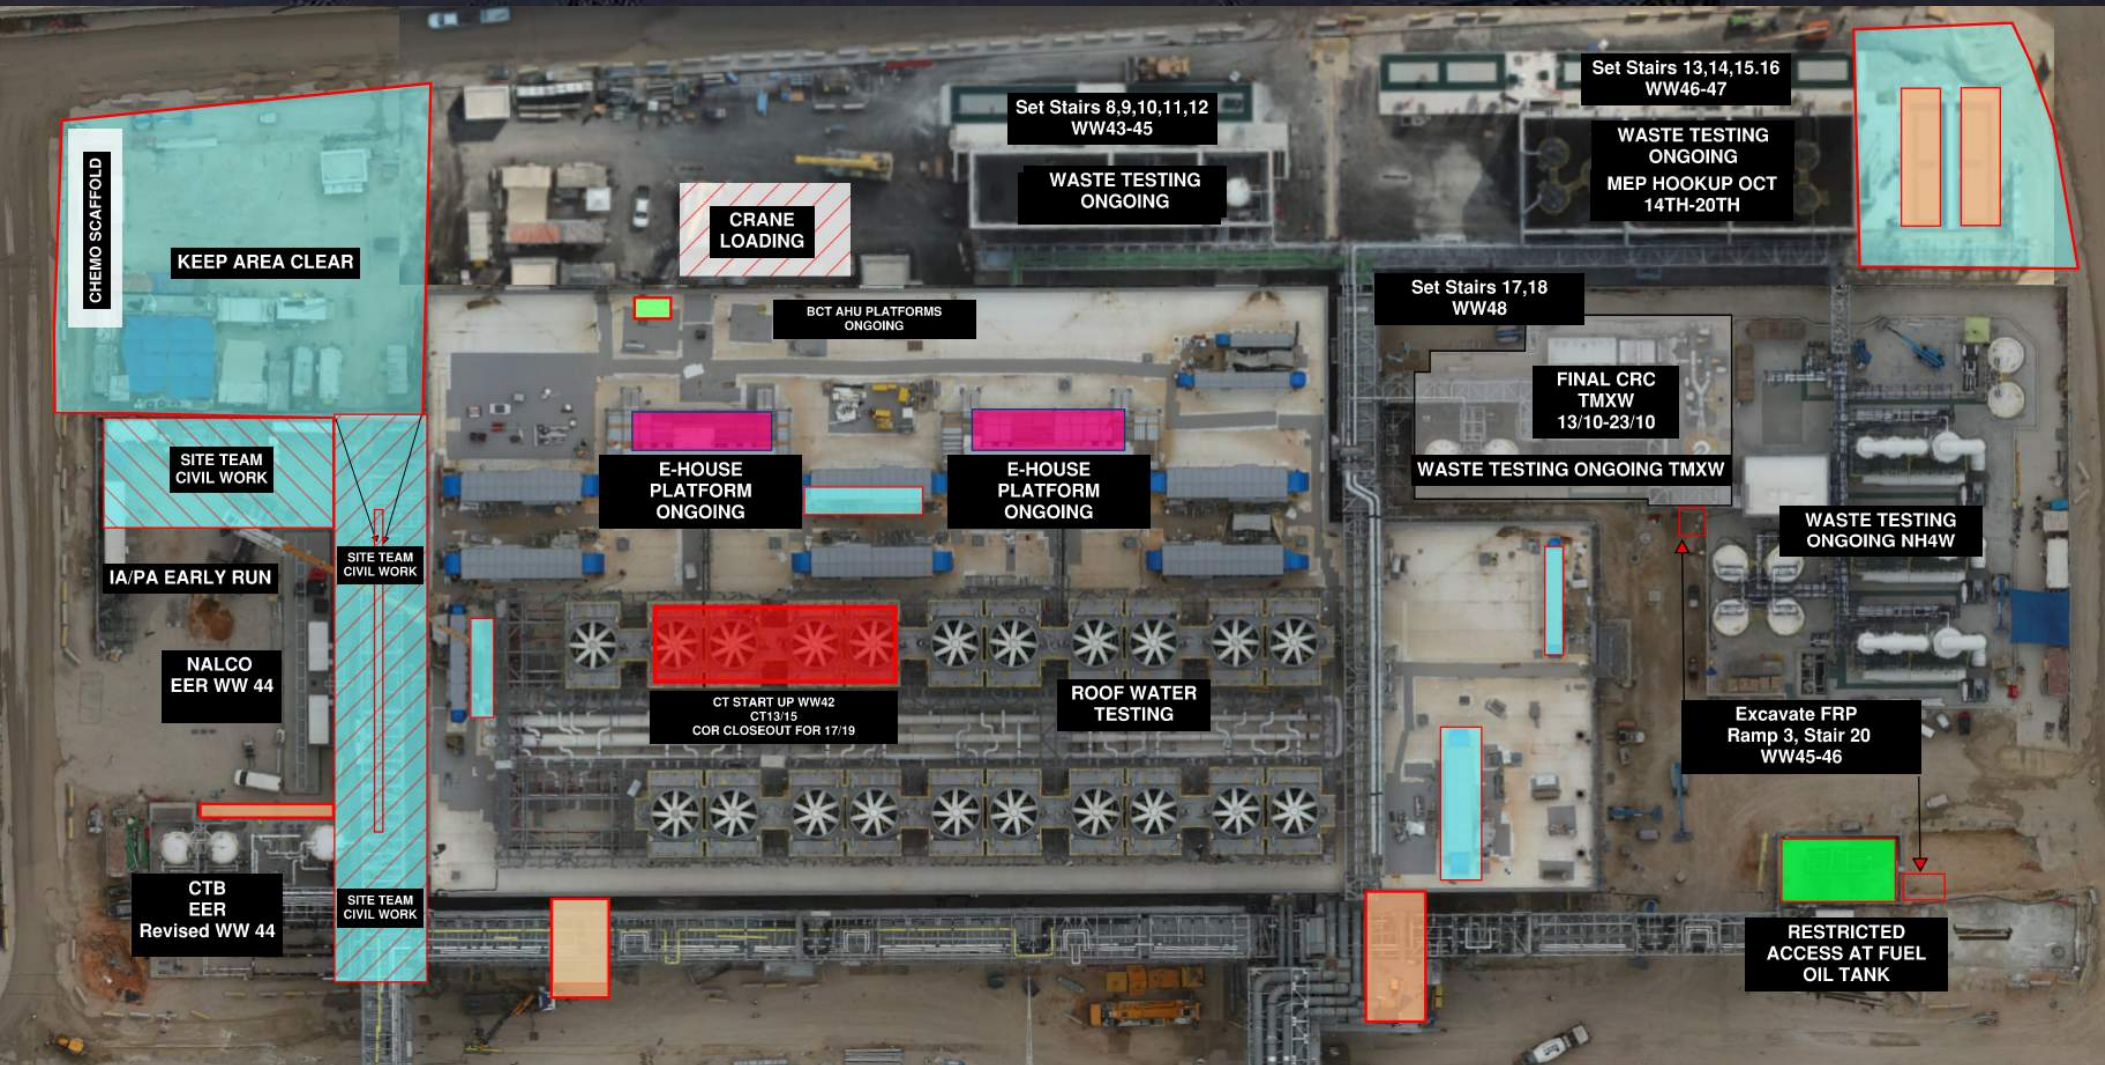


CUB 2 COORDINATION MAP

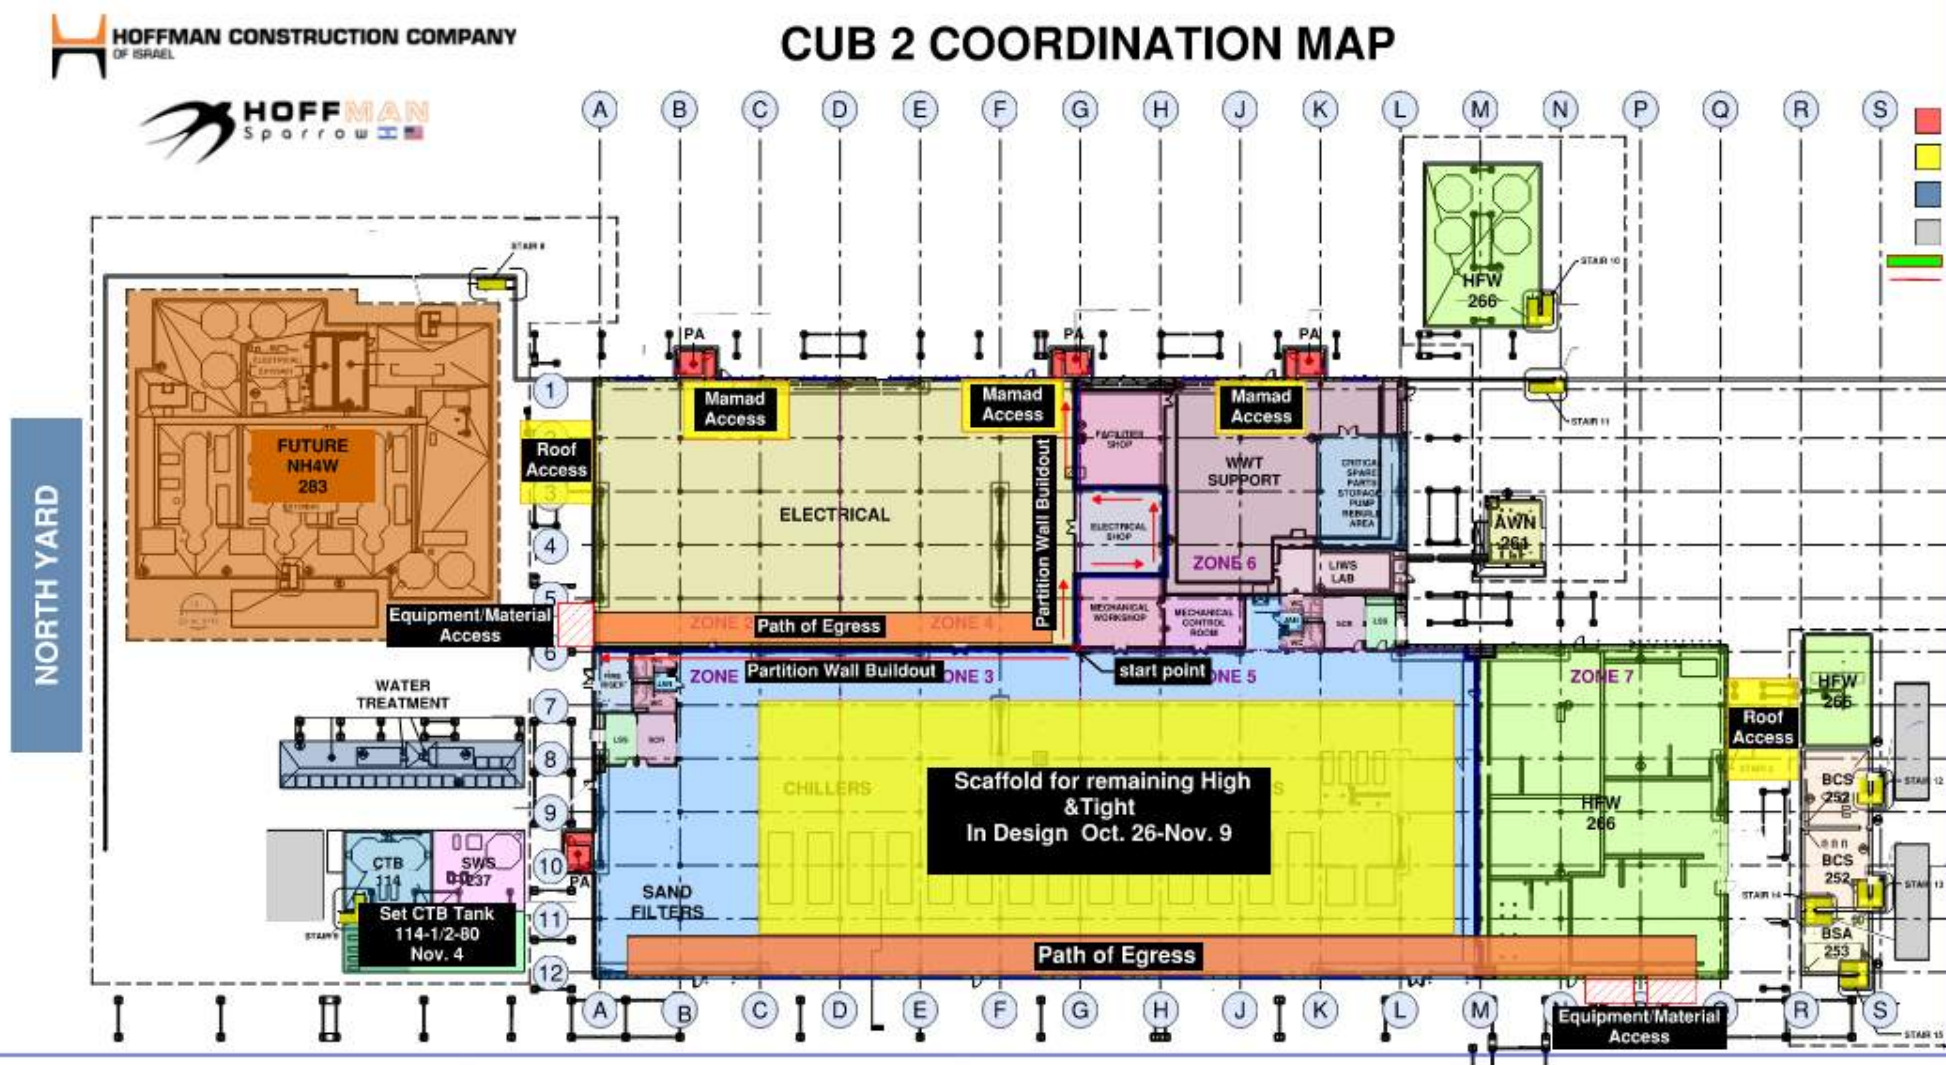


CUB 2 – EXTERIOR/ROOF

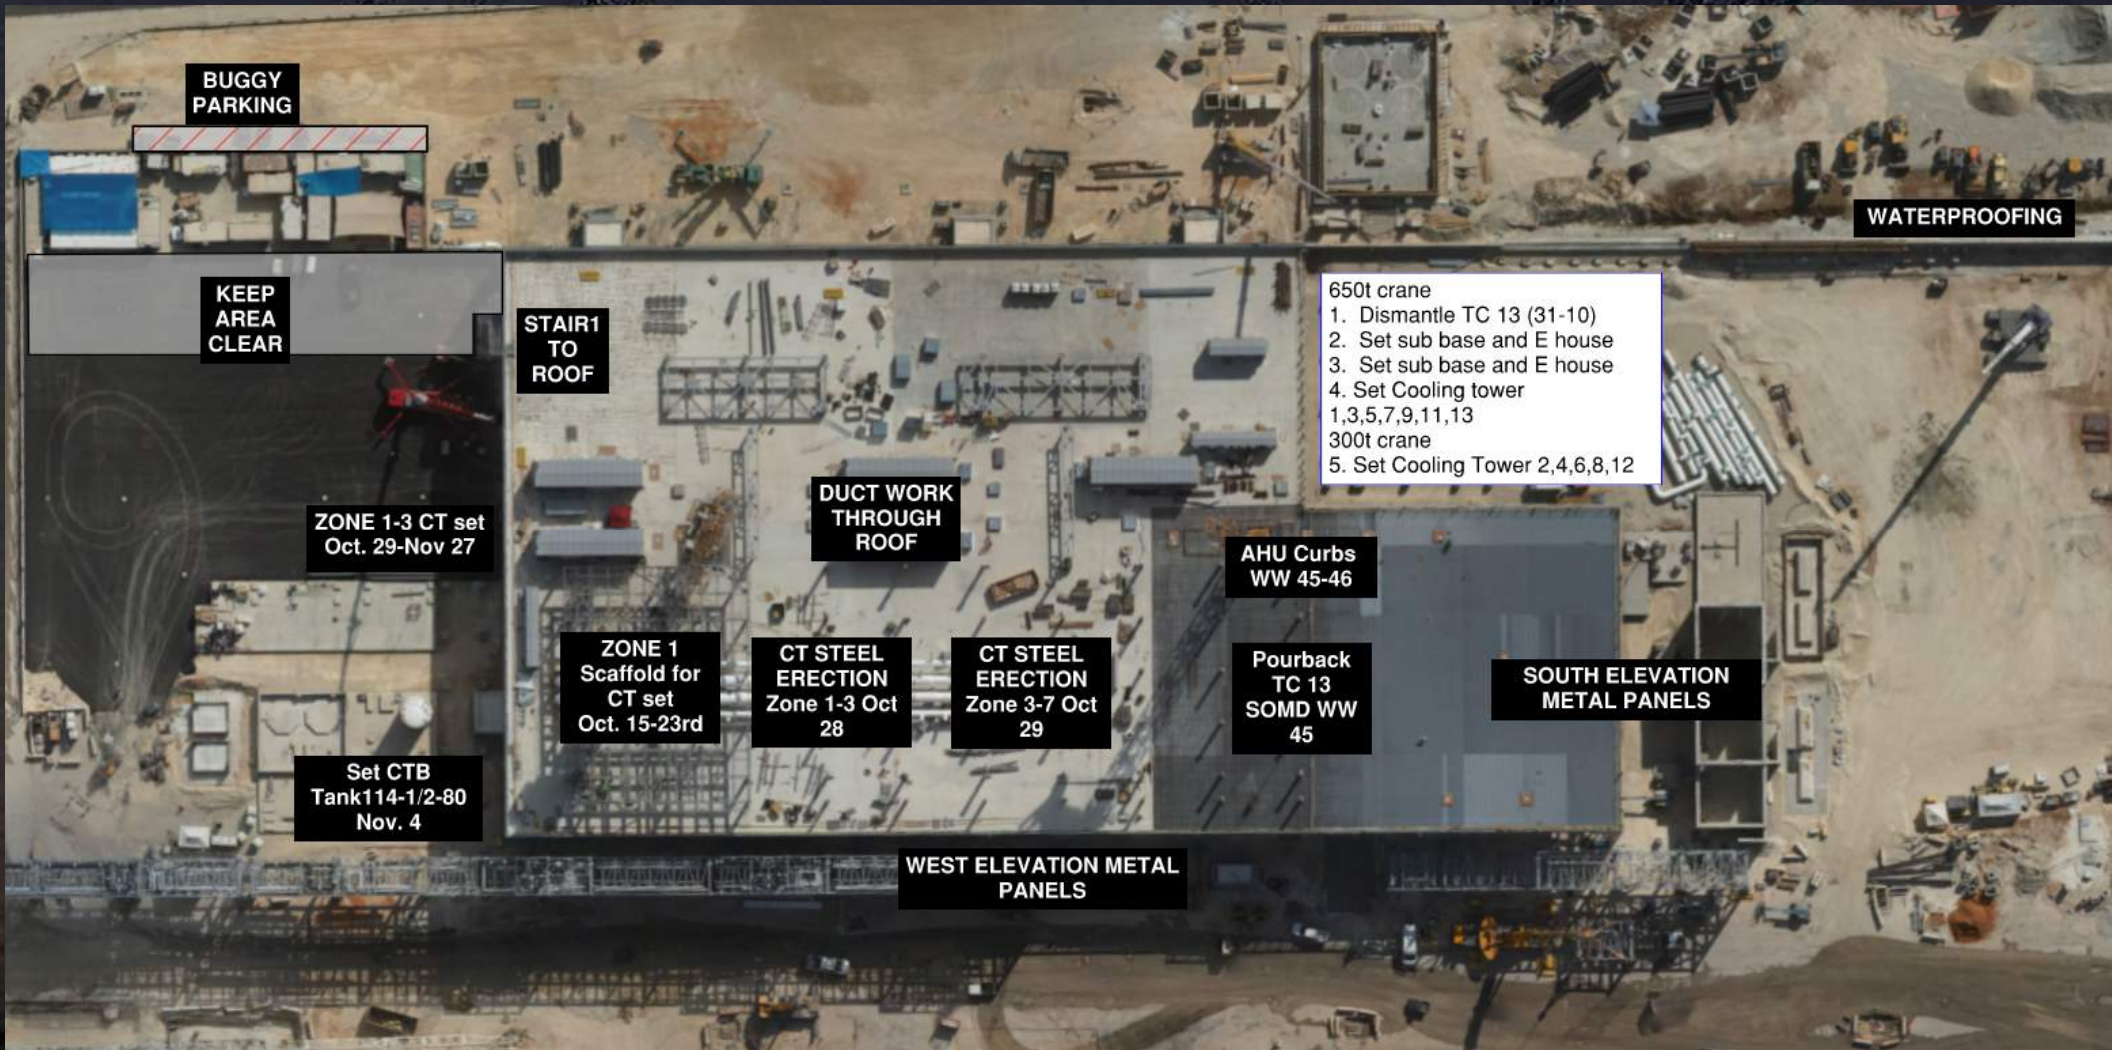



CUB 2 – Crane Logistics

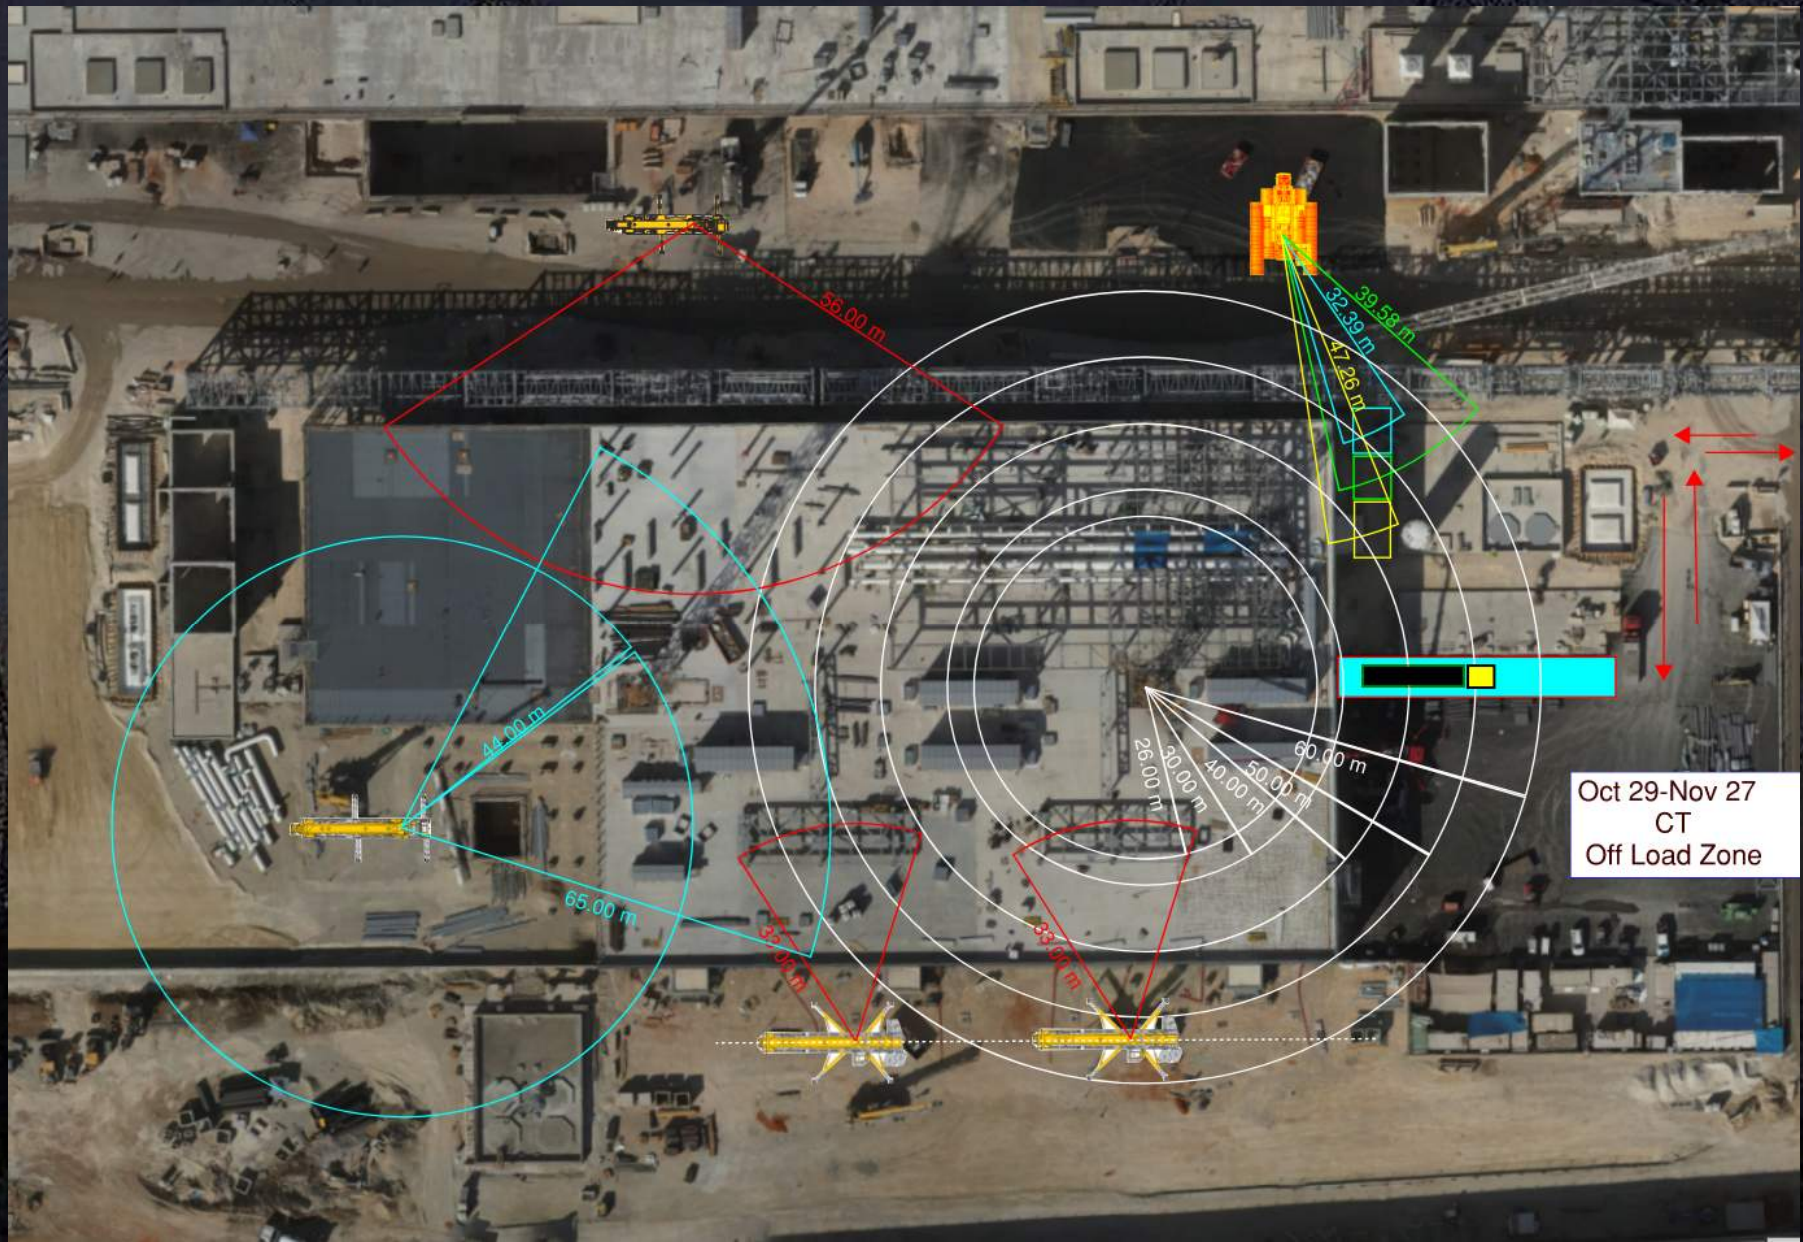



HOFFMAN CONSTRUCTION COMPANY

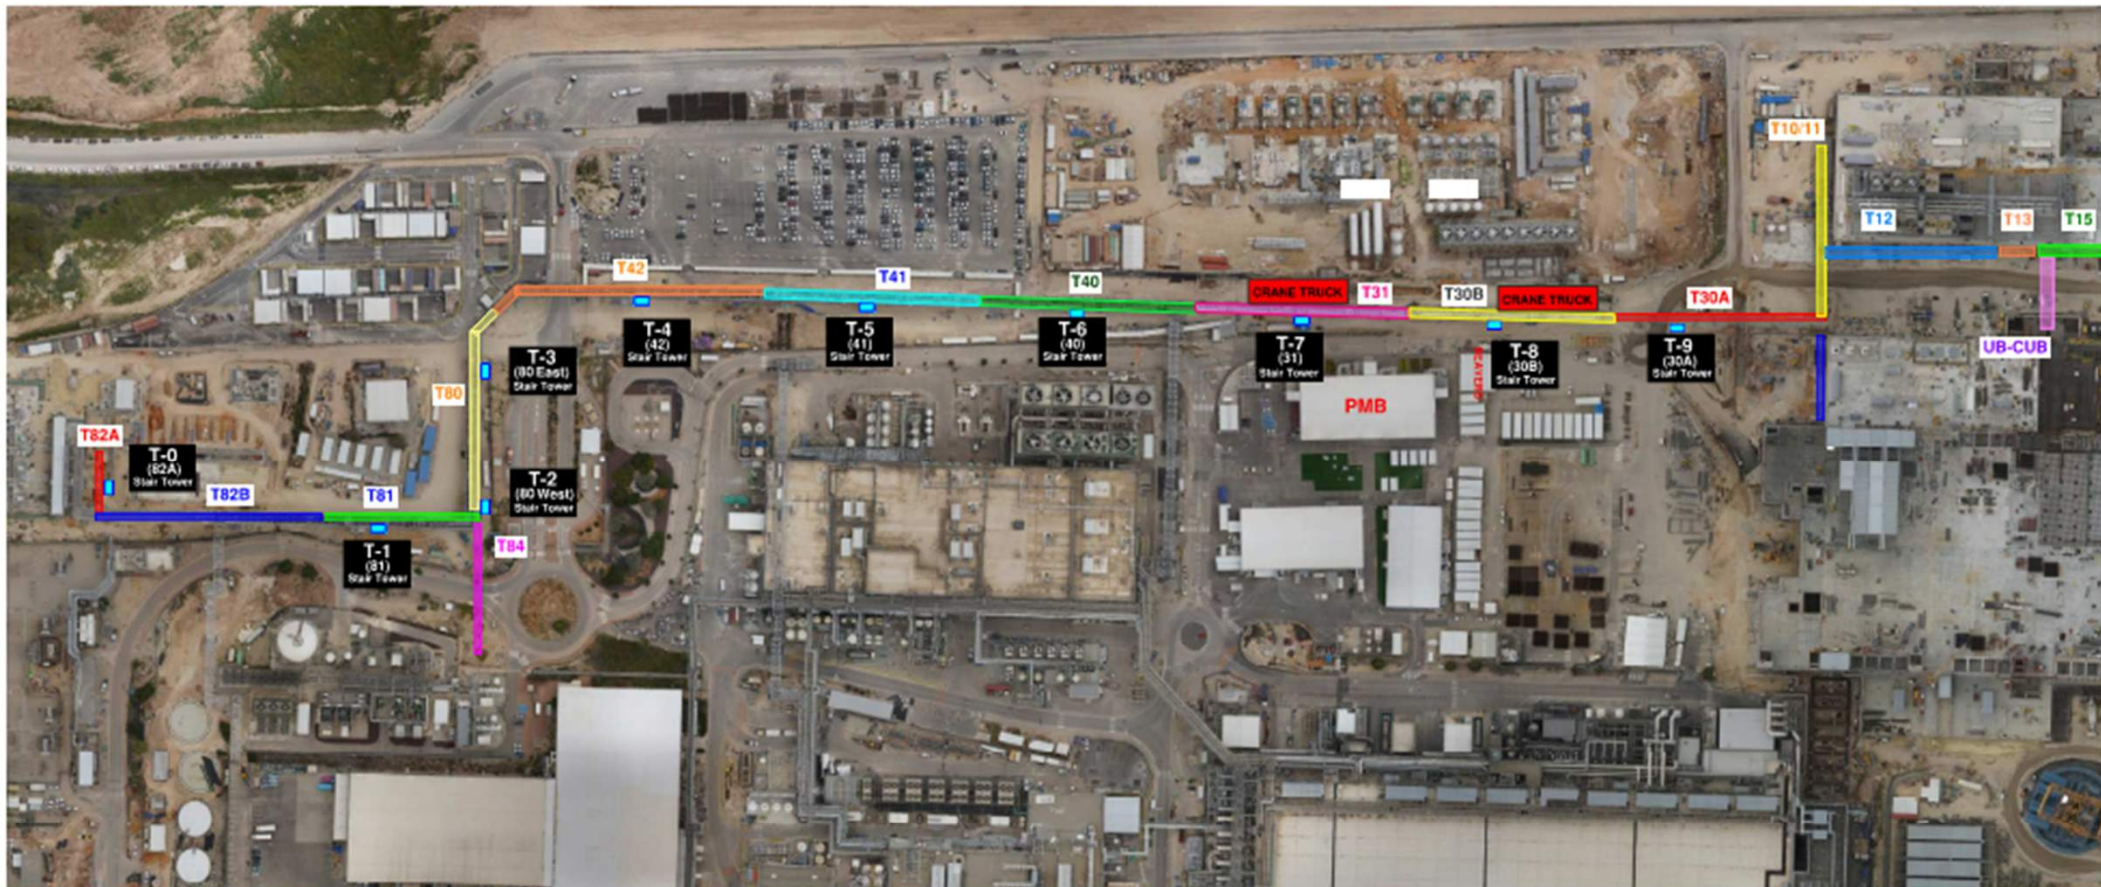



HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

T18

CUB 2 - NOV 3th - NOV 11th

nov 7th


nov 6th

nov 5th


nov 3th

nov 10th

nov 11th



5m



HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  






HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

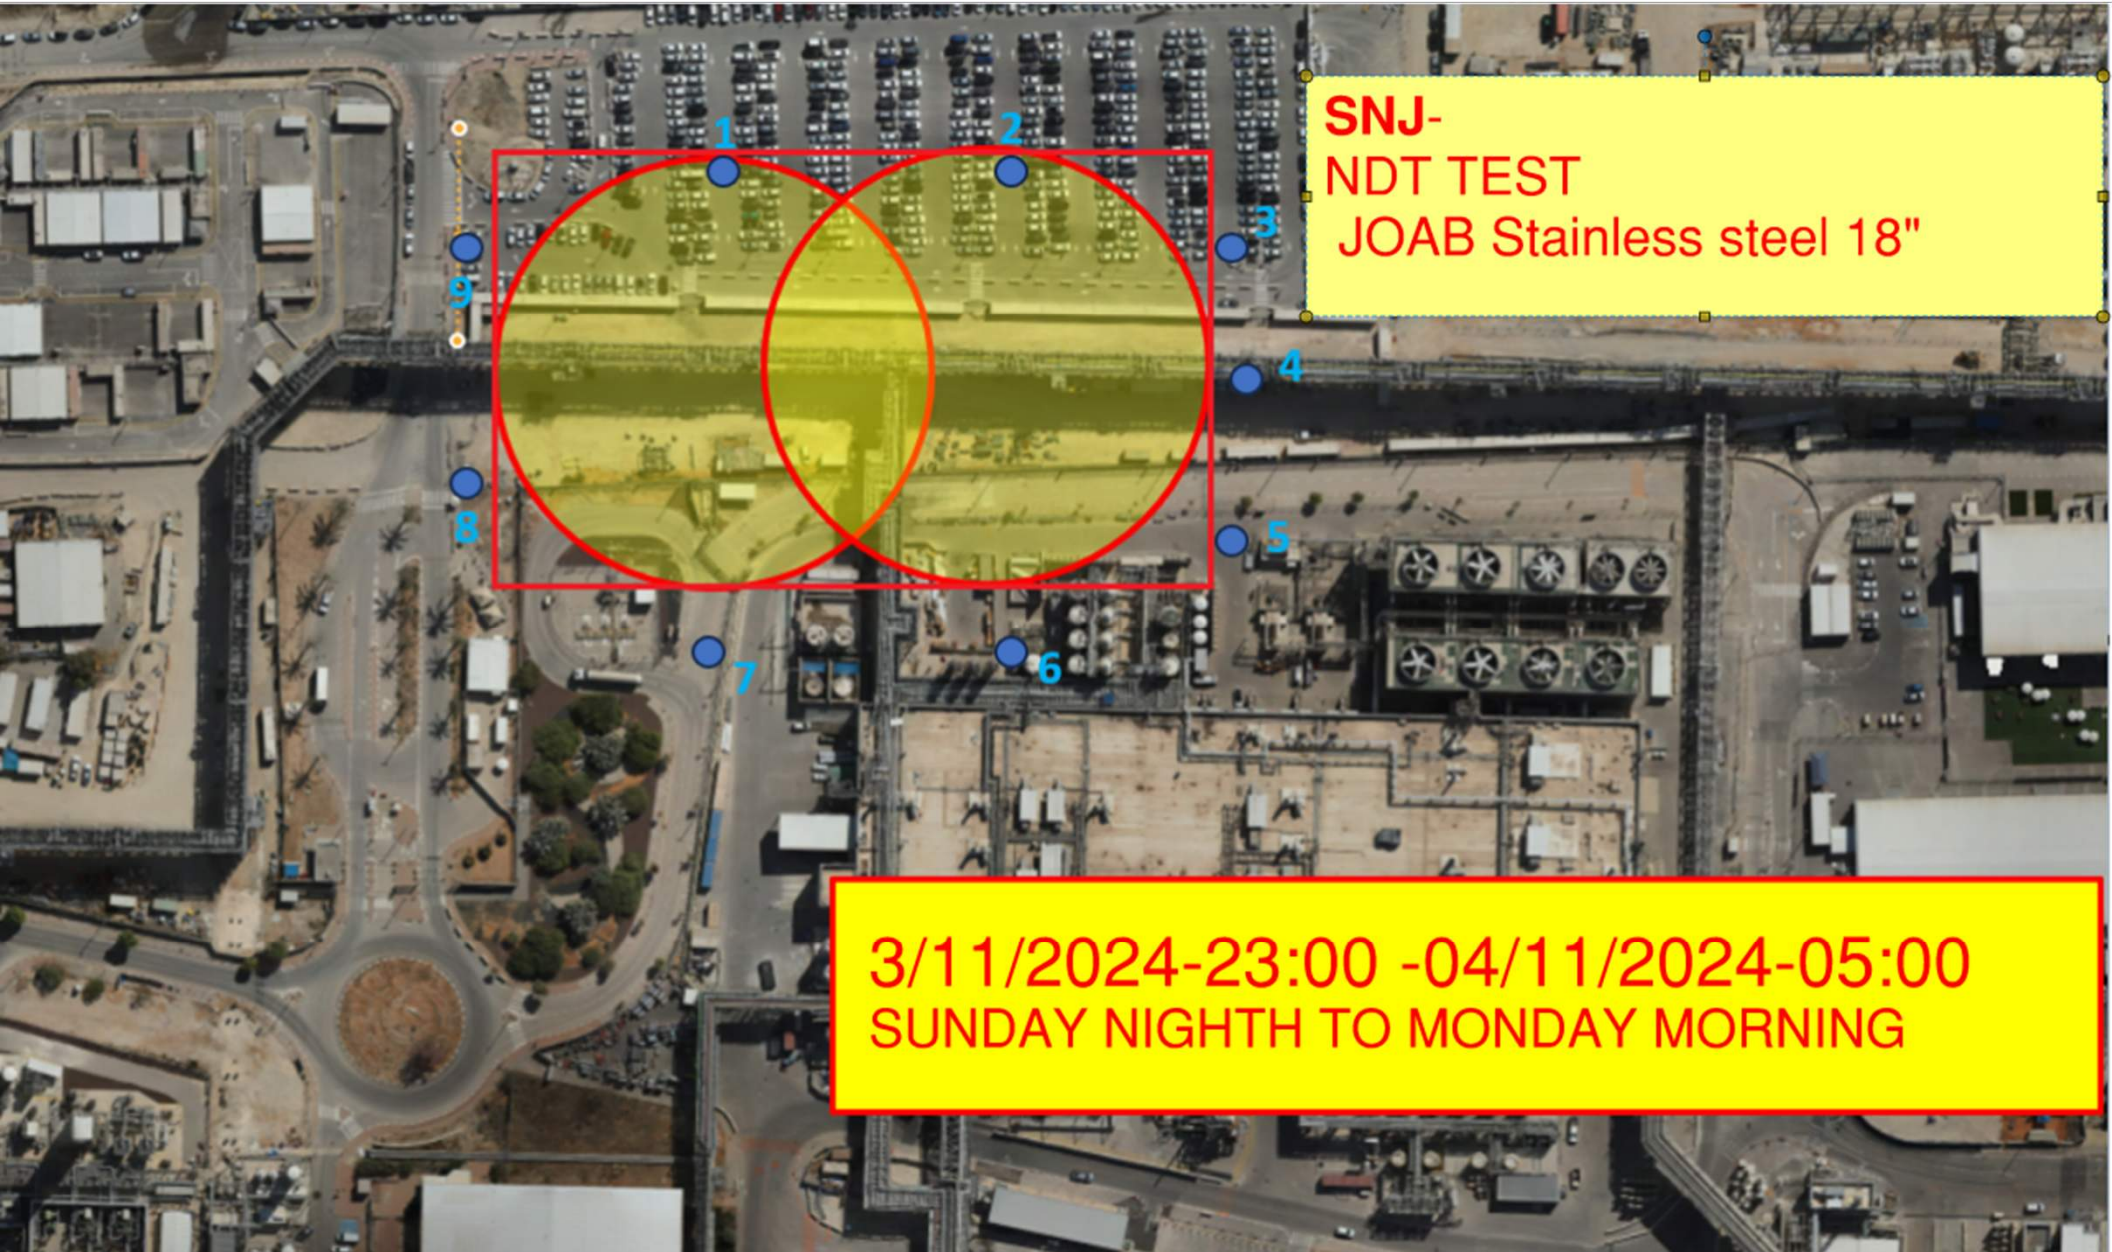

SNJ-
NDT TEST
JOAB Stainless steel 18"

3/11/2024-23:00 -04/11/2024-05:00
SUNDAY NIGHTH TO MONDAY MORNING



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North






Daily Coordination Meeting

Site Logistics

South

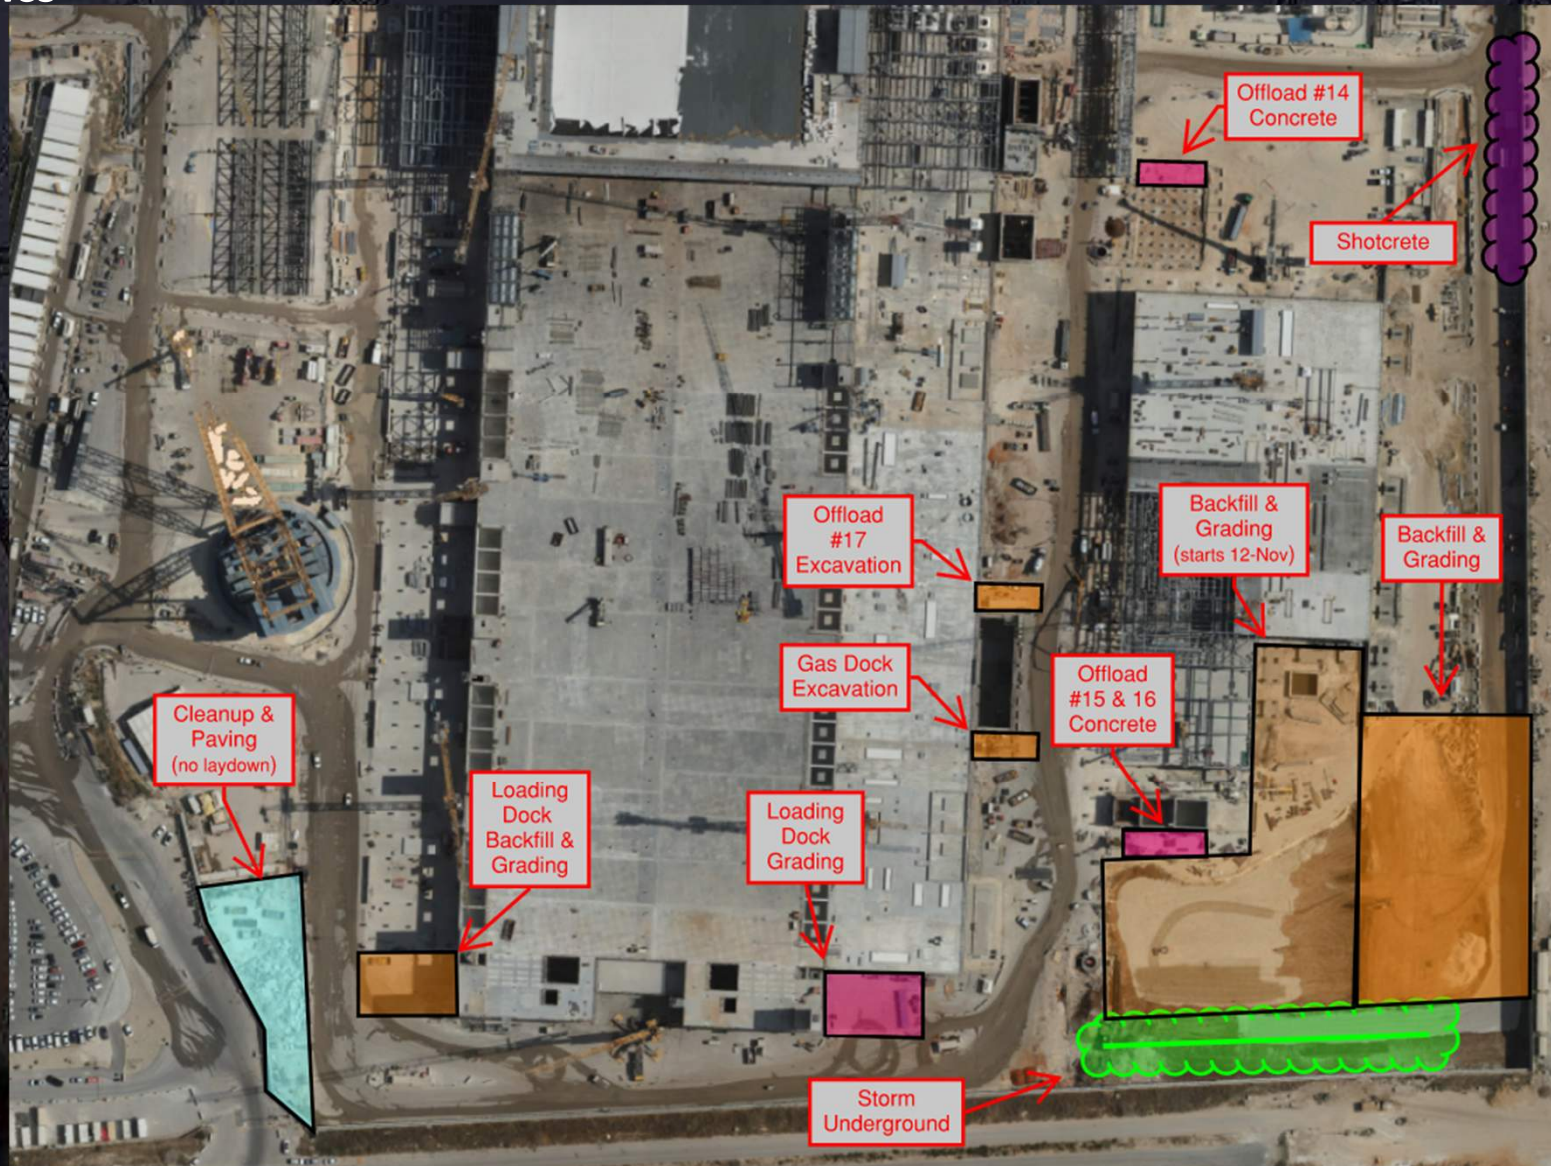







Open CORs by Subcontractor

WW 42 – 516 CORs

WW 45 – 595 CORs

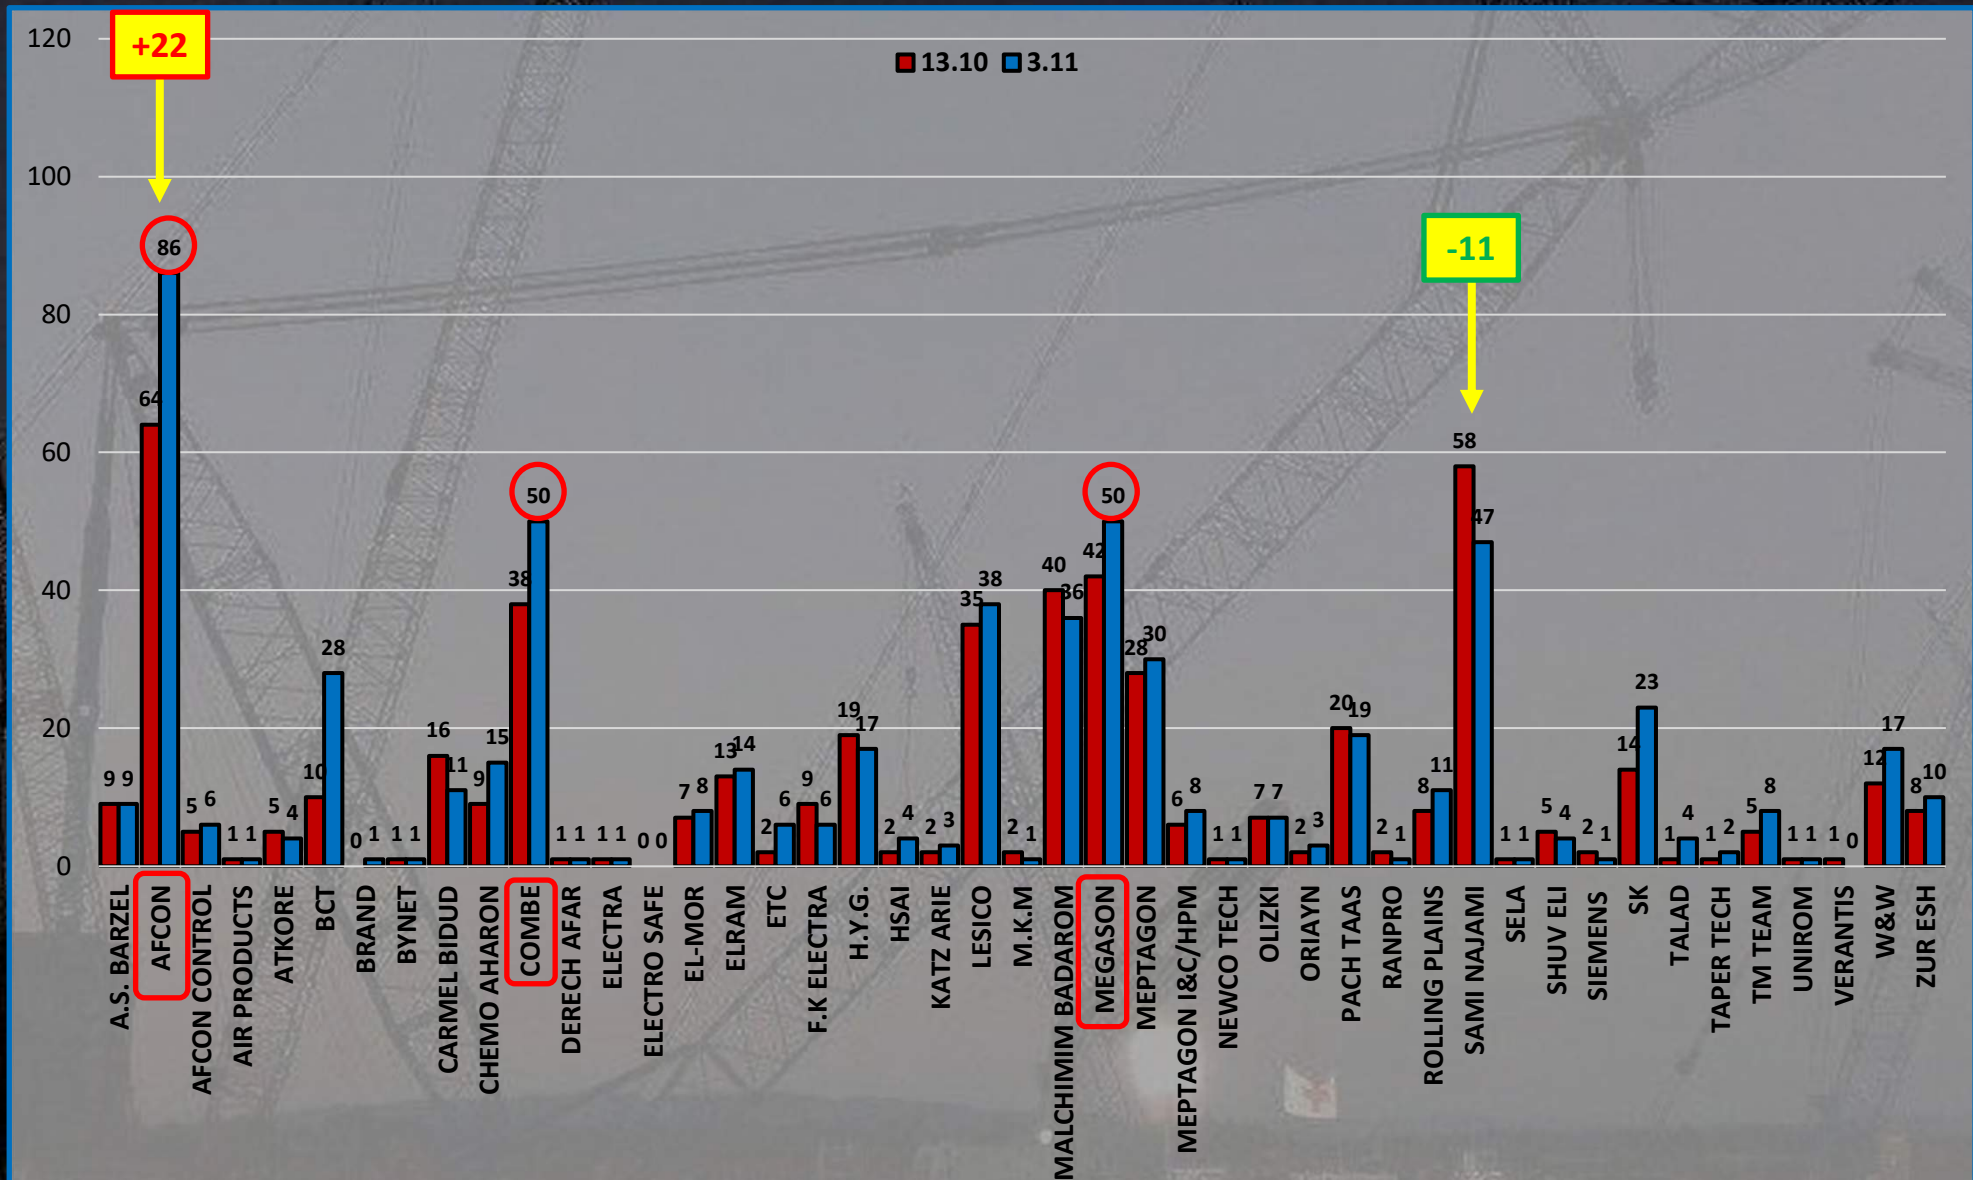




Overdue CORs by Subcontractor

WW 42 – 173 CORs

WW 45 – 178 CORs

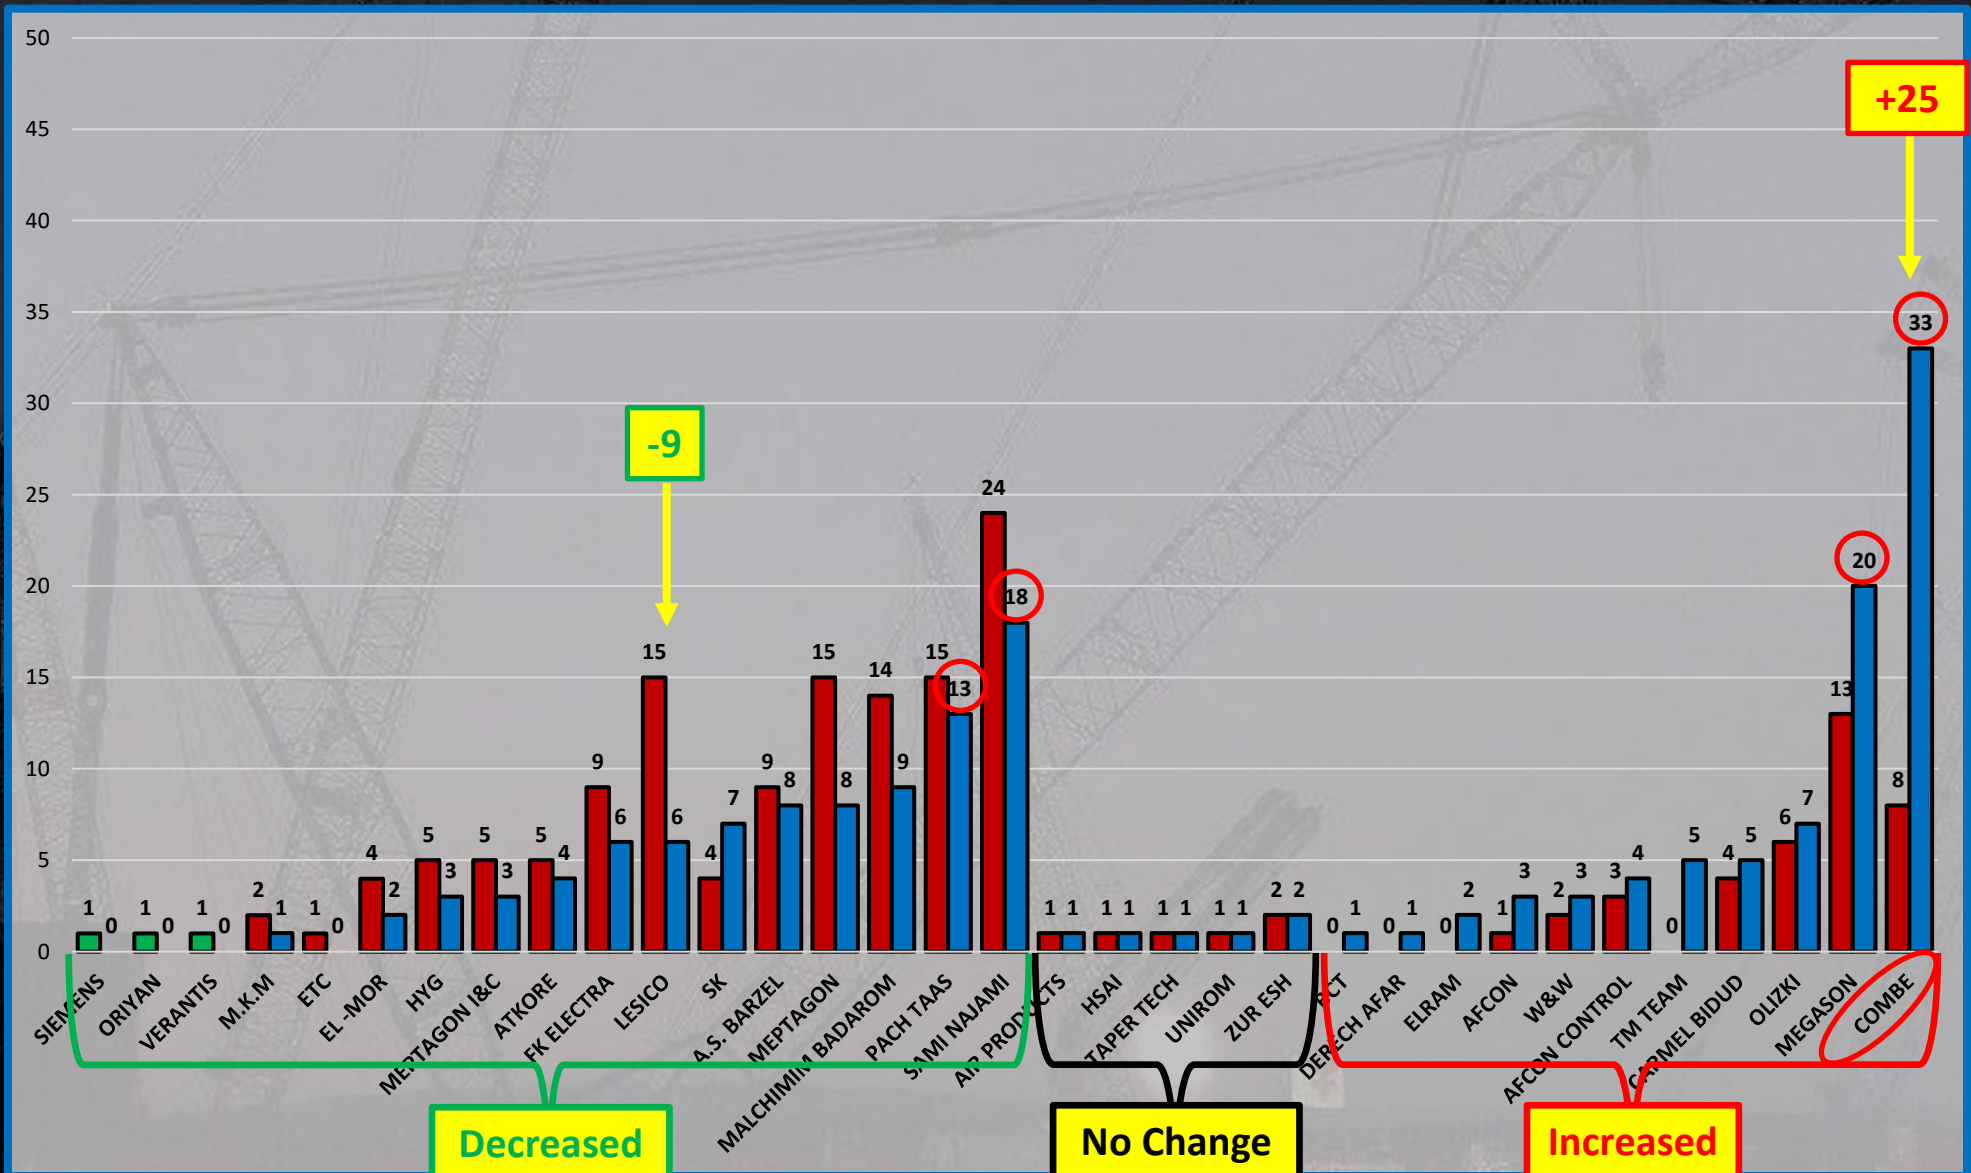

Communication

- Crews must have access to the plans you have made for them.
- We are seeing fewer and fewer crews having access to supplemental plans. Such as fall protection plans, lifting plans, pressure test procedures, etc.
- Plans are not just for HCC to review, but for your crews to understand and follow.
- We are continuing to not communicate messages from this meeting to our team leaders as well. Remember, this meeting is to ensure that people are aware of access changes, work activities, and safety related information.
- You should be taking notes and discussing the information shared with you in this meeting with your team leaders.

HCC/EHS Weekend Work- 01.11.2024

White Board Meeting in Beavers at 06:30

Superintendents

Marteen Jimenez 052-2399853

David Kanzevich 052-2045446

Pini Kahlon 052-7343004

CSA CM

Brandon Britton 052-6042828

Nitzan Mulay 052-3257365

MEP

Troy Odella 052-3217034

Asher Amar 052-8801316

Leslie Kelly 052-6391546

OSM

Jenia Shtein 052-2720940

CX/QA

David Young 052-2241683

Cranes

Craig Mowry 052-3002769

Safety

- Safety Foreman- Nadav Alfasi- 052-5115772 Nadav-Alfasi@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Ron Miara- 050-4555854 Ron-Miara@Hoffmancorp.com

Subcontractor Weekend Work- 01.11.2024

FAB

Utility Level / Roof / Stair Shaft

SK

Foreman – Robi – 054-3065139

HSAI – Roof / Link Ramp

Foreman – Dave – 052-

4121028

Safety – Sam – 052-5259268

Dvir – All over

Foreman – Dov – 054-

6305664

Pach Taas -

Chemo – Duct

Foreman – 054-7175157

W&W / Sami Najami – Elevator

Shafts / Tool Dock / Girts

Foreman – Teddy – 052-

2392473

Sami Najami – Cleaning in Bulk Gas

Yard

Foreman – Victor – 054-

9220163

Elram – LSSS Drywall / Stairs Drywall

Foreman - Roni – 050-

7196939

Afcon Electrical – All over

Foreman - Slava – 052-

5508724

Subfab

BCT

Mod 1, 2 Workers.

Afcon E

Mars 1W + LSS rooms

Team Lead : Avi Eli 0526008487

WW Steel

Elevators 1-4

Teddy 0522392473

Clean Room

Subcontractor Weekend Work- 01.11.2024

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2, and EPA Platform 1&2P

Foreman – Vadim – 053-5552472

Safety – Offek – 050-2161429

Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-2P Roof & Lift 2

Foreman – Charles – 055-2740190

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-4P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

W&W – SEQ 135, 137

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Elram – 5P Corridor, UPW Ceiling

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Combe UPW – UPW Room Piping and Yard

Foreman – Boris – 054-8346412

Safety – Michael – 052-5506596

HSAI – BPS Blast Walls

Foreman – Dave – 052-4121028

Safety – Sam – 052-5259268

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcela – 054-5210133

Safety – Marzuke – 054-447-7112

WJG

W&W – Steel Erection 5J lift 2 Erection

Foreman: Chris Isaac 052 588 3215

Safety: Moshe 054 801 2959

Afcon – 2J Lift 3 Cable Pulling

Foreman: Sarat 055 274 0190

Safety: Pradeep 055 274 2935

SK: 2J lift 2 piping

Chemo: 5J Lift 2 Piping

Foreman: Sergey 054 465 9688

Safety: Lilach 054 788 6704

Siding

Subcontractor Weekend Work- 01.11.2024

CUB

Sami Najami Cub 1+ Cub 2:

Husein - 0526917461

Alon - 0509895008

S.K.E Cub 1 + Cub 2:

Renato- 0548991623

Mario - 0548991051

Majd - 0546192581

Brand CUB 2:

Salame- 0528846057

David - 0542033459

Chemo Aharon:

Dudu - 0509808846

Leonid - 0548883878

HSAl:

Sergey - 0552728807

Meptagon I&C:

Genadi- 0546785106

Sergey – 0537981592

Sela CUB 1:

Yuval - 0502649246

Shmuel- 0506306031

Trestle

GIS/NEY

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Olizki – Sweepers and water trucks

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

Sami Najami – Retaining wall waterproofing @ CUB2

Supervision = Jalal: 054-2823030

EHS = Raja: 052-3965284

Daily Coordination Meeting



14:00 Sign In
