

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- Site is open tomorrow
- Site closes at 12:00 tomorrow
- Conduct proper area assessments for long weekend



RES-13 Roof
pour 10 PM

Truck off load #15
6:00 am

Truck off load #15
6:00 am

RES-13 Roof pour
10:00 pm

אינטל קרית גת

FAB-28


AB-18



HOFFMAN CONSTRUCTION COMPANY




UTILITY LEVEL MOD1

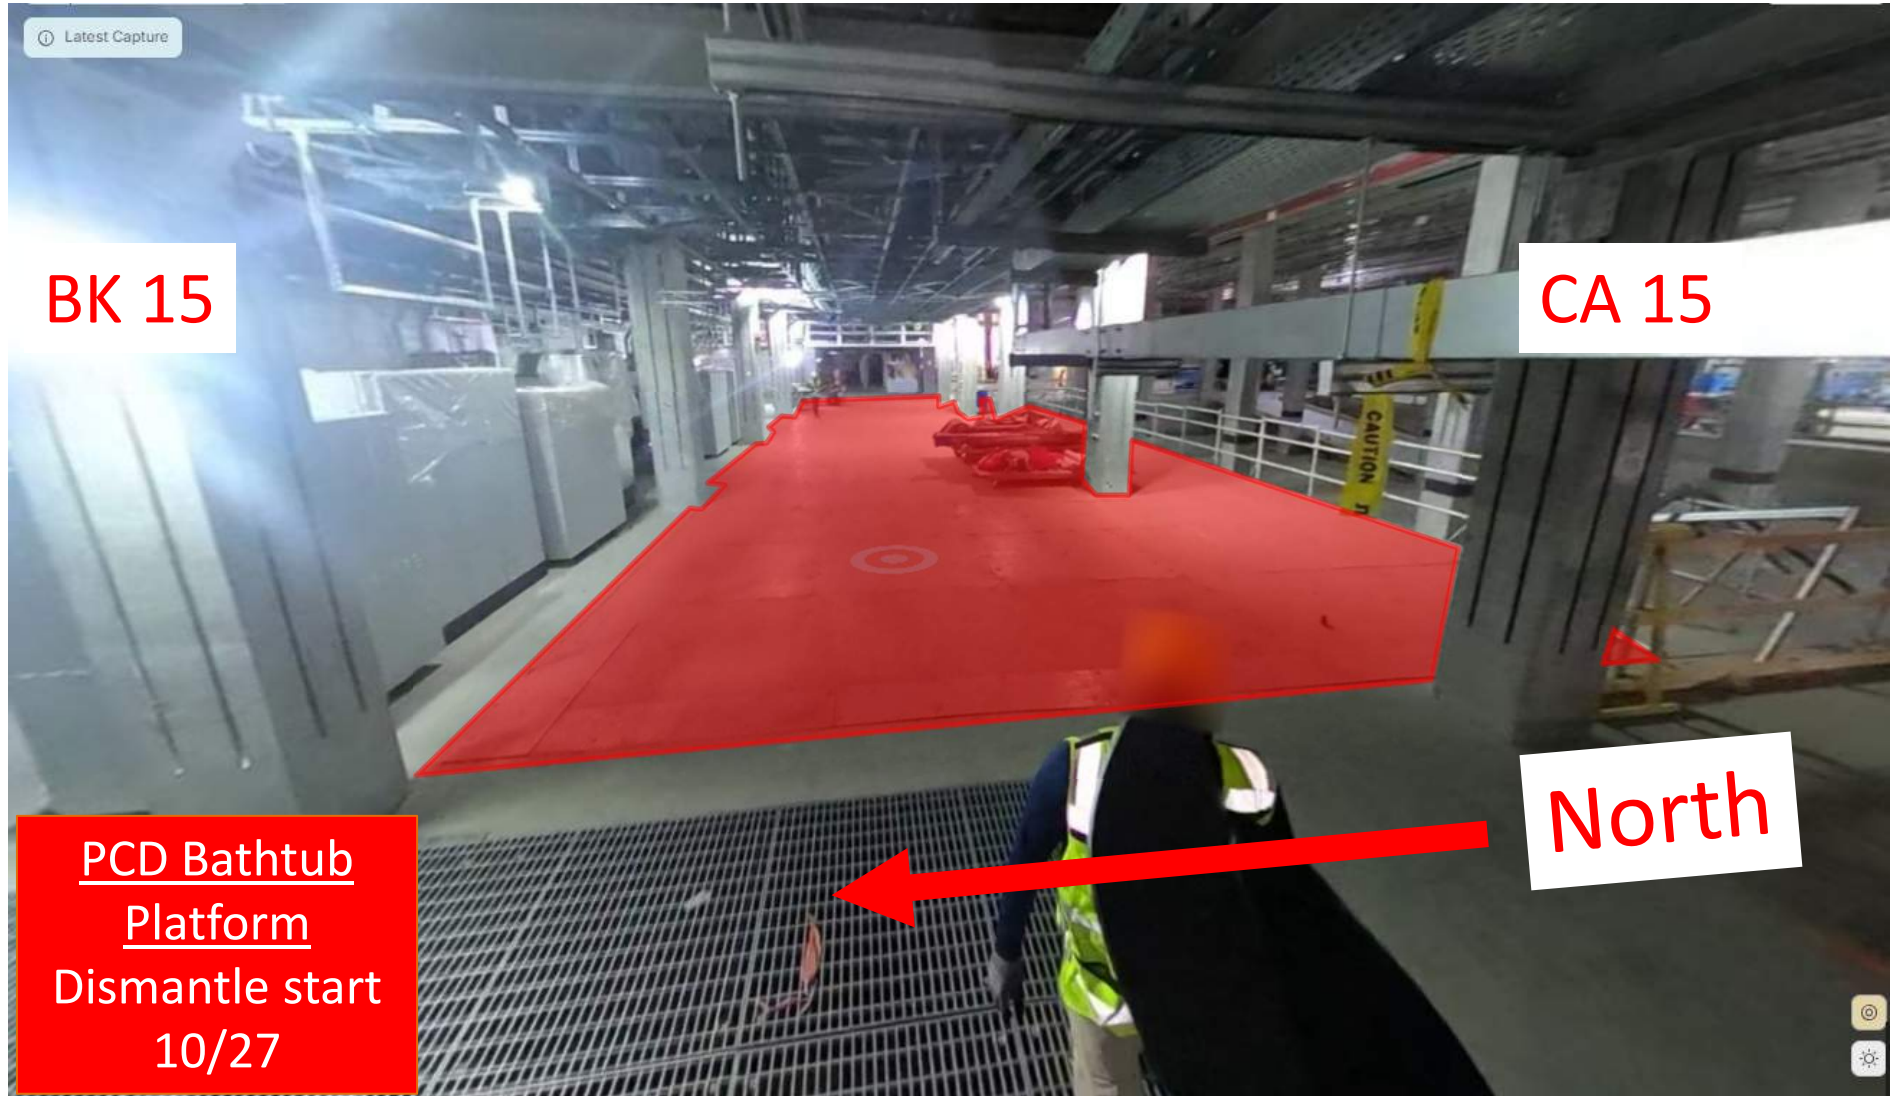



UTILITY LEVEL MOD1

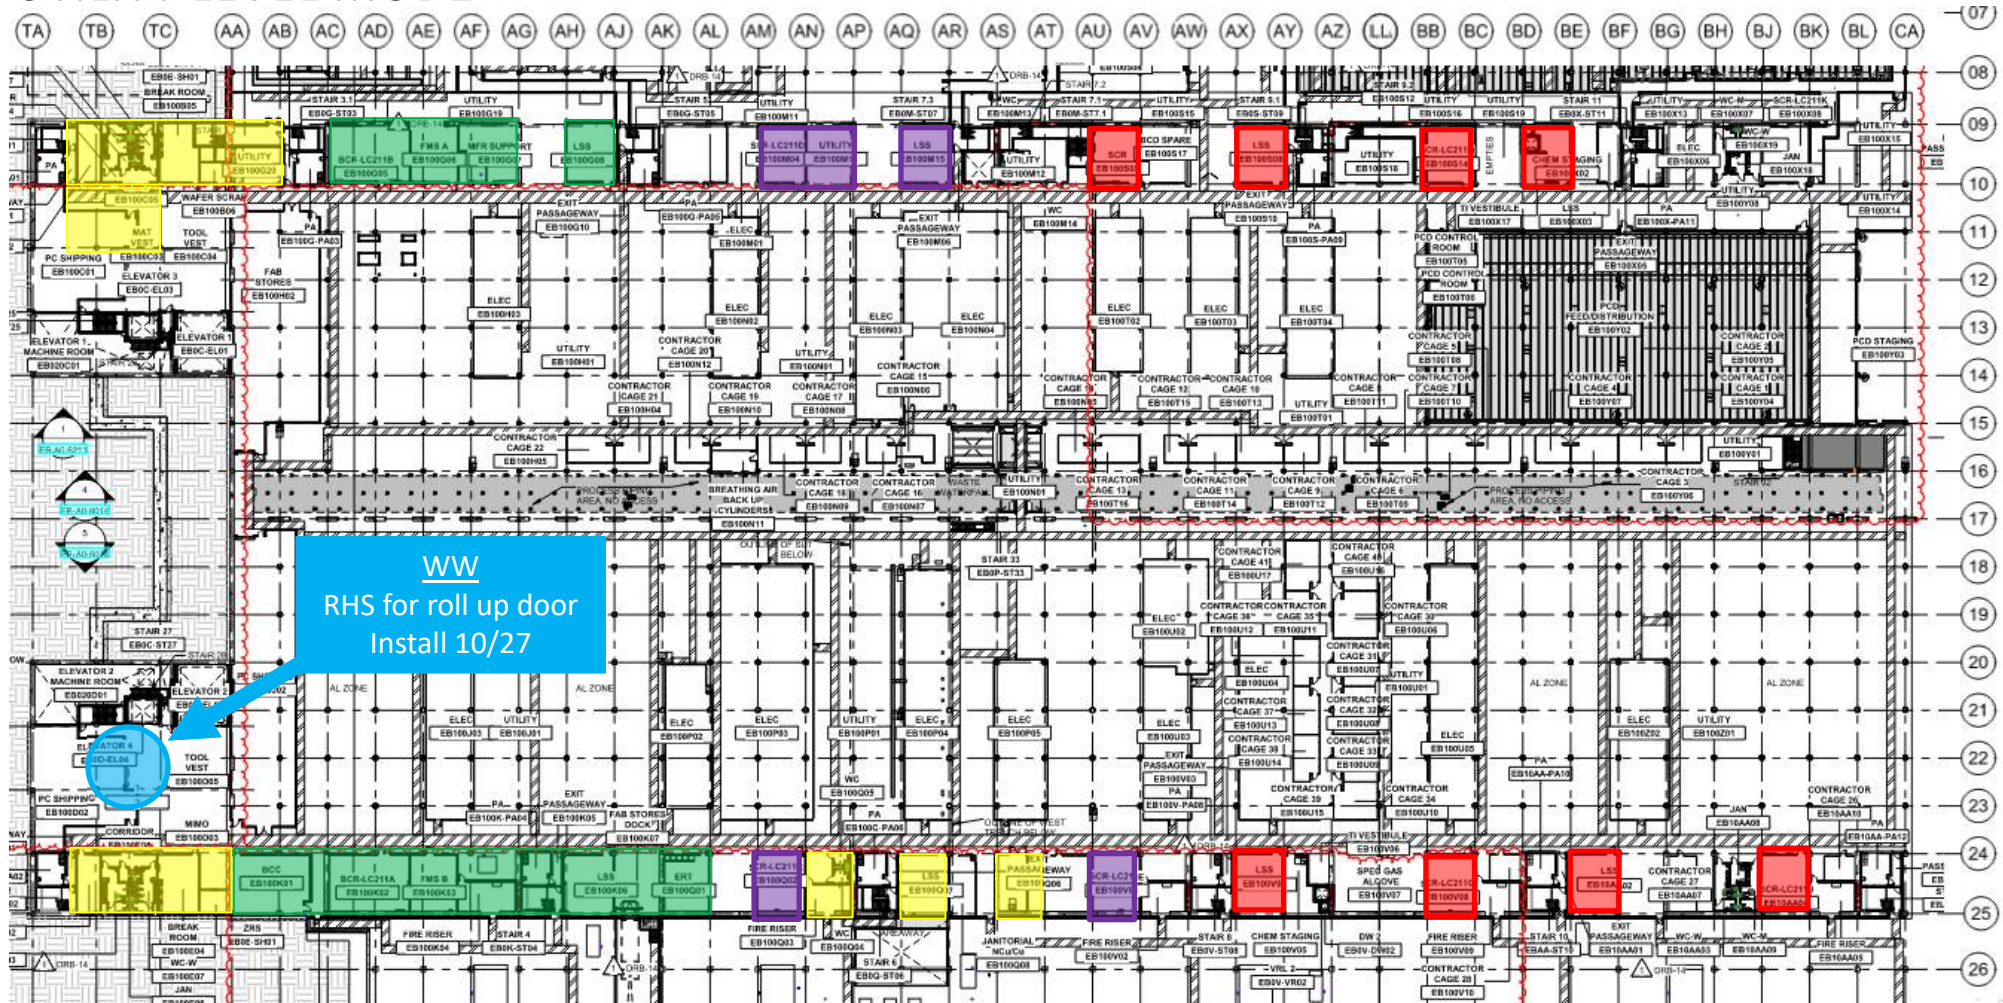

Pre-mold Rem dismantle
Should be uninstll

BELFOR
Mold remediation

ELRAM
Drywall install


MEP+Elctrical
Ready for re-install




MALHIMIM
7W
Sprinklers install
Finish 10/16




SUT 38.1 LEVEL

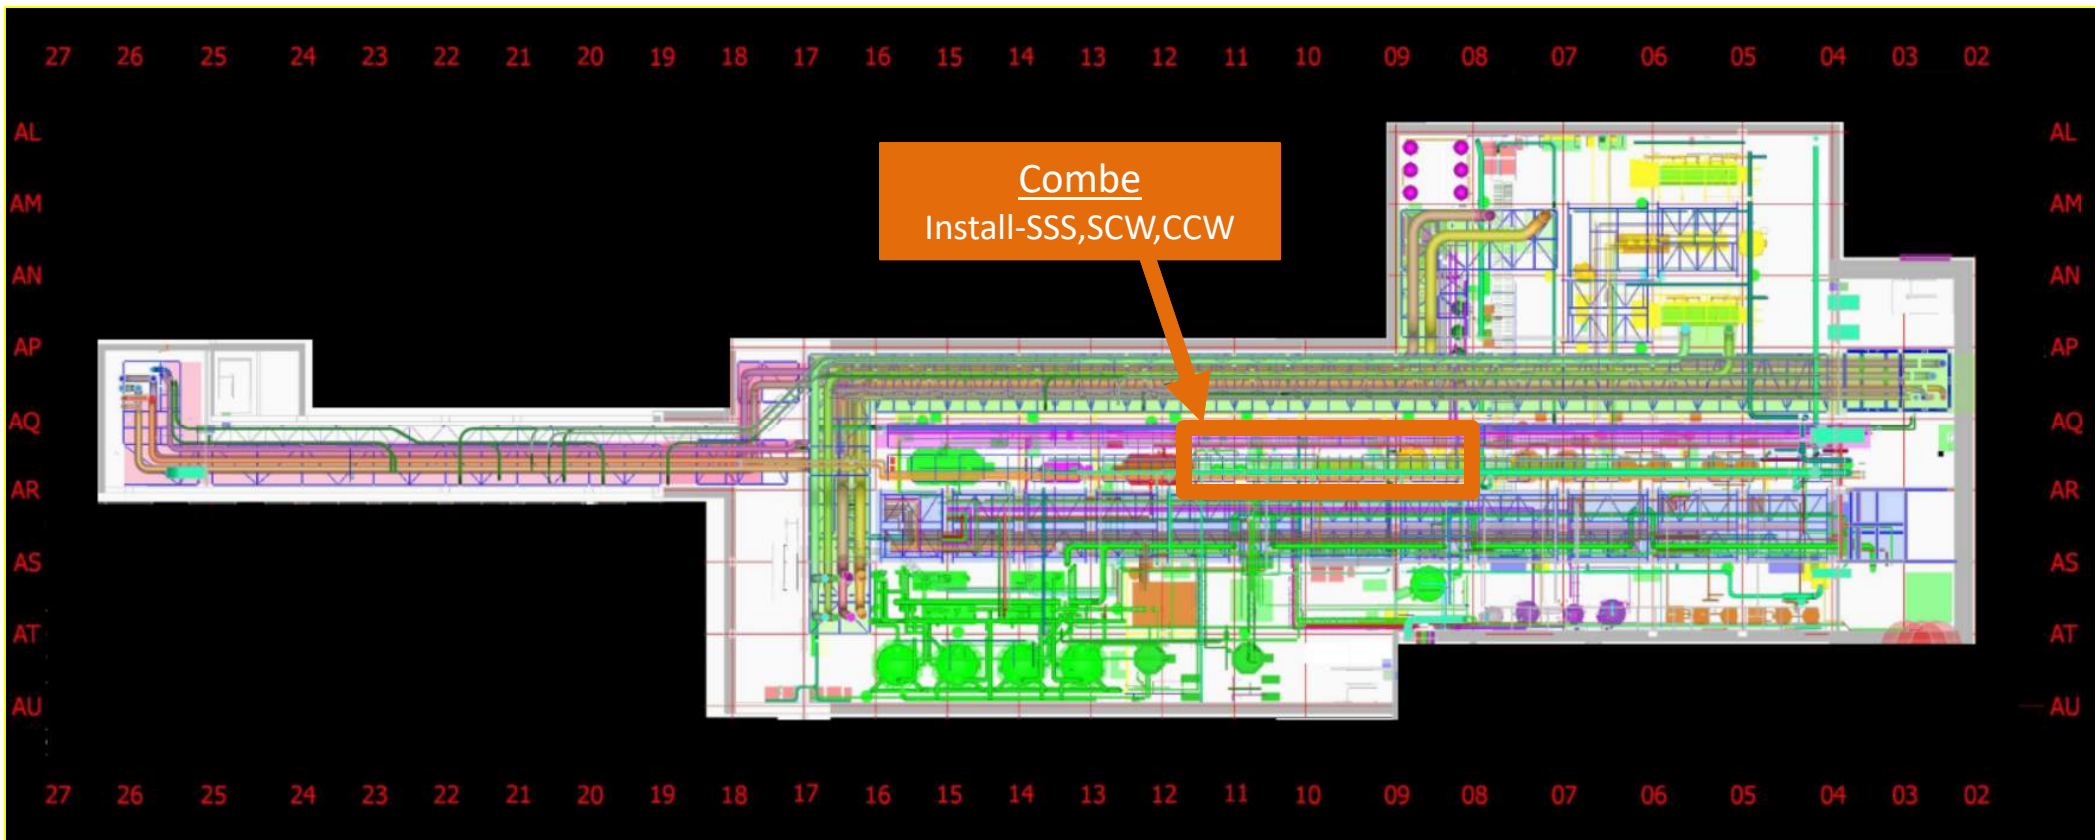


SUT 38.2 LEVEL

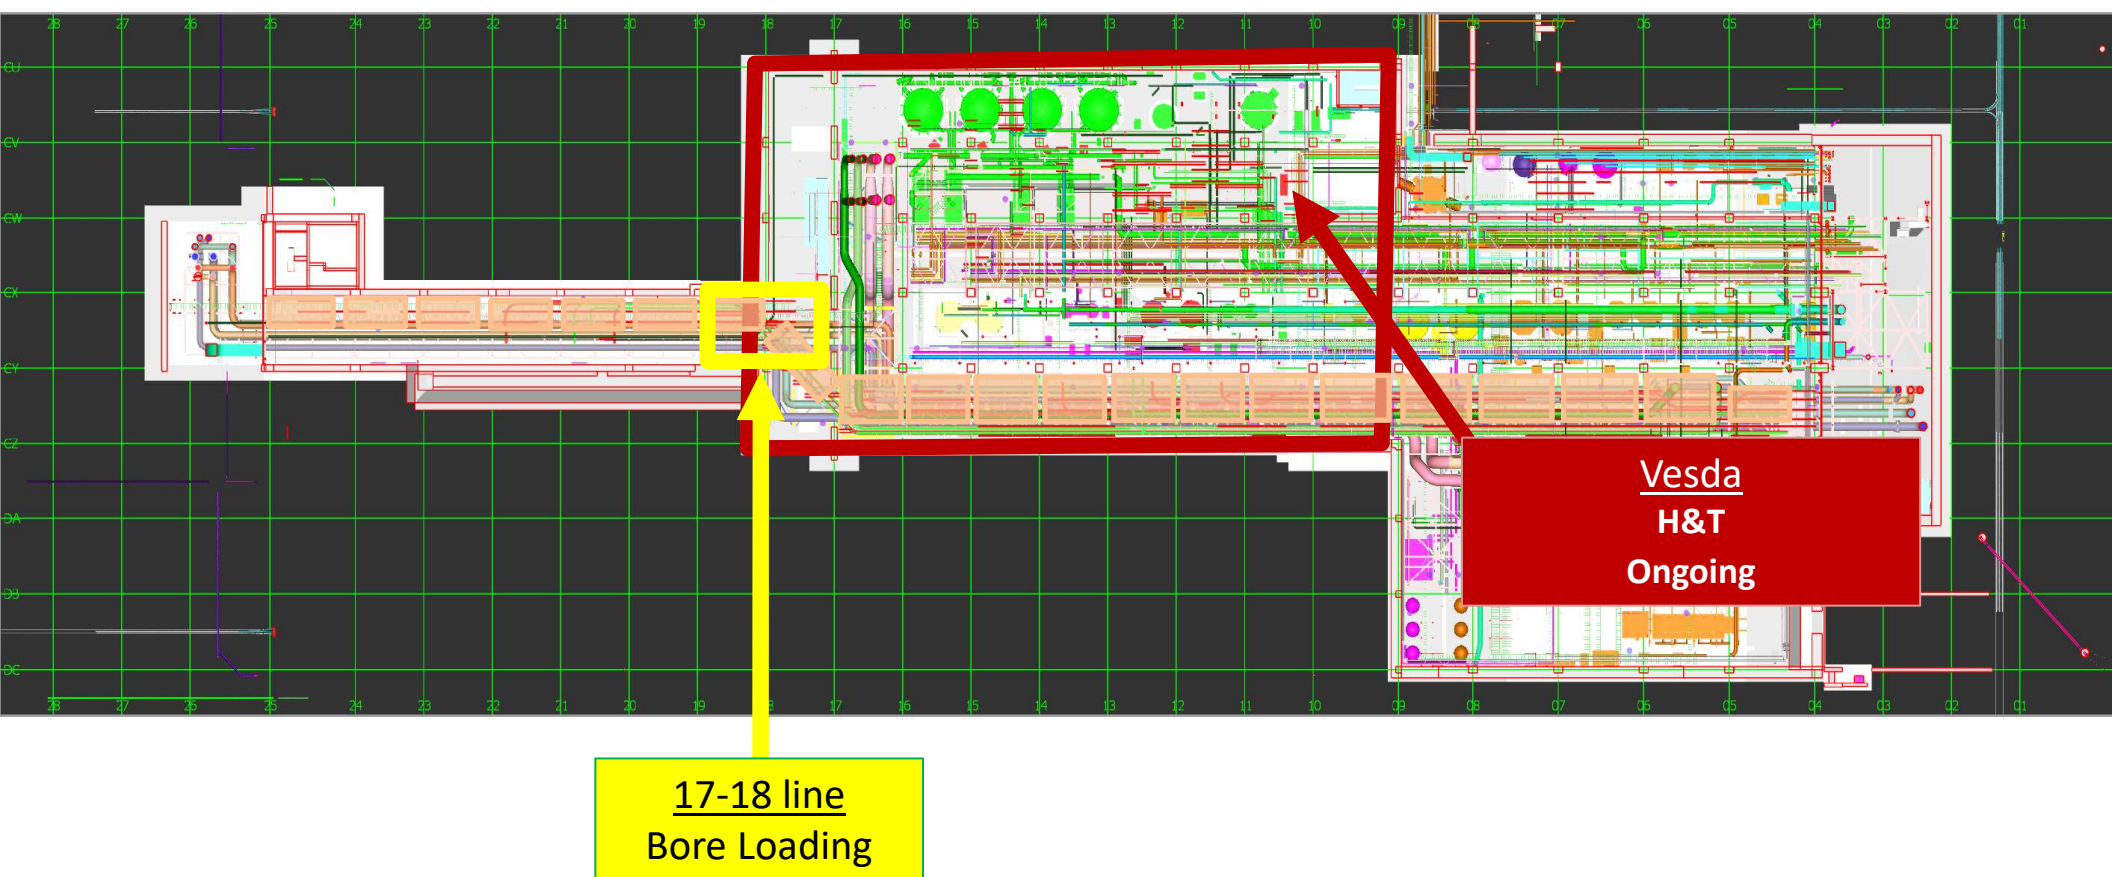

SUBFAB BUILDOUT MOD 1

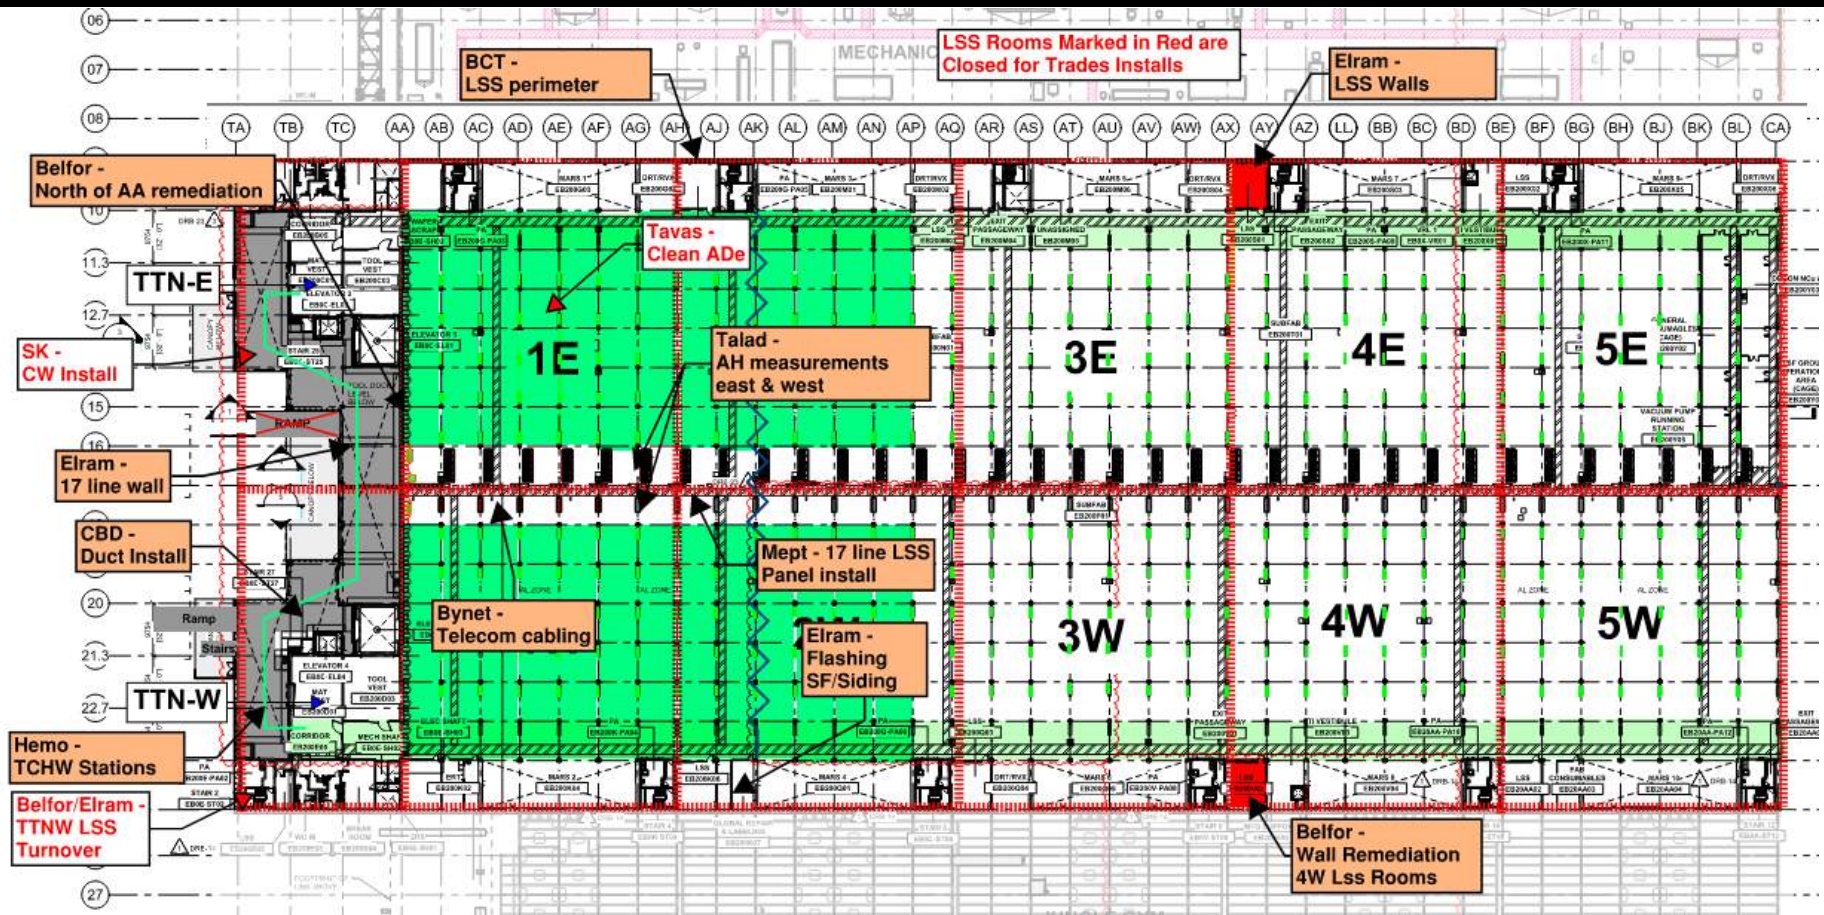

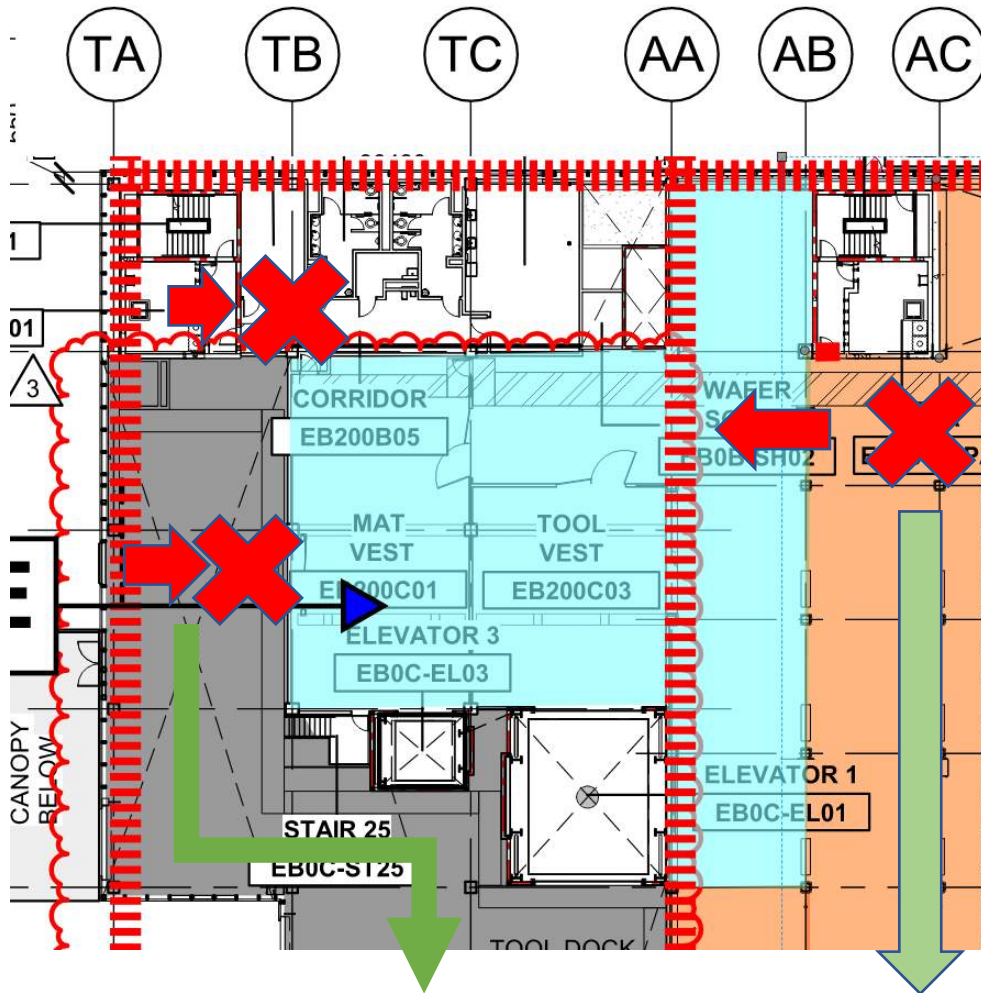


Sunday OCT 20th


CRC AAe & TTNE Upper Dock.

- Temp stairs – Access blocked.
- Stairs1 – Access blocked, SF level only.
- QC on Sunday 27/10


SUBFAB CRC TOPCOAT

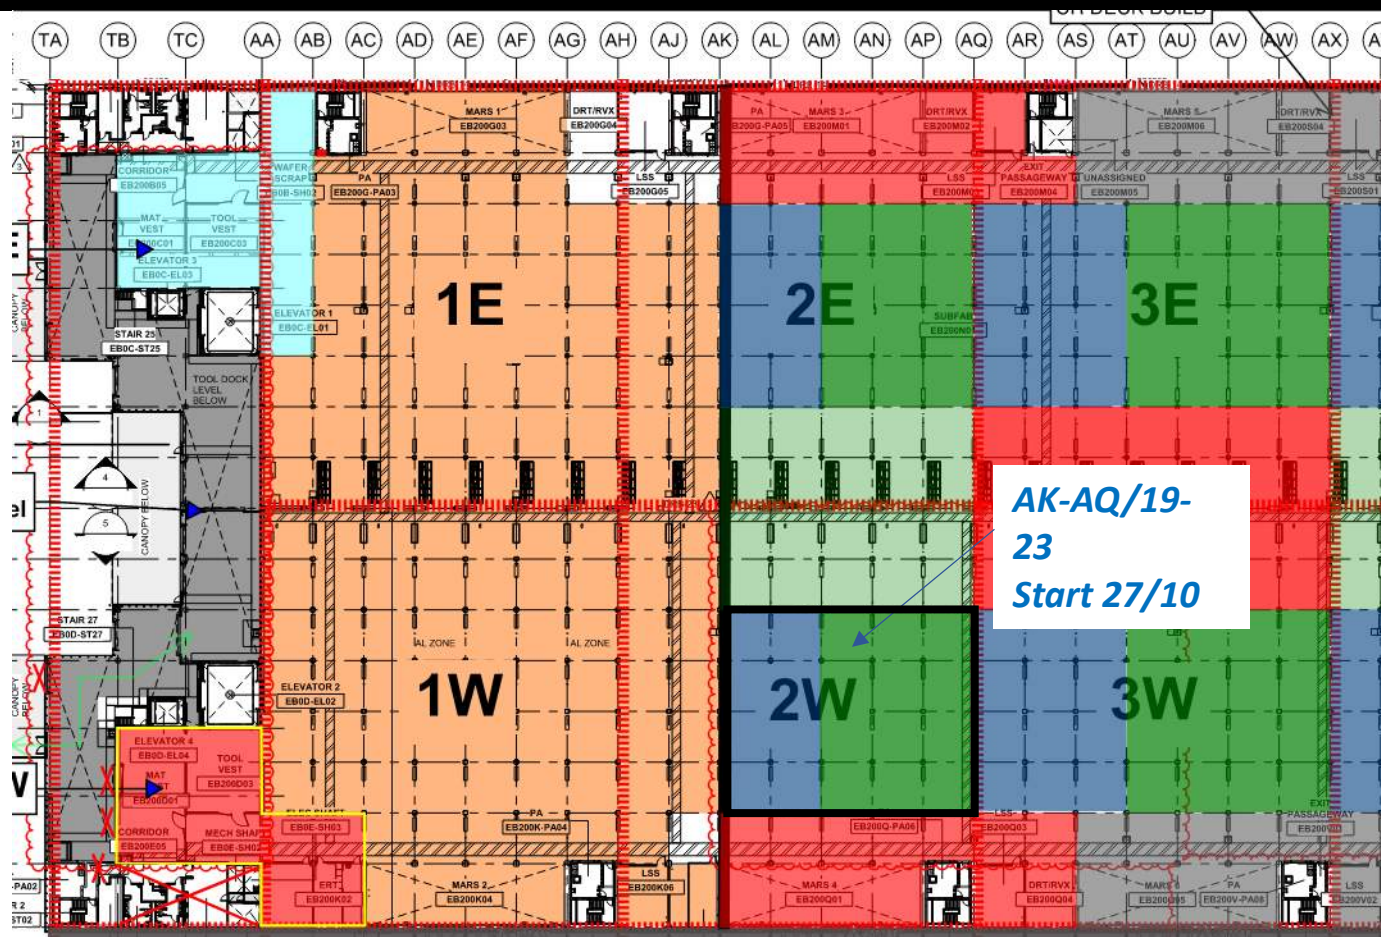


BCT Pressure Test Exclusion Zone

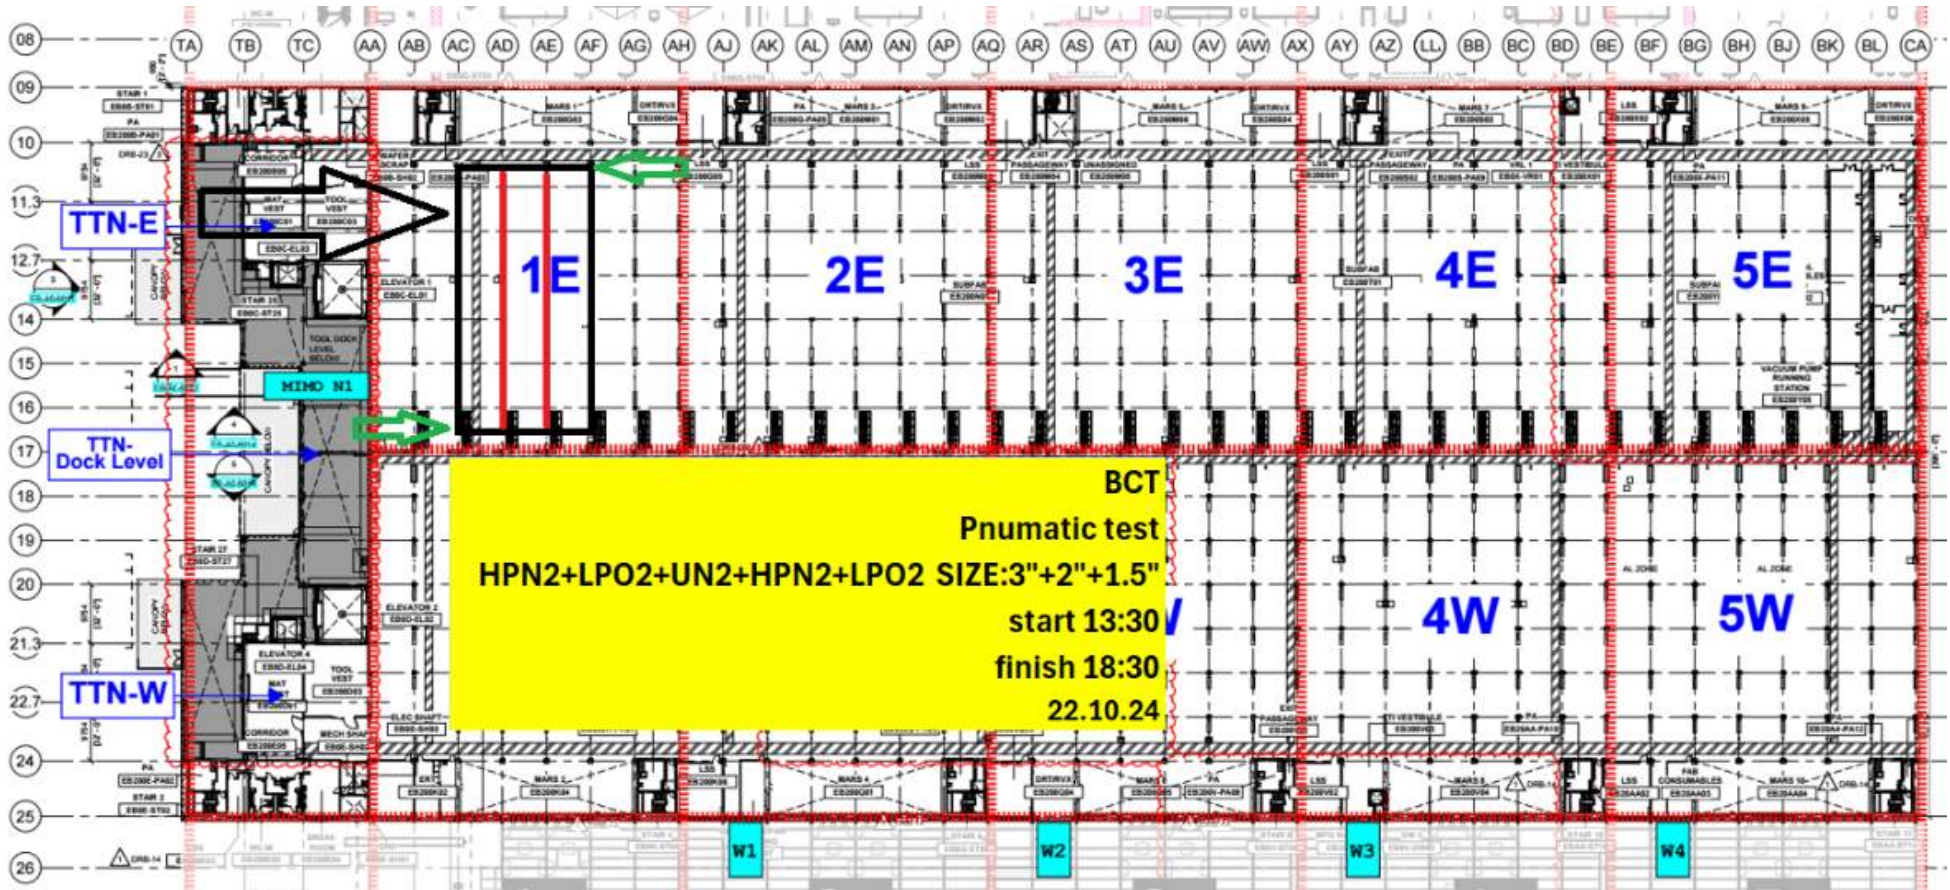

BCT Pressure Test Exclusion Zone

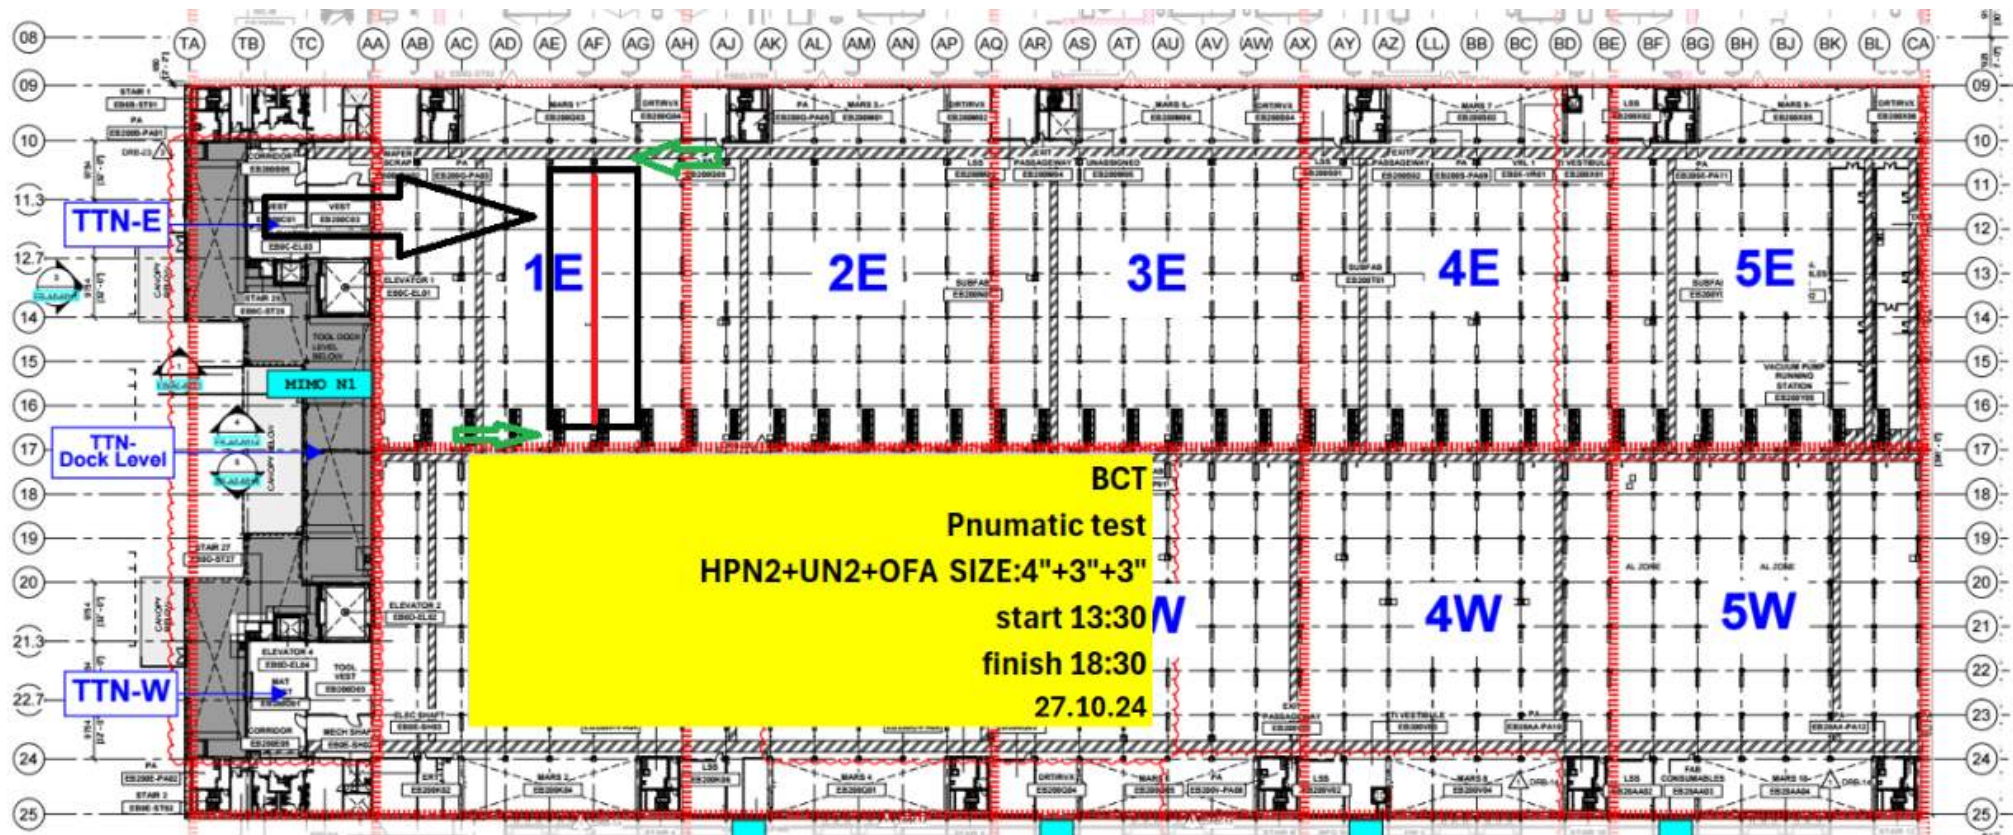

SUBFAB BUILDOUT MOD 2

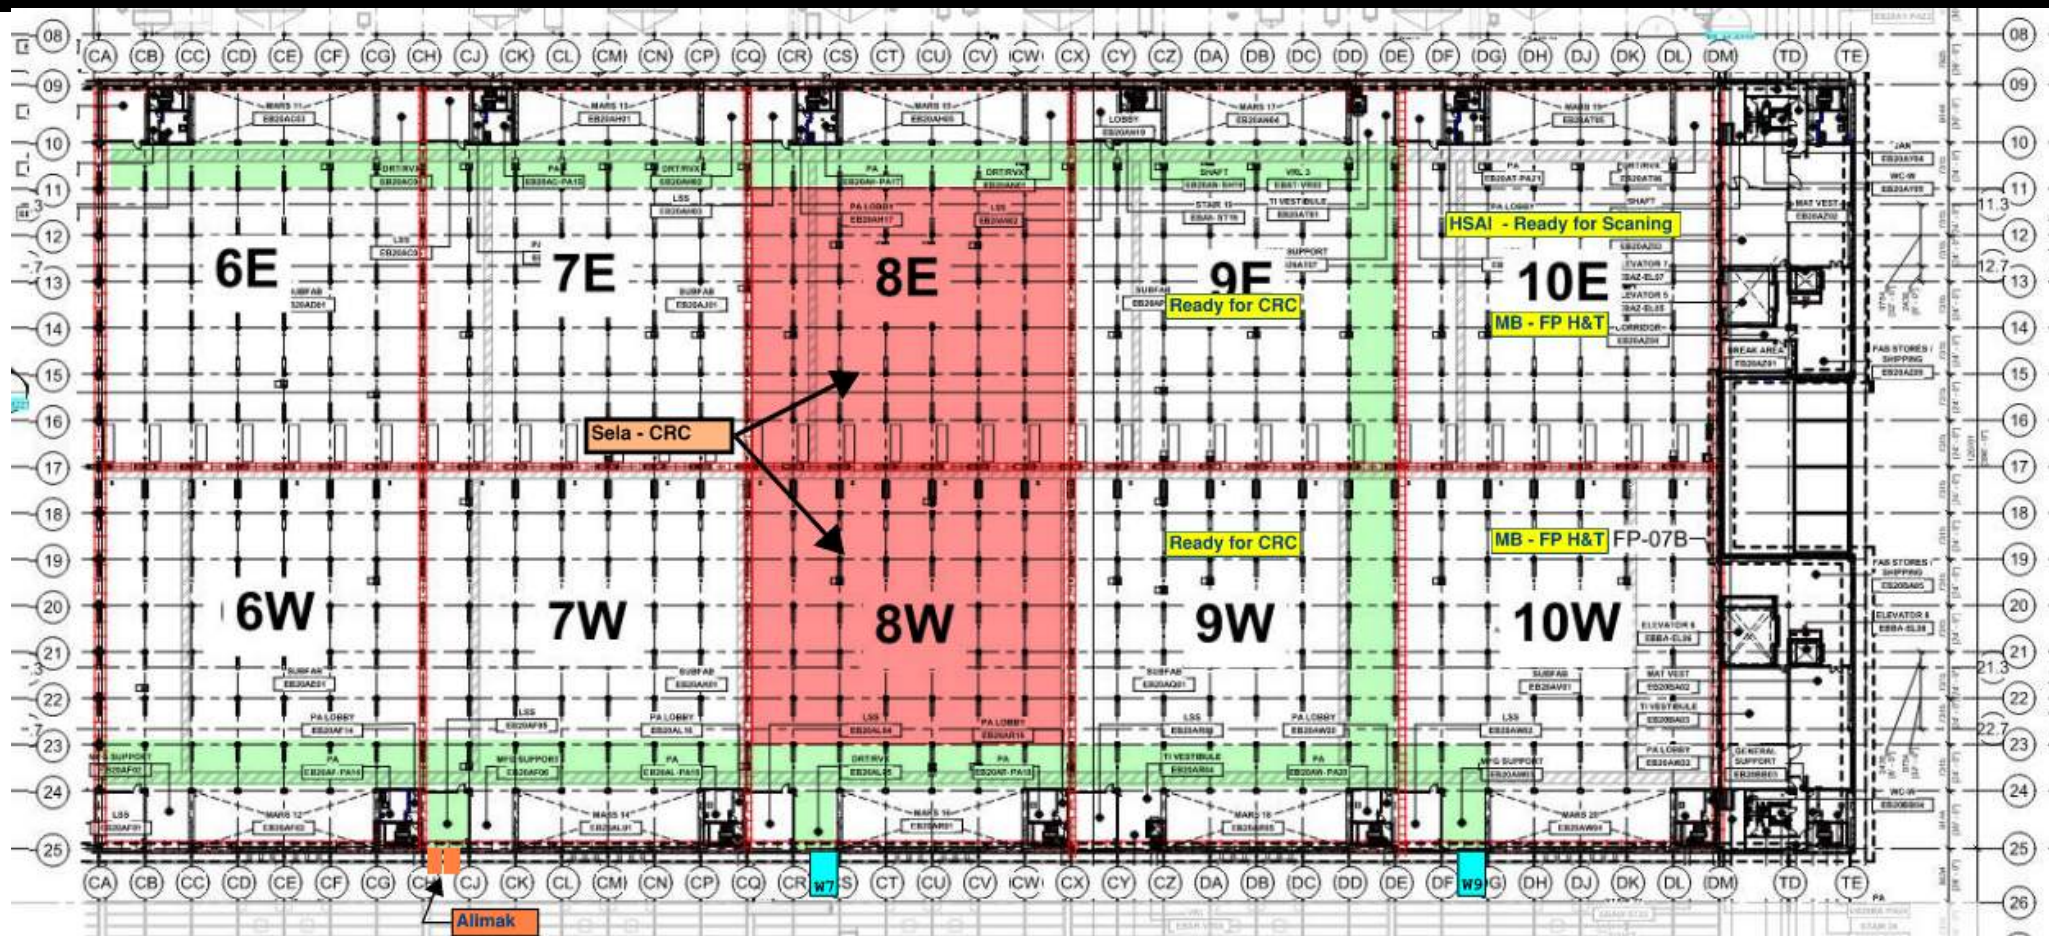

Tavas + Talent solution
P1 cleaning 1E

D&P blades
install

Elram- AA line
columns+G1 wall
mock-up
Chemo- Hangers
install
SN - Beams layout

SELA-crc spraying 17 aa-ak

CRC AA-AK/17-23

Sela: CRC Done

Talad- Cutting arc

TALAD CRC PREP

3

Link
Pah-Taas - exhaust duct install and tie in
SIG- Mobile scaffold install
Afcon- Rack install
Newcotech- temp wall
Afcon - cable tray & racks install

Sella's next prepped
areas.

CR level:
Afcon - Cable trays, modules and stickers, 2E, 2W, 3E, 3W, 4E
MB- 1W drops, 2E- 2W pipes and drops
Elram - 9-10, 24-25 columns/shaft walls, AA line column wraps
VW/JS - 17-18 line added beams+ AS south stocker beams
Meptagon - I&C 2W
D&P - 5E blades install.
Tavaresh - 5E blades, 1W-1E shaft walls
HYG- 5W Litho crane steel
T - Duct prep for test AA-AH east
Talad- 1W 4DA holes drilling, 1W cutting around steel, 17 line bracing
TMT - Safety net install

1E

All trades should do
training and the have
correct equipment to
work in this area

2E

3E

4E

5E

Talad-ongoing beam bracing across 17 line+aa/ab

2W

3W


4W

5N

L
I
N
K






HOFFMAN CONSTRUCTION COMPANY

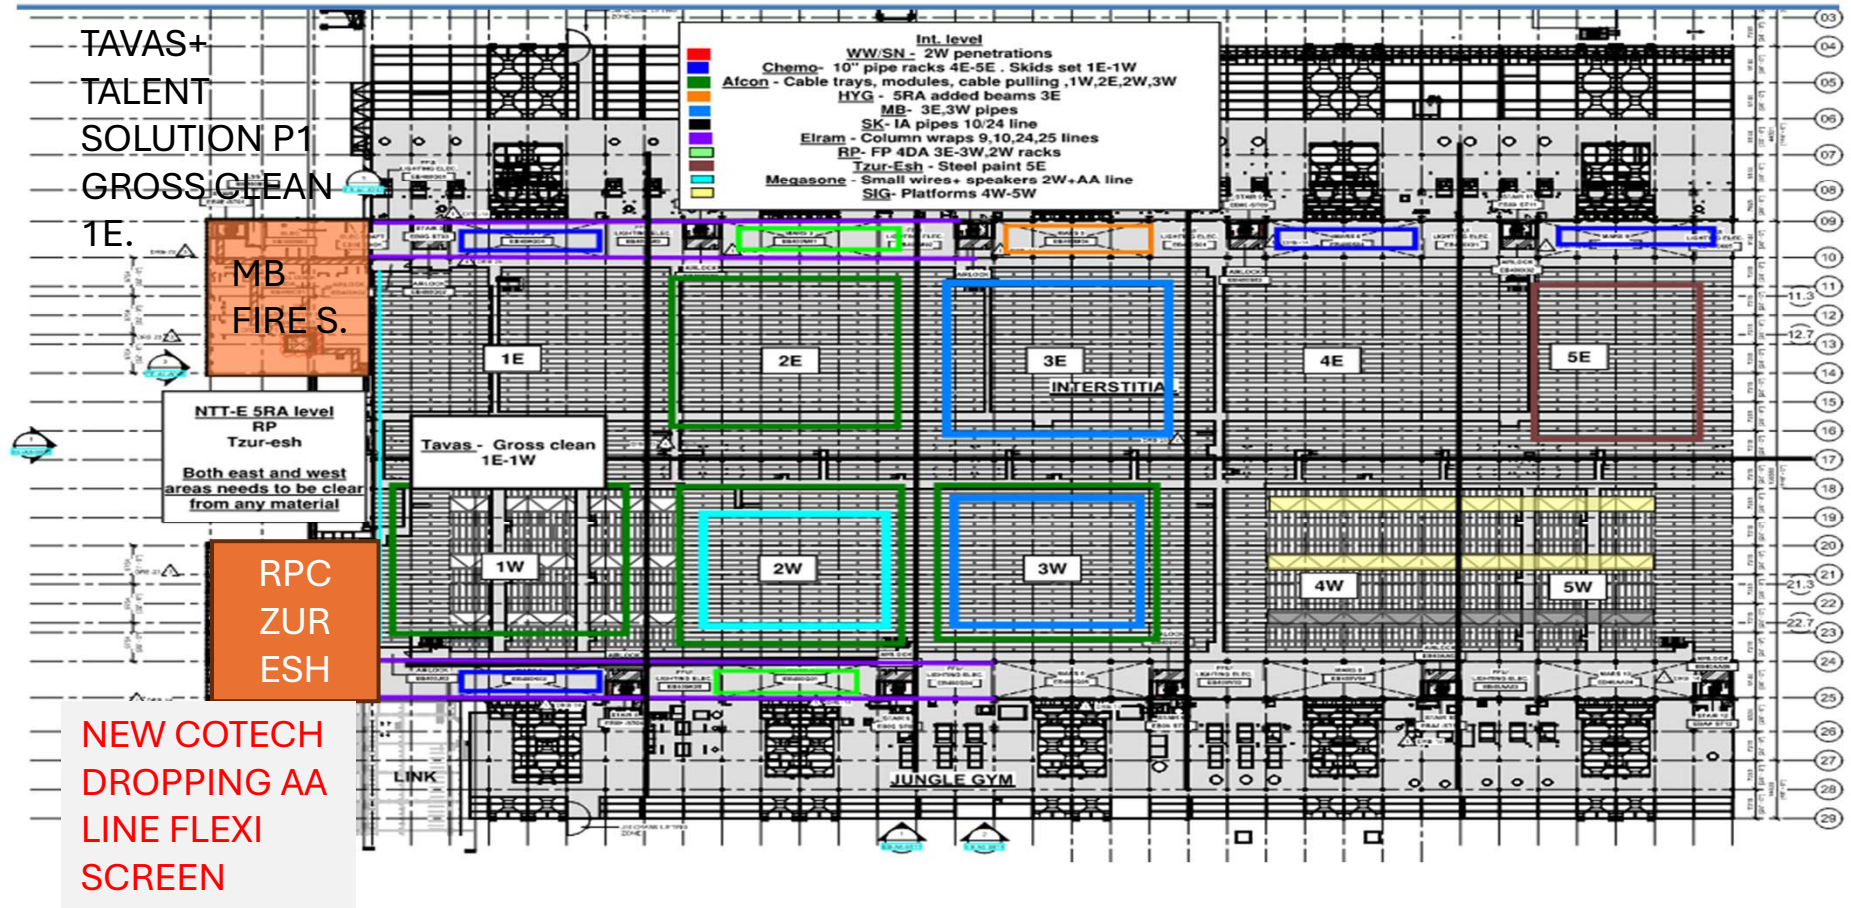

Clean Room Wall Of Shame

22.10.2024

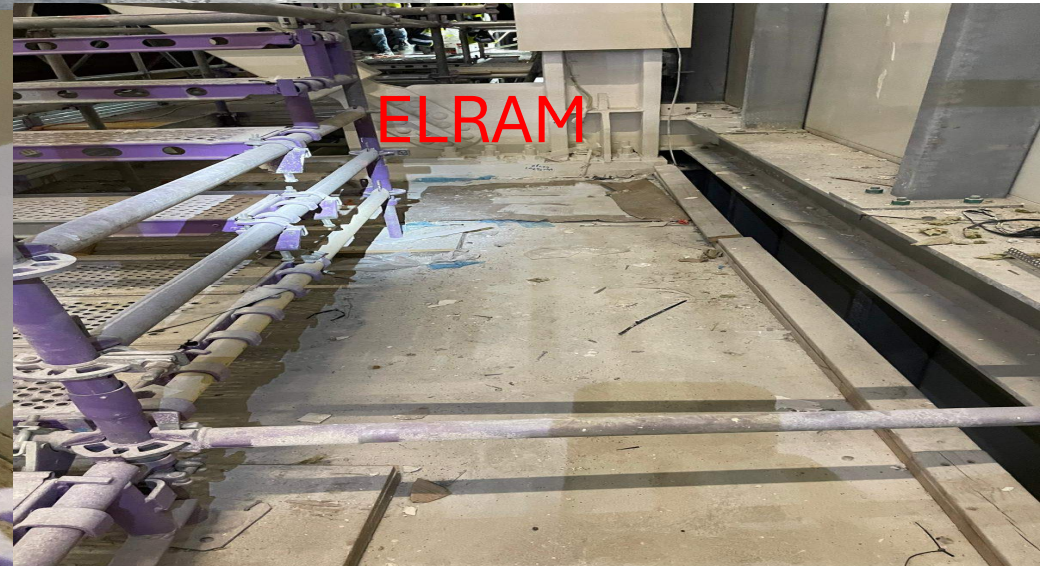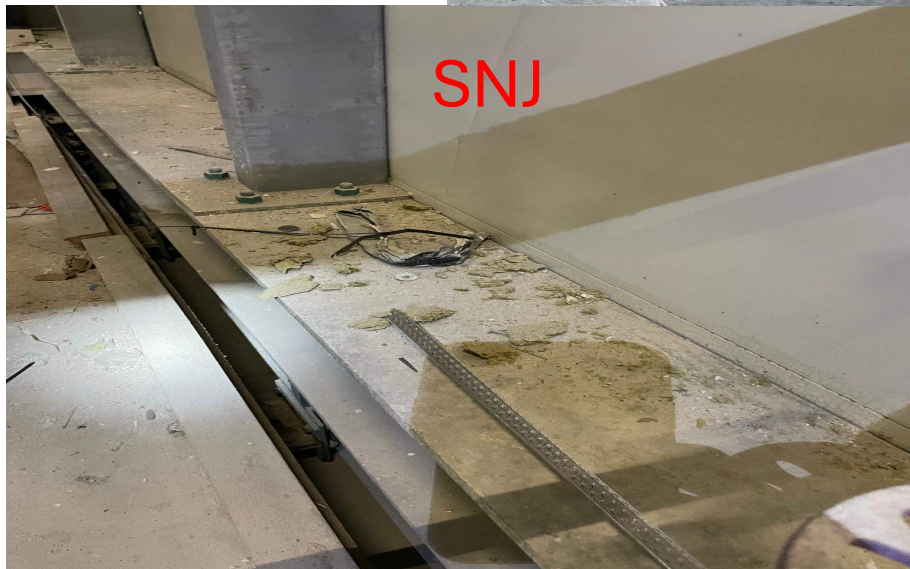

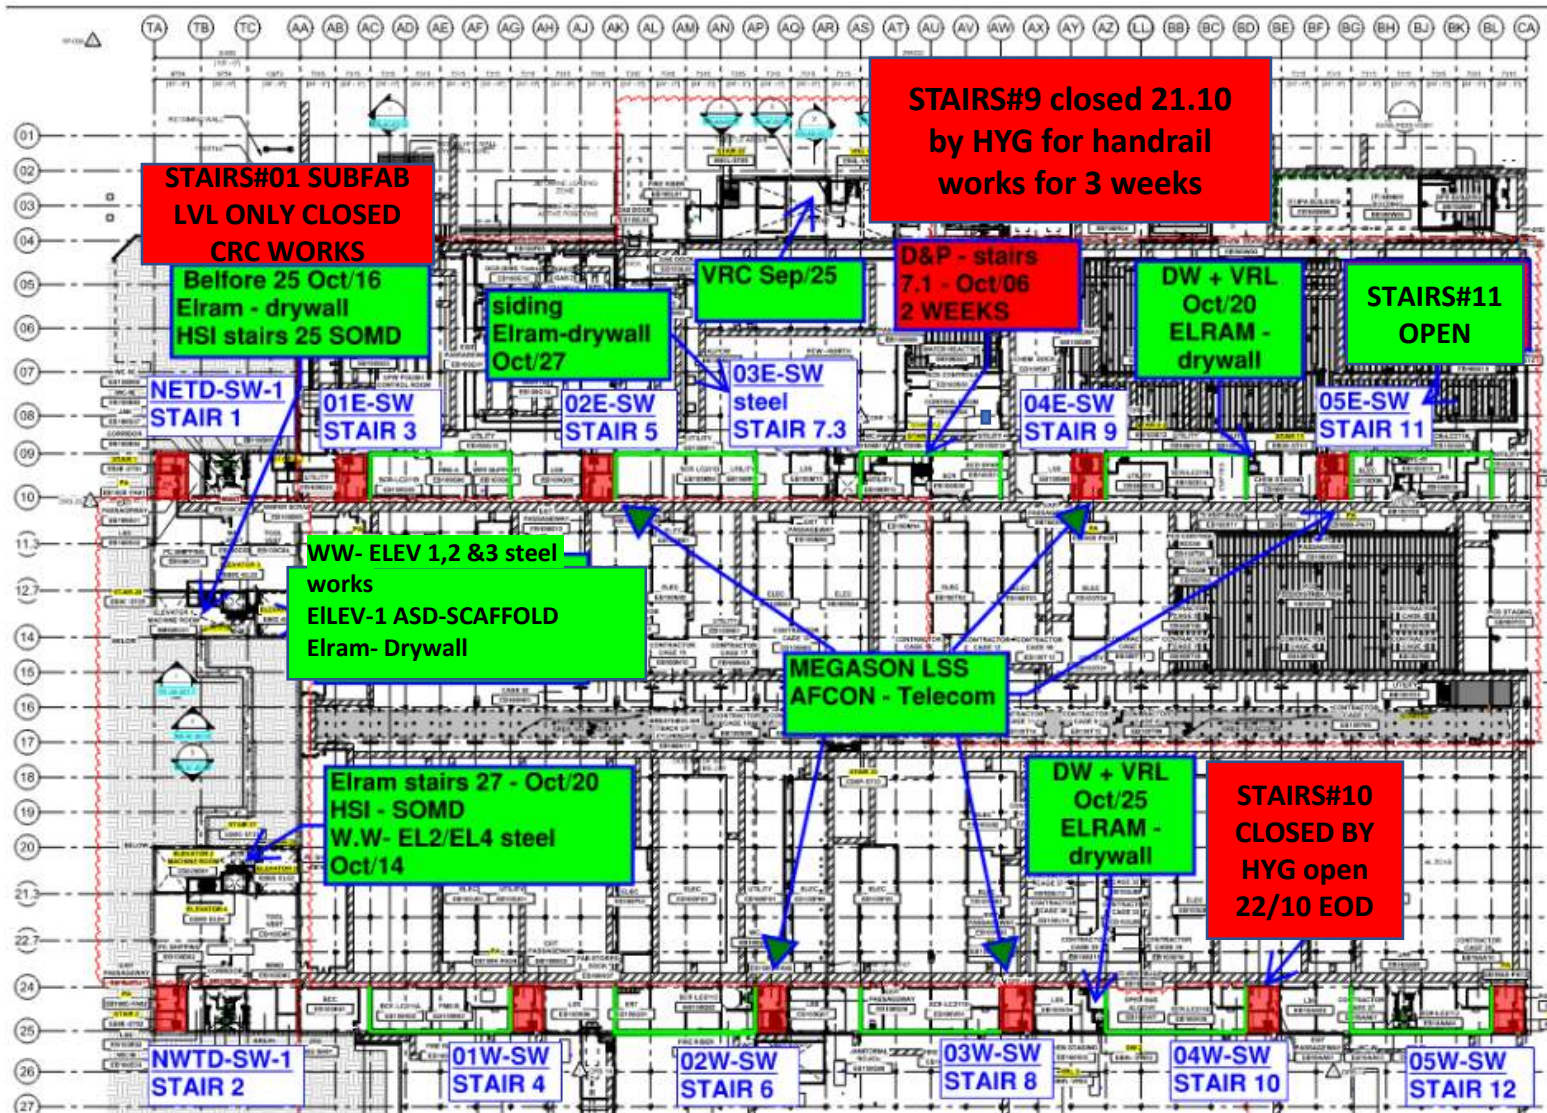

Siding - East FAB - PSSS

BLOWDOWN 30%


[illegible]


Siding - West FAB - JYG

BLOWDOWN 30%

[illegible]




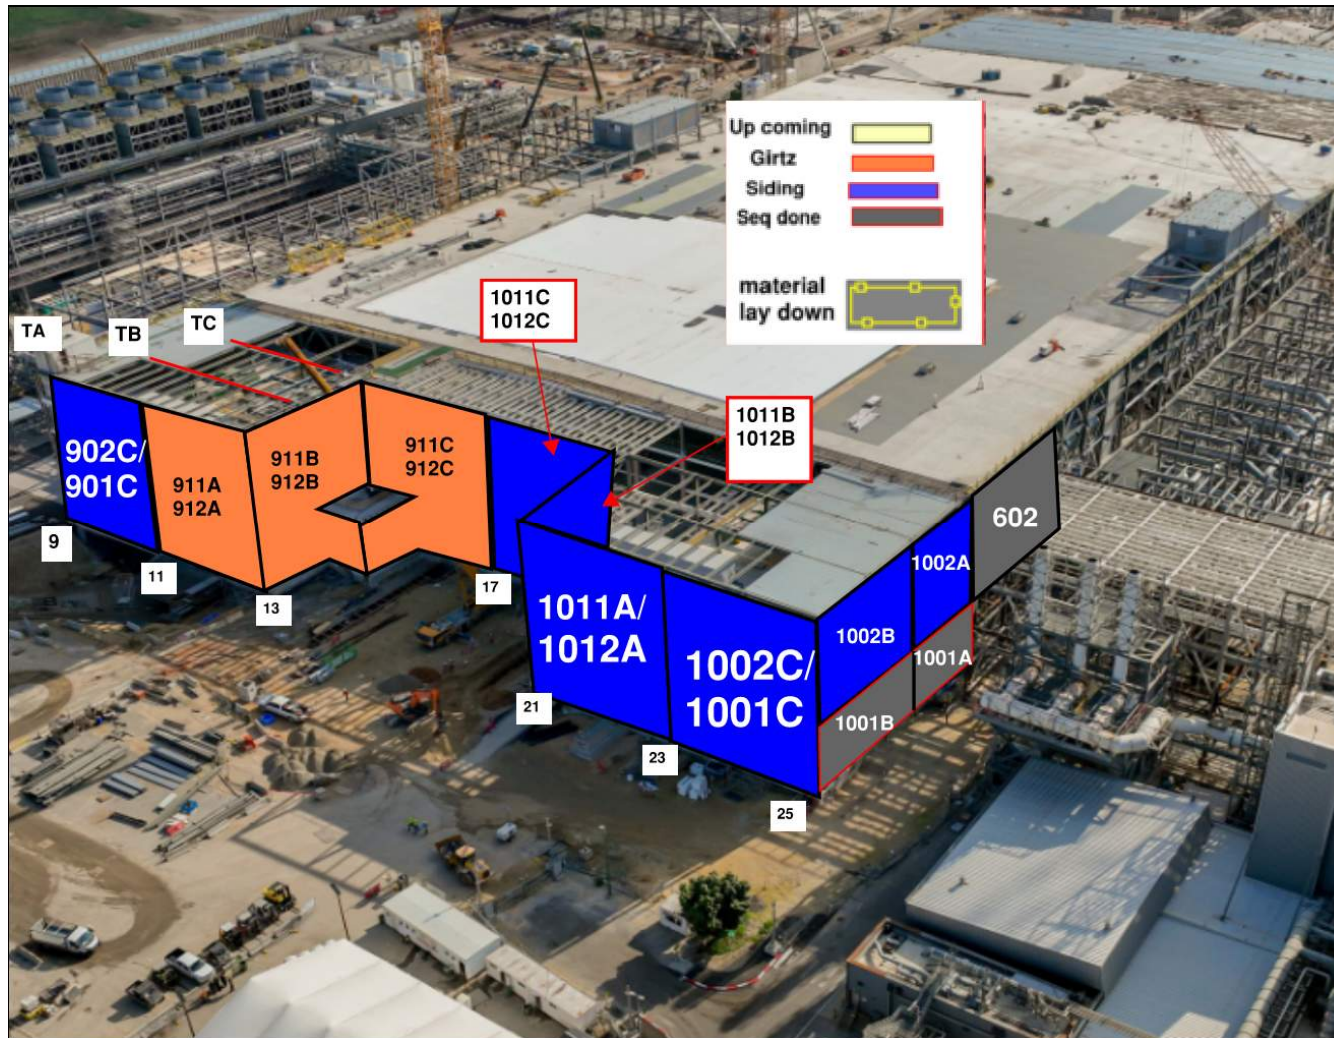

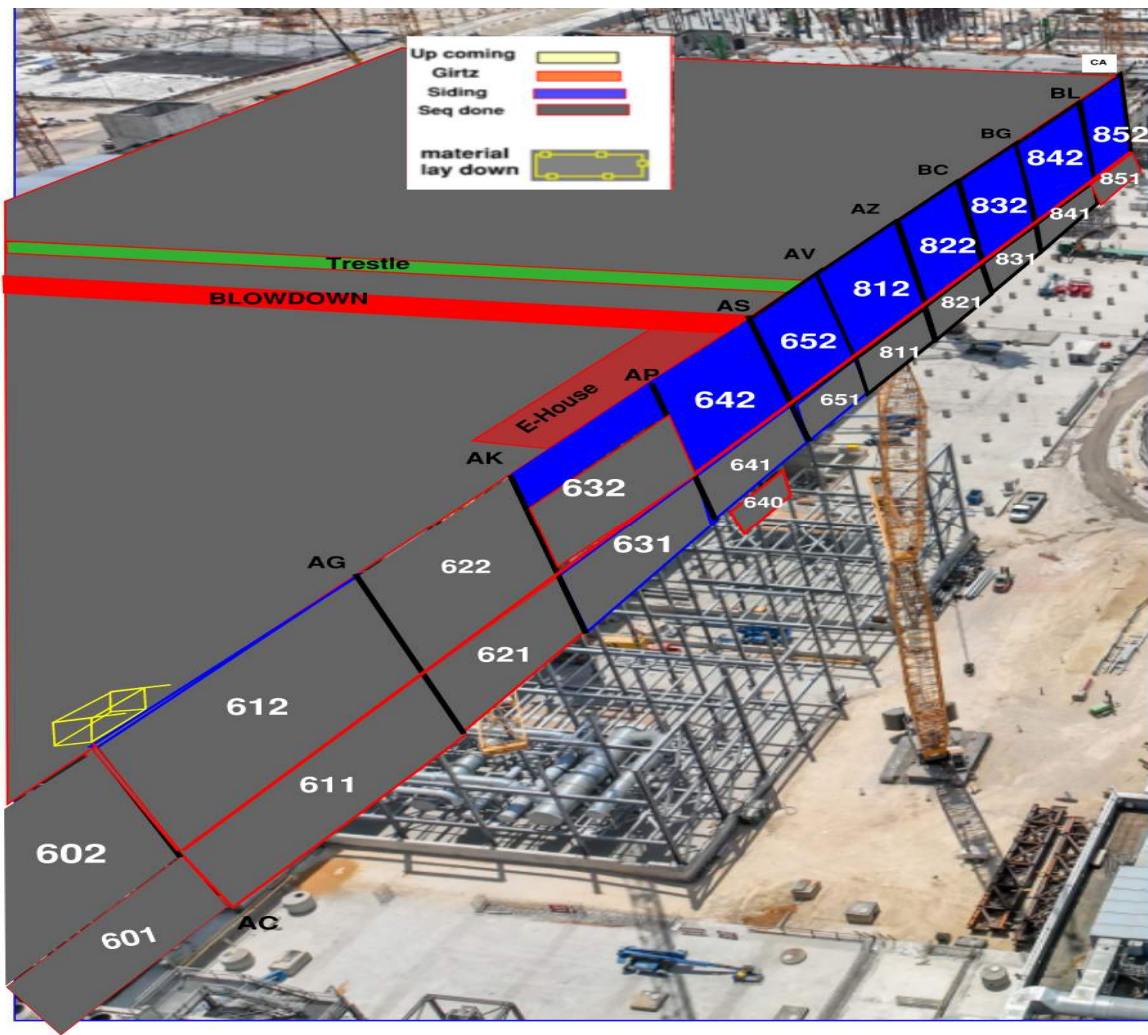


PSSS.1

Utility Level 1YA

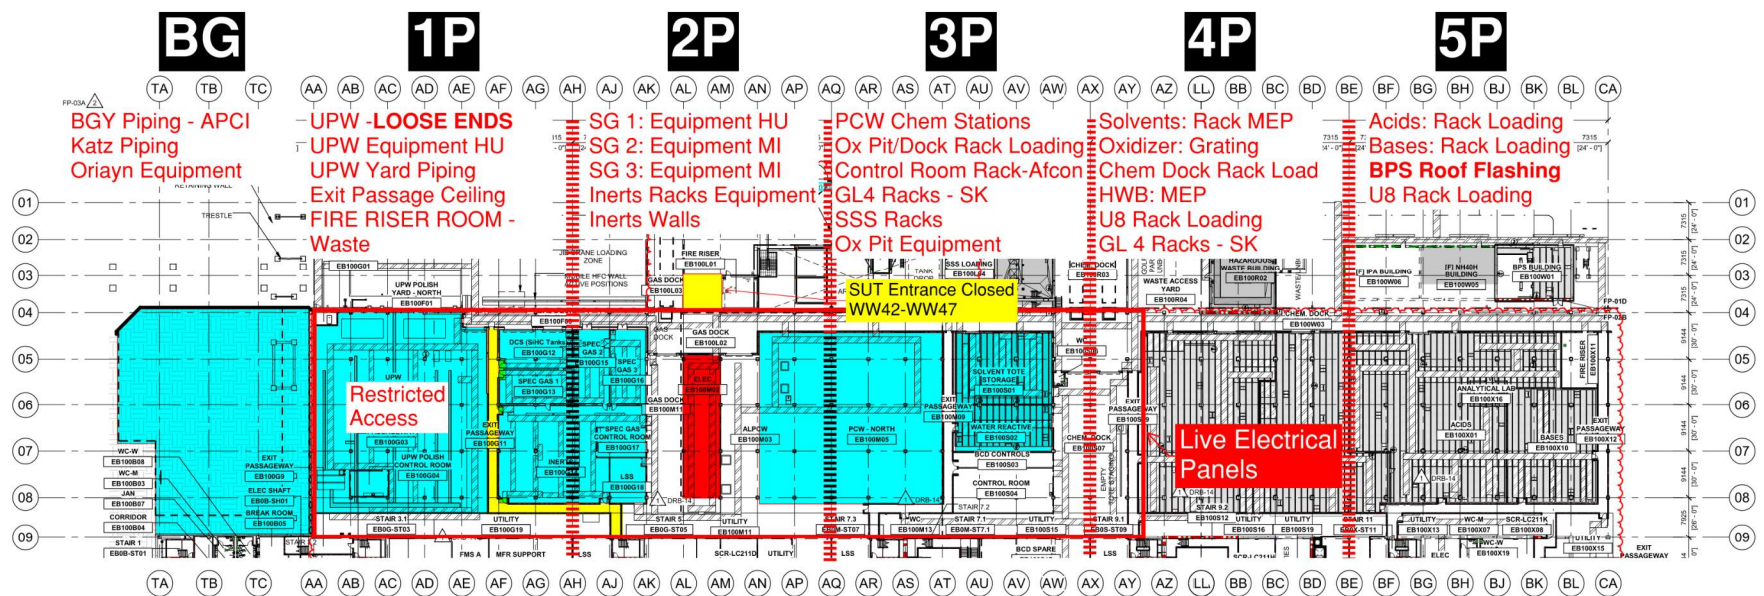


PSSS Roof 2SA

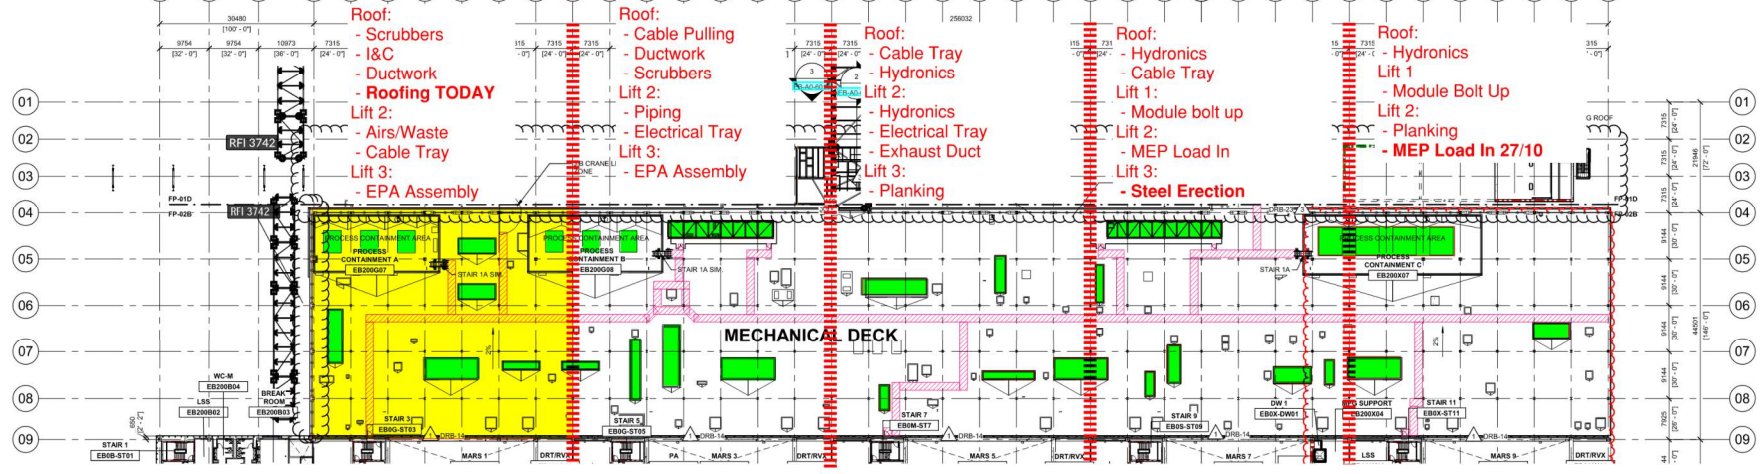


PSSS.2


Utility Level
1YA

PSSS Roof
2SA

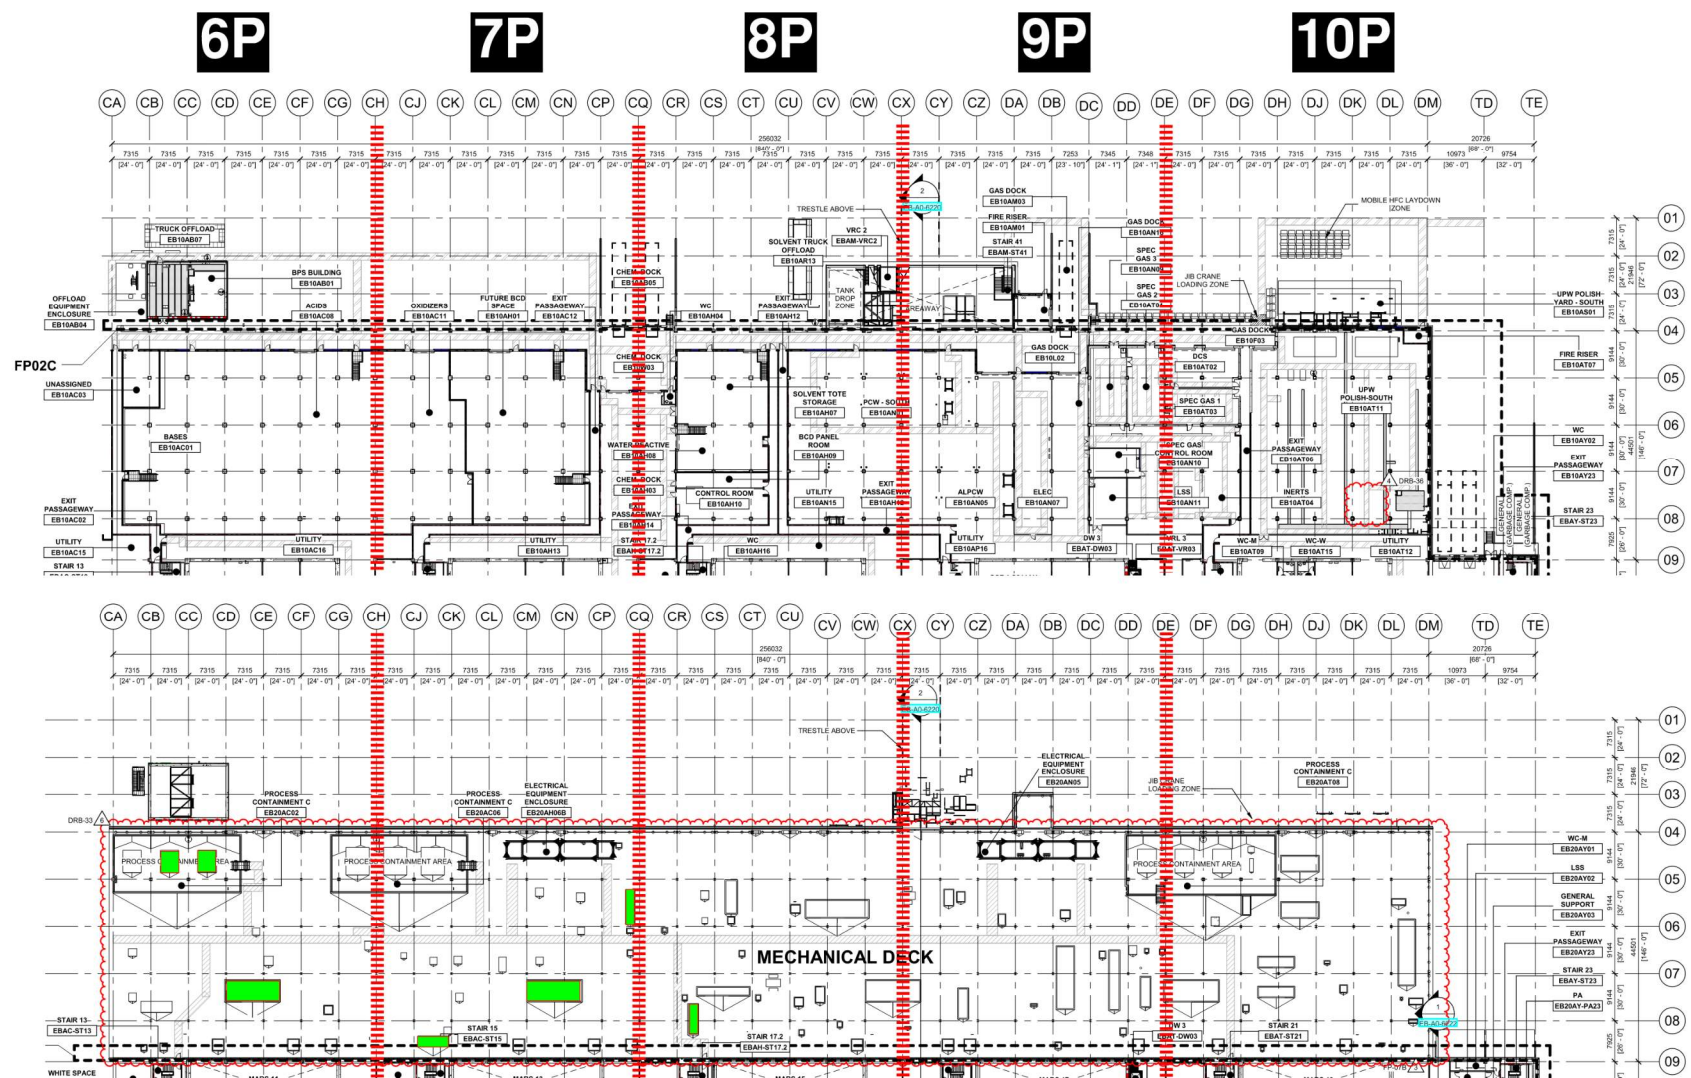



DMAG MOVE FOR Plenum Set

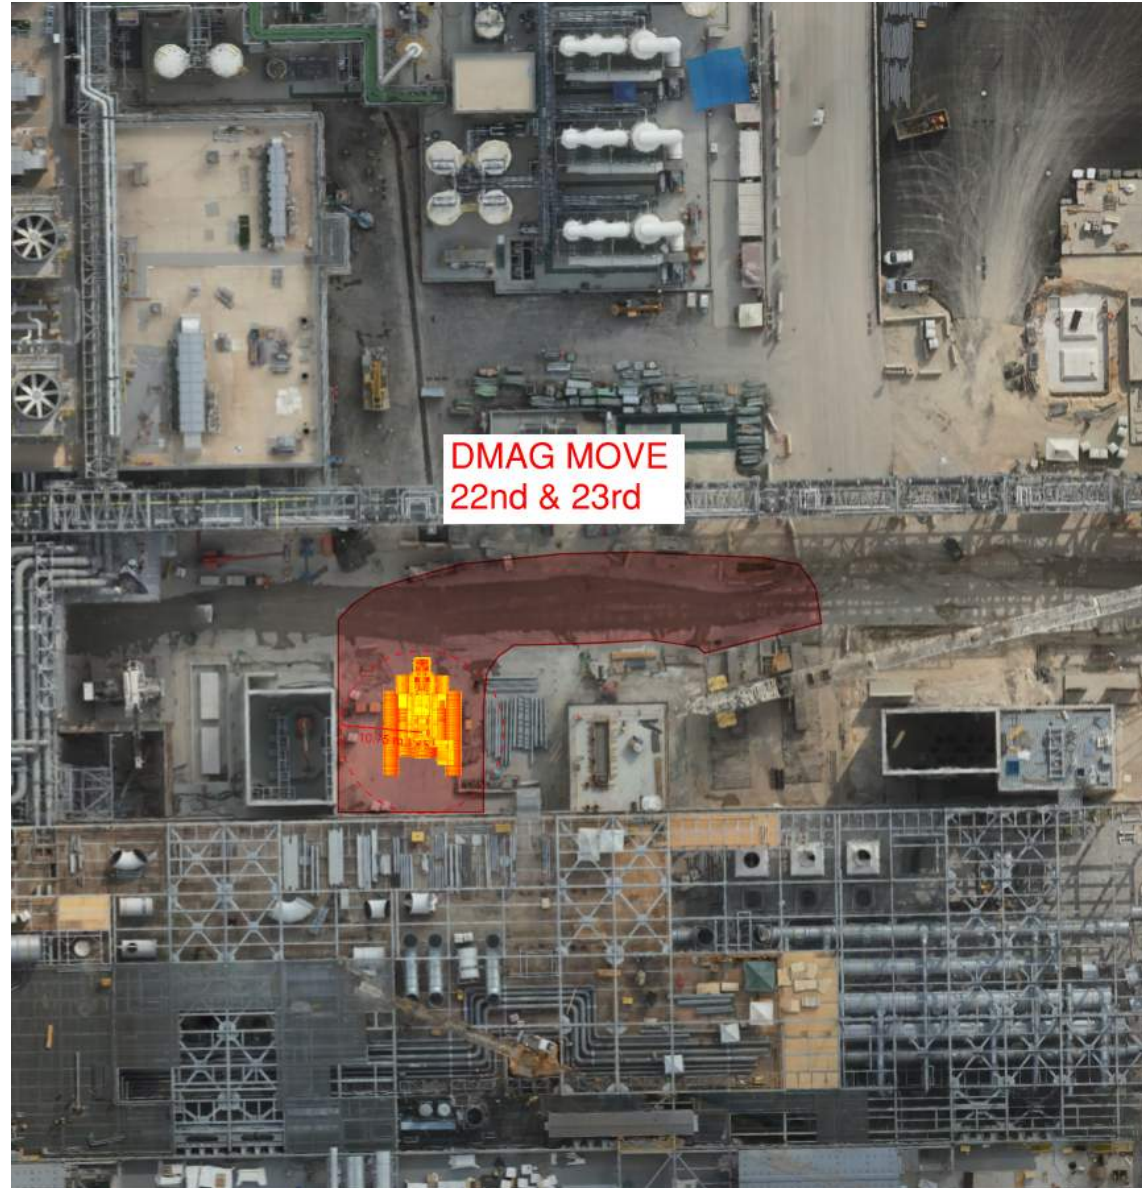




WJG 01J, 02J LIFT 2 & 3

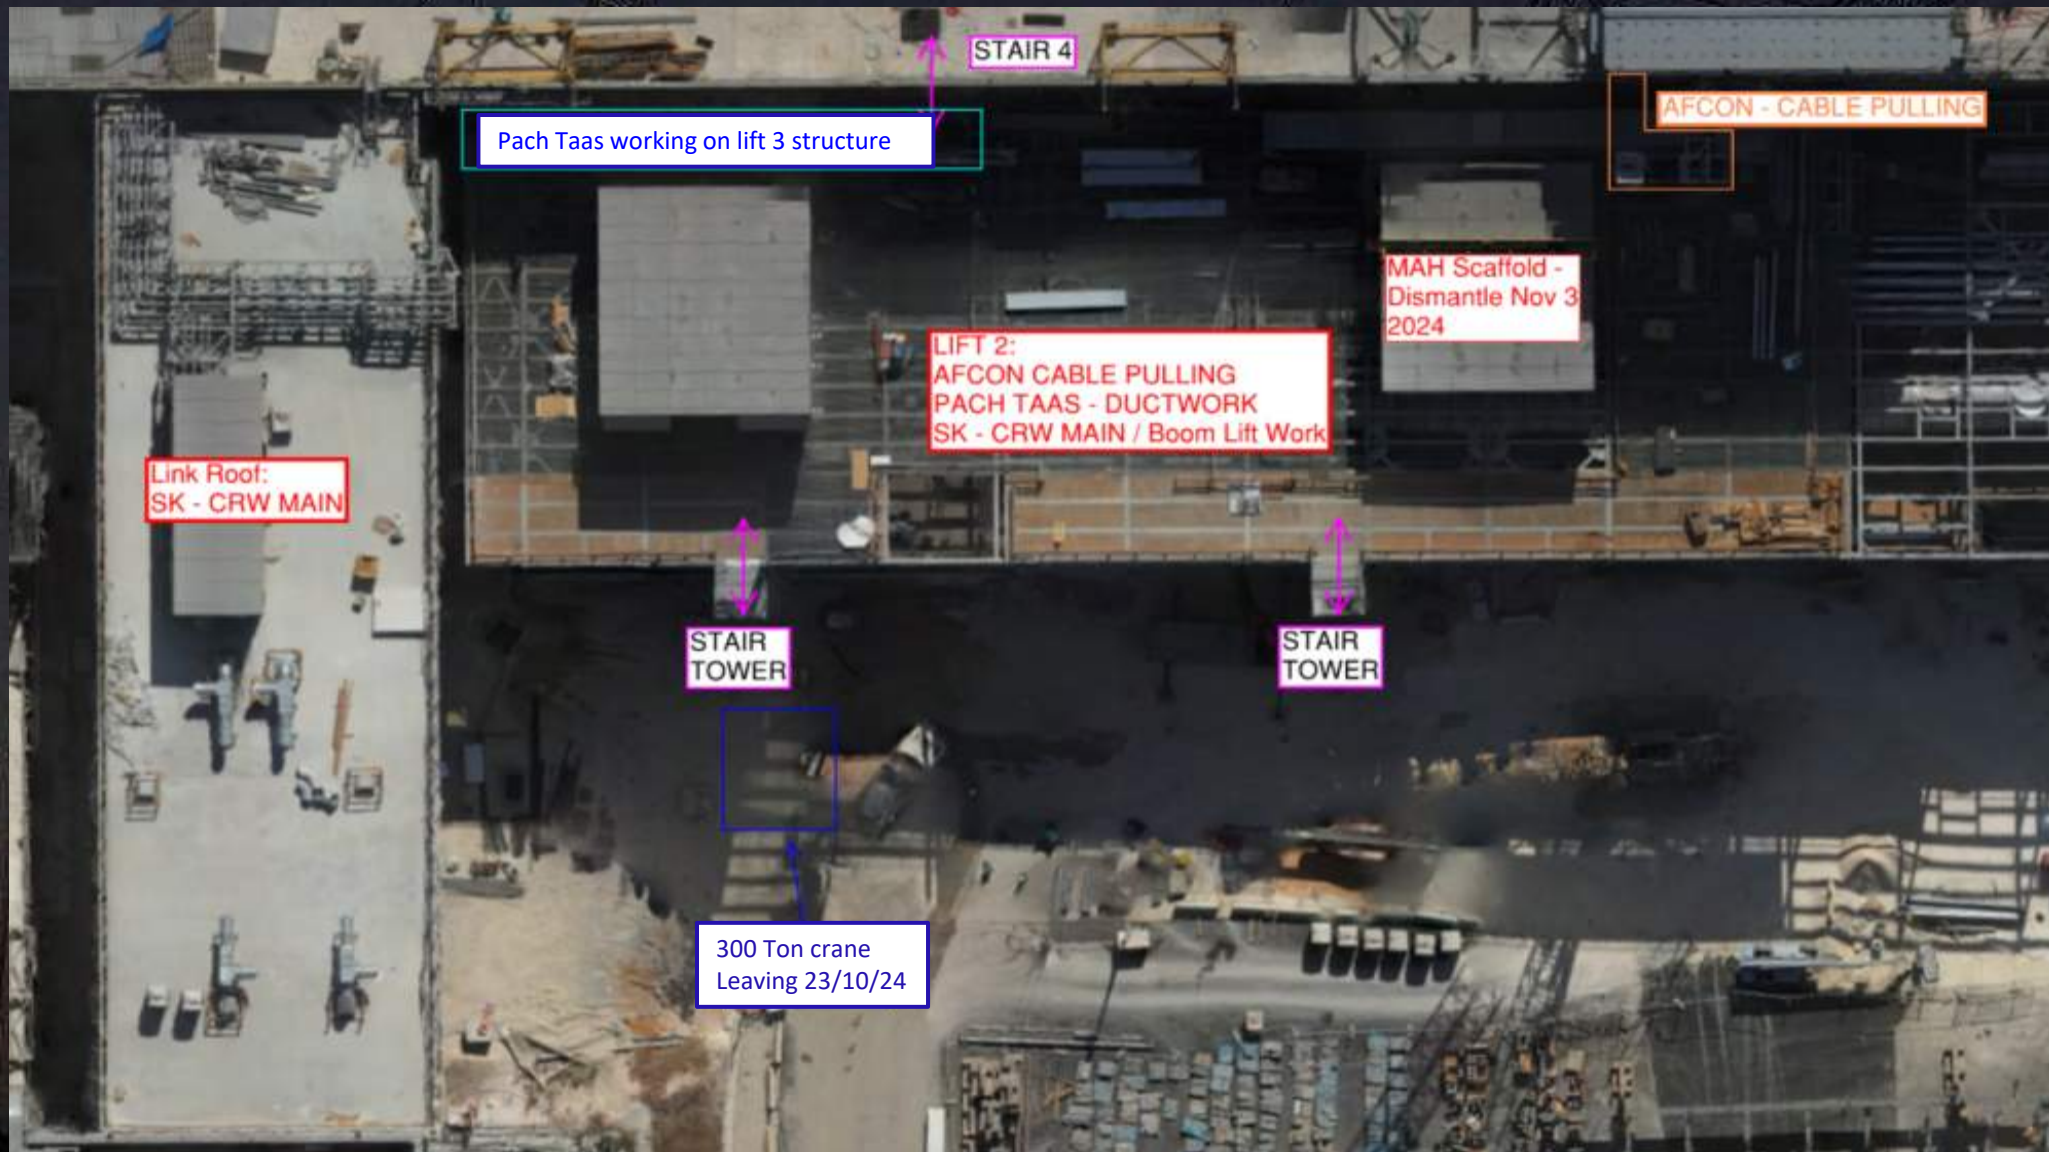





WJG 03J, 04J, 05J LIFT 2 & 3







Walk Path Reroute WW43 & WW44

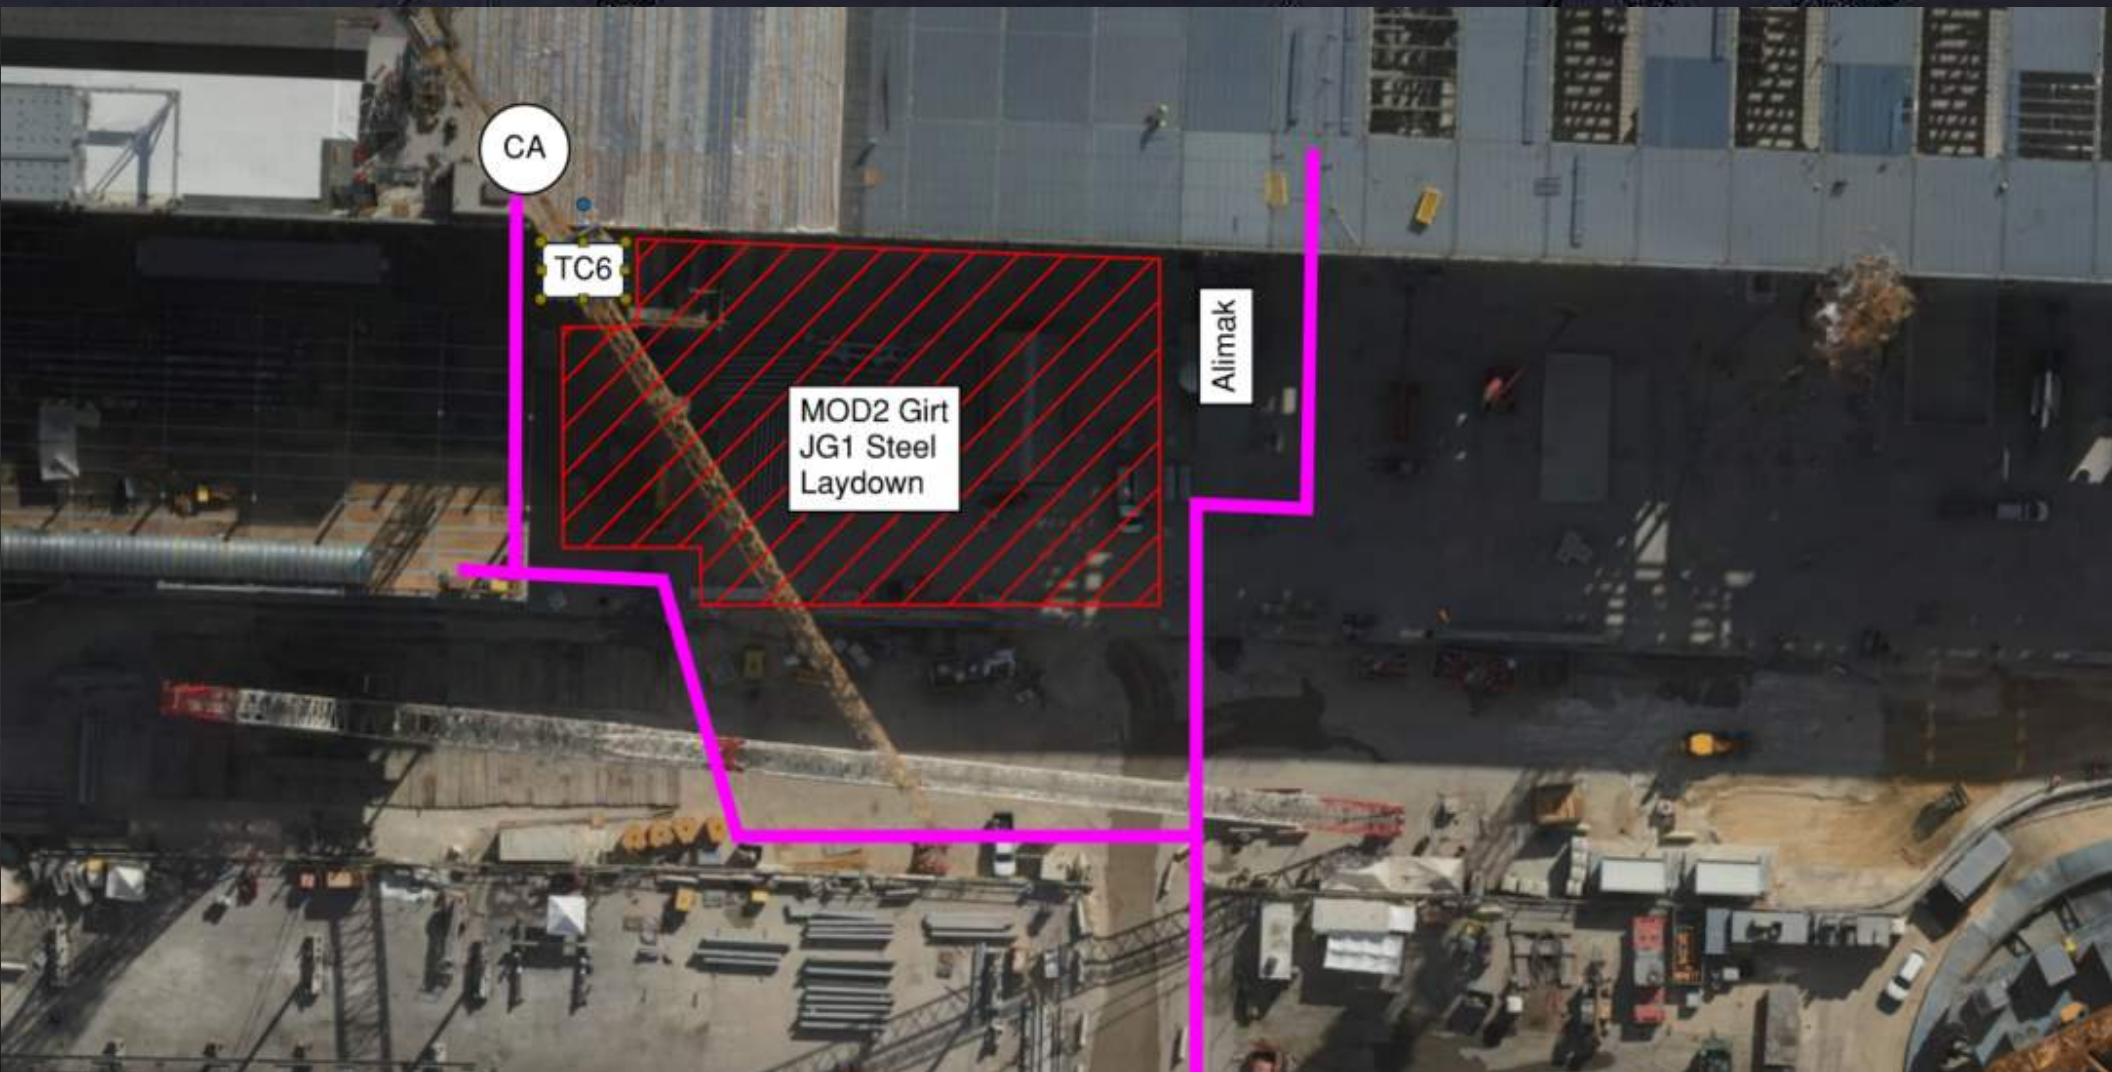



AH104-22-00 Set – 29/10

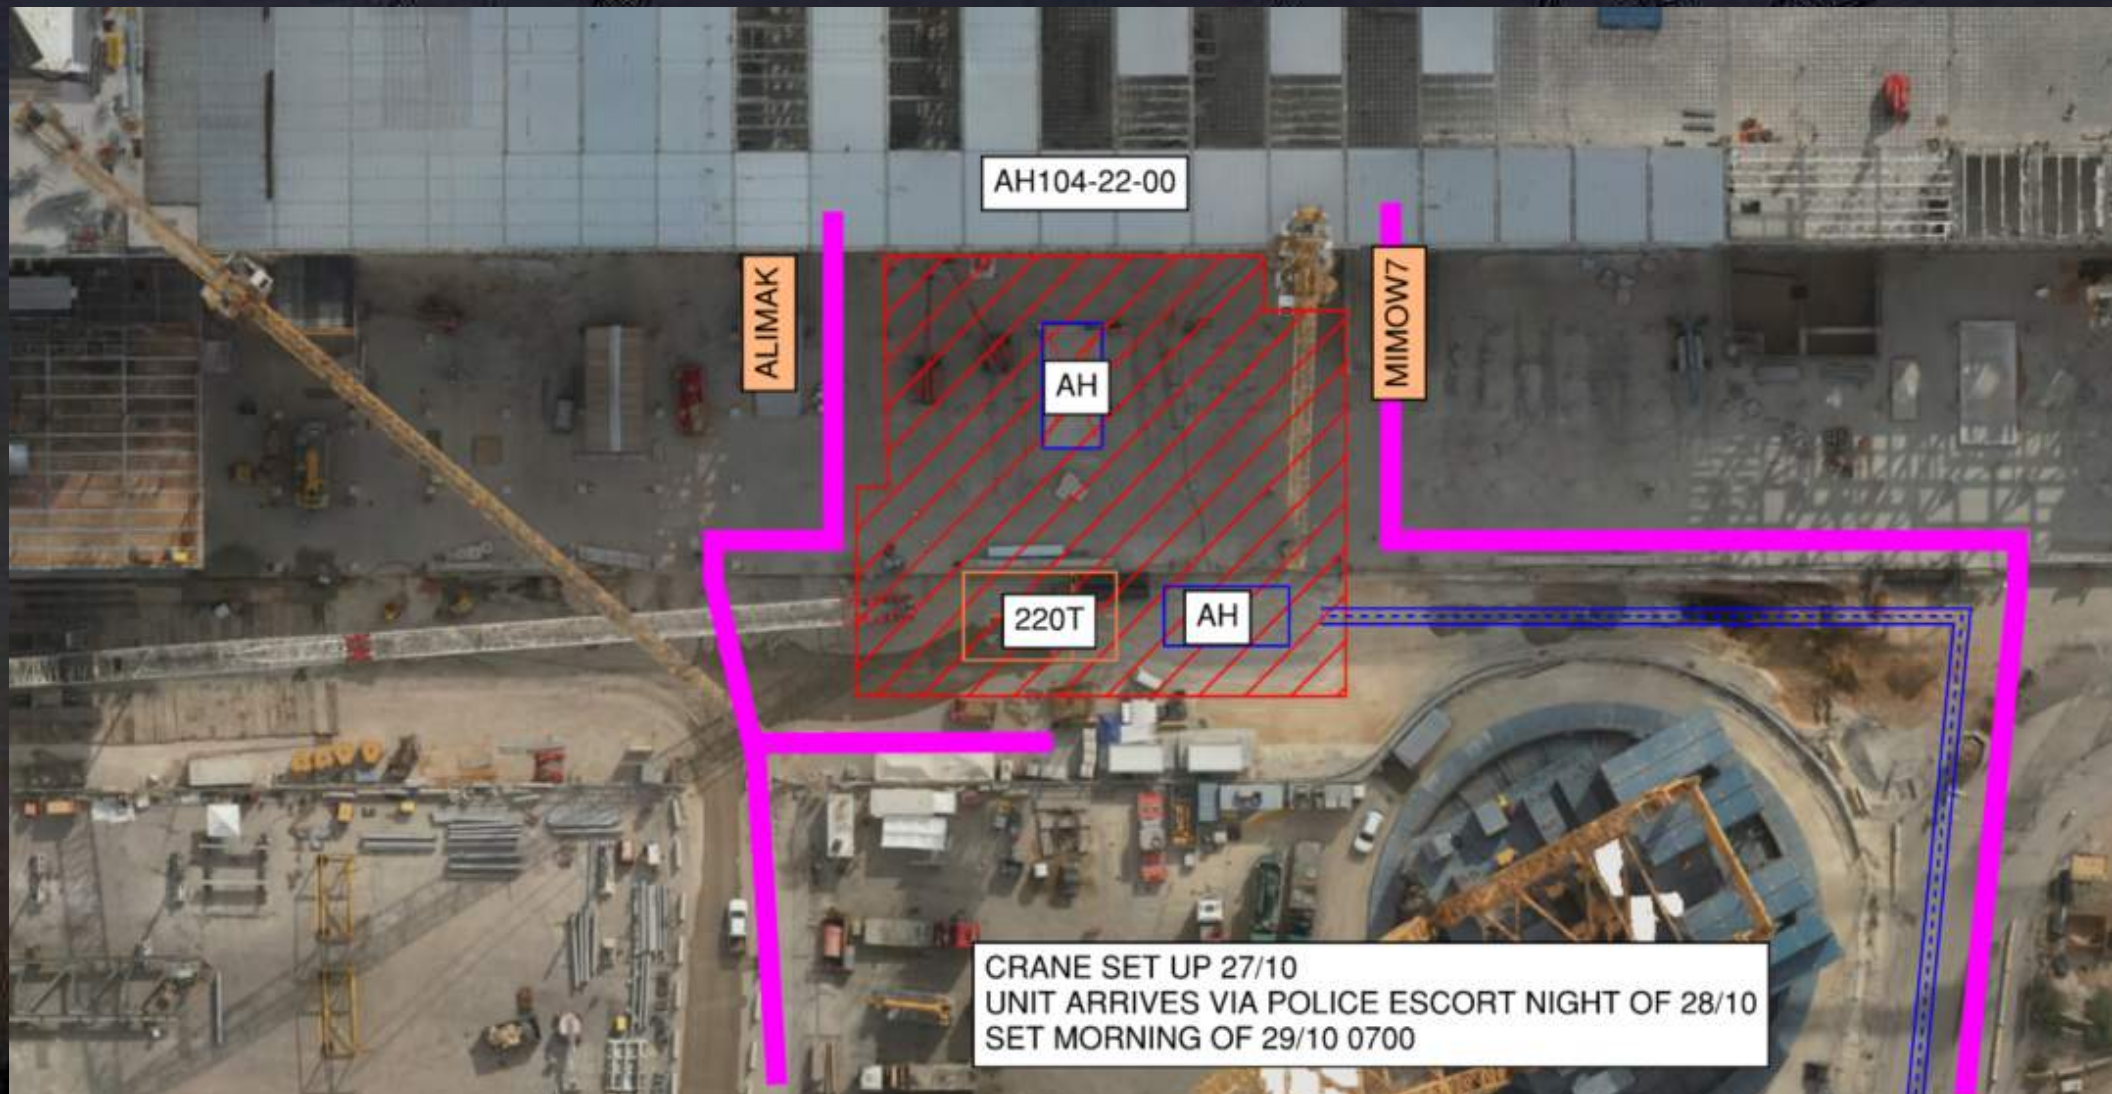

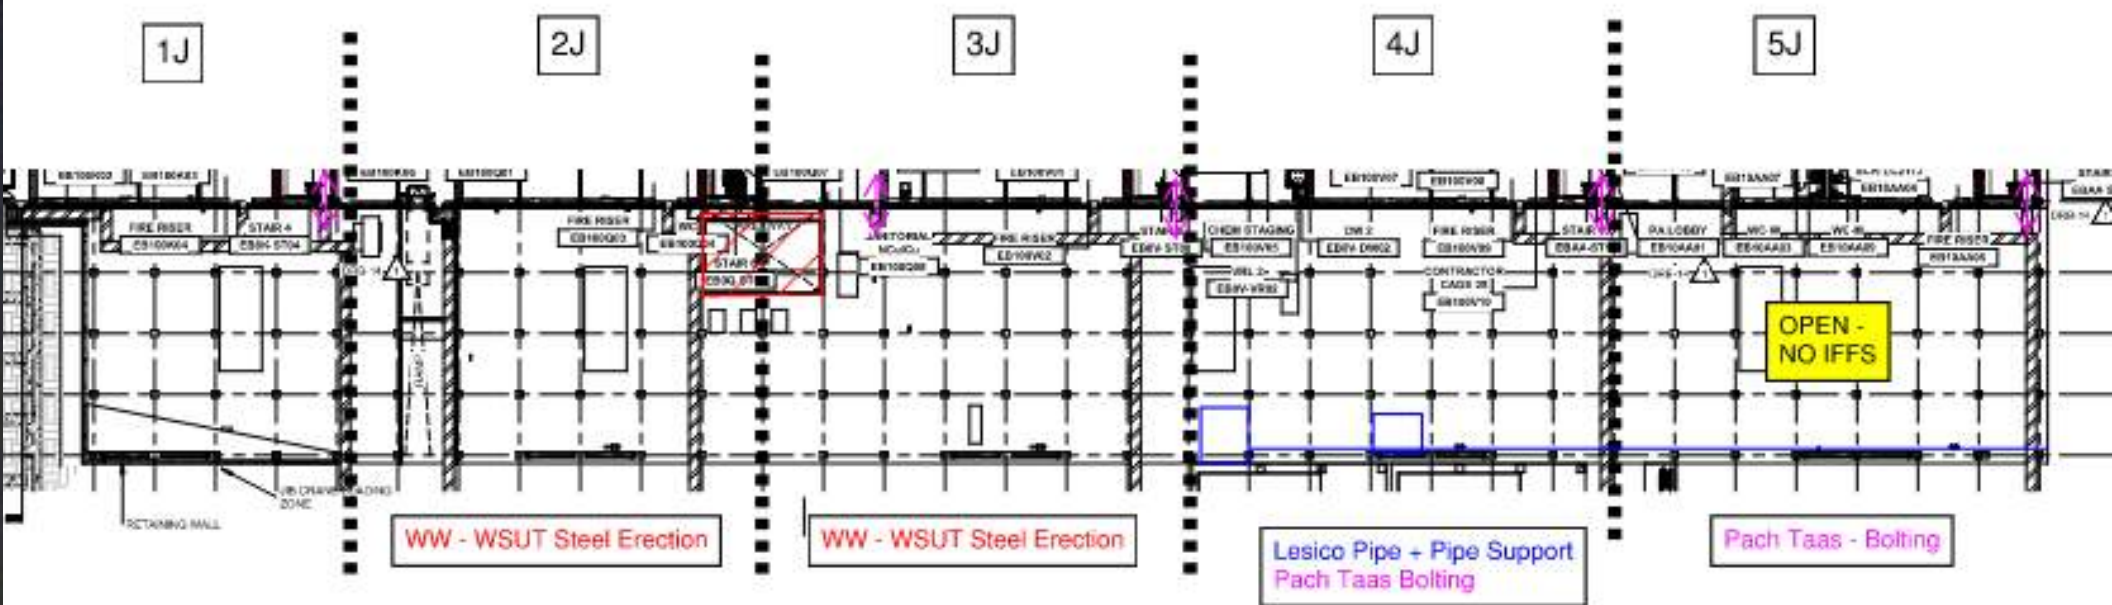




CUB 1

CUB 1 COORDINATION MAP


UPDATED

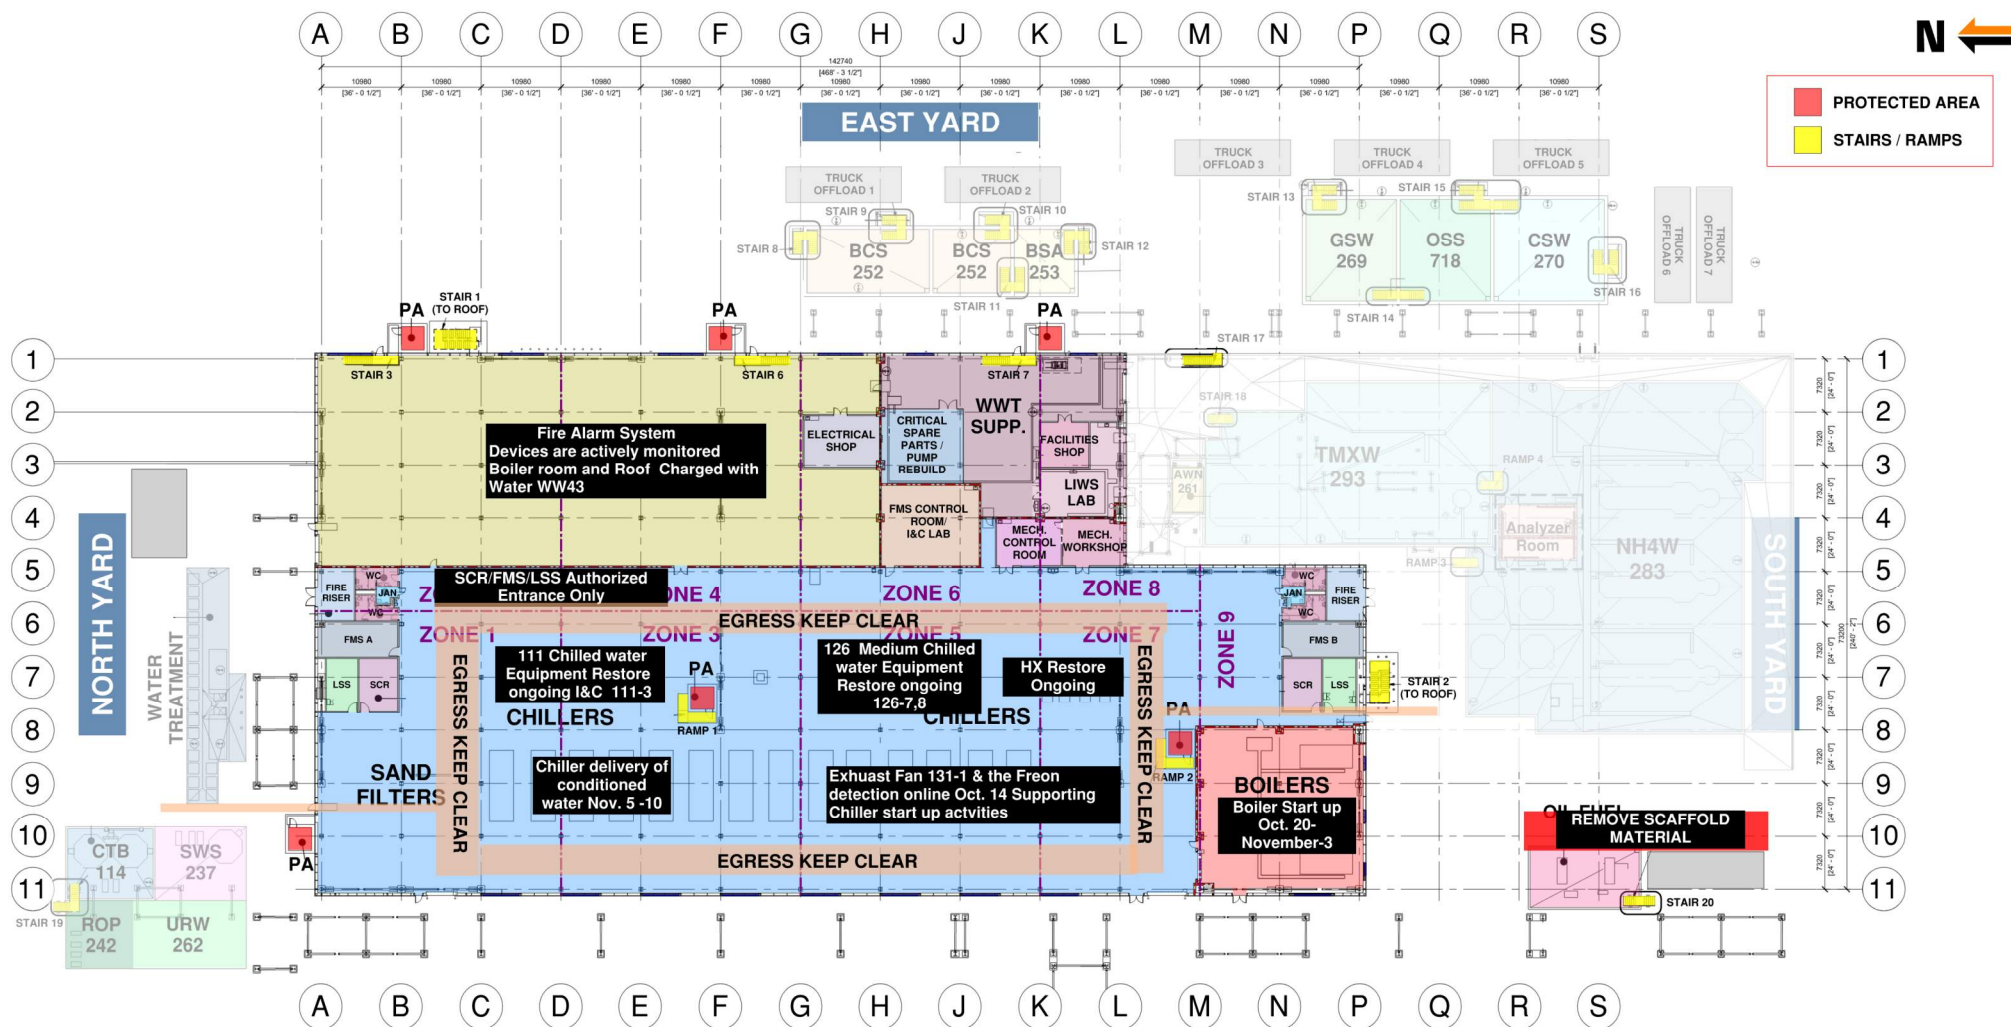


CUB 1 – EXTERIOR/ROOF




CUB 2

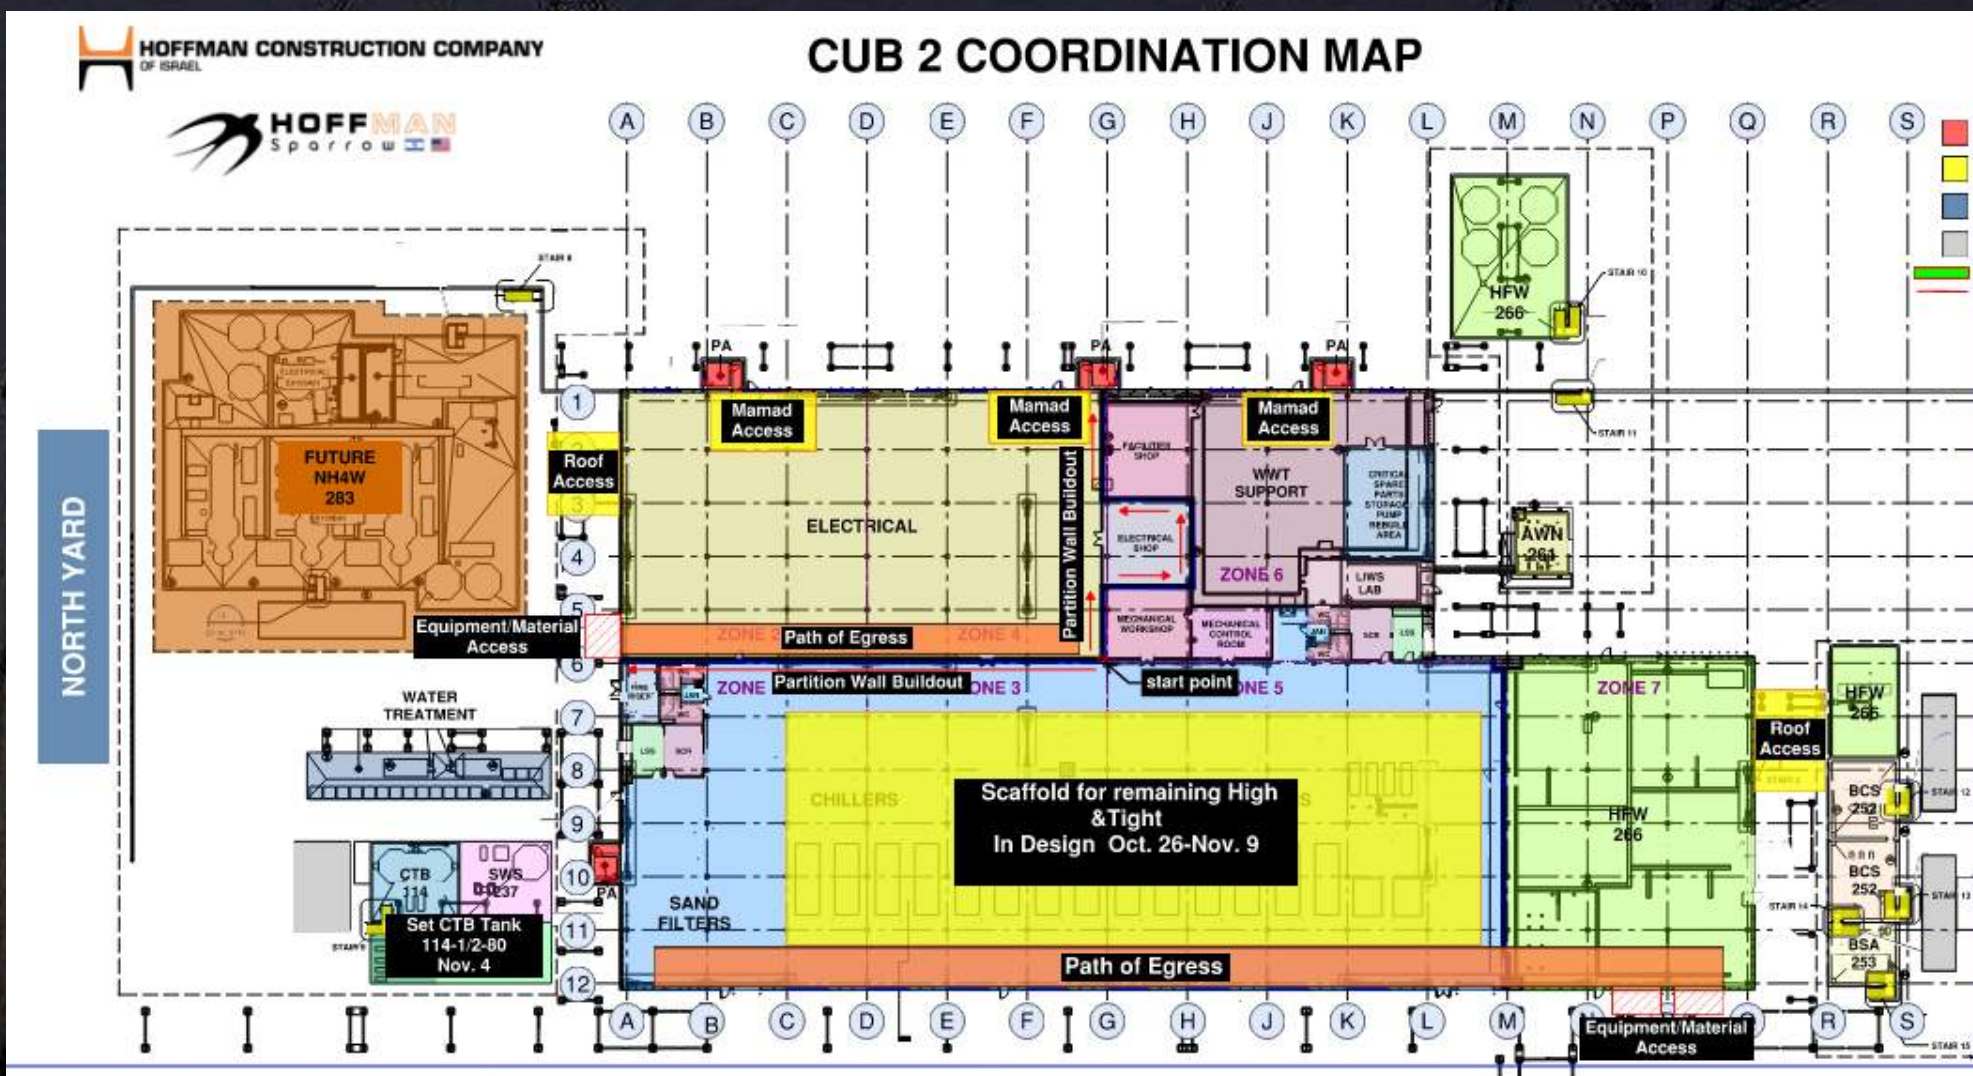

CUB 2 – EXTERIOR/ROOF

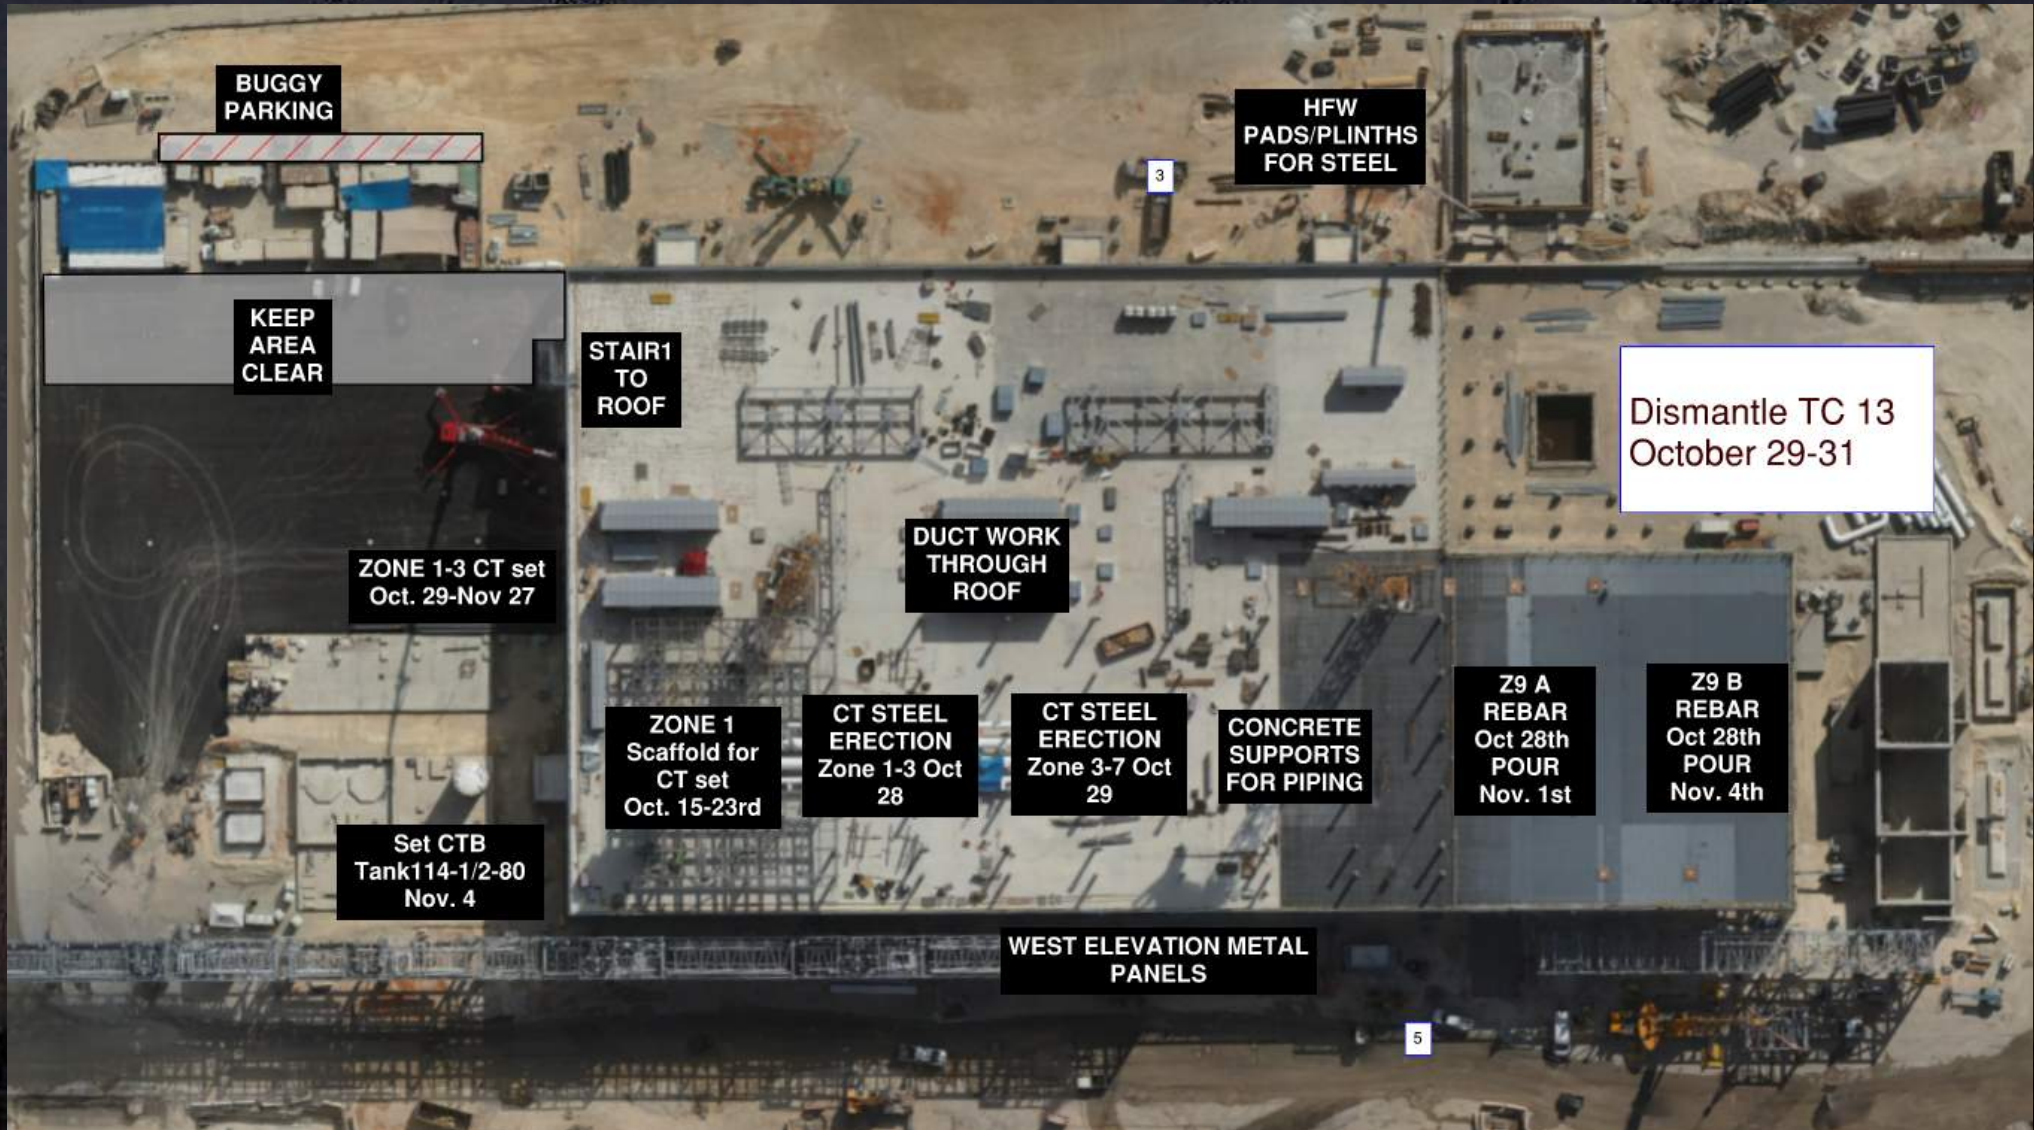



CUB 2 – Crane Logistics

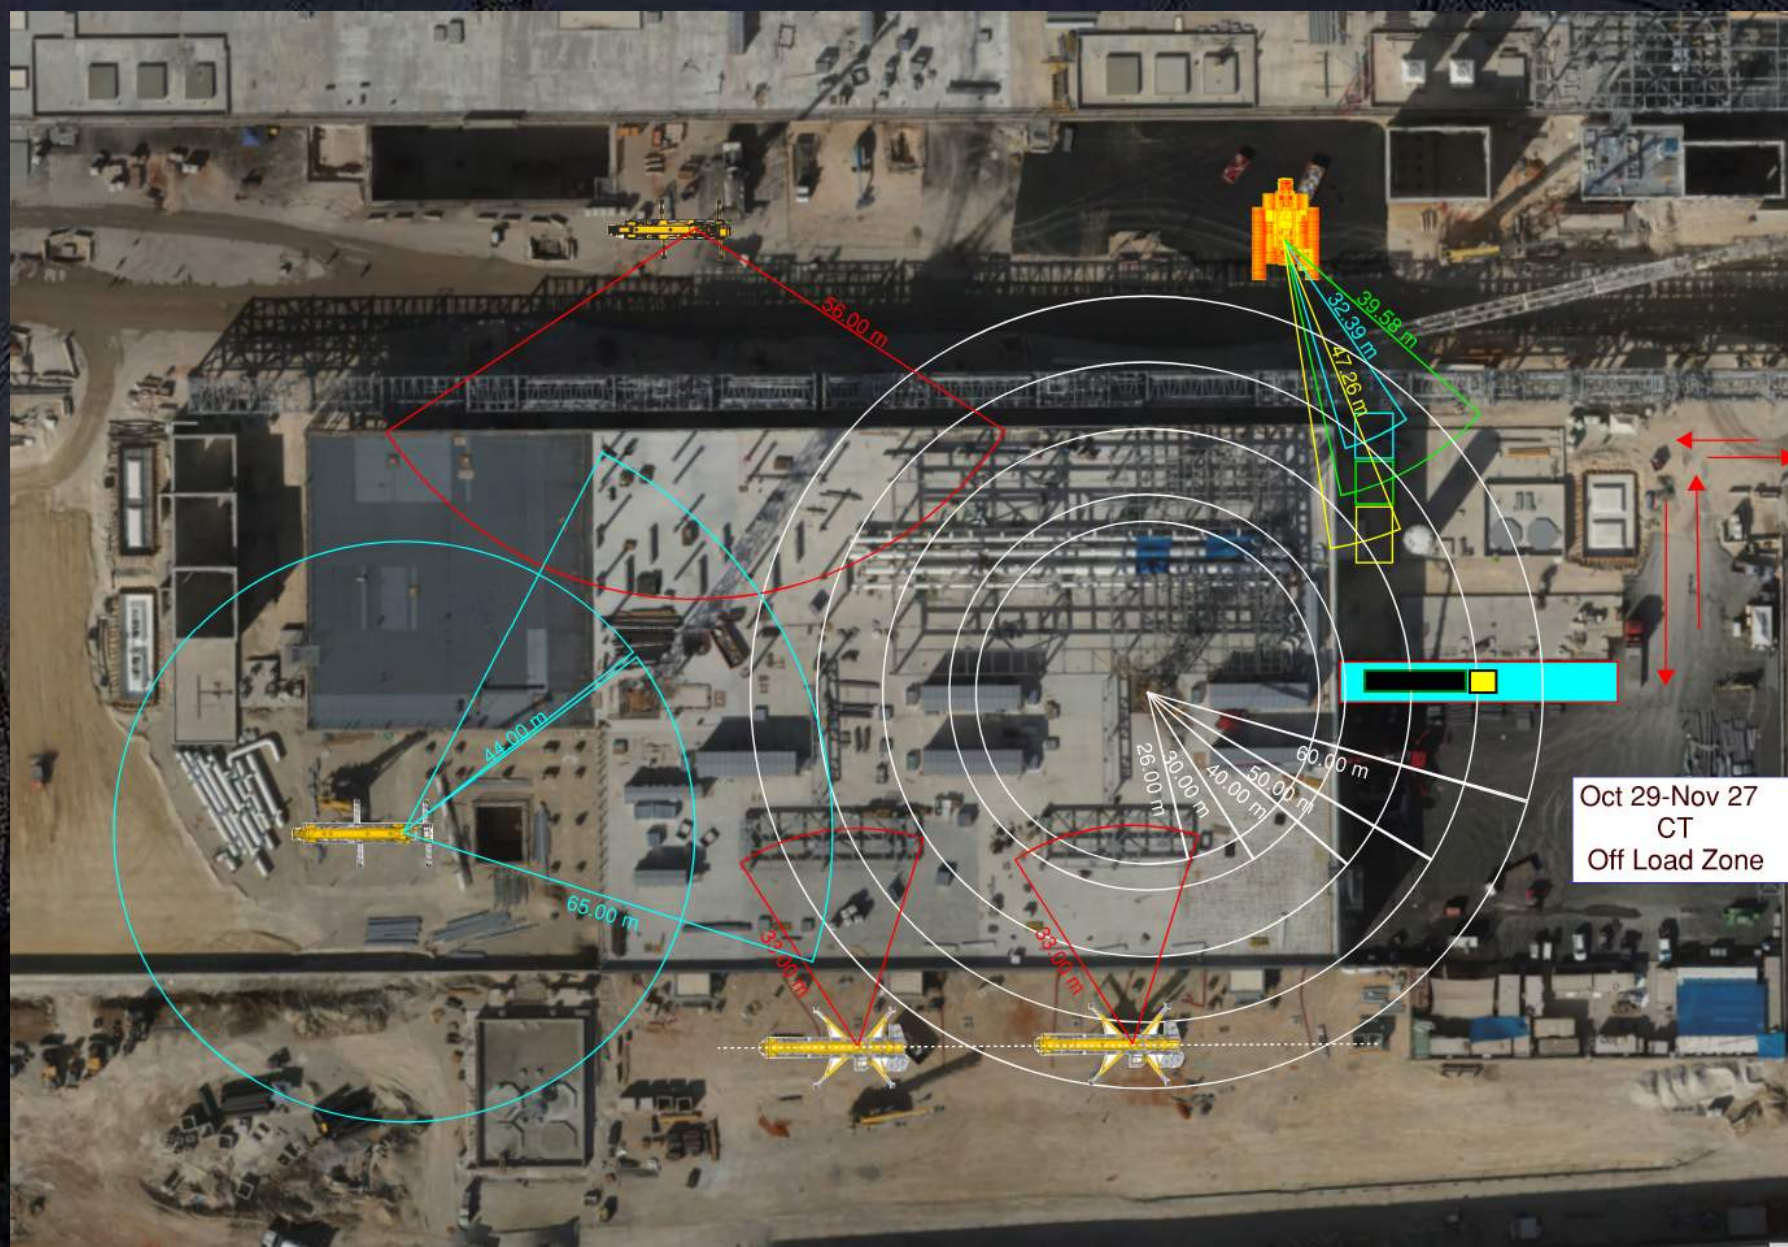




CUB 2 – Crane Logistics

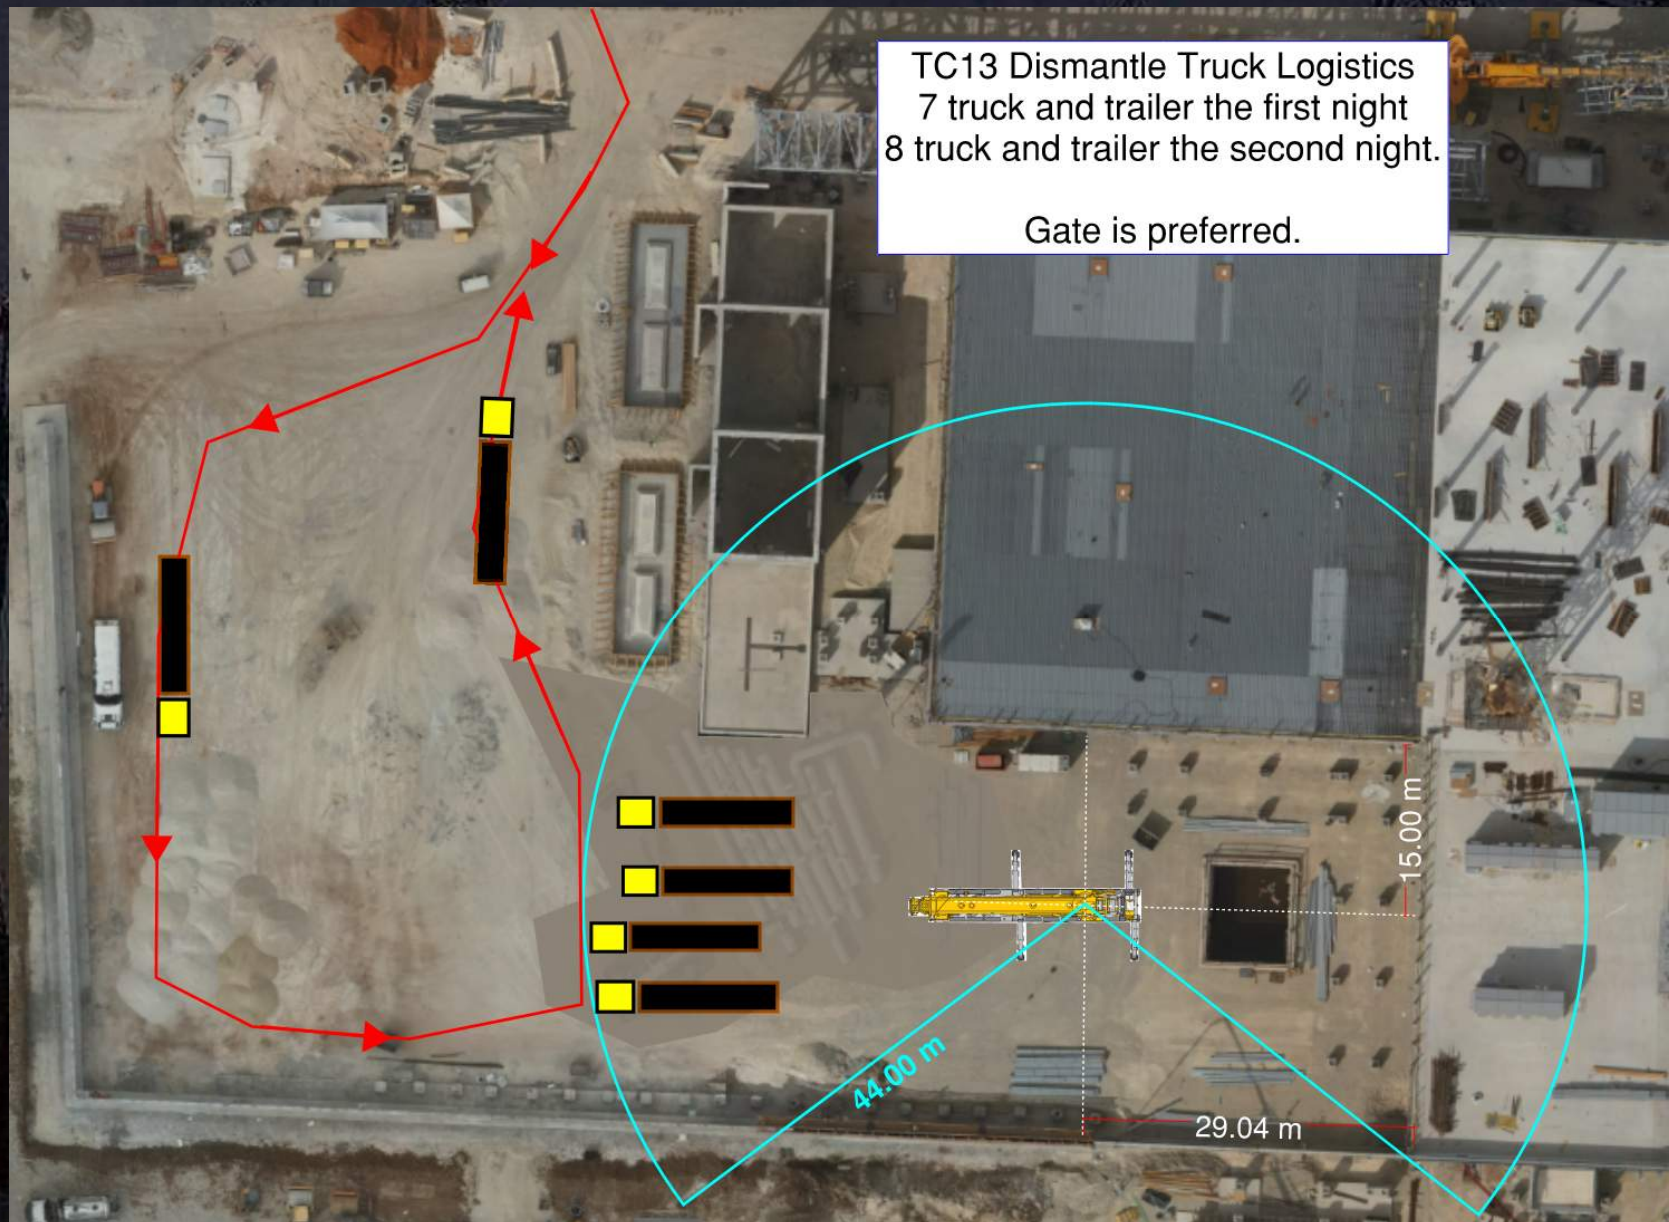



HOFFMAN CONSTRUCTION COMPANY

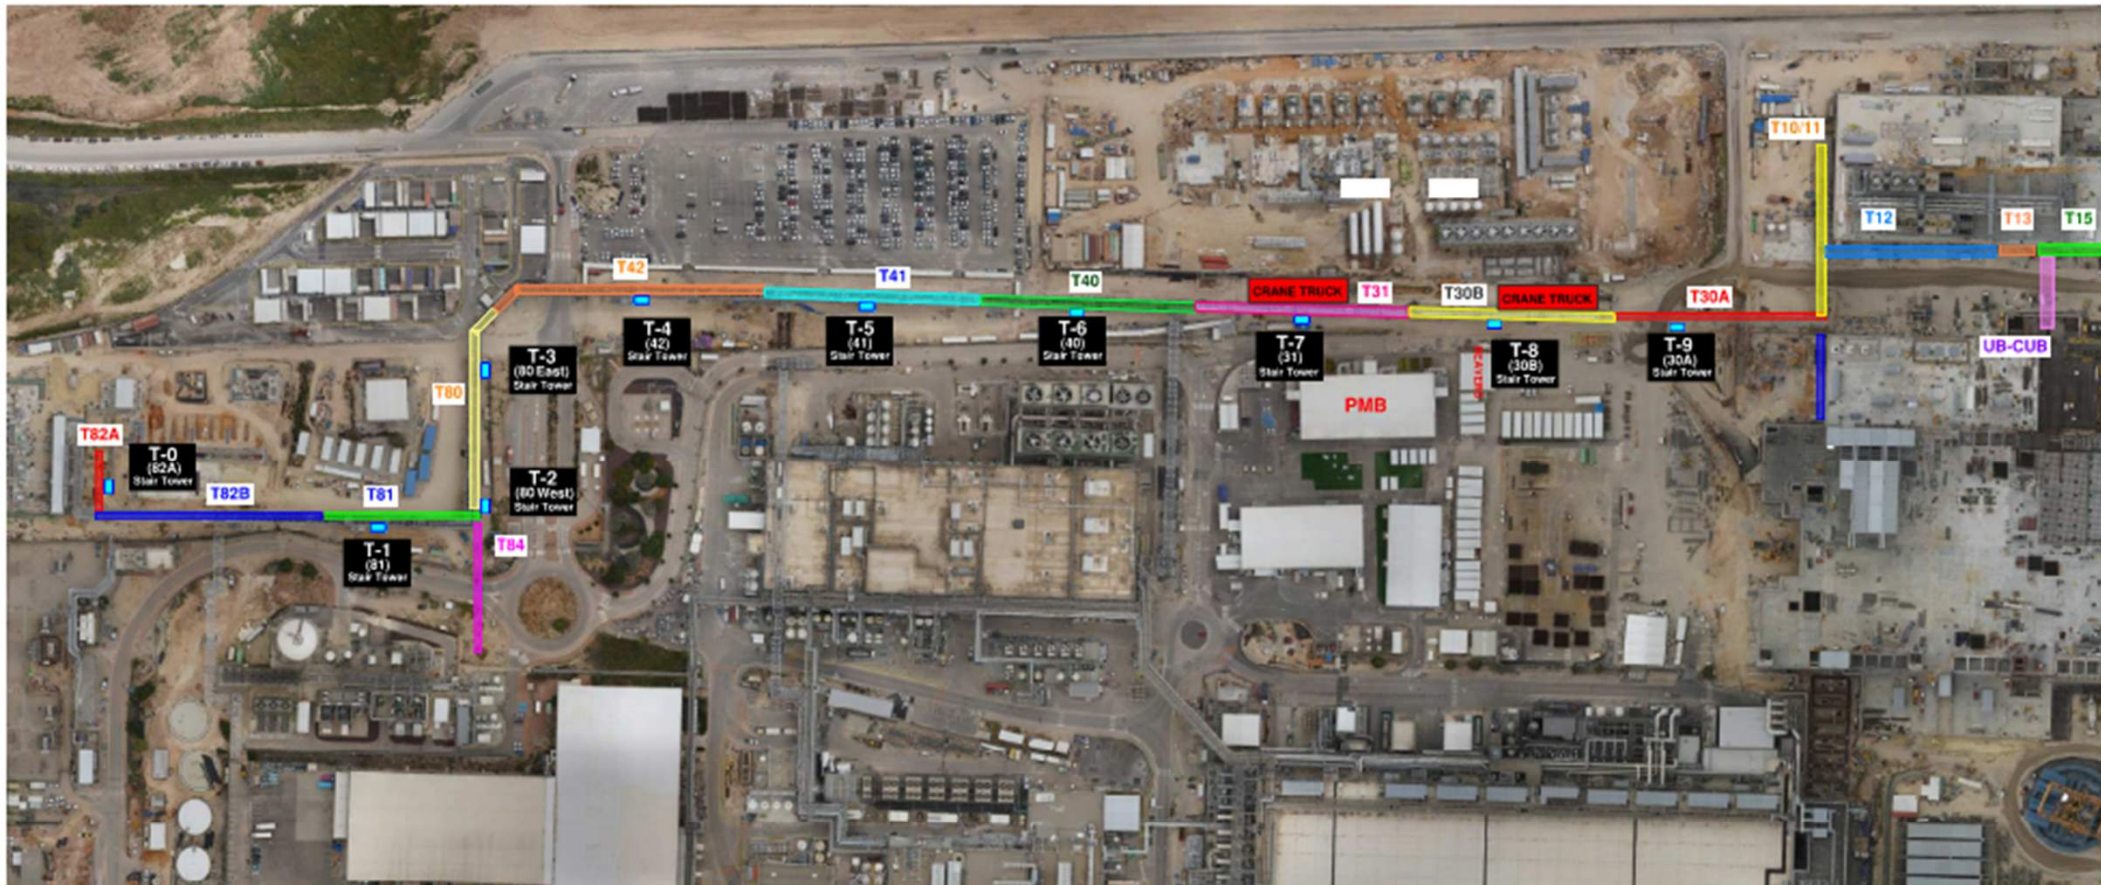

T18

CUB 2 - NOV 3th - NOV 11rh

nov 7th

nov 6th

nov 5th

nov 3th

nov 10th

nov 11th



5 m



Daily Coordination Meeting

Site Logistics

North






Daily Coordination Meeting

Site Logistics

South

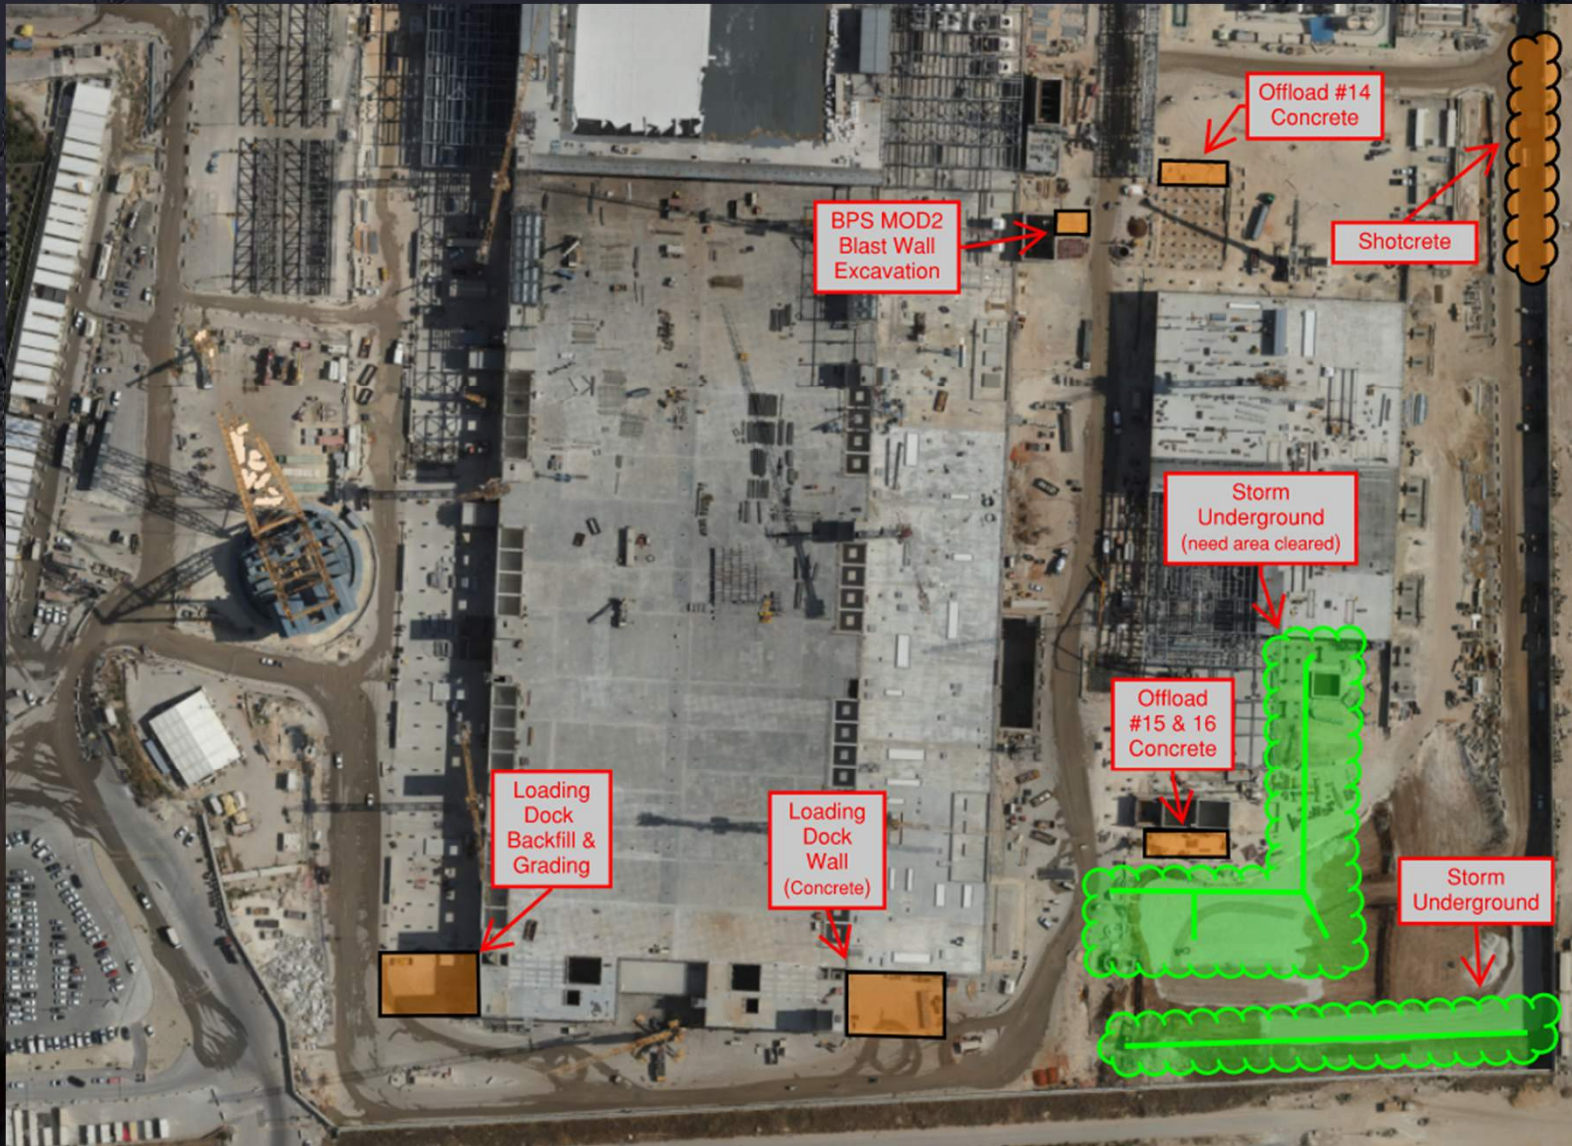

4 WAYS TO PREVENT SUICIDE:

1. Remove the stigma. We can't avoid talking about suicide if we hope that people will speak up when they need support.
2. Learn the warning signs. Pulling away from friends and family, giving up on themselves, feeling that they are a burden, and many more.
3. Learn how to reach out and connect. QPR (Question, Persuade, Refer)- suicide prevention training is available online as a one-hour course.
4. Know the resources.

ERAN's Suicide Prevention Hotline is available 24/7 at *1201, and their website also has a chat feature.

Crisis Text Line is available from 08:00 to 00:00 at 052-999-3544

TOUGH ENOUGH TO TALK

HCC/EHS Weekend Work- 27.09.2024

White Board Meeting in Beavers at 06:30

Superintendents

Brian Grevious 052-5394339

Igor Shuster 054-4743767

Josh Noll 052-5590653

Husein Abu Hammad 052-4106872

CSA CM

Tarek Nairoukh 052-6636782

Idan Turjeman 052-4093025

MEP

David Jollands 052-3961675

Andy Jollands 052-9659290

Paruic O'Reilly 052-3571665

OSM

CX/QA

Darryl Hicks 052-3215975

Cranes

Brady Prouty 052-6047531

Safety

Safety Foreman- Adir Elmakayes- 054-7254767 Adir-Elmakayes@Hoffmancorp.com

Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com

Safety Officer - Arkady Gerber-050-6851432 Arkady-Garber@Hoffmancorp.com

Subcontractor Weekend Work- 27.09.2024

FAB

UTILITY LEVEL

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

EIram

Foreman: Shlomo

0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

Pach Taas

Perim Rack Aae

Team Lead : Nuriel 0549012324

Afcon E

PA/Stairs

Team Lead : Avi Eli 0526008487

Chemo

TTNW

Team lead: Tommy 0523759408

Safety: Lilah 0547886704

Belfor

TTNE / TTNC

Team Lead: Salame 0546651886

HYG

SF Zones 3- White steel touchups/Mamad plates weld/

Stair # 8

Salah 0507773119

WW Steel

Elevator 3

Teddy 0522392473

Clean Room

W&W 17-18 Line added the beams 10-24 line – catwalks, MOD2: steel fan deck east west, infill ongoing (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)

Talad – CR 1W – Drilling holes, 1 metal lids removal (EHS Guy 0544915407, Super Igor 0544509386)

Sig – 5W INT Platforms MIMO CB-CC/25 (EHS Beni 0506232032, Super Nodar 0546313261)

EIram – CR Level 9,25 line, AA line 2W shafts walls INT level 9,10,17,24 column wrap (EHS Royi 0538312234, Super Bonio 0544236899)

Afcon – CR – 2E-5E, 2W-5W, INT- 2E-3E, 3E-3W ,LINK Rack install (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Sela – 1E-AB-AK/10-12 CRC (EHS Shmuel – 0506306031, Supervisor Yuval 0502649246)

Subcontractor Weekend Work- 27.09.2024

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2, and EPA Platform
1&2P

Foreman – Vadim – 052-6229005

Safety – Offek – 050-7838486

Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-
2P Roof & Lift 2

Foreman – Charles – 055-2740190

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-4P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

W&W – SEQ 135, 137

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Elram – 5P Corridor, UPW Ceiling

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

Lesico – 5P UN2 Welding

Foreman – Selvin – 052-4787370

Safety – Itay – 054-2336103

Combe UPW – UPW Room Piping and Yard

Foreman – Boris – 054-8346412

Safety – Abed – 052-5148747

SNJ Flashing – BPS Roof

HSAl – BPS Blast Walls

Foreman – Dave – 052-4121028

Safety – Sam – 052-5259268

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcela – 054-5210133

Safety – Marzuke – 054-447-7112

WJG

Pach Taas

Adiv Pereg- EHS

Netanel Ivgi – Forman

Siding

SAMI NAJAMI -ROOF METAL

SAMI NAJAMI -PANTRETION

SAMI NAJAMI -GERTZ

Victor 0549220163

Subcontractor Weekend Work- 27.09.2024

CUB

Sami Najami CUB 2:

Husein - 0526917461

Alon - 0509895008

Meptagon I+C:

Raziel - 0584360845

Netanel - 0538398999

Pach Taas:

Adiv - 0506909390

Nati - 0543301880

ETC south yard:

Yosef - 0506708990

Leonid - 0545991846

S.K.E:

Reynato - 0548991623

HSAI

Chemo Aharon:

Dudu - 0509808846

Leonid – 0548883878

Date: 27 September 2024

Dayshift Working time 07:00 to 19:00

CUB1

1.SOMSAK PAKPANUPAT, AC5253797, TEL 054-8112261 (Leader)

Nightshift Working time 19:00 to 07:00

CUB1

1.SARAWUT KHRUEASING, AC5094850, TEL 052-3628607 (Leader)

Date: 28 September 2024

Dayshift Working time 07:00 to 19:00

CUB1

1.SOMSAK PAKPANUPAT, AC5253797, TEL 054-8112261 (Leader)

Nightshift Working time 19:00 to 07:00

CUB1

1.YOTSAWAT

Trestle

SNJ:

PIPES –UB CUB

ISOLATION –UB CUB

STEEL

FORMAN- BASHIR YONES - tel. 05273649963

SAFETY TRESTLE-Alon Matan tel. +972 50-989-5008

Site

Derech Afar – Shotcrete, Storm water bypass at Sarens & Fire protection water

Supervision = Raed: 054-2442030

EHS = Alex: 054-5403849

Olizki – Sweepers and water trucks

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

TM Team – LSS underground

Supervision = Nadav: 052-5893171

EHS = Alon: 054-7711469

GIS/NEY

Daily Coordination Meeting



14:00 Sign In
