

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting


General Topics:

- See something, say something






UTILITY LEVEL TRUSS

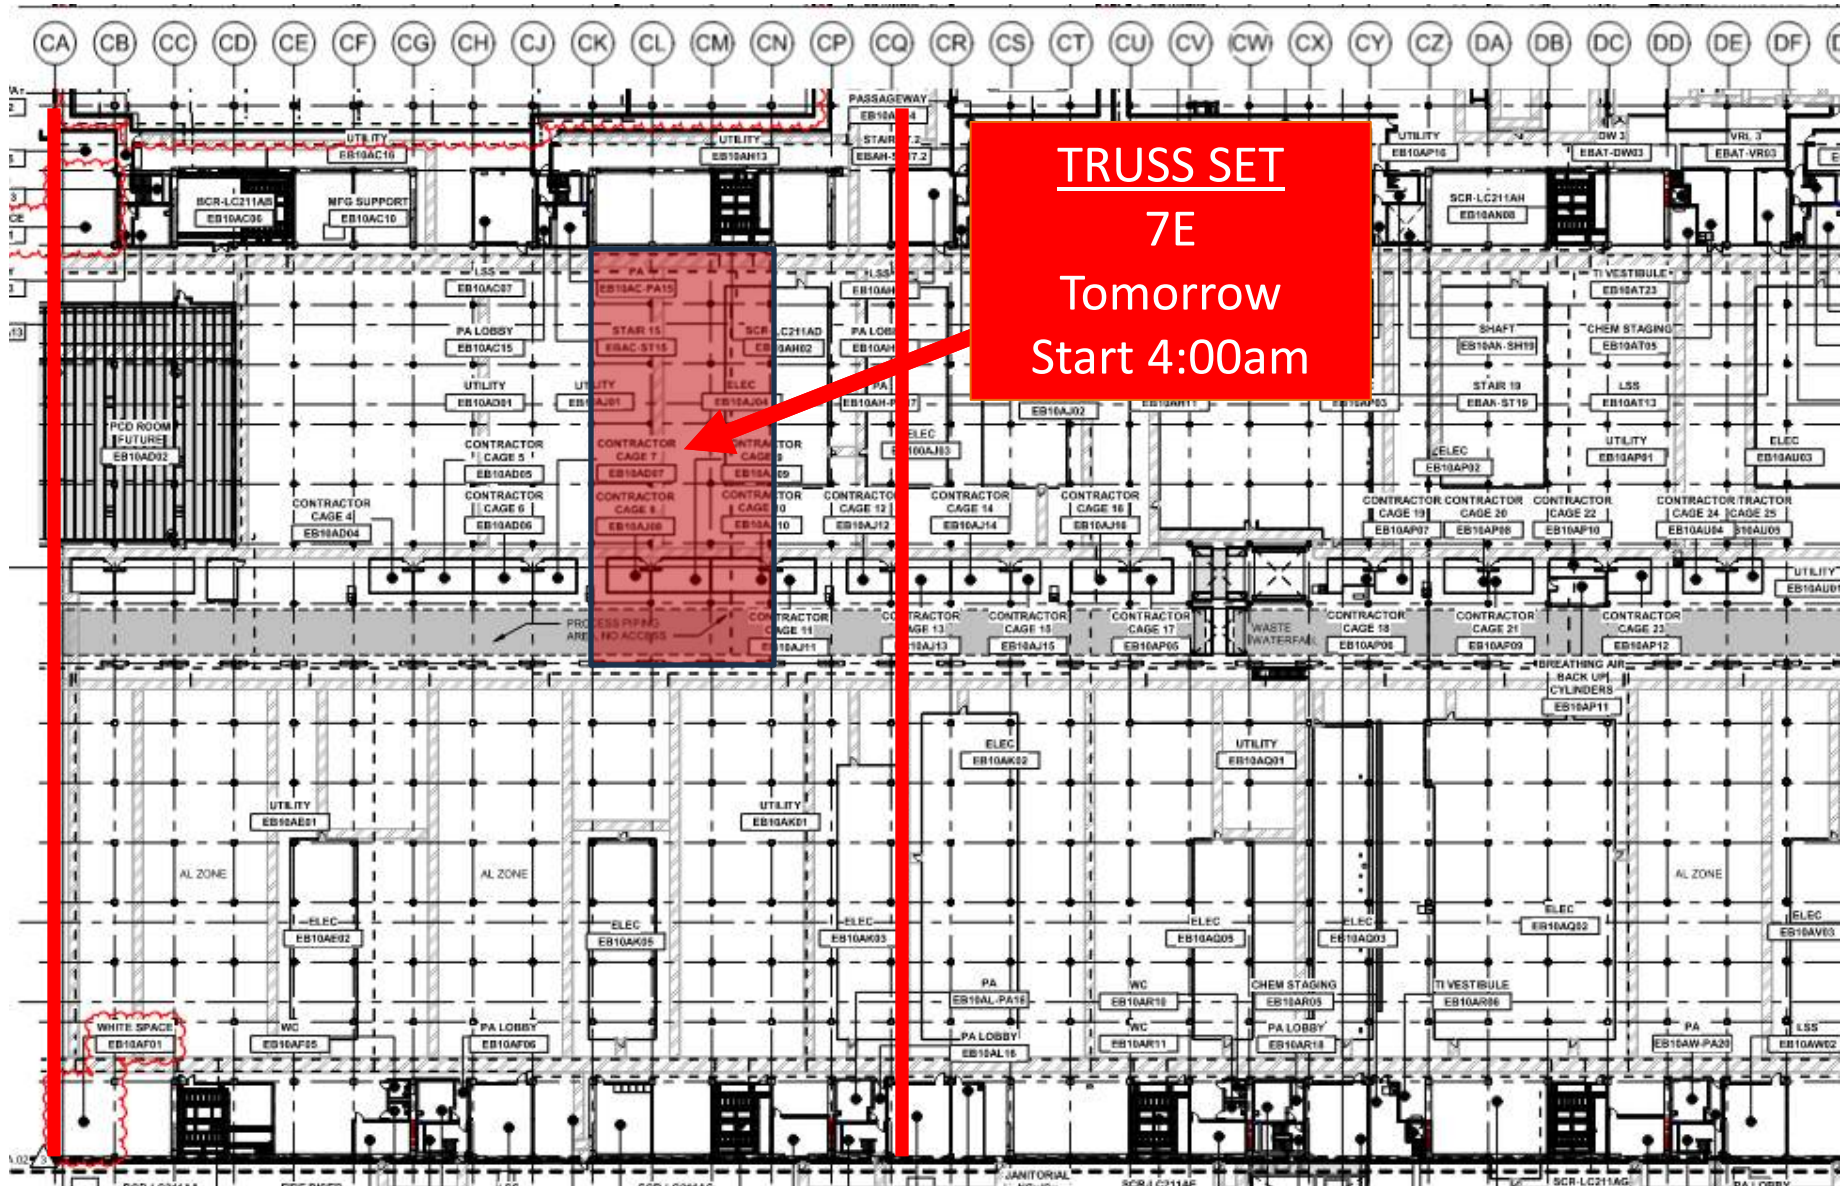



UTILITY LEVEL MOD1

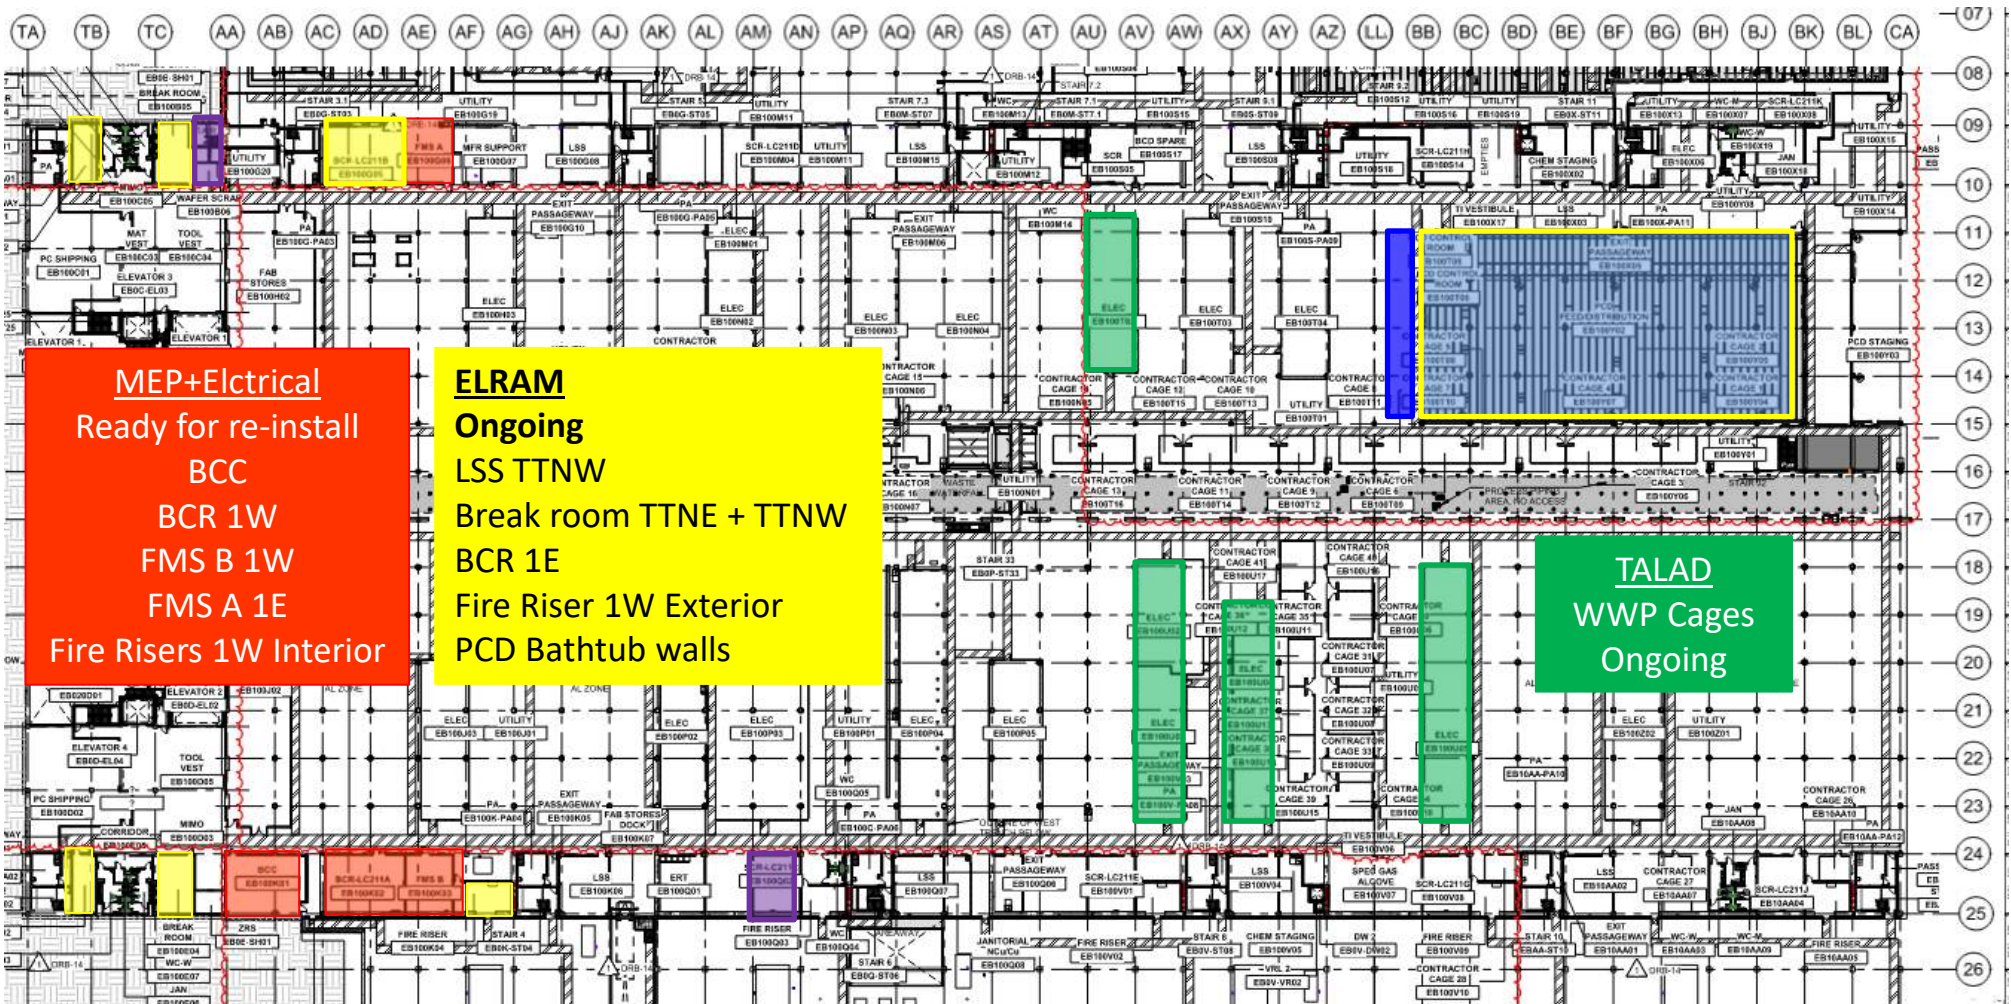


MEP+Electrical
Ready for re-install
BCC
BCR 1W
FMS B 1W
FMS A 1E
Fire Risers 1W Interior


ELRAM
Ongoing
LSS TTNW
Break room TTNE + TTNW
BCR 1E
Fire Riser 1W Exterior
PCD Bathtub walls

TALAD
WWP Cages
Ongoing

UTILITY LEVEL MOD2

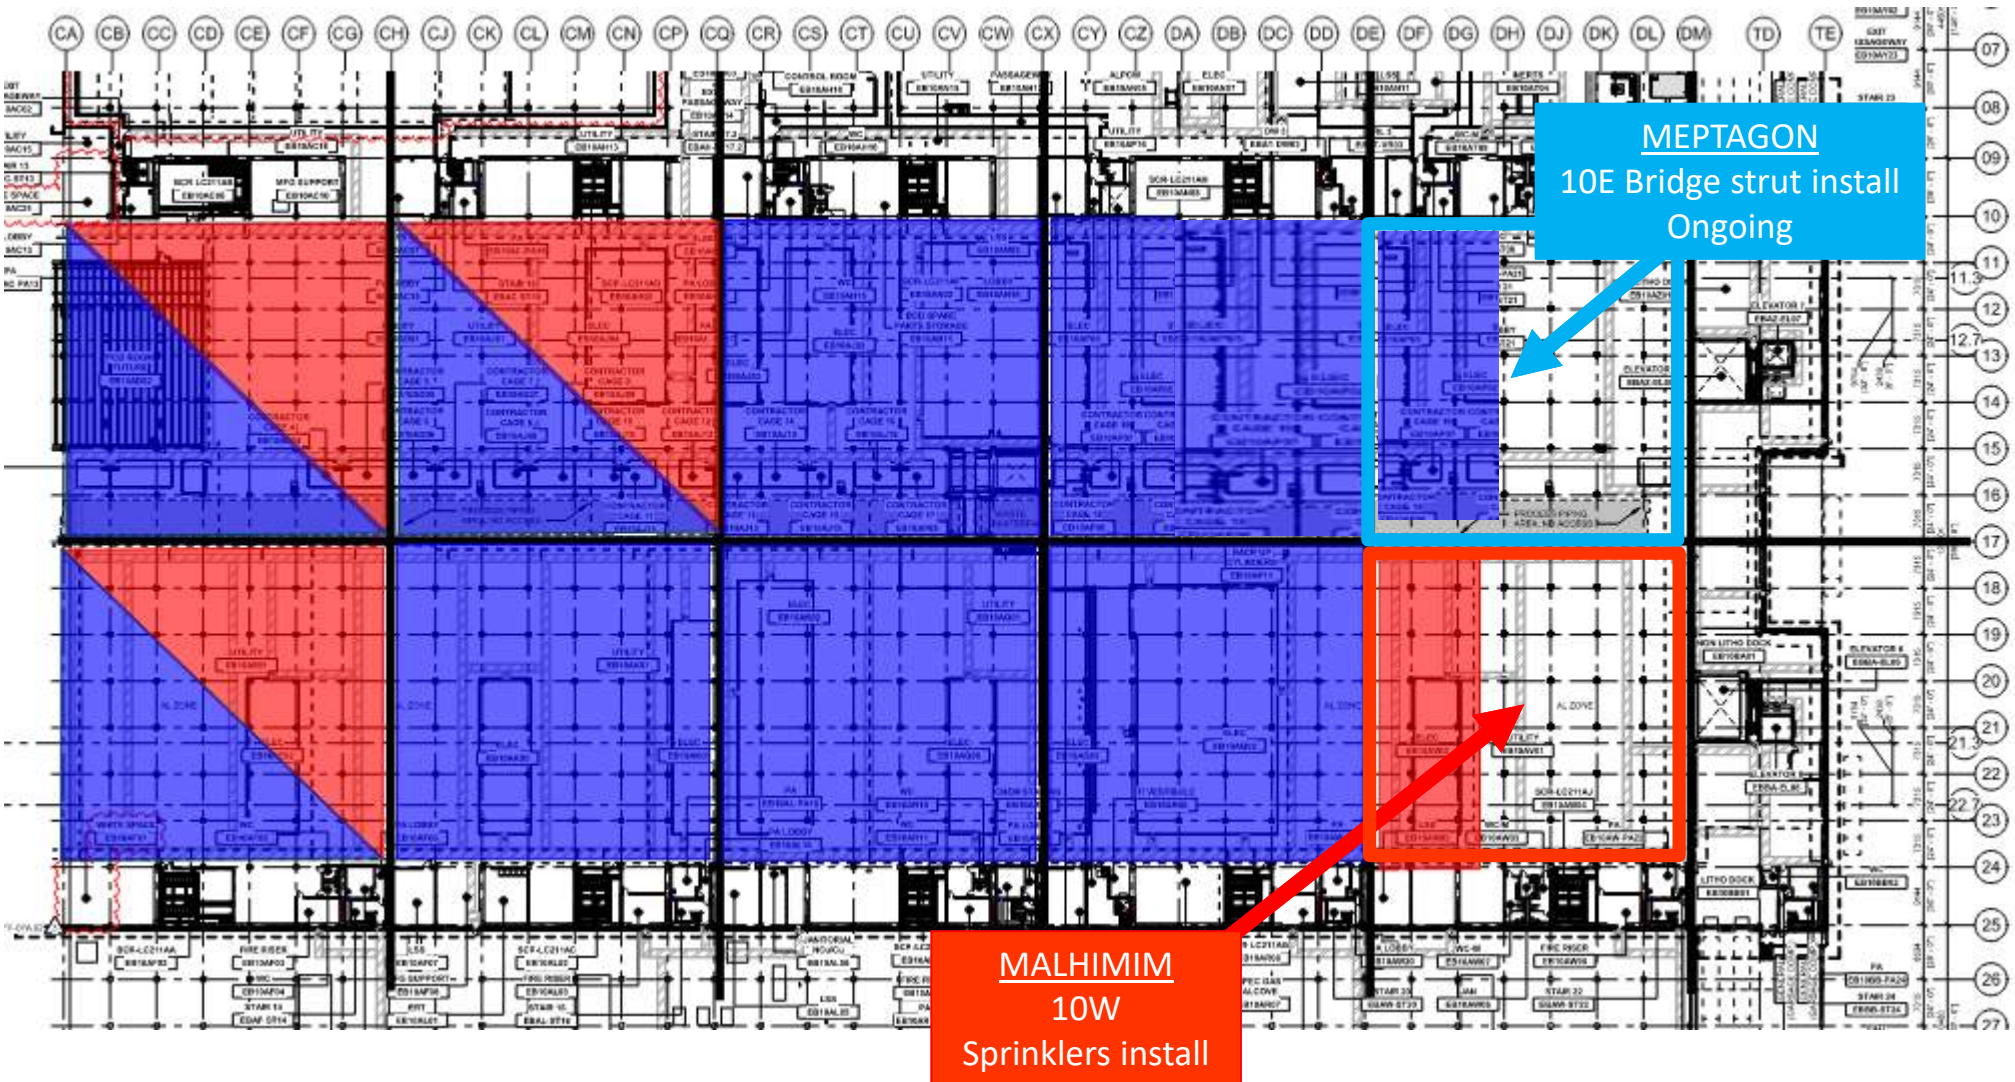


SUT 38.1 LEVEL

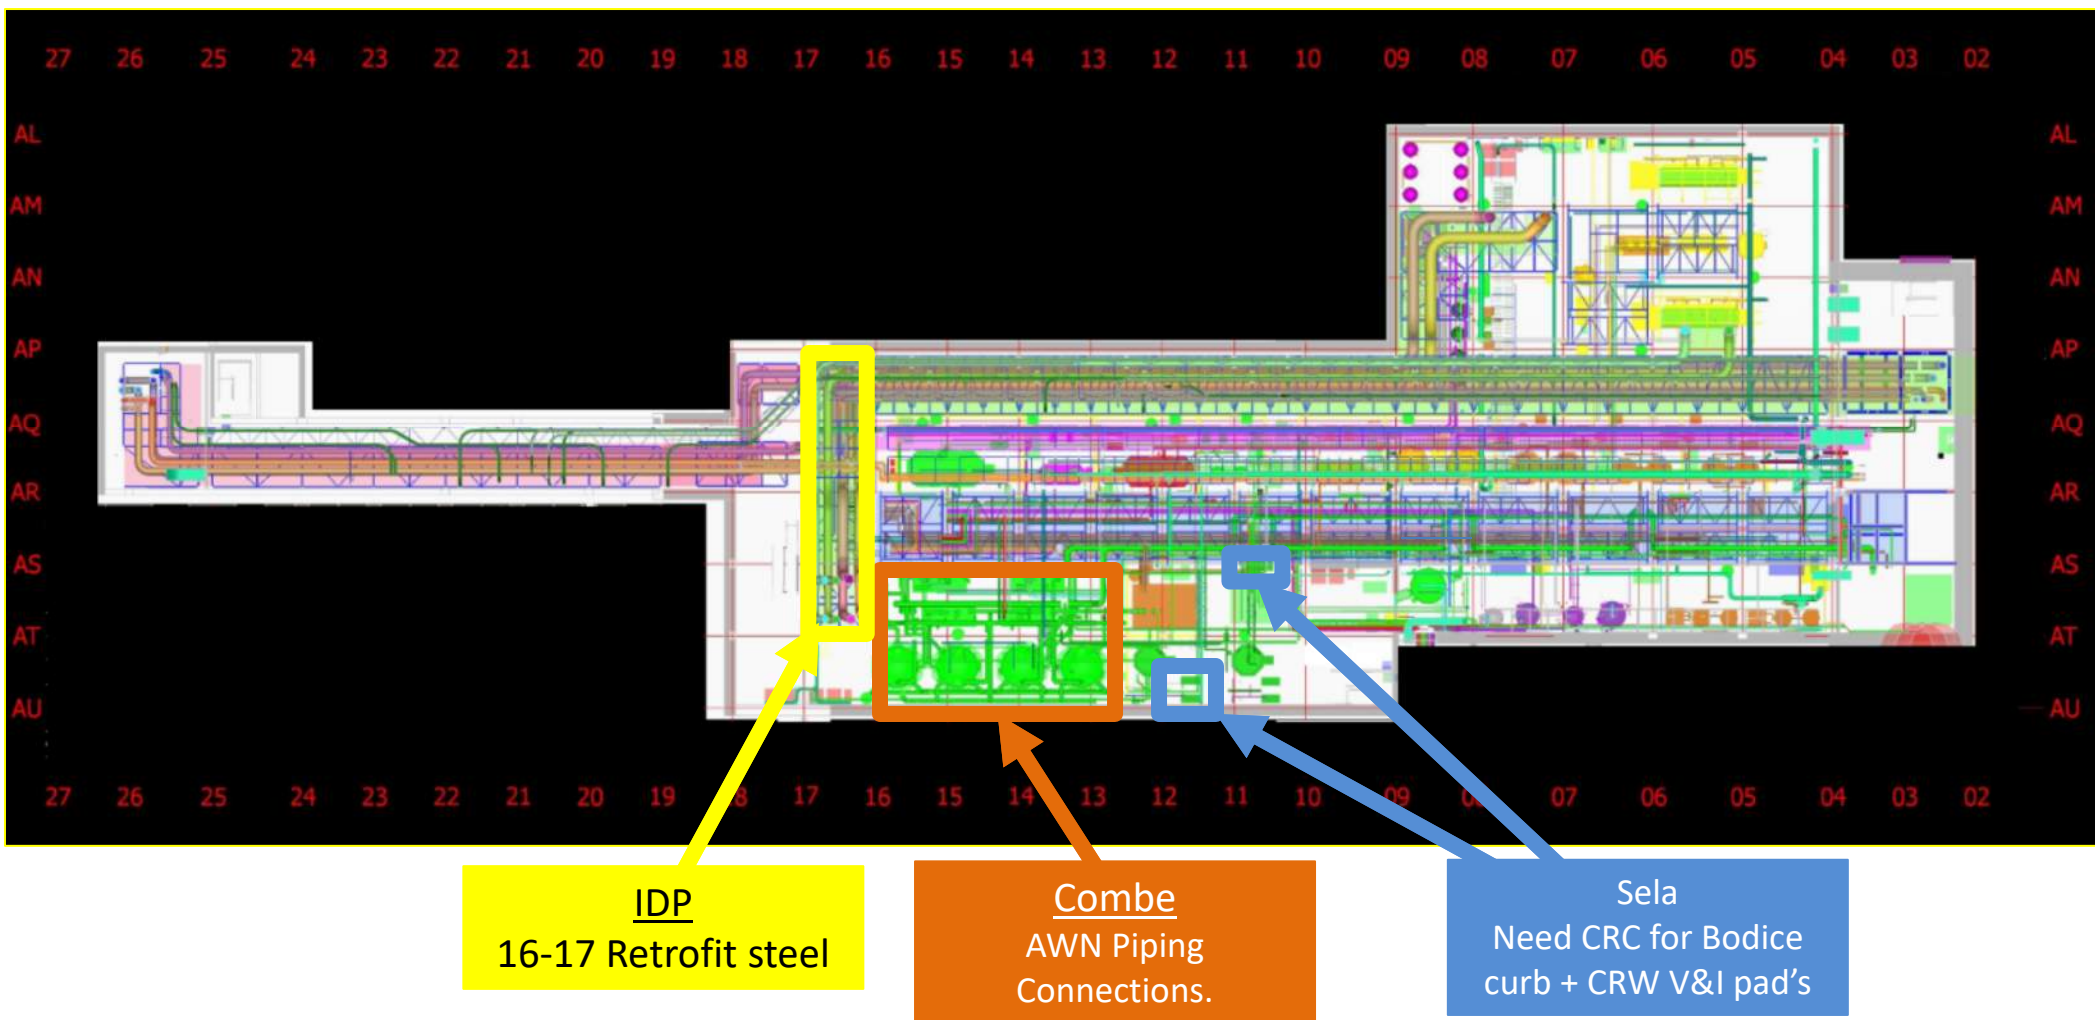



SUT 38.2 LEVEL

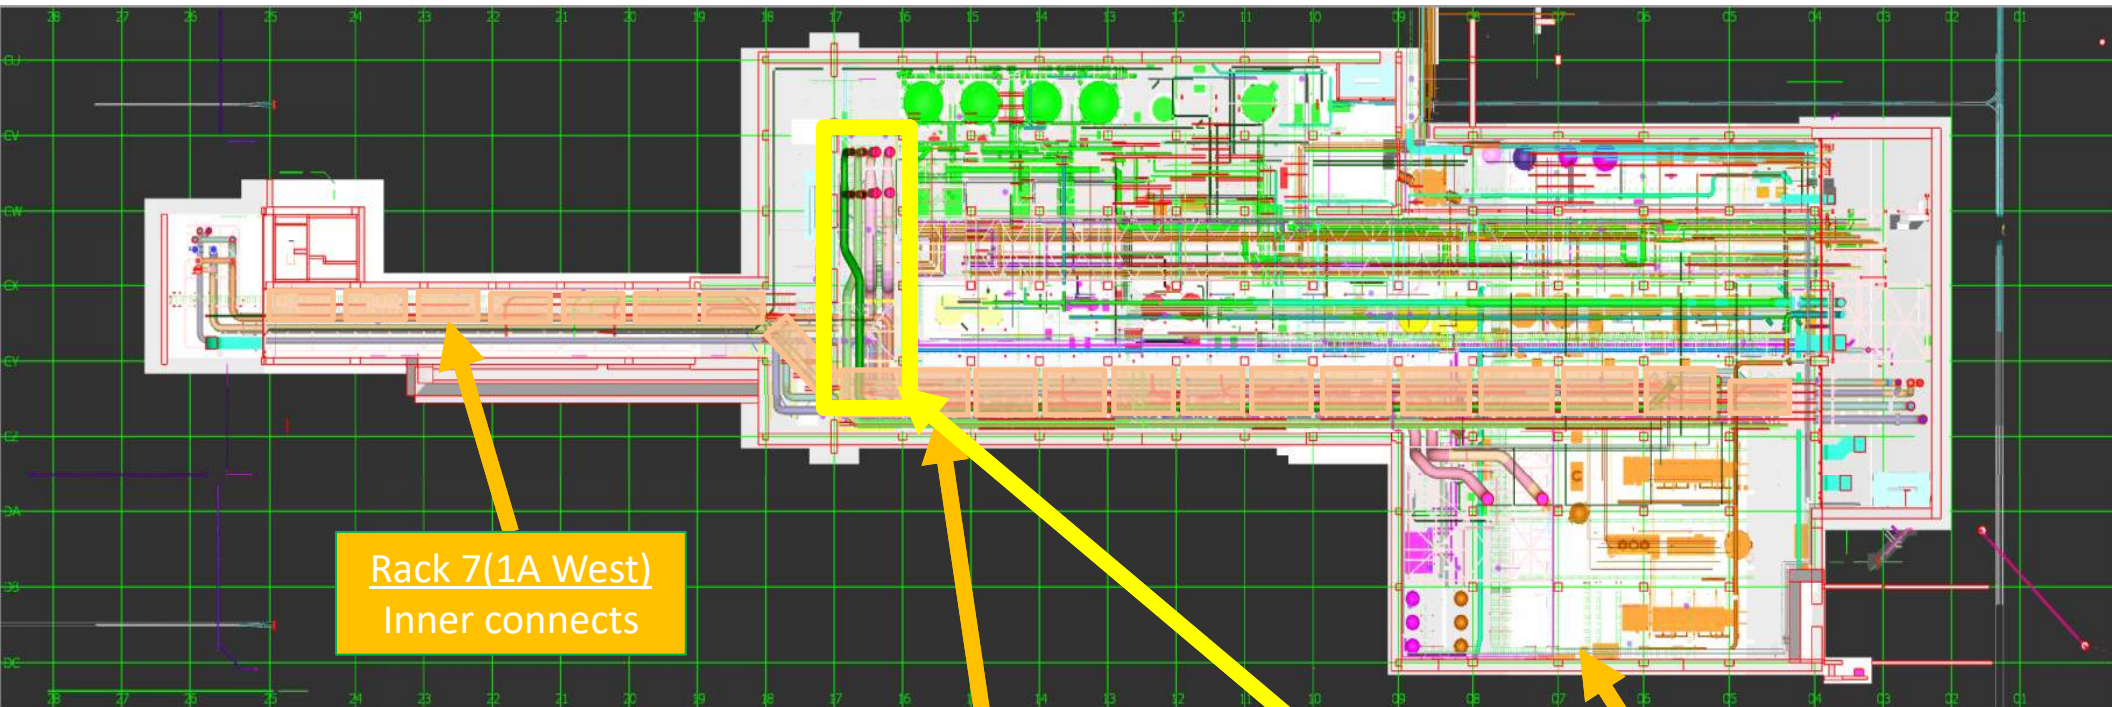

Rack 7(1A West)
Inner connects

1A Rack
Inner connects


16-17 line
Upper Steel Bed
build

8 Rack
Lifting


CRW
H&T
Installing supports

Vesda
H&T
Not actively installing

SUBFAB BUILDOUT MOD 1

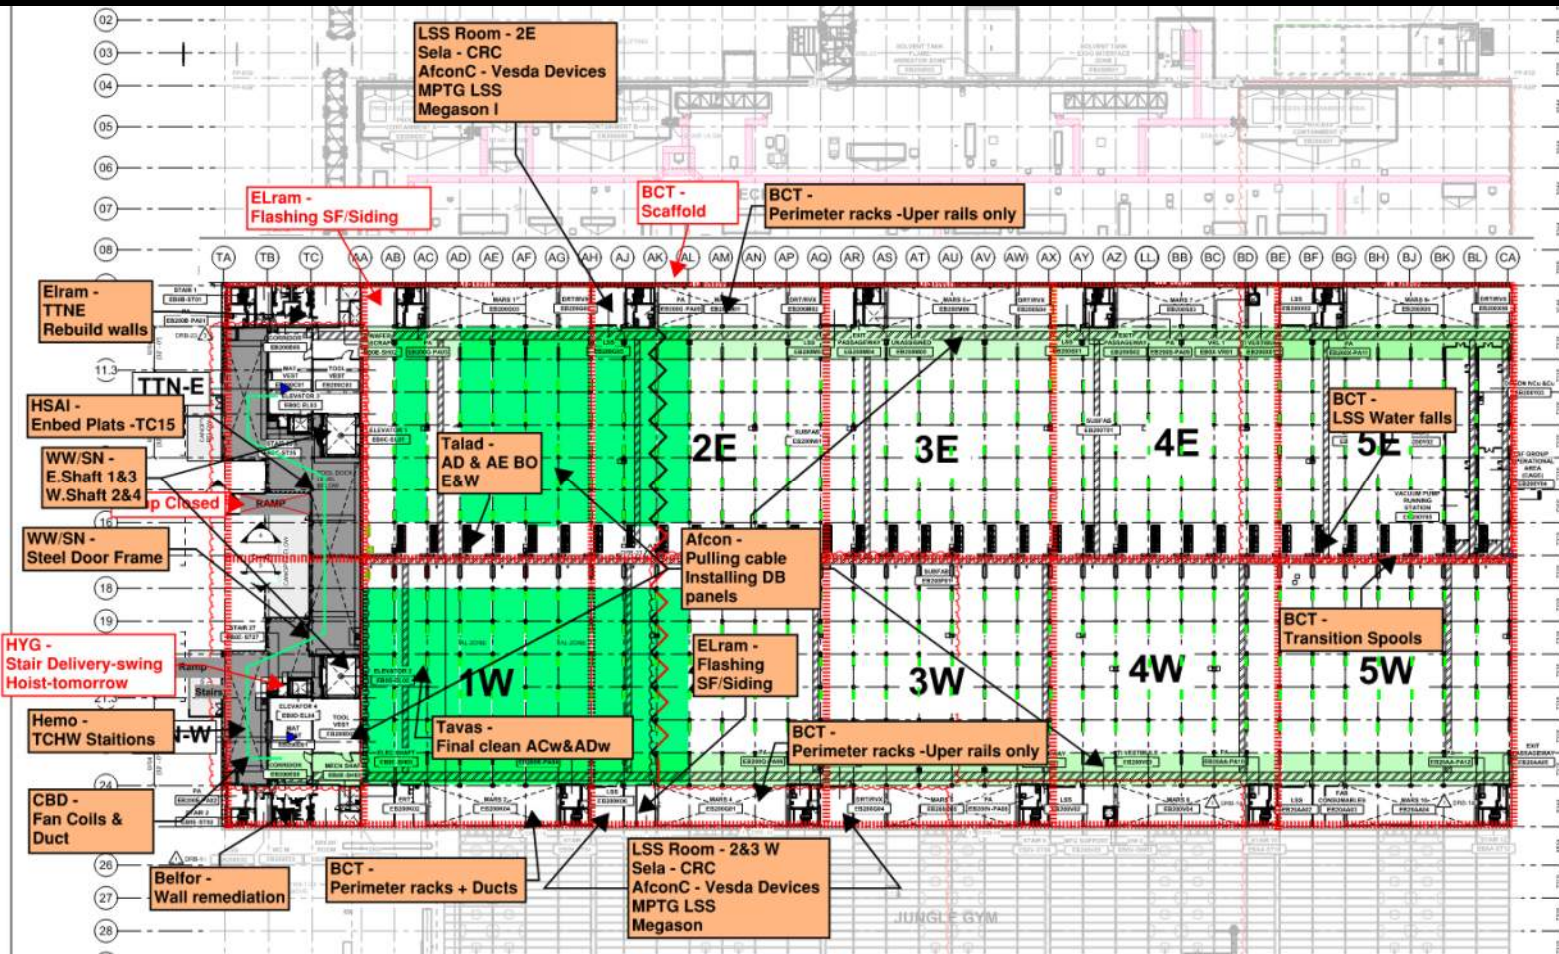


SUBFAB BUILDOUT MOD 2

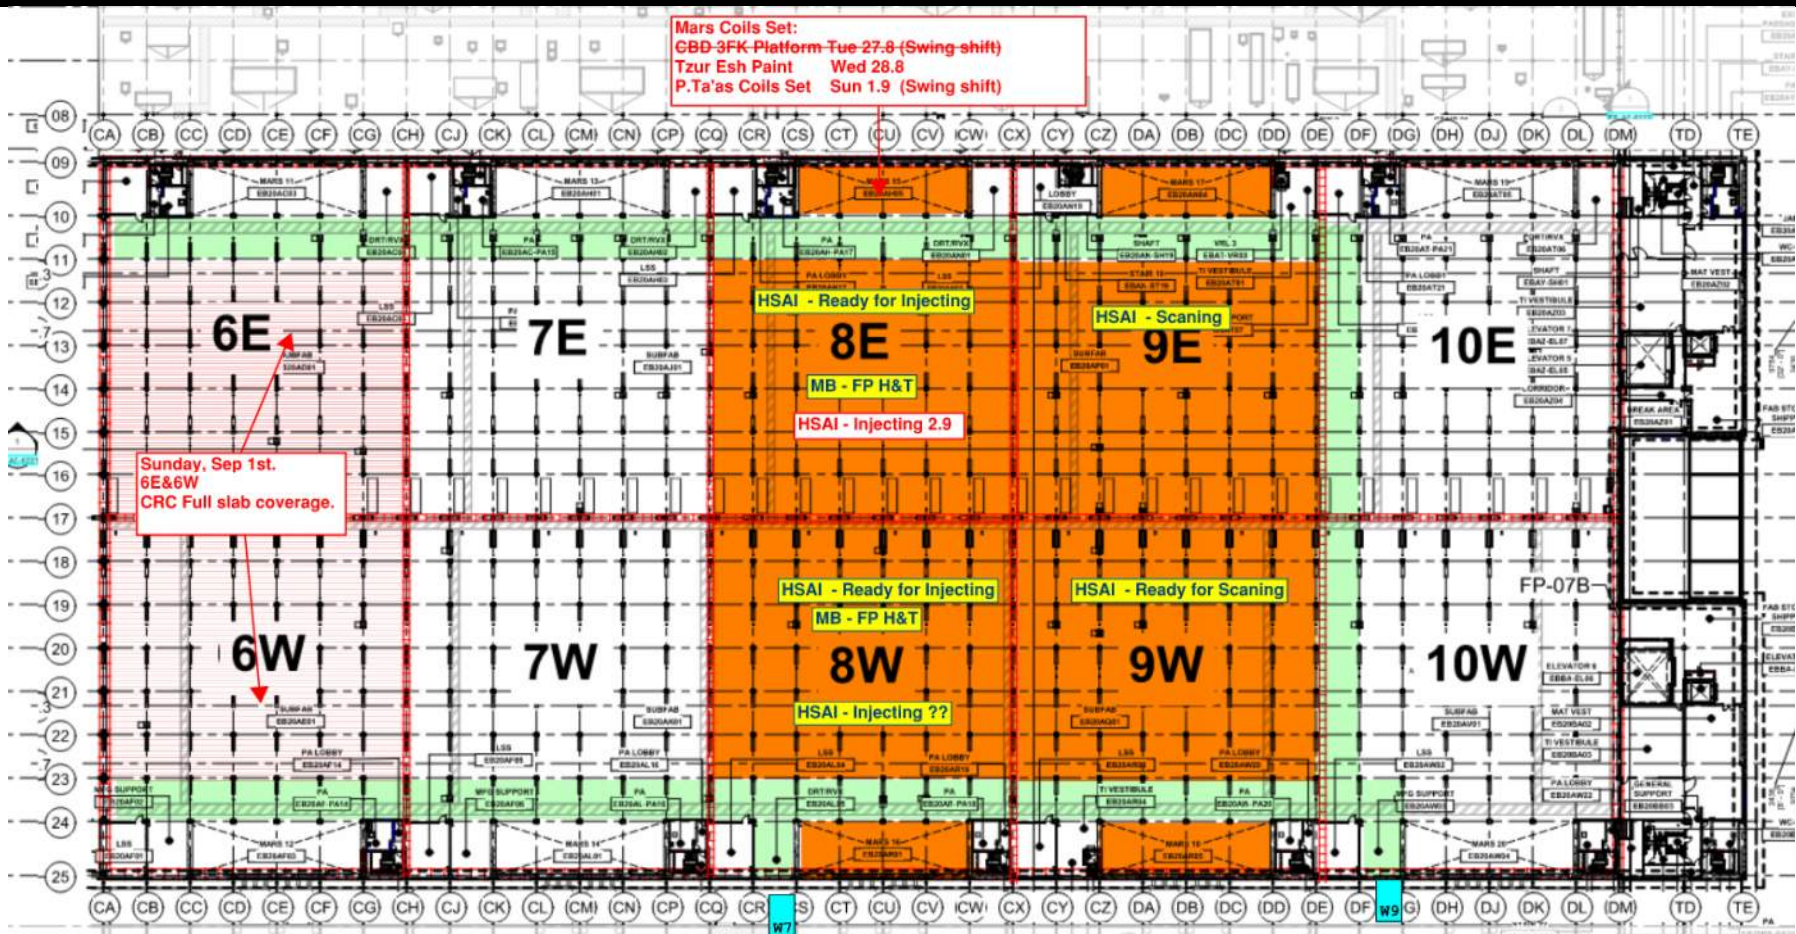



BAY:AB(e)
Line:LCHe
Size:1/2"


BAY:AC(e)
Line:LCHe
Size:1/2"

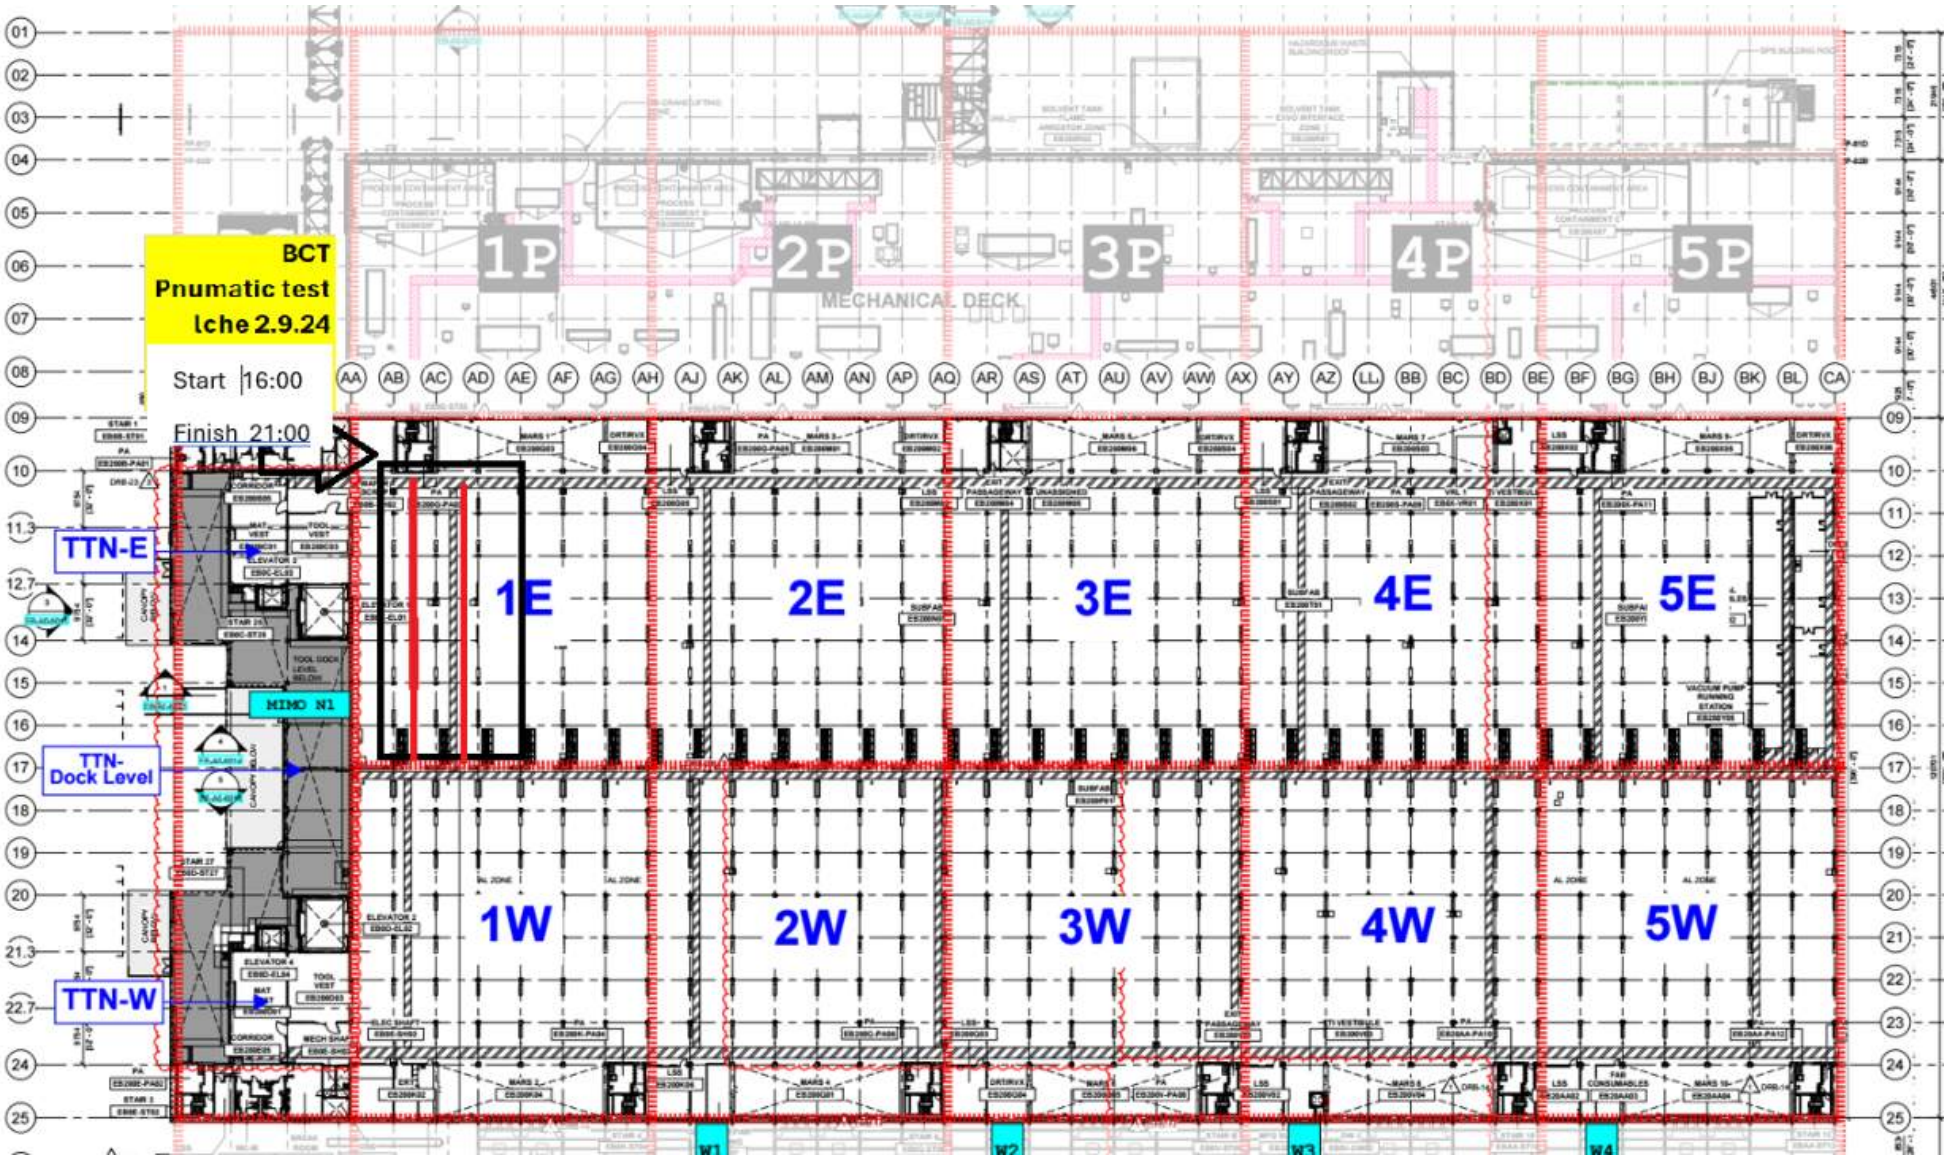

SUBFAB CRC TOPCOAT

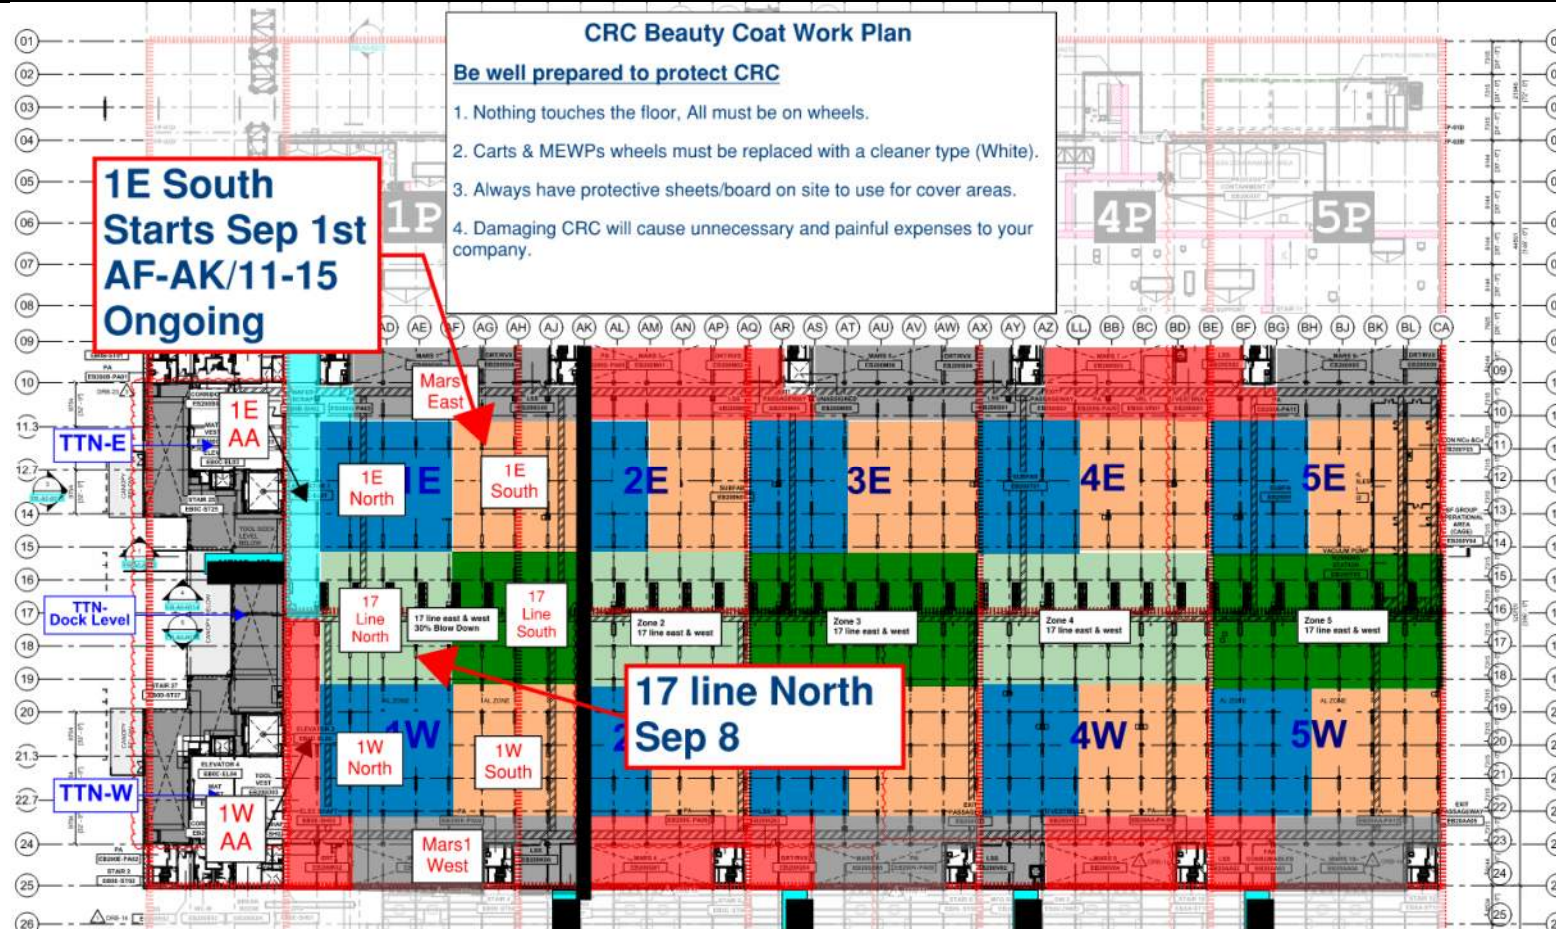


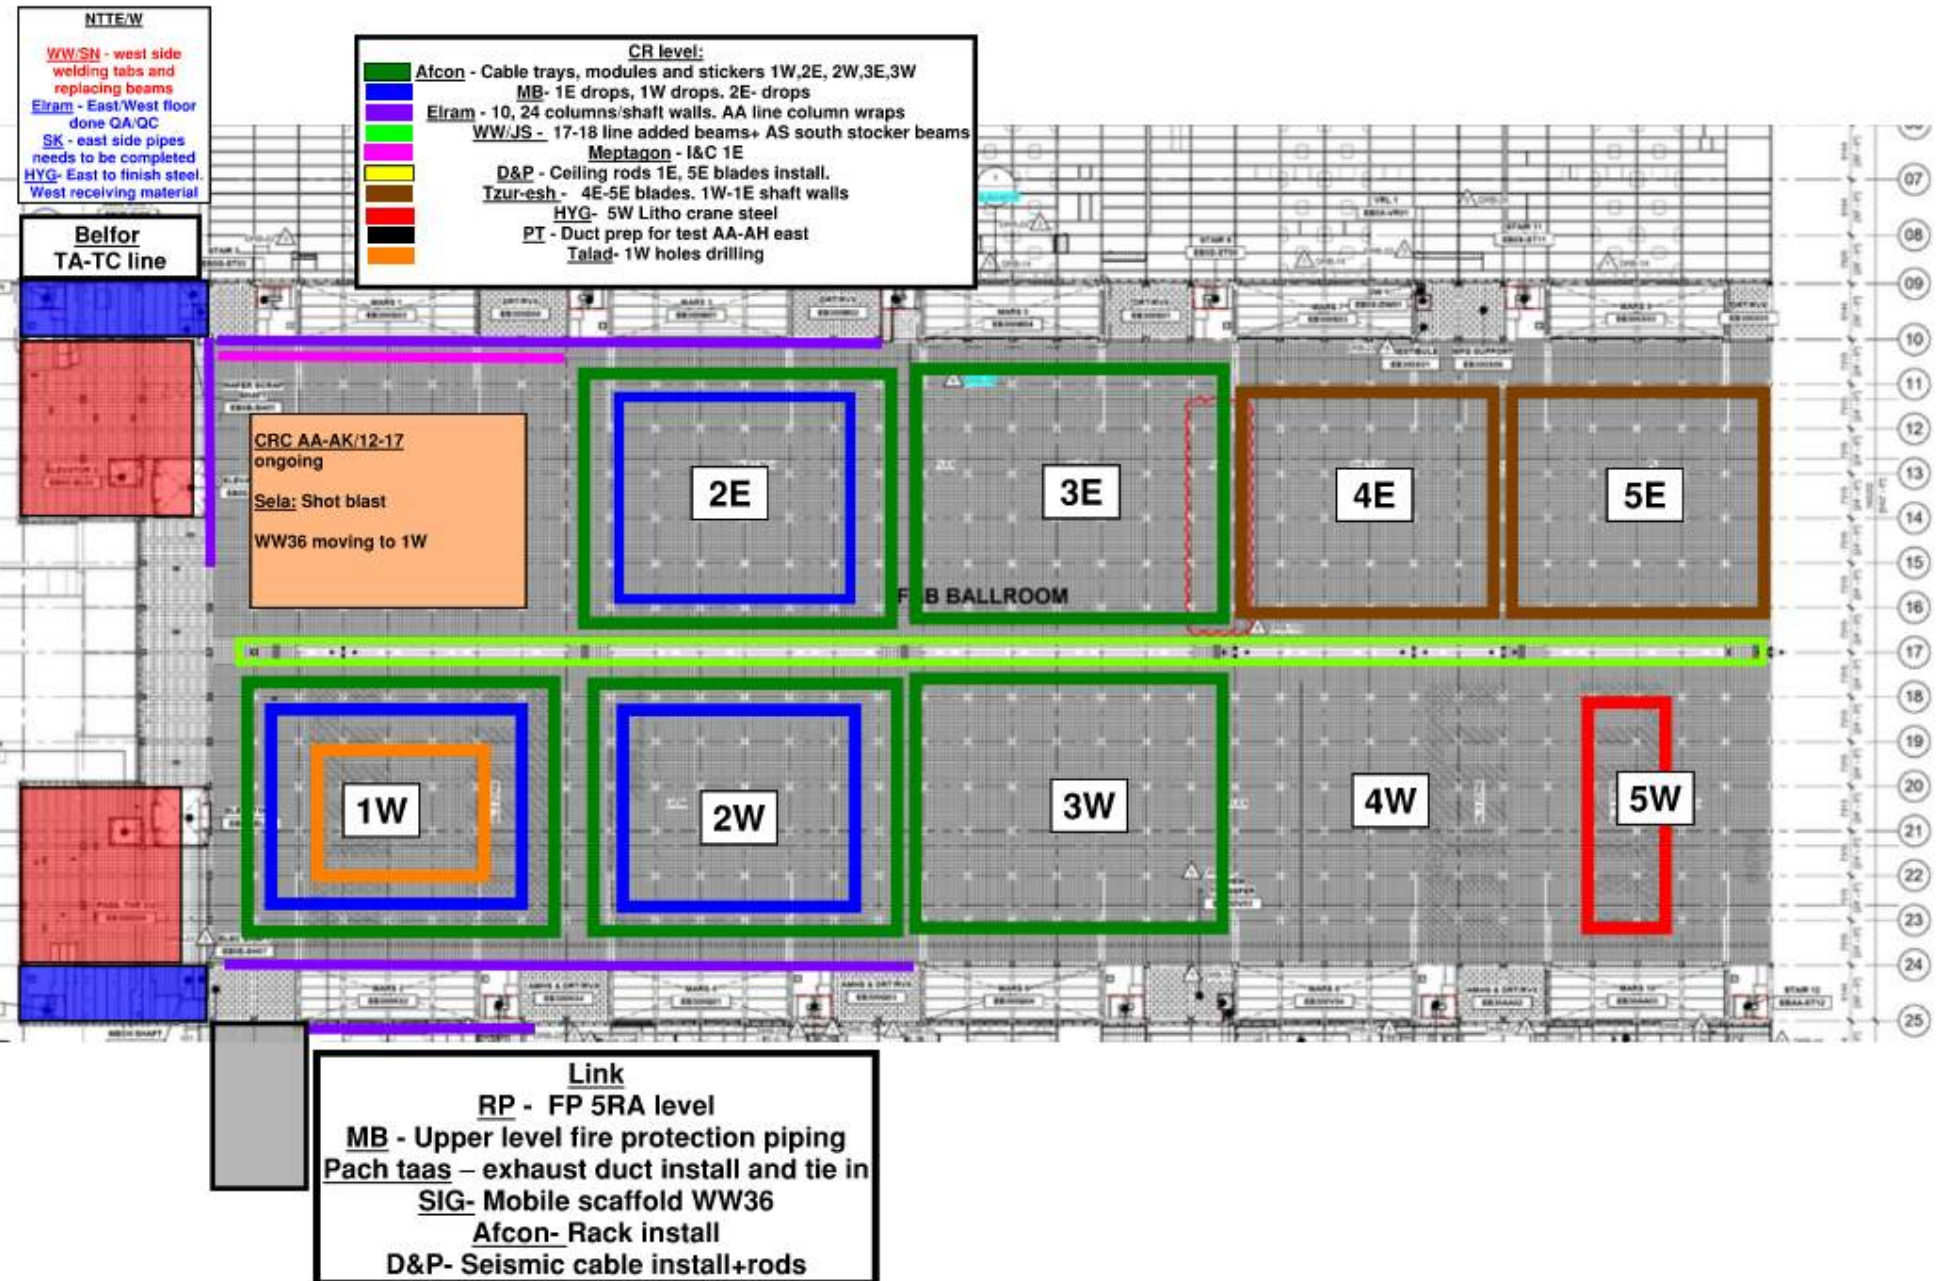


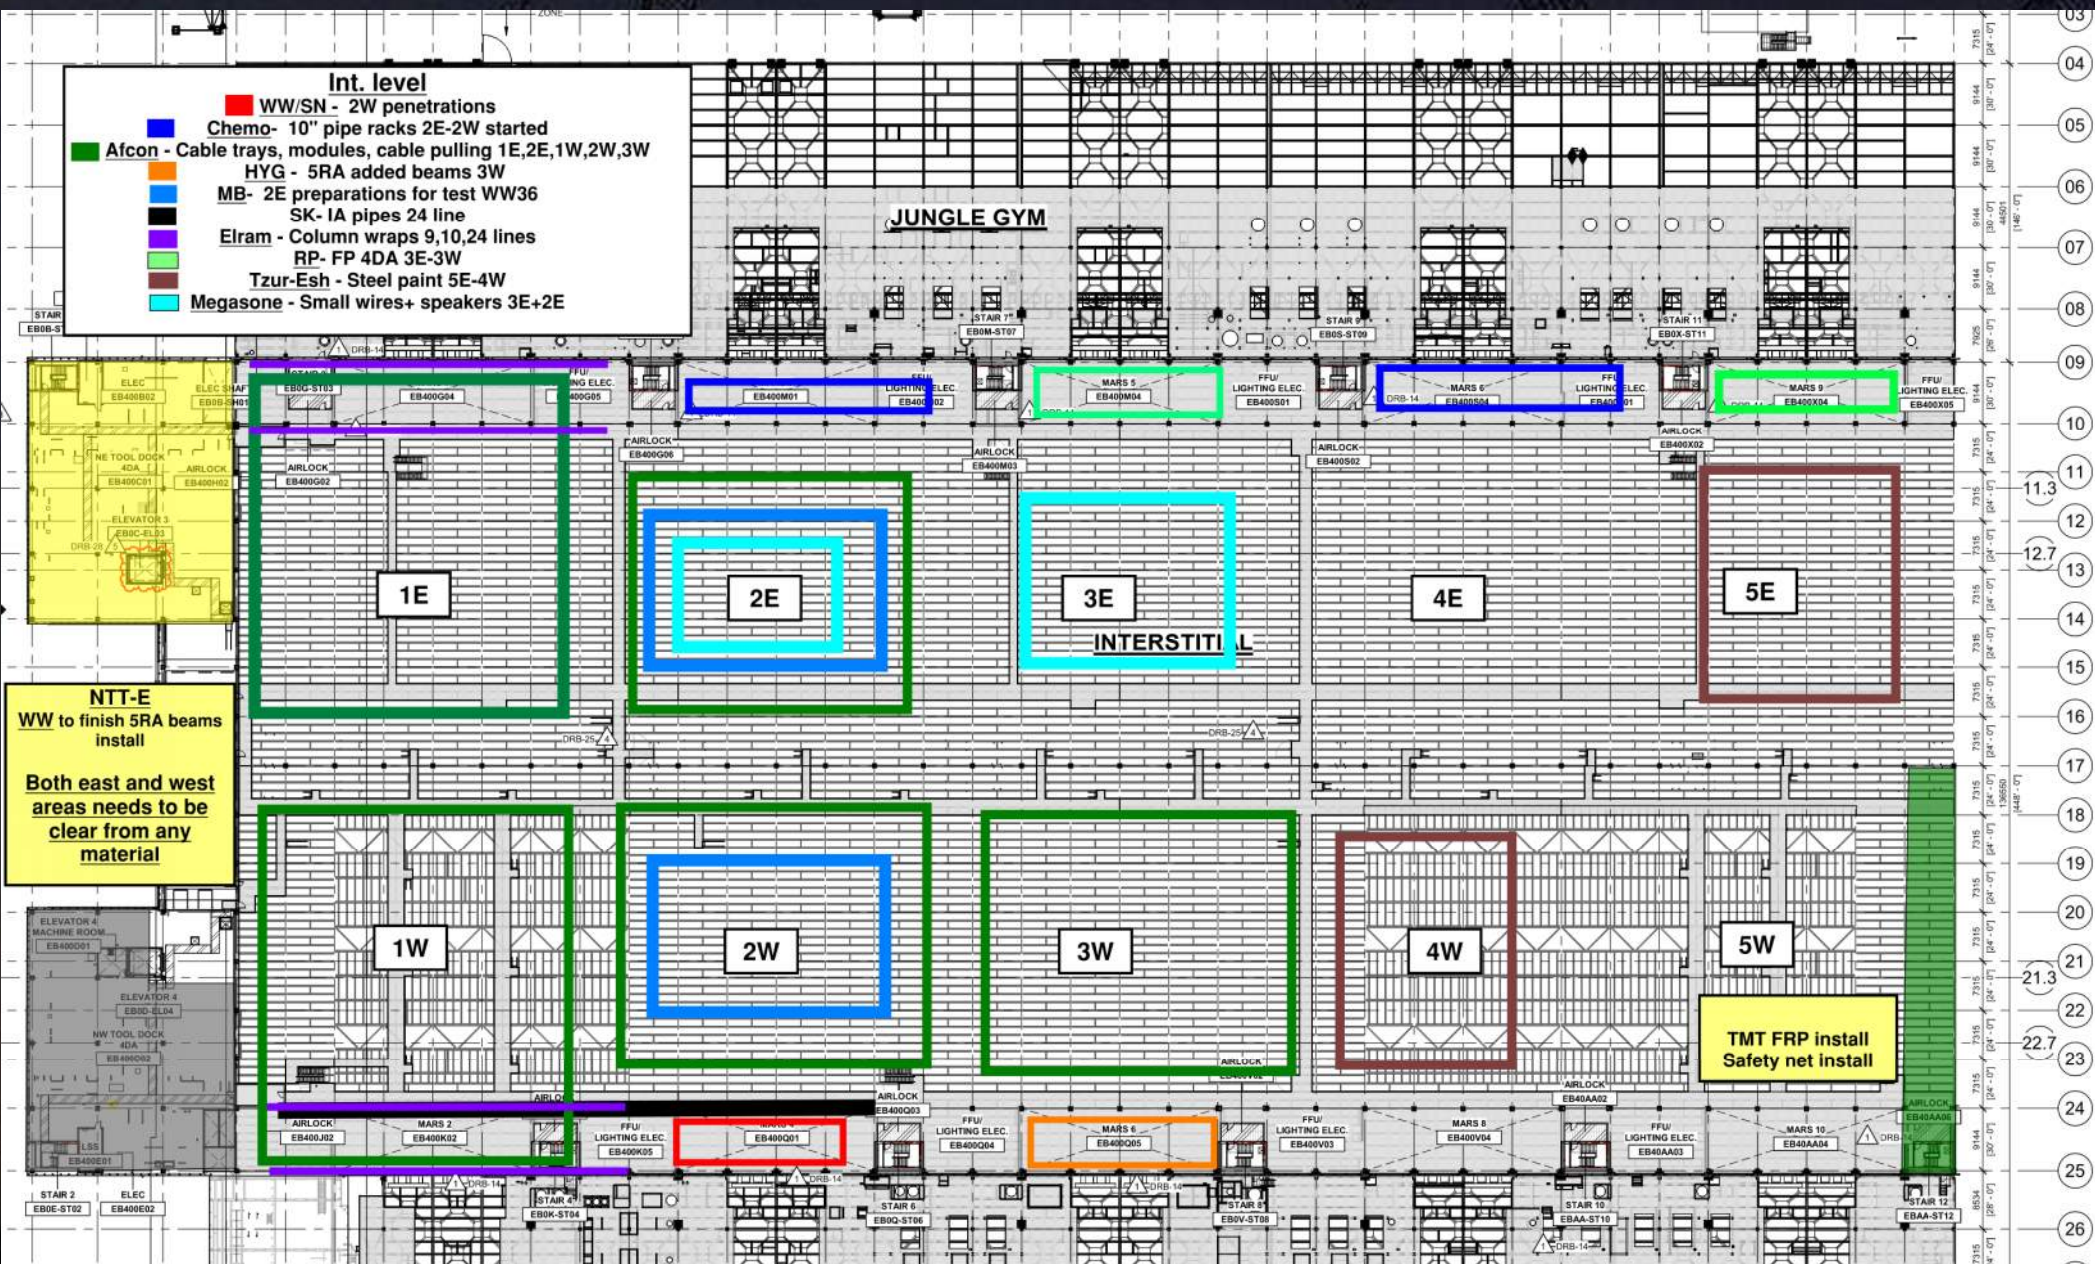





Truss Yard:
RP and Tzur-Esh to start FP and paint trusses on night shift

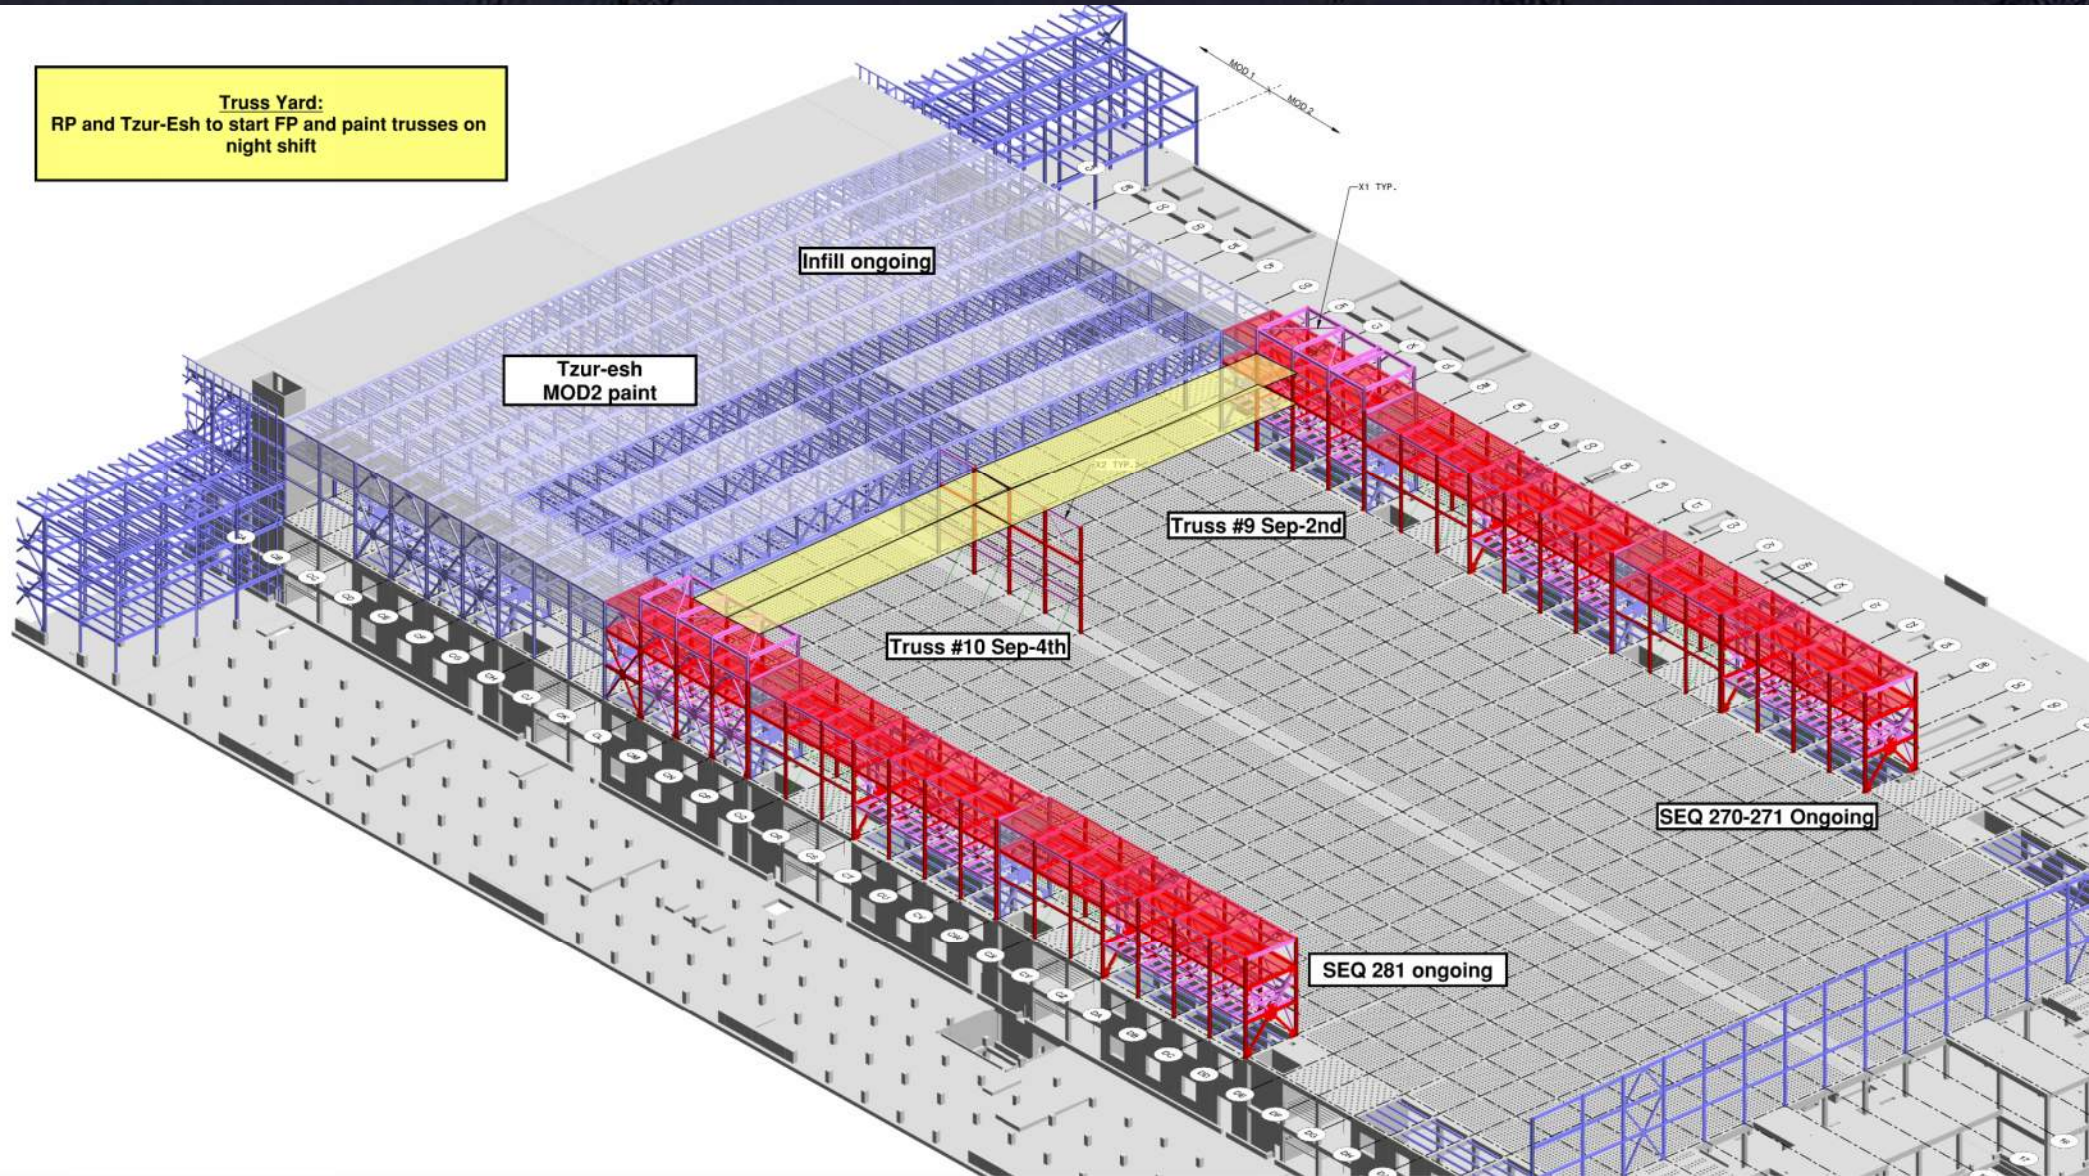


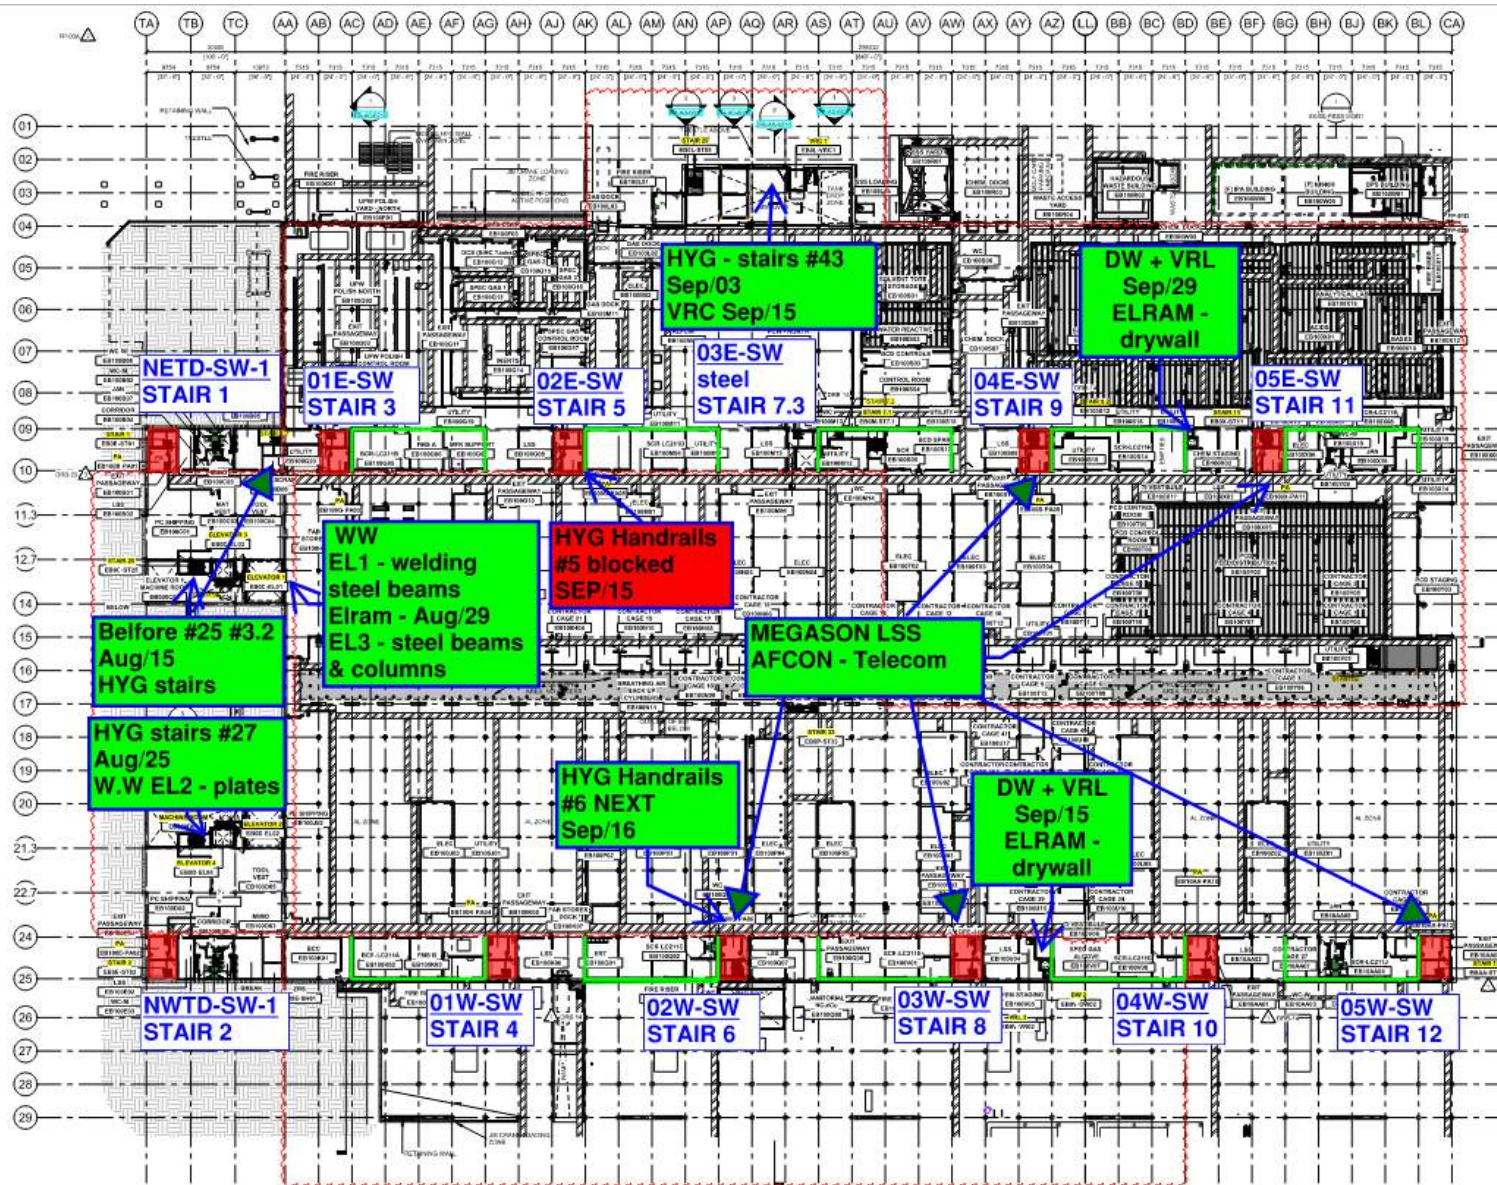

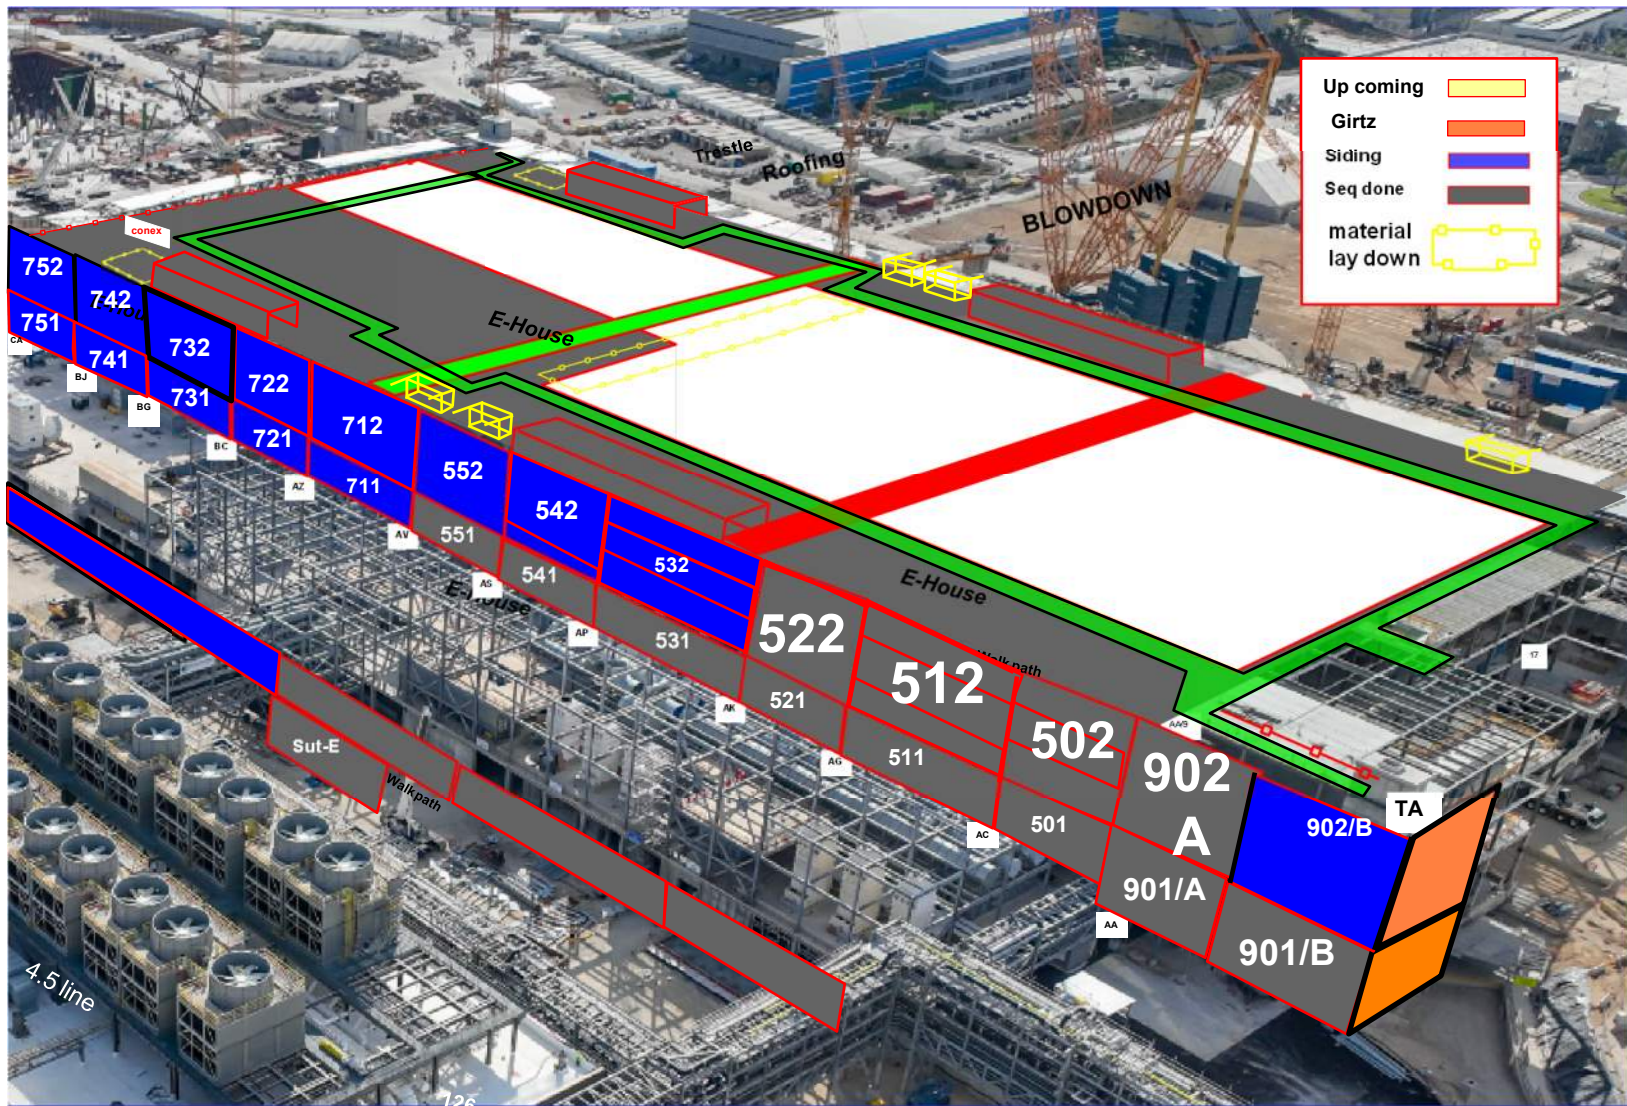

Walkpath

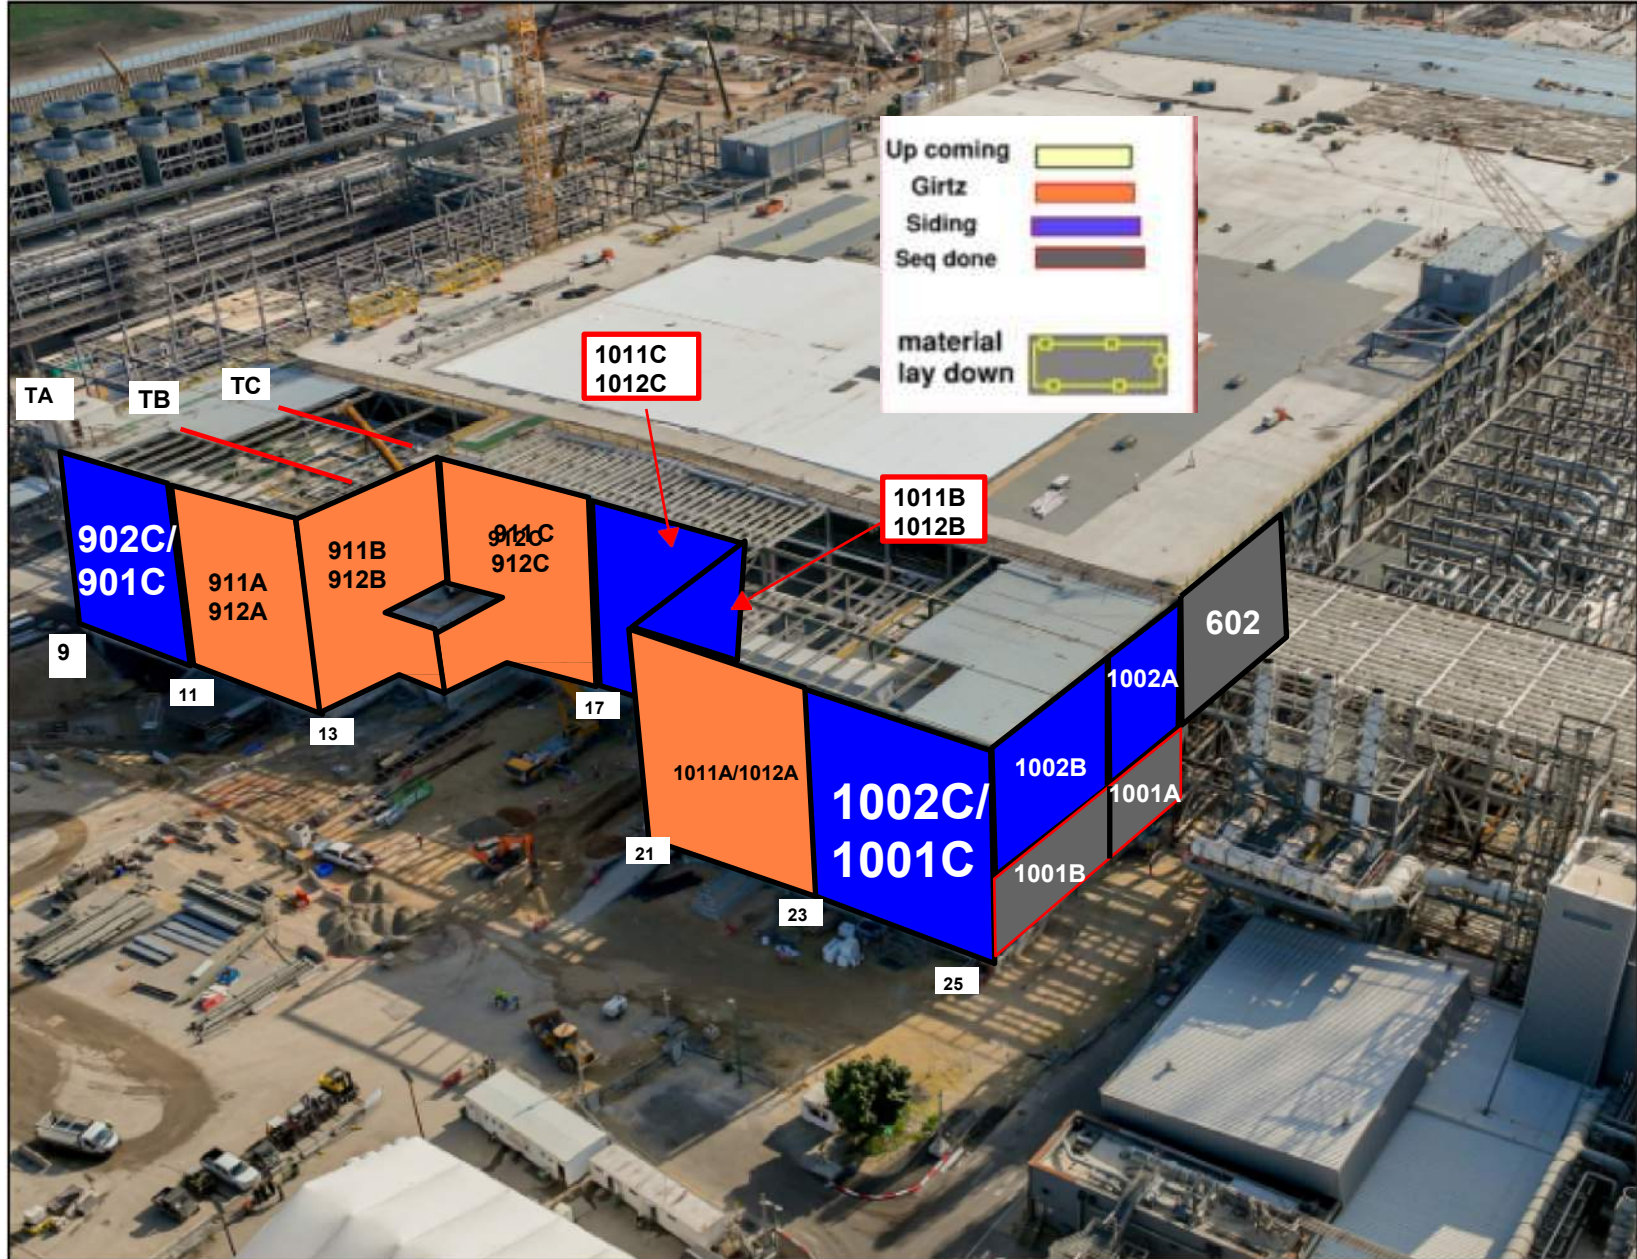

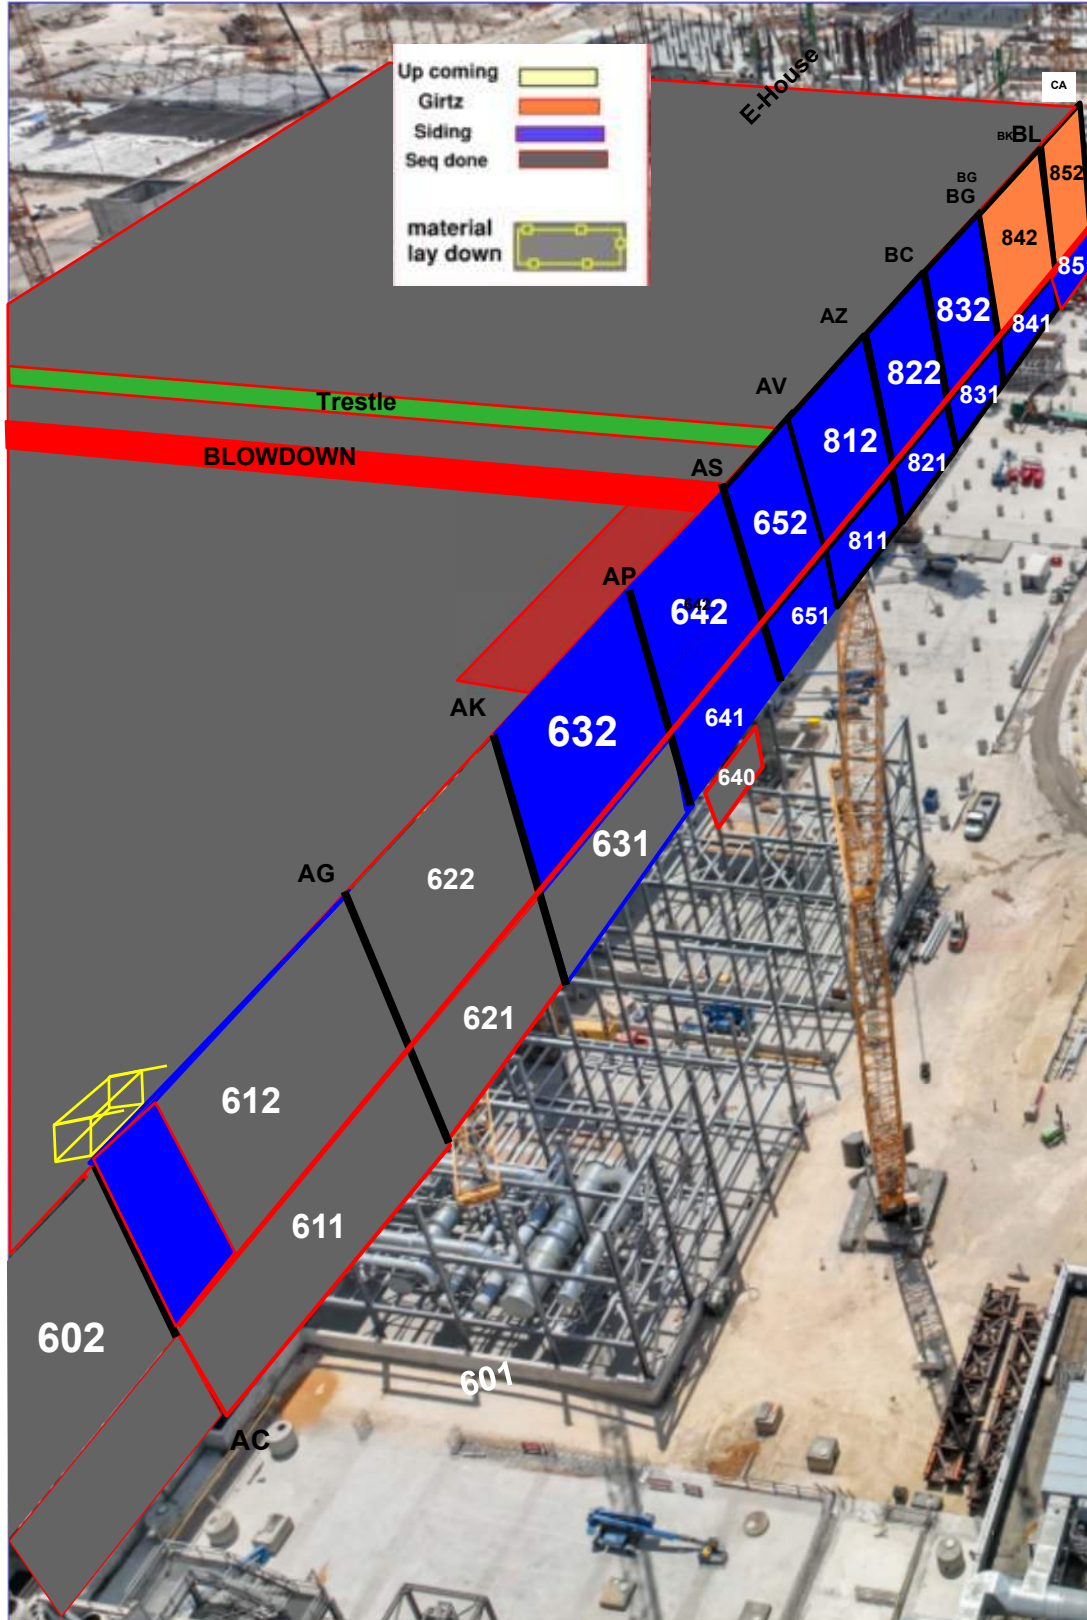

[illegible]


Siding - West FAB - JYG

[illegible]


PSSS.1

Utility Level
1YA

PSSS Roof
2SA

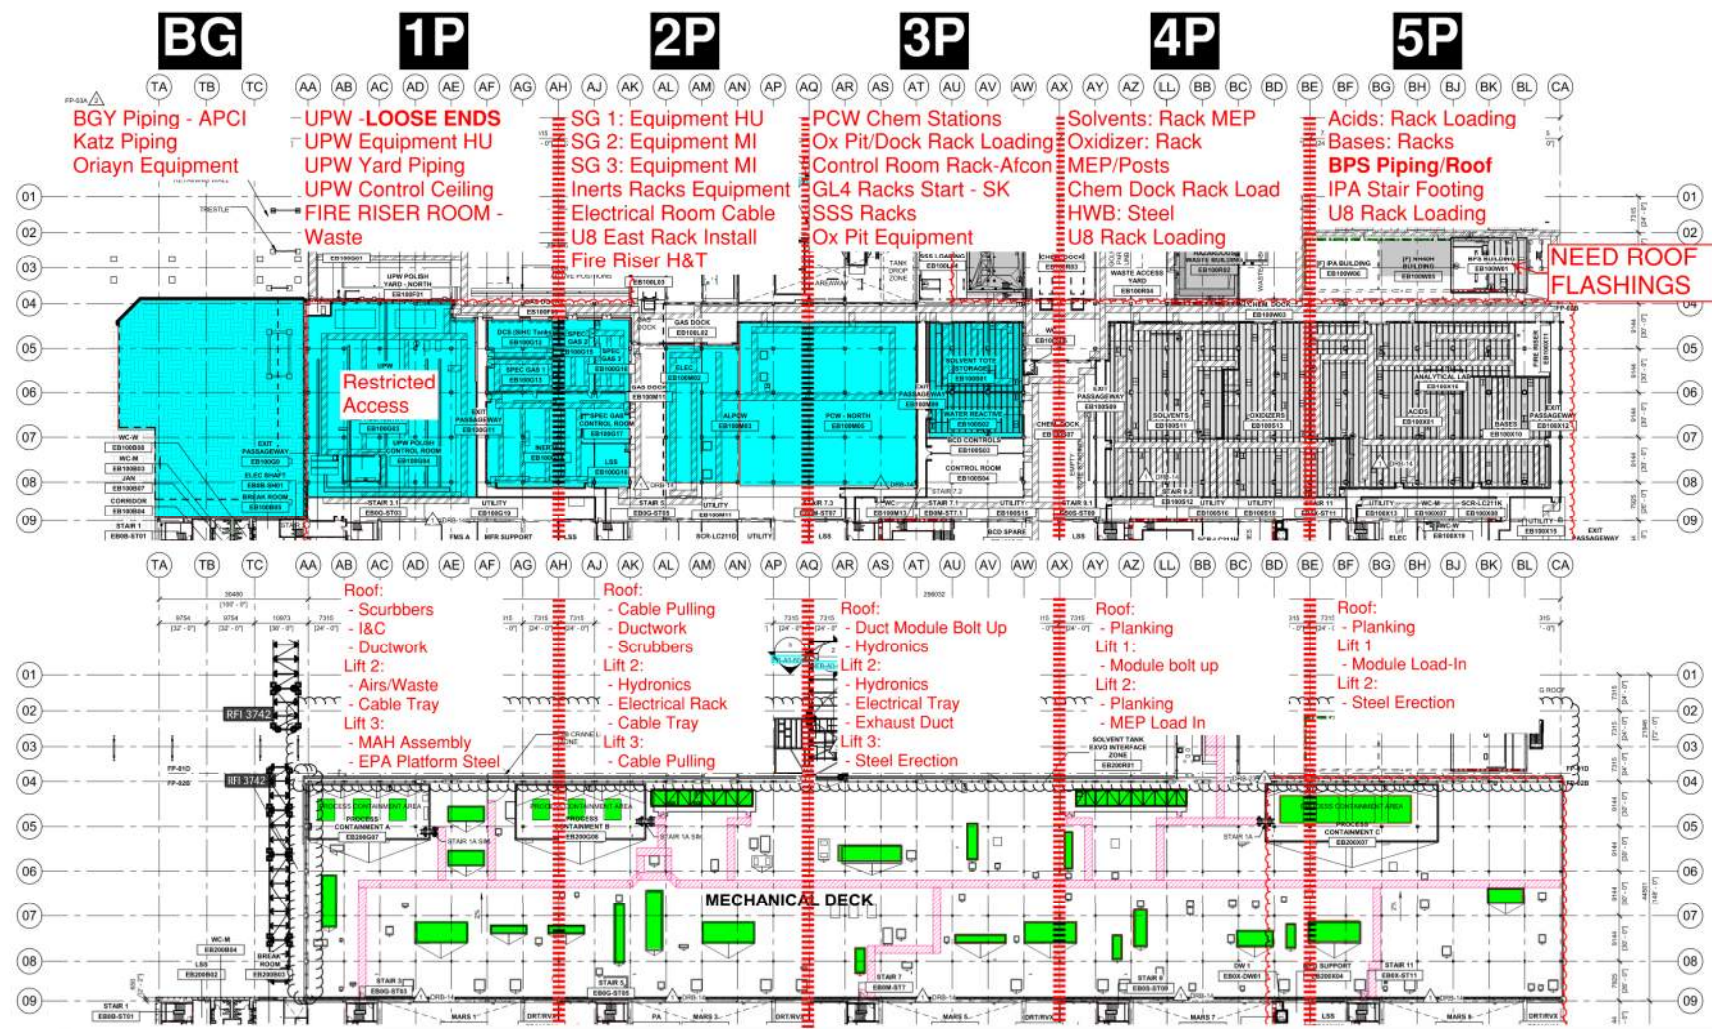


PSSS.2

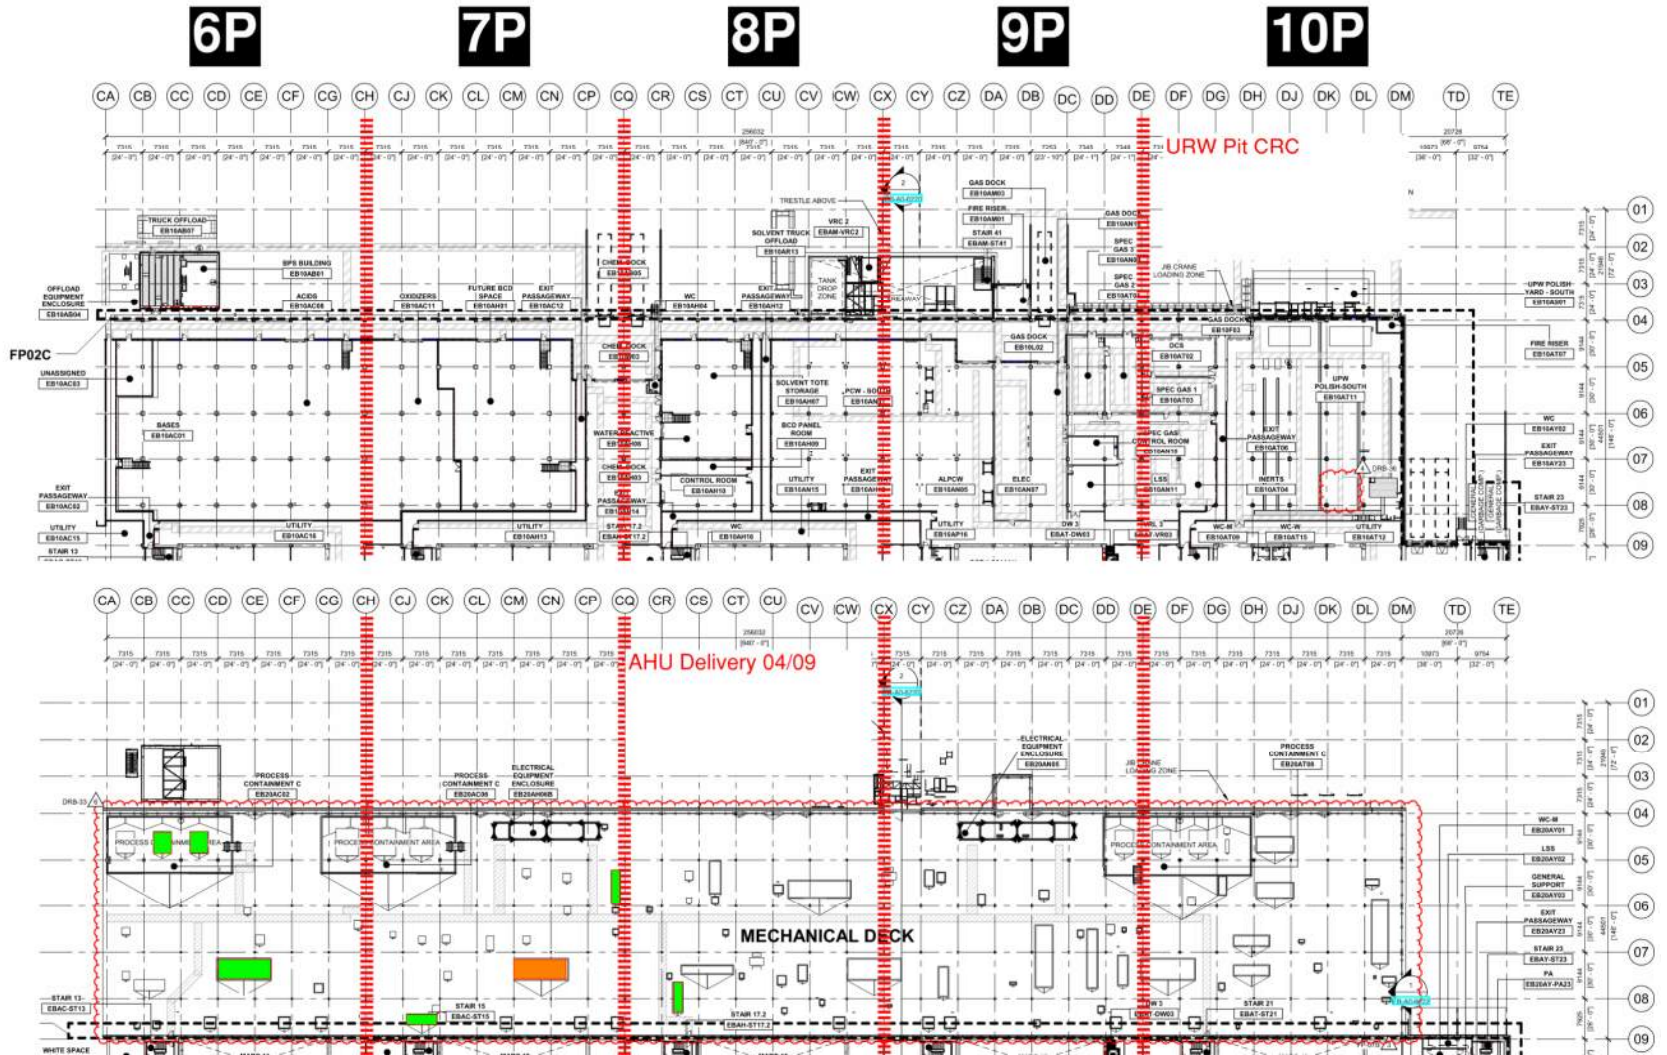


02/09
EPA
Platform

17:00: Road
Closure of
East Road
18:30
Hoisting EPA
platform

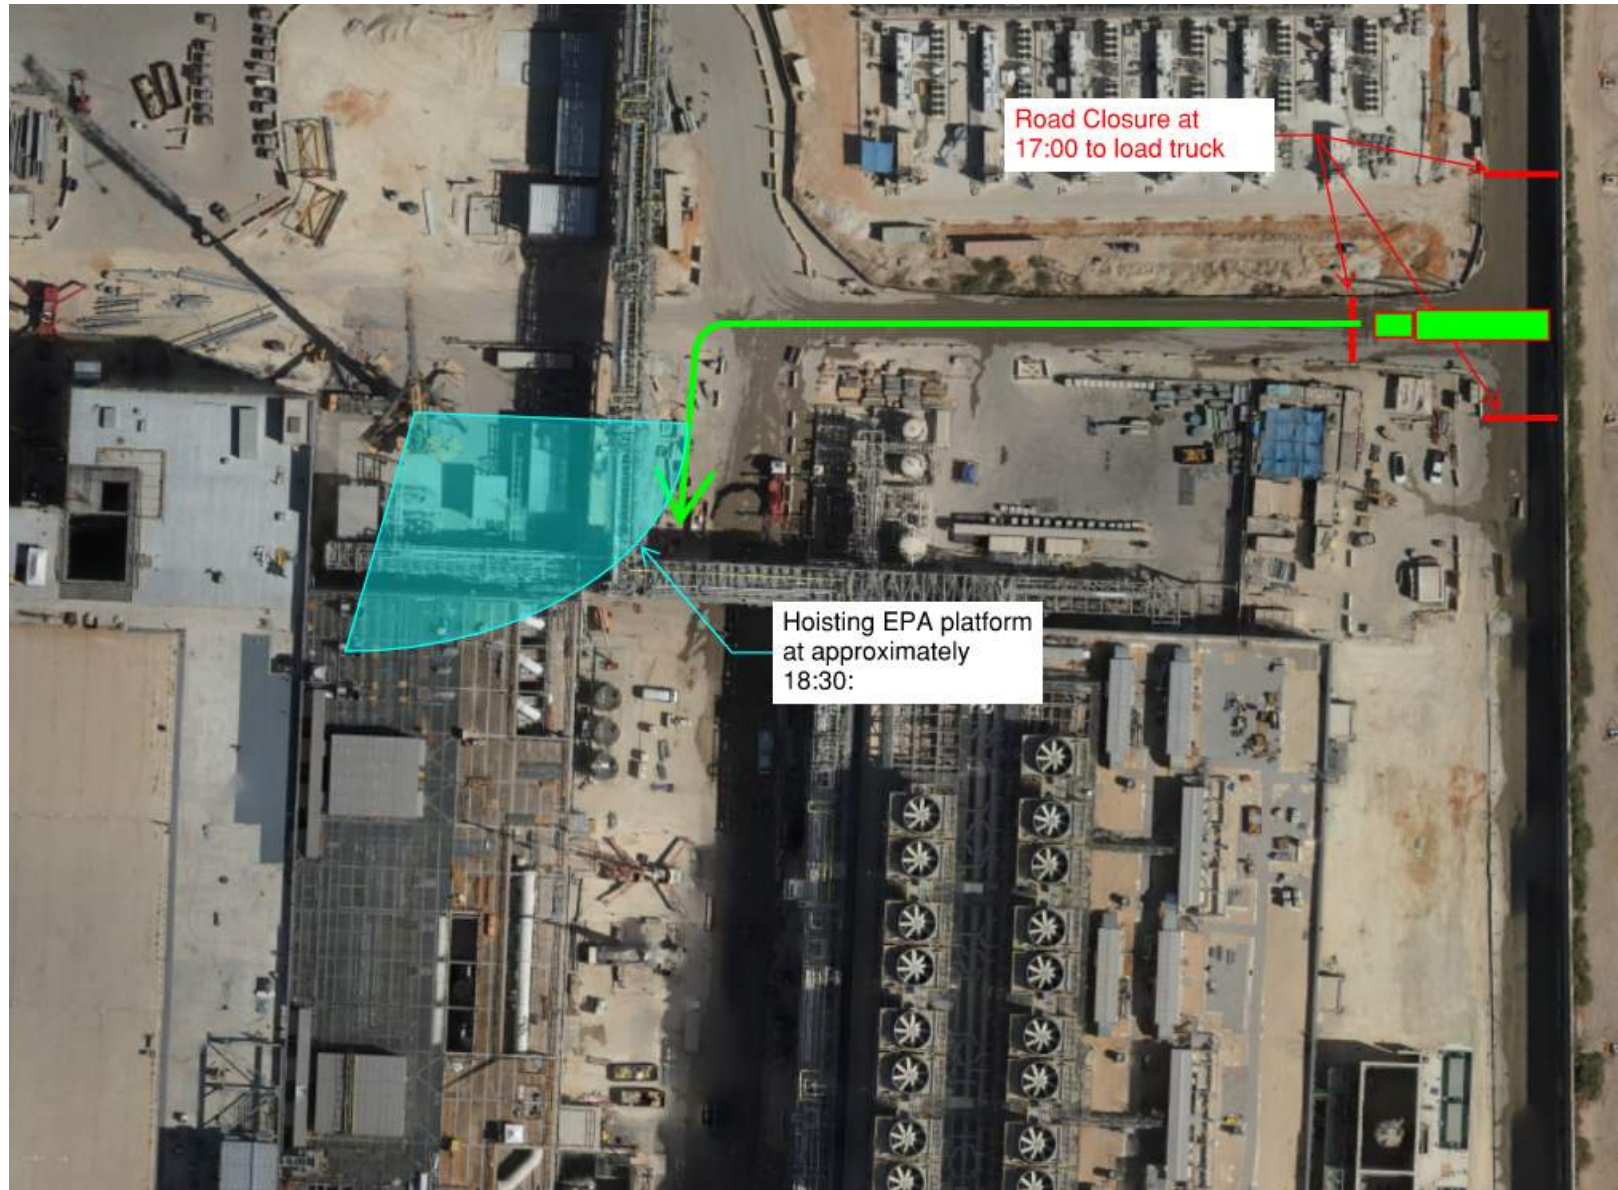




WJG 01J, 02J LIFT 2 & 3

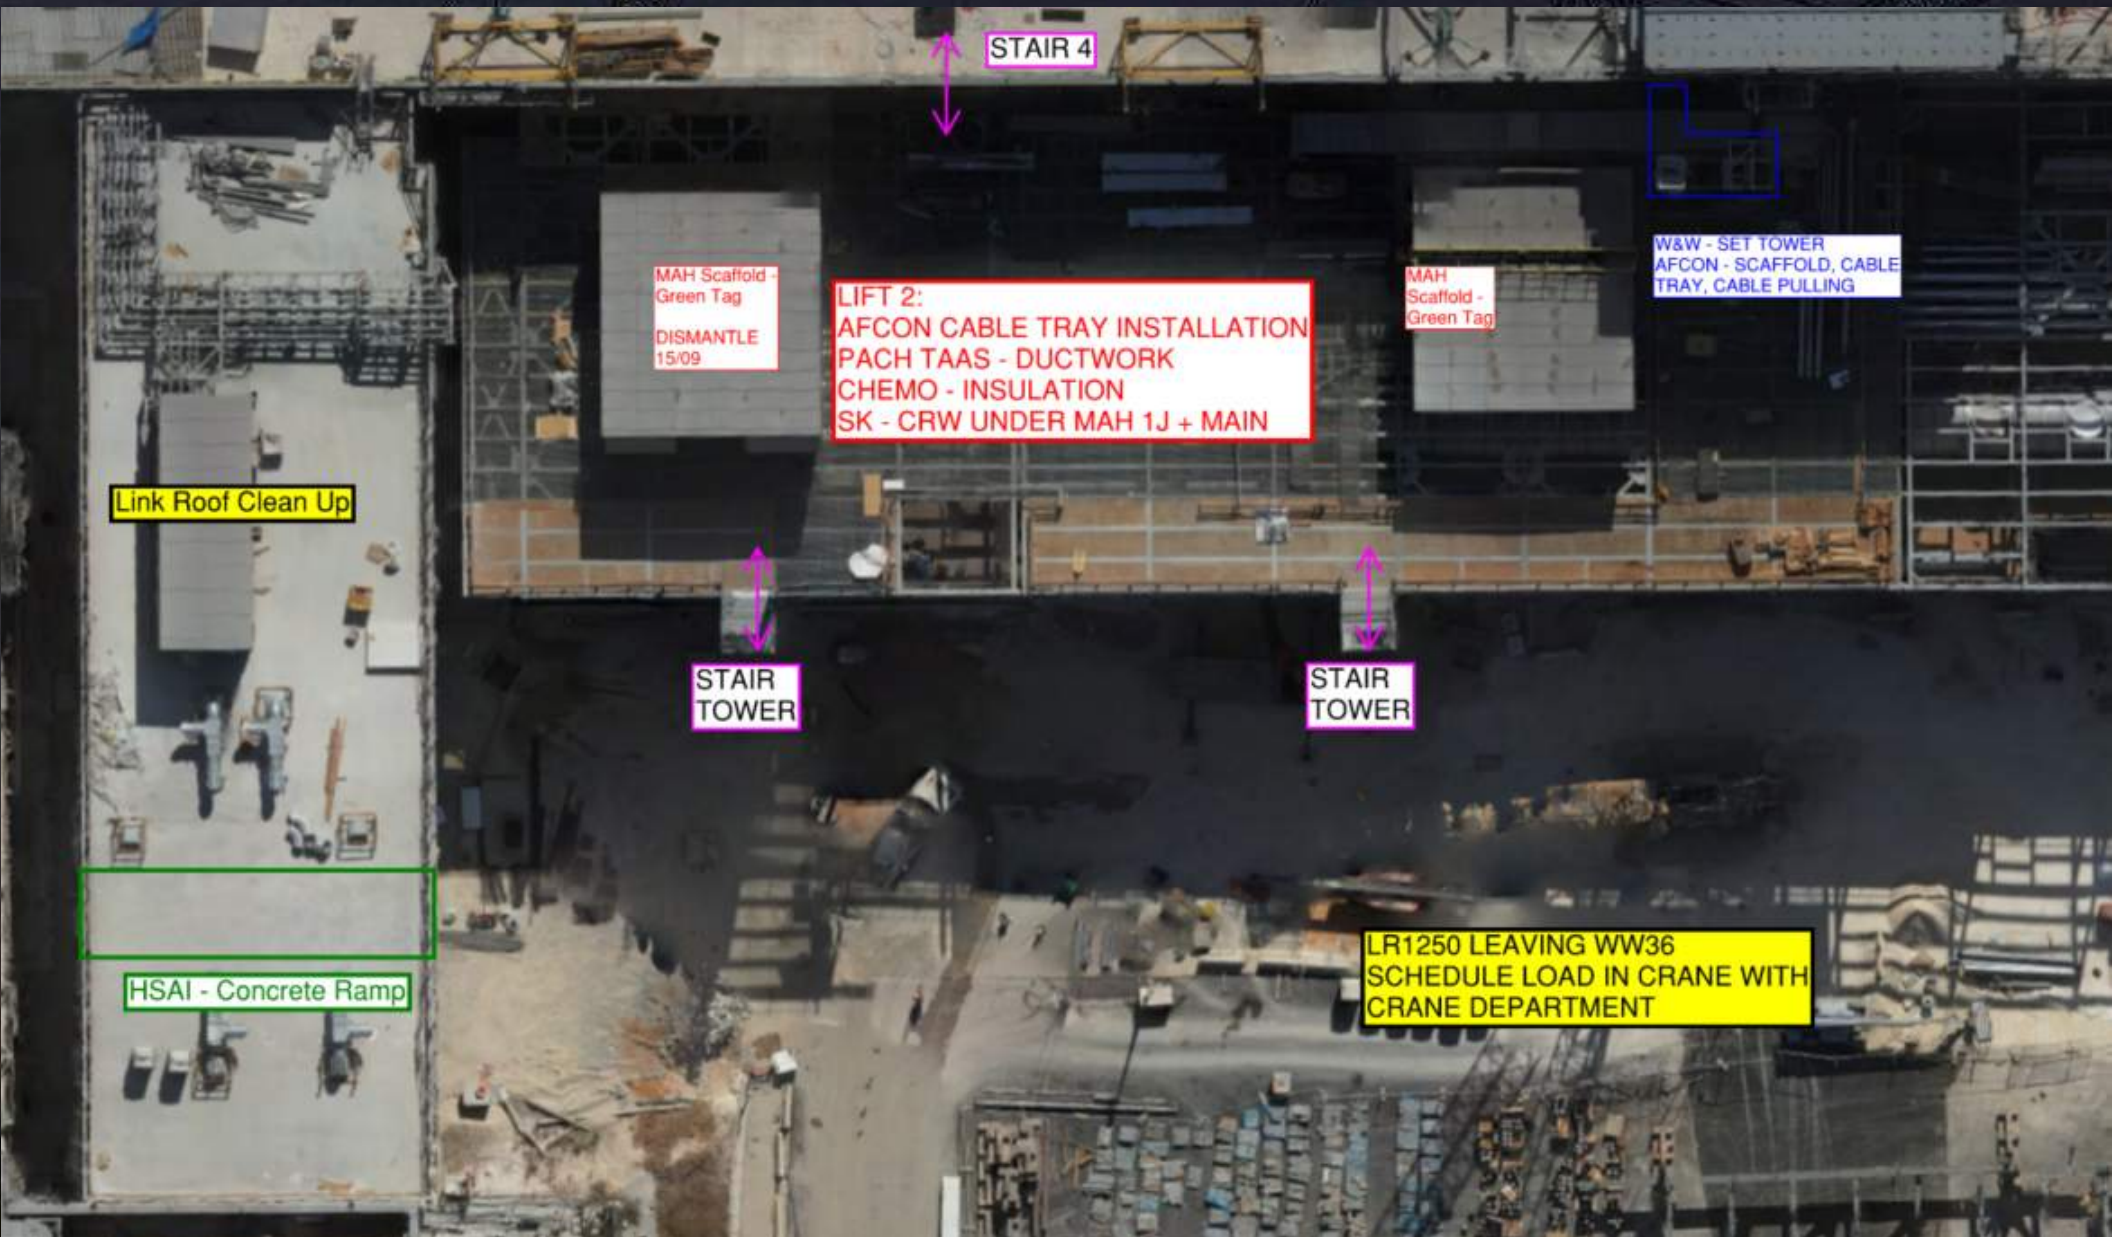

WJG 03J, 04J, 05J LIFT 2 & 3




WJG UTILITY LEVEL BUILD OUT

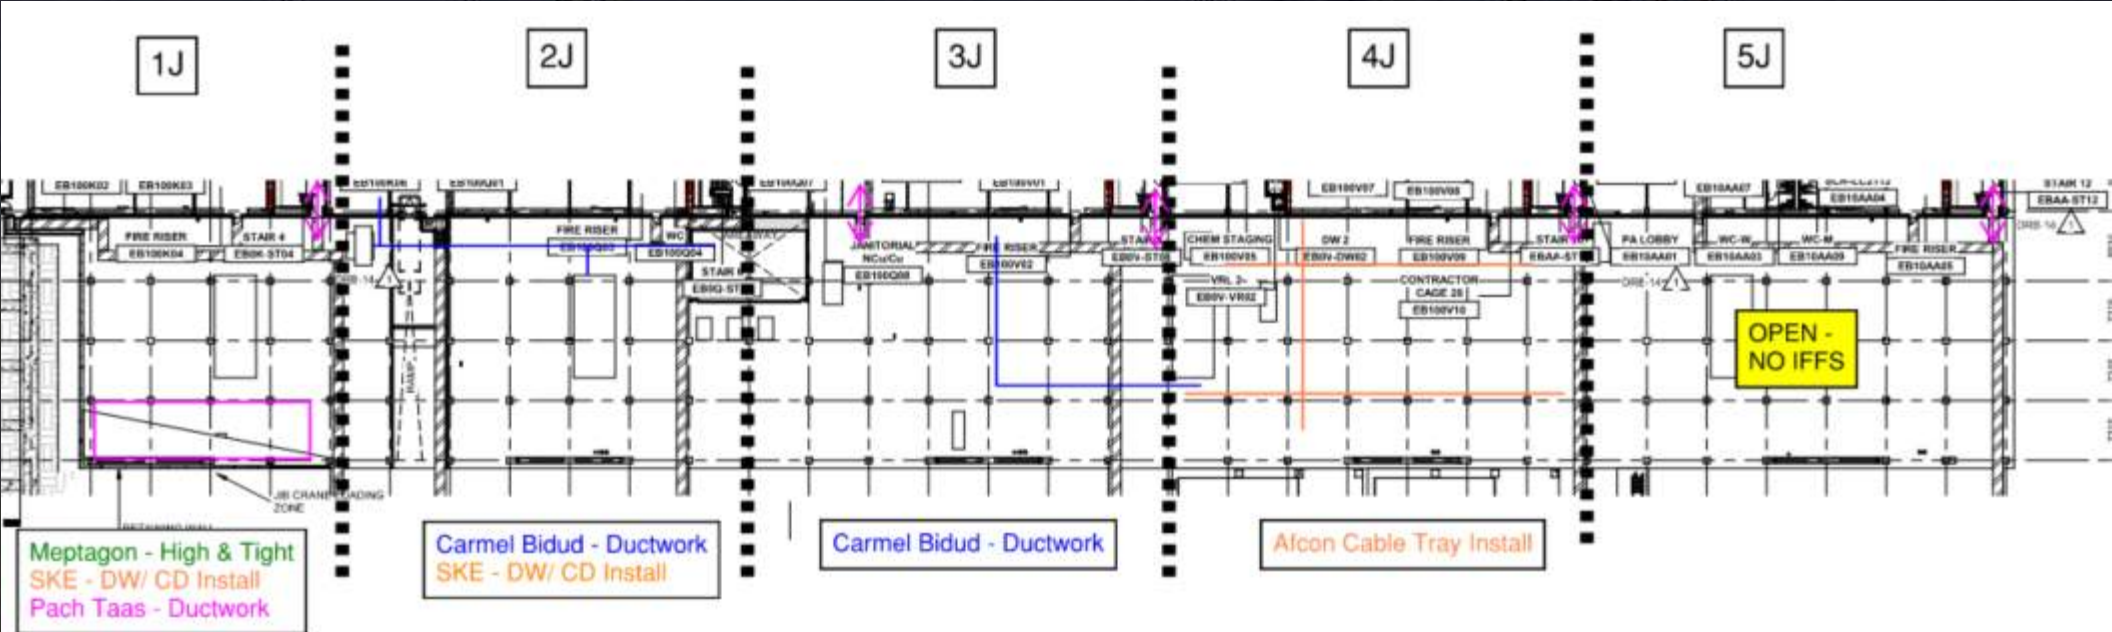






CUB 1

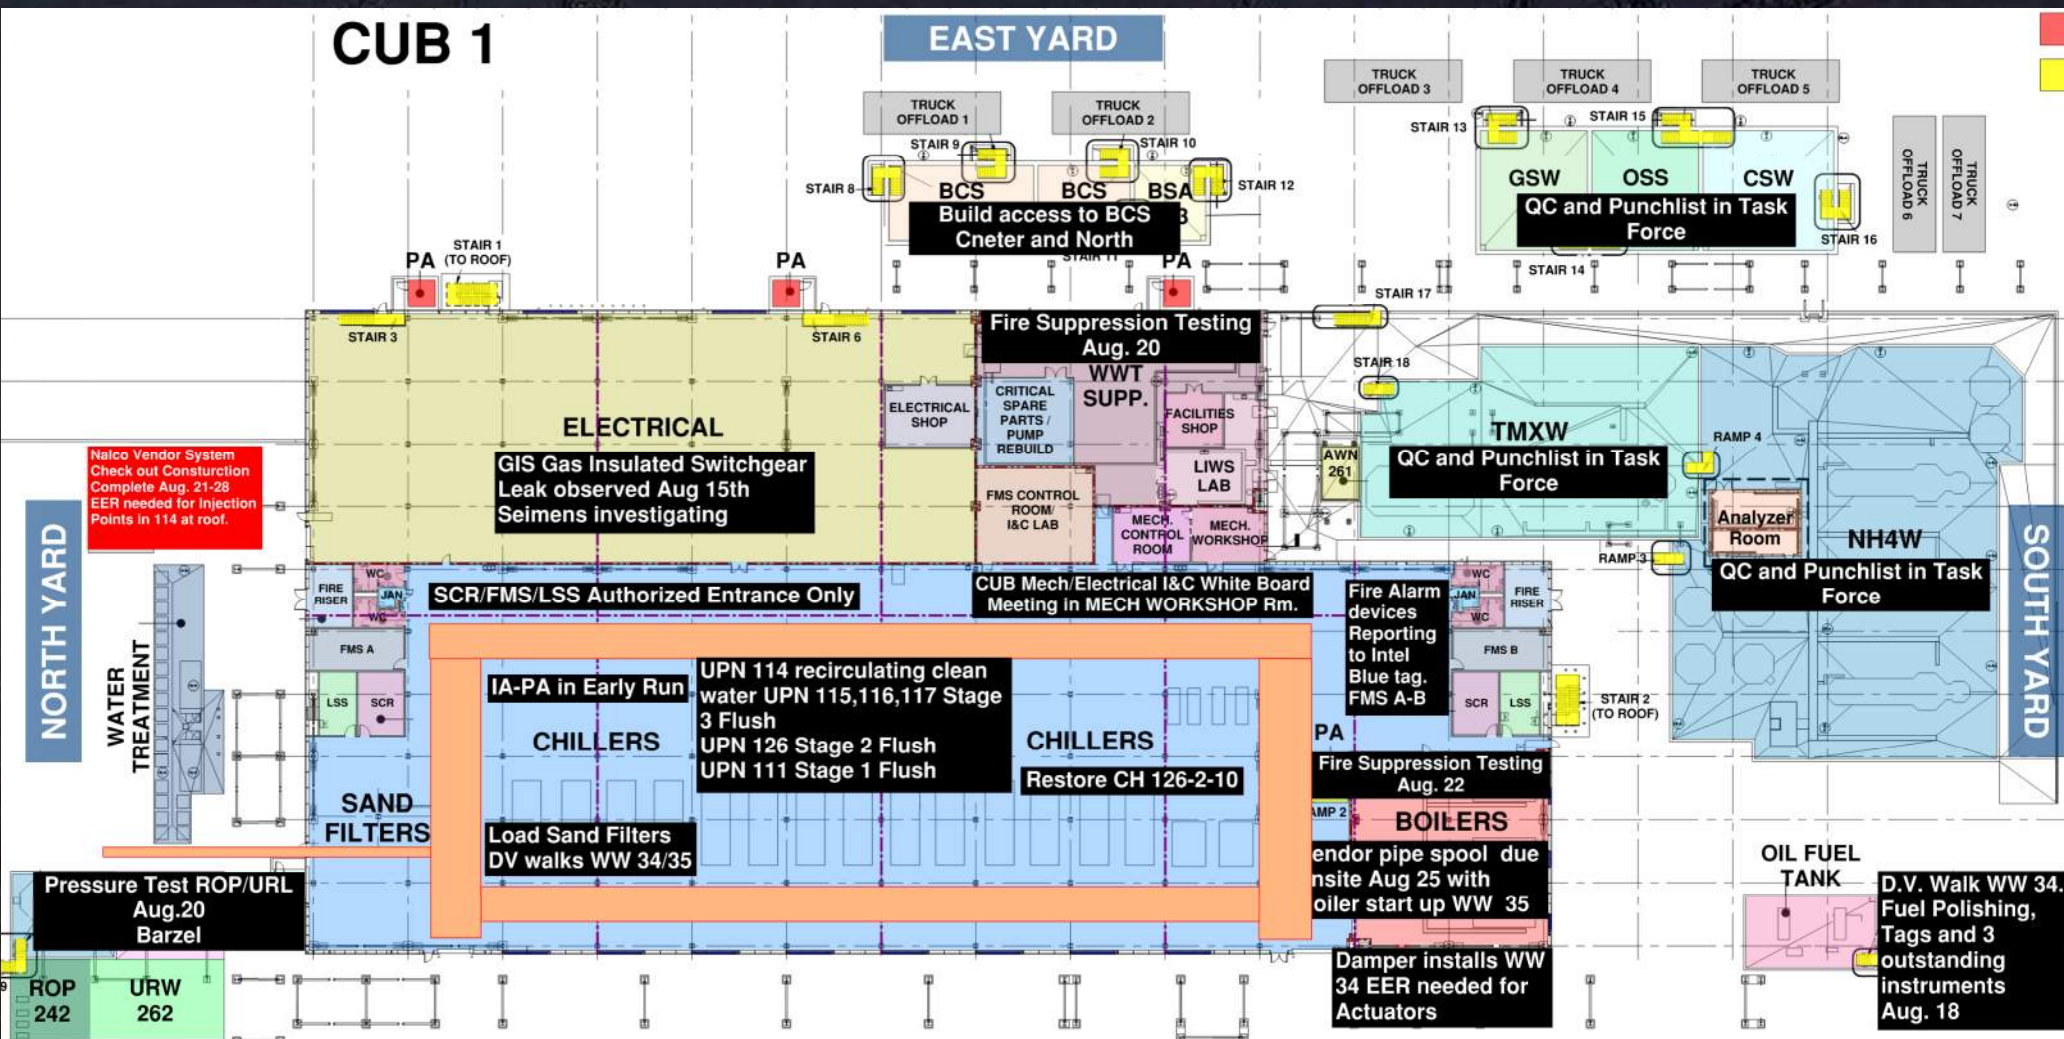




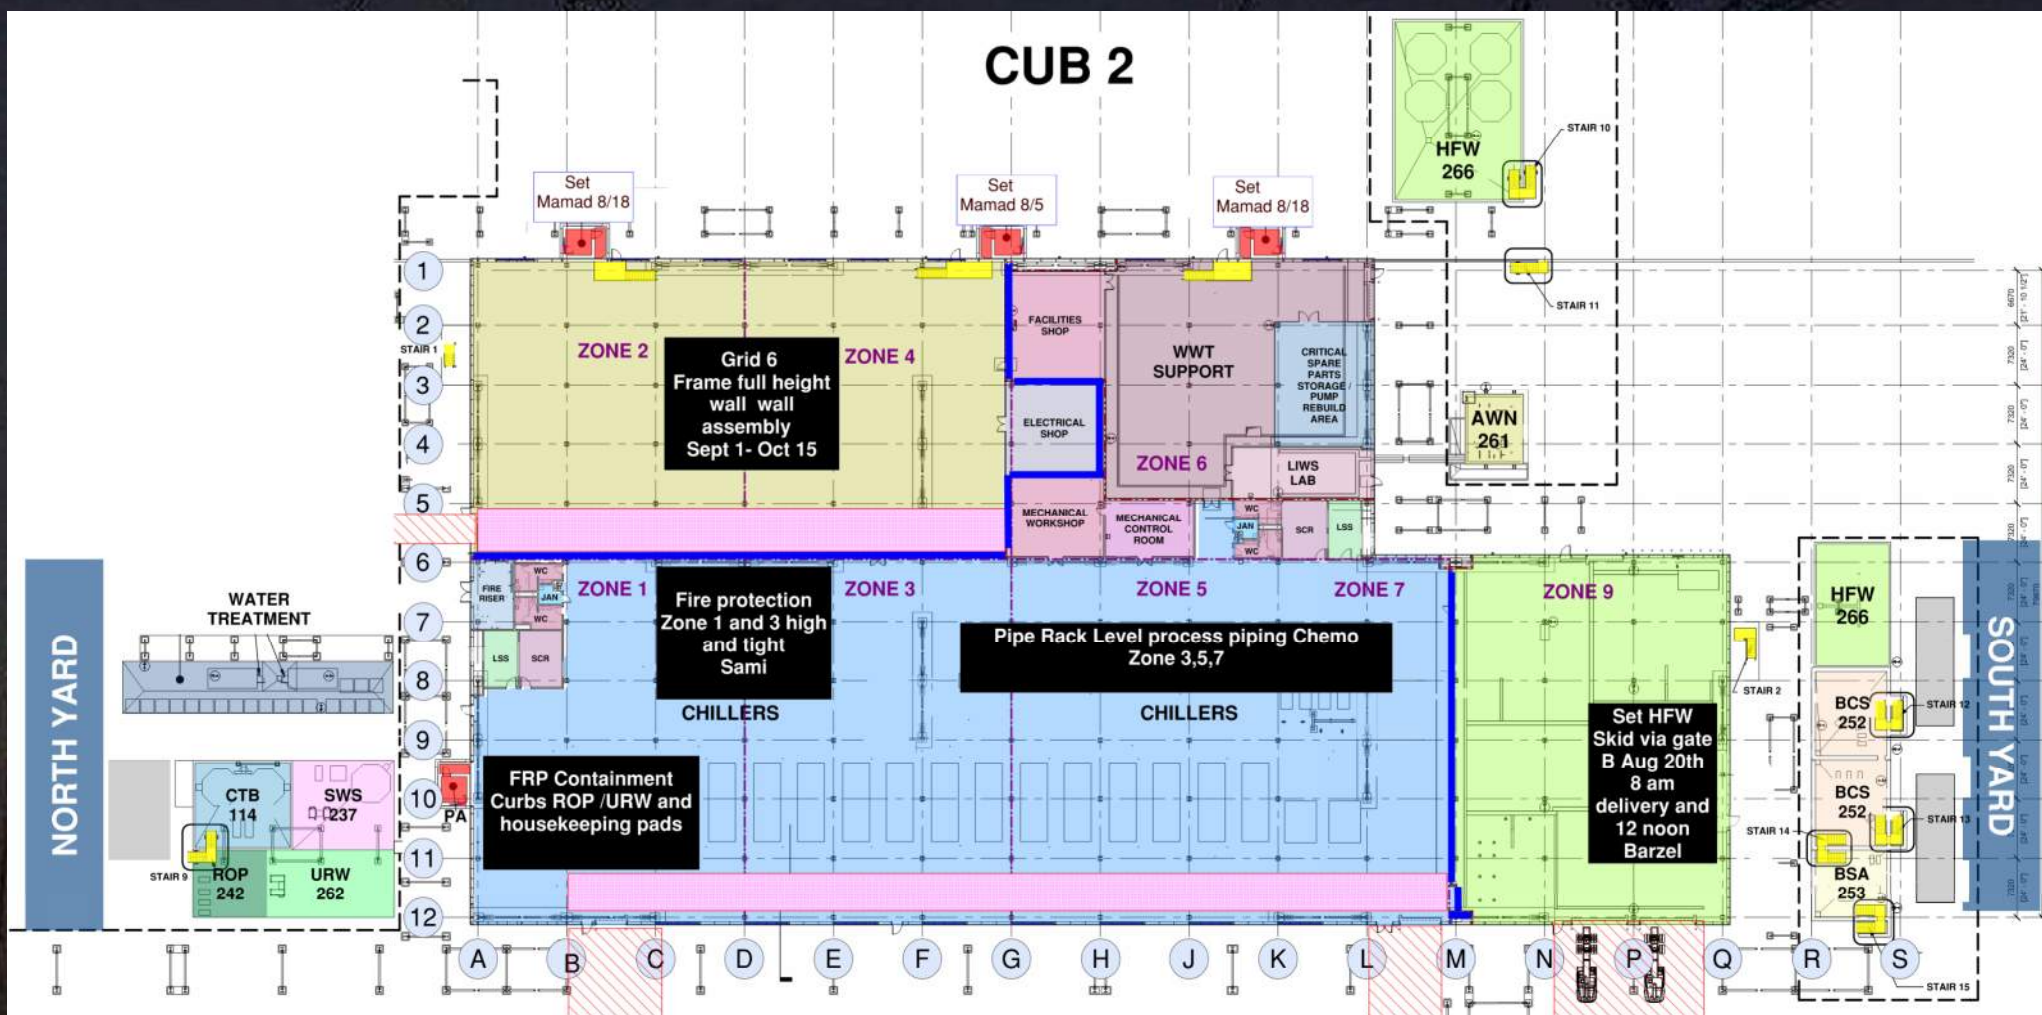

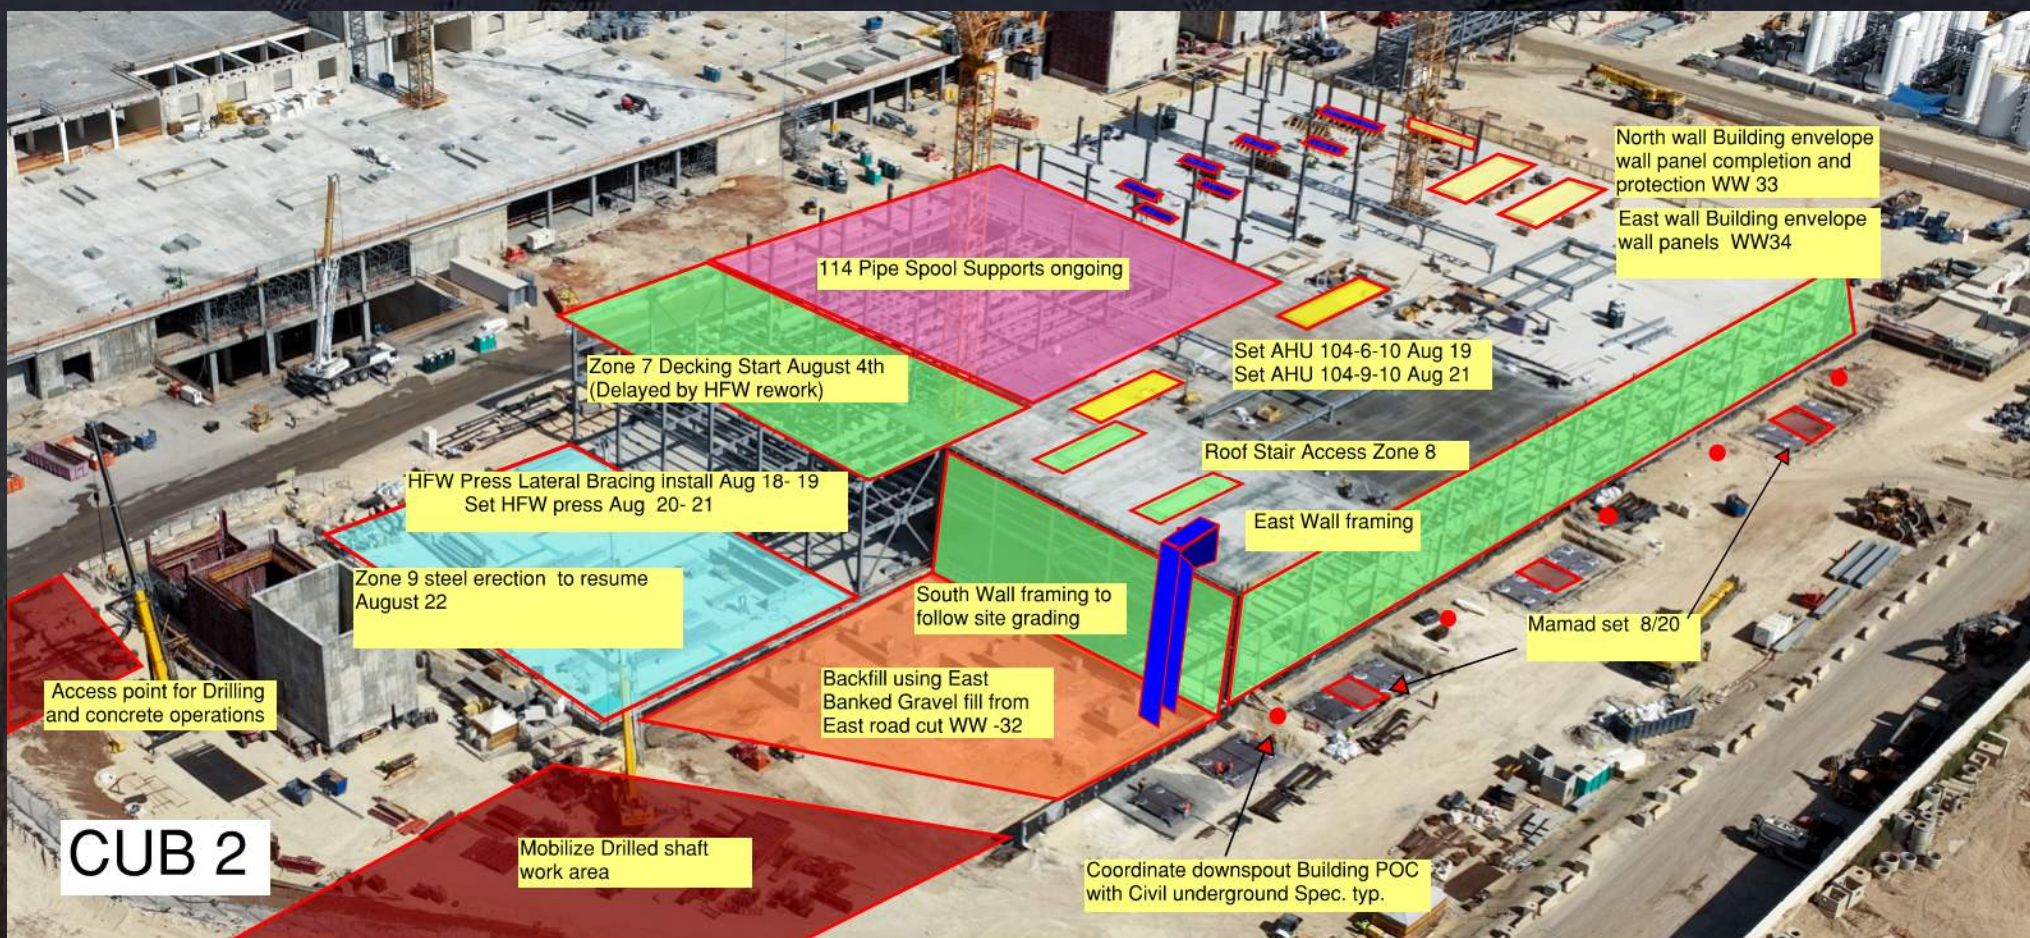

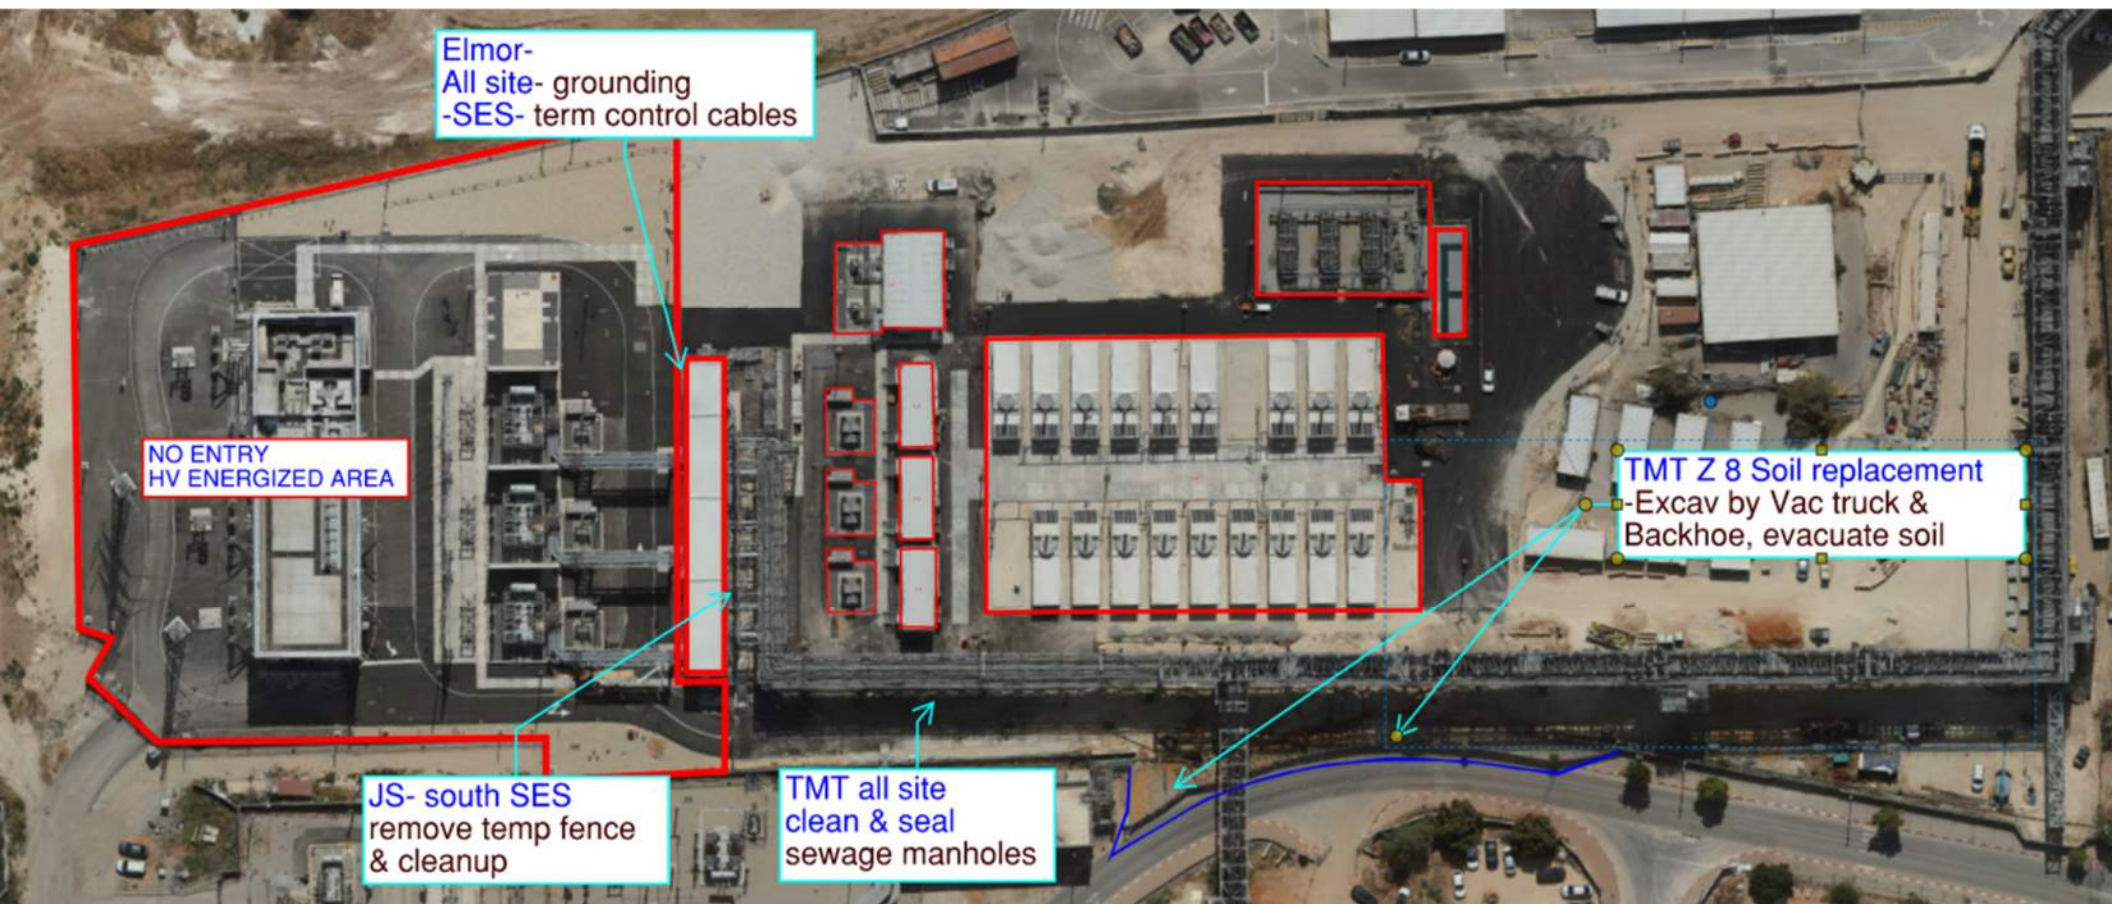

FAB GIS 33&34 PERMENENT POWER
September 3rd and 5th 7:00am to
8:00am.

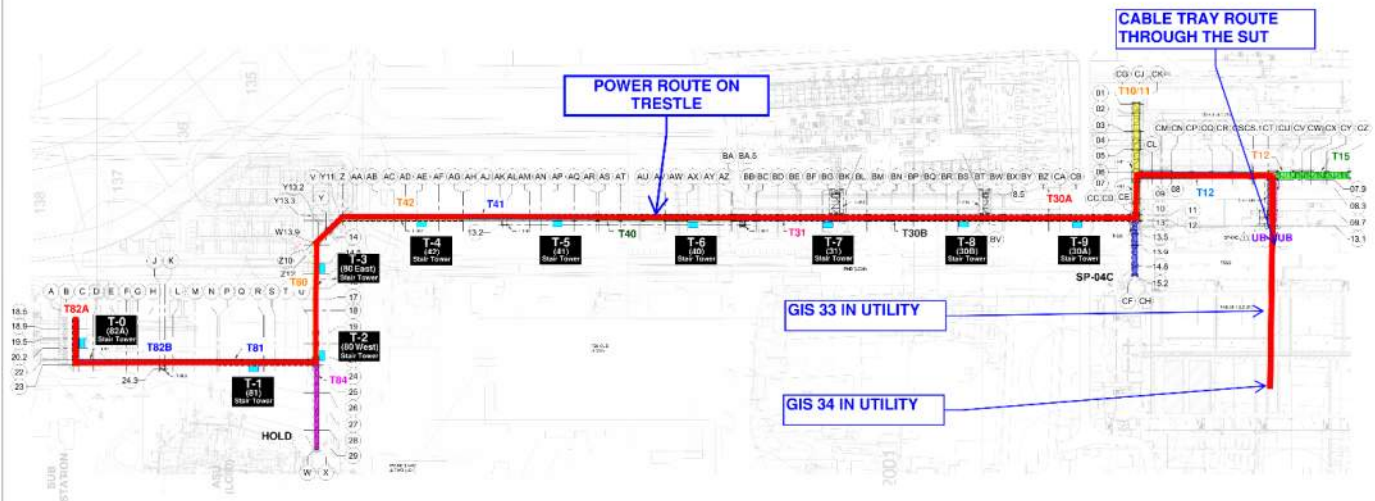



HOFFMAN CONSTRUCTION COMPANY




Lesico 12" natural gas pipe pressure test exclusion zone

Wednesday, September 4th 18:00 -Thursday, September 5th 01:00

All access to vehicles within exclusion zone will cut off at 17:50






HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

Trestle Lesico NDT-10"-8" 4 welds 04/09/24

22:00-05:00

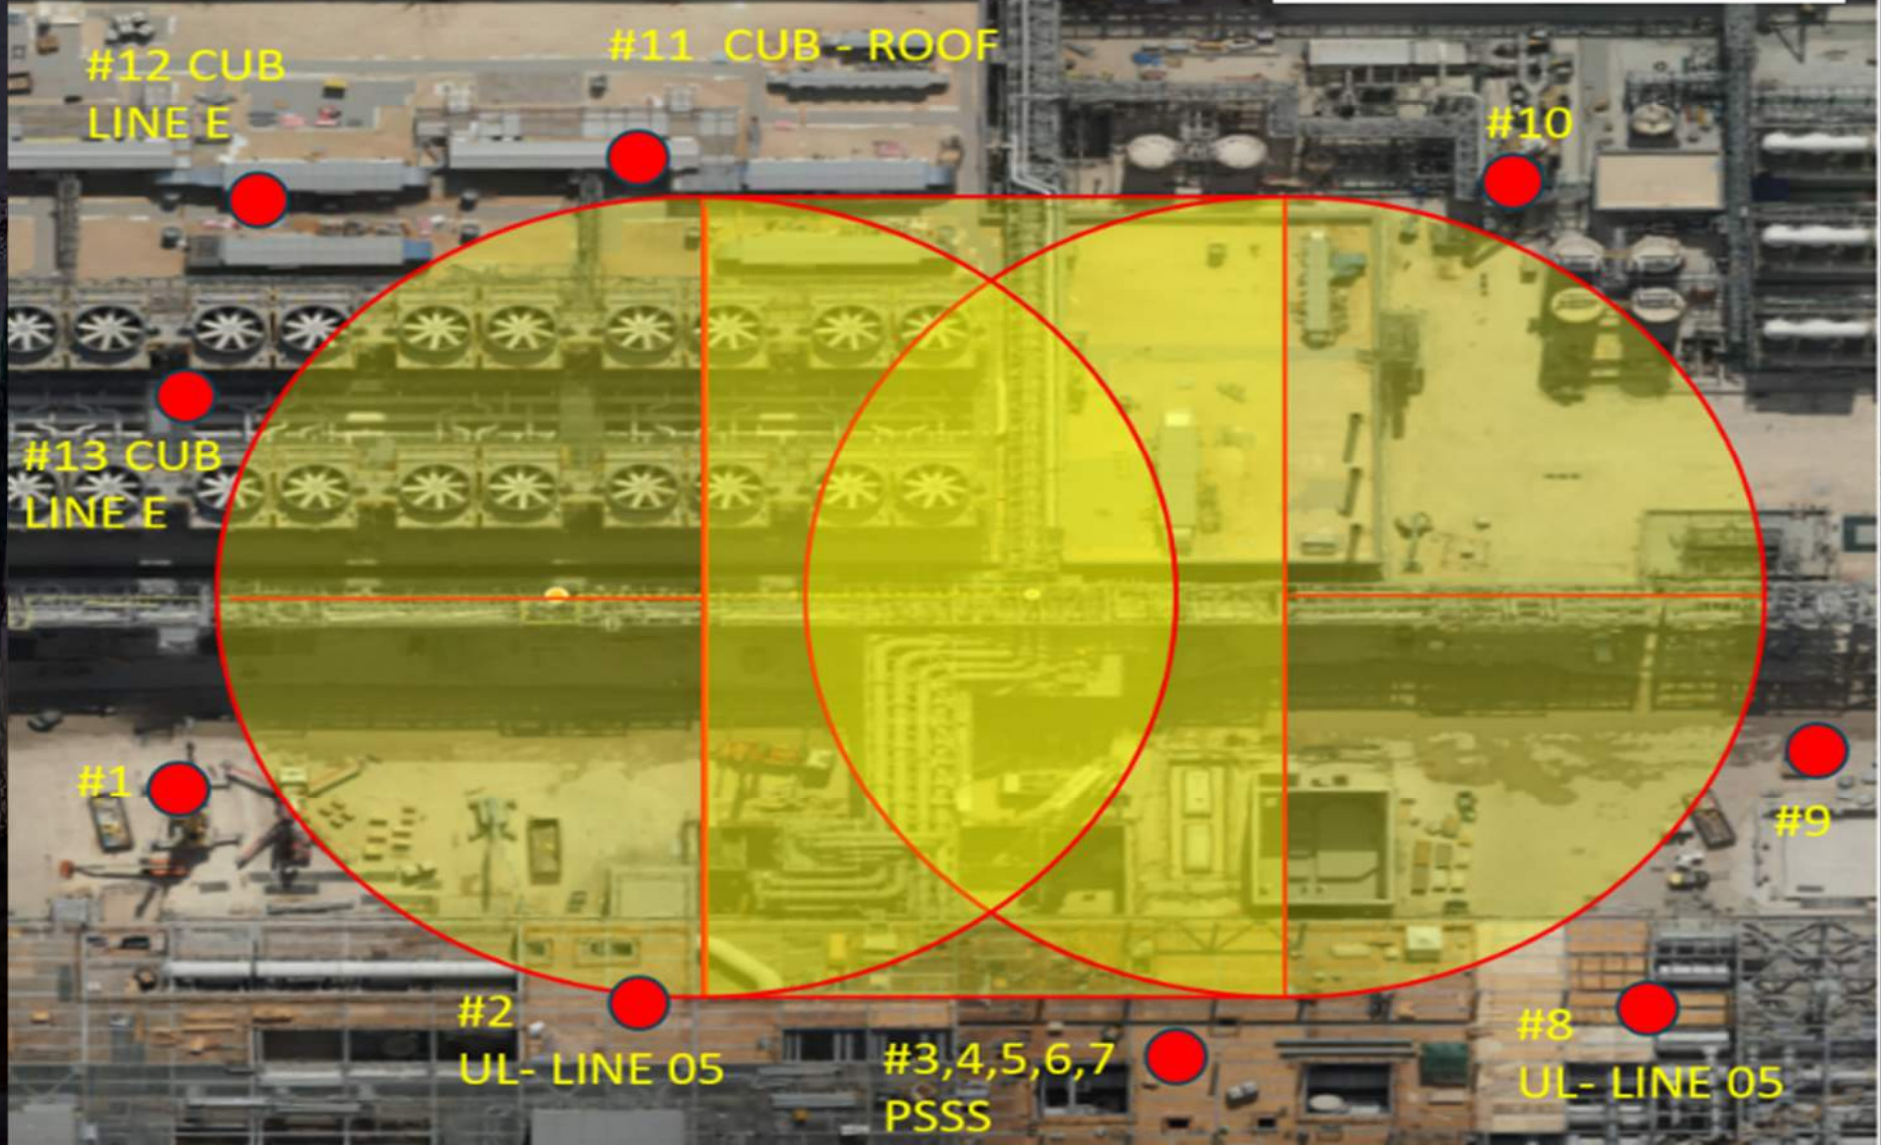




HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

Trestle Lesico NDT-10", 7 welds 05/09/24

22:00-05:00

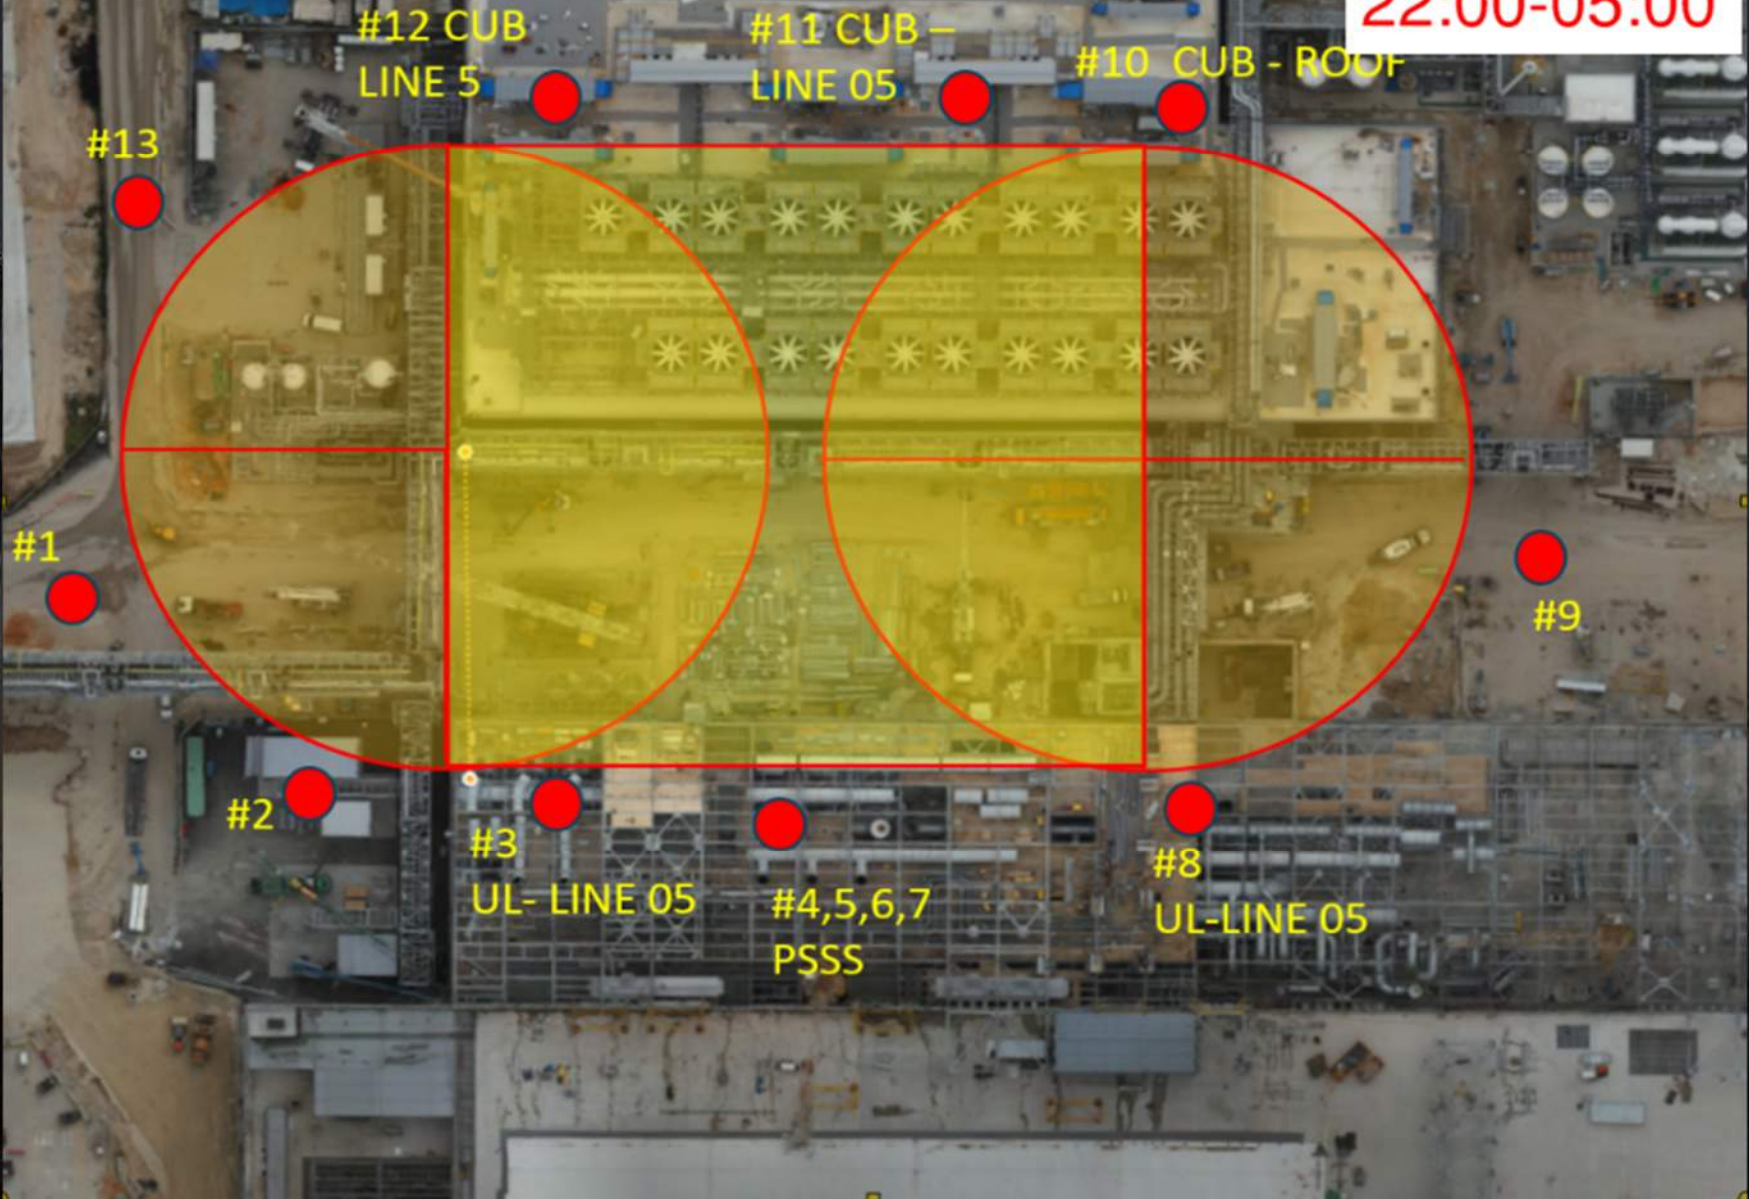



HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

BGC VACUM TANKS AREA

Area out of BGC site will be marked with
YELLOW stripe.

And 2 spotters will be posted!!(yellow)


Starting –Sunday night September 1st at 22:00


Finish on Monday Sep 2nd at 05:00am.

Safety spotter



Safety spotter

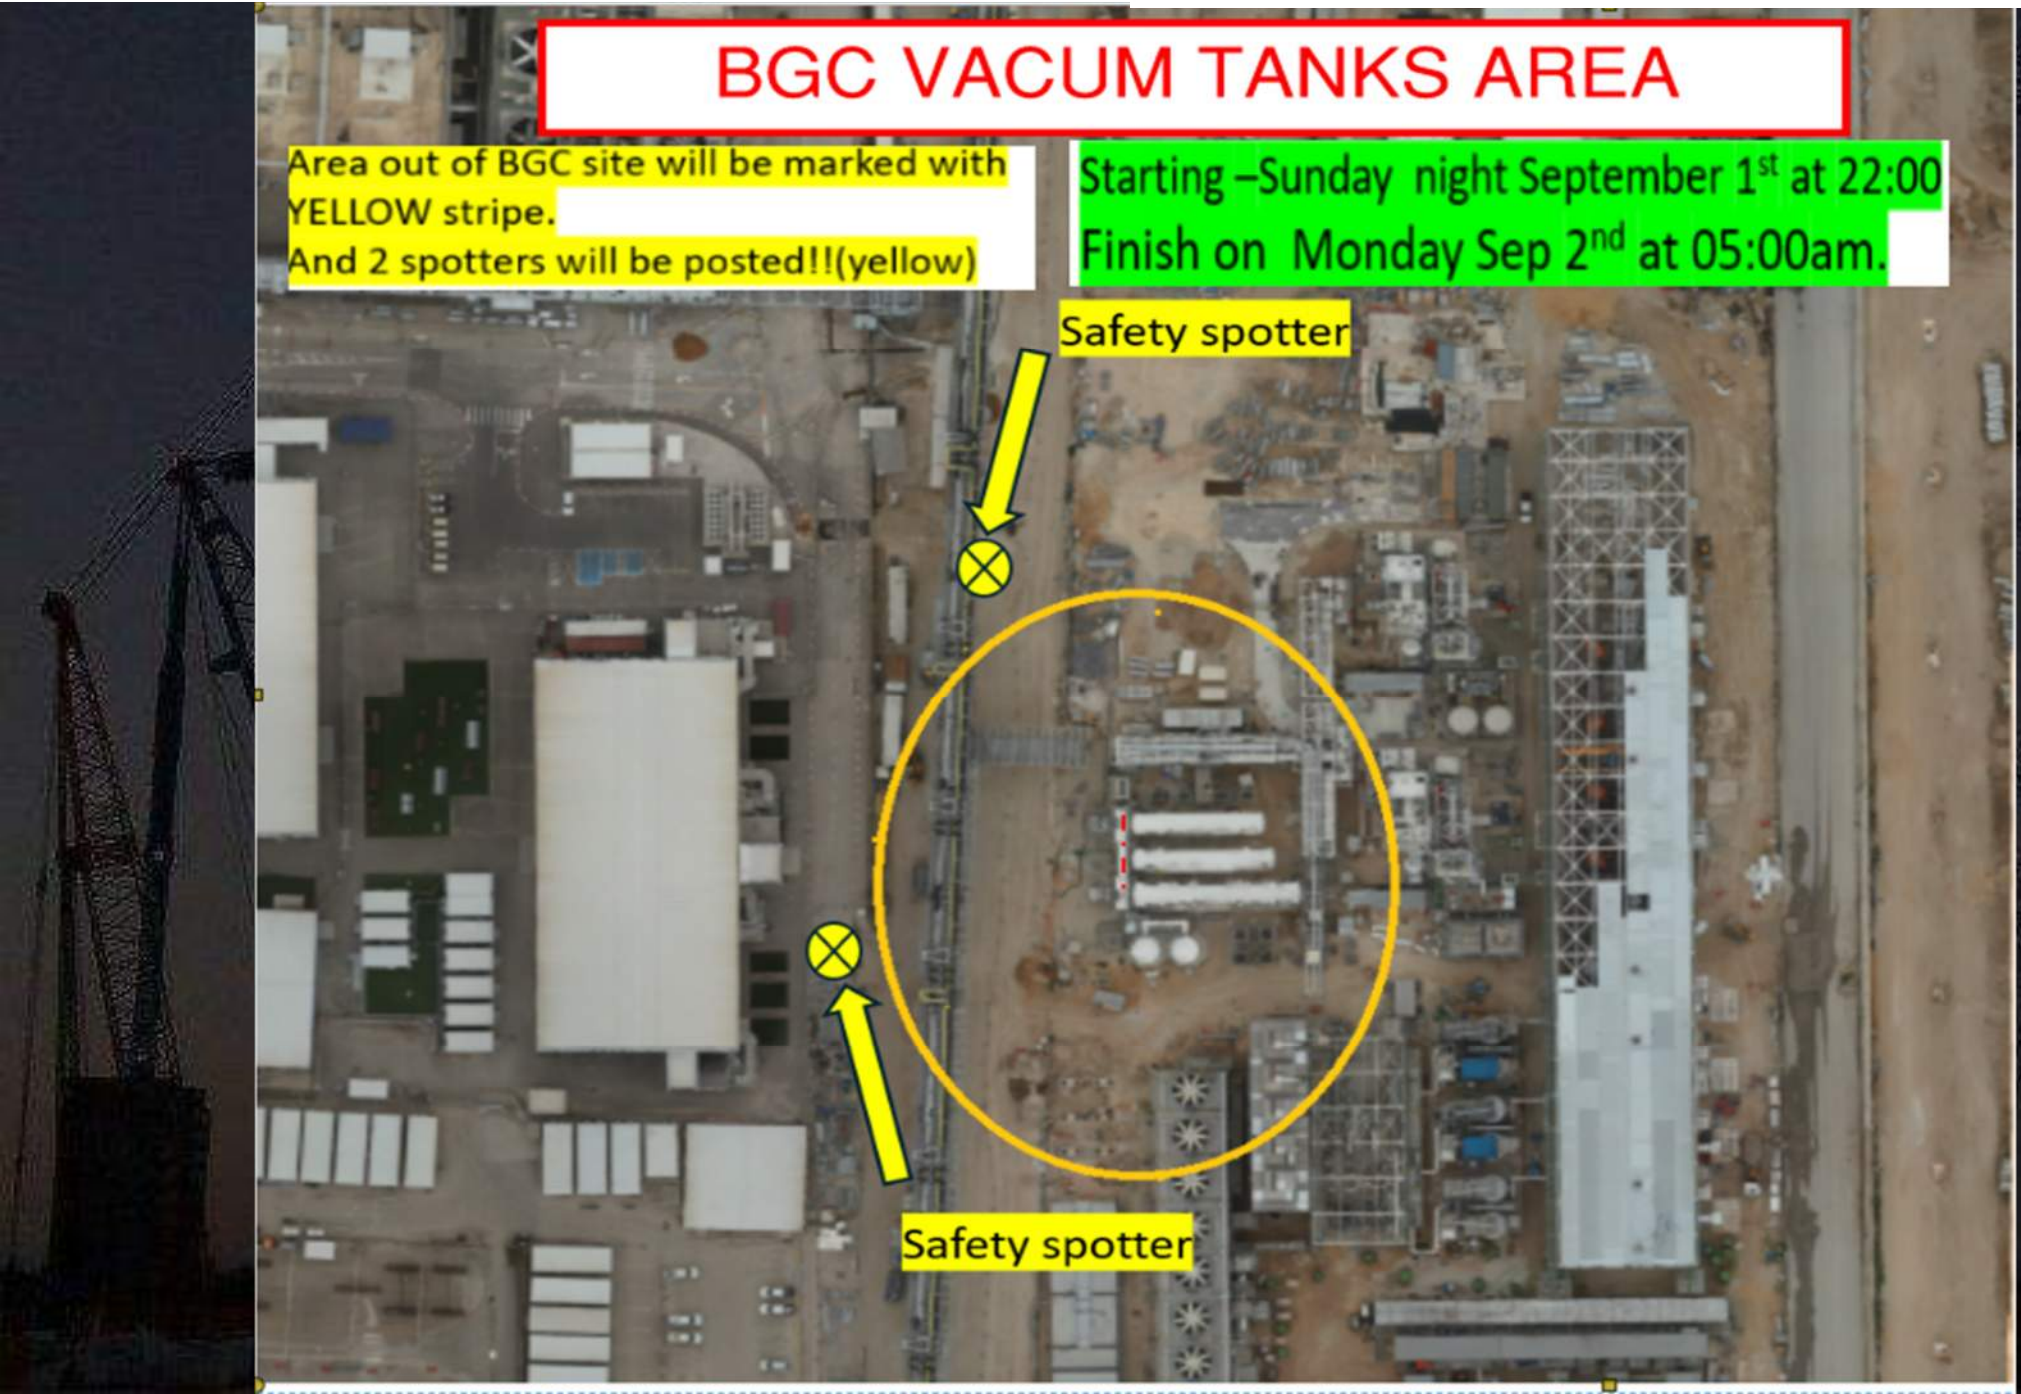

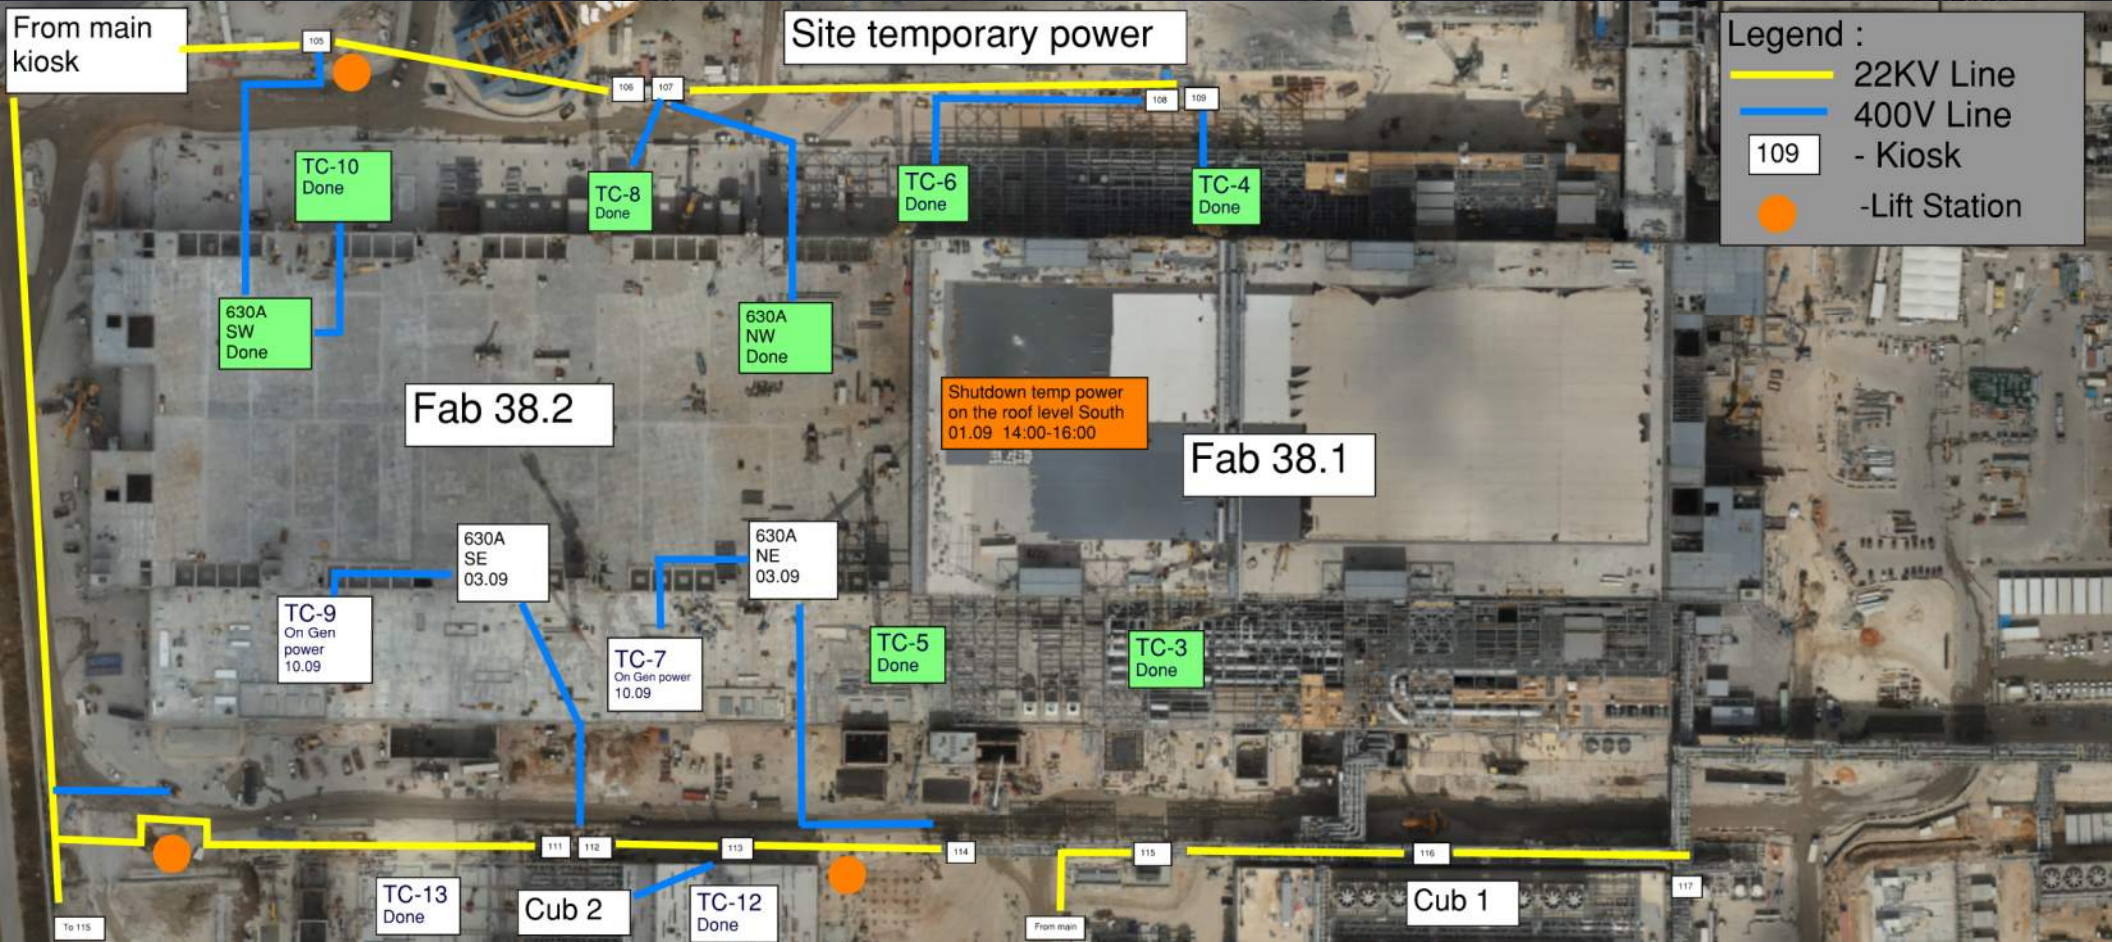



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
North Gate B






HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North

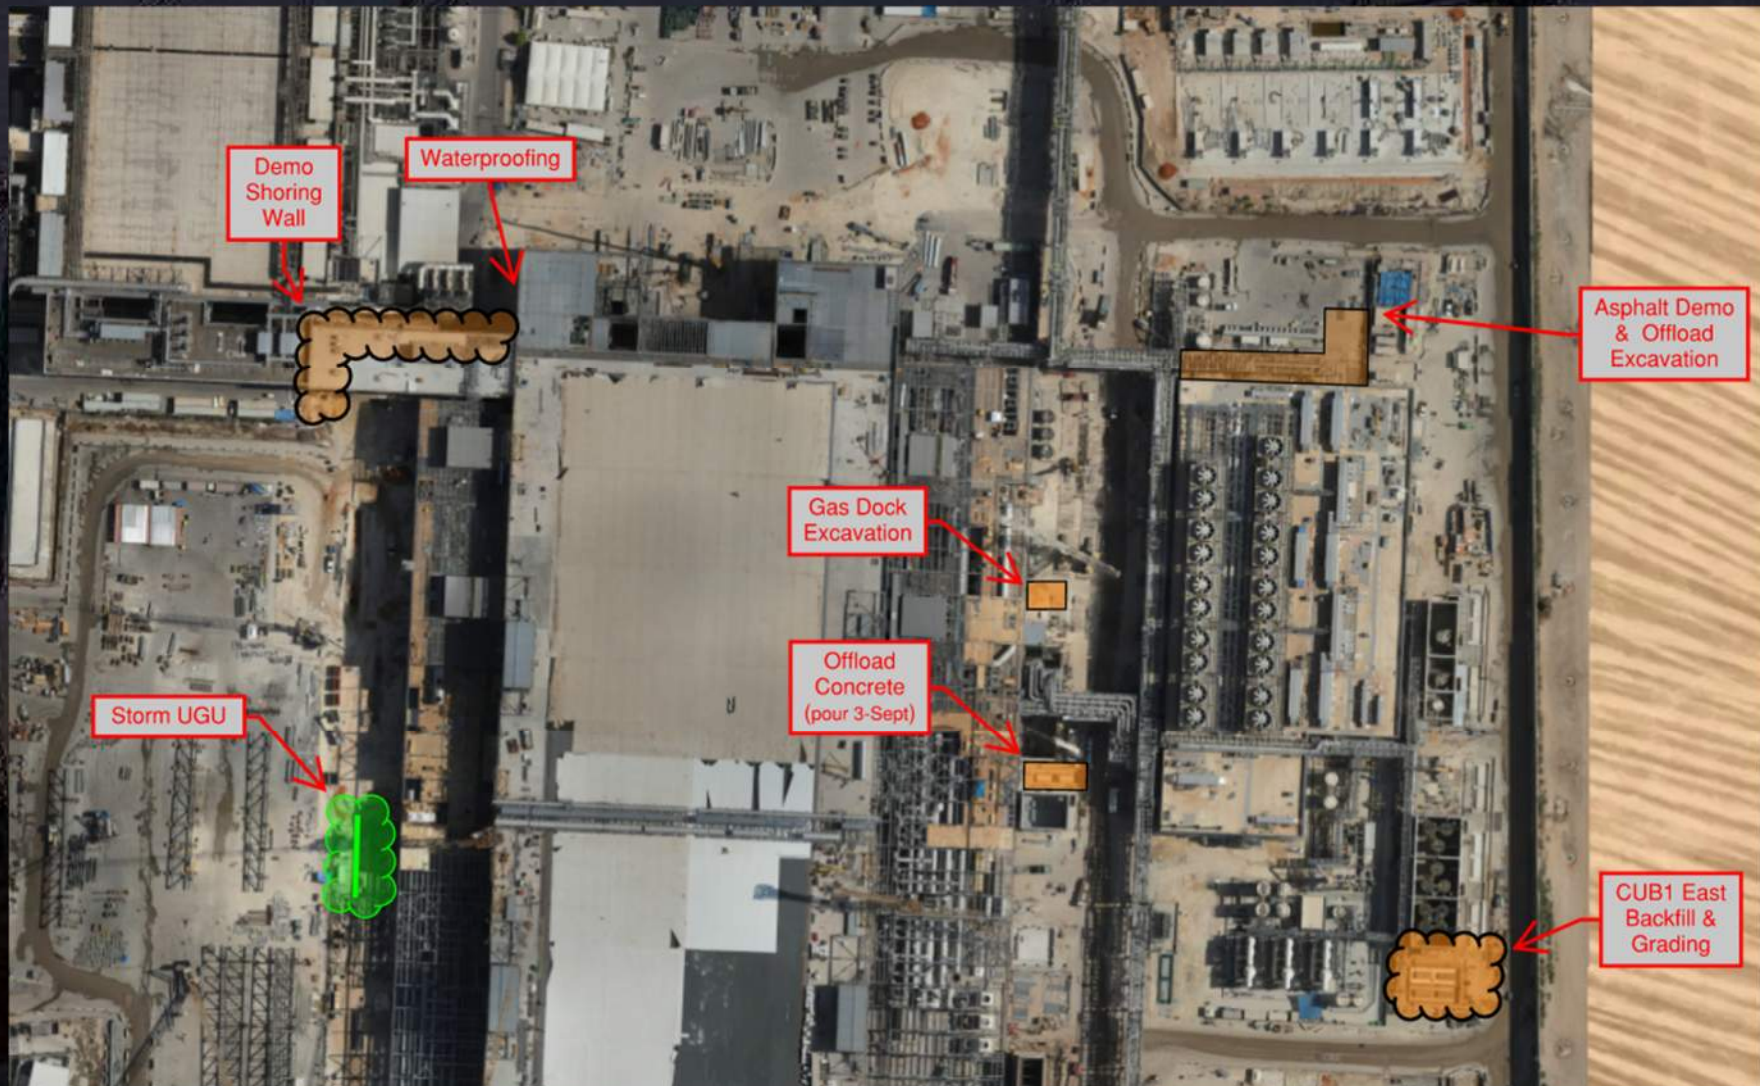



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South







Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

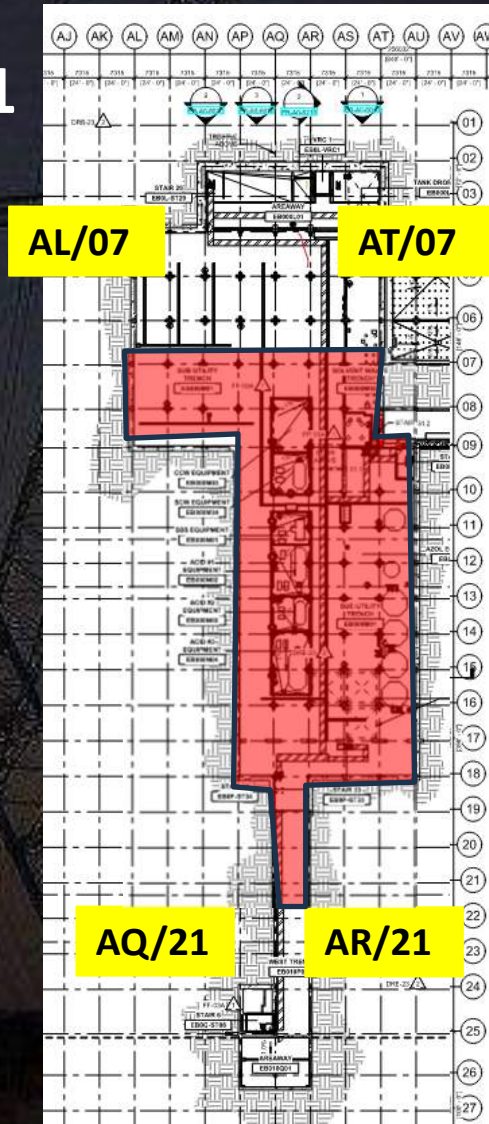

SUT2

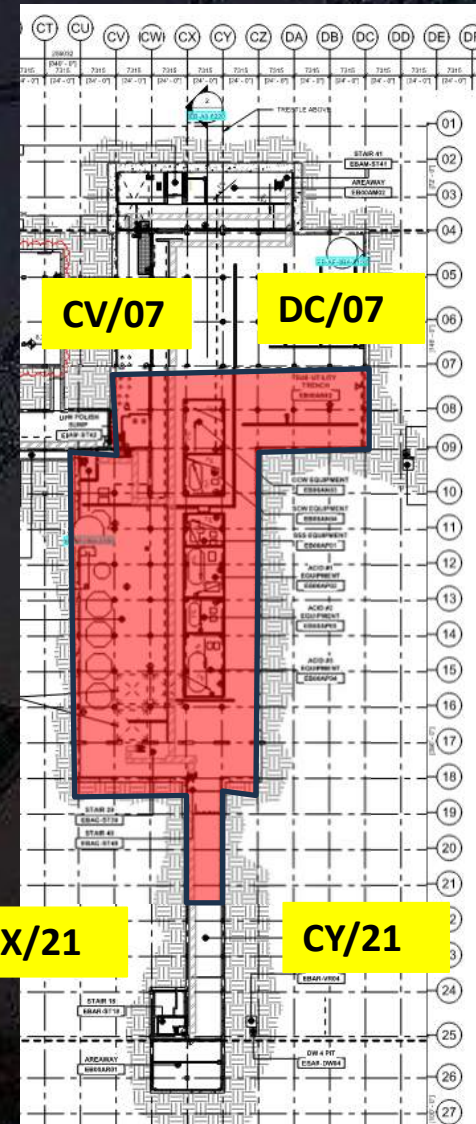





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics - Protected Areas (Utility Level)

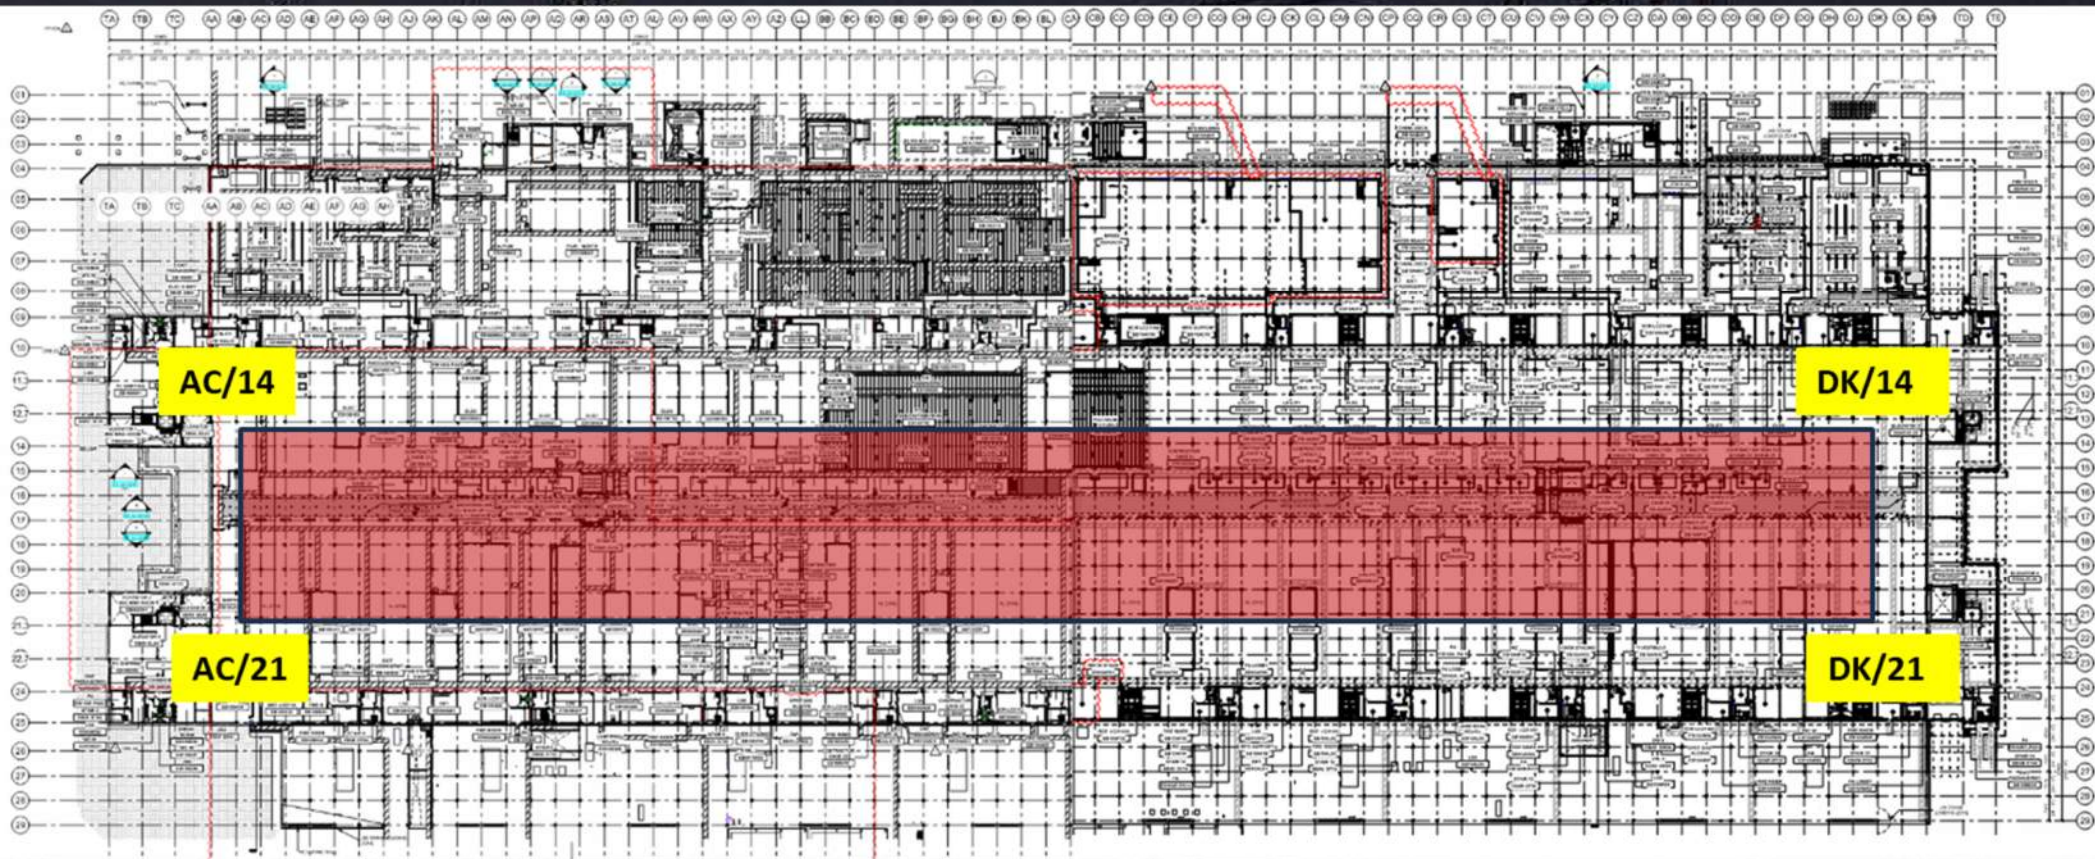

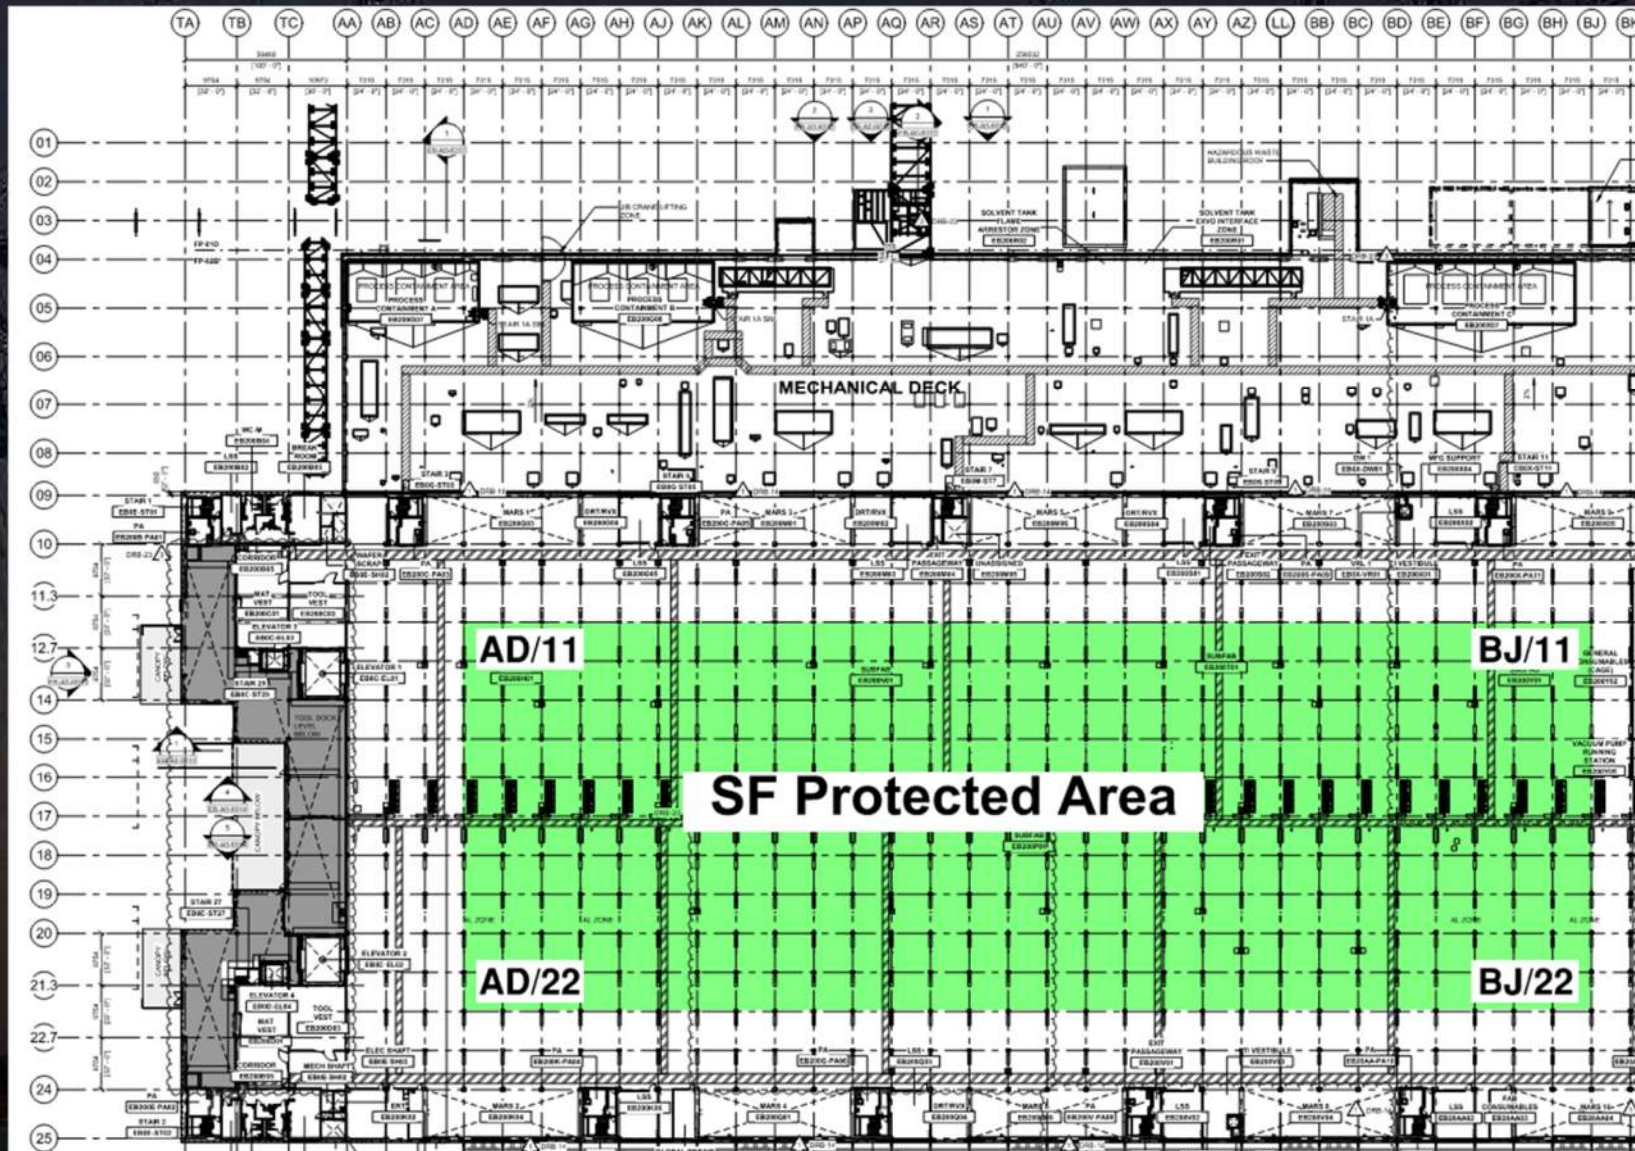




Daily Coordination Meeting

Site Logistics


Protected Areas

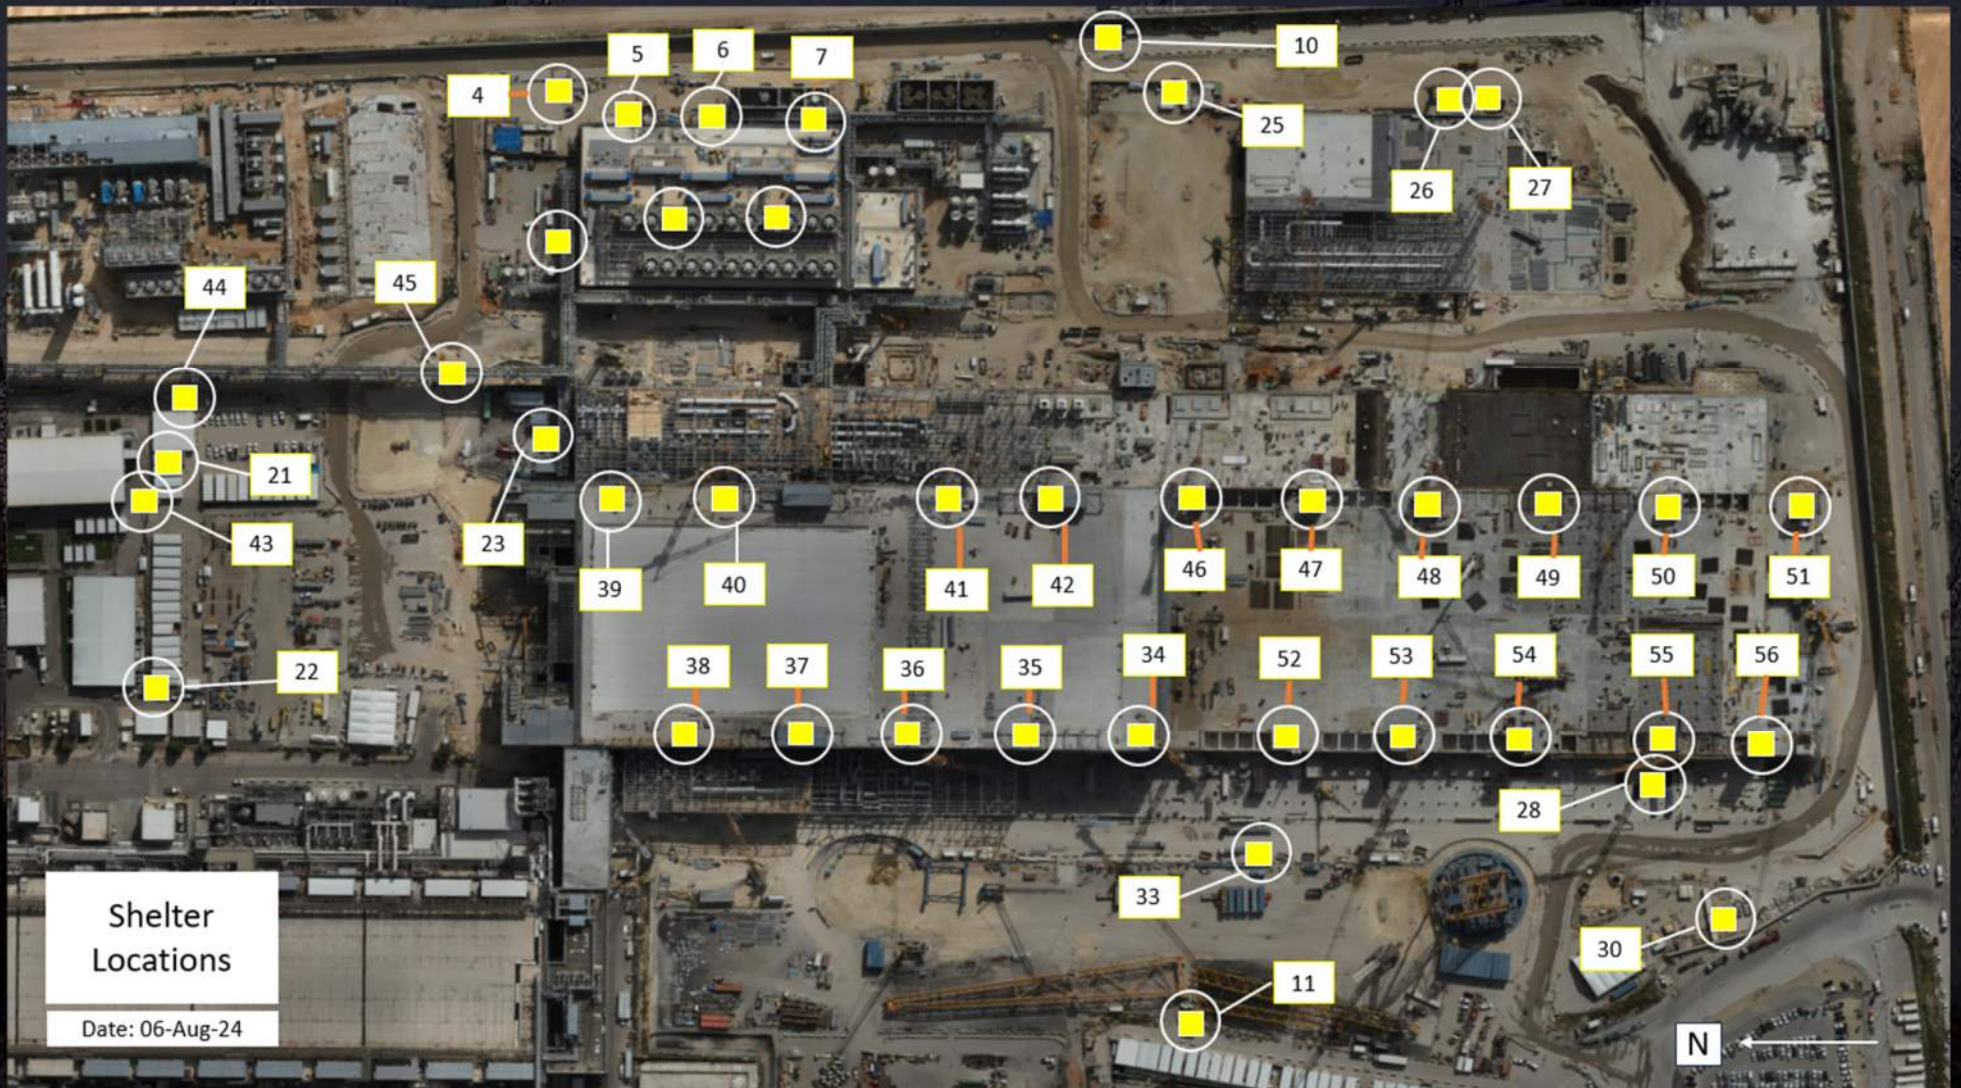


Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

BF (1) AT GIS

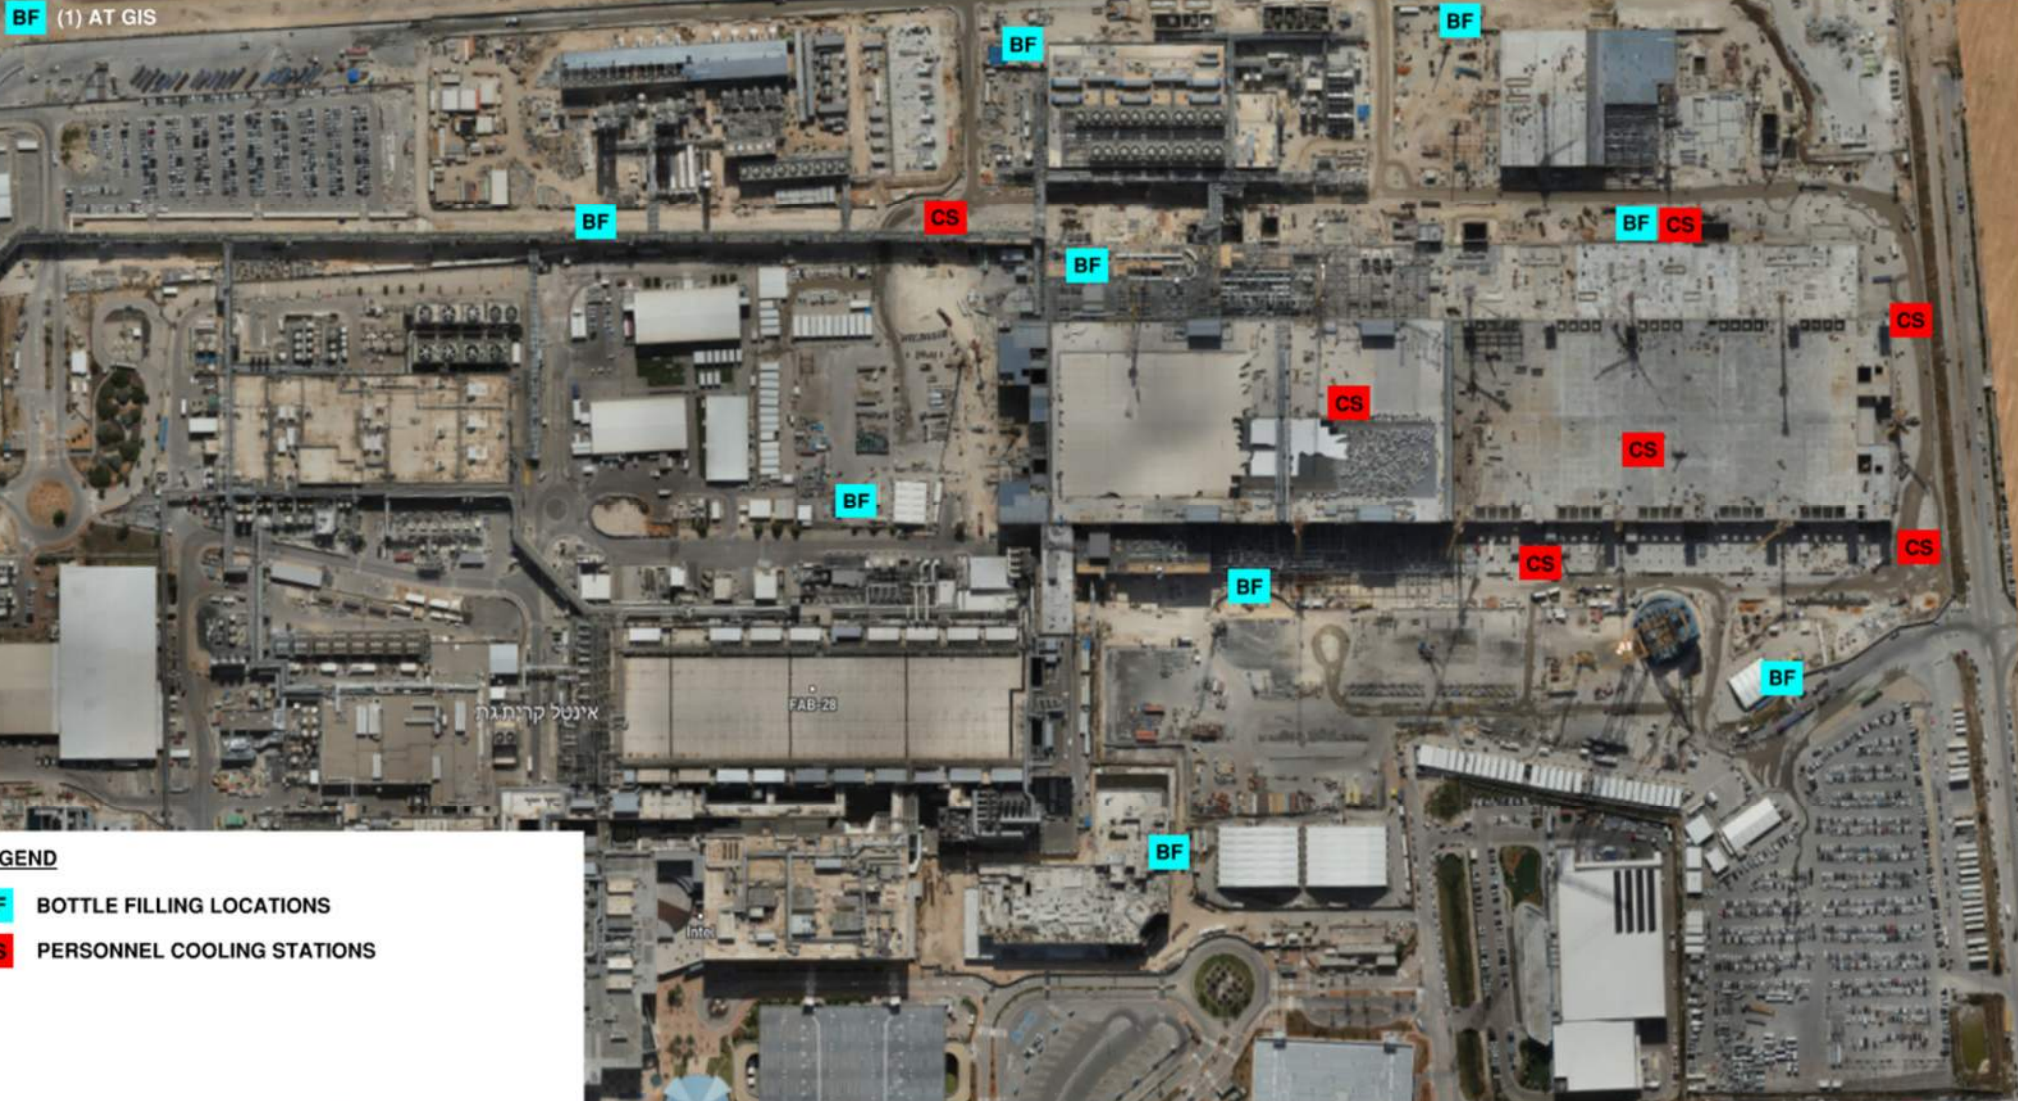






Open CORs by Subcontractor

WW 34 – 477 CORs

WW 36 – 456 CORs

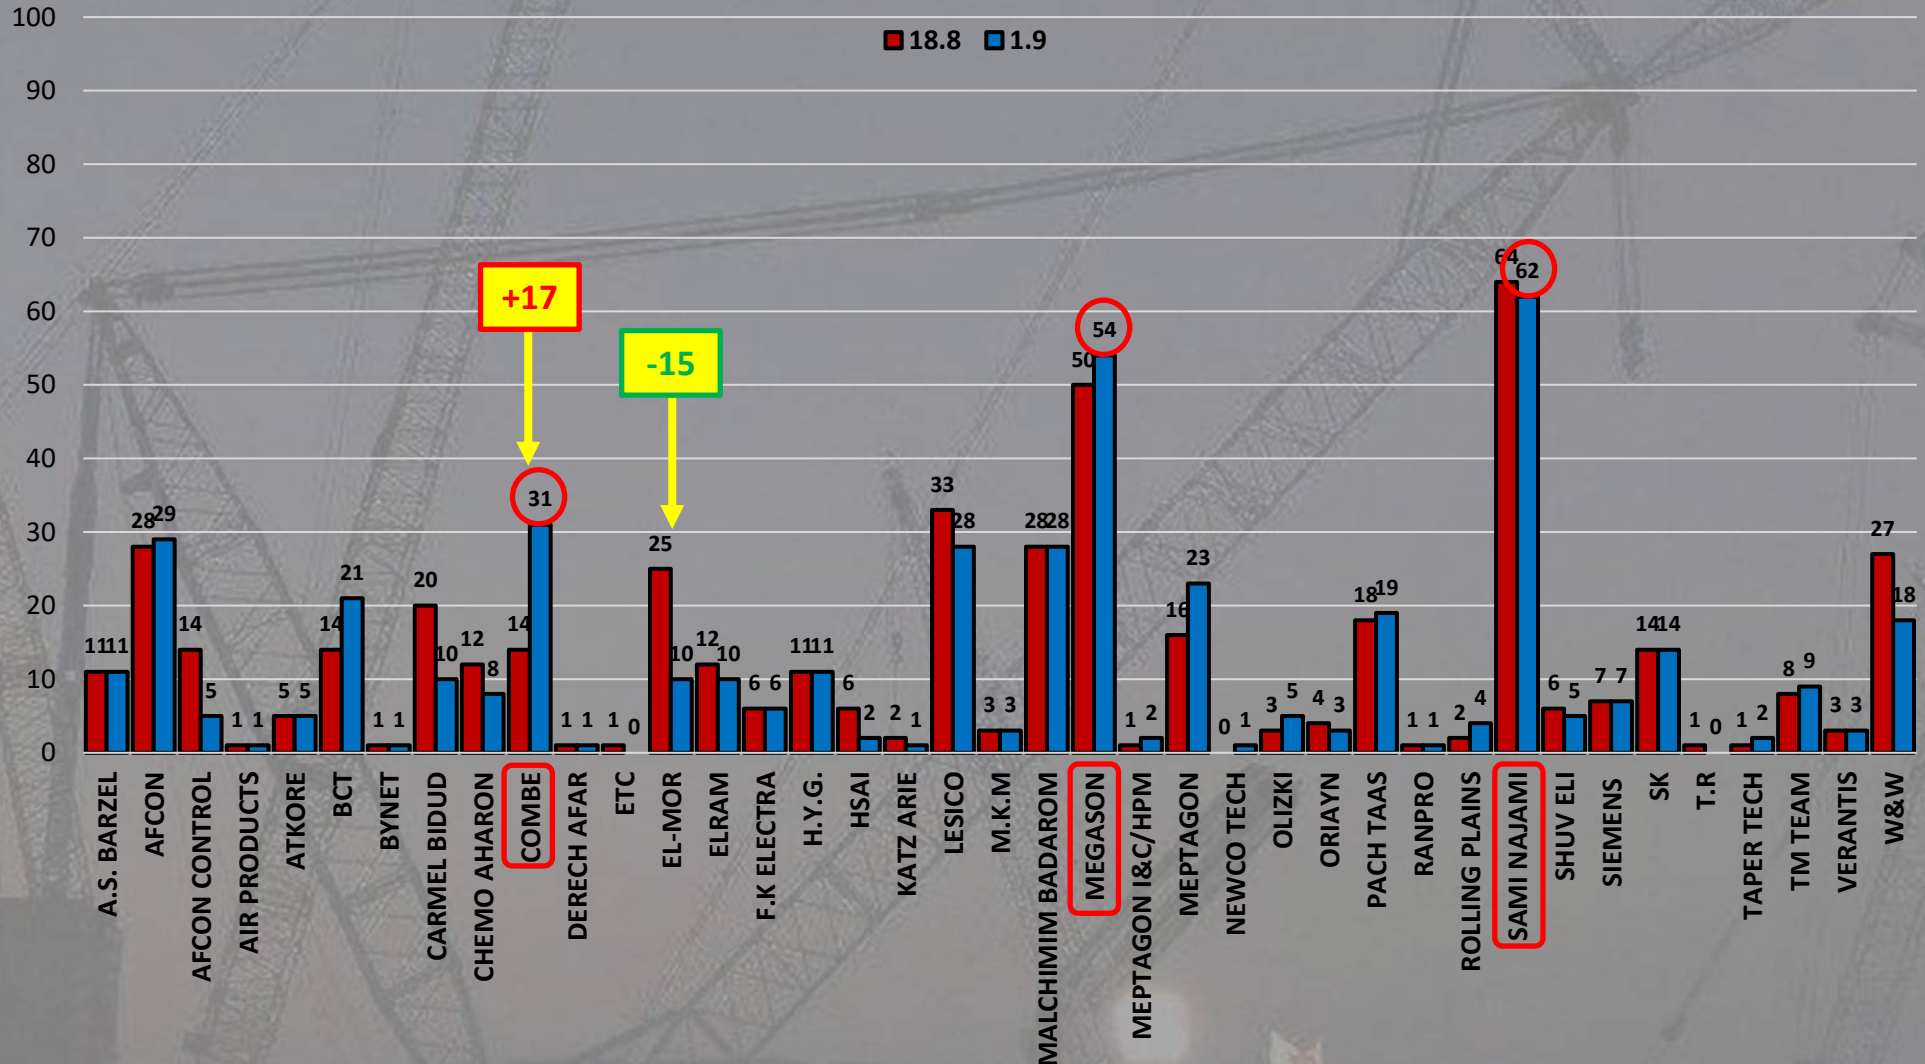




Overdue CORs by Subcontractor

WW 34 – 191 Overdue CORs

WW 36 – 152 Overdue CORs

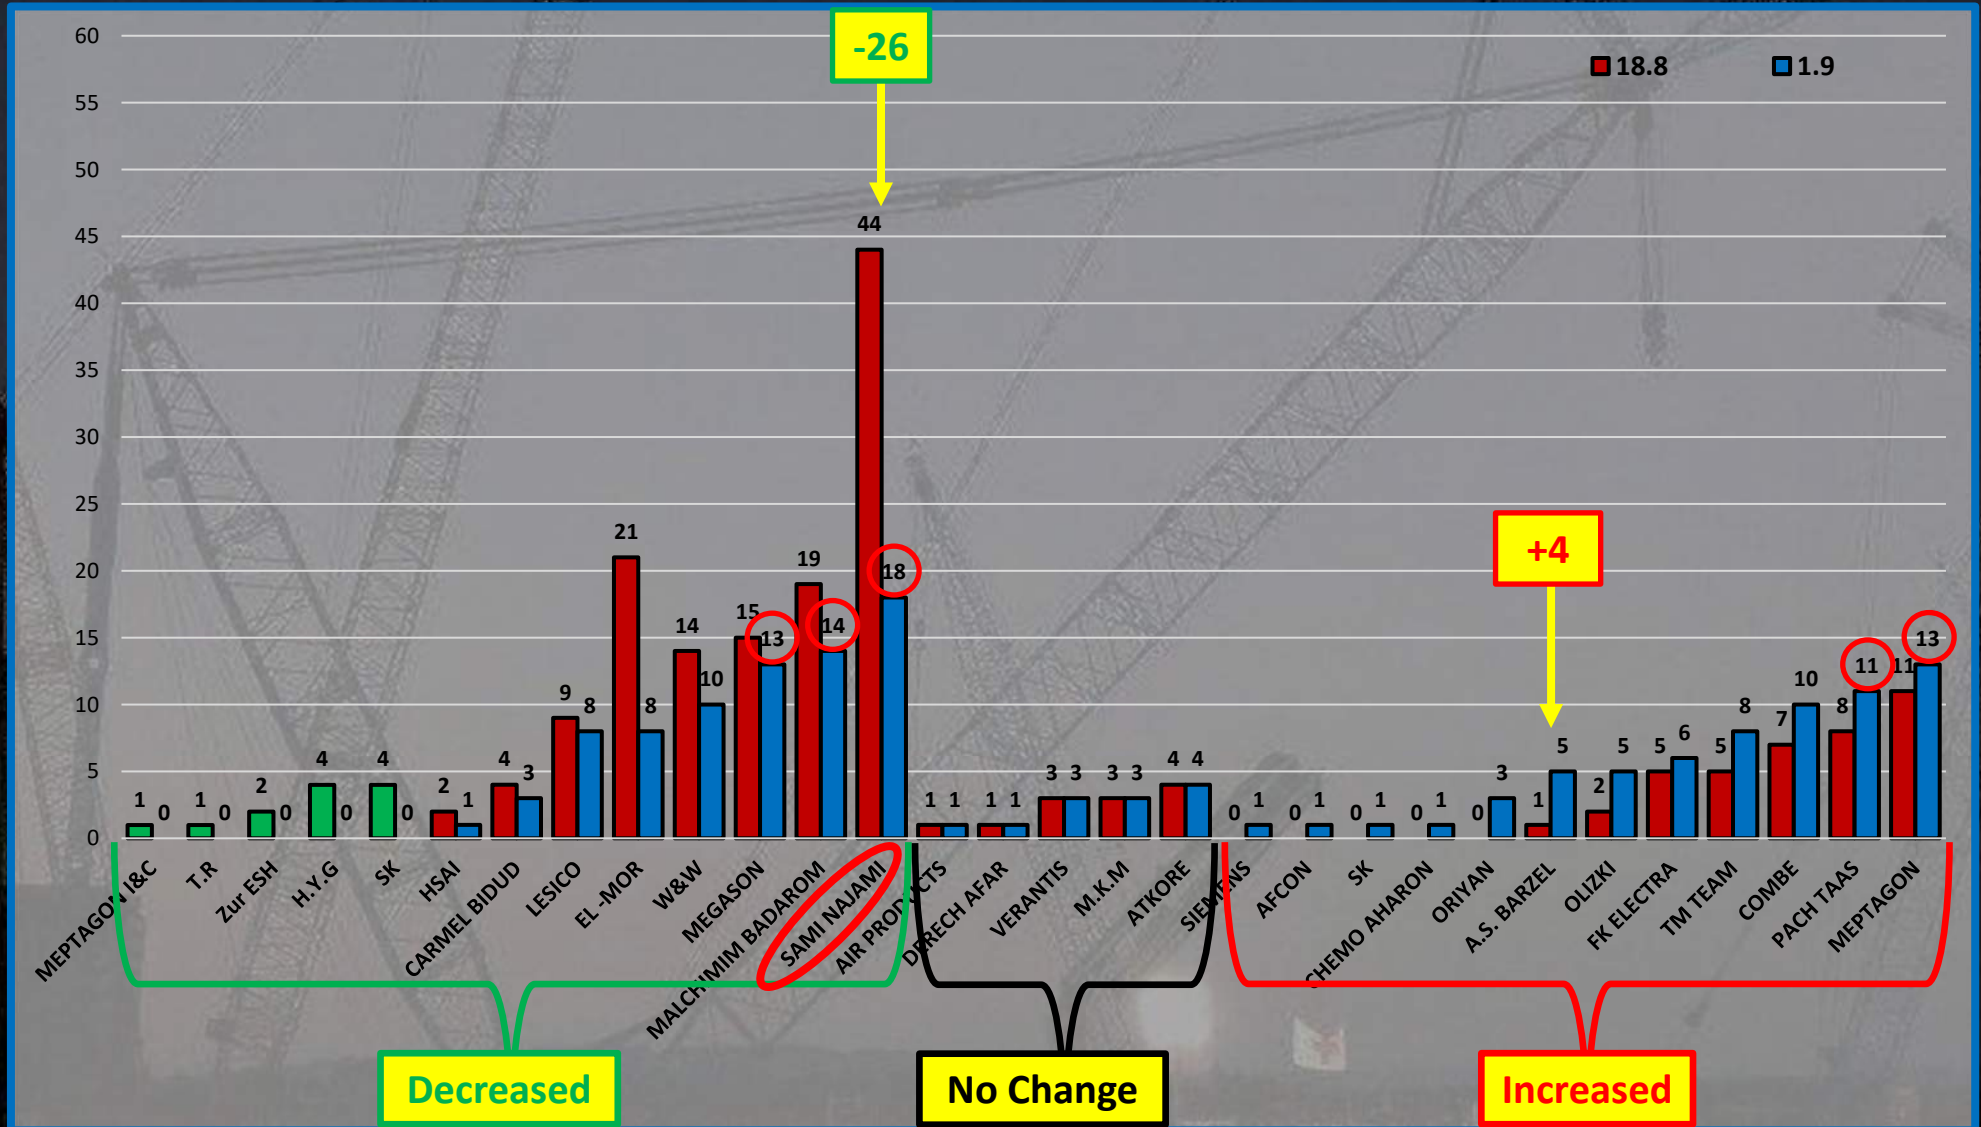

Be Prepared

WINTER is COMING

- Our small shower earlier today is a good reminder that winter is just around the corner.
- We do work in the rain. Please make sure your workers understand this and that you are starting to procure whatever you need to ensure they can be safe and productive if it rains during their shift.
- We also have holidays next month. Many people take PTO surrounding the days the site is closed. Start speaking with your teams in and out of the office and get an idea of what coverage you are going to need.
- This month is a good opportunity to start training peoples' backfills, so take advantage of it.

Heat Index- September 2nd

		temperature (°F)															
		80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110
Relative Humidity (%)	40	80	81	83	85	88	91	97	101	105	109	114	119	124	130	136	
	45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137	
	50	81	83	85	88	91	95	99	103	108	113	118	124	131	137		
	55	81	84	86	89	93	97	101	106	112	117	124	130	137			
	60	82	84	88	91	95	100	105	110	116	123	129	137				
	65	82	85	89	93	98	103	108	114	121	128	136					
	70	83	86	90	95	100	105	112	119	126	134						
	75	84	88	92	97	103	109	116	124	132							
	80	84	89	94	100	106	113	121	129								
	85	85	90	96	102	110	117	126	135								
	90	86	91	98	105	113	122	131									
	95	86	93	100	108	117	127										
	100	87	95	103	112	121	132										

 Caution
  Extreme Caution
  Danger
  Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

Daily Coordination Meeting



14:00 Sign In
